Dammam 3rd Industrial City Gates and Fence

سور للمدينة الصناعية - الدمام الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Deri Construction Company	EGIS	Eng. Affat M. Al-Enezi	06-May-2026	05-Aug-2026

Scope: Type 1 and Type 2 perimeter fence, main and chain-link gates, and guard rooms with water tanks, with their mechanical and electrical works (lighting, gate barriers, intrusion detection). Contract duration 91 days; contract value 16,500,001.96 SAR.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (25,284 man-hours in total). At 27-Oct-2026 the project is 97.9% complete against 100% planned, behind by 2.1%, after gaining 0.30% (76 man-hours) this week. The contract completion date of 05-Aug-2026 passed 83 days ago.

PHYSICAL % COMPLETE
97.9% / 100% plan
▼ SPI 0.98 −2.1%

PROGRESS THIS WEEK
+0.30% / 0.00% plan
▼ 2.1% still open after the planned finish

CONTRACT TIME ELAPSED
191% · day 174 of 91
▼ P6 finish 02-Nov-2026


INVOICED TO DATE (GROSS)
59.3% · 9.78M SAR
5 invoices, last period ends 26-Sep-2026

The project is 83 days past its contract completion date and P6 now forecasts handover on 02-Nov-2026.

The P6 update (data date 27-Oct-2026) schedules initial handover on 02-Nov-2026, 89 days after the contract date of 05-Aug-2026, with −70.5 to −75 days of float on the 21 open activities. The weekly report still gives 05-Aug-2026 as the forecast completion. Construction is 99.9% complete; most of the remaining work is testing and commissioning (84.4%) and handing over (10.5%). Deductions and penalties of 1,501,000 SAR were applied to invoice 5.


Site photos this week

Four photos from the Weekly Photos sheet of the 27-Oct-2026 weekly report. The photos carry no date or GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.

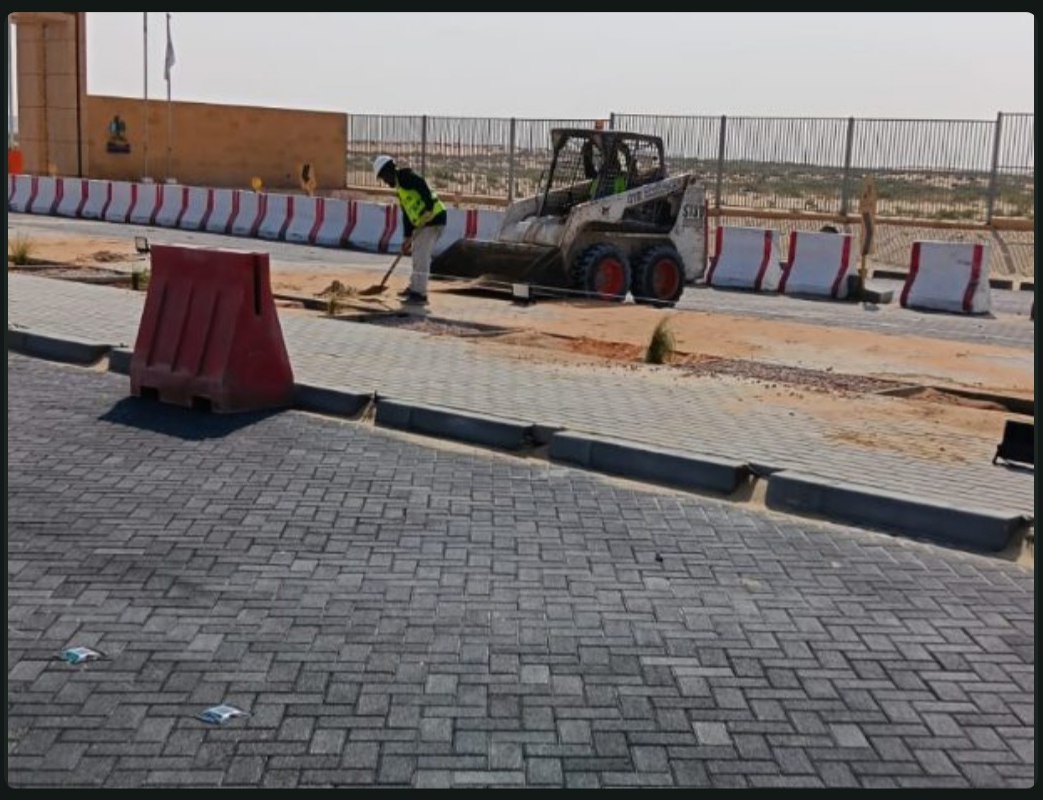

Landscape works

Planting strip being prepared beside the interlock paving, with a skid-steer loader.

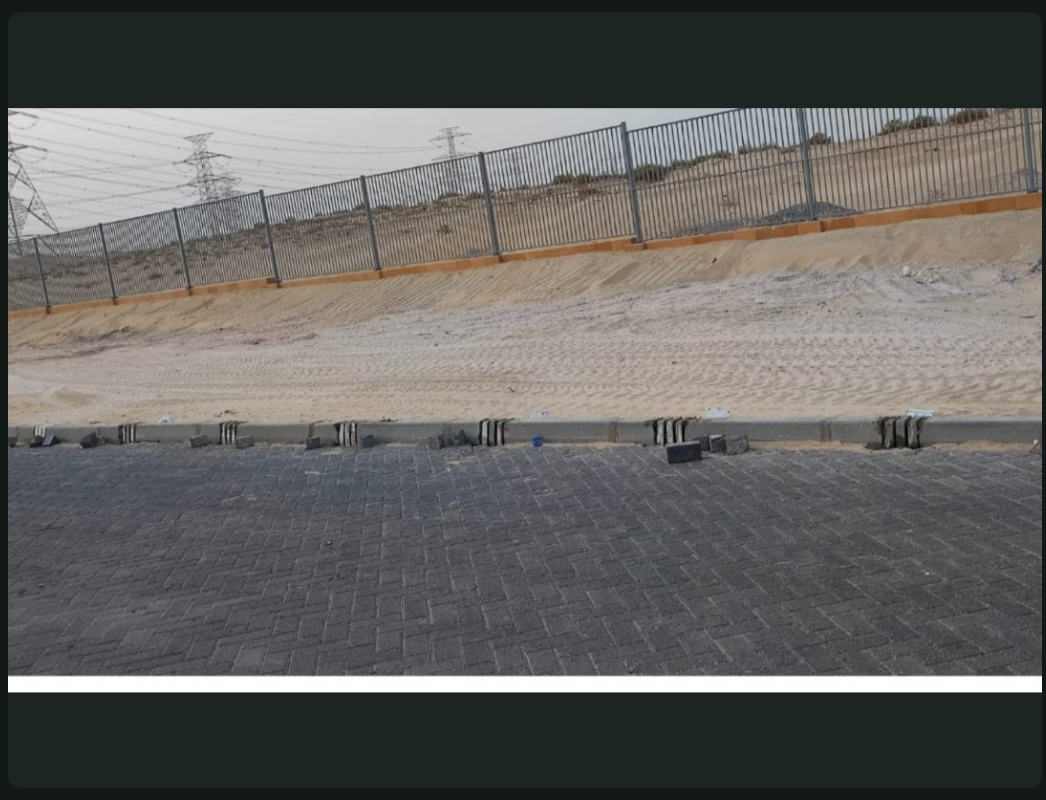


Fence and paving

Installed steel fence above the interlock paving and kerb line. Labelled "electrical works" in the report.



Landscape works

Planting pit with a gravel bed beside the sidewalk.

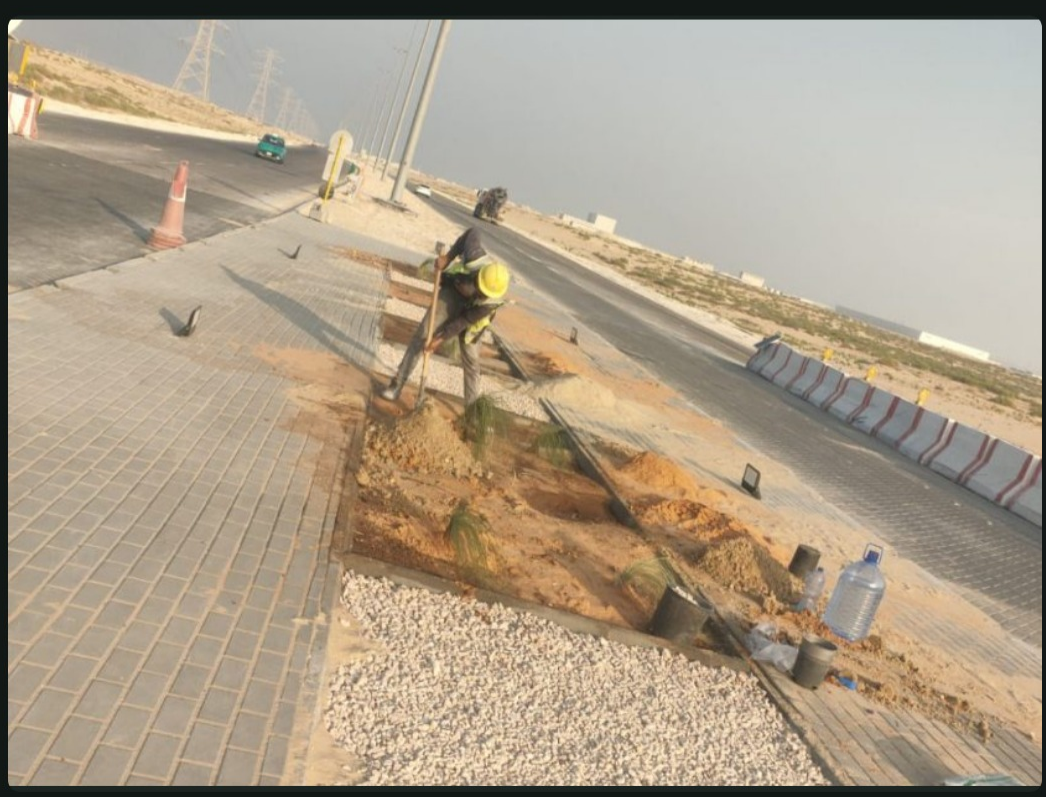


Landscape works

Shrubs planted in the strip between the sidewalk and the road.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

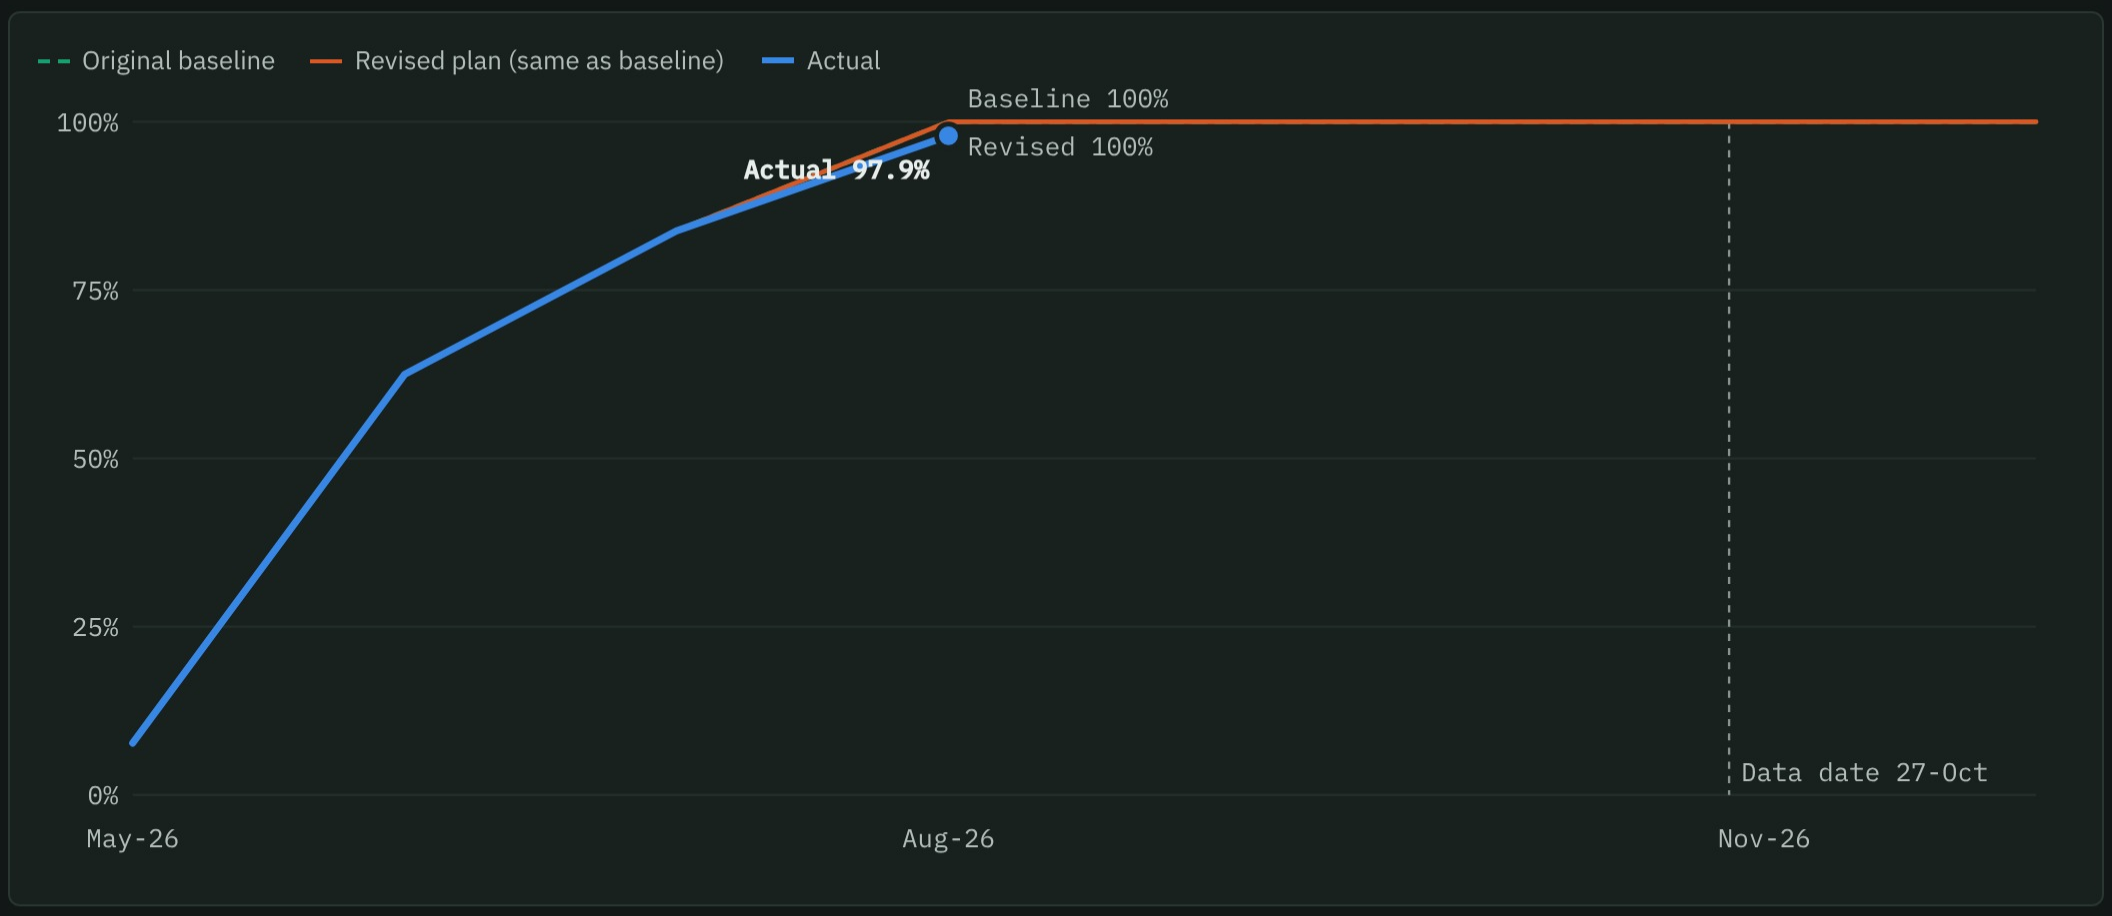

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
20-Oct-2026	100.0	97.6	−2.4%	–	0.98
27-Oct-2026	**100.0**	**97.9**	**−2.1%**	**+0.30%**	**0.98**

Both rows come from the Progress sheet of the 27-Oct-2026 weekly report, which gives this week's and the previous week's earned man-hours (24,757 and 24,681 of 25,284). No earlier weekly report was uploaded. The chart sheet books all progress made after July in August, so the actual line ends there at 97.9%.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	1.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Preliminary submittals	0.2%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	26.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	26.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
Construction	43.5%	100.0%	99.9%	−0.1%	1.00	▼ Finishing
Testing & commissioning	0.3%	100.0%	84.4%	−15.6%	0.84	▼ Late
Handing over	2.2%	100.0%	10.5%	−89.5%	0.11	▼ Late
Total	100%	**100.0%**	**97.9%**	**−2.1%**	**0.98**	▼ Late

Within construction, the Type 2 structural-steel fence is at 99.5% and the electrical works at 99.7%; all other trades are complete. The P6 update has 391 activities: 370 completed, 21 in progress and none not started. Its scheduled finish is 02-Nov-2026, 89 days after the contract date.

Milestones

Contractual milestones of the P6 schedule. The weekly report's milestone sheet uses other dates and forecasts no delay; both are shown so the difference can be resolved with the contractor.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	06-May-2026	30-Apr-2026	–	–	✓ Done
Preliminary submittals	25-May-2026	–	01-Aug-2026 (actual)	–	✓ Done late
Mobilization	31-May-2026	20-May-2026	02-Aug-2026 (actual)	–	✓ Done late
Shop drawings	22-Jun-2026	–	24-Aug-2026 (actual)	–	✓ Done late
Material submittal & approval	18-Jul-2026	–	19-Sep-2026 (actual)	–	✓ Done late
Fabrication & delivery	04-Aug-2026	–	12-Aug-2026 (actual)	–	✓ Done late
Construction	05-Aug-2026	25-Aug-2026	16-Sep-2026 (marked done)	−73.7	? Works still open
Project completion	05-Aug-2026	05-Aug-2026	02-Nov-2026	−75	▼ Late

The weekly report and the P6 update disagree on the completion date.

The weekly report gives 05-Aug-2026 as the forecast completion (General Information sheet) and 30-Aug-2026 on its milestone sheet, both with no delay. The P6 update finishes the project on 02-Nov-2026. P6 marks the Construction and Project Finish milestones complete on 16-Sep-2026, yet four construction activities are still open: the chain-link gate, lighting fixtures, the electrical gate barrier and the smoke and heat detectors.

Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

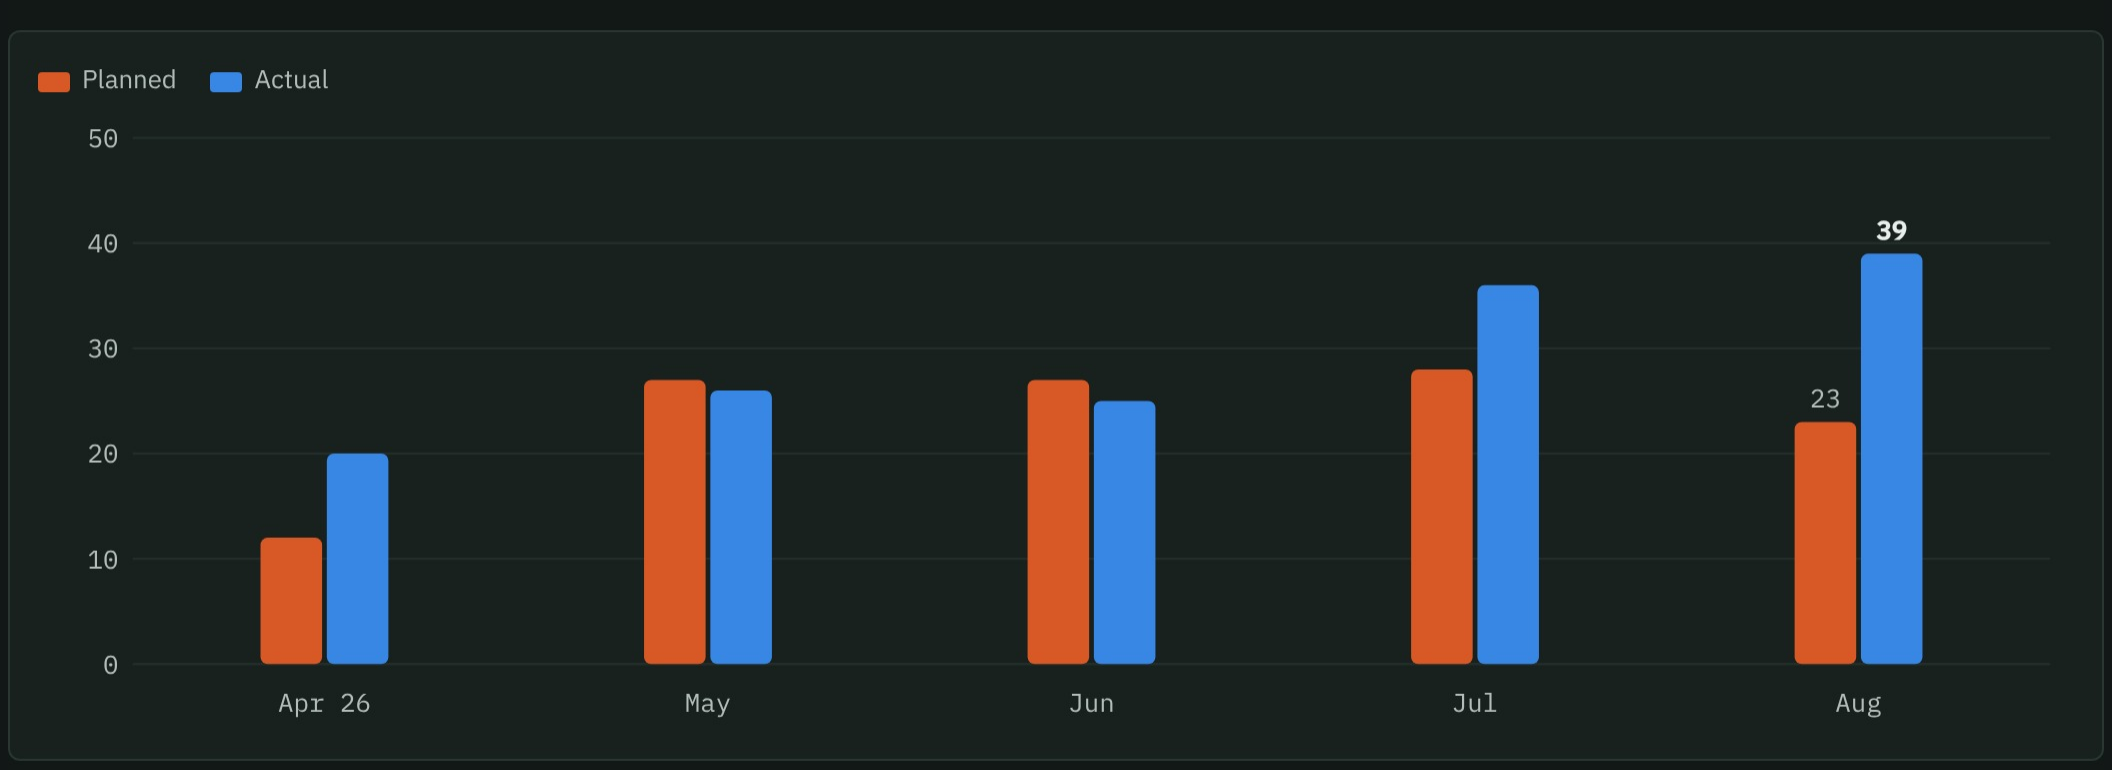

The manpower sheet has no figures after August 2026. The weekly report summary repeats August's head count: 39 actual (11 staff, 28 labour) against 23 planned.

Cost and invoicing

Contract value

Original contract value	16,500,001.96
Revised contract value	16,500,001.96
Change orders	0
Potential changes	0

All values in SAR. No change orders are registered. The invoice log also shows a revised value of 21,100,000 and potential changes of 200,000; see Data notes.

Invoices

Invoices submitted	5
Gross value	9,780,875.90
Approved by the consultant	5
Approved by the MODON PM / paid	0 / 0
Deductions and penalties	1,501,000
Net incl. VAT	9,747,007.29
FIR value to date	10,232,434.64

Invoicing is 59.3% of the contract value against 97.9% physical progress. Invoice 5 (06-Aug to 26-Sep-2026) carries a deduction of 1,500,000.

Health, safety and quality

Safety Score 0.80

Safe man-hours (cumulative)	13,577
Man-hours this week	2,208
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	40 / 124

HSE site inspection no. 30 on 26-Oct-2026.

Quality Score 0.88

FIRs issued / closed / pending	848 / 829 / 19
MIRs issued / closed / pending	90 / 88 / 2
NCRs issued / closed	4 / 4
Site instructions issued / closed	4 / 4
Approved shop drawings	72 of 75
Approved material submittals	101 of 113

QC observation no. 25, 11-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Remaining construction items	Contractor	Chain-link gate, lighting fixtures (final fix), electrical gate barrier and smoke and heat detectors are still open in P6, due 28-Oct-2026, with −70.5 to −73.7 days of float.
Testing and commissioning	Contractor	Electrical and mechanical systems are 85% complete, due 29-Oct and 01-Nov-2026.
Close-out documents	Contractor / Consultant	As-built drawings 50% prepared; operational spares 50% submitted and 33% accepted; warranties, manuals and training not yet submitted.
Snag list and initial handover	Contractor / MODON	Snag-list rectification, demobilization and initial handover have not progressed; P6 schedules handover for 02-Nov-2026.
Invoice approval	MODON	All five invoices are approved by the consultant, but none is approved by the MODON PM or paid. Deductions and penalties of 1,501,000 SAR are applied.

All eleven items in the risk and issue logs are marked closed, the last on 15-Oct-2026: Type 2 fence accessory shortages, a medium-voltage cable on the Type 2 fence alignment, dirt-road works held up by backfill, equipment and payments, late lighting supplies, and the change of gate width (RFI-0009).

Data notes

- Physical % complete is taken from the Progress sheet of the weekly report (earned vs budgeted man-hours). The "Actual %" column in the P6 PDF layouts and the earned-value cells of the weekly report are cost-based, so they are not used.
- No earlier weekly report was uploaded for this project. This week's gain comes from the previous-week columns of the same Progress sheet; quantities this week are not available.
- Dates disagree inside the weekly report: the General Information sheet gives site handover 06-May-2026 and completion 05-Aug-2026 (as does the P6 baseline), while the Milestones sheet gives award 16-Apr-2026, handover 30-Apr-2026 and completion 30-Aug-2026. The lower table of the Milestones sheet belongs to another fence project (SUD1-05-015).
- The weekly report still forecasts completion on 05-Aug-2026 with zero variance, although that date has passed; P6 forecasts 02-Nov-2026.
- In the P6 update, the Construction and Project Finish milestones are marked complete on 16-Sep-2026 while 21 activities are still in progress. Actual dates start on 13-Jul-2026 (Project Start), two months after handover; the electrical gate barrier shows an actual start of 12-Apr-2026, before the contract award.
- The Major Quantities sheet is not usable: actual quantities are fractions of one unit (for example 0.25 LM of 18,500 LM of chain-link fence) and its resource table is from another project. The scope section is left out.
- The Procurement sheet carries another project's code and has delivery data for only a few minor items, so the procurement section is left out.
- The invoice log shows a revised contract value of 21,100,000, an estimate at completion of 20,900,000 and potential changes of 200,000, against 16,500,001.96 and 0 in the General Information and Weekly Progress Report sheets.
- The project stage is still "Mobilization" in the weekly report, and the MODON PM field is empty; the PM's name is taken from the HSE inspection sheet. The quality checklist names the contractor (HMA) as the consultant.
- The risk and issue logs mark all items closed while their "current status" column reads "In Progress", and the Top 5 issues panel is empty. Several summary panels show #REF! or #N/A errors.
- The four photos have no date or GPS stamp. Three show landscape planting, although the P6 planting activity was completed on 07-Oct-2026.

Compiled 01-Nov-2026 from the weekly report and P6 update with data date 27-Oct-2026, uploaded in folder W04 - 22-Oct-2026.
