Playground Initiative for Western Region (Asir, Jazan, Jeddah)

مبادرة الملاعب بالمنطقة الغربية (عسير, جازان, واحة جدة)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Profast Company Ltd.	EGIS	Eng. Yazeed Al Ragabh	26-Mar-2026	25-Jan-2027

Scope: sports grounds (padel, basketball and football), a service and toilet building, landscape works, bike and walking paths, and parking at three sites in Asir, Jazan and Jeddah.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours, over the WBS phases as in last week's report. The project is at 44.6% against 55.2% planned, 10.6% behind (SPI 0.81). It gained 2.2% this week against 4.2% planned, so the gap widened from 8.6% last week. Jazan is furthest behind at 30.4% against 49.4% planned; Jeddah is slightly ahead of its plan.

PHYSICAL % COMPLETE

44.6% / 55.2% plan

▼ SPI 0.81 −10.6%

PROGRESS THIS WEEK

+2.2% / +4.2% plan

▼ 2.0% below the weekly plan

CONTRACT TIME ELAPSED

70.2% · day 214 of 305

▼ Forecast finish 19-May-2027

INVOICED TO DATE (GROSS)

14.6% · 4.94M SAR

5 invoices, last period ends 08-Oct-2026

Project completion is now forecast 114 days late.

The weekly report and the P6 update (data date 26-Oct-2026) both forecast completion on 19-May-2027, ten days later than last week and 114 days after the contract completion date of 25-Jan-2027. P6 shows −91 days of float on project completion and 320 open activities with negative float. The most critical path still runs through the air dome: on the most critical of the three domes, approval of the PVC membrane, steel tension cables, emergency doors and lock doors has not started and carries −91 days of float. The weekly report's own headline of 60.7% against 76.1% is not comparable with last week; see Data notes.

Site photos this week

Six photos from the Weekly Photos sheet of the 26-Oct-2026 weekly report, two from each site. Where a stamp is visible it reads 25-Oct-2026. Select a photo to view it larger, then use the arrows to move between photos.




Irrigation works, Jazan

HDPE irrigation pipe laid in the trench. No stamp visible.



Walkway backfilling, Jazan

Backfilled and graded walking path along the fence. Stamped 25-Oct-2026, 09:14, Abu Arish.

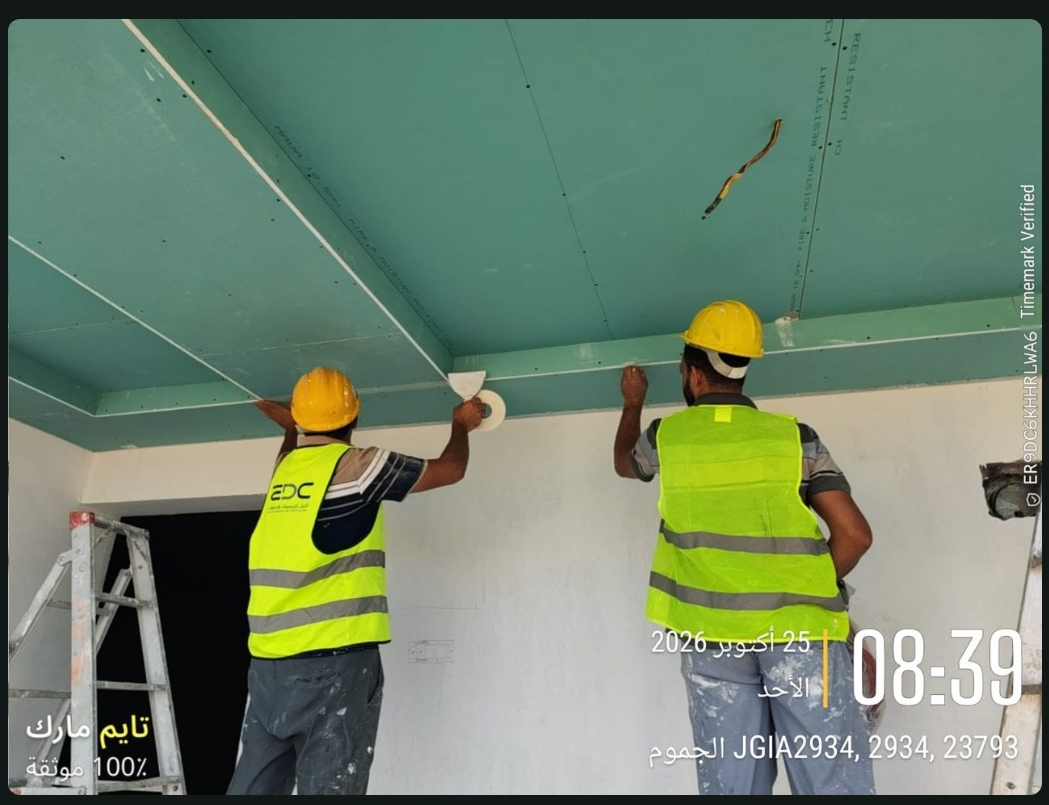

Ceiling works, Jeddah

Joint finishing on the gypsum board ceiling. Stamped 25-Oct-2026, 08:39.



Planting works, Jeddah

Curbs set around a circular planting bed. No stamp visible.



Lighting pole works, Asir

Pole base set in the cable trench. Stamped 25-Oct-2026, 14:48, Khamis Mushait.




Backfilling works, Asir

Backfilling with a backhoe loader. Stamped 25-Oct-2026, 14:56, GPS 18.3343373°N, 42.6572196°E.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly, plotted at mid-month. Source: Physical-Chart Data sheet, weekly report 26-Oct-2026; the October actual is the like-for-like 44.6%.

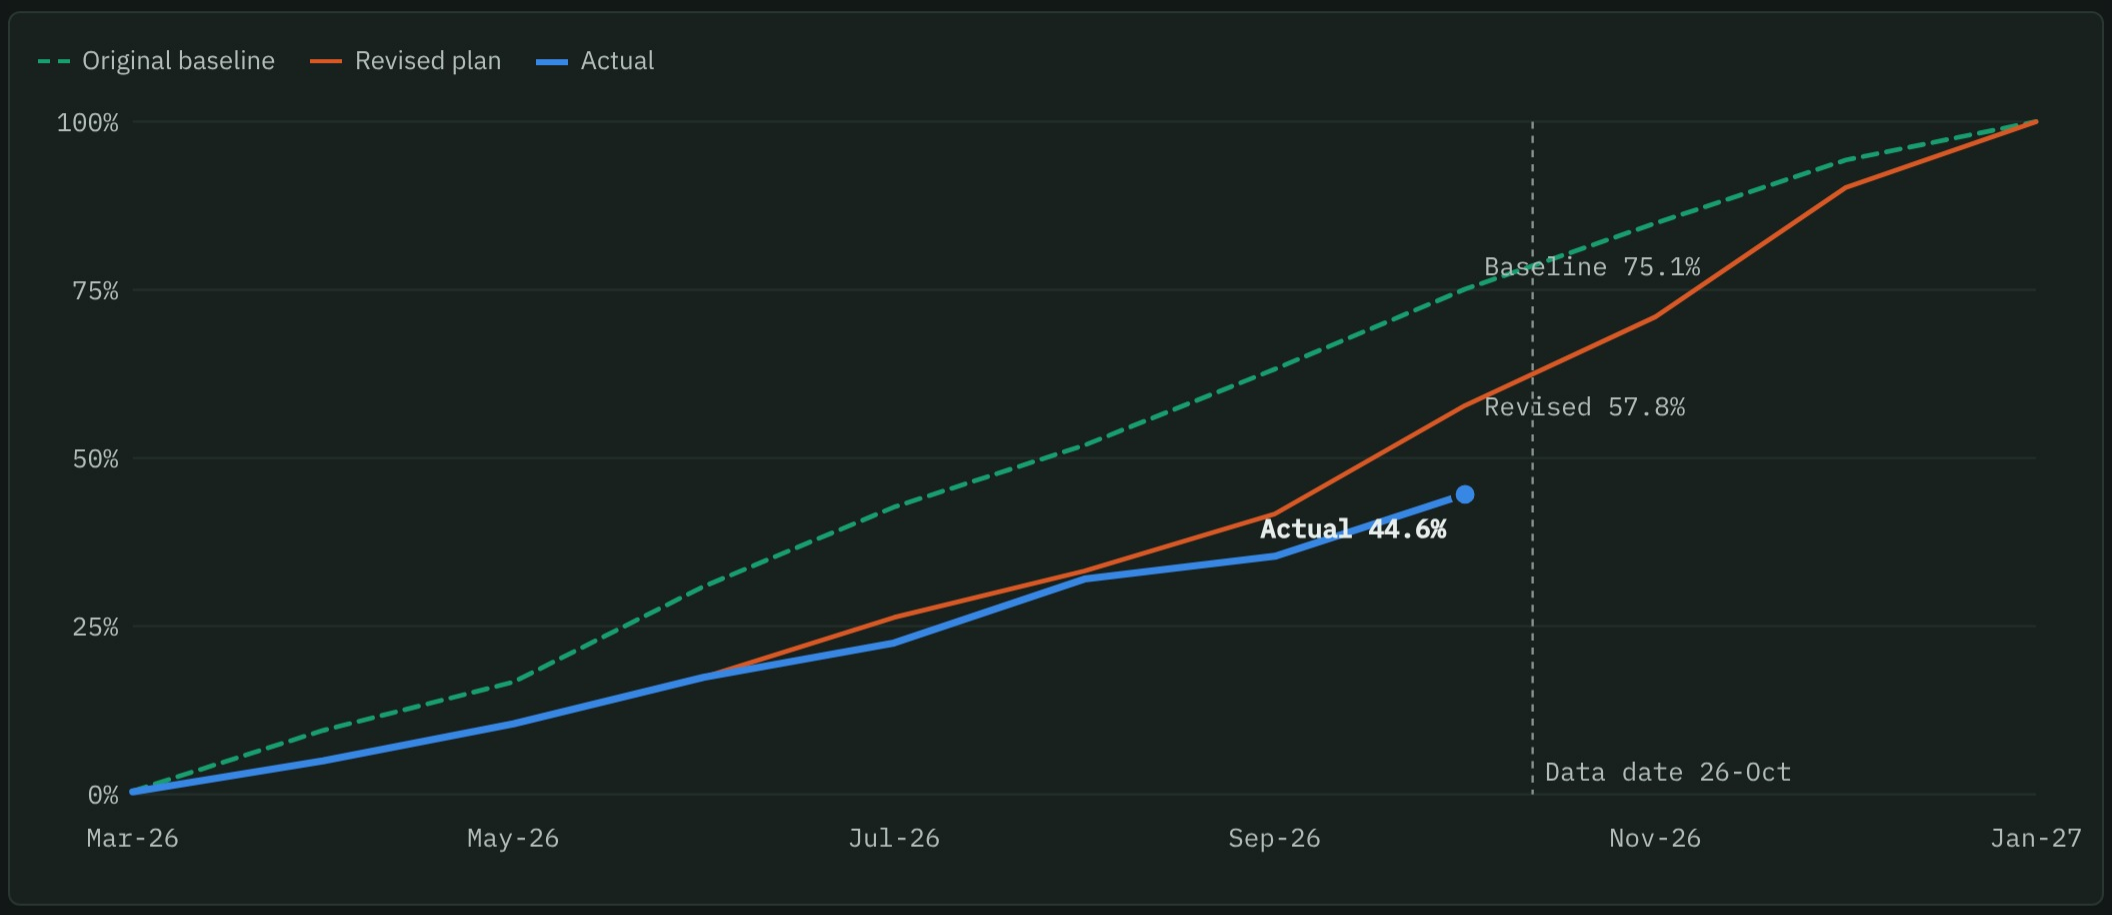

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	47.0	39.0	−8.0	—	0.83
19-Oct-2026	51.0	42.4	−8.6	+3.4	0.83
26-Oct-2026	**55.2**	**44.6**	**−10.6**	**+2.2**	**0.81**

Values for 12 and 19 Oct come from the 19-Oct report, and 26 Oct from this week's report over the same WBS phases. This week's planned gain was +4.2%. The gain for 12 Oct is not in these two reports.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Construction is split into the three sites.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.1%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	5.2%	100.0%	98.6%	−1.4	0.99	▼ Slightly behind
Procurement	12.6%	99.1%	62.2%	−37.0	0.63	▼ Behind
Construction	73.8%	46.6%	38.6%	−8.0	0.83	▼ Behind
Construction: Jazan	25.2%	49.4%	30.4%	−19.0	0.62	▼ Behind
Construction: Asir	23.8%	47.5%	41.7%	−5.9	0.88	▼ Behind
Construction: Jeddah	24.8%	42.8%	43.9%	+1.2	1.03	▲ Ahead
Testing & commissioning	3.2%	0.0%	0.0%	0.0	–	○ Not yet due
Close-out	2.1%	0.0%	0.0%	0.0	–	○ Not yet due
Total	100%	**55.2%**	**44.6%**	**−10.6**	**0.81**	▼ Behind

Site weights are shares of the whole project. This week Jazan gained 6.2% of its own scope, Jeddah 1.8% and Asir 0.8%. The P6 update (data date 26-Oct-2026) has 2,134 activities: 1,737 completed, 26 in progress and 371 not started. Its scheduled finish is 19-May-2027, against a must-finish date of 25-Jan-2027.

Scope of work: quantities

Major quantities for the three sites combined, from the Major Quantities sheet of the 26-Oct-2026 weekly report. "This week" is the change since the 19-Oct-2026 report: none of the quantities changed. Backfilling does not apply to these items.

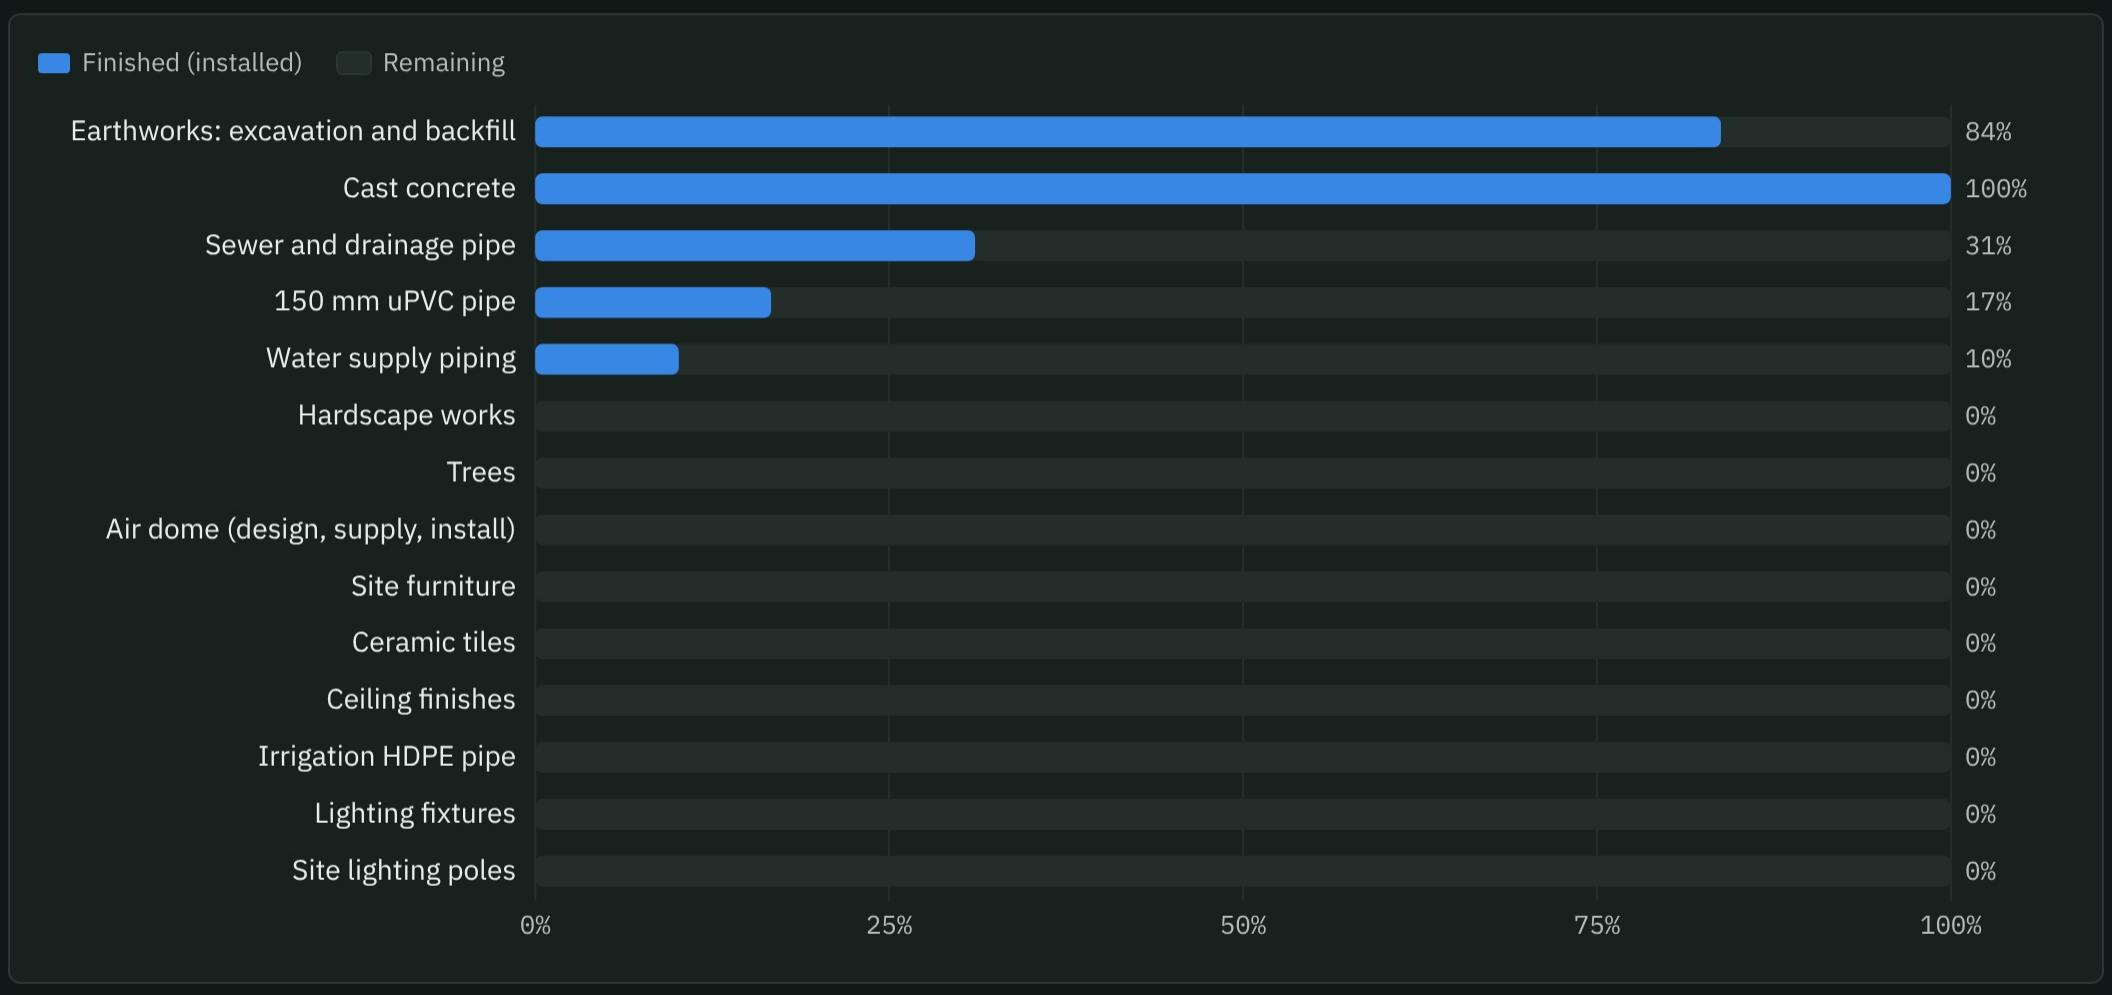

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Earthworks: excavation and backfill	All sites	m³	68,052	57,000	0	11,052	83.8%	–
Cast concrete	All sites	m³	145	145	0	0	100.0%	–
Sewer and drainage pipe	All sites	LM	177	55	0	122	31.1%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
150 mm uPVC pipe	All sites	LM	300	50	0	250	16.7%	–
Water supply piping	All sites	LM	138	14	0	124	10.1%	–
Hardscape works	All sites	m²	30,380	0	0	30,380	0.0%	–
Trees	All sites	EA	895	0	0	895	0.0%	–
Air dome (design, supply, install)	All sites	item	3	0	0	3	0.0%	–
Site furniture	All sites	EA	248	0	0	248	0.0%	–
Ceramic tiles	All sites	m²	219	0	0	219	0.0%	–
Ceiling finishes	All sites	m²	207	0	0	207	0.0%	–
Irrigation HDPE pipe	All sites	LM	7,150	0	0	7,150	0.0%	–
Lighting fixtures	All sites	EA	129	0	0	129	0.0%	–
Site lighting poles	All sites	EA	322	0	0	322	0.0%	–

Work done this week

The weekly summary lists the same ten items as last week: courts ground slab in Asir, air dome foundations and glazed-façade steelwork at all sites, irrigation pipes in Asir and Jeddah, curbs around the Jeddah courts, toilet ceramics and roof insulation, and lighting cables and pole foundations. New this week: stone cladding on the toilets now also finished in Jazan, and the Jazan water tank cast and cured.

Quantities behind the plan to date

Sewer and drainage pipe is still at 55 LM against 177 LM planned to date, 150 mm uPVC pipe at 50 LM against 150 LM, and earthworks at 57,000 m³ against 57,844 m³. Hardscape, trees, the air dome, irrigation pipe and lighting are still at 0 in this sheet, although this week's photos show irrigation pipe, planting beds and lighting pole bases being installed.

Milestones

The weekly report and the P6 update give the same forecast dates for every milestone; the delays are against the baseline. The day counts in brackets are the change from baseline given in the weekly report.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	26-Mar-2026	26-Mar-2026	26-Mar-2026 (actual)	–	✓ Done
Baseline programme approval	29-Apr-2026	29-Apr-2026	29-Apr-2026 (actual)	–	✓ Done
Complete mobilisation	02-Jun-2026	02-Jun-2026	02-Jun-2026 (actual)	–	✓ Done
Levelling works	22-Jul-2026	27-Oct-2026 (+97 d)	27-Oct-2026	11	▼ Late
Engineering	19-Jan-2027	12-Nov-2026 (−68 d)	12-Nov-2026	63	● Ahead of baseline
Toilet building	09-Aug-2026	11-Jan-2027 (+155 d)	11-Jan-2027	12	▼ Late
Playground area	30-Nov-2026	06-May-2027 (+157 d)	06-May-2027	−83	▼ Late
Asir works	13-Dec-2026	05-Apr-2027 (+113 d)	05-Apr-2027	−56	▼ Late
Natural landscape works	16-Jan-2027	18-Mar-2027 (+61 d)	18-Mar-2027	−59	▼ Late
Jazan works	19-Jan-2027	19-May-2027 (+120 d)	19-May-2027	−91	▼ Late
Jeddah works	25-Jan-2027	01-Apr-2027 (+66 d)	01-Apr-2027	−53	▼ Late
Testing & commissioning	29-Apr-2026 *	18-Apr-2027 (+354 d)	18-Apr-2027	−67	▼ Late
Project finish	25-Jan-2027	19-May-2027 (+114 d)	19-May-2027	−91	▼ Late

Jazan sets the finish date.

Jazan works and project completion share the latest forecast, 19-May-2027, at −91 days of float. Every open milestone forecast slipped 7 to 10 days this week; project finish moved from 09-May to 19-May-2027. Open activities with negative float are led by furniture (18), electrical works (15), fixtures (14), air lock doors (12), steel tension cables (11), emergency doors (11) and pressure units (10). * The testing and commissioning baseline of 29-Apr-2026 is as given in the Milestones sheet and appears to be wrong.

Procurement of key materials

Share of total quantity delivered to site. Source: supply tracker in the Procurement Log file of the 26-Oct-2026 report.

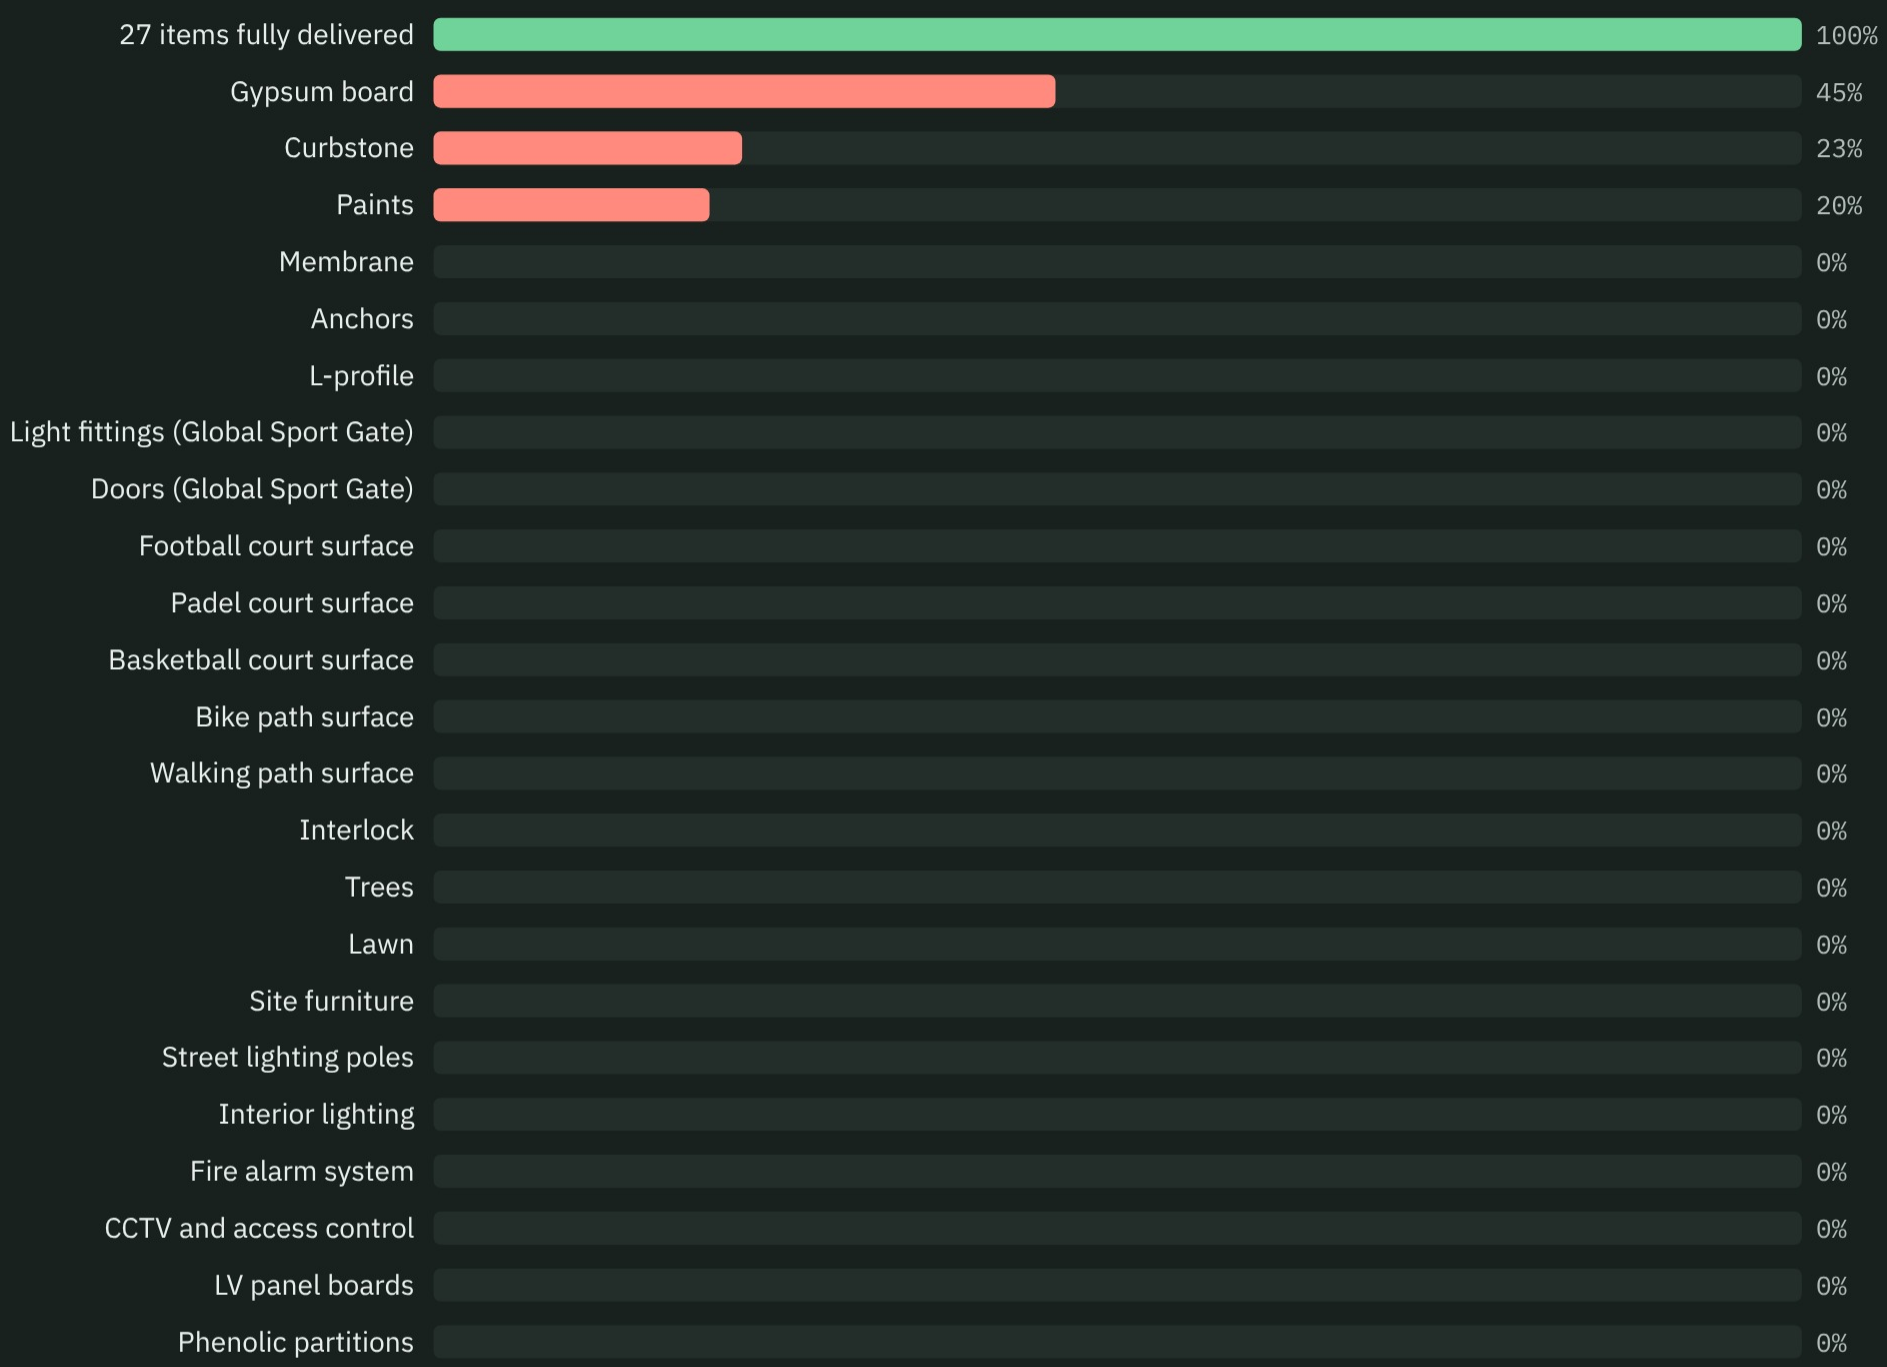

Air dome and sports surfaces: nothing delivered


The 12 Global Sport Gate items (membrane 18,019 m², 1,521 anchors, 1,488 LM of L-profile, 162 light fittings, 24 doors, generators and panels) are still at 0, with supply due from 01-Nov to 25-Dec-2026. Five new rows show the sports surfaces from First Roshn in manufacture for 01-Dec-2026: football 2,982 m², padel 600 m², basketball 1,530 m², bike path 2,896 m² and walking path 2,779.5 m².

Delivered this week and still outstanding

Since the 19-Oct tracker: LV cable is complete (7,700 LM, +3,200), curbstone reached 2,000 of 8,868 LM, stone cladding is complete (258 m²), and gypsum board (90 of 198 m²) and paints (70 of 347 m²) started arriving. Interlock, trees, lawn, site furniture, street lighting poles (in manufacture), interior lighting, fire alarm, CCTV and LV panel boards are still at 0; 37 tracked items have nothing delivered.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

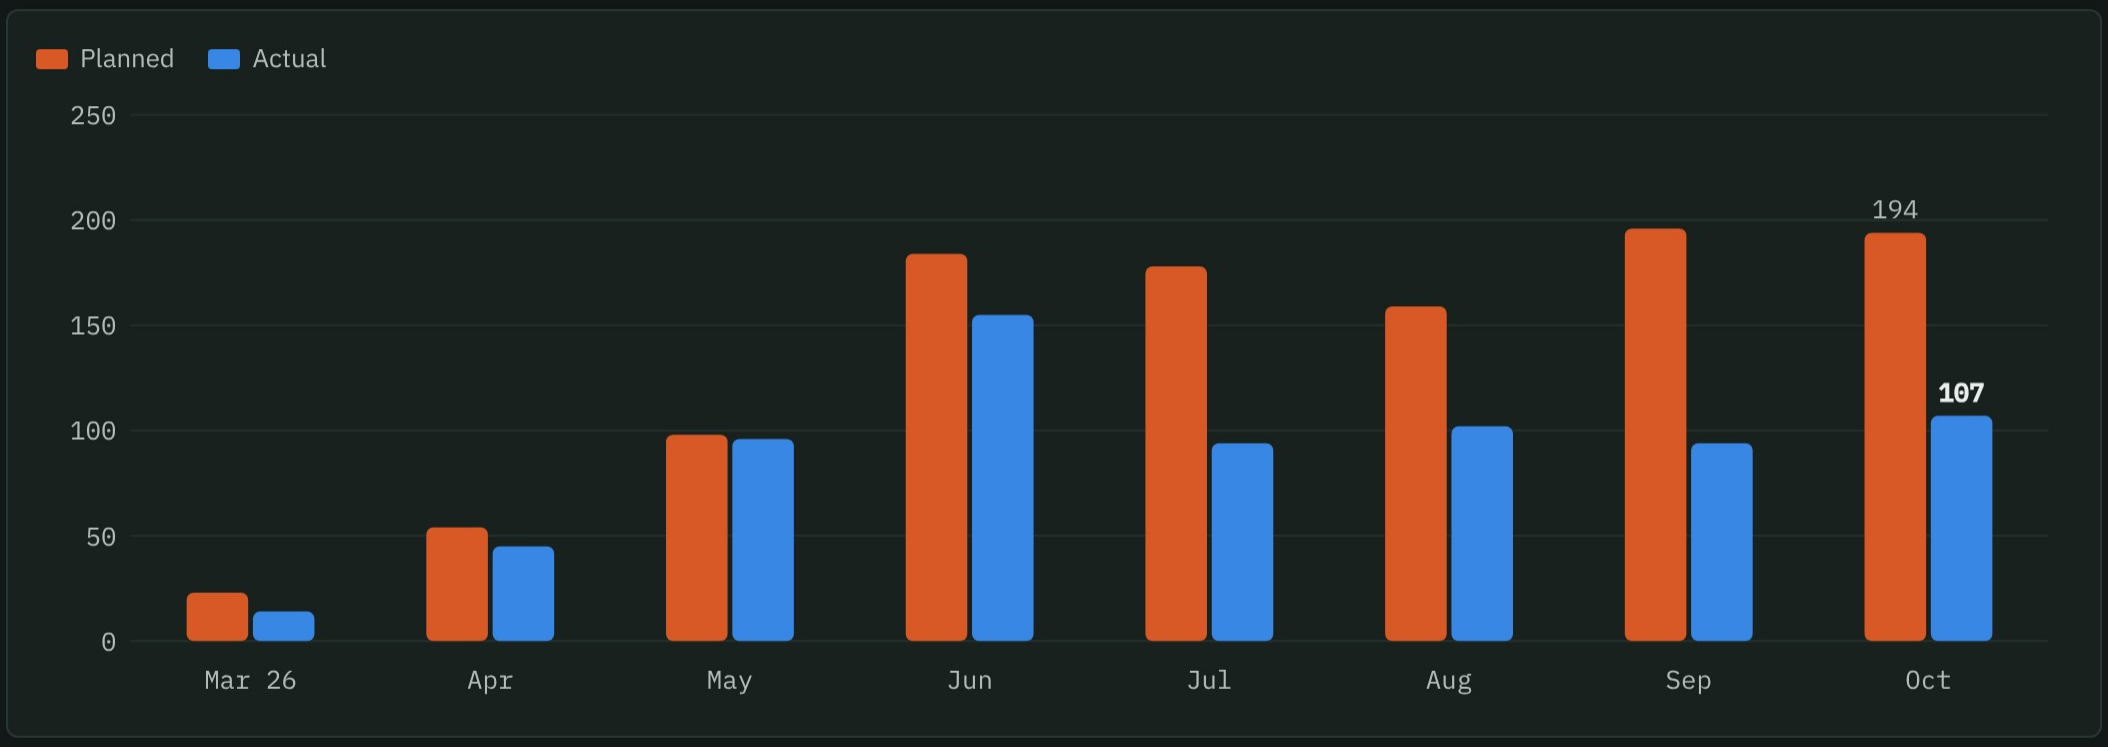

October head count is now 107 against 194 planned (−45%): 77 workers against 175 planned and 30 staff against 19. The monthly sheet shows 27 items of equipment against 27 planned, while the report summary shows 8 against 9.

Cost and invoicing

Contract value

Original contract value	33,997,787
Potential changes	−204,183
Revised contract value	33,793,604
Estimate at completion	33,997,787
Change orders	0

All values in SAR. The Conclusion sheet gives 33,997,787 as including VAT. No change orders are registered.

Invoices

Invoices submitted	5
Gross value	4,943,711
Deductions and penalties	11,000
Net incl. VAT	5,674,267
Approved by MODON PM / paid	0 / 0
FIR value to date	6,488,909

Invoicing is 14.6% of the revised contract value against 44.6% physical progress. No new invoice was submitted this week. All five invoices are approved by the consultant, but none is recorded as approved by the MODON PM or paid.

Health, safety and quality

Safety Score 0.84

Safe man-hours (cumulative)	132,050
Man-hours this week	6,480
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	160 / 156

MODON HSE site inspection 13-Oct-2026 (report no. 13). The safety figures are unchanged from last week.

Quality Score 0.86

FIRs issued / closed	704 / 683
FIRs pending	19
MIRs issued / closed	106 / 103
NCRs issued / closed / pending	23 / 33 / 1
Site instructions issued / closed	27 / 25
Shop drawing submittals processed	141 of 145
Material submittals processed	130 of 147

QC observations checklist no. 26, inspection day 26-Oct-2026. 47 FIRs were issued this week.

Open issues and risks

ISSUE	OWNER	DETAIL
MV cables on the excavation route	Owner	Raised 10-Oct-2026 (Jazan, per the risk and issue log) and still open; its expected closure date of 17-Oct-2026 has passed. Medium-voltage cables conflict with the excavation route; coordination on mitigation is ongoing and the contractor is waiting for the owner's permission.
Air dome supply	Contractor	Still named as the project challenge in the weekly summary. The risk register rates delay in air-dome material delivery High (score 20); mitigation is close follow-up with MODON to speed up approval of the air dome design, target 15-Nov-2026. In P6, for the most critical of the three domes, the PVC membrane, emergency door and lock door approvals have not started and carry −91 days of float.

The risk register is unchanged from last week: 9 open risks, six rated High (air-dome delivery delay, air quality in confined spaces, equipment maintenance and certification, fall protection, heat stress, separation of public traffic), two Medium (unauthorised site entry, unsafe material storage) and one Low (defective tools). The seven earlier issues in the issue log are closed.

Data notes

- The weekly report's headline physical progress jumped from 42.41% to 60.74% (plan 51.03% to 76.10%), with 18.33% "earned this week". The jump comes from a row that this week's total adds and last week's left out: P6's "No W-Construction" group, 84,775.4 planned and 65,538.7 earned man-hours. Its earned value was already 65,538.7 last week, and its 106,595.4-hour budget is not in the 406,255-hour denominator. This report therefore uses the WBS phases only, as last week: 44.6% against 55.2%.
- The report week is the project week counted from site handover (26-Mar-2026 to 26-Oct-2026 is 214 days, week 30). The files carry the serial WPR-26 but state no week number.
- This-week values compare this report with the 19-Oct-2026 report (week 29).
- The weekly summary sheets (files 15 and 16), the Conclusion file (12) and the Tracking Progress file (10) label a cost-based progress figure as "actual". This report uses physical progress (man-hour weighted) only.
- The list of works done this week (files 15 and 16) repeats last week's text almost word for word, and the Major Quantities sheet, invoices, safety statistics and risk register are unchanged from last week.
- File 16 still names a different contractor (شركة الانجاز للتجارة والمقاولات), project manager (عبد الله الشنيفي), sector (القطاع الأوسط), start date 24-Nov-2025 and contract end 23-May-2026.
- The supply summary in the Conclusion file changed its totals from last week (reinforcement 25 to 160 t, concrete 100 to 1,500, interlock 6,400 to 8,044 m², curbstone 17,550 to 8,900 LM) and gives curbstone as 1,900 delivered, against 2,000 of 8,868 LM in the Procurement Log tracker.
- The quality statistics show 33 NCRs closed against 23 issued.
- The Milestones sheet's baseline dates for programme approval (02-Jun-2026), mobilisation (25-Jan-2027) and testing and commissioning (29-Apr-2026) still look shifted, and the Conclusion file still dates project end as 25-Jan-2026.
- The HSE statistics sheet still covers 06–13 Oct 2026 (137,270 cumulative man-hours, 159 toolbox talks), against 132,050 and 156 in the report summary. The invoice log still counts 47 consultant-approved invoices against 5 submitted.
- File 08 is named for the 19-Oct-2026 report (WPR-25) and contains only a title page.

Compiled 01-Nov-2026 from the weekly reports dated 19-Oct-2026 and 26-Oct-2026.
