Improvement of Waad Al Shamal Industrial City Fence & Gates

تسوير المنطقة المطورة بوعد الشمال

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Hamza Mohammad Alderi Construction Co.	Consolidated Consultants Group	Muhammed H. Al-Essa	06-May-2026	05-Oct-2026

Scope: 35,400 m of galvanised chain-link fence with gates and electric gate barriers, an intrusion detection system on fibre-optic cable, three guard houses and external works.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. All work was planned to finish by the contract completion date of 05-Oct-2026, so planned progress is 100%. The project is at 77.1%, behind by 22.9%, after a reported gain of 20.2% this week.

PHYSICAL % COMPLETE
77.1% / 100% plan
▼ SPI 0.77 −22.9%

PROGRESS THIS WEEK
+20.2% / +0.0% plan
● Plan already at 100%

CONTRACT TIME ELAPSED
113.8% · day 173 of 152
▼ P6 finish 26-Nov-2026

INVOICED TO DATE (GROSS)
55.3% · 8.80M SAR
4 invoices, last period ends 05-Oct-2026

The contract completion date has passed with 22.9% of the work still to do.

The contract was due to finish on 05-Oct-2026, three weeks before this data date. The P6 update uploaded with this week's report schedules project finish on 26-Nov-2026, 52 days after the contract date, with −44.5 days of float. The weekly report still forecasts 05-Oct-2026 with no variance. Testing and commissioning, 4% of the man-hours, has not started.

Site photos this week

Six photos from the "Weekly Photos" sheet of the 26-Oct-2026 weekly report. The photos carry no date or GPS stamp. They show backfilling and waterproofing at the guard houses and the MEP final fix inside the rooms. Select a photo to view it larger, then use the arrows to move between photos.



Backfilling works

Backfilling against a guard-house wall.



Waterproofing works

Bituminous membrane being applied around a pipe and a box.



Rooms MEP final fix

Final fix under way inside a guard-house room.



Rooms MEP final fix

Ceiling light fittings and a split AC unit installed.



Rooms MEP final fix

Light fittings installed; the AC unit is still wrapped.




Rooms MEP final fix

Exhaust fan fixed to the wall and being connected.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

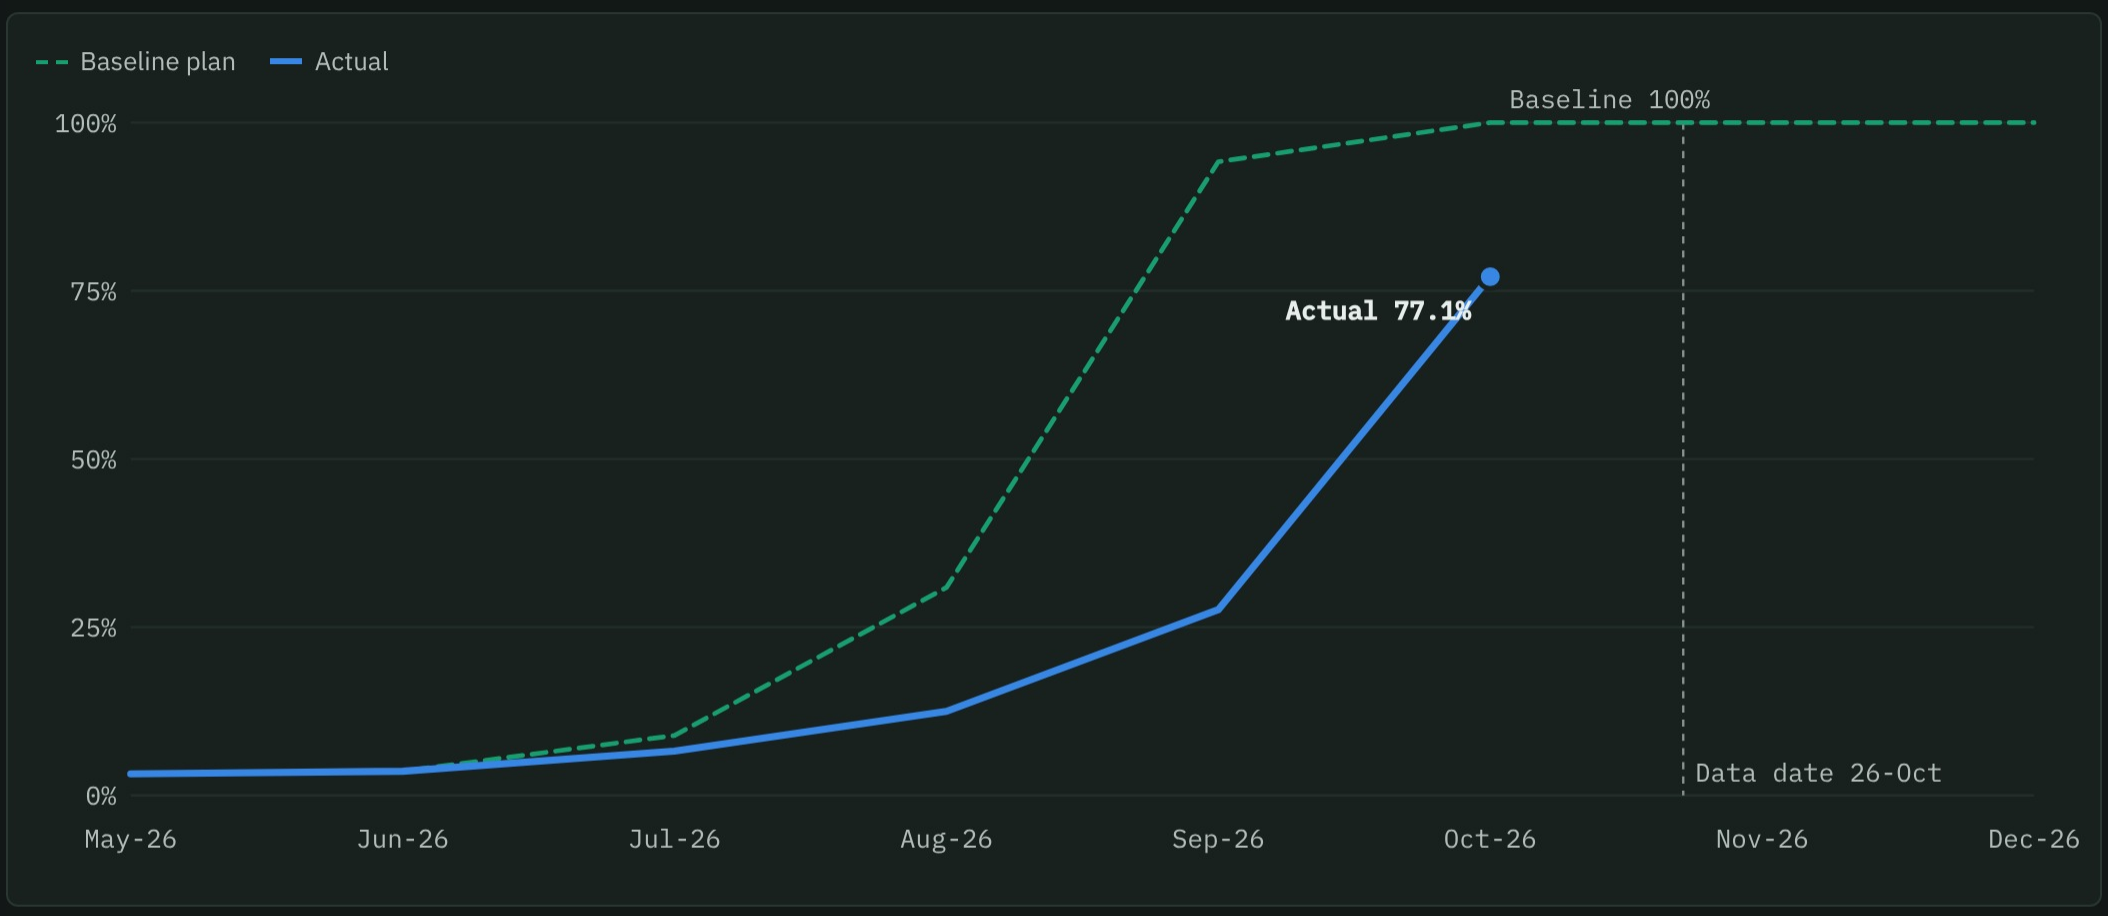

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
Previous report	100.0	56.9	-43.1%	—	0.57
26-Oct-2026	**100.0**	**77.1**	**-22.9%**	**+20.2%**	**0.77**

Physical % complete from the 26-Oct-2026 weekly report. The previous figure is that report's "Previous week Effort" column. No earlier weekly report has been uploaded, so earlier weeks are not shown.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5%	100.0%	74.8%	-25.2%	0.75	▼ Behind
Procurement	13%	100.0%	90.4%	-9.6%	0.90	▼ Behind
Construction	75%	100.0%	78.2%	-21.8%	0.78	▼ Behind
· Fences	5.0%	100.0%	83.0%	-17.0%	0.83	▼ Behind
· Guard house 1	22.6%	100.0%	78.1%	-21.9%	0.78	▼ Behind
· Guard house 2	22.6%	100.0%	77.3%	-22.7%	0.77	▼ Behind
· Guard house 3	22.6%	100.0%	77.8%	-22.2%	0.78	▼ Behind
· External works	2.2%	100.0%	80.0%	-20.0%	0.80	▼ Behind
Testing & commissioning	4%	100.0%	0.0%	-100.0%	0.00	▼ Not started
Total	100%	**100.0%**	**77.1%**	**-22.9%**	**0.77**	▼ Behind

Weights are shares of the 98,544 budgeted man-hours; the construction items (·) are part of Construction. This week Construction gained 22.3%, Procurement 20.1% and Engineering 16.8% of their own man-hours. The P6 update (data date 26-Oct-2026) has 554 activities: 309 completed, 137 in progress and 108 not started.

Milestones

Baseline dates from the P6 schedule print-out, weekly report forecasts from its Milestones sheet, and P6 forecasts and float from the P6 update (data date 26-Oct-2026).


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	06-May-2026	06-May-2026	07-Jul-2026 (actual)	–	✓ Done
Complete mobilisation	31-May-2026	06-May-2026	09-Jul-2026 (actual)	–	✓ Done
Complete fences	26-Aug-2026	–	27-Oct-2026	-18.0	▼ Late
Complete guard house 1	26-Aug-2026	–	27-Oct-2026	-18.0	▼ Late
Complete engineering	22-Sep-2026	22-Sep-2026	28-Oct-2026	-19.5	▼ Late
Complete external works	27-Sep-2026	–	08-Nov-2026	-28.9	▼ Late
Complete procurement	28-Sep-2026	28-Sep-2026	07-Nov-2026	-27.3	▼ Late
Testing & commissioning	05-Oct-2026	05-Oct-2026	11-Nov-2026	-31.6	▼ Late
Project finish	05-Oct-2026	05-Oct-2026	26-Nov-2026	-44.5	▼ Late

The weekly report's forecasts are already in the past.

The weekly report forecasts engineering, procurement and completion on their baseline dates (22-Sep, 28-Sep and 05-Oct-2026), all before the 26-Oct data date, and none is marked achieved. The P6 update moves every open milestone to between 27-Oct and 26-Nov-2026, with float from –18 to –44.5 days. It also records site handover on 07-Jul-2026, not 06-May-2026.

Manpower

Monthly head count on site, planned vs actual (staff plus labour). Source: Manpower sheet.

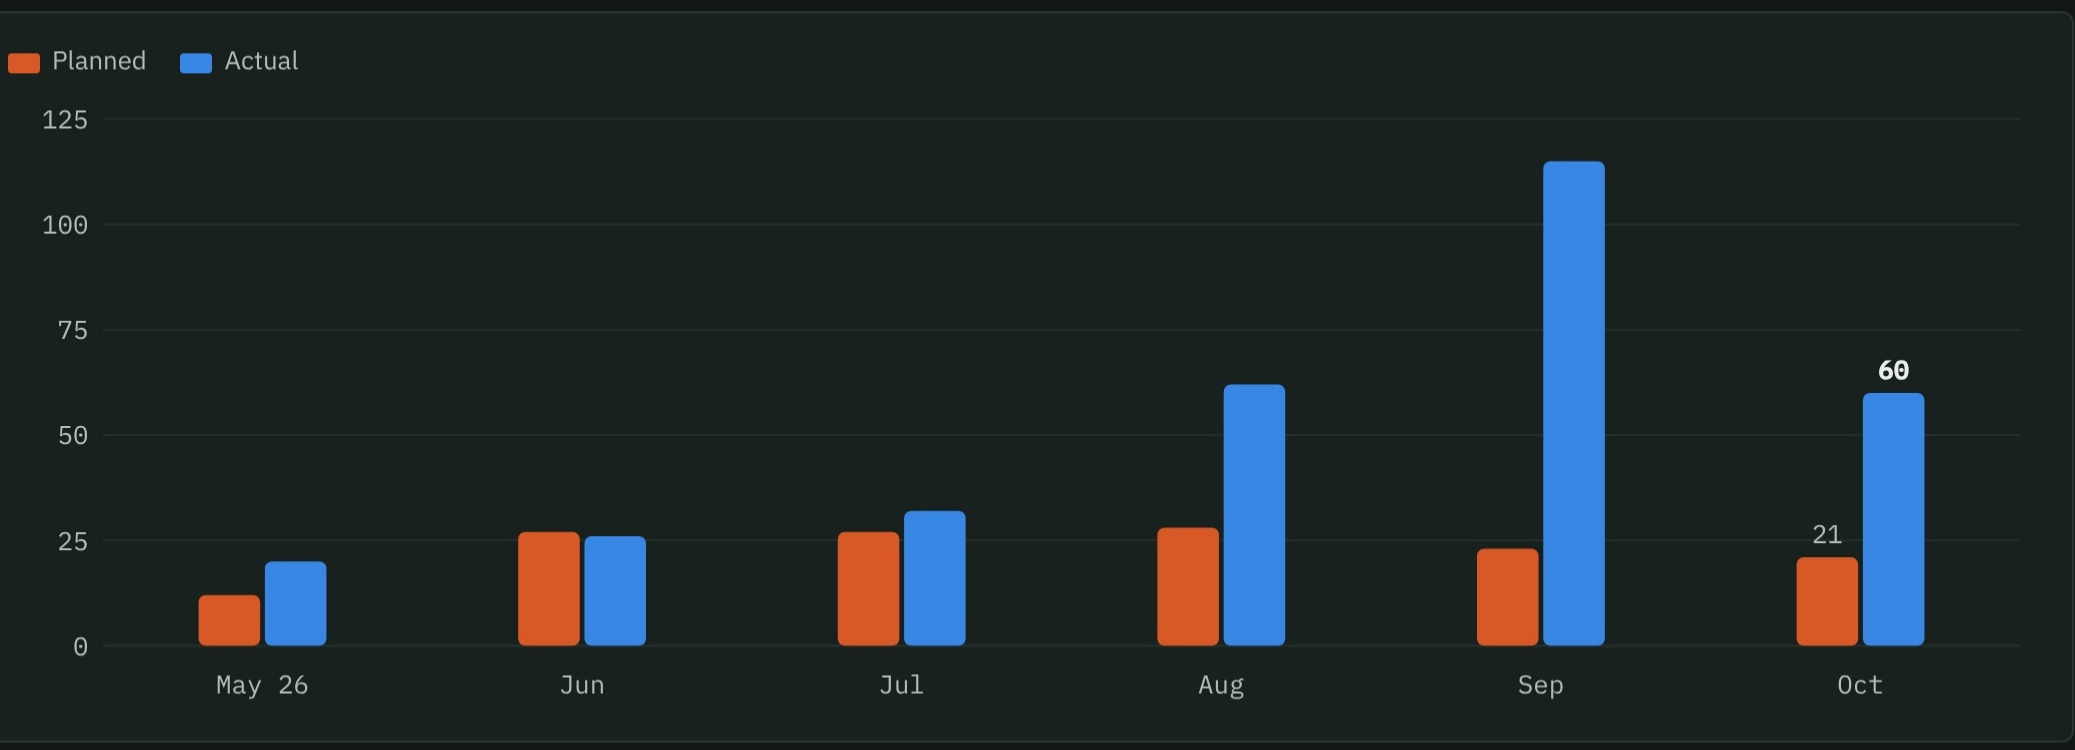

October head count is 60 (10 staff, 50 labour) against 21 planned. Actual head count has been above plan since July and peaked at 115 in September. Equipment on site is 9 against 4 planned.

Cost and invoicing

Contract value

Original contract value	15,898,659
Revised contract value	15,898,659
Change orders	0
Potential changes	0

All values in SAR. The contract change order log is empty. The invoice log header shows different values; see Data notes.

Invoices

Invoices submitted	4
Gross value	8,797,318
Approved by CM / PgM	4
Approved by MODON PM	0
Paid	0
Net incl. VAT	9,756,785

Invoicing is 55.3% of the contract value against 77.1% physical progress. The last invoice covers 25-Sep to 05-Oct-2026. No retention, advance payment or deduction is recorded.

Health, safety and quality

Safety Score 0.85

Safe man-hours (cumulative)	42,116
Man-hours this week	6,138
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	23 / 24

Sessions to date: 137 attended inductions and 360 attended toolbox talks.

Quality Score 0.86

NCRs issued (cumulative)	0
Site instructions	0
FIRs issued / closed	485 / 420
FIRs pending	65
MIRs issued / closed	64 / 57
MIRs pending	7
Shop drawings: code A / B / D	11 / 26 / 1
Material submittals	94

Consultant QC observation No. 17, 24-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Contract date passed	Contractor	The contract was due to finish on 05-Oct-2026. At 26-Oct-2026 the work is 77.1% complete and P6 schedules finish on 26-Nov-2026, with –44.5 days of float.
Materials approval and delivery	Contractor	Open risk in the register since 06-Jun-2026: delay in materials approval and delivery could delay completion. The treatment (expedite approvals and deliveries) was due 23-Oct-2026 and is still open, rated very high.
Guard-house materials	Contractor	In P6, 100 of 147 procurement activities are still in progress, including doors, windows, panel boards, UPS, CCTV and access control, all with float between –18.8 and –44.5 days.
Testing and commissioning	Contractor	Not started. Planned for 26-Sep to 05-Oct-2026; P6 now forecasts the milestone on 11-Nov-2026.
Invoice approval	MODON	Four invoices (8.80M SAR gross) are approved by the CM / PgM, but none is recorded as approved by the MODON PM or paid.

The weekly report's issue log and top-5 issues are empty. The risk register holds one open risk.

Data notes

- No earlier weekly report has been uploaded for this project. The previous-week figure (56.9%) and this week's gain (20.2%) come from the 26-Oct report's own "Previous week Effort" column. A gain of 20.2% in one week is unusually large: the monthly S-curve data shows 27.6% in September and 77.1% in October. Please confirm.
- The weekly report gives 05-Oct-2026 as the forecast completion with 0 days of variance, although the data date is 26-Oct-2026. The P6 update schedules 26-Nov-2026.
- Site handover is 06-May-2026 in the weekly report but 07-Jul-2026 in the P6 update. The week number (24) counts from 06-May-2026.
- The P6 update records actual start or finish dates after its 26-Oct-2026 data date for 107 activities (up to 24-Nov-2026), so its progress status is not reliable.
- Activity counts differ: the weekly report shows 195 completed, 123 in progress and 236 not started; the P6 update shows 309, 137 and 108.
- The P6 print-out labels a cost-based progress figure as "Actual %". This report uses physical (man-hour) progress only.
- The "Two Week Look Ahead" print-out covers 28-Sep to 05-Oct-2026, before the data date.
- Several sheets hold another project's data: Major Quantities (sewer, storm and water items dated 2024), the lower table of the Milestones sheet (SUD1-05-015) and Sheet1 (KUMT-05-001). The Procurement sheet's P6 activity column shows KHJ1-05010. The scope quantities section is therefore left out.
- The Procurement sheet marks 156 of 166 items as delivered, with no quantities delivered, while P6 shows most procurement activities still in progress. The procurement section is left out until the two agree.
- The invoice log header shows a revised contract value of 21,100,000 SAR, an estimate at completion of 20,900,000 SAR and potential changes of 200,000 SAR; all other sheets show 15,898,659.13 SAR and 0. Invoice 4's net amount incl. VAT repeats invoice 3's (2,864,258.52 SAR).
- Labour by trade totals 50 in the Weekly Progress Report sheet and 109 in the Manpower sheet.
- The Weekly Progress Report sheet shows MIRs and FIRs shifted by one column (57 / 7 and 420 / 65); the Quality-Stat sheet gives 64 issued, 57 closed, 7 pending and 485, 420, 65.
- Cumulative man-hours are 42,166 but safe man-hours 42,116, although no incident is recorded. The safety score is 0.85 in the summary and 0.88 for the consultant's 24-Oct inspection.
- The DB sheet shows #REF ! for the project scope and for several key dates.

Compiled 01-Nov-2026 from the weekly report, P6 update and schedule print-outs uploaded for the week of 22-Oct-2026 (data date 26-Oct-2026).
