
Construction of a SAR Train Passenger Drop-Off Station in Sudair

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SUD1-05-018-1	Project:PASSENGER STATION FOR SAR RAILWAY - PA	194	07-Jul-26	07-Jan-27	03-Aug-26 A	19-Dec-26	24.59%	21.37%
SUD1-05-018-1.5	Construction	194	07-Jul-26	07-Jan-27	03-Aug-26 A	19-Dec-26	24.59%	21.37%
SUD1-05-018-1.5.1	Package-1	194	03-Aug-26	07-Jan-27	03-Aug-26 A	19-Dec-26	23.09%	21.79%
SUD1-05-018-1.5.1.15	ROAD WORKS 1	167	15-Oct-26	06-Dec-26	07-Sep-26 A	14-Dec-26	17.32%	18.42%
SUD1-05-018-1.5.1.15.8	ROAD - 01	45	31-Oct-26	06-Dec-26	11-Oct-26 A	02-Dec-26	3.12%	14.48%
SUD1-05-018-1.5.1.15.8.6	ROAD-01 From 0 to 470 m (3)	45	05-Nov-26	29-Nov-26	11-Oct-26 A	02-Dec-26	3.11%	54.78%
SUD1-05-018-1.5.1.15.8.6.3	Asphalt Works	6	21-Nov-26	29-Nov-26	11-Oct-26 A	15-Nov-26	0%	70%
SUD1-05-018-1.5.1.15.8.6.3.1	Bituminous base course	6	21-Nov-26	29-Nov-26	11-Oct-26 A	15-Nov-26	0%	70%
SDR-ST-COI	Bituminous base course (Grading I - Class A 1st Layer wit	6	21-Nov-26	29-Nov-26	11-Oct-26 A	15-Nov-26	0%	70%
SUD1-05-018-1.5.1.15.8.6.4	Kerbstone Installation	21	05-Nov-26	29-Nov-26	09-Nov-26	02-Dec-26	14.29%	0%
SDR-ST-CON-F	Precast Concrete Curbstone, Type A2	21	05-Nov-26	29-Nov-26	09-Nov-26	02-Dec-26	14.29%	0%
SUD1-05-018-1.5.1.15.8.7	ROAD-01 From 470 to 1125 m (6)	20	09-Nov-26	01-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SUD1-05-018-1.5.1.15.8.7.3	Asphalt Works	6	22-Nov-26	28-Nov-26	09-Nov-26	15-Nov-26	0%	0%
SUD1-05-018-1.5.1.15.8.7.3.1	Bituminous base course	6	22-Nov-26	28-Nov-26	09-Nov-26	15-Nov-26	0%	0%
SDR-ST-COI	Bituminous base course (Grading I - Class A 1st Layer wit	6	22-Nov-26	28-Nov-26	09-Nov-26	15-Nov-26	0%	0%
SUD1-05-018-1.5.1.15.8.7.4	Kerbstone Installation	20	09-Nov-26	01-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-ST-CON-F	Precast Concrete Curbstone, Type A2	20	09-Nov-26	01-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SUD1-05-018-1.5.1.15.8.9	ROAD-01 From 1125 to 1765 m (7)	20	31-Oct-26	06-Dec-26	09-Nov-26	01-Dec-26	4.88%	0%
SUD1-05-018-1.5.1.15.8.9.3	Asphalt Works	11	17-Nov-26	06-Dec-26	09-Nov-26	21-Nov-26	0%	0%
SUD1-05-018-1.5.1.15.8.9.3.1	Bituminous base course	11	17-Nov-26	06-Dec-26	09-Nov-26	21-Nov-26	0%	0%
SDR-ST-COI	Bituminous base course (Grading I - Class A 1st Layer wit	6	17-Nov-26	25-Nov-26	09-Nov-26	15-Nov-26	0%	0%
SDR-ST-COI	Bituminous base course (Grading I - Class A 2nd layer wi	5	26-Nov-26	06-Dec-26	16-Nov-26	21-Nov-26	0%	0%
SUD1-05-018-1.5.1.15.8.9.4	Kerbstone Installation	20	31-Oct-26	22-Nov-26	09-Nov-26	01-Dec-26	40%	0%
SDR-ST-CON-F	Precast Concrete Curbstone, Type A2	20	31-Oct-26	22-Nov-26	09-Nov-26	01-Dec-26	40%	0%
SUD1-05-018-1.5.1.15.6	ROAD - 02	135	15-Oct-26	26-Nov-26	07-Sep-26 A	14-Dec-26	72.04%	33.57%
SUD1-05-018-1.5.1.15.6.1	ROAD-01 From 0 to 400 m (9)	13	15-Oct-26	29-Oct-26	07-Sep-26 A	23-Nov-26	100%	80%
SUD1-05-018-1.5.1.15.6.1.11	Subgrade	13	15-Oct-26	29-Oct-26	07-Sep-26 A	23-Nov-26	100%	80%
SDR-ST-CON-F	Subgrade layer works	13	15-Oct-26	29-Oct-26	07-Sep-26 A	23-Nov-26	100%	80%
SUD1-05-018-1.5.1.15.6.2	ROAD-01 From 400 to 900 m (10)	132	19-Oct-26	26-Nov-26	07-Sep-26 A	14-Dec-26	48.22%	23.44%
SUD1-05-018-1.5.1.15.6.2.11	Subgrade	11	19-Oct-26	03-Nov-26	07-Sep-26 A	21-Nov-26	100%	75%
SDR-ST-CON-F	Subgrade layer works	11	19-Oct-26	03-Nov-26	07-Sep-26 A	21-Nov-26	100%	75%
SUD1-05-018-1.5.1.15.6.2.2	Base Course	10	04-Nov-26	19-Nov-26	22-Nov-26	02-Dec-26	28.57%	0%
SDR-ST-CON-F	Aggregate base course layer	10	04-Nov-26	19-Nov-26	22-Nov-26	02-Dec-26	28.57%	0%
SUD1-05-018-1.5.1.15.6.2.4	Kerbstone Installation	20	04-Nov-26	26-Nov-26	22-Nov-26	14-Dec-26	20%	0%
SDR-ST-CON-F	Precast Concrete Curbstone, Type A2	20	04-Nov-26	26-Nov-26	22-Nov-26	14-Dec-26	20%	0%
SUD1-05-018-1.5.1.15.6.3	ROAD-01 From 900 to 1239 m (11)	131	18-Oct-26	09-Nov-26	07-Sep-26 A	25-Nov-26	93.93%	27.22%
SUD1-05-018-1.5.1.15.6.3.11	Subgrade	8	18-Oct-26	29-Oct-26	07-Sep-26 A	17-Nov-26	100%	60%
SDR-ST-CON-F	Subgrade layer works	8	18-Oct-26	29-Oct-26	07-Sep-26 A	17-Nov-26	100%	60%
SUD1-05-018-1.5.1.15.6.3.2	Base Course	7	31-Oct-26	09-Nov-26	18-Nov-26	25-Nov-26	88.89%	0%
SDR-ST-CON-F	Aggregate base course layer	7	31-Oct-26	09-Nov-26	18-Nov-26	25-Nov-26	88.89%	0%
SUD1-05-018-1.5.1.12	ELECTRICAL WORKS	127	03-Aug-26	24-Dec-26	03-Aug-26 A	19-Dec-26	94.46%	58.09%
SUD1-05-018-1.5.1.12.2	MV Network	32	28-Sep-26	07-Nov-26	04-Nov-26 A	15-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5	ROAD - 01	32	28-Sep-26	07-Nov-26	04-Nov-26 A	15-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.4	ROAD-01 From 1125 to 1765 m (7)	21	28-Sep-26	21-Oct-26	08-Nov-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.4.6	Excavation	21	28-Sep-26	21-Oct-26	08-Nov-26 A	02-Dec-26	100%	100%
SDR-ST-COI	Excavation Works Part 1	21	28-Sep-26	21-Oct-26	08-Nov-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.3	ROAD-01 From 470 to 1125 m (6)	21	06-Oct-26	29-Oct-26	07-Nov-26 A	09-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.3.6	Excavation	21	06-Oct-26	29-Oct-26	07-Nov-26 A	09-Dec-26	100%	100%
SDR-ST-COI	Excavation Works Part 1	21	06-Oct-26	29-Oct-26	07-Nov-26 A	09-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.2	ROAD-01 N 03	21	14-Oct-26	07-Nov-26	04-Nov-26 A	15-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.2.5.2.6	Excavation	21	14-Oct-26	07-Nov-26	04-Nov-26 A	15-Dec-26	100%	100%
SDR-ST-COI	Excavation Works Part 1	21	14-Oct-26	07-Nov-26	04-Nov-26 A	15-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.16	Street Lighting Network	109	03-Aug-26	28-Nov-26	03-Aug-26 A	05-Dec-26	92.72%	43.69%
SUD1-05-018-1.5.1.12.16.7	ROAD - 01	109	03-Aug-26	28-Nov-26	03-Aug-26 A	05-Dec-26	90.32%	47.88%
SUD1-05-018-1.5.1.12.16.7.2	ROAD-01 From 470 to 1125 m (6)	88	03-Aug-26	18-Oct-26	03-Aug-26 A	02-Dec-26	100%	56.67%
SUD1-05-018-1.5.1.12.16.7.2.10	Excavation	88	03-Aug-26	18-Oct-26	03-Aug-26 A	02-Dec-26	100%	56.67%
SDR-ST-COI	Excavation for LV Cable trench Section 3	21	24-Sep-26	18-Oct-26	05-Nov-26 A	02-Dec-26	100%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 2	21	30-Aug-26	22-Sep-26	05-Nov-26 A	02-Dec-26	100%	50%

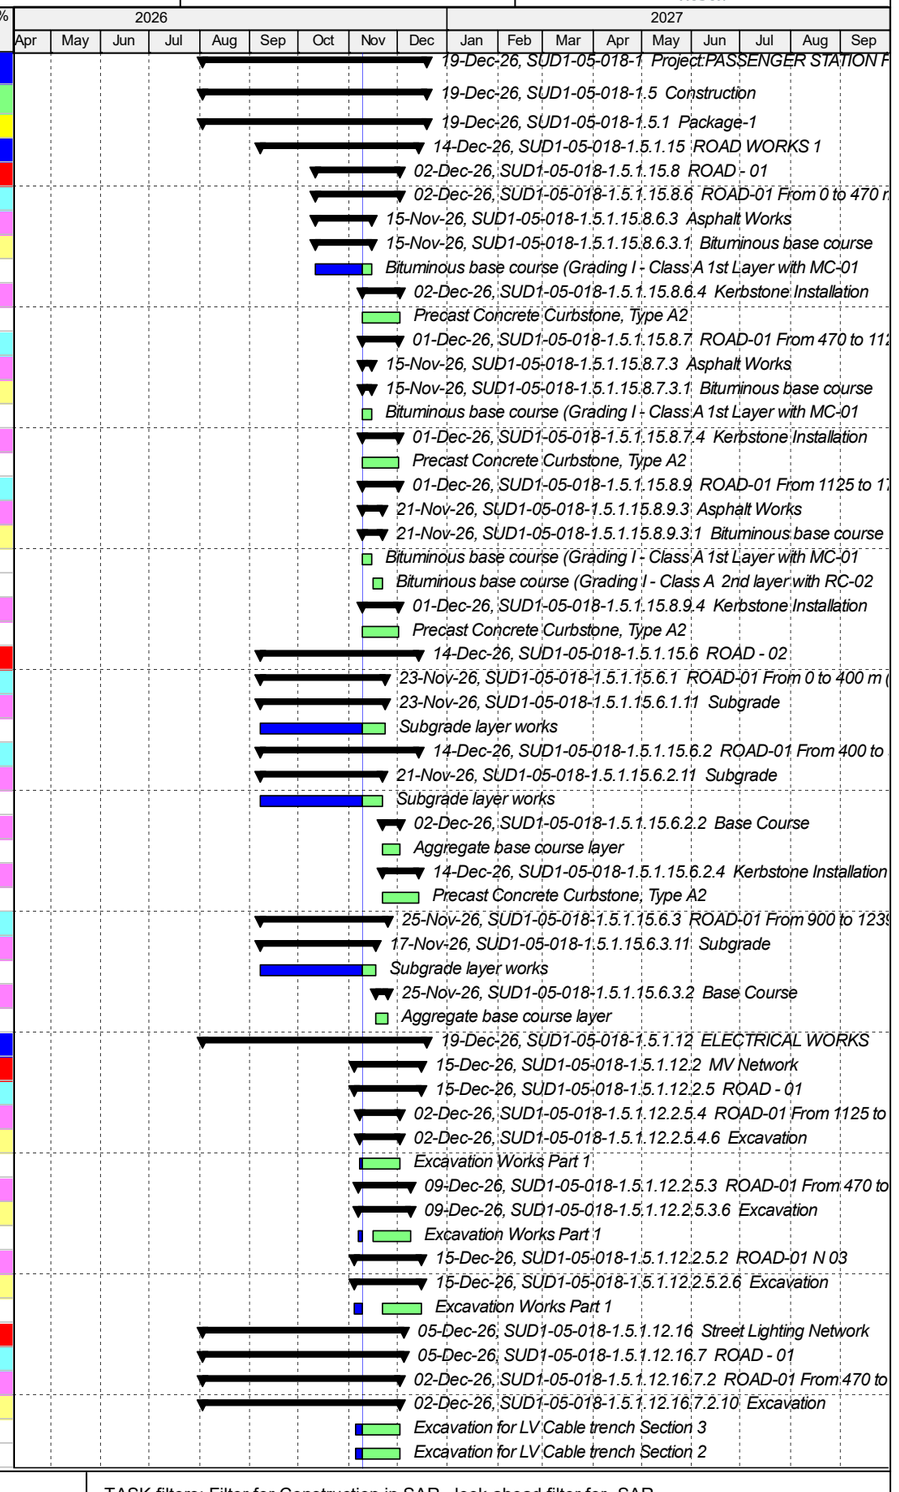

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filters: Filter for Construction in SAR , look ahead filter for -SAR.

© Oracle Corporation

Construction of a SAR Train Passenger Drop-Off Station in Sudair

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-ST-COI	Excavation for LV Cable trench Section 1	21	03-Aug-26	26-Aug-26	03-Aug-26 A	01-Dec-26	100%	70%
SUD1-05-018-1.5.1.12.16.7.3	ROAD-01 From 1125 to 1765 m (7)	21	27-Aug-26	20-Sep-26	03-Aug-26 A	01-Dec-26	100%	70%
SUD1-05-018-1.5.1.12.16.7.3.10	Excavation	21	27-Aug-26	20-Sep-26	03-Aug-26 A	01-Dec-26	100%	70%
SDR-ST-COI	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	03-Aug-26 A	01-Dec-26	100%	70%
SUD1-05-018-1.5.1.12.16.7.1	ROAD-01 From 0 to 470 m (3)	109	27-Aug-26	09-Nov-26	05-Sep-26 A	02-Dec-26	98.41%	56.67%
SUD1-05-018-1.5.1.12.16.7.1.10	Excavation	109	27-Aug-26	09-Nov-26	05-Sep-26 A	02-Dec-26	98.41%	56.67%
SDR-ST-COI	Excavation for LV Cable trench Section 3	21	17-Oct-26	09-Nov-26	03-Nov-26 A	02-Dec-26	95.24%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 2	21	21-Sep-26	15-Oct-26	04-Nov-26 A	02-Dec-26	100%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	05-Sep-26 A	02-Dec-26	100%	70%
SUD1-05-018-1.5.1.12.16.7.4	ROAD-01 N (1)	23	27-Aug-26	11-Nov-26	04-Nov-26 A	05-Dec-26	95.24%	50%
SUD1-05-018-1.5.1.12.16.7.4.10	Excavation	23	27-Aug-26	11-Nov-26	04-Nov-26 A	05-Dec-26	95.24%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 3	21	19-Oct-26	11-Nov-26	04-Nov-26 A	05-Dec-26	85.71%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 2	21	24-Sep-26	18-Oct-26	05-Nov-26 A	05-Dec-26	100%	50%
SDR-ST-COI	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	05-Nov-26 A	02-Dec-26	100%	50%
SUD1-05-018-1.5.1.12.16.7.5	Road Crossing & Drawpits	21	27-Aug-26	28-Nov-26	09-Nov-26	02-Dec-26	44.62%	0%
SUD1-05-018-1.5.1.12.16.7.5.1	ROAD - 01	21	27-Aug-26	28-Nov-26	09-Nov-26	02-Dec-26	44.62%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.1	ROAD-01 From 470 to 1125 m (6)	13	02-Nov-26	16-Nov-26	09-Nov-26	23-Nov-26	28.99%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.1.1	Road crossing Ducts & Drawpits	13	02-Nov-26	16-Nov-26	09-Nov-26	23-Nov-26	28.99%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.1.1.6	Testing	7	02-Nov-26	09-Nov-26	09-Nov-26	16-Nov-26	86.96%	0%
SDR-	Testing ST GRP Pipes	7	02-Nov-26	09-Nov-26	09-Nov-26	16-Nov-26	85.71%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.1.1.3	Backfilling	6	10-Nov-26	16-Nov-26	17-Nov-26	23-Nov-26	0%	0%
SDR-	Backfilling ST GRP Pipes	6	10-Nov-26	16-Nov-26	17-Nov-26	23-Nov-26	0%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.3	ROAD-01 From 0 to 470 m (3)	17	01-Nov-26	28-Nov-26	09-Nov-26	28-Nov-26	23.33%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.3.1	Road crossing Ducts & Drawpits	17	01-Nov-26	28-Nov-26	09-Nov-26	28-Nov-26	23.33%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.3.1.6	Testing	6	01-Nov-26	11-Nov-26	09-Nov-26	15-Nov-26	70%	0%
SDR-	Testing ST GRP Pipes	6	01-Nov-26	11-Nov-26	09-Nov-26	15-Nov-26	70%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.3.1.3	Backfilling	10	14-Nov-26	28-Nov-26	17-Nov-26	28-Nov-26	0%	0%
SDR-	Backfilling ST GRP Pipes	10	14-Nov-26	28-Nov-26	17-Nov-26	28-Nov-26	0%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.4	ROAD-01 N (1)	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.4.1	Road crossing Ducts & Drawpits	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.16.7.5.1.4.1.1	Excavation	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.16.8	ROAD - 02	23	13-Aug-26	14-Nov-26	22-Oct-26 A	05-Dec-26	97.03%	36.2%
SUD1-05-018-1.5.1.12.16.8.6	ROAD-01 From 0 to 400 m (9) 2 Way 110 mm	15	15-Aug-26	31-Aug-26	04-Nov-26 A	25-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.6.10	Excavation	15	15-Aug-26	31-Aug-26	04-Nov-26 A	25-Nov-26	100%	30%
SDR-ST-COI	Excavation for LV Cable trench Section 1	15	15-Aug-26	31-Aug-26	04-Nov-26 A	25-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.5	ROAD-01 From 400 to 900 m (10) 4 Way 110 mm	15	13-Aug-26	07-Oct-26	01-Nov-26 A	25-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.5.10	Excavation	15	13-Aug-26	07-Oct-26	01-Nov-26 A	25-Nov-26	100%	30%
SDR-ST-COI	Excavation for LV Cable trench Section 3	15	20-Sep-26	07-Oct-26	01-Nov-26 A	25-Nov-26	100%	30%
SDR-ST-COI	Excavation for LV Cable trench Section 2	15	02-Sep-26	19-Sep-26	01-Nov-26 A	25-Nov-26	100%	30%
SDR-ST-COI	Excavation for LV Cable trench Section 1	15	13-Aug-26	30-Aug-26	01-Nov-26 A	25-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.4	ROAD-01 From 900 to 1239 m (11) 2 Way 110 mm	14	27-Aug-26	12-Sep-26	05-Nov-26 A	24-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.4.10	Excavation	14	27-Aug-26	12-Sep-26	05-Nov-26 A	24-Nov-26	100%	30%
SDR-ST-COI	Excavation for LV Cable trench Section 1	14	27-Aug-26	12-Sep-26	05-Nov-26 A	24-Nov-26	100%	30%
SUD1-05-018-1.5.1.12.16.8.1	Road Crossing & Drawpits	23	13-Aug-26	14-Nov-26	22-Oct-26 A	05-Dec-26	87.01%	57.14%
SUD1-05-018-1.5.1.12.16.8.1.2	ROAD - 02	23	13-Aug-26	14-Nov-26	22-Oct-26 A	05-Dec-26	87.01%	57.14%
SUD1-05-018-1.5.1.12.16.8.1.2.1	ROAD-01 From 0 to 400 m (9) 2 Way 110 mm	23	19-Oct-26	14-Nov-26	09-Nov-26	05-Dec-26	69.7%	0%
SUD1-05-018-1.5.1.12.16.8.1.2.1.1	Road crossing Ducts & Drawpits	23	19-Oct-26	14-Nov-26	09-Nov-26	05-Dec-26	69.7%	0%
SUD1-05-018-1.5.1.12.16.8.1.2.1.1.6	Testing	12	19-Oct-26	01-Nov-26	09-Nov-26	22-Nov-26	100%	0%
SDR-	Testing ST GRP Pipes	12	19-Oct-26	01-Nov-26	09-Nov-26	22-Nov-26	100%	0%
SUD1-05-018-1.5.1.12.16.8.1.2.1.1.3	Backfilling	11	02-Nov-26	14-Nov-26	23-Nov-26	05-Dec-26	54.55%	0%
SDR-	Backfilling ST GRP Pipes	11	02-Nov-26	14-Nov-26	23-Nov-26	05-Dec-26	54.55%	0%
SUD1-05-018-1.5.1.12.16.8.1.2.2	ROAD-01 From 400 to 900 m (10) 4 Way 110 mm	21	13-Aug-26	06-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.16.8.1.2.2.1	Road crossing Ducts & Drawpits	21	13-Aug-26	06-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.16.8.1.2.2.1.1	Excavation	21	13-Aug-26	06-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SDR-	Excavation for GRP Pipes Section 1	21	13-Aug-26	06-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.16.8.1.2.3	ROAD-01 From 900 to 1239 m (11) 2 Way 110 m	21	27-Aug-26	20-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.16.8.1.2.3.1	Road crossing Ducts & Drawpits	21	27-Aug-26	20-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%

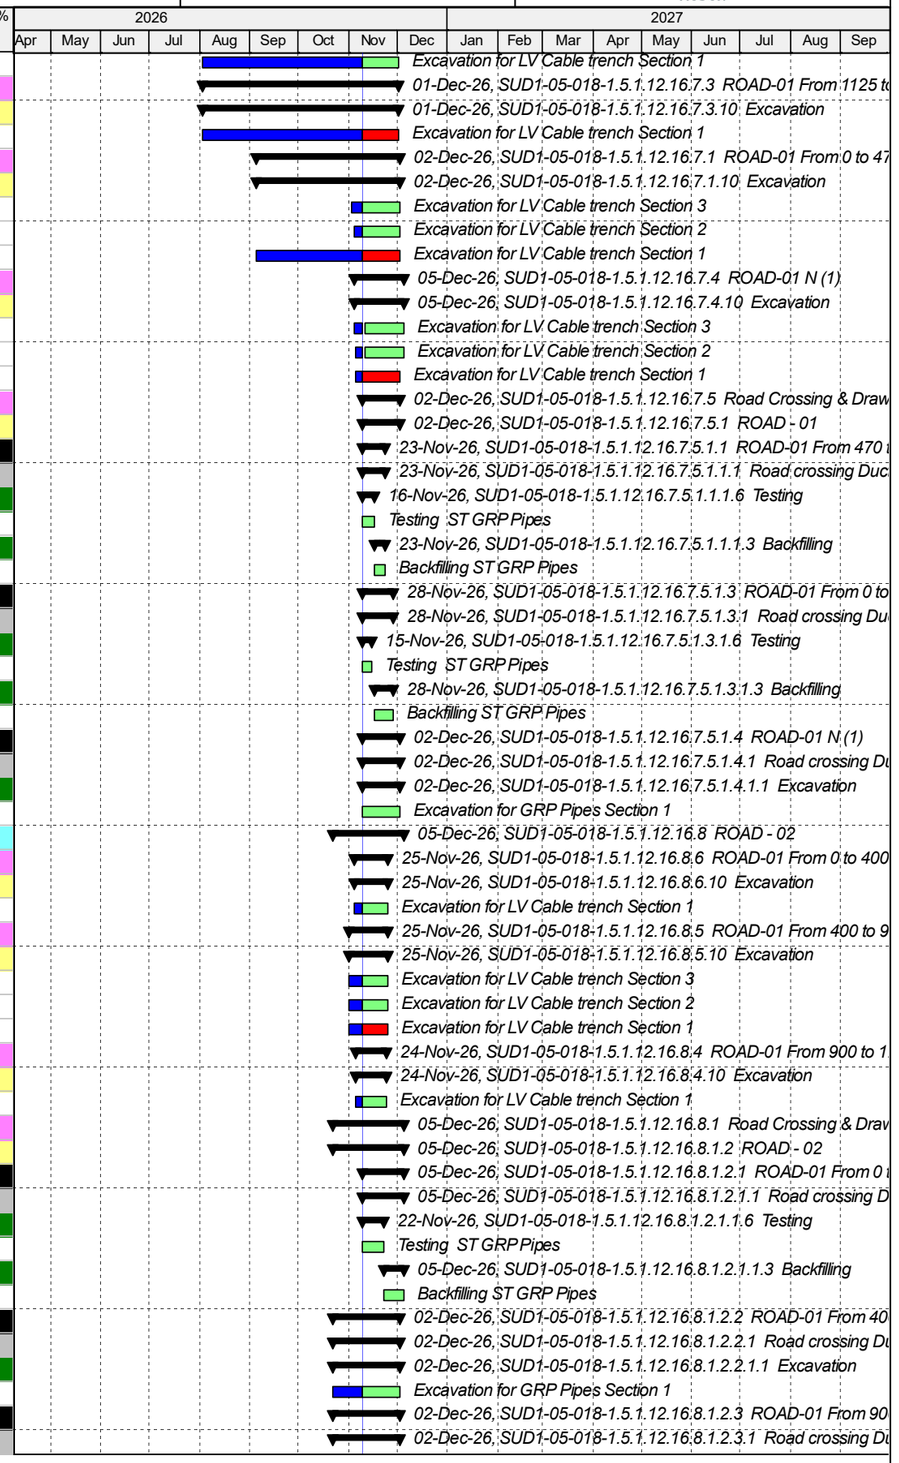

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filters: Filter for Construction in SAR , look ahead filter for -SAR.

© Oracle Corporation

Construction of a SAR Train Passenger Drop-Off Station in Sudair

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SUD1-05-018-1.5.1.12.16.8.1.2.3.1.1	Excavation	21	27-Aug-26	20-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	22-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5	TELECOMMUNICATIONS WORKS	39	13-Aug-26	24-Dec-26	05-Oct-26 A	19-Dec-26	88.25%	14.41%
SUD1-05-018-1.5.1.12.5.3	ROAD - 01	39	27-Aug-26	24-Dec-26	05-Oct-26 A	19-Dec-26	77.17%	34.29%
SUD1-05-018-1.5.1.12.5.3.4	ROAD-01 N 1 (2X3)X50 mm MH-15 to MH-16	21	27-Aug-26	24-Dec-26	04-Nov-26 A	02-Dec-26	60.04%	18.01%
SUD1-05-018-1.5.1.12.5.3.4.3	Ducts	21	27-Aug-26	20-Sep-26	04-Nov-26 A	02-Dec-26	100%	30%
SUD1-05-018-1.5.1.12.5.3.4.3.2	Excavation	21	27-Aug-26	20-Sep-26	04-Nov-26 A	02-Dec-26	100%	30%
SDR-ST-C	Excavation for telecom trench Section 1	21	27-Aug-26	20-Sep-26	04-Nov-26 A	02-Dec-26	100%	30%
SUD1-05-018-1.5.1.12.5.3.4.4	Manholes	20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SUD1-05-018-1.5.1.12.5.3.4.4.4	Testting	20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-ST-C	Telecom Manhole finishing works	20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SUD1-05-018-1.5.1.12.5.3.2	ROAD-01 From 0 to 470 m (3) (2X3)X50 mm MH-12 to MH-	21	21-Sep-26	15-Oct-26	05-Oct-26 A	19-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5.3.2.3	Ducts	21	21-Sep-26	15-Oct-26	19-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5.3.2.3.2	Excavation	21	21-Sep-26	15-Oct-26	19-Oct-26 A	02-Dec-26	100%	100%
SDR-ST-C	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	19-Oct-26 A	02-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5.3.2.4	Manholes	21	21-Sep-26	15-Oct-26	05-Oct-26 A	19-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5.3.2.4.1	Excavation	21	21-Sep-26	15-Oct-26	05-Oct-26 A	19-Dec-26	100%	100%
SDR-ST-C	Excavation for Telecom Manhole Section 2	21	21-Sep-26	15-Oct-26	05-Oct-26 A	19-Dec-26	100%	100%
SUD1-05-018-1.5.1.12.5.3.1	ROAD-01 From 470 to 1125 m (6) (2X3)X50 mm MH-10 to M	21	08-Sep-26	03-Oct-26	05-Nov-26 A	02-Dec-26	100%	20%
SUD1-05-018-1.5.1.12.5.3.1.3	Ducts	21	08-Sep-26	03-Oct-26	05-Nov-26 A	02-Dec-26	100%	20%
SUD1-05-018-1.5.1.12.5.3.1.3.2	Excavation	21	08-Sep-26	03-Oct-26	05-Nov-26 A	02-Dec-26	100%	20%
SDR-ST-C	Excavation for telecom trench Section 2	21	08-Sep-26	03-Oct-26	05-Nov-26 A	02-Dec-26	100%	20%
SUD1-05-018-1.5.1.12.5.3.3	ROAD-01 From 1125 to 1765 m (7) (2X3)X50 mm MH-8 to M	21	21-Sep-26	21-Dec-26	09-Nov-26	02-Dec-26	60.04%	0%
SUD1-05-018-1.5.1.12.5.3.3.3	Ducts	21	21-Sep-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.3.3.3.2	Excavation	21	21-Sep-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.3.3.4	Manholes	18	01-Dec-26	21-Dec-26	09-Nov-26	29-Nov-26	0%	0%
SUD1-05-018-1.5.1.12.5.3.3.4.4	Testting	18	01-Dec-26	21-Dec-26	09-Nov-26	29-Nov-26	0%	0%
SDR-ST-C	Telecom Manhole finishing works	18	01-Dec-26	21-Dec-26	09-Nov-26	29-Nov-26	0%	0%
SUD1-05-018-1.5.1.12.5.4	ROAD - 02	39	13-Aug-26	14-Dec-26	07-Oct-26 A	02-Dec-26	94.04%	4.02%
SUD1-05-018-1.5.1.12.5.4.3	ROAD-01 From 0 to 400 m (9) (2X3)X50 mm MH-5 to MH-7	21	15-Aug-26	14-Dec-26	09-Nov-26	02-Dec-26	90.01%	0%
SUD1-05-018-1.5.1.12.5.4.3.3	Ducts	21	15-Aug-26	27-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.3.3.2	Excavation	21	15-Aug-26	03-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 2	21	08-Sep-26	03-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 1	21	15-Aug-26	07-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.3.3.5	Pipe laying	21	04-Oct-26	27-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	HDPE Pipes for Telecom Installation	21	04-Oct-26	27-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.3.4	Manholes	21	21-Nov-26	14-Dec-26	09-Nov-26	02-Dec-26	0%	0%
SUD1-05-018-1.5.1.12.5.4.3.4.4	Testting	21	21-Nov-26	14-Dec-26	09-Nov-26	02-Dec-26	0%	0%
SDR-ST-C	Telecom Manhole finishing works	21	21-Nov-26	14-Dec-26	09-Nov-26	02-Dec-26	0%	0%
SUD1-05-018-1.5.1.12.5.4.1	ROAD-01 From 400 to 900 m (10) (2X3)X50 mm MH-1 to MI	39	13-Aug-26	01-Oct-26	07-Oct-26 A	02-Dec-26	100%	17.98%
SUD1-05-018-1.5.1.12.5.4.1.3	Ducts	21	13-Aug-26	01-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.1.3.2	Excavation	21	13-Aug-26	01-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 2	21	07-Sep-26	01-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 1	21	13-Aug-26	06-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.1.4	Manholes	21	07-Sep-26	01-Oct-26	07-Oct-26 A	02-Dec-26	100%	90%
SUD1-05-018-1.5.1.12.5.4.1.4.1	Excavation	21	07-Sep-26	01-Oct-26	07-Oct-26 A	02-Dec-26	100%	90%
SDR-ST-C	Excavation for Telecom Manhole Section 2	21	07-Sep-26	01-Oct-26	07-Oct-26 A	02-Dec-26	100%	90%
SUD1-05-018-1.5.1.12.5.4.2	ROAD-01 From 900 to 1239 m (11) (2)X32 mm MH-1	21	27-Aug-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.2.3	Ducts	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.2.3.2	Excavation	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for telecom trench Section 1	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.2.4	Manholes	21	27-Aug-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.12.5.4.2.4.1	Excavation	21	27-Aug-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for Telecom Manhole Section 2	21	21-Sep-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-C	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.13	LOW VOLTAGE	35	22-Oct-26	01-Dec-26	20-Aug-26 A	02-Dec-26	38.21%	56.67%
SUD1-05-018-1.5.1.13.1	ROAD - 01	21	22-Oct-26	15-Nov-26	20-Aug-26 A	02-Dec-26	71.77%	70%

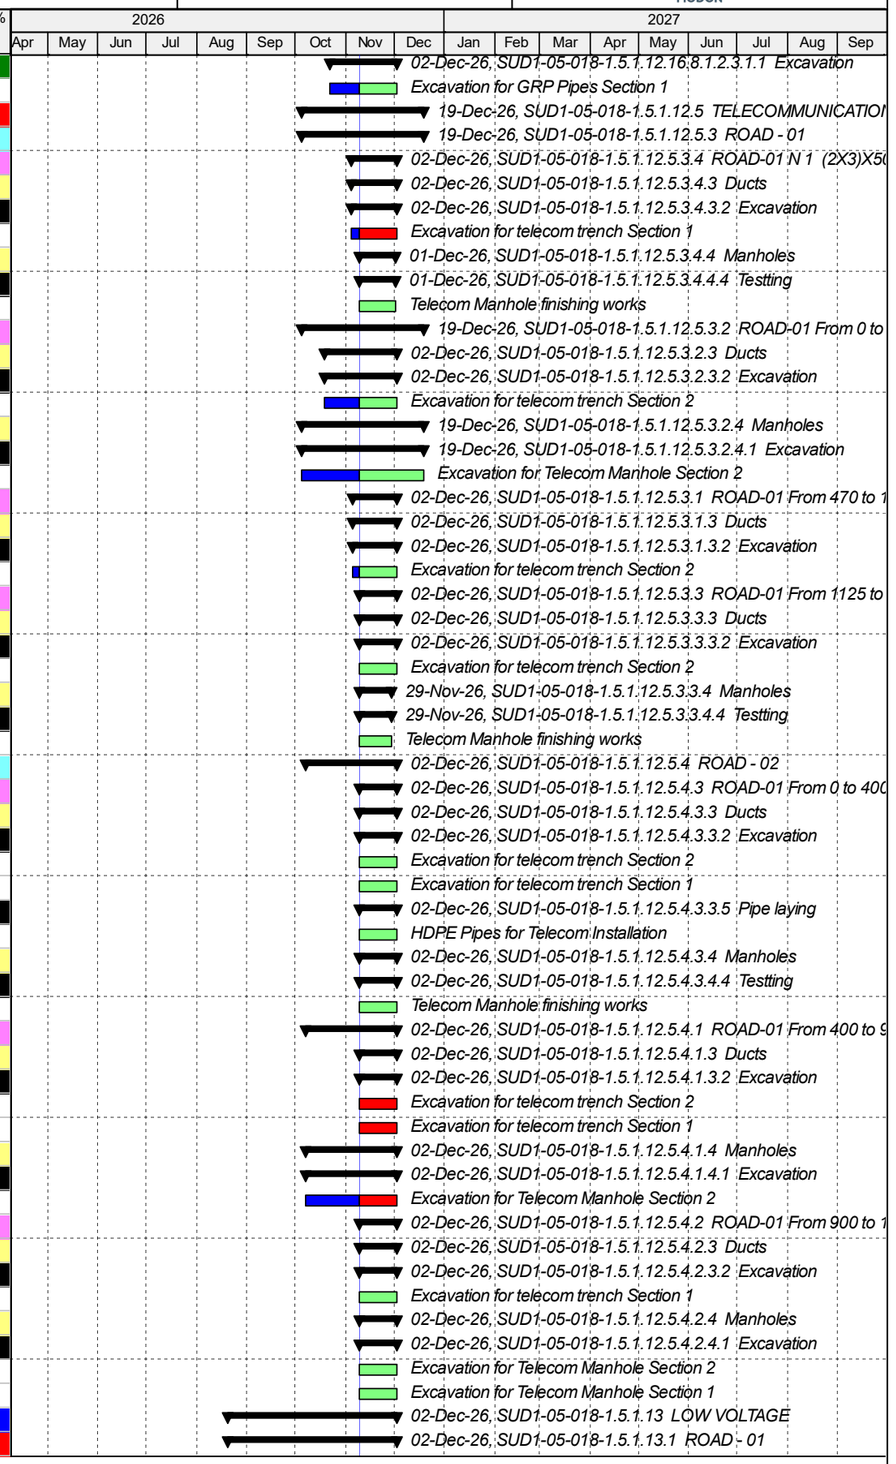

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filters: Filter for Construction in SAR , look ahead filter for -SAR.

© Oracle Corporation

Construction of a SAR Train Passenger Drop-Off Station in Sudair

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SUD1-05-018-1.5.1.13.1.1	ROAD-01 From 470 to 1125 m (6)	21	22-Oct-26	15-Nov-26	20-Aug-26 A	02-Dec-26	71.77%	70%
SUD1-05-018-1.5.1.13.1.1.6	Excavation	21	22-Oct-26	15-Nov-26	20-Aug-26 A	02-Dec-26	71.77%	70%
SDR-ST-CON-F	Excavation Works Part 1	21	22-Oct-26	15-Nov-26	20-Aug-26 A	02-Dec-26	71.43%	70%
SUD1-05-018-1.5.1.13.2	ROAD - 02	28	31-Oct-26	01-Dec-26	24-Aug-26 A	02-Dec-26	21.43%	50%
SUD1-05-018-1.5.1.13.2.1	ROAD-01 From 400 to 900 m (10)	21	31-Oct-26	23-Nov-26	24-Aug-26 A	02-Dec-26	38.1%	50%
SUD1-05-018-1.5.1.13.2.1.6	Excavation	21	31-Oct-26	23-Nov-26	24-Aug-26 A	02-Dec-26	38.1%	50%
SDR-ST-CON-F	Excavation Works Part 1	21	31-Oct-26	23-Nov-26	24-Aug-26 A	02-Dec-26	38.1%	50%
SUD1-05-018-1.5.1.13.2.4	ROAD-01 From 900 to 1239 m (11)	21	08-Nov-26	01-Dec-26	24-Aug-26 A	02-Dec-26	4.76%	50%
SUD1-05-018-1.5.1.13.2.4.6	Excavation	21	08-Nov-26	01-Dec-26	24-Aug-26 A	02-Dec-26	4.76%	50%
SDR-ST-CON-F	Excavation Works Part 1	21	08-Nov-26	01-Dec-26	24-Aug-26 A	02-Dec-26	4.76%	50%
SUD1-05-018-1.5.1.10	PORTABLE WATER	151	07-Sep-26	07-Jan-27	22-Sep-26 A	07-Dec-26	63.59%	52.77%
SUD1-05-018-1.5.1.10.2	ROAD - 01	21	12-Sep-26	17-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.2	ROAD-01 From 0 to 470 m (3)	21	22-Sep-26	17-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.2.3	Valve Chambers & Valves & Fire Hydrant	21	22-Sep-26	17-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.2.3.3	Excavation	21	22-Sep-26	17-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	21	22-Sep-26	17-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.1	ROAD-01 From 470 to 1125 m (6)	21	12-Sep-26	06-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.1.3	Valve Chambers & Valves & Fire Hydrant	21	12-Sep-26	06-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.1.3.3	Excavation	21	12-Sep-26	06-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	21	12-Sep-26	06-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.3	ROAD-01 From 1125 to 1765 m (7)	21	13-Sep-26	07-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.3.3	Valve Chambers & Valves & Fire Hydrant	21	13-Sep-26	07-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.2.3.3.3	Excavation	21	13-Sep-26	07-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	21	13-Sep-26	07-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3	ROAD - 02	151	07-Sep-26	07-Jan-27	22-Sep-26 A	07-Dec-26	60.52%	57.22%
SUD1-05-018-1.5.1.10.3.3	ROAD-01 From 0 to 400 m (9)	35	07-Sep-26	07-Jan-27	24-Oct-26 A	07-Dec-26	19.74%	40.13%
SUD1-05-018-1.5.1.10.3.3.7	Pipes Work	21	15-Dec-26	07-Jan-27	24-Oct-26 A	07-Dec-26	0%	50%
SUD1-05-018-1.5.1.10.3.3.7.5	Testing	21	15-Dec-26	07-Jan-27	24-Oct-26 A	07-Dec-26	0%	50%
SDR-ST-COI	Testing of PW HDPE Pipe 315 mm.	21	15-Dec-26	07-Jan-27	24-Oct-26 A	07-Dec-26	0%	50%
SUD1-05-018-1.5.1.10.3.3.3	Valve Chambers & Valves & Fire Hydrant	20	07-Sep-26	30-Sep-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3.3.3.3	Excavation	20	07-Sep-26	30-Sep-26	09-Nov-26	01-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	20	07-Sep-26	30-Sep-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3.2	ROAD-01 From 400 to 900 m (10)	20	08-Sep-26	30-Nov-26	25-Oct-26 A	01-Dec-26	19.74%	40.13%
SUD1-05-018-1.5.1.10.3.2.7	Pipes Work	14	15-Nov-26	30-Nov-26	25-Oct-26 A	29-Nov-26	0%	50%
SUD1-05-018-1.5.1.10.3.2.7.5	Testing	14	15-Nov-26	30-Nov-26	25-Oct-26 A	29-Nov-26	0%	50%
SDR-ST-COI	Testing of PW HDPE Pipe 315 mm.	14	15-Nov-26	30-Nov-26	25-Oct-26 A	29-Nov-26	0%	50%
SUD1-05-018-1.5.1.10.3.2.3	Valve Chambers & Valves & Fire Hydrant	20	08-Sep-26	01-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3.2.3.3	Excavation	20	08-Sep-26	01-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	20	08-Sep-26	01-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3.1	ROAD-01 From 900 to 1239 m (11)	151	09-Sep-26	25-Nov-26	22-Sep-26 A	06-Dec-26	76.79%	64.04%
SUD1-05-018-1.5.1.10.3.1.7	Pipes Work	141	18-Oct-26	25-Nov-26	22-Sep-26 A	06-Dec-26	75.83%	66.67%
SUD1-05-018-1.5.1.10.3.1.7.8	bedding Works	10	18-Oct-26	28-Oct-26	22-Sep-26 A	19-Nov-26	100%	80%
SDR-ST-COI	Sand bedding for PW HDPE Pipes 315 mm	10	18-Oct-26	28-Oct-26	22-Sep-26 A	19-Nov-26	100%	80%
SUD1-05-018-1.5.1.10.3.1.7.2	Pipes Laying	10	29-Oct-26	09-Nov-26	24-Sep-26 A	19-Nov-26	90%	80%
SDR-ST-COI	Install PW 315 mm HDPE Pipe	10	29-Oct-26	09-Nov-26	24-Sep-26 A	19-Nov-26	90%	80%
SUD1-05-018-1.5.1.10.3.1.7.5	Testing	14	10-Nov-26	25-Nov-26	21-Nov-26	06-Dec-26	0%	0%
SDR-ST-COI	Testing of PW HDPE Pipe 315 mm.	14	10-Nov-26	25-Nov-26	21-Nov-26	06-Dec-26	0%	0%
SUD1-05-018-1.5.1.10.3.1.3	Valve Chambers & Valves & Fire Hydrant	20	09-Sep-26	03-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.10.3.1.3.3	Excavation	20	09-Sep-26	03-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SDR-ST-COI	Excavation for Valve Chambers Section 1	20	09-Sep-26	03-Oct-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.1.7	SEWARAGE NETWORK	138	27-Aug-26	16-Dec-26	07-Sep-26 A	07-Dec-26	62.85%	53.65%
SUD1-05-018-1.5.1.7.6	ROAD - 01	125	27-Aug-26	16-Dec-26	07-Sep-26 A	07-Dec-26	38.58%	29.18%
SUD1-05-018-1.5.1.7.6.2	ROAD-01 From 0 to 470 m (3) 110 mm HDPE	21	24-Nov-26	16-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SUD1-05-018-1.5.1.7.6.2.7	Pipes Work	21	24-Nov-26	16-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SUD1-05-018-1.5.1.7.6.2.7.3	Testing	21	24-Nov-26	16-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SDR-ST-COI	Testing of 200 mm GRP Pipe.	21	24-Nov-26	16-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SUD1-05-018-1.5.1.7.6.1	ROAD-01 From 470 to 1125 m (6) 110 mm HDPE	21	19-Nov-26	12-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SUD1-05-018-1.5.1.7.6.1.7	Pipes Work	21	19-Nov-26	12-Dec-26	14-Nov-26	07-Dec-26	0%	0%

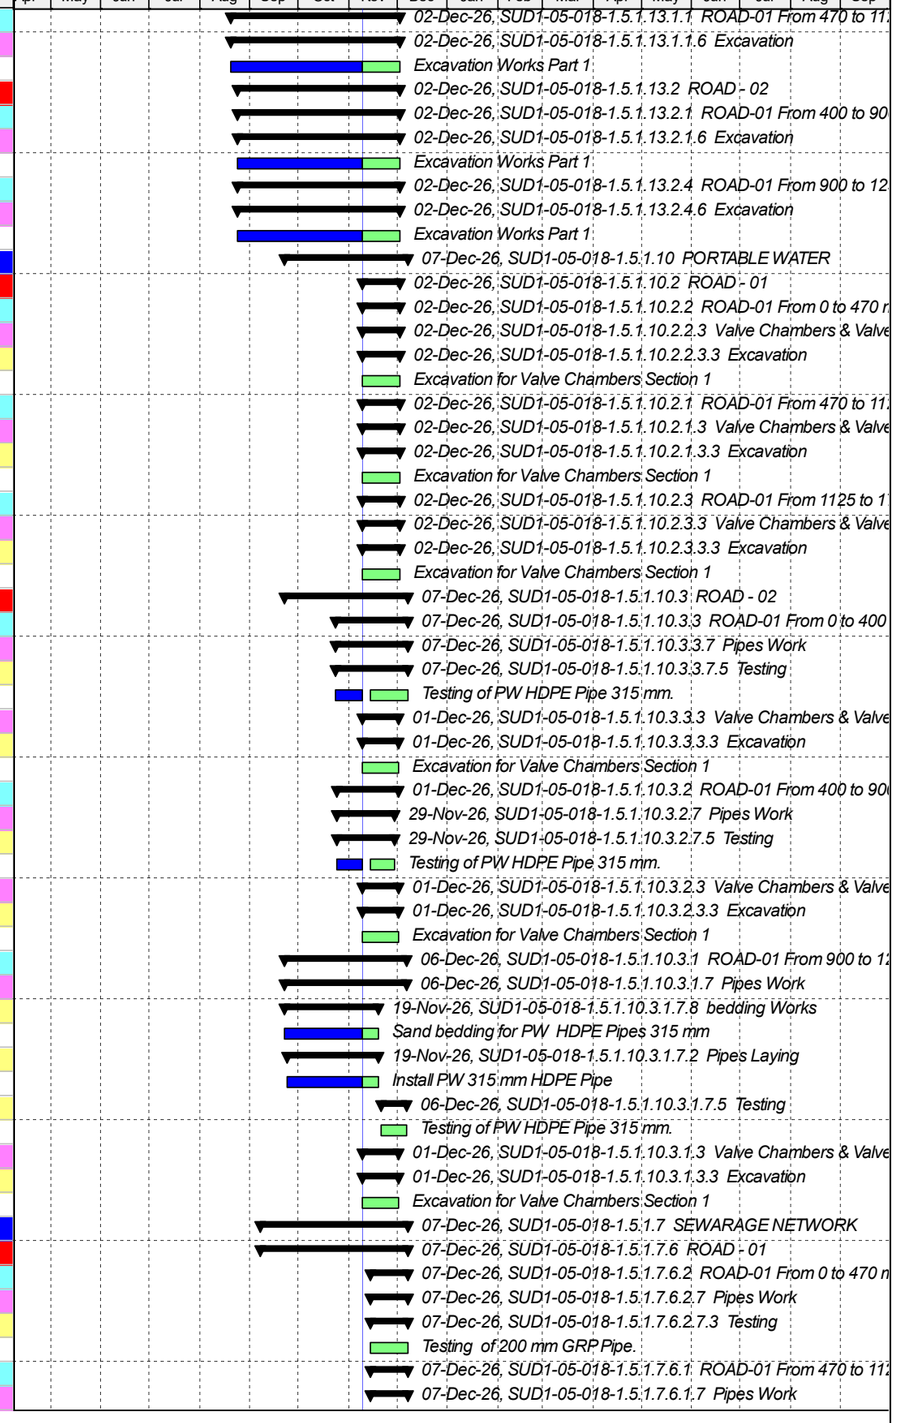

Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary


TASK filters: Filter for Construction in SAR , look ahead filter for -SAR.

© Oracle Corporation

Construction of a SAR Train Passenger Drop-Off Station in Sudair

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SUD1-05-018-1.5.1.7.6.1.7.3	Testing	21	19-Nov-26	12-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SDR-ST-CON	Testing of 200 mm GRP Pipe.	21	19-Nov-26	12-Dec-26	14-Nov-26	07-Dec-26	0%	0%
SUD1-05-018-1.5.1.7.6.3	ROAD-01 From 1125 to 1765 m (7) 110 mm HDPE	125	27-Aug-26	15-Oct-26	07-Sep-26 A	02-Dec-26	100%	75.63%
SUD1-05-018-1.5.1.7.6.3.7	Pipes Work	17	20-Sep-26	10-Oct-26	07-Sep-26 A	28-Nov-26	100%	95%
SUD1-05-018-1.5.1.7.6.3.7.1	Excavation	17	20-Sep-26	10-Oct-26	07-Sep-26 A	28-Nov-26	100%	95%
SDR-ST-CON	Excavation for GRP Pipe 200mm Diameter Section 2	17	20-Sep-26	10-Oct-26	07-Sep-26 A	28-Nov-26	100%	95%
SUD1-05-018-1.5.1.7.6.3.4	Manholes	21	27-Aug-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.7.6.3.4.1	Excavation	21	27-Aug-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-CON	Excavation for manhole. Section 2	21	21-Sep-26	15-Oct-26	09-Nov-26	02-Dec-26	100%	0%
SDR-ST-CON	Excavation for manhole. Section 1	21	27-Aug-26	20-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SUD1-05-018-1.5.1.7.1	ROAD - 02	128	30-Aug-26	28-Oct-26	07-Sep-26 A	02-Dec-26	100%	91.11%
SUD1-05-018-1.5.1.7.1.1	ROAD-01 From 400 to 900 m (10) 110 mm HDPE	17	30-Aug-26	17-Sep-26	07-Sep-26 A	21-Nov-26	100%	98%
SUD1-05-018-1.5.1.7.1.1.7	Pipes Work	17	30-Aug-26	17-Sep-26	07-Sep-26 A	21-Nov-26	100%	98%
SUD1-05-018-1.5.1.7.1.1.7.1	Excavation	17	30-Aug-26	17-Sep-26	07-Sep-26 A	21-Nov-26	100%	98%
SDR-ST-CON	Excavation for GRP Pipe 200mm Diameter Section 1	17	30-Aug-26	17-Sep-26	07-Sep-26 A	21-Nov-26	100%	98%
SUD1-05-018-1.5.1.7.1.3	ROAD-01 From 900 to 1239 m (11) 110 mm HDPE	128	09-Sep-26	28-Oct-26	07-Sep-26 A	02-Dec-26	100%	85%
SUD1-05-018-1.5.1.7.1.3.7	Pipes Work	16	09-Sep-26	28-Sep-26	07-Sep-26 A	21-Nov-26	100%	85%
SUD1-05-018-1.5.1.7.1.3.7.1	Excavation	16	09-Sep-26	28-Sep-26	07-Sep-26 A	21-Nov-26	100%	85%
SDR-ST-CON	Excavation for GRP Pipe 200mm Diameter Section 1	16	09-Sep-26	28-Sep-26	07-Sep-26 A	21-Nov-26	100%	85%
SUD1-05-018-1.5.1.7.1.3.4	Manholes	21	05-Oct-26	28-Oct-26	25-Oct-26 A	02-Dec-26	100%	85%
SUD1-05-018-1.5.1.7.1.3.4.1	Excavation	21	05-Oct-26	28-Oct-26	25-Oct-26 A	02-Dec-26	100%	85%
SDR-ST-CON	Excavation for manhole. Section 2	21	05-Oct-26	28-Oct-26	25-Oct-26 A	02-Dec-26	100%	85%
SUD1-05-018-1.5.3	Package-3	20	07-Jul-26	03-Sep-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.3.1	Site Works	20	07-Jul-26	16-Aug-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.3.1.1	Earthworks	20	07-Jul-26	16-Aug-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.3.1.1.2	Excavation	20	07-Jul-26	29-Jul-26	09-Nov-26	01-Dec-26	100%	0%
SDR-ST-CON-P3-	Excavation in all types of soil to the required depth include	20	07-Jul-26	29-Jul-26	09-Nov-26	01-Dec-26	100%	0%
SUD1-05-018-1.5.3.1.1.1	Fill	15	30-Jul-26	16-Aug-26	09-Nov-26	25-Nov-26	100%	0%
SDR-ST-CON-P3-	Backfilling with improved and select fill material from the sit	15	30-Jul-26	16-Aug-26	09-Nov-26	25-Nov-26	100%	0%
SUD1-05-018-1.5.3.2	Platform Works	16	17-Aug-26	03-Sep-26	09-Nov-26	26-Nov-26	100%	0%
SUD1-05-018-1.5.3.2.1	Platform	16	17-Aug-26	03-Sep-26	09-Nov-26	26-Nov-26	100%	0%
SUD1-05-018-1.5.3.2.1.1	Earthworks	16	17-Aug-26	03-Sep-26	09-Nov-26	26-Nov-26	100%	0%
SUD1-05-018-1.5.3.2.1.1.1	Excavation	16	17-Aug-26	03-Sep-26	09-Nov-26	26-Nov-26	100%	0%
SDR-ST-CON-F	Excavation in all types of soil to the required depth include	16	17-Aug-26	03-Sep-26	09-Nov-26	26-Nov-26	100%	0%

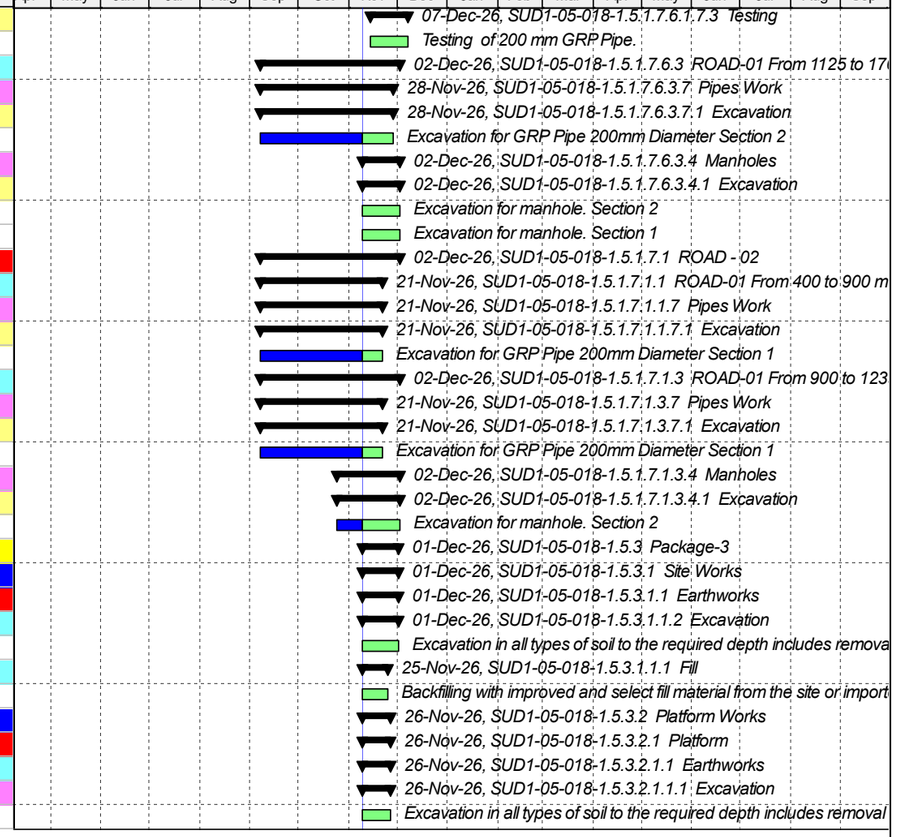

Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filters: Filter for Construction in SAR , look ahead filter for -SAR.

© Oracle Corporation
