Infrastructure Development in the Third Industrial City, Jeddah

تطوير البنية التحتية بالمدينة الصناعية الثالثة بجدة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Alrawaf Contracting	Egis	Ahmed Alkutbi	16-Mar-2025	15-Mar-2028

Scope: sewage, storm water (to the ponds), irrigation and potable water networks, 13.8 kV medium-voltage cables, street lighting, telecom ducts and cables, internal and external roads with asphalt and sidewalks, the potable water and TSE pump stations, three lift stations and a mosque. Contract value SAR 560 million excluding VAT, 36 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-days. This week a full MODON weekly report workbook was uploaded, so the figures come from it rather than from the P6 file: its summary puts the project at 58.70% against 55.32% planned, 3.38% ahead, SPI 1.06. The P6 export inside the same workbook gives a lower 53.45% against 53.97% (SPI 0.99), and only 0.21% was earned this week against 0.66% planned.

PHYSICAL % COMPLETE
58.70% / 55.32%
plan
▲ SPI 1.06 +3.38%

PROGRESS THIS WEEK
+0.21% / +0.66%
plan
▼ 0.45% below the weekly plan

CONTRACT TIME ELAPSED
54.5% · day 597 of 1,096
● Report forecast 15-Mar-2028

INVOICED TO DATE (GROSS)
47.1% · 263.9M SAR
17 invoices, last period ends 30-Sep-2026

The reported lead rests on figures that the workbook's own P6 data does not support.

The summary's earned man-days exceed the budget in three areas (mosque 185%, irrigation 110%, earthworks for blocks 101%), and its total budget (169,568 man-days) differs from the P6 export (159,298). On the P6 basis the project is 0.52% behind its revised plan and 8.8% behind the original baseline (62.29% due by 01-Nov-2026). Earned man-days fell to 514 in October and 56 so far in November, against 8,136 planned for October, and this week's gain of 0.21% is a third of the 0.66% planned. Roads (34.9% against 51.8%) and street lighting (40.0% against 68.8%) are the weakest areas. The P6 update of 26-Oct-2026 finishes the project on 19-Mar-2028, 4 days after the contract date; the weekly report still forecasts 15-Mar-2028.

Site photos this week

Six of the ten photos uploaded for this week, stamped 31-Oct and 01-Nov-2026. Asphalt and base course work on the Mobco road, road R100-01 and at the potable water pump station, waterproofing at lift station 1 and formwork at the TSE pump station. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt base course, Mobco road

Crew and tipper on the new layer. Stamped 31-Oct-2026, 08:03.



Asphalt base course, road R100-01

Paver fed by a tipper. Stamped 31-Oct-2026, 08:37.



Aggregate base course, potable water pump station

Paver laying the base course. Stamped 01-Nov-2026, 08:07.



Base course compaction, potable water pump station

Roller on the new layer. Stamped 01-Nov-2026, 08:08.



Lift station 1

Waterproofing applied to the structure walls. Stamped 01-Nov-2026, 09:11.



TSE pump station

Scaffolding and formwork between the columns. Stamped 01-Nov-2026, 09:53.

Progress S-curve

Cumulative physical progress (man-day weighted) at the start of each month. Source: Physical-Chart Data sheet of the weekly report 02-Nov-2026 (P6 export, 159,298 budgeted man-days).



WEEK ENDING	BASIS	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
26-Oct-2026	P6 export	53.27	53.23	−0.04%	–	1.00
02-Nov-2026	P6 export	53.97	53.45	−0.52%	+0.22%	0.99
02-Nov-2026	**Weekly report summary**	**55.32**	**58.70**	**+3.38%**	**+0.21%**	**1.06**

Both bases come from the 02-Nov-2026 workbook: the P6 export rows from its Progress Summery sheet (which also holds the 26-Oct-2026 values), the summary row from its Weekly Progress Report sheet. Last week's report (week 84) computed 52.75% from the P6 file itself, weighting by current rather than baseline man-days, so it is not directly comparable.

Progress by phase

Physical progress to date by WBS, measured by budgeted man-days. Source: Weekly Progress Report sheet, 02-Nov-2026. SPI is not shown where less than 5% was planned.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Al-Khorayef road	0.57%	62.59%	65.08%	+2.49%	1.04	▲ Ahead
Jeddah-Jizan link road	2.46%	92.15%	72.52%	−19.63%	0.79	▼ Behind
Earthworks for blocks	1.72%	97.86%	100.54%	+2.68%	1.03	? Over 100%
Earthworks for roads	2.90%	69.76%	78.88%	+9.12%	1.13	▲ Ahead
Sewage network	1.54%	97.56%	99.16%	+1.60%	1.02	▲ Ahead
Storm network	19.57%	74.50%	85.77%	+11.27%	1.15	▲ Ahead
Irrigation network	4.37%	109.36%	110.19%	+0.83%	1.01	? Over 100%
Potable water network	5.89%	85.95%	78.55%	−7.40%	0.91	▼ Behind
Electrical network	2.09%	83.09%	77.20%	−5.89%	0.93	▼ Behind
Street lighting network	5.12%	68.77%	39.95%	−28.82%	0.58	▼ Behind
Telecom network	1.68%	86.00%	74.68%	−11.32%	0.87	▼ Behind
Road network	19.87%	51.77%	34.90%	−16.87%	0.67	▼ Behind
Landscape	5.41%	17.71%	29.19%	+11.48%	1.65	▲ Ahead
TSE pump station	5.20%	3.59%	22.70%	+19.11%	–	▲ Ahead
Potable water pump station	16.49%	22.28%	41.14%	+18.86%	1.85	▲ Ahead
Mosque	1.21%	70.76%	185.10%	+114.34%	2.62	? Over 100%
Lift station 1	1.44%	5.60%	32.84%	+27.24%	–	▲ Ahead
Lift station 2	1.50%	17.88%	33.38%	+15.50%	1.87	▲ Ahead
Lift station 3	0.95%	3.37%	14.82%	+11.45%	–	▲ Ahead
Total	100%	**55.32%**	**58.70%**	**+3.38%**	**1.06**	▲ Ahead

Engineering, procurement, testing and the guard rail carry no man-days and are not in the physical measure. The P6 schedule in the workbook has 16,623 activities: 9,117 completed, 357 in progress and 7,149 not started; failed starts rose from 1,994 to 2,108.

Milestones

Baseline and forecast from the weekly report of 02-Nov-2026; P6 forecast and float from the P6 update of 26-Oct-2026 (no newer P6 file was uploaded).

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	16-May-2025	16-Apr-2025	16-Mar-2025 (actual)	–	? Dates conflict
Complete mobilisation	16-Apr-2025	17-Aug-2025	08-May-2025 (actual)	–	✓ Done
Submit shop drawings	16-Apr-2025	17-May-2025	29-Jun-2025 (actual)	–	✓ Done
Finish road works	16-Jan-2026	16-Jan-2026	18-Jul-2027	204	▼ Late
Finish deep works	16-Sep-2026	16-Sep-2026	12-Jun-2027	235	▼ Late
Finish MV works	19-Nov-2026	19-Nov-2026	17-Dec-2026	378	▼ At risk
Finish all networks	25-Feb-2027	25-Feb-2027	14-Feb-2027	328	● On time
Project finish	15-Mar-2028	15-Mar-2028	19-Mar-2028	0	▼ Late

The weekly report's milestone dates do not match the schedule.

The report keeps road works at 16-Jan-2026 and deep works at 16-Sep-2026, both already past, with a forecast equal to the baseline and "0 days change", while marking road works as behind. The P6 update forecasts 18-Jul-2027 and 12-Jun-2027 for the same milestones. The report's own Conclusion sheet gives yet other dates (all networks 16-Mar-2027, whole project 28-Jul-2026).

Procurement of key materials

Share of the total quantity delivered to site. Source: MODON supplier follow-up sheet updated 02-Nov-2026, and the Status of Procurement sheet of the weekly report for the HDPE pipes.



Station systems not yet approved


CCTV, public address, access control, fire alarm and data and telephone systems are still not approved (supplier, samples, shop drawings); the contractor is to resubmit because the twice-approved supplier is too expensive. Interlock (166,014 m²) is still not delivered, with its PO issued.

Items in manufacture

Panels and substations due end of November 2026; fuel system 15-Nov-2026; water hammer vessels 30-Nov-2026; altitude valves complete by early December; cranes within two weeks; penstocks (6) in January 2027; SCADA in January 2027. The remaining 11 station pumps are due within a week.

Manpower

Monthly labour, in man-days, planned vs actual. Source: Manpower sheet of the weekly report 02-Nov-2026.

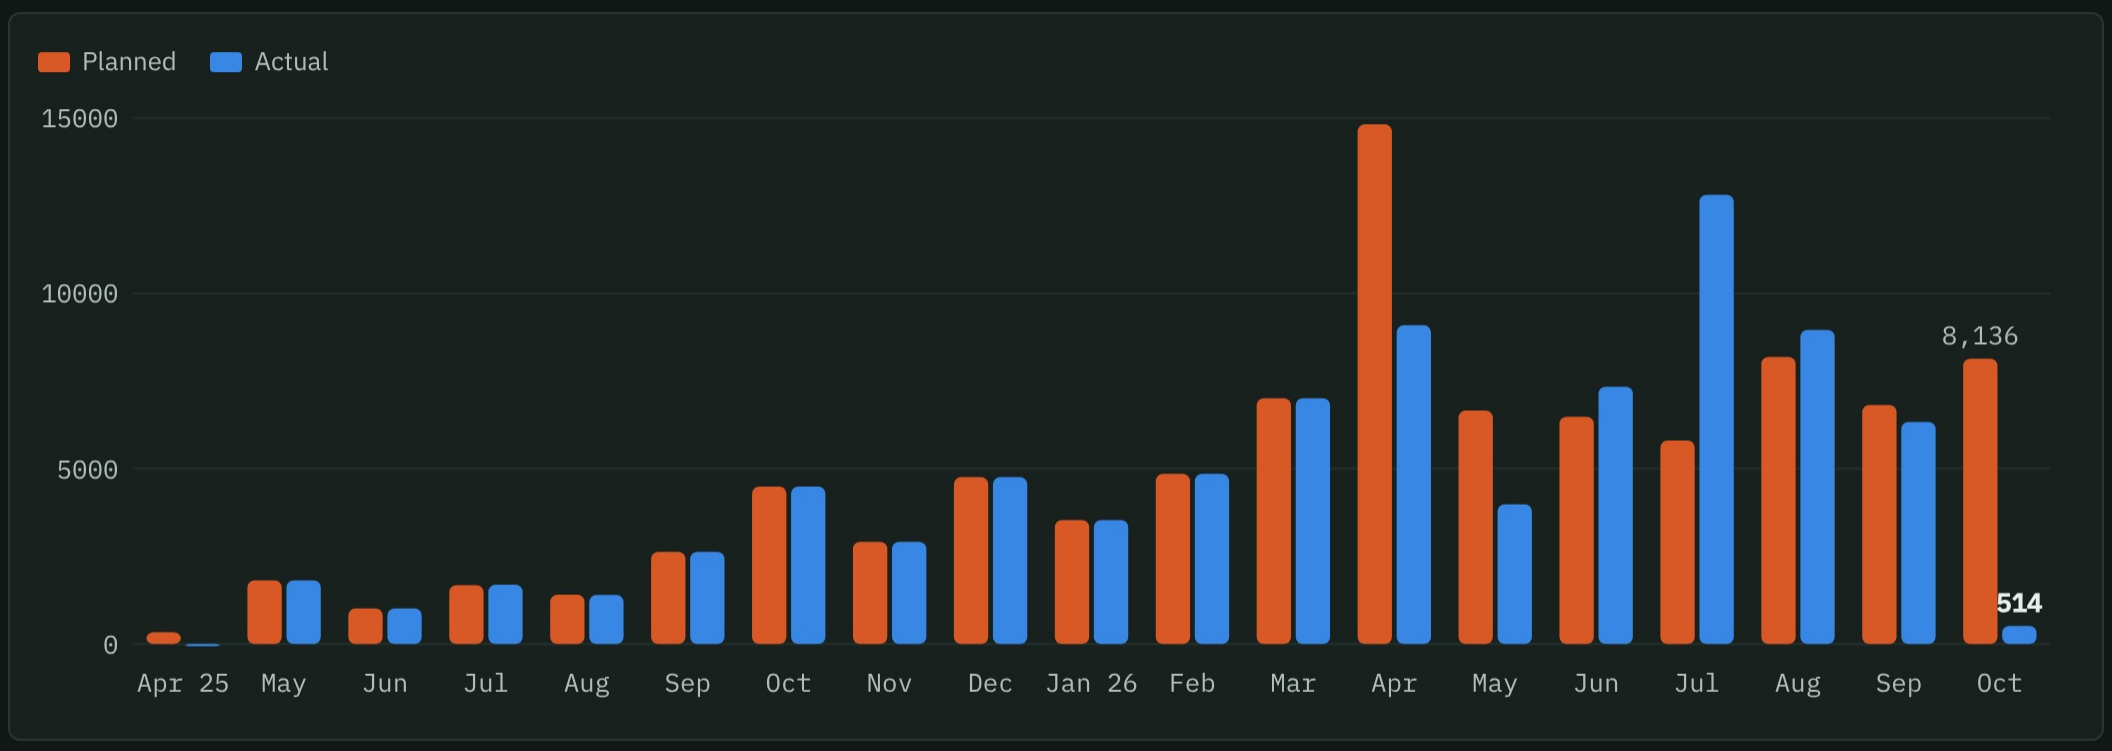

October recorded 514 man-days against 8,136 planned (−94%), and November so far 56. The report's resource table lists 6,329 as the actual manual head count, which is September's man-day total, against 1,703.5 planned.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	560,000,000
Revised contract value	560,000,000
Contract value incl. 15% VAT	644,000,000
Change orders	0
Advance payment (10%)	56,000,000

All values in SAR. The VAT-inclusive value is from the procurement tracker's Info sheet; the change order log is empty and potential changes are 0.

Invoices

Invoices in the log	17
Gross value	263,926,803
Advance payment recovered	26,392,680
Deductions and penalties	600,000
Approved and paid (net incl. VAT)	272,564,241

Invoicing is 47.1% of the contract value; the last invoice covers September 2026. The summary counts 16 submitted against 17 approved and paid ("−1 pending") because two log rows share invoice number 16.

Health, safety and quality

Safety Score 0.78

Man-hours this week	17,640
Man-hours (cumulative)	2,082,696
Safe man-hours since last reset	27,160
Fatalities (cumulative)	1
Lost-time injuries	0
First-aid cases / near misses (cumulative)	4 / 2
Inspections / toolbox talks this week	25 / 15

MODON HSE inspection of 22-Oct-2026 scored 78.12% and rated excavation and trenches and fire protection as "fail (life-threatening)".

Quality Score 0.93

NCRs issued / closed / open	121 / 110 / 11
Site instructions issued / open	55 / 5
MIRs issued / open	206 / 5
FIRs issued / open	17,521 / 201
Shop drawings: total / code A / code B / pending	3,799 / 1,197 / 2,307 / 26
Material submittals: total / code A / code B	179 / 15 / 141

QC inspection of 25-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Fatality and slow restart of works	Contractor	The weekly report records one fatality this year and resets safe man-hours to 27,160. Last week's risk log recorded works not resumed pending safety requirements; this week's photos (31-Oct and 01-Nov) show work under way, but only 56 man-days are booked for November.
Roads and street lighting behind	Contractor	Road network 34.9% against 51.8% planned and street lighting 40.0% against 68.8%; the two together weigh 25% of the physical measure.
Networks after asphalt	MODON	Issue 1 (16-Apr-2025, on hold, 565 days): building networks after the asphalt is finished would destroy the asphalt and cause rework.
Severe weather	Other	Issue 2 (19-Apr-2025, active): severe weather affects the productivity rate.
Station systems not approved	Contractor	CCTV, public address, access control, fire alarm and data systems still need supplier, sample and shop drawing approval.

The report's issue log has four entries; the two on manhole and catch basin supply were closed in 2025.

Data notes

- Basis: this week's physical figures come from the MODON weekly report workbook (1111.xlsx, data date 02-Nov-2026). Its summary (58.70% against 55.32%) and its P6 export (53.45% against 53.97%) disagree; both are shown. The workbook also reports cost-based progress labelled "Earn Value", which is not used here.
- In the summary, earned man-days exceed the budget for the mosque (3,783 of 2,044), irrigation (8,164 of 7,409) and earthworks for blocks, and planned irrigation is 109%. Landscape shows 2,680 earned man-days in the summary but 0 in the P6 export.
- The Physical-Chart Data and Manpower sheets show actual man-days falling to 514 in October and 56 in November, while the summary reports 356 man-days earned this week.
- Site handover is 16-Mar-2025 in the General Information sheet but 16-May-2025 (baseline) and 16-Apr-2025 (forecast) in the milestone table. The safety plan approval date is entered as 05-May-2028.
- Milestone dates in the weekly report (road works 16-Jan-2026, deep works 16-Sep-2026) have passed but show "0 days change"; they disagree with the P6 update and with the report's Conclusion sheet.
- The resource table gives 6,329 actual against 1,703.5 planned manual head count; 6,329 is September's man-day total. Saudi staff 52.
- Procurement totals differ between files: MV cables 100,000 of 116,000 m in the MODON supplier sheet but 189,522 of 189,522 m in the Status of Procurement sheet; lighting poles 1,132 of 1,273 against 1,161 of 1,161; catch basin covers 1,373 against 1,441.
- No new P6 file was uploaded this week; the P6 forecast (19-Mar-2028) is from the 26-Oct-2026 update. The invoice log numbers two invoices as 16, so the summary shows "−1" pending invoices. The tracker's Info sheet is still dated 15-Jun-2026.

Compiled 08-Nov-2026 from the files uploaded for week W06 (05-Nov-2026): MODON weekly report workbook 1111.xlsx (data date 02-Nov-2026), MODON supplier follow-up sheet 02-Nov-2026, procurement tracker 02-Nov-2026, 3-week look-ahead and site photos; P6 forecasts from the 26-Oct-2026 update.
