Dammam 3rd Industrial City Gates and Fence

سور للمدينة الصناعية - الدمام الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Deri Construction Company	EGIS	Eng. Affat M. Al-Enezi	06-May-2026	05-Aug-2026

Scope: Type 1 and Type 2 perimeter fence, main and chain-link gates, and guard rooms with water tanks, with their mechanical and electrical works (lighting, gate barriers, intrusion detection). Contract duration 91 days; contract value 16,500,001.96 SAR.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (25,284 man-hours in total). At 03-Nov-2026 the project is 98.4% complete against 100% planned, behind by 1.6%, after gaining 0.51% (130 man-hours) this week. The contract completion date of 05-Aug-2026 passed 90 days ago.

PHYSICAL % COMPLETE
98.4% / 100% plan
▼ SPI 0.98 −1.6%

PROGRESS THIS WEEK
+0.51% / 0.00% plan
▼ 1.6% still open after the planned finish

CONTRACT TIME ELAPSED
199% · day 181 of 91
▼ P6 finish 02-Nov-2026 (passed)

INVOICED TO DATE (GROSS)
59.3% · 9.78M SAR
5 invoices, last period ends 26-Sep-2026

The project is 90 days past its contract completion date, and the P6 handover date of 02-Nov-2026 has passed with work still open.

The P6 file uploaded this week (named DD03-11-2026) still has a data date of 27-Oct-2026 and was not rescheduled. It keeps initial handover on 02-Nov-2026, 89 days after the contract date of 05-Aug-2026, with −70.5 to −75 days of float on the 21 open activities, all of which were due by that date. The weekly report still gives 05-Aug-2026 as the forecast completion. Construction is unchanged at 99.9%; handing over rose to 33.4% and testing and commissioning to 87.5%. Four issues in the issue log were reopened this week.

Site photos this week


Four of the five photos uploaded with the 03-Nov-2026 weekly report. Only one carries a date and GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.



MODON sign
Illuminated MODON sign on the guard-house wall, at night.



Median planting and lighting
Planted median with ground lights, at night.

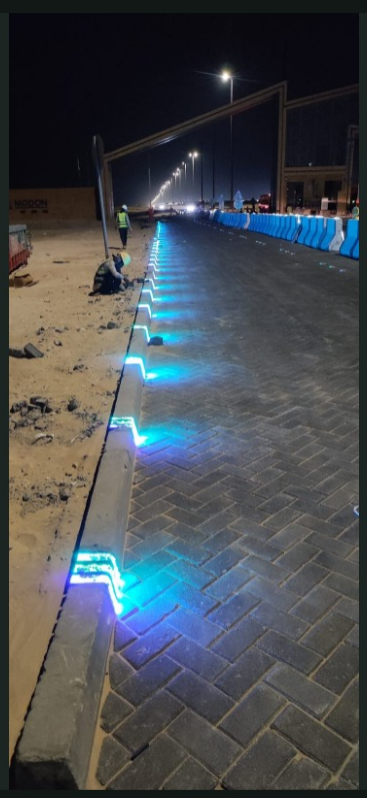

Kerb lighting

Kerb-mounted lights along the interlock road, with a crew at work, at night.




Landscape works

Planting in the median. GPS-stamped 03-Nov-2026, 09:31.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

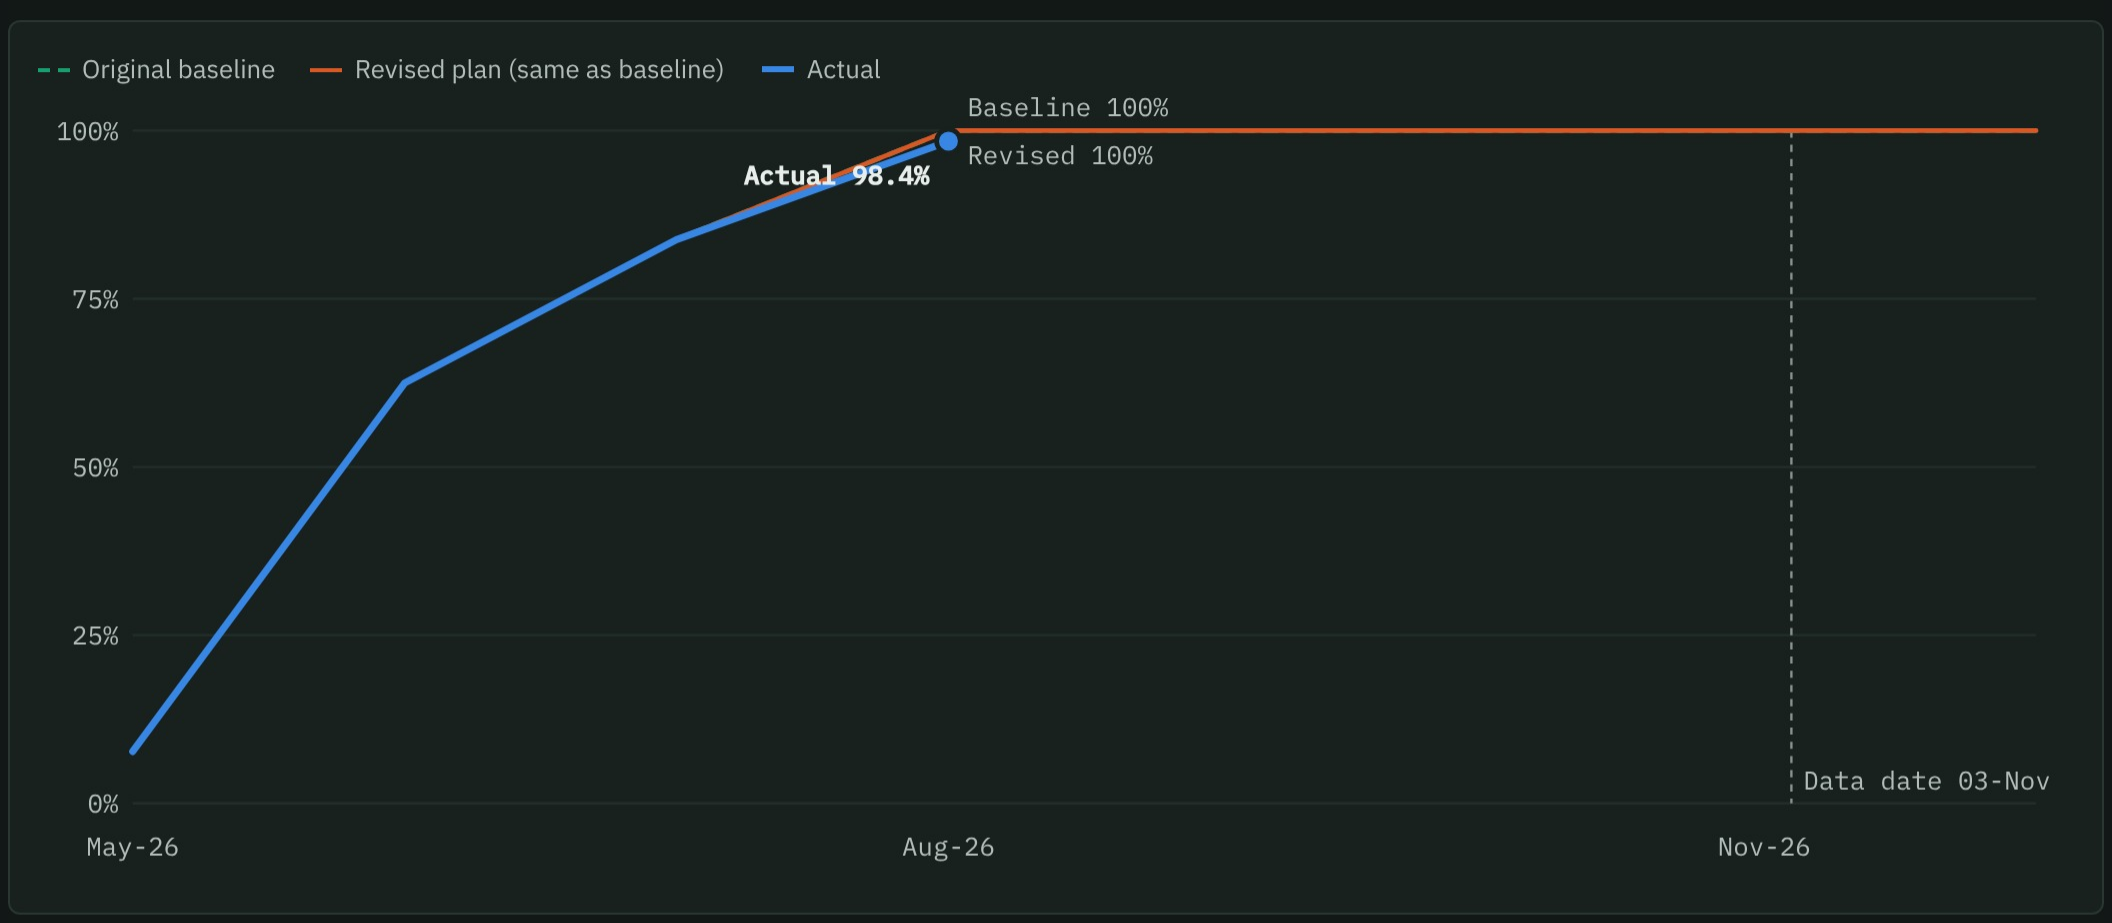

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
20-Oct-2026	100.0	97.6	−2.4%	–	0.98
27-Oct-2026	100.0	97.9	−2.1%	+0.30%	0.98
03-Nov-2026	**100.0**	**98.4**	**−1.6%**	**+0.51%**	**0.98**

Earned man-hours from the Progress sheets of the 27-Oct-2026 and 03-Nov-2026 weekly reports (24,681, 24,757 and 24,887 of 25,284); the 20-Oct row comes from the previous-week columns of the 27-Oct report. The chart sheet books all progress made after July in August, so the actual line ends there at 98.4%.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	1.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Preliminary submittals	0.2%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	26.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	26.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
Construction	43.5%	100.0%	99.9%	−0.1%	1.00	▼ Finishing
Testing & commissioning	0.3%	100.0%	87.5%	−12.5%	0.88	▼ Late
Handing over	2.2%	100.0%	33.4%	−66.6%	0.33	▼ Late
Total	100%	**100.0%**	**98.4%**	**−1.6%**	**0.98**	▼ Late

Within construction, the Type 2 structural-steel fence is at 99.5% and the electrical works at 99.7%; all other trades are complete. The P6 update has 391 activities: 370 completed, 21 in progress and none not started. Its scheduled finish is still 02-Nov-2026, 89 days after the contract date, because the file was not rescheduled.

Milestones

Contractual milestones of the P6 schedule. The weekly report's milestone sheet uses other dates and forecasts no delay; both are shown so the difference can be resolved with the contractor.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	06-May-2026	30-Apr-2026	–	–	✓ Done
Preliminary submittals	25-May-2026	–	01-Aug-2026 (actual)	–	✓ Done late
Mobilization	31-May-2026	20-May-2026	02-Aug-2026 (actual)	–	✓ Done late
Shop drawings	22-Jun-2026	–	24-Aug-2026 (actual)	–	✓ Done late
Material submittal & approval	18-Jul-2026	–	19-Sep-2026 (actual)	–	✓ Done late
Fabrication & delivery	04-Aug-2026	–	12-Aug-2026 (actual)	–	✓ Done late
Construction	05-Aug-2026	25-Aug-2026	16-Sep-2026 (marked done)	−73.7	? Works still open
Project completion	05-Aug-2026	05-Aug-2026	02-Nov-2026	−75	▼ Late

The weekly report and the P6 update disagree on the completion date.

The weekly report gives 05-Aug-2026 as the forecast completion (General Information sheet) and 30-Aug-2026 on its milestone sheet, both with no delay. The P6 update finishes the project on 02-Nov-2026, a date that has now passed. P6 marks the Construction and Project Finish milestones complete on 16-Sep-2026, yet four construction activities are still open: the chain-link gate, lighting fixtures, the electrical gate barrier and the smoke and heat detectors.

Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

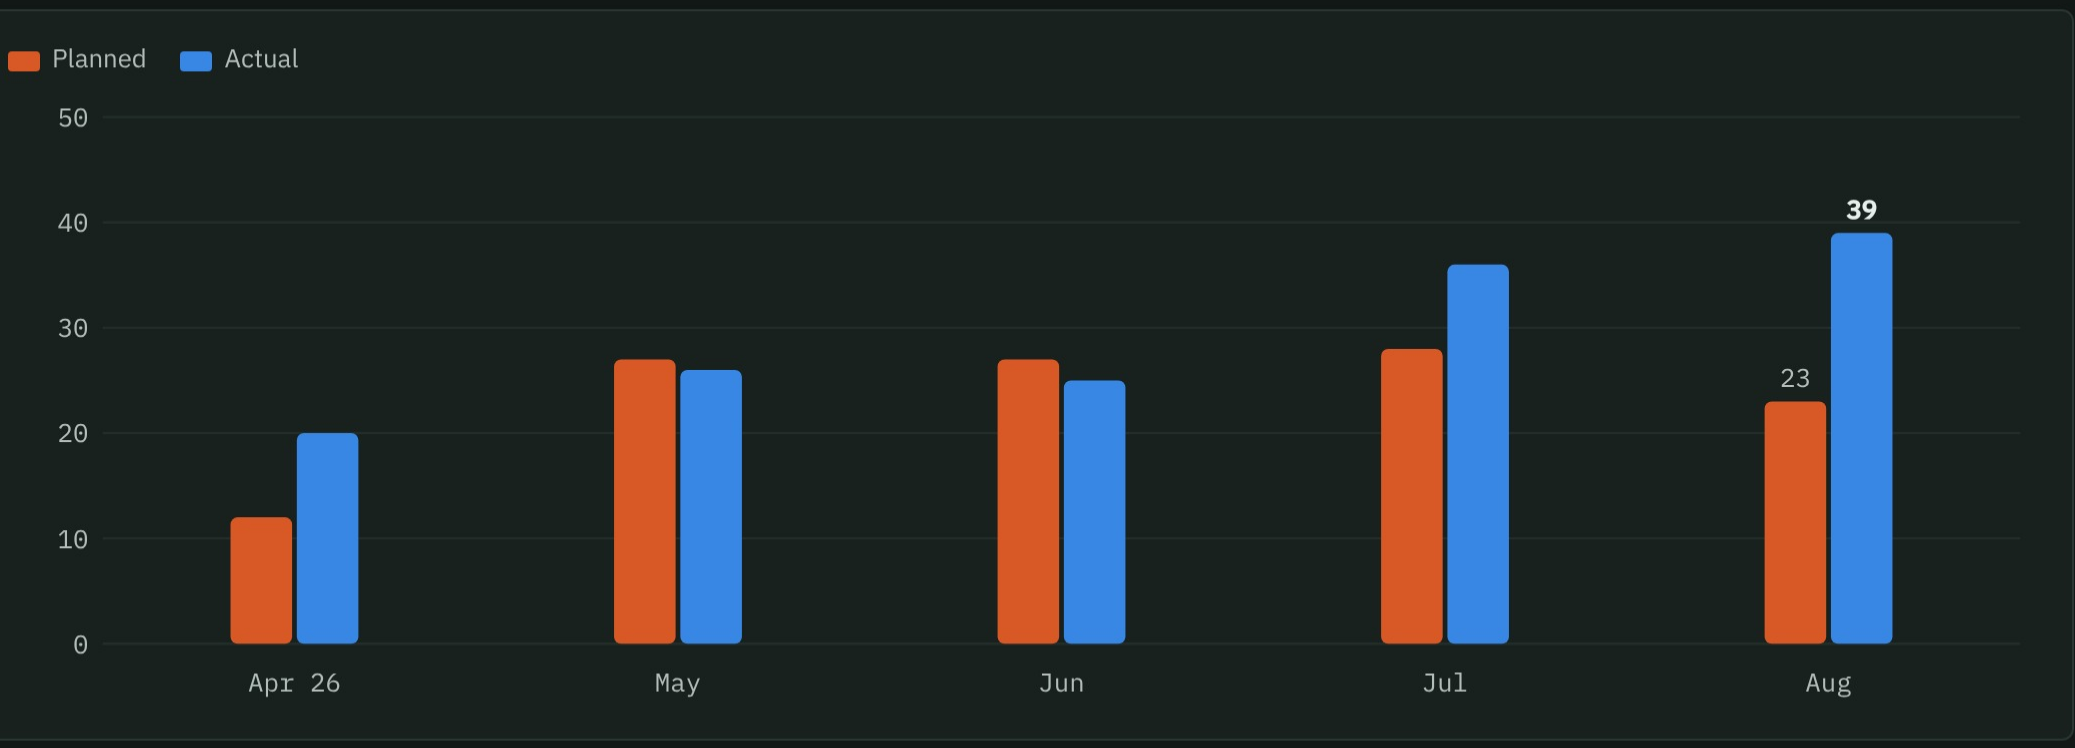

The manpower sheet has no figures after August 2026. The weekly report summary repeats August's head count: 39 actual (11 staff, 28 labour) against 23 planned.

Cost and invoicing

Contract value

Original contract value	16,500,001.96
Revised contract value	16,500,001.96
Change orders	0
Potential changes	0

All values in SAR. No change orders are registered. The invoice log also shows a revised value of 21,100,000 and potential changes of 200,000; see Data notes.

Invoices

Invoices submitted	5
Gross value	9,780,875.90
Approved by the consultant	5
Approved by the MODON PM / paid	0 / 0
Deductions and penalties	1,501,000
Net incl. VAT	9,747,007.29
FIR value to date	10,354,344.40

Invoicing is 59.3% of the contract value against 98.4% physical progress. Invoice 5 (06-Aug to 26-Sep-2026) carries a deduction of 1,500,000.

Health, safety and quality

Safety Score 0.80

Safe man-hours (cumulative)	15,737
Man-hours this week	2,160
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	42 / 129

HSE site inspection no. 31 on 02-Nov-2026.

Quality Score 0.88

FIRs issued / closed / pending	858 / 842 / 16
MIRs issued / closed / pending	92 / 90 / 2
NCRs issued / closed	4 / 4
Site instructions issued / closed	4 / 4
Approved shop drawings	72 of 75
Approved material submittals	103 of 113

QC observation no. 25, 11-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Remaining construction items	Contractor	Chain-link gate, lighting fixtures (final fix), electrical gate barrier and smoke and heat detectors are still at 0% in P6. They were due 28-Oct-2026 and have −70.5 to −73.7 days of float.
Testing and commissioning	Contractor	Electrical and mechanical systems are 88% complete; they were due 29-Oct and 01-Nov-2026.
Close-out documents	Contractor / Consultant	As-built drawings 85% prepared and 85% reviewed; operational spares 85% submitted, 35% inspected and 85% accepted; warranties 35%; manuals and training 20–24%.
Snag list and initial handover	Contractor / MODON	Snag-list rectification, demobilization and initial handover are still at 0%, although P6 scheduled handover for 02-Nov-2026.
Reopened issues	Contractor	The issue log reopened four issues this week: Type 2 fence accessory shortages, the medium-voltage cable on the Type 2 alignment, dirt-road works held up by backfill, equipment and payments, and lighting supplies. Their target dates (10–15 Oct 2026) have passed.
Invoice approval	MODON	All five invoices are approved by the consultant, but none is approved by the MODON PM or paid. Deductions and penalties of 1,501,000 SAR are applied.

The risk log still marks all six risks closed, and the gate-width issue (RFI-0009) remains closed.

Data notes

- Physical % complete is taken from the Progress sheet of the weekly report (earned vs budgeted man-hours). The "Actual %" column in the P6 PDF layouts and the earned-value cells of the weekly report are cost-based, so they are not used.
- This week's gain is the difference between the earned man-hours of the 03-Nov-2026 report (24,887) and the 27-Oct-2026 report (24,757); the previous-week columns of the 03-Nov report agree. Quantities this week are not available.
- Dates disagree inside the weekly report: the General Information sheet gives site handover 06-May-2026 and completion 05-Aug-2026 (as does the P6 baseline), while the Milestones sheet gives award 16-Apr-2026, handover 30-Apr-2026 and completion 30-Aug-2026. The lower table of the Milestones sheet belongs to another fence project (SUD1-05-015).
- The weekly report still forecasts completion on 05-Aug-2026 with zero variance, although that date has passed; P6 forecasts 02-Nov-2026.
- The P6 file uploaded this week is named DD03-11-2026 but has a data date of 27-Oct-2026 and was not rescheduled: activity percentages were updated, but its remaining dates (28-Oct to 02-Nov-2026) are now in the past.
- The FIR summary records inspections on 01-Nov-2026 for three chain-link gates (one 6 m, two 5 m) and 4.3 LM of Type 1 steel fence with pedestrian gates, while the P6 file still shows the chain-link gate activity at 0%.
- In the P6 update, the Construction and Project Finish milestones are marked complete on 16-Sep-2026 while 21 activities are still in progress. Actual dates start on 13-Jul-2026 (Project Start), two months after handover; the electrical gate barrier shows an actual start of 12-Apr-2026, before the contract award.
- The Major Quantities sheet is not usable: actual quantities are fractions of one unit (for example 0.25 LM of 18,500 LM of chain-link fence) and its resource table is from another project. The scope section is left out.
- The Procurement sheet carries another project's code and has delivery data for only a few minor items, so the procurement section is left out.
- The invoice log shows a revised contract value of 21,100,000, an estimate at completion of 20,900,000 and potential changes of 200,000, against 16,500,001.96 and 0 in the General Information and Weekly Progress Report sheets.

- The project stage is still "Mobilization" in the weekly report, and the MODON PM field is empty; the PM's name is taken from the HSE inspection sheet. The quality checklist names the contractor (HMA) as the consultant.
- The issue log reopened four items that were marked closed last week, keeping their original target dates; the risk log still marks all items closed while its "current status" column reads "In Progress", and the Top 5 issues panel is empty. Several summary panels show #REF! or #N/A errors.

- Only one of the five uploaded photos has a date and GPS stamp (03-Nov-2026). The fifth photo, a floodlight lying beside a wall, is left out to keep an even number.

Compiled 05-Nov-2026 from the weekly report with data date 03-Nov-2026 and the P6 file uploaded with it (data date 27-Oct-2026), in folder W06 - 05-Nov-2026.
