Playgrounds Initiative: Qassim Oasis, Hail and Tabuk Industrial City

مبادرة الملاعب بالمنطقة الوسطى (حائل, واحة القصيم, تبوك)

CLIENT	CONTRACTOR	CONSULTANT	COMMENCEMENT	CONTRACT COMPLETION	P6 FORECAST FINISH
MODON	ADV	Egis	17-Feb-2026	16-Dec-2026	10-Feb-2027

Scope: football, basketball and padel playgrounds, air domes (Qassim and Tabuk), toilet buildings, landscaping, tanks and site services at three sites: Qassim Oasis, Hail and Tabuk Industrial City.

Status at a glance

Progress is physical % complete weighted by planned man-hours (labour units) in the P6 update, rolled up from the activities' physical % complete; planned progress is spread linearly over the recovery baseline dates up to the P6 data date of 09-Oct-2026. The project is 67.93% complete against 76.61% planned, behind by 8.68% (SPI 0.89). Hail is furthest behind, at 65.96% against 81.93%.

PHYSICAL % COMPLETE
67.93% / 76.61% plan
▼ SPI 0.89 8.68% behind plan

PROGRESS THIS WEEK
— not stated
This week's files give no weekly increment.

CONTRACT TIME ELAPSED
78.1% · day 236 of 302
▼ P6 finish 10-Feb-2027

FORECAST DELAY TO COMPLETION
56 days
Contract 16-Dec-2026, P6 forecast 10-Feb-2027, float −47.4 days

The P6 update forecasts completion on 10-Feb-2027, 56 days after the contract date.

Substantial completion of all works moves from 16-Dec-2026 to 10-Feb-2027, with −47.4 days of total float. 205 of the 338 open activities have negative float, and the failed-start list of 11-Oct-2026 names 77 activities that did not start on time (Qassim 28, Hail 31, Tabuk 18). The air domes are the largest gap: Qassim is at 39.96% physical against 74.00% planned and Tabuk at 35.13% against 65.24%.

Progress by phase

Physical % complete by site and phase, weighted by planned man-hours from the P6 update (data date 09-Oct-2026); planned from the recovery baseline, spread linearly. Weight is the share of man-hours. Engineering and procurement carry no man-hours in the schedule, so they cannot be shown.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Qassim Oasis	**36.4%**	**76.81%**	**67.79%**	**−9.02%**	**0.88**	▼ Behind
Construction	34.8%	80.31%	70.24%	−10.07%	0.87	▼ Behind
Project closeout	1.6%	2.92%	16.04%	+13.12%	5.49	▲ Ahead
Hail	**27.2%**	**81.93%**	**65.96%**	**−15.97%**	**0.81**	▼ Behind
Construction	25.6%	87.01%	69.52%	−17.49%	0.80	▼ Behind
Project closeout	1.6%	2.92%	10.79%	+7.87%	3.70	▲ Ahead
Tabuk	**36.4%**	**72.44%**	**69.53%**	**−2.91%**	**0.96**	▼ Behind
Construction	34.8%	75.73%	72.06%	−3.67%	0.95	▼ Behind

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Project closeout	1.6%	2.92%	16.04%	+13.12%	5.49	▲ Ahead
Total	100%	**76.61%**	**67.93%**	**−8.68%**	**0.89**	▼ Behind

The P6 update (project PG-Reco-4, data date 09-Oct-2026) has 1,929 activities: 1,591 completed, 205 in progress and 133 not started. Its scheduled finish is 10-Feb-2027, against a must-finish date of 16-Dec-2026. Closeout runs ahead of plan because as-built drawings started early.

Scope of work: sites and work packages

The schedule holds no quantities, so the scope is shown as the construction work packages at each site, measured in planned man-hours from the P6 update: man-hours, man-hours completed (physical % complete × man-hours) and planned % to date from the recovery baseline. This week's files give no previous figures, so “This week” shows –.

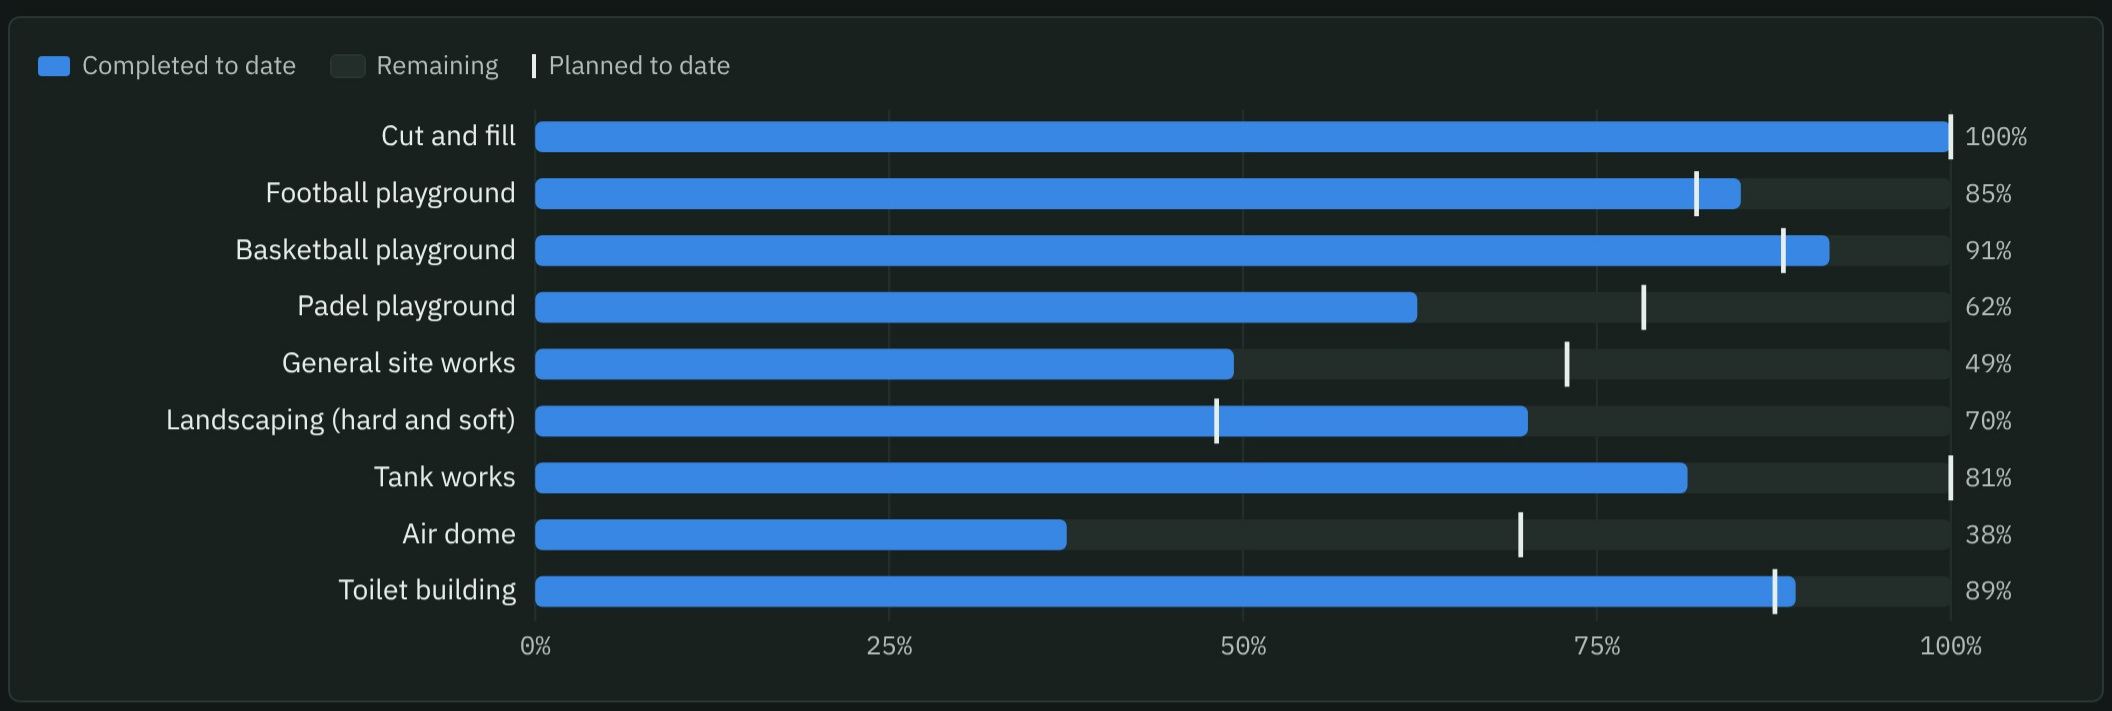

WORK PACKAGE	SITE	UNIT	MAN-HOURS	COMPLETED	THIS WEEK	REMAINING	% COMPLETE	PLANNED %
Cut and fill	Qassim	h	376	376	–	0	100.0%	100.0%
	Hail	h	376	376	–	0	100.0%	100.0%
	Tabuk	h	376	376	–	0	100.0%	100.0%
	Total	h	**1,128**	**1,128**	–	**0**	**100.0%**	100.0%
Football playground	Qassim	h	864	741.6	–	122.4	85.8%	82.6%
	Hail	h	864	713.1	–	150.9	82.5%	82.1%
	Tabuk	h	864	752.8	–	111.2	87.1%	81.4%
	Total	h	**2,592**	**2,208**	–	**384.5**	**85.2%**	82.0%
Basketball playground	Qassim	h	608	564	–	44	92.8%	88.6%
	Tabuk	h	608	547.8	–	60.2	90.1%	87.7%
	Total	h	**1,216**	**1,112**	–	**104.2**	**91.4%**	88.2%
Padel playground	Qassim	h	424	242.8	–	181.2	57.3%	79.2%
	Tabuk	h	424	285.6	–	138.4	67.4%	77.4%
	Total	h	**848**	**528.4**	–	**319.6**	**62.3%**	78.3%
General site works	Qassim	h	1,996	966.5	–	1,030	48.4%	71.1%
	Hail	h	1,996	888	–	1,108	44.5%	78.6%
	Tabuk	h	1,996	1,101	–	895	55.2%	69.0%

WORK PACKAGE	SITE	UNIT	MAN-HOURS	COMPLETED	THIS WEEK	REMAINING	% COMPLETE	PLANNED %
	Total	h	**5,988**	**2,956**	**–**	**3,033**	**49.4%**	72.9%
Landscaping (hard and soft)	Qassim	h	392	259	–	133	66.1%	49.8%
	Hail	h	392	244.8	–	147.2	62.4%	54.0%
	Tabuk	h	392	320.9	–	71.1	81.9%	40.6%
	Total	h	**1,176**	**824.7**	**–**	**351.3**	**70.1%**	48.1%
Tank works	Qassim	h	628	576	–	52	91.7%	100.0%
	Hail	h	628	484	–	144	77.1%	100.0%
	Tabuk	h	628	473.6	–	154.4	75.4%	100.0%
	Total	h	**1,884**	**1,534**	**–**	**350.4**	**81.4%**	100.0%
Air dome	Qassim	h	1,116	446	–	670	40.0%	74.0%
	Tabuk	h	1,116	392.1	–	723.9	35.1%	65.2%
	Total	h	**2,232**	**838.1**	**–**	**1,394**	**37.5%**	69.6%
Toilet building	Qassim	h	1,708	1,526	–	181.6	89.4%	86.8%
	Hail	h	1,708	1,440	–	268	84.3%	99.3%
	Tabuk	h	1,708	1,596	–	112	93.4%	76.6%
	Total	h	**5,124**	**4,562**	**–**	**561.6**	**89.0%**	87.6%

Reported this week

Stamped concrete, curbstone, steel posts for the fence, backfilling of the irrigation network, asphalt, waterproofing of the raft foundation for the glass facade and toilet area, and compaction and levelling (weekly executive summary). Next week: compaction and levelling, asphalt, curbstone, fence installation and stamped concrete.

Air domes and general site works lag most

Air dome: Qassim 39.96% against 74.00% planned, Tabuk 35.13% against 65.24%. General site works are at 44–55% against 69–79% planned at all three sites. Padel playgrounds and tank works are also behind; landscaping and the Qassim and Tabuk toilet buildings are ahead of plan.

Milestones

Baseline from the recovery baseline schedule (Recovery Schedule.01). Forecasts from the Level 5 schedule (PDF, 11-Oct-2026) and the P6 update (XER, data date 09-Oct-2026), which agree on every milestone. Float is the P6 total float.

MILESTONE	BASELINE	LEVEL 5 SCHEDULE FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	17-Feb-2026	17-Feb-2026	17-Feb-2026 (actual)	–	✓ Done
Completion of earthworks (cut and fill)	05-May-2026	05-May-2026	05-May-2026 (actual)	–	✓ Done
Site preparation, work plans, schedule and drawing submittals	04-Aug-2026	16-Sep-2026 (+43 d)	16-Sep-2026 (actual)	–	✓ Done late
Completion of toilet building	28-Oct-2026	28-Nov-2026 (+31 d)	28-Nov-2026	−5.5	▼ Late
Completion of playground works	07-Dec-2026	14-Dec-2026 (+7 d)	14-Dec-2026	+2.6	▼ At risk
Completion of landscape works	16-Dec-2026	25-Jan-2027 (+40 d)	25-Jan-2027	−33.0	▼ Late
Substantial completion: all works	16-Dec-2026	10-Feb-2027 (+56 d)	10-Feb-2027	−47.4	▼ Late

MILESTONE	BASELINE	LEVEL 5 SCHEDULE FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project completion date	16-Dec-2026	10-Feb-2027 (+56 d)	10-Feb-2027	−47.4	▼ Late

Every open contractual milestone is now forecast after its baseline date.

Toilet building completion moves by 31 days, landscape works by 40 days and substantial completion by 56 days. Playground works keeps +2.6 days of float but is forecast 7 days after its baseline. The site preparation and submittals milestone was achieved on 16-Sep-2026, 43 days late.

Procurement of key materials

Physical % complete of the open “delivery to site” activities for key materials (P6 update, data date 09-Oct-2026).



Air dome materials: 60% delivered

At both Qassim and Tabuk, with −38.8 and −47.4 days of float. Tabuk's air dome materials carry the same −47.4 days of float as project completion.

Curtain wall (remaining)

Qassim delivery has not started: fabrication was due to start on 25-Jun-2026 and is now forecast to start on 10-Oct-2026, with delivery from 08-Nov-2026 to 24-Nov-2026. Hail is at 80% and Tabuk at 60%. Fire extinguishers at Hail are at 20%.

Health, safety and quality

This week's upload has no safety statistics or site inspection records (MIR, IR, NCR). The technical submittals register is the only quality record provided. Source: Technical Document Submittals Tracker, % Summary sheet.

Technical submittals

Submitted to date	819
Approved (codes A and B)	677 (82.7%)
Revise and resubmit (code C)	50
Under review	57
Delayed review (5 days or more)	35

Approved / submitted by type

Shop drawings	309 / 375
Document submittals (technical and general)	148 / 183
Material submittals	120 / 137
Pre-qualification	47 / 55
RFIs	30 / 34
Method statements	22 / 22
Material source approvals	1 / 13

9 of the 13 material source approvals are in delayed review.

Open issues and risks

From the failed-start list (11-Oct-2026), the P6 update and the submittals tracker. The files do not assign owners.

ISSUE	SITE	DETAIL
Air dome works	Qassim, Tabuk	Physical progress is 39.96% (Qassim) and 35.13% (Tabuk) against 74.00% and 65.24% planned. Steel cable structure, membrane, air package units, HVAC and lighting installation are on the failed-start list (15 activities).
Site electrical, ELV and fire alarm	All sites	29 of the 77 failed starts: MDB and power panels, wiring, lighting fixtures, fibre optic, telecom, CCTV and fire alarm installation.
Storm water and utility works	All sites	Concrete encasement, backfilling and compaction, and surface reinstatement have not started on time (14 mechanical failed starts, including fire extinguishers and irrigation bubblers).
Water storage tanks	All sites	GRP water tank installation is on the failed-start list at all three sites. Tank works are at 91.72% (Qassim), 77.07% (Hail) and 75.41% (Tabuk) physical complete against 100% planned.
Curtain wall	Qassim, Hail	Fabrication of the remaining curtain wall is on the failed-start list at Qassim and Hail (baseline start 25-Jun-2026, now 10-Oct-2026).
Delayed submittal reviews	All sites	35 submittals are in delayed review, 12 of them shop drawings and 12 document submittals.

Data notes

- This report uses only the W2 upload (data date 11-Oct-2026). It has no physical progress sheet, no S-curve data, no site photos, no manpower, no invoice data and no HSE statistics, so those sections are left out.
- Physical progress was computed from the original P6 XER of this week (the Markdown copy omits the needed fields): each activity's physical % complete weighted by its planned labour units, over the 488 labour-loaded activities, excluding the two “Project Durations” activities that carry 10,000 h of management staff time. Planned % uses the same units in the recovery baseline XER, spread linearly between planned start and finish, up to 09-Oct-2026. Engineering and procurement activities carry no labour units.
- No previous-week or “this week” figures are stated in these files, so progress this week and the this-week column show –.
- The P6 XER has a data date of 09-Oct-2026, while the PDF schedules and the failed-start list are dated 11-Oct-2026.
- Three PDFs (Level 5 schedule, 3-week look-ahead, remaining works) are named MLTX-05-047 although they contain this project (MLTX-02-003).

- The WBS summary and Level 5 PDFs label a cost-loaded percentage as “Performance % complete”. This report uses physical % complete only and does not show those figures.
- 108 in-progress activities in the P6 update have a finish date before its data date (for example Air dome materials, Qassim: 60%, finish 06-Oct-2026). Their remaining durations need updating.
- Hail curtain wall fabrication is on the failed-start list (not started), but the P6 update shows Hail curtain wall delivery 80% complete.
- The submittals tracker has no planned submissions or deadlines (N/A) and its Design Drawings rows show #DIV/0!.

Compiled 28-Oct-2026 from the W2 weekly upload only (data date 11-Oct-2026).
