
Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Development of the Technology City in Dammam-RECOVERY SCHEDULE		195	22-Jul-26 A	05-Mar-27	23-Jun-26	28-Jan-27	14,010,152
Procurement Cycle		187	22-Jul-26 A	05-Mar-27	23-Jun-26	28-Jan-27	0
Short Lead Time Items		187	22-Jul-26 A	05-Mar-27	23-Jun-26	28-Jan-27	0
Infrastructure Networks		187	22-Jul-26 A	05-Mar-27	23-Jun-26	28-Jan-27	0
Softscape and Planting Works		83	27-Oct-26	31-Jan-27	11-Jul-26	17-Oct-26	0
Issuance of Purchase Orders		6	27-Oct-26	02-Nov-26	11-Jul-26	19-Jul-26	0
Main Line Pipes		6	27-Oct-26	02-Nov-26	11-Jul-26	19-Jul-26	0
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	27-Oct-26	02-Nov-26	12-Jul-26	19-Jul-26	0
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and	6	27-Oct-26	02-Nov-26	11-Jul-26	18-Jul-26	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	18-Jul-26	17-Oct-26	0
Main Line Pipes		90	03-Nov-26	31-Jan-27	18-Jul-26	17-Oct-26	0
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	03-Nov-26	31-Jan-27	19-Jul-26	17-Oct-26	0
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gra	90	03-Nov-26	31-Jan-27	18-Jul-26	16-Oct-26	0
Sewage Network		130	27-Oct-26	05-Mar-27	15-Jul-26	21-Nov-26	0
Manufacturing of Material		130	27-Oct-26	05-Mar-27	15-Jul-26	21-Nov-26	0
Testing and Finishes		130	27-Oct-26	05-Mar-27	15-Jul-26	21-Nov-26	0
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	27-Oct-26	05-Mar-27	15-Jul-26	21-Nov-26	0
Storm Drainage Network		164	02-Aug-26 A	03-Feb-27	15-Jul-26	22-Oct-26	0
Manufacturing of Material		100	27-Oct-26	03-Feb-27	15-Jul-26	22-Oct-26	0
Testing and Finishes		100	27-Oct-26	03-Feb-27	15-Jul-26	22-Oct-26	0
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	27-Oct-26	03-Feb-27	15-Jul-26	22-Oct-26	0
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	27-Oct-26	03-Feb-27	15-Jul-26	22-Oct-26	0
Material Delivery & Site Inspection		0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0
Catch Basin Sections		0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0
Potable Water Network		125	02-Aug-26 A	25-Feb-27	08-Jul-26	06-Nov-26	0
Issuance of Purchase Orders		10	27-Oct-26	07-Nov-26	08-Jul-26	19-Jul-26	0
Main Line Sections		6	27-Oct-26	02-Nov-26	08-Jul-26	14-Jul-26	0
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	27-Oct-26	02-Nov-26	08-Jul-26	14-Jul-26	0
Fire Hydrant		10	27-Oct-26	07-Nov-26	08-Jul-26	19-Jul-26	0
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	27-Oct-26	07-Nov-26	08-Jul-26	19-Jul-26	0
Testing and Finishes		10	27-Oct-26	07-Nov-26	08-Jul-26	19-Jul-26	0
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	27-Oct-26	07-Nov-26	08-Jul-26	19-Jul-26	0
Manufacturing of Material		115	03-Nov-26	25-Feb-27	15-Jul-26	06-Nov-26	0
Main Line Sections		90	03-Nov-26	31-Jan-27	15-Jul-26	12-Oct-26	0
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	03-Nov-26	31-Jan-27	15-Jul-26	12-Oct-26	0
Fire Hydrant		60	08-Nov-26	06-Jan-27	20-Jul-26	17-Sep-26	0
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	08-Nov-26	06-Jan-27	20-Jul-26	17-Sep-26	0
Testing and Finishes		110	08-Nov-26	25-Feb-27	20-Jul-26	06-Nov-26	0
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	08-Nov-26	25-Feb-27	20-Jul-26	06-Nov-26	0
Material Delivery & Site Inspection		0	02-Aug-26 A	17-Jan-27	29-Sep-26	29-Sep-26	0
Main Line Sections		0	02-Aug-26 A	17-Jan-27	29-Sep-26	29-Sep-26	0
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Re	0	02-Aug-26 A	17-Jan-27	29-Sep-26	29-Sep-26	0
Irrigation Network		170	22-Jul-26 A	07-Feb-27	15-Jul-26	19-Oct-26	0
Issuance of Purchase Orders		6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0
Main Line Pipes		6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0
Manufacturing of Material		90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0
Main Line Pipes		90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0
1st Material Delivery & Site Inspection		5	22-Jul-26 A	31-Oct-26	05-Oct-26	11-Oct-26	0
Main Line Pipes		5	22-Jul-26 A	31-Oct-26	05-Oct-26	11-Oct-26	0

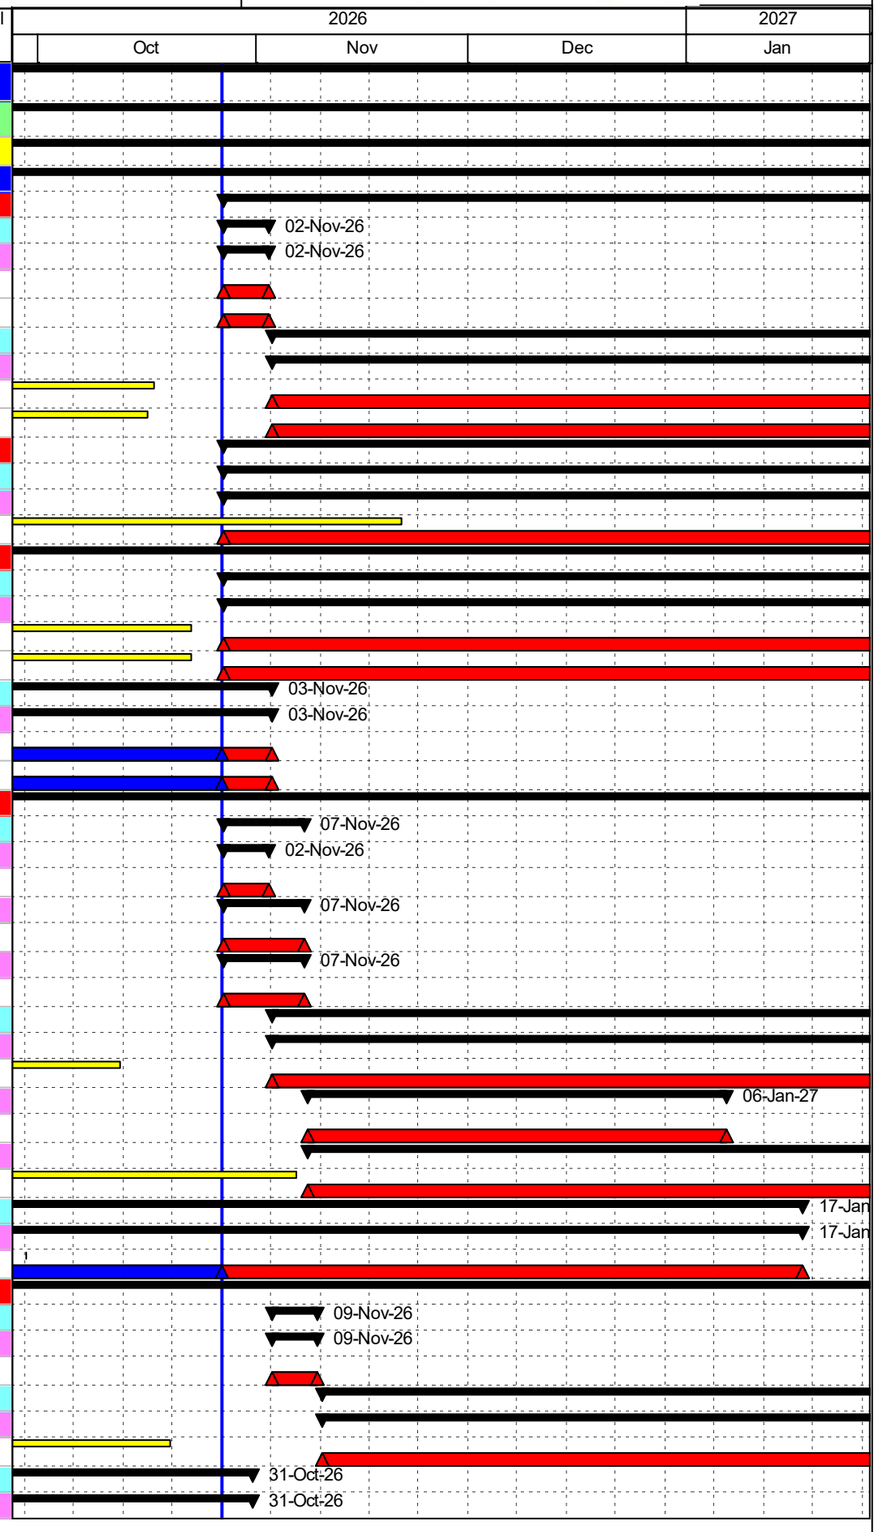


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	22-Jul-26 A	31-Oct-26	05-Oct-26	11-Oct-26	0
Material Delivery & Site Inspection		0	31-Oct-26	31-Oct-26	11-Oct-26	11-Oct-26	0
Main Line Pipes		0	31-Oct-26	31-Oct-26	11-Oct-26	11-Oct-26	0
PRO-R25-IR-DL-1(	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	31-Oct-26	31-Oct-26	11-Oct-26	11-Oct-26	0
Treated Sewage Effluent (Tse)		83	27-Oct-26	31-Jan-27	27-Jun-26	02-Oct-26	0
Issuance of Purchase Orders		6	27-Oct-26	02-Nov-26	27-Jun-26	04-Jul-26	0
Main Line Pipes		6	27-Oct-26	02-Nov-26	27-Jun-26	04-Jul-26	0
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	27-Oct-26	02-Nov-26	27-Jun-26	04-Jul-26	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	04-Jul-26	02-Oct-26	0
Main Line Pipes		90	03-Nov-26	31-Jan-27	04-Jul-26	02-Oct-26	0
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	03-Nov-26	31-Jan-27	04-Jul-26	02-Oct-26	0
Medium Voltage Network		89	27-Oct-26	07-Feb-27	23-Jun-26	19-Oct-26	0
Issuance of Purchase Orders		12	27-Oct-26	09-Nov-26	23-Jun-26	21-Jul-26	0
Cabling Works		12	27-Oct-26	09-Nov-26	23-Jun-26	06-Jul-26	0
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	27-Oct-26	09-Nov-26	23-Jun-26	06-Jul-26	0
Termination and Testing Works		12	27-Oct-26	09-Nov-26	08-Jul-26	21-Jul-26	0
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Netw	12	27-Oct-26	09-Nov-26	08-Jul-26	21-Jul-26	0
Manufacturing of Material		90	10-Nov-26	07-Feb-27	07-Jul-26	19-Oct-26	0
Cabling Works		60	10-Nov-26	08-Jan-27	07-Jul-26	04-Sep-26	0
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	10-Nov-26	08-Jan-27	07-Jul-26	04-Sep-26	0
Termination and Testing Works		90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0
Low Voltage and Street Lighting Network		41	27-Oct-26	13-Dec-26	28-Sep-26	28-Jan-27	0
1st Material Delivery & Site Inspection		15	27-Oct-26	12-Nov-26	28-Sep-26	29-Dec-26	0
Cabling Works		6	27-Oct-26	02-Nov-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	27-Oct-26	02-Nov-26	28-Sep-26	04-Oct-26	0
Lighting Poles Works		6	27-Oct-26	02-Nov-26	28-Sep-26	19-Dec-26	0
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	27-Oct-26	02-Nov-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	27-Oct-26	02-Nov-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	27-Oct-26	02-Nov-26	13-Dec-26	19-Dec-26	0
Distribution Panel Board		6	27-Oct-26	02-Nov-26	24-Oct-26	29-Oct-26	0
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	27-Oct-26	02-Nov-26	24-Oct-26	29-Oct-26	0
Termination and Testing Works		15	27-Oct-26	12-Nov-26	03-Nov-26	29-Dec-26	0
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	27-Oct-26	12-Nov-26	13-Dec-26	29-Dec-26	0
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	27-Oct-26	12-Nov-26	03-Nov-26	21-Nov-26	0
Earthing System Works		6	27-Oct-26	02-Nov-26	03-Dec-26	09-Dec-26	0
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	27-Oct-26	02-Nov-26	03-Dec-26	09-Dec-26	0
Material Delivery & Site Inspection		35	03-Nov-26	13-Dec-26	05-Oct-26	28-Jan-27	0
Cabling Works		0	03-Nov-26	03-Nov-26	05-Oct-26	05-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	03-Nov-26	03-Nov-26	05-Oct-26	05-Oct-26	0
Lighting Poles Works		18	03-Nov-26	23-Nov-26	05-Oct-26	20-Dec-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting I	18	03-Nov-26	23-Nov-26	05-Oct-26	25-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	03-Nov-26	03-Nov-26	05-Oct-26	05-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	03-Nov-26	03-Nov-26	20-Dec-26	20-Dec-26	0
Distribution Panel Board		0	03-Nov-26	03-Nov-26	31-Oct-26	31-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting N	0	03-Nov-26	03-Nov-26	31-Oct-26	31-Oct-26	0
Termination and Testing Works		26	14-Nov-26	13-Dec-26	21-Nov-26	28-Jan-27	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	14-Nov-26	13-Dec-26	30-Dec-26	28-Jan-27	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	14-Nov-26	13-Dec-26	21-Nov-26	21-Dec-26	0
Earthing System Works		0	03-Nov-26	03-Nov-26	10-Dec-26	10-Dec-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	03-Nov-26	03-Nov-26	10-Dec-26	10-Dec-26	0
Telecom Network		83	27-Oct-26	31-Jan-27	07-Jul-26	11-Oct-26	0
Issuance of Purchase Orders		6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0

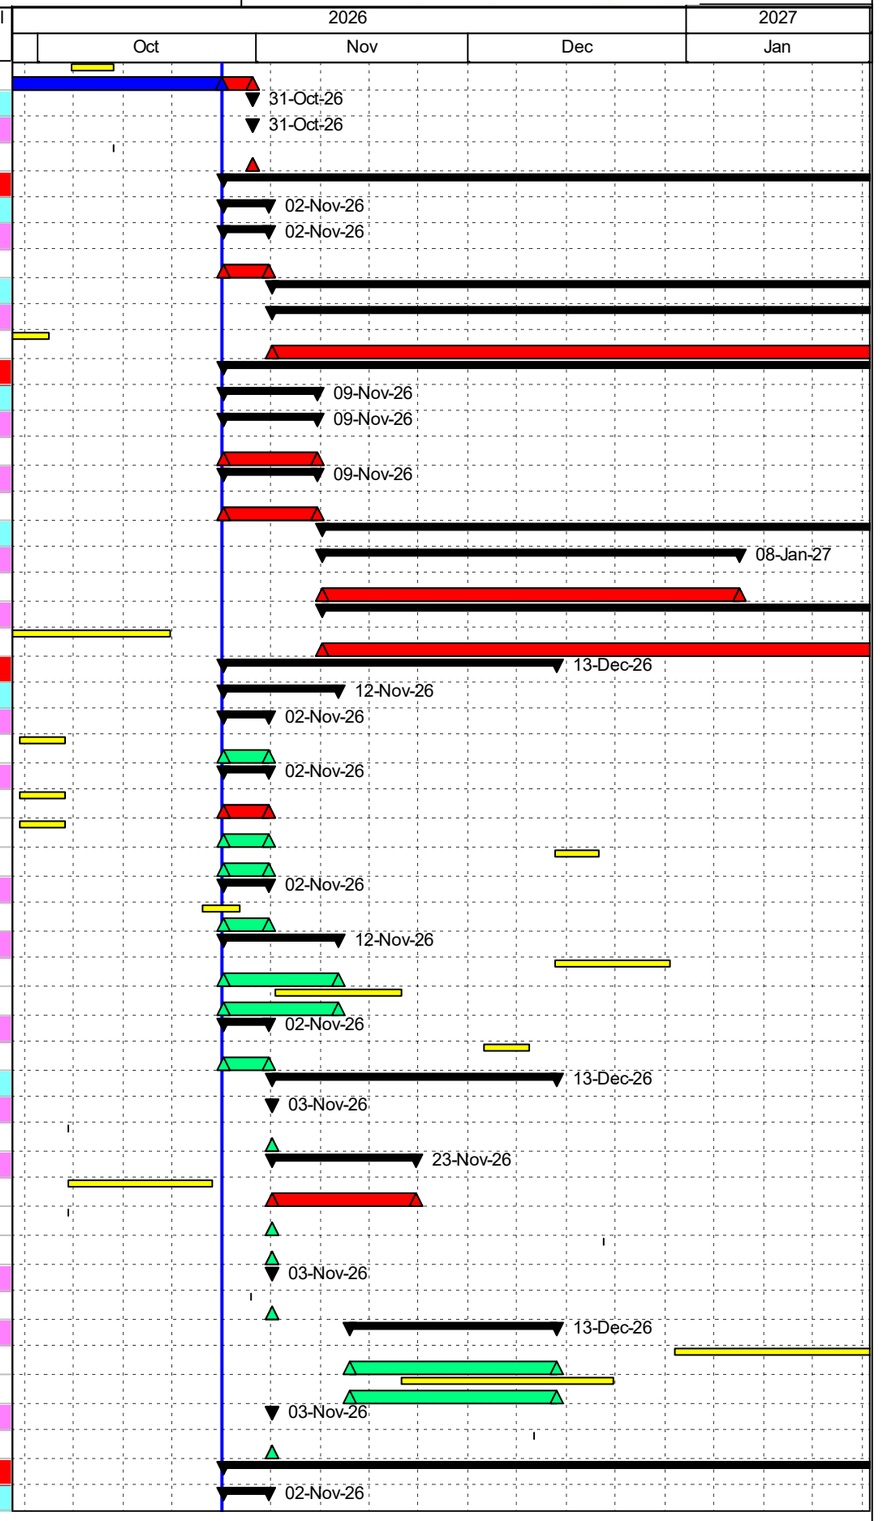


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Ducts Works		6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
Manholes Works		6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
CCTV System Wroks		6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	27-Oct-26	02-Nov-26	07-Jul-26	13-Jul-26	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	14-Jul-26	11-Oct-26	0
Ducts Works		60	03-Nov-26	01-Jan-27	14-Jul-26	11-Sep-26	0
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	03-Nov-26	01-Jan-27	14-Jul-26	11-Sep-26	0
Manholes Works		90	03-Nov-26	31-Jan-27	14-Jul-26	11-Oct-26	0
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	03-Nov-26	31-Jan-27	14-Jul-26	11-Oct-26	0
CCTV System Wroks		90	03-Nov-26	31-Jan-27	14-Jul-26	11-Oct-26	0
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	03-Nov-26	31-Jan-27	14-Jul-26	11-Oct-26	0
Superstructure Works		90	27-Oct-26	24-Jan-27	13-Jul-26	11-Oct-26	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	13-Jul-26	11-Oct-26	0
Softscape and Planting Works		90	27-Oct-26	24-Jan-27	13-Jul-26	11-Oct-26	0
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	27-Oct-26	24-Jan-27	13-Jul-26	11-Oct-26	0
Long Lead Time Items		77	26-Aug-26 A	25-Dec-26	23-Jun-26	09-Nov-26	0
Infrastructure Networks		20	27-Oct-26	18-Nov-26	23-Jun-26	15-Jul-26	0
CCTV System Wroks of Telecom Network		20	27-Oct-26	18-Nov-26	23-Jun-26	15-Jul-26	0
Issuance of Purchase Orders		20	27-Oct-26	18-Nov-26	23-Jun-26	15-Jul-26	0
PRO-CTV-LL-PO-1(	Issuance of Purchase Order for Low Current Works of CCTV Complete System with	20	27-Oct-26	18-Nov-26	23-Jun-26	15-Jul-26	0
Superstructure Works		77	26-Aug-26 A	25-Dec-26	04-Jul-26	09-Nov-26	0
Pump Stations		59	26-Aug-26 A	22-Dec-26	07-Aug-26	09-Nov-26	0
Manufacturing of Material		60	26-Aug-26 A	17-Nov-26	07-Aug-26	05-Oct-26	0
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	26-Aug-26 A	17-Nov-26	07-Aug-26	05-Oct-26	0
Material Shipping/Custom Clearance/Delivery		30	17-Nov-26	22-Dec-26	06-Oct-26	09-Nov-26	0
PRO-SPS-LL-SH/DI	Material Delivery for Electromechanical Works for Pump Stations	30	17-Nov-26	22-Dec-26	06-Oct-26	09-Nov-26	0
Lift Stations		60	27-Oct-26	25-Dec-26	07-Aug-26	05-Oct-26	0
Manufacturing of Material		60	27-Oct-26	25-Dec-26	07-Aug-26	05-Oct-26	0
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	27-Oct-26	25-Dec-26	07-Aug-26	05-Oct-26	0
Storage Tank (TSE)		30	27-Oct-26	30-Nov-26	04-Jul-26	06-Aug-26	0
Issuance of Purchase Orders		30	27-Oct-26	30-Nov-26	04-Jul-26	06-Aug-26	0
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	27-Oct-26	30-Nov-26	04-Jul-26	06-Aug-26	0
Construction Works		189	02-Aug-26 A	11-Jan-27	15-Jul-26	11-Jan-27	14,010,152
Infrastructure Networks		168	02-Aug-26 A	11-Jan-27	15-Jul-26	22-Oct-26	2,917,507
Storm Drainage Network		113	02-Aug-26 A	23-Nov-26	15-Jul-26	29-Aug-26	2,505,375
FROM MH-25:MH-12		110	02-Aug-26 A	21-Nov-26	15-Jul-26	29-Aug-26	2,099,018
Main Line Sections		18	02-Aug-26 A	12-Nov-26	15-Jul-26	04-Aug-26	1,787,973
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	07-Nov-26	15-Jul-26	18-Jul-26	496,659
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	07-Nov-26	19-Jul-26	23-Jul-26	893,986
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	12-Nov-26	25-Jul-26	04-Aug-26	397,327
Manholes		11	17-Oct-26 A	21-Nov-26	09-Aug-26	29-Aug-26	181,625
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	17-Oct-26 A	08-Nov-26	09-Aug-26	16-Aug-26	49,534
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network	7	08-Nov-26	16-Nov-26	17-Aug-26	24-Aug-26	82,557
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	4	16-Nov-26	21-Nov-26	25-Aug-26	29-Aug-26	49,534
Catch Basin Sections		10	08-Nov-26	19-Nov-26	17-Aug-26	27-Aug-26	129,420
CO-SD-CB-140	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	10	08-Nov-26	19-Nov-26	17-Aug-26	27-Aug-26	129,420
FROM MH-12:MH-01		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
Main Line Sections		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
Sewage Network		29	22-Oct-26 A	29-Nov-26	03-Aug-26	30-Aug-26	267,063
FROM MH-18:MH-10		29	22-Oct-26 A	29-Nov-26	03-Aug-26	30-Aug-26	173,901

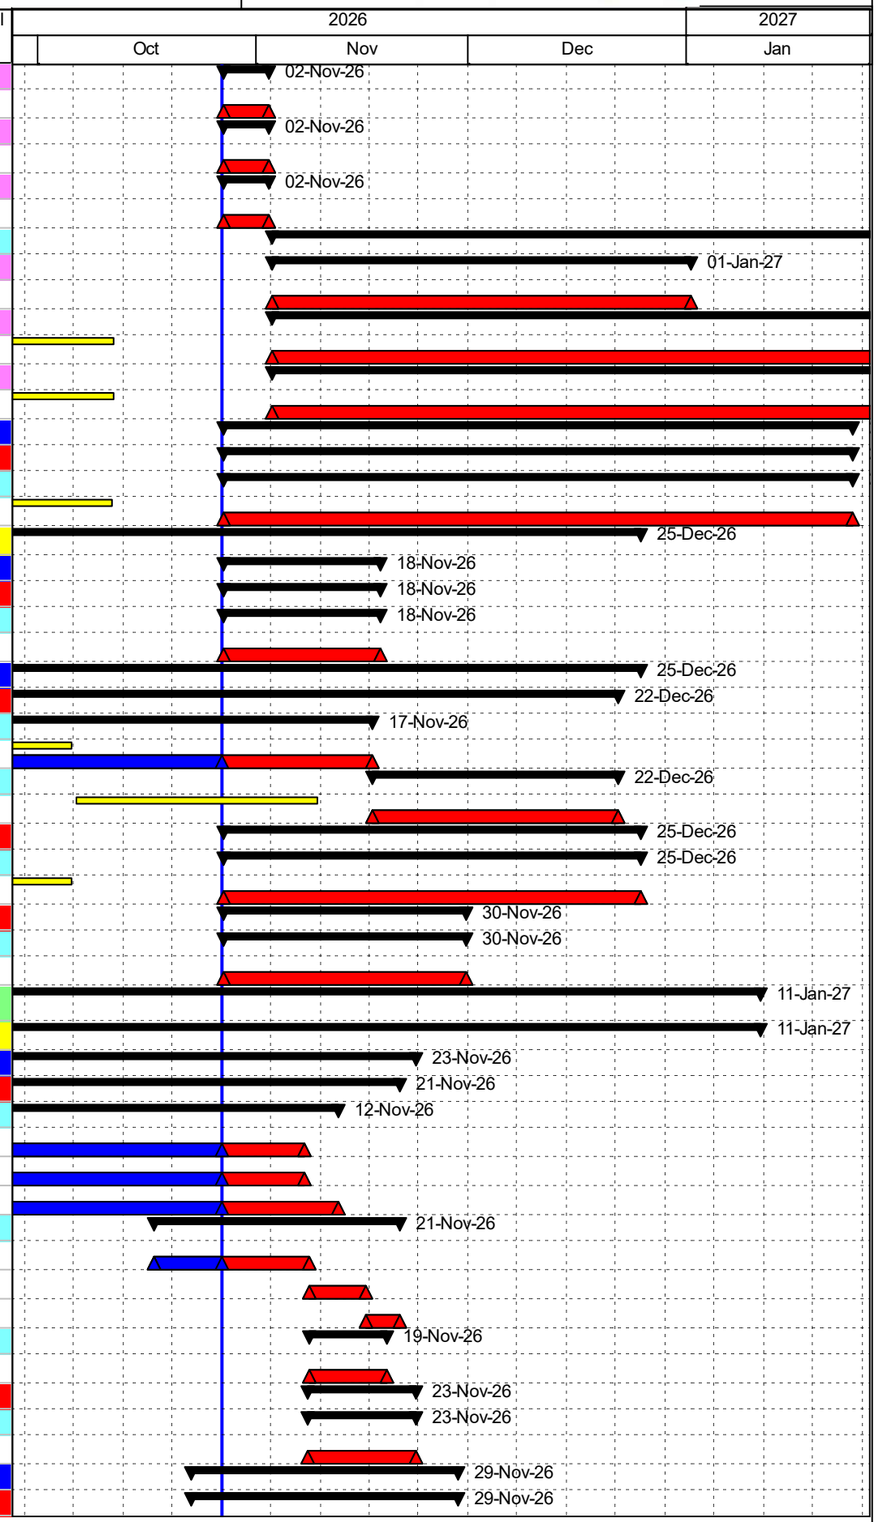


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Main Line Sections		29	22-Oct-26 A	29-Nov-26	03-Aug-26	30-Aug-26	173,901
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	22-Oct-26 A	15-Nov-26	03-Aug-26	16-Aug-26	62,108
CO-SW-ML-120	Pipes Laying Works for Main Lines of Sewage Network	12	15-Nov-26	29-Nov-26	17-Aug-26	30-Aug-26	111,794
FROM MH-10:MH-01		6	15-Nov-26	22-Nov-26	17-Aug-26	23-Aug-26	93,161
Main Line Sections		6	15-Nov-26	22-Nov-26	17-Aug-26	23-Aug-26	93,161
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network	6	15-Nov-26	22-Nov-26	17-Aug-26	23-Aug-26	93,161
Potable Water Network		8	21-Oct-26 A	11-Jan-27	14-Oct-26	22-Oct-26	145,069
Main Line Sections		8	21-Oct-26 A	11-Jan-27	14-Oct-26	22-Oct-26	145,069
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network	8	21-Oct-26 A	11-Jan-27	14-Oct-26	22-Oct-26	145,069
Superstructure Work		164	02-Aug-26 A	30-Nov-26	15-Aug-26	11-Jan-27	11,092,645
Utility Buildings		57	23-Sep-26 A	21-Nov-26	07-Sep-26	26-Dec-26	2,293,824
Pump Station		20	27-Oct-26	18-Nov-26	02-Dec-26	26-Dec-26	775,847
Architectural work		15	27-Oct-26	12-Nov-26	02-Dec-26	20-Dec-26	640,717
CO-UB-PS-260	Executing Masonry Works for Pump station building	5	27-Oct-26	01-Nov-26	02-Dec-26	08-Dec-26	183,776
CO-UB-PS-270	Executing Plastering Works for Pump station building	5	02-Nov-26	07-Nov-26	08-Dec-26	14-Dec-26	229,720
CO-UB-PS-280	Executing Painting Works for Pump station building	5	08-Nov-26	12-Nov-26	14-Dec-26	20-Dec-26	227,221
Electrical work		5	14-Nov-26	18-Nov-26	20-Dec-26	26-Dec-26	135,130
CO-UB-PS-290	Lighting system for pump house	5	14-Nov-26	18-Nov-26	20-Dec-26	26-Dec-26	135,130
Lift Station		57	23-Sep-26 A	18-Nov-26	15-Oct-26	23-Nov-26	479,260
Civil work		57	23-Sep-26 A	18-Nov-26	15-Oct-26	23-Nov-26	479,260
Super structure		57	23-Sep-26 A	18-Nov-26	15-Oct-26	23-Nov-26	479,260
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	29-Oct-26	15-Oct-26	22-Oct-26	84,081
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	29-Oct-26	24-Oct-26	02-Nov-26	84,081
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	29-Oct-26	03-Nov-26	03-Nov-26	50,448
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	2	17-Oct-26 A	01-Nov-26	04-Nov-26	05-Nov-26	8,408
CO-UB-LS-330	Waterproofing for Walls columns	4	01-Nov-26	05-Nov-26	07-Nov-26	10-Nov-26	84,081
CO-UB-LS-340	Formwork for pump roof	5	05-Nov-26	11-Nov-26	11-Nov-26	16-Nov-26	84,081
CO-UB-LS-350	Steel fixing for pump roof	6	11-Nov-26	18-Nov-26	17-Nov-26	23-Nov-26	84,081
Potable Water Tank		21	27-Oct-26	21-Nov-26	07-Sep-26	01-Oct-26	201,053
Structural Work		15	27-Oct-26	14-Nov-26	07-Sep-26	24-Sep-26	118,429
CO-UB-PWT-120	Plain Concrete works	3	27-Oct-26	31-Oct-26	07-Sep-26	09-Sep-26	24,787
CO-UB-PWT-130	Form work for Tank Foundation	5	31-Oct-26	05-Nov-26	10-Sep-26	15-Sep-26	41,312
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation	6	05-Nov-26	12-Nov-26	16-Sep-26	22-Sep-26	38,558
CO-UB-PWT-150	Casting concrete for Tank Foundation	1	12-Nov-26	14-Nov-26	24-Sep-26	24-Sep-26	13,771
Tank Shell Erection&Roof Installation		6	14-Nov-26	21-Nov-26	26-Sep-26	01-Oct-26	82,625
CO-UB-PWT-160	Bottom ring installation	6	14-Nov-26	21-Nov-26	26-Sep-26	01-Oct-26	82,625
IrrigationTank		21	27-Oct-26	19-Nov-26	23-Nov-26	16-Dec-26	201,053
Structural Work		15	27-Oct-26	12-Nov-26	23-Nov-26	09-Dec-26	118,429
CO-UB-IRT-160	Plain Concrete works	3	27-Oct-26	29-Oct-26	23-Nov-26	25-Nov-26	24,787
CO-UB-IRT-170	Form work for Tank Foundation	6	31-Oct-26	05-Nov-26	26-Nov-26	02-Dec-26	41,312
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation	5	07-Nov-26	11-Nov-26	03-Dec-26	08-Dec-26	38,558
CO-UB-IRT-190	Casting concrete for Tank Foundation	1	12-Nov-26	12-Nov-26	09-Dec-26	09-Dec-26	13,771
Tank Shell Erection&Roof Installation		6	14-Nov-26	19-Nov-26	10-Dec-26	16-Dec-26	82,625
CO-UB-IRT-200	Bottom ring installation	6	14-Nov-26	19-Nov-26	10-Dec-26	16-Dec-26	82,625
Control Room		19	24-Oct-26 A	19-Nov-26	28-Oct-26	25-Nov-26	636,611
Civil Work		8	24-Oct-26 A	31-Oct-26	28-Oct-26	05-Nov-26	252,242
CO-UB-CR-140	Pouring Beams and Slab For Control Room	8	24-Oct-26 A	31-Oct-26	28-Oct-26	05-Nov-26	252,242
Finishing Work		17	01-Nov-26	19-Nov-26	07-Nov-26	25-Nov-26	384,369
Architictural work		16	01-Nov-26	18-Nov-26	07-Nov-26	24-Nov-26	192,184
CO-UB-CR-150	Brick Work For Control Room	9	01-Nov-26	10-Nov-26	07-Nov-26	16-Nov-26	96,092
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	7	11-Nov-26	18-Nov-26	17-Nov-26	24-Nov-26	96,092
Mechanical Work		8	11-Nov-26	19-Nov-26	17-Nov-26	25-Nov-26	192,184
HVAC System		4	11-Nov-26	15-Nov-26	17-Nov-26	21-Nov-26	96,092

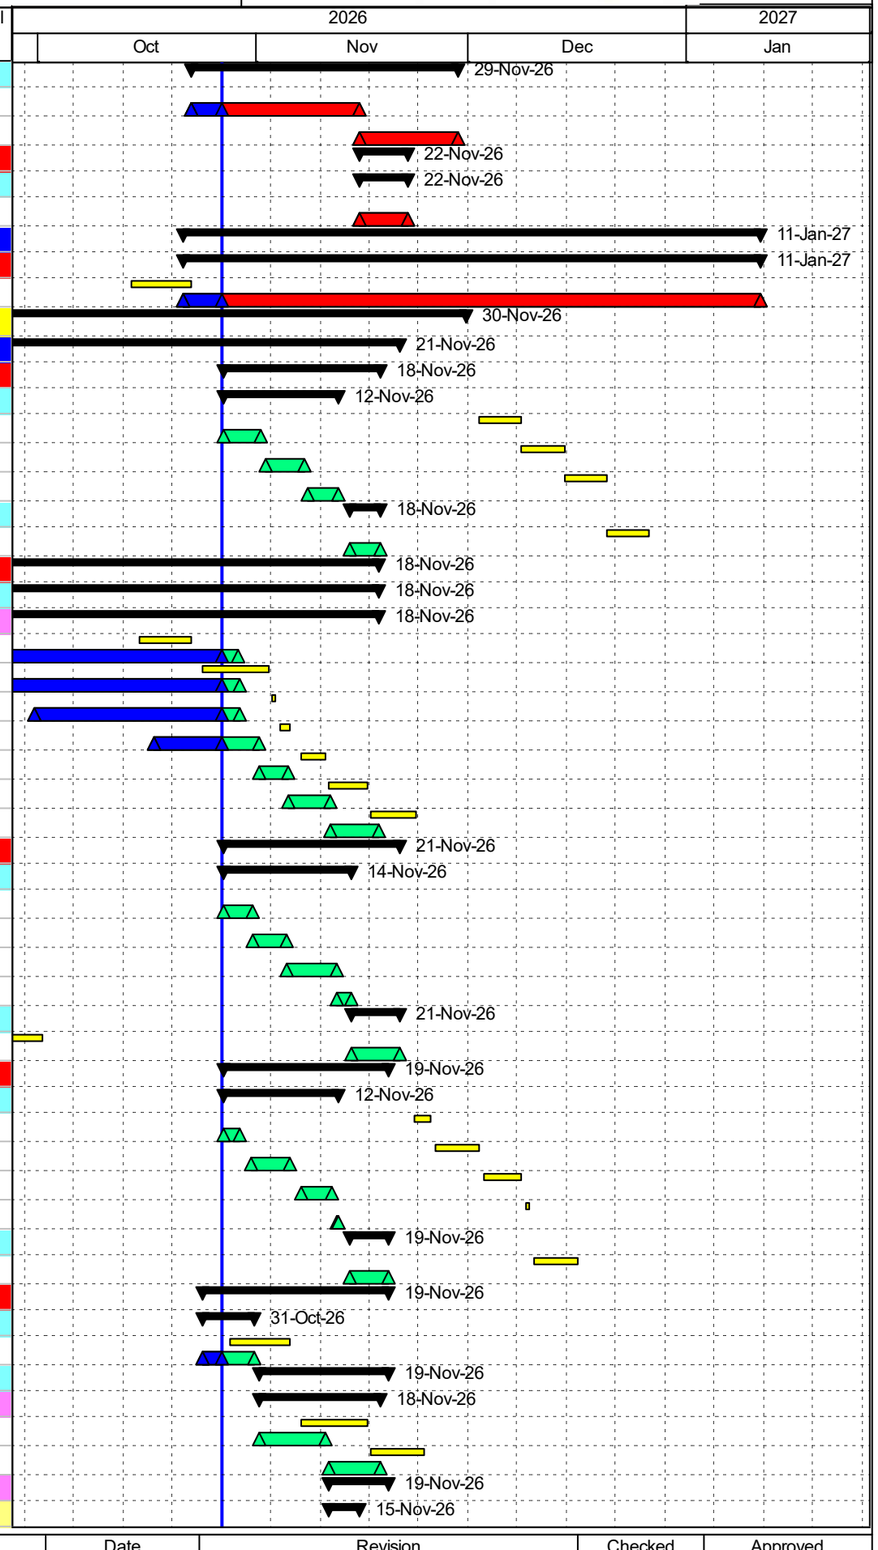


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with suppc	4	11-Nov-26	15-Nov-26	17-Nov-26	21-Nov-26	96,092
Fire Fitting System		4	16-Nov-26	19-Nov-26	22-Nov-26	25-Nov-26	96,092
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between r	4	16-Nov-26	19-Nov-26	22-Nov-26	25-Nov-26	96,092
Fence and Gaurd Room		164	02-Aug-26 A	30-Nov-26	15-Aug-26	11-Jan-27	8,798,821
Gaurd Room Work		61	20-Oct-26 A	21-Nov-26	29-Aug-26	05-Oct-26	115,200
Civil Work		61	20-Oct-26 A	21-Nov-26	29-Aug-26	05-Oct-26	115,200
A1000	Excavation Work For Gaurd Room Foundation	7	20-Oct-26 A	29-Oct-26	29-Aug-26	05-Sep-26	0
A1010	Pouring for Plain Concrete	4	23-Oct-26 A	29-Oct-26	06-Sep-26	09-Sep-26	42,000
A1020	Pouring R.C Footing For Gaurd Room	11	25-Oct-26 A	09-Nov-26	10-Sep-26	22-Sep-26	60,600
A1030	Pouring R.C Columns For Gaurd Room	10	09-Nov-26	21-Nov-26	24-Sep-26	05-Oct-26	12,600
Fence Work		164	02-Aug-26 A	30-Nov-26	15-Aug-26	11-Jan-27	8,683,621
Northern Fence N01:N03		50	21-Oct-26 A	24-Nov-26	29-Aug-26	14-Nov-26	2,228,030
Finishing Work		50	21-Oct-26 A	24-Nov-26	29-Aug-26	14-Nov-26	2,228,030
Electrical Work		25	27-Oct-26	24-Nov-26	29-Aug-26	27-Sep-26	43,078
CO-SU-FE-N-EL-	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	27-Oct-26	04-Nov-26	29-Aug-26	06-Sep-26	17,844
CO-SU-FE-N-EL-	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	27-Oct-26	04-Nov-26	29-Aug-26	06-Sep-26	8,182
CO-SU-FE-N-EL-	Fixing of Control cable,CAT6A cable	9	05-Nov-26	15-Nov-26	07-Sep-26	16-Sep-26	4,241
CO-SU-FE-N-EL-	Install 800mm x 800mm x 800mm height concrete handhole	9	05-Nov-26	15-Nov-26	07-Sep-26	16-Sep-26	4,436
CO-SU-FE-N-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	8	05-Nov-26	14-Nov-26	07-Sep-26	15-Sep-26	5,767
CO-SU-FE-N-EL-	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	8	16-Nov-26	24-Nov-26	17-Sep-26	27-Sep-26	2,609
Architictural work		43	21-Oct-26 A	15-Nov-26	18-Oct-26	14-Nov-26	2,184,952
CO-SU-FE-N-AR-	External plastering to walls and columns	7	21-Oct-26 A	01-Nov-26	18-Oct-26	25-Oct-26	0
CO-SU-FE-N-AR-	Install 50mm thick random cut stone cladding	7	22-Oct-26 A	03-Nov-26	26-Oct-26	02-Nov-26	2,046,910
CO-SU-FE-N-AR-	Install 2 coats of weatherproof paint at walls	6	03-Nov-26	10-Nov-26	03-Nov-26	09-Nov-26	64,012
CO-SU-FE-N-AR-	Install Stone coping 500mm,525mm	4	10-Nov-26	15-Nov-26	10-Nov-26	14-Nov-26	74,030
Western Fence P1 (W01:W06)		106	17-Sep-26 A	21-Nov-26	12-Sep-26	11-Jan-27	1,799,881
Civil Work		28	17-Sep-26 A	31-Oct-26	12-Sep-26	01-Nov-26	757,244
CO-SU-FE-WP1-C	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	28-Oct-26	12-Sep-26	01-Oct-26	675,382
CO-SU-FE-WP1-C	Pouring Beams For Northern Fence	17	05-Oct-26 A	31-Oct-26	12-Oct-26	01-Nov-26	81,862
Finishing Work		93	29-Sep-26 A	21-Nov-26	01-Oct-26	11-Jan-27	1,042,637
Electrical Work		14	05-Nov-26	21-Nov-26	12-Oct-26	28-Oct-26	52,051
CO-SU-FE-WP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	14	05-Nov-26	21-Nov-26	12-Oct-26	28-Oct-26	35,687
CO-SU-FE-WP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	14	05-Nov-26	21-Nov-26	12-Oct-26	28-Oct-26	16,364
Architictural work		93	29-Sep-26 A	15-Nov-26	01-Oct-26	11-Jan-27	990,586
CO-SU-FE-WP1-A	Install Brick Work For Northern Fence	9	29-Sep-26 A	31-Oct-26	01-Oct-26	12-Oct-26	317,018
CO-SU-FE-WP1-A	External plastering to walls and columns	6	22-Oct-26 A	03-Nov-26	19-Dec-26	24-Dec-26	0
CO-SU-FE-WP1-A	Install 50mm thick random cut stone cladding	5	24-Oct-26 A	03-Nov-26	26-Dec-26	30-Dec-26	397,485
CO-SU-FE-WP1-A	Install 2 coats of weatherproof paint at walls	6	03-Nov-26	10-Nov-26	31-Dec-26	06-Jan-27	128,024
CO-SU-FE-WP1-A	Install Stone coping 500mm,525mm	4	10-Nov-26	15-Nov-26	07-Jan-27	11-Jan-27	148,059
Western Fence P2 (W07:W12)		27	29-Sep-26 A	19-Nov-26	18-Oct-26	18-Nov-26	485,036
Civil Work		7	11-Oct-26 A	31-Oct-26	01-Nov-26	09-Nov-26	81,862
CO-SU-FE-WP2-C	Pouring Beams For Northern Fence	7	11-Oct-26 A	31-Oct-26	01-Nov-26	09-Nov-26	81,862
Finishing Work		19	29-Sep-26 A	19-Nov-26	18-Oct-26	18-Nov-26	403,175
Electrical Work		19	28-Oct-26	19-Nov-26	27-Oct-26	18-Nov-26	86,156
CO-SU-FE-WP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	28-Oct-26	02-Nov-26	27-Oct-26	01-Nov-26	35,687
CO-SU-FE-WP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	28-Oct-26	04-Nov-26	27-Oct-26	03-Nov-26	16,364
CO-SU-FE-WP2-E	Fixing of Control cable,CAT6A cable	7	04-Nov-26	12-Nov-26	03-Nov-26	11-Nov-26	8,482
CO-SU-FE-WP2-E	Install 800mm x 800mm x 800mm height concrete handhole	7	04-Nov-26	12-Nov-26	03-Nov-26	10-Nov-26	8,871
CO-SU-FE-WP2-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	6	04-Nov-26	11-Nov-26	03-Nov-26	10-Nov-26	11,535
CO-SU-FE-WP2-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	12-Nov-26	19-Nov-26	11-Nov-26	18-Nov-26	5,218
Architictural work		8	29-Sep-26 A	28-Oct-26	18-Oct-26	27-Oct-26	317,018
CO-SU-FE-WP2-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	28-Oct-26	18-Oct-26	27-Oct-26	317,018

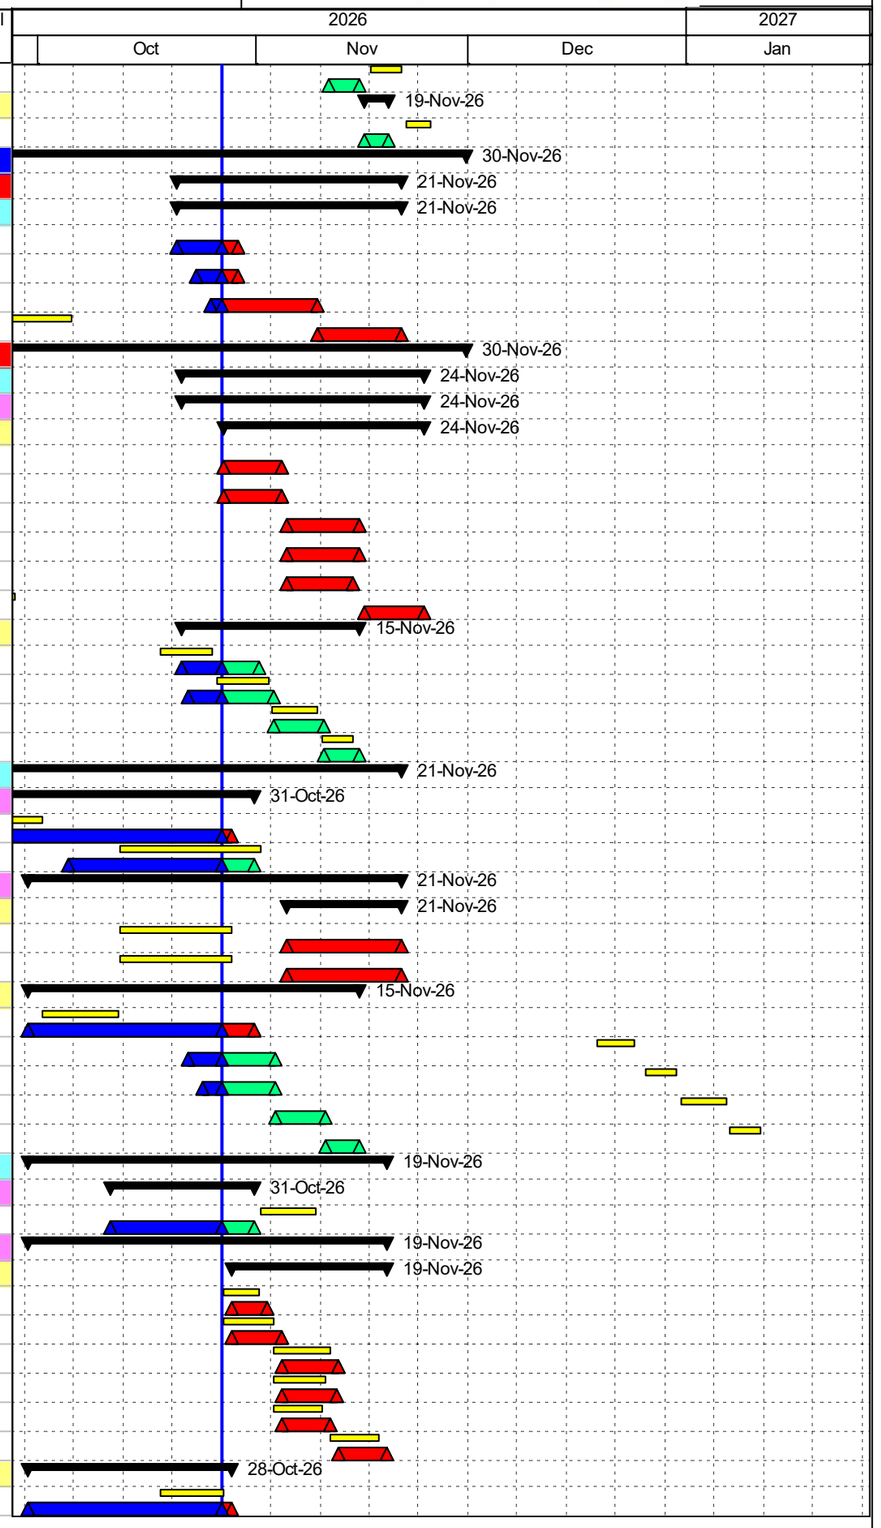


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update27-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Southern Fence S01:S05		94	02-Aug-26 A	30-Nov-26	15-Aug-26	10-Oct-26	2,108,714
Civil Work		73	02-Aug-26 A	29-Oct-26	15-Aug-26	14-Sep-26	1,777,084
CO-SU-FE-S-CI-27	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	28-Oct-26	15-Aug-26	23-Aug-26	990,000
CO-SU-FE-S-CI-28	Pouring R.C Columns For Northern Fence	10	05-Oct-26 A	28-Oct-26	24-Aug-26	03-Sep-26	718,865
CO-SU-FE-S-CI-29	Pouring Beams For Northern Fence	9	08-Oct-26 A	29-Oct-26	05-Sep-26	14-Sep-26	68,218
Finishing Work		36	29-Sep-26 A	30-Nov-26	05-Sep-26	10-Oct-26	331,631
Electrical Work		30	27-Oct-26	30-Nov-26	05-Sep-26	10-Oct-26	67,449
CO-SU-FE-S-EL-5	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	27-Oct-26	12-Nov-26	05-Sep-26	21-Sep-26	29,739
CO-SU-FE-S-EL-6	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	27-Oct-26	12-Nov-26	05-Sep-26	21-Sep-26	13,636
CO-SU-FE-S-EL-6	Fixing of Control cable,CAT6A cable	15	14-Nov-26	30-Nov-26	22-Sep-26	10-Oct-26	7,068
CO-SU-FE-S-EL-6	Install 800mm x 800mm x 800mm height concrete handhole	15	14-Nov-26	30-Nov-26	22-Sep-26	10-Oct-26	7,393
CO-SU-FE-S-EL-6	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	15	14-Nov-26	30-Nov-26	22-Sep-26	10-Oct-26	9,612
Architictural work		6	29-Sep-26 A	31-Oct-26	05-Sep-26	10-Sep-26	264,182
CO-SU-FE-S-AR-3	Install Brick Work For Northern Fence	6	29-Sep-26 A	31-Oct-26	05-Sep-26	10-Sep-26	264,182
Eastern Fence P1 (E01:E06)		29	29-Sep-26 A	22-Nov-26	21-Sep-26	08-Nov-26	1,035,743
Civil Work		22	06-Oct-26 A	01-Nov-26	21-Sep-26	26-Oct-26	600,676
CO-SU-FE-EP1-CI	Pouring R.C Columns For Northern Fence	15	06-Oct-26 A	01-Nov-26	21-Sep-26	08-Oct-26	518,815
CO-SU-FE-EP1-CI	Pouring Beams For Northern Fence	7	08-Oct-26 A	01-Nov-26	19-Oct-26	26-Oct-26	81,862
Finishing Work		20	29-Sep-26 A	22-Nov-26	10-Oct-26	08-Nov-26	435,067
Electrical Work		18	01-Nov-26	22-Nov-26	19-Oct-26	08-Nov-26	118,049
CO-SU-FE-EP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	01-Nov-26	05-Nov-26	19-Oct-26	22-Oct-26	35,687
CO-SU-FE-EP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	01-Nov-26	05-Nov-26	19-Oct-26	22-Oct-26	16,364
CO-SU-FE-EP1-E	Fixing of Control cable,CAT6A cable	4	05-Nov-26	10-Nov-26	24-Oct-26	27-Oct-26	8,482
CO-SU-FE-EP1-E	Install 800mm x 800mm x 800mm height concrete handhole	4	05-Nov-26	10-Nov-26	24-Oct-26	27-Oct-26	8,871
CO-SU-FE-EP1-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	4	05-Nov-26	10-Nov-26	24-Oct-26	27-Oct-26	11,535
CO-SU-FE-EP1-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	10-Nov-26	17-Nov-26	28-Oct-26	03-Nov-26	5,218
CO-SU-FE-EP1-E	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	17-Nov-26	22-Nov-26	04-Nov-26	08-Nov-26	31,892
CO-SU-FE-EP1-E	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	4	17-Nov-26	22-Nov-26	04-Nov-26	08-Nov-26	0
Architictural work		8	29-Sep-26 A	01-Nov-26	10-Oct-26	18-Oct-26	317,018
CO-SU-FE-EP1-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	01-Nov-26	10-Oct-26	18-Oct-26	317,018
Eastern Fence P2 (E07:E13)		43	15-Sep-26 A	10-Nov-26	03-Nov-26	02-Dec-26	1,026,217
Civil Work		43	15-Sep-26 A	04-Nov-26	03-Nov-26	02-Dec-26	571,829
CO-SU-FE-EP2-CI	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	01-Nov-26	03-Nov-26	14-Nov-26	476,324
CO-SU-FE-EP2-CI	Pouring Beams For Northern Fence	10	01-Oct-26 A	04-Nov-26	22-Nov-26	02-Dec-26	95,505
Finishing Work		33	29-Sep-26 A	10-Nov-26	15-Nov-26	29-Nov-26	454,388
Electrical Work		7	02-Nov-26	10-Nov-26	22-Nov-26	29-Nov-26	84,533
CO-SU-FE-EP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	02-Nov-26	07-Nov-26	22-Nov-26	25-Nov-26	41,635
CO-SU-FE-EP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	02-Nov-26	07-Nov-26	22-Nov-26	25-Nov-26	19,091
CO-SU-FE-EP2-E	Install 800mm x 800mm x 800mm height concrete handhole	3	07-Nov-26	10-Nov-26	26-Nov-26	29-Nov-26	10,350
CO-SU-FE-EP2-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	3	07-Nov-26	10-Nov-26	26-Nov-26	29-Nov-26	13,457
Architictural work		6	29-Sep-26 A	02-Nov-26	15-Nov-26	21-Nov-26	369,855
CO-SU-FE-EP2-A	Install Brick Work For Northern Fence	6	29-Sep-26 A	02-Nov-26	15-Nov-26	21-Nov-26	369,855
Handing over and close out		14	27-Oct-26	11-Nov-26	04-Jan-27	19-Jan-27	0
As-Built		14	27-Oct-26	11-Nov-26	04-Jan-27	19-Jan-27	0
HO-130	Submission As-Built Drawing For Pond	14	27-Oct-26	11-Nov-26	04-Jan-27	19-Jan-27	0

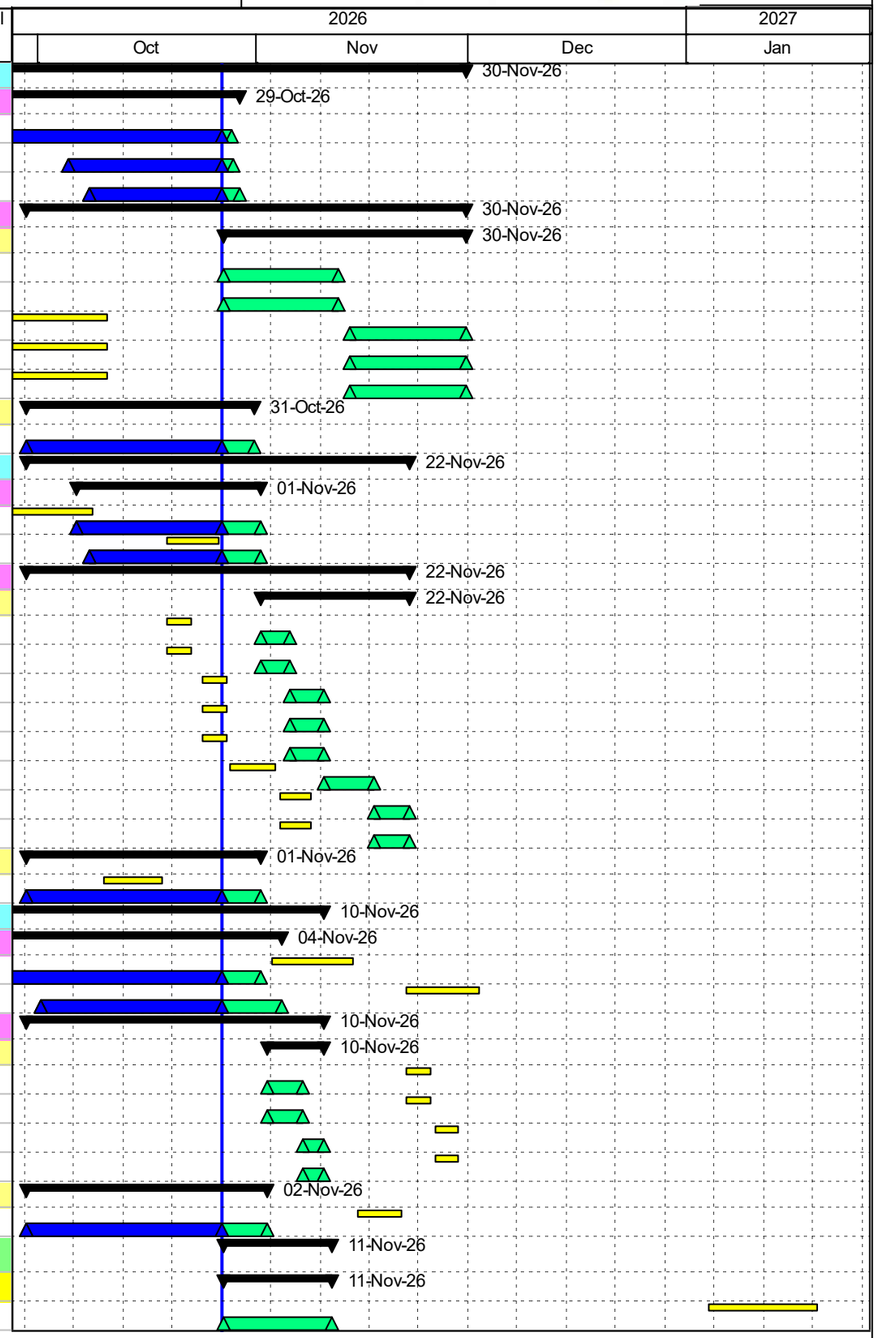

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
27-Oct-26	Third Industrial City		
