

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Development of the Technology City in Dammam-Project UPDATE 06-1		437	23-Dec-25	23-Feb-27	23-Dec-25 A	20-Jun-27	67,768,369.77	13,722,721.53	30.95%	20.25%
Key Milestones		437	23-Dec-25	23-Feb-27	23-Dec-25 A	20-Jun-27	0.00	0.00	0%	0%
Contractual Milestones		437	23-Dec-25	23-Feb-27	23-Dec-25 A	20-Jun-27	0.00	0.00	0%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		02-Jan-27		21-Apr-27	0.00	0.00	0%	0%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		10-Jan-27		29-Apr-27	0.00	0.00	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		26-Jan-27		22-May-27	0.00	0.00	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0		14-Feb-27		07-Jun-27	0.00	0.00	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0		13-Jan-27		21-Apr-27	0.00	0.00	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		03-Jan-27		24-Apr-27	0.00	0.00	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		26-Jan-27		22-May-27	0.00	0.00	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom Network	0		19-Jan-27		09-May-27	0.00	0.00	0%	0%
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0		14-Jan-27		04-May-27	0.00	0.00	0%	0%
MS-CF-EBL	Completion of Execution Plan and Baseline Schedule	0		23-Jun-26		18-Jan-26 A	0.00	0.00	100%	100%
MS-CF-MOB	Completion of Mobilization and Site Preperation Works	0		23-Jun-26		18-Jan-26 A	0.00	0.00	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		13-Jul-26		14-Oct-26	0.00	0.00	100%	0%
MS-CS-PS	Project Commencement Date (Site Handover)	0	23-Dec-25		23-Dec-25 A		0.00	0.00	100%	100%
MS-CF-PF	Project Completion Date	0		23-Feb-27		20-Jun-27	0.00	0.00	0%	0%
Preliminaries and Mobilization Works		30	23-Dec-25	27-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	0%	0%
Mobilization Works		30	23-Dec-25	27-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	23	31-Dec-25	26-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-40	Construction Project Store	23	31-Dec-25	26-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-80	Construction Site Access Roads	29	23-Dec-25	25-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-70	Installation Project Sign Board	13	12-Jan-26	26-Jan-26	12-Jan-26 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-60	Mobilization of Major Equipments	23	31-Dec-25	27-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-50	Mobilization of Major Manpower	23	31-Dec-25	27-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-20	Project Site Layout Plan Approval	6	23-Dec-25	30-Dec-25	23-Dec-25 A	29-Dec-25 A	0.00	0.00	100%	100%
MOB-90	Site Surveying Work	30	23-Dec-25	26-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-30	Supply & Install of Project Supervision Offices	29	23-Dec-25	25-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
Project Main Documents From The Contractor		23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	0%	0%
PRE-CON-MDC-2	Submission Project Baseline Schedule	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-7	Submission Project Environmental Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-1	Submission Project Execution Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-6	Submission Project Geotechnical Soil Report	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-3	Submission Project Health & Safety Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-8	Submission Project Organization Chart and Communications Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-4	Submission Project Quality Control Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-5	Submission Project Surveying Report	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%

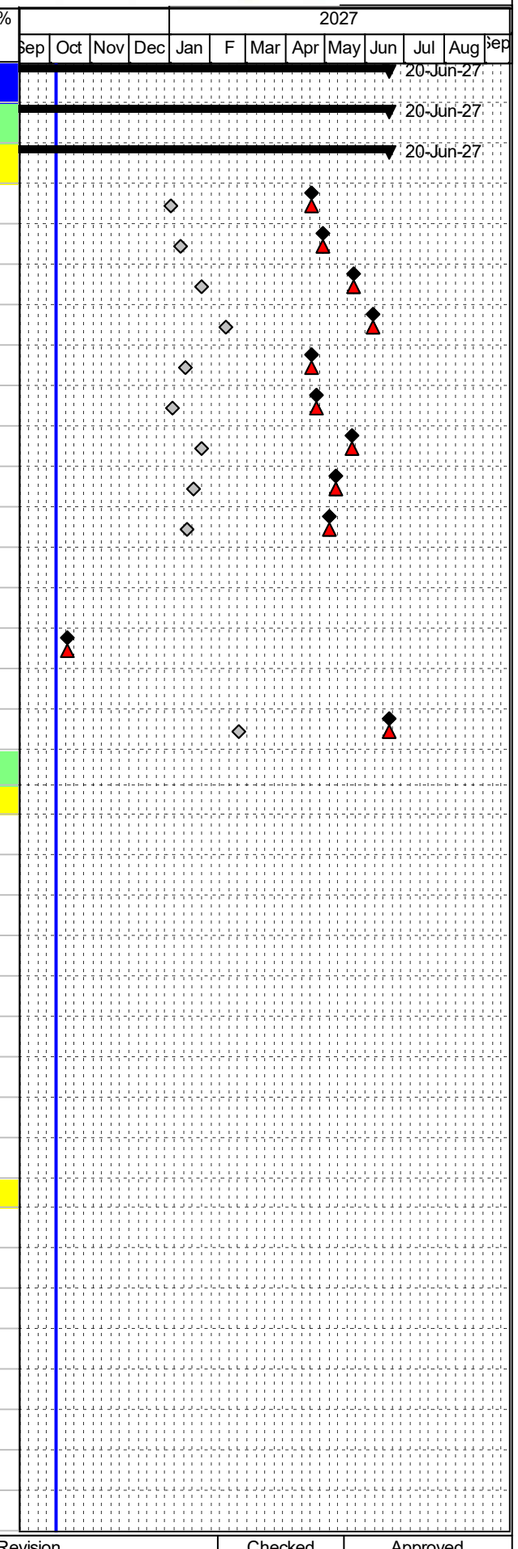

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Engineering Works		227	06-Jan-26	13-Jul-26	06-Jan-26 A	14-Oct-26	0.00	0.00	0%	0%
Shop Drawings		138	17-Jan-26	13-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Infrastructure Networks		138	17-Jan-26	13-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Road Works		138	17-Jan-26	13-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Sewage Network		128	17-Jan-26	30-Jun-26	17-Jan-26 A	30-Jun-26 A	0.00	0.00	0%	0%
Storm Drainage Network		132	17-Jan-26	06-Jul-26	17-Jan-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Potable Water Network		132	18-Jan-26	06-Jul-26	18-Jan-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Irrigation Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Treated Sewage Effluent Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Medium Voltage Network		134	17-Jan-26	07-Jul-26	17-Jan-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Low Voltage Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Street Lighting Network		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Telecom Network		8	29-Jun-26	07-Jul-26	29-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Superstructure Works		134	17-Jan-26	07-Jul-26	17-Jan-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Pump Stations		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Lift Station		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Storm Drainage Ponds		7	28-Jun-26	06-Jul-26	28-Jun-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Storage Tank (TSE)		7	30-Jun-26	07-Jul-26	30-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Gaurd Room		6	23-Jun-26	29-Jun-26	23-Jun-26 A	29-Jun-26 A	0.00	0.00	0%	0%
Fence		114	29-Jan-26	28-Jun-26	29-Jan-26 A	28-Jun-26 A	0.00	0.00	0%	0%
Material Submittals and Approvals		227	06-Jan-26	12-Jul-26	06-Jan-26 A	14-Oct-26	0.00	0.00	0%	0%
Short Lead Time Items		226	06-Jan-26	12-Jul-26	06-Jan-26 A	13-Oct-26	0.00	0.00	0%	0%
Infrastructure Networks		146	06-Jan-26	12-Jul-26	06-Jan-26 A	12-Jul-26 A	0.00	0.00	0%	0%
Superstructure Works		218	15-Jan-26	30-Jun-26	15-Jan-26 A	13-Oct-26	0.00	0.00	0%	0%
Long Lead Time Items		219	15-Jan-26	02-Jul-26	15-Jan-26 A	14-Oct-26	0.00	0.00	0%	0%
Infrastructure Networks		3	15-Jan-26	19-Jan-26	15-Jan-26 A	22-Jan-26 A	0.00	0.00	0%	0%
Superstructure Works		8	24-Jun-26	02-Jul-26	06-Oct-26	14-Oct-26	0.00	0.00	0%	0%
Procurement Cycle		371	28-Jan-26	28-Jan-27	28-Jan-26 A	03-May-27	0.00	0.00	0%	0%
Short Lead Time Items		371	28-Jan-26	28-Jan-27	28-Jan-26 A	03-May-27	0.00	0.00	0%	0%
Infrastructure Networks		371	28-Jan-26	28-Jan-27	28-Jan-26 A	03-May-27	0.00	0.00	0%	0%
Road Works		140	23-Jun-26	05-Dec-26	23-Jun-26 A	06-Oct-26	0.00	0.00	0%	0%
Softscape and Planting Works		105	11-Jul-26	10-Nov-26	06-Oct-26	04-Feb-27	0.00	0.00	0%	0%
Sewage Network		236	23-Jun-26	28-Dec-26	23-Jun-26 A	05-Apr-27	0.00	0.00	0%	0%
Storm Drainage Network		200	23-Jun-26	10-Dec-26	02-Aug-26 A	17-Mar-27	0.00	0.00	0%	0%
Potable Water Network		292	01-Apr-26	13-Dec-26	01-Apr-26 A	24-Mar-27	0.00	0.00	0%	0%
Irrigation Network		295	28-Jan-26	27-Oct-26	28-Jan-26 A	25-Jan-27	0.00	0.00	0%	0%
Treated Sewage Effluent (Tse)		244	01-Apr-26	10-Oct-26	01-Apr-26 A	18-Jan-27	0.00	0.00	0%	0%
Medium Voltage Network		129	23-Jun-26	05-Dec-26	06-Oct-26	15-Mar-27	0.00	0.00	0%	0%
Low Voltage and Street Lighting Network		171	23-Jun-26	28-Jan-27	06-Oct-26	03-May-27	0.00	0.00	0%	0%
Telecom Network		93	07-Jul-26	24-Oct-26	06-Oct-26	23-Jan-27	0.00	0.00	0%	0%
Superstructure Works		276	29-Jan-26	11-Oct-26	29-Jan-26 A	04-Jan-27	0.00	0.00	0%	0%
Issuance of Purchase Orders		217	29-Jan-26	13-Jul-26	29-Jan-26 A	26-Oct-26	0.00	0.00	0%	0%
Manufacturing of Material		183	23-Jun-26	11-Oct-26	05-Jul-26 A	03-Jan-27	0.00	0.00	0%	0%
1st Material Delivery & Site Inspection		84	02-Aug-26	08-Oct-26	03-Aug-26 A	10-Dec-26	0.00	0.00	0%	0%
Material Delivery & Site Inspection		139	25-Jul-26	11-Oct-26	02-Aug-26 A	04-Jan-27	0.00	0.00	0%	0%
Long Lead Time Items		157	23-Jun-26	23-Dec-26	06-Oct-26	17-Apr-27	0.00	0.00	0%	0%
Infrastructure Networks		112	23-Jun-26	31-Oct-26	06-Oct-26	15-Feb-27	0.00	0.00	0%	0%
CCTV System Wroks of Telecom Network		112	23-Jun-26	31-Oct-26	06-Oct-26	15-Feb-27	0.00	0.00	0%	0%
Superstructure Works		149	04-Jul-26	23-Dec-26	15-Oct-26	17-Apr-27	0.00	0.00	0%	0%
Pump Stations		146	04-Jul-26	20-Dec-26	15-Oct-26	13-Apr-27	0.00	0.00	0%	0%
Lift Stations		149	04-Jul-26	23-Dec-26	15-Oct-26	17-Apr-27	0.00	0.00	0%	0%
Storage Tank (TSE)		149	04-Jul-26	23-Dec-26	15-Oct-26	17-Apr-27	0.00	0.00	0%	0%
Construction Works		368	07-Mar-26	23-Feb-27	07-Mar-26 A	07-Jun-27	67,768,369.77	13,722,721.53	30.95%	20.25%
Infrastructure Networks		368	07-Mar-26	14-Feb-27	07-Mar-26 A	07-Jun-27	27,934,729.42	4,660,166.92	37.3%	16.68%
Earthworks		117	07-Mar-26	01-Aug-26	07-Mar-26 A	24-Oct-26	5,376,162.05	4,606,527.74	100%	85.68%

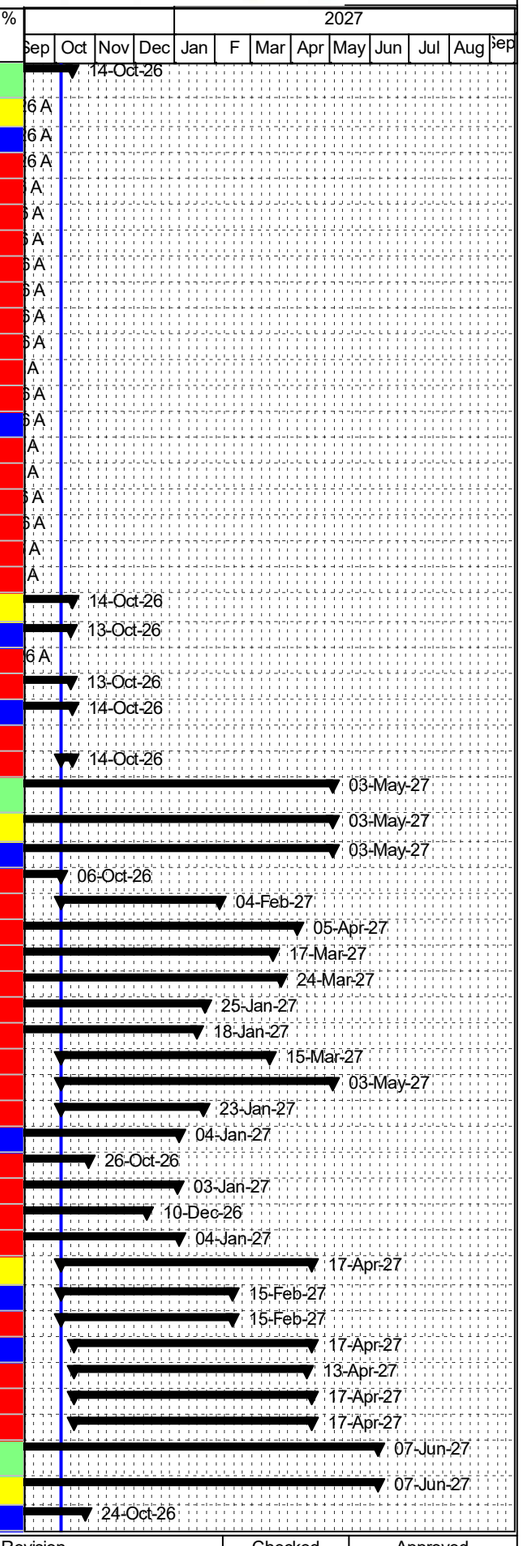


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Earthworks	117	07-Mar-26	01-Aug-26	07-Mar-26 A	24-Oct-26	5,376,162.05	4,606,527.74	100%	85.68%
	Storm Drainage Network	183	13-Jul-26	01-Nov-26	02-Aug-26 A	15-Feb-27	4,958,378.40	53,639.18	88.9%	1.08%
	FROM MH-25:MH-12	156	13-Jul-26	30-Sep-26	02-Aug-26 A	13-Jan-27	2,725,882.92	53,639.18	100%	1.97%
	FROM MH-12:MH-01	96	01-Aug-26	01-Nov-26	25-Oct-26	15-Feb-27	2,232,495.48	0.00	75.34%	0%
	Sewage Network	61	01-Aug-26	12-Oct-26	25-Oct-26	03-Jan-27	651,749.20	0.00	97.58%	0%
	FROM MH-18:MH-10	53	01-Aug-26	03-Oct-26	25-Oct-26	24-Dec-26	258,640.96	0.00	100%	0%
	FROM MH-10:MH-01	49	15-Aug-26	12-Oct-26	08-Nov-26	03-Jan-27	393,108.24	0.00	95.98%	0%
	Potable Water Network	61	12-Oct-26	22-Dec-26	19-Jan-27	11-Apr-27	956,108.40	0.00	0%	0%
	Main Line Sections	24	12-Oct-26	09-Nov-26	19-Jan-27	18-Feb-27	522,248.40	0.00	0%	0%
	Valve Chamber	16	09-Nov-26	28-Nov-26	20-Feb-27	17-Mar-27	259,440.00	0.00	0%	0%
	Fire Hydrant	21	28-Nov-26	22-Dec-26	17-Mar-27	11-Apr-27	174,420.00	0.00	0%	0%
	Irrigation Network	50	21-Oct-26	19-Dec-26	28-Jan-27	07-Apr-27	760,970.00	0.00	0%	0%
	Main Line Pipes	50	21-Oct-26	19-Dec-26	28-Jan-27	07-Apr-27	760,970.00	0.00	0%	0%
	Treated Sewage Effluent (Tse)	50	21-Oct-26	19-Dec-26	28-Jan-27	07-Apr-27	530,262.40	0.00	0%	0%
	Main Line Pipes	50	21-Oct-26	19-Dec-26	28-Jan-27	07-Apr-27	530,262.40	0.00	0%	0%
	Medium Voltage Network	43	31-Oct-26	20-Dec-26	07-Feb-27	08-Apr-27	639,985.36	0.00	0%	0%
	Cabling Works	43	31-Oct-26	20-Dec-26	07-Feb-27	08-Apr-27	639,985.36	0.00	0%	0%
	Street Lighting Network	67	31-Oct-26	17-Jan-27	08-Feb-27	06-May-27	824,676.69	0.00	0%	0%
	Lighting Poles Works	35	31-Oct-26	10-Dec-26	08-Feb-27	30-Mar-27	239,640.00	0.00	0%	0%
	Cabling Works	25	09-Nov-26	08-Dec-26	20-Feb-27	28-Mar-27	554,959.89	0.00	0%	0%
	Distrubution Panel Boards	24	20-Dec-26	17-Jan-27	08-Apr-27	06-May-27	30,076.80	0.00	0%	0%
	Telecom Network	42	12-Nov-26	31-Dec-26	23-Feb-27	20-Apr-27	4,775,135.00	0.00	0%	0%
	Ducts Works	26	12-Nov-26	13-Dec-26	23-Feb-27	01-Apr-27	1,277,742.00	0.00	0%	0%
	Manholes Works	19	22-Nov-26	14-Dec-26	08-Mar-27	03-Apr-27	266,796.00	0.00	0%	0%
	CCTV System Wroks	15	14-Dec-26	31-Dec-26	03-Apr-27	20-Apr-27	3,230,597.00	0.00	0%	0%
	Road Works	51	03-Dec-26	31-Jan-27	23-Mar-27	26-May-27	294,864.10	0.00	0%	0%
	ST+1000:ST+1531	28	03-Dec-26	04-Jan-27	23-Mar-27	24-Apr-27	127,701.70	0.00	0%	0%
	ST+500:ST+1000	25	20-Dec-26	17-Jan-27	08-Apr-27	06-May-27	78,701.70	0.00	0%	0%
	ST+01:ST+500	26	02-Jan-27	31-Jan-27	21-Apr-27	26-May-27	88,460.70	0.00	0%	0%
	Finishes for Infrastructure Networks	119	12-Oct-26	14-Feb-27	04-Jan-27	07-Jun-27	8,166,437.82	0.00	0%	0%
	Storm Drainage Network	56	02-Nov-26	05-Jan-27	15-Feb-27	01-May-27	825,219.60	0.00	0%	0%
	Sewage Network	84	12-Oct-26	13-Jan-27	04-Jan-27	21-Apr-27	85,302.80	0.00	0%	0%
	Potable Water Network	31	22-Dec-26	26-Jan-27	11-Apr-27	22-May-27	83,407.60	0.00	0%	0%
	Irrigation Network	12	19-Dec-26	02-Jan-27	07-Apr-27	21-Apr-27	19,320.00	0.00	0%	0%
	Treated Sewage Effluent (Tse)	12	02-Jan-27	14-Jan-27	21-Apr-27	04-May-27	30,693.60	0.00	0%	0%
	Medium Voltage Network	18	20-Dec-26	10-Jan-27	08-Apr-27	29-Apr-27	66,481.77	0.00	0%	0%
	Street Lighting Network	14	10-Jan-27	03-Feb-27	29-Apr-27	22-May-27	143,686.20	0.00	0%	0%
	Telecom Network	16	31-Dec-26	19-Jan-27	20-Apr-27	09-May-27	82,794.00	0.00	0%	0%
	Road Works	47	20-Dec-26	14-Feb-27	08-Apr-27	07-Jun-27	6,829,532.25	0.00	0%	0%
	Superstructure Work	240	28-Jul-26	23-Feb-27	28-Jul-26 A	20-May-27	39,833,640.35	9,062,554.60	26.5%	22.75%
	Utility Buildings	211	24-Aug-26	27-Jan-27	01-Aug-26 A	20-May-27	14,839,553.75	2,033,362.52	5.56%	13.7%
	Storm Drainage Ponds	63	22-Oct-26	03-Jan-27	02-Aug-26 A	01-Sep-26 A	446,400.00	446,400.00	0%	100%
	Pump Station	211	30-Aug-26	27-Jan-27	01-Aug-26 A	20-May-27	4,089,766.36	905,909.08	6.76%	22.15%
	Lift Station	142	08-Sep-26	20-Jan-27	01-Sep-26 A	16-Feb-27	2,816,702.49	428,811.43	5.97%	15.22%
	Potable Water Tank	66	24-Aug-26	09-Nov-26	07-Dec-26	25-Feb-27	615,094.02	0.00	40.6%	0%
	IrrigationTank	54	10-Nov-26	11-Jan-27	25-Feb-27	05-May-27	615,094.02	0.00	0%	0%
	Control Room	142	15-Sep-26	20-Jan-27	02-Aug-26 A	07-Mar-27	2,330,956.41	252,242.01	5.58%	10.82%
	Softscape and Planting Works	39	07-Nov-26	22-Dec-26	01-Feb-27	28-Mar-27	3,925,540.44	0.00	0%	0%
	Fence and Gaurd Room	240	28-Jul-26	23-Feb-27	28-Jul-26 A	20-May-27	24,994,086.60	7,029,192.08	38.94%	28.12%
	Gaurd Room Work	124	29-Aug-26	20-Jan-27	12-Dec-26	20-May-27	2,138,080.85	0.00	5.39%	0%
	Fence Work	230	28-Jul-26	23-Feb-27	28-Jul-26 A	03-May-27	22,856,005.75	7,029,192.08	42.08%	30.75%
	Testing and Comissioning	184	04-Jan-27	18-Feb-27	24-Oct-26	10-Jun-27	0.00	0.00	0%	0%
	Infrastructure Networks	31	06-Jan-27	18-Feb-27	01-May-27	10-Jun-27	0.00	0.00	0%	0%
	Irrigation Network	5	27-Jan-27	02-Feb-27	23-May-27	27-May-27	0.00	0.00	0%	0%
T/C-IR	Testing and Commissioning of Irrigation Network	5	27-Jan-27	02-Feb-27	23-May-27	27-May-27	0.00	0.00	0%	0%

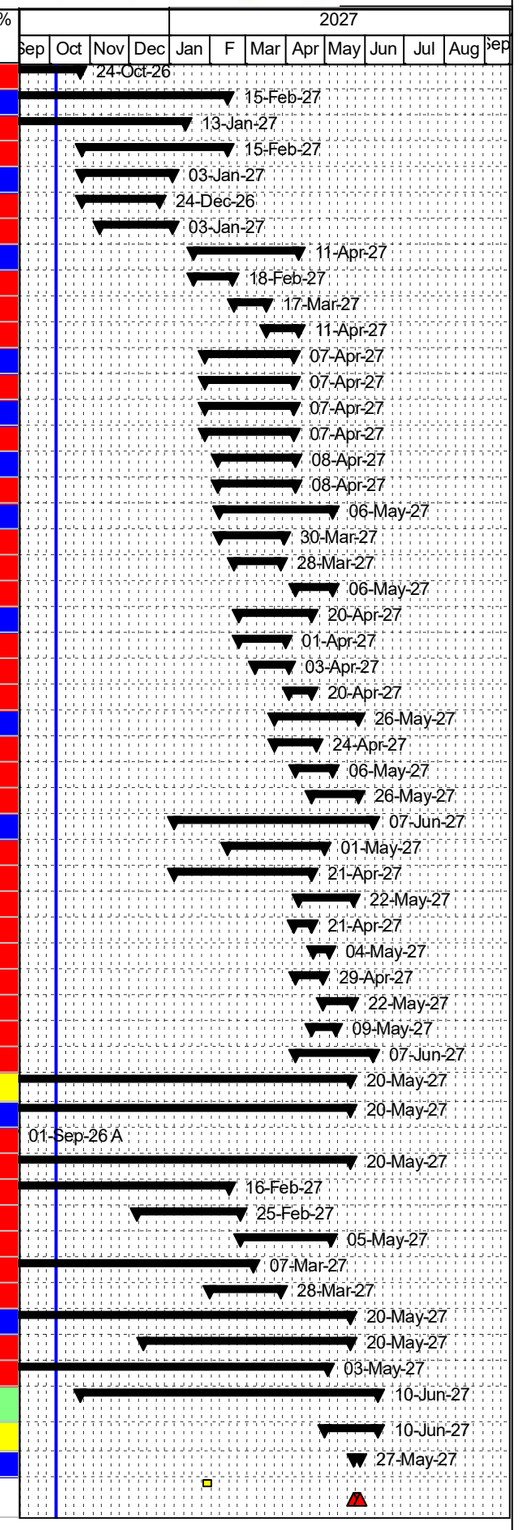


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
TSE Network		15	17-Jan-27	02-Feb-27	11-May-27	03-Jun-27	0.00	0.00	0%	0%
T/C-TSE-10	Testing and Commissioning of TSE Network	15	17-Jan-27	02-Feb-27	11-May-27	03-Jun-27	0.00	0.00	0%	0%
Potable Water Network		6	27-Jan-27	03-Feb-27	23-May-27	29-May-27	0.00	0.00	0%	0%
T/C-PW	Testing and Commissioning of Potable Water Network	6	27-Jan-27	03-Feb-27	23-May-27	29-May-27	0.00	0.00	0%	0%
Sewage Network		3	17-Jan-27	19-Jan-27	11-May-27	20-May-27	0.00	0.00	0%	0%
T/C-SW	Testing and Commissioning of Sewage Network	3	17-Jan-27	19-Jan-27	11-May-27	20-May-27	0.00	0.00	0%	0%
Storm Drainage Network		9	06-Jan-27	16-Jan-27	01-May-27	11-May-27	0.00	0.00	0%	0%
T/C-SD	Testing and Commissioning of Storm Drainage Network	9	06-Jan-27	16-Jan-27	01-May-27	11-May-27	0.00	0.00	0%	0%
Street Lighting Network		6	04-Feb-27	11-Feb-27	29-May-27	03-Jun-27	0.00	0.00	0%	0%
T/C-SL	Testing and Commissioning of Street Lighting Network	6	04-Feb-27	11-Feb-27	29-May-27	03-Jun-27	0.00	0.00	0%	0%
Telecom Network		3	20-Jan-27	23-Jan-27	20-May-27	24-May-27	0.00	0.00	0%	0%
T/C-TE	Testing and Commissioning of Telecom Network	3	20-Jan-27	23-Jan-27	20-May-27	24-May-27	0.00	0.00	0%	0%
Medium Voltage Network		14	20-Jan-27	04-Feb-27	20-May-27	06-Jun-27	0.00	0.00	0%	0%
T/C-MV	Testing and Commissioning of Medium Voltage Network	14	20-Jan-27	04-Feb-27	20-May-27	06-Jun-27	0.00	0.00	0%	0%
Road Works		4	13-Feb-27	18-Feb-27	07-Jun-27	10-Jun-27	0.00	0.00	0%	0%
T/C-RD	Testing and Commissioning of Road Works	4	13-Feb-27	18-Feb-27	07-Jun-27	10-Jun-27	0.00	0.00	0%	0%
Utility Buildings		177	04-Jan-27	03-Feb-27	24-Oct-26	03-Jun-27	0.00	0.00	0%	0%
T/C-CTV	Testing and Commissioning of Guard Room and Fence	0	21-Jan-27	21-Jan-27	22-May-27	22-May-27	0.00	0.00	0%	0%
T/C-SPS	Testing and Commissioning of Sewage Pump Stations& soft scape and planting work	0	03-Feb-27	03-Feb-27	03-Jun-27	03-Jun-27	0.00	0.00	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	04-Jan-27	04-Jan-27	24-Oct-26	24-Oct-26	0.00	0.00	0%	0%
Handing over and close out		191	04-Jan-27	22-Feb-27	24-Oct-26	20-Jun-27	0.00	0.00	0%	0%
As-Built		191	04-Jan-27	22-Feb-27	24-Oct-26	20-Jun-27	0.00	0.00	0%	0%
HO-190	As-Built Drawing For Potable Water Network	12	03-Feb-27	21-Feb-27	30-May-27	12-Jun-27	0.00	0.00	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	12	02-Feb-27	18-Feb-27	29-May-27	10-Jun-27	0.00	0.00	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	06-Feb-27	22-Feb-27	06-Jun-27	20-Jun-27	0.00	0.00	0%	0%
HO-130	Submission As-Built Drawing For Pond	14	04-Jan-27	19-Jan-27	24-Oct-26	08-Nov-26	0.00	0.00	0%	0%
HO-210	Submission As-Built Drawing For Pump station	1	03-Feb-27	03-Feb-27	03-Jun-27	05-Jun-27	0.00	0.00	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	3	18-Feb-27	22-Feb-27	12-Jun-27	14-Jun-27	0.00	0.00	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	14	20-Jan-27	04-Feb-27	20-May-27	06-Jun-27	0.00	0.00	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	7	13-Feb-27	22-Feb-27	05-Jun-27	12-Jun-27	0.00	0.00	0%	0%
HO-160	Submission As-Built Drawing For Telecom Network	12	24-Jan-27	06-Feb-27	24-May-27	07-Jun-27	0.00	0.00	0%	0%
De-Mobilization Works		5	13-Feb-27	20-Feb-27	07-Jun-27	12-Jun-27	0.00	0.00	0%	0%
HO-230	Remove Temporary Car Shades	5	13-Feb-27	20-Feb-27	07-Jun-27	12-Jun-27	0.00	0.00	0%	0%
Handing Over		3	18-Feb-27	22-Feb-27	12-Jun-27	14-Jun-27	0.00	0.00	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	3	18-Feb-27	22-Feb-27	12-Jun-27	14-Jun-27	0.00	0.00	0%	0%

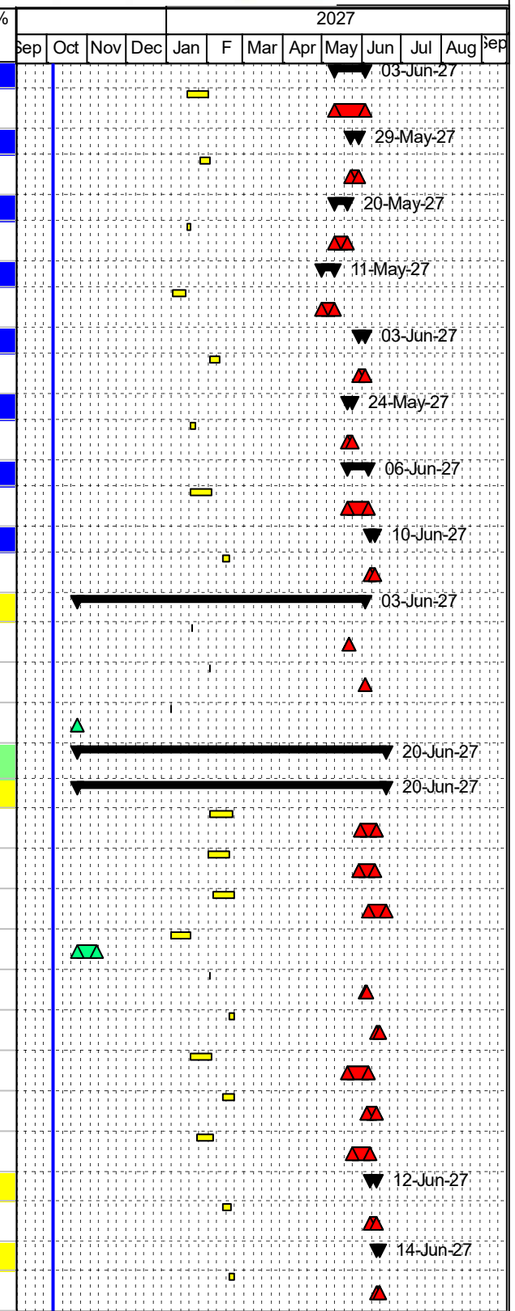

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
