
Development of the Technology City in Dammam Project
BL-Update28-09-2026
WBS Summary Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	Schedule % Complete	Performance % Complete	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
	Development of the Technology City in Dhahran Project Reco	448	06-Jan-26 A	01-Jul-27	34.19%	23.68%	93,388,698	31,926,434	22,116,233
	Key Milestones	448	06-Jan-26 A	01-Jul-27	0%	0%	0	0	0
	Preliminaries and Mobilization Works	79	06-Jan-26 A	11-Apr-26 A	0%	0%	0	0	0
	Engineering Works	254	06-Jan-26 A	08-Nov-26	0%	0%	0	0	0
	Procurement Cycle	331	02-May-26 A	06-Jun-27	0%	0%	0	0	0
	Construction Works	376	10-Mar-26 A	09-Jun-27	34.19%	23.68%	93,388,698	31,926,434	22,116,233
	Infrastructure Networks	374	10-Mar-26 A	07-Jun-27	51.66%	23.46%	57,696,530	29,804,234	13,535,825
	Internal	374	10-Mar-26 A	07-Jun-27	50.67%	9.4%	32,508,953	16,471,322	3,055,456
	Alignment-RD-01	357	10-Mar-26 A	12-May-27	53.38%	20.1%	15,199,337	8,113,094	3,055,456
	Earthworks	222	10-Mar-26 A	23-Dec-26	100%	65.04%	4,697,995	4,697,995	3,055,456
	Storm Drainage Network	61	12-Oct-26	21-Dec-26	100%	0%	2,292,989	2,292,989	0
	Sewage Network	60	06-Dec-26	13-Feb-27	75.55%	0%	801,144	605,264	0
	Treated Sewage Effluent (Tse)	42	29-Nov-26	16-Jan-27	100%	0%	94,795	94,795	0
	Potable Water Network	32	29-Nov-26	04-Jan-27	100%	0%	373,599	373,599	0
	Irrigation Network	36	17-Jan-27	27-Feb-27	8.05%	0%	601,521	48,452	0
	Medium Voltage Network	18	14-Feb-27	06-Mar-27	0%	0%	153,221	0	0
	Low Voltage Network	25	07-Mar-27	07-Apr-27	0%	0%	158,103	0	0
	Street Lighting Network	23	21-Feb-27	22-Mar-27	0%	0%	80,615	0	0
	Telecom and Light Current Network	21	23-Mar-27	15-Apr-27	0%	0%	1,517,343	0	0
	Road Network	10	17-Apr-27	27-Apr-27	0%	0%	2,662,858	0	0
	Finishes for Infrastructure Networks	55	07-Mar-27	12-May-27	0%	0%	1,765,154	0	0
	Alignment-RD-02	174	08-Nov-26	07-Jun-27	50.04%	0%	7,655,882	3,830,987	0
	Alignment-RD-03-1	171	12-Oct-26	02-May-27	36.65%	0%	3,448,486	1,263,997	0
	Alignment-RD-03-2	192	14-Oct-26	03-Jun-27	55.03%	0%	3,959,670	2,178,866	0
	Alignment-RD-03-3	165	26-Oct-26	09-May-27	48.29%	0%	2,245,578	1,084,377	0
	External	328	01-Apr-26 A	27-Apr-27	52.93%	41.61%	25,187,577	13,332,912	10,480,369
	External Road - 1 - 1	327	01-Apr-26 A	26-Apr-27	62.19%	49.95%	5,221,714	3,247,135	2,608,226
	External Road - 1 - 2	314	18-Apr-26 A	27-Apr-27	62.3%	23.4%	7,651,591	4,767,067	1,790,191
	External Road - 2	296	09-May-26 A	27-Apr-27	62.12%	35.19%	3,781,297	2,348,995	1,330,763
	External Road - 3	296	09-May-26 A	27-Apr-27	34.8%	55.68%	8,532,974	2,969,716	4,751,189
	Superstructure Work	214	01-Aug-26 A	09-Jun-27	5.95%	24.04%	35,692,169	2,122,199	8,580,408
	Testing and Comissioning	25	31-May-27	28-Jun-27	0%	0%	0	0	0
	Handing over and close out	24	05-Jun-27	01-Jul-27	0%	0%	0	0	0

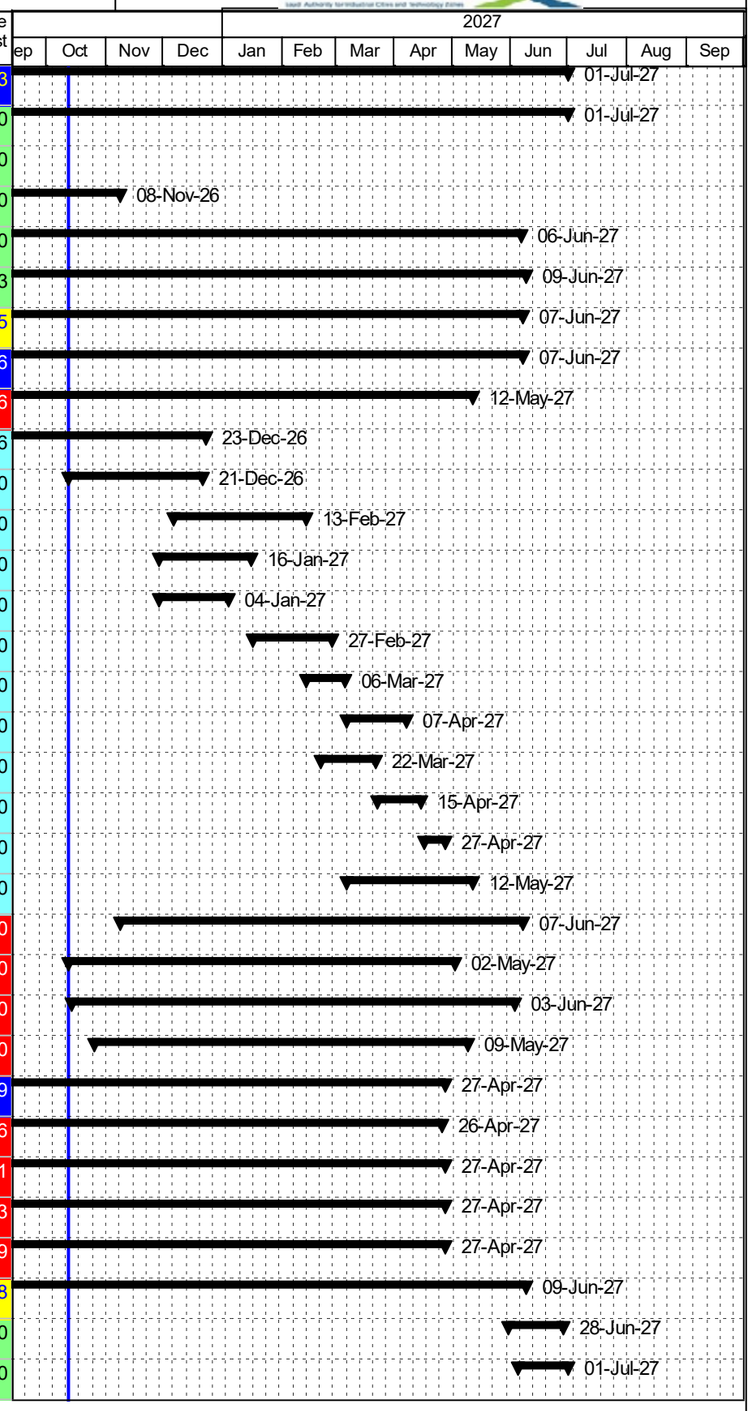

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
28-Sep-26	Third Industrial City		
