
Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Development of the Technology City in Dhahran Project Recovery -R** | | 448 | 06-Jan-26 A | 01-Jul-27 | 93,388,698 | 31,926,434 | 22,116,233 | 19,232,277 | 34.19% | 23.68% |
| **Key Milestones** | | 448 | 06-Jan-26 A | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Contractual Milestones** | | 448 | 06-Jan-26 A | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-EBL | Completion of Execution Plan and Baseline Schedule | 0 | | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CF-ENG | Completion of Submitting and Approval of Shopdrawing and Materials | 0 | | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| MS-CF-IR | Completion of Construction Works for Irrigation Network | 0 | | 28-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-LO | Completion of Construction Works for Low Voltage Network | 0 | | 28-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-MOB | Completion of Mobilization Works | 0 | | 07-Mar-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CF-MV | Completion of Construction Works for Medium Voltage Network | 0 | | 03-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-PF | Project Completion Date | 0 | | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-PW | Completion of Construction Works for Potable Water Network | 0 | | 28-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-RD | Completion of Construction Works for Road Works | 0 | | 28-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-SD | Completion of Construction Works for Storm Drainage Network | 0 | | 27-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-SL | Completion of Construction Works for Street Lighting Network | 0 | | 27-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-SW | Completion of Construction Works for Sewage Network | 0 | | 18-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-TE | Completion of Construction Works for Telecom and Light Current Networks | 0 | | 28-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CF-TSE | Completion of Construction Works for Treated Sewage Effluent Network | 0 | | 22-May-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CS-PS | Project Commencement Date ( Site Handover ) | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-MO-10 | Completion of Sewage Pump Station | 0 | | 09-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-MO-20 | Completion of Storm Drainage Ponds | 0 | | 21-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-MO-40 | Completion of Control Room | 0 | | 28-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-MO-50 | Completion of Water Pump Station | 0 | | 09-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-MO-60 | Completion of Irrigation and Potable Tank | 0 | | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Control Milestones** | | 230 | 06-Jan-26 A | 12-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **The Employer** | | 206 | 03-Feb-26 A | 12-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-MM-100 | Right of Access and Possession of the Site | 0 | | 03-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-MM-120 | Receipt of Advance Payment for the Project From The Employer | 0 | | 12-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| MS-MM-130 | Receipt the Site Benchmark Coordinates (Original Point) From The Employer | 0 | | 03-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-MM-140 | Receipt the Site Levels Details From The Employer | 0 | | 03-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-MM-150 | Receipt of Approved Concept Master Plan for the Project From the Employer | 0 | | 03-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-MM-160 | Receipt of Master Plan Approval Letter for the Project From the Employer | 0 | | 03-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **NOC's** | | 0 | 06-Jan-26 A | 06-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 0 | 06-Jan-26 A | 06-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CS-IR | Receipt of Approval NOC From Relevant Authorities For Irrigation Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |





Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

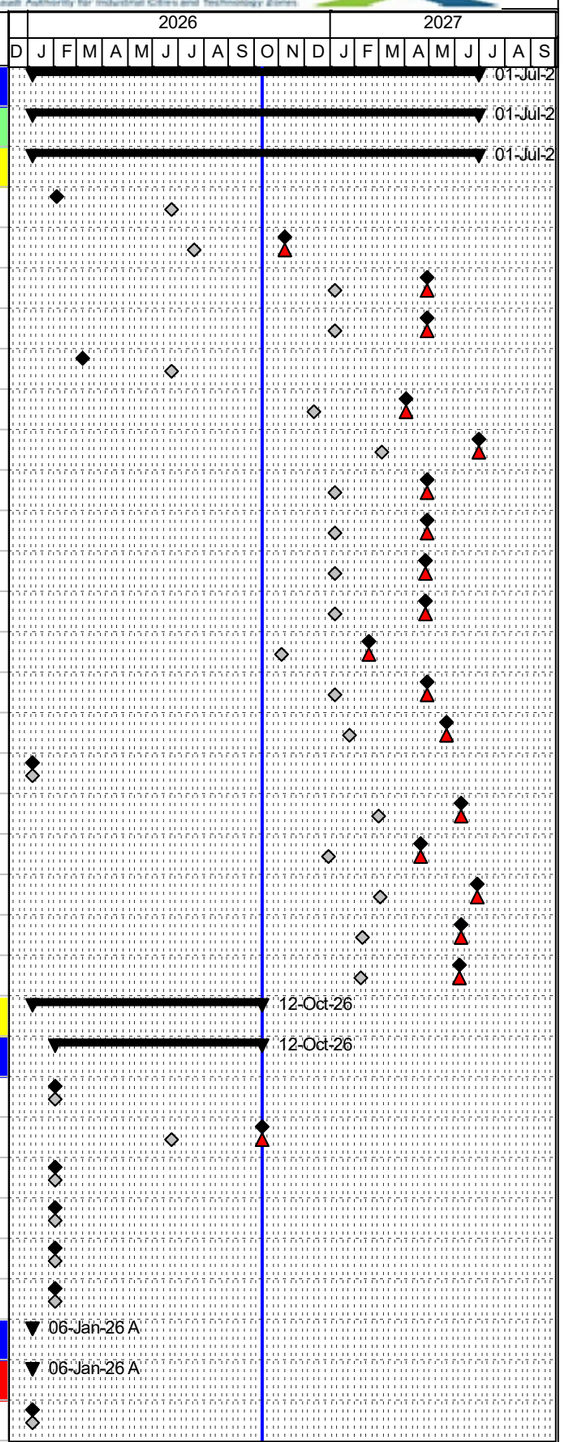

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| MS-CS-LV | Receipt of Approval NOC From Relevant Authorities For Low Voltage Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-MV | Receipt of Approval NOC From Relevant Authorities For Medium Voltage Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-PW | Receipt of Approval NOC From Relevant Authorities For Potable Water Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-RD | Receipt of Approval NOC From Relevant Authorities For Roads Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-SD | Receipt of Approval NOC From Relevant Authorities For Storm Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-SL | Receipt of Approval NOC From Relevant Authorities For Street Lighting Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-SW | Receipt of Approval NOC From Relevant Authorities For Sewage Network | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-TE | Receipt of Approval NOC From Relevant Authorities For Telecom and Light Current | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-TSE | Receipt of Approval NOC From Relevant Authorities For Treated Sewage Effluent | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| **Superstructure Works** | | 0 | 06-Jan-26 A | 06-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| MS-CS-IR10 | Receipt of Approval NOC From Relevant Authorities For Sewage Pump Station | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-LV10 | Receipt of Approval NOC From Relevant Authorities For Boundary Fence | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-MV10 | Receipt of Approval NOC From Relevant Authorities For Water Pump Station | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-SL10 | Receipt of Approval NOC From Relevant Authorities For Storm Drainage Ponds | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-TE10 | Receipt of Approval NOC From Relevant Authorities For Storage Tank (TSE) | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-TE20 | Receipt of Approval NOC From Relevant Authorities For Control Room | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| MS-CS-TSE10 | Receipt of Approval NOC From Relevant Authorities For Gaurd Room | 0 | 06-Jan-26 A | | 0 | 0 | 0 | 0 | 100% | 100% |
| **Preliminaries and Mobilization Works** | | 79 | 06-Jan-26 A | 11-Apr-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Mobilization Works** | | 79 | 06-Jan-26 A | 11-Apr-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| MOB-10 | Clear and Grub for Offices and Access Roads | 14 | 06-Jan-26 A | 20-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-20 | Project Site Layout Plan Approval | 7 | 21-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-30 | Supply & Install of Temporary Offices for the Project | 9 | 01-Apr-26 A | 09-Apr-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-40 | Construction Project Store | 10 | 01-Apr-26 A | 11-Apr-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-50 | Mobilization of Major Manpower | 6 | 12-Feb-26 A | 26-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-60 | Mobilization of Major Equipments | 6 | 12-Feb-26 A | 07-Mar-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-70 | Installation Project Sign Board | 10 | 01-Apr-26 A | 11-Apr-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| MOB-80 | Construction Site Access Roads | 17 | 28-Jan-26 A | 15-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Project Main Documents From The Contractor** | | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRE-CON-MDC-10 | Submission Project Execution Plan | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-20 | Submission Project Baseline Schedule | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-30 | Submission Project Health & Safety Plan | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-40 | Submission Project Quality Control Plan | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-50 | Submission Project Surveying Report | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-60 | Submission Project Geotechnical Soil Report | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |

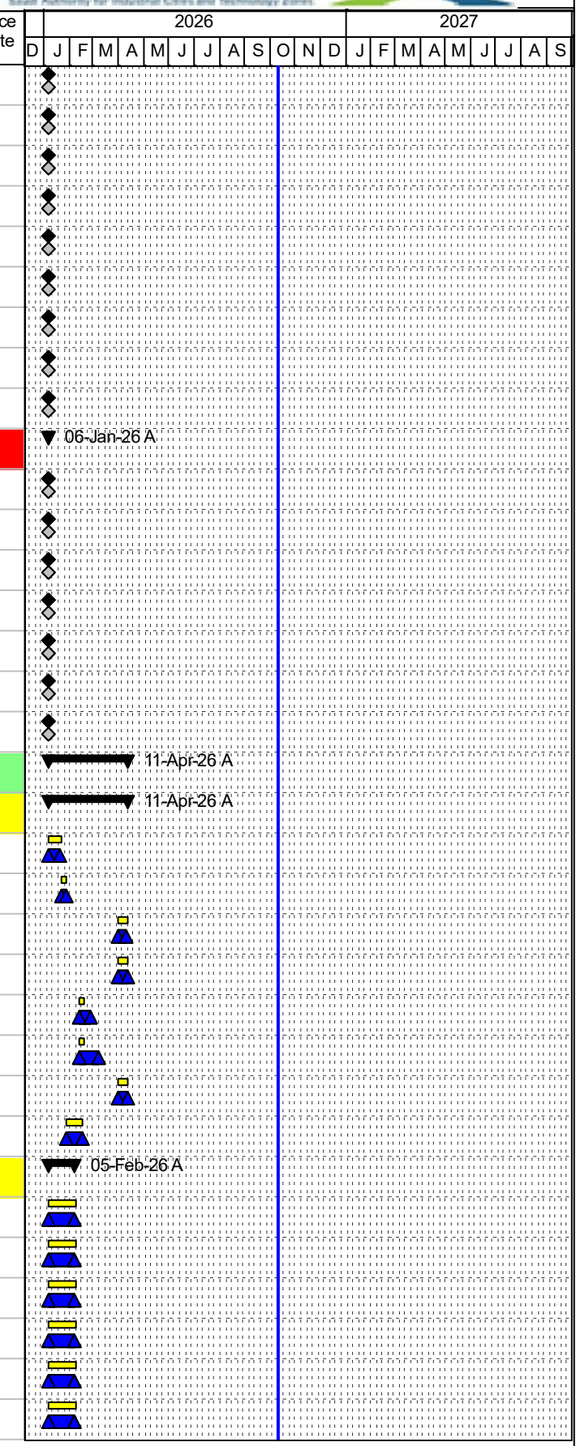



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRE-CON-MDC-70 | Submission Project Environmental Plan | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRE-CON-MDC-80 | Submission Project Organization Chart and Communications Plan | 28 | 06-Jan-26 A | 05-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Engineering Works** | | 254 | 06-Jan-26 A | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Shop Drawings** | | 27 | 06-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 27 | 06-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 27 | 06-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **General Road Works** | | 21 | 06-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-RD-A-100 | Approval Shop Drawings for Plan and Profile of Road Works | 7 | 11-Jan-26 A | 17-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-RD-A-110 | Approval Shop Drawings for Roads Typical Sections and Pavement Details | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-RD-S-100 | Submission Shop Drawings for Plan and Profile of Road Works | 5 | 06-Jan-26 A | 10-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-RD-S-110 | Submission Shop Drawings for Roads Typical Sections and Pavement Details | 5 | 18-Jan-26 A | 21-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Landscape Works** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-HS-A-110 | Approval Shop Drawings for Landscape Works | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-HS-S-100 | Submission Shop Drawings for Landscape Works | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Traffic Sign Boards and Road Marking** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-MRK-A-110 | Approval Shop Drawings for Road Markings | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-MRK-S-110 | Submission Shop Drawings for Road Markings | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-TSB-A-100 | Approval Shop Drawings for Traffic Signs Boards | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-TSB-S-100 | Submission Shop Drawings for Traffic Signs Boards | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storm Drainage Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-SD-ML-A-110 | Approval Shop Drawings for Main Line and Manholes of Storm Drainage Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-SD-ML-S-100 | Submission Shop Drawings for Main Line and Manholes of Storm Drainage Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-SD-CB-A-110 | Approval Shop Drawings for Secondary Line and Catch Basin of Storm Drainage Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-SD-CB-S-100 | Submission Shop Drawings for Secondary Line and Catch Basin of Storm Drainage | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storm Drainage Ponds** | | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-DPO-A-120 | Approval Shop Drawings Package for Storm Drainage Ponds | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-DPO-S-110 | Submission Shop Drawings Package for Storm Drainage Ponds | 4 | 22-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-SW-ML-A-110 | Approval Shop Drawings for Main Line and Manholes of Sewage Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-SW-ML-S-100 | Submission Shop Drawings for Main Line and Manholes of Sewage Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Treated Sewage Effluent Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

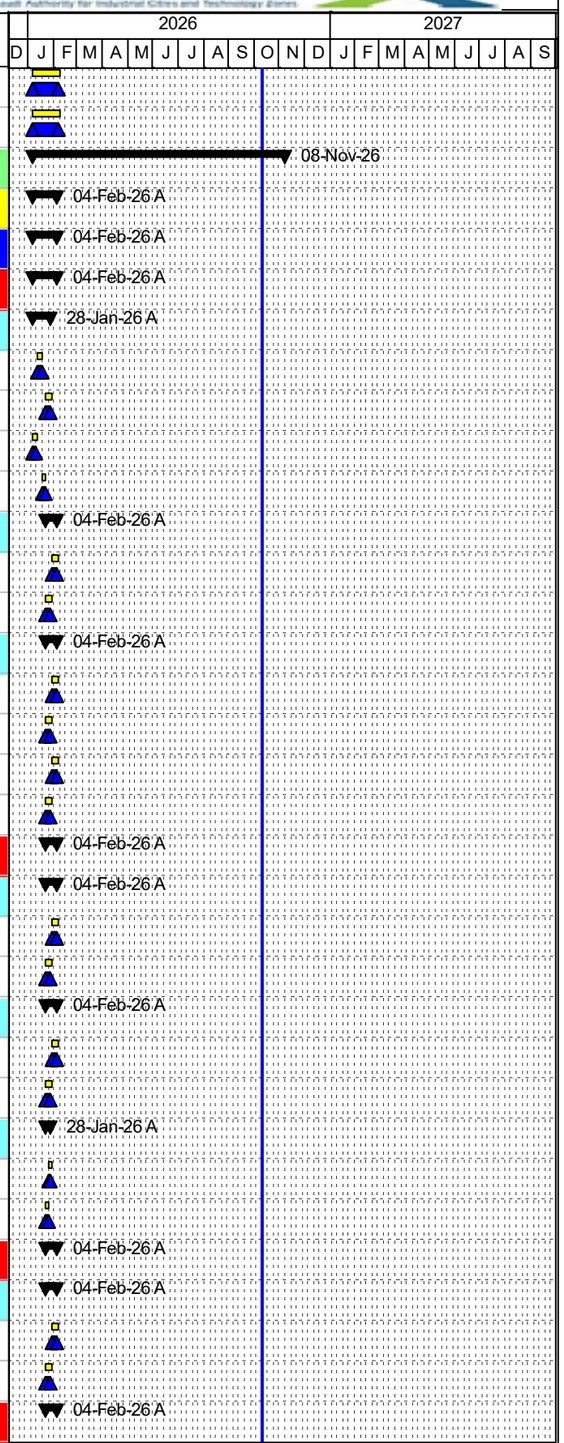



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| ENG-SH-TSE-ML-A-120 | Approval Shop Drawings for Main Line Treated Sewage Effluent Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-TSE-ML-S-110 | Submission Shop Drawings for Main Line Treated Sewage Effluent Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Potable Water Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-PW-ML-A-110 | Approval Shop Drawings for Main Line and Valve Chambers of Potable Water Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-PW-ML-S-100 | Submission Shop Drawings for Main Line and Valve Chambers of Potable Water Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Fire Hydrant** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-PW-FH-A-110 | Approval Shop Drawings for Fire Hydrant Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-PW-FH-S-100 | Submission Shop Drawings for Fire Hydrant Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Irrigation Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-IR-ML-A-110 | Approval Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-IR-ML-S-100 | Submission Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Medium Voltage Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-MV-A-110 | Approval Shop Drawings for Medium Voltage Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-MV-S-100 | Submission Shop Drawings for Medium Voltage Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Low Voltage Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-LV-A-120 | Approval Shop Drawings for Low Voltage Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-LV-S-110 | Submission Shop Drawings for Low Voltage Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Street Lighting Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-SL-A-110 | Approval Shop Drawings for Street Lighting Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-SL-S-100 | Submission Shop Drawings for Street Lighting Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Telecom Network** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-CTV-A-110 | Approval Shop Drawings for CCTV and Telephone Complete Systems | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-CTV-S-100 | Submission Shop Drawings for CCTV and Telephone Complete Systems | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-MSN-A-120 | Approval Shop Drawings for MSN and Access Control Systems | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-MSN-S-110 | Submission Shop Drawings for MSN and Access Control Systems | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-TE-A-110 | Approval Shop Drawings for Telecom Network | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-TE-S-100 | Submission Shop Drawings for Telecom Network | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Superstructure Works** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-LS-A-170 | Approval Shop Drawings Package for Water Pump Station | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-LS-S-160 | Submission Shop Drawings Package for Water Pump Station | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storage Tank (TSE)** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

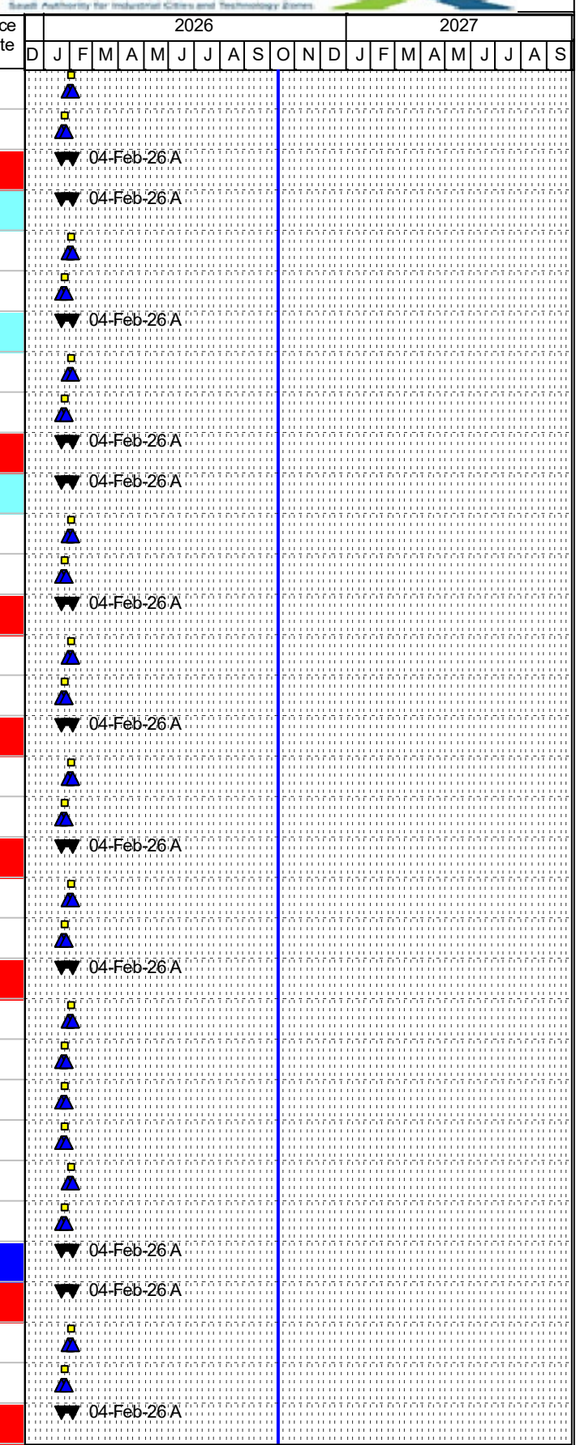



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| ENG-SH-ST-A-180 | Approval Shop Drawings Package for Storage Tank TSE | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-ST-S-170 | Submission Shop Drawings Package for Storage Tank TSE | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Control Room** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-ST-A-190 | Approval Shop Drawings Package for Control Room | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-ST-S-180 | Submission Shop Drawings Package for Control Room | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Pump Stations** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-SPS-A-160 | Approval Shop Drawings Package for Sewage Pump Station | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-SPS-S-150 | Submission Shop Drawings Package for Sewage Pump Station | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Gaurd Room** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-GR-A-190 | Approval Shop Drawings Package for Gaurd Room | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-GR-S-180 | Submission Shop Drawings Package for Gaurd Room | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Boundary Fence** | | 13 | 22-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-SH-GR-A-200 | Approval Shop Drawings Package for Boundary Fence | 7 | 29-Jan-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-SH-GR-S-190 | Submission Shop Drawings Package for Boundary Fence | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Method Statements** | | 13 | 18-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 13 | 18-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 5 | 25-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-SD-ML-A-110 | Approval Method Statement for Main Line of Storm Drainage Network | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-SD-ML-S-100 | Submission Method Statement for Main Line of Storm Drainage Network | 2 | 25-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-SD-CB-A-110 | Approval Method Statement for Catch Basin of Storm Drainage Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-SD-CB-S-100 | Submission Method Statement for Catch Basin of Storm Drainage Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storm Drainage Ponds** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-DPO-A-130 | Approval Method Statement Package for Storm Drainage Ponds | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-DPO-S-120 | Submission Method Statement Package for Storm Drainage Ponds | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-SW-ML-A-110 | Approval Method Statement for Main Line of Sewage Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-SW-ML-S-100 | Submission Method Statement for Main Line of Sewage Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Treated Sewage Effluent Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-TSE-ML-A-120 | Approval Method Statement for Main Line of Treated Sewage Effluent Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-TSE-ML-S-110 | Submission Method Statement for Main Line of Treated Sewage Effluent Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Potable Water Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

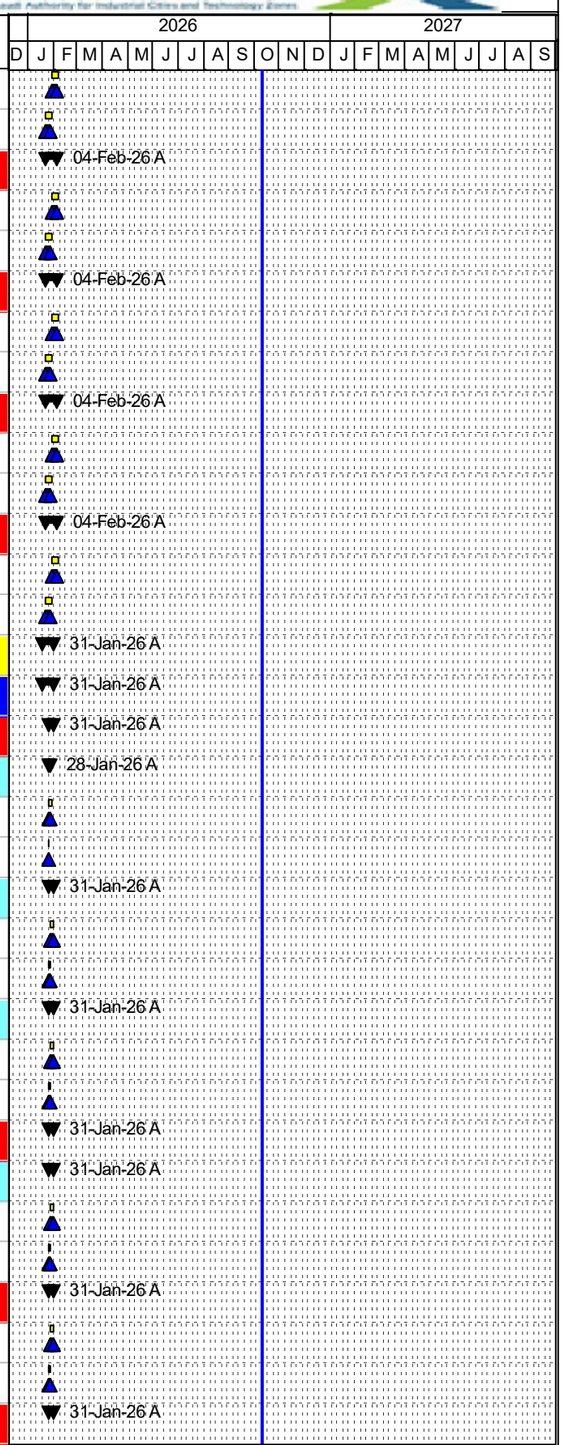



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Main Line Sections** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-PW-ML-A-110 | Approval Method Statement for Main Line of Potable Water Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-PW-ML-S-100 | Submission Method Statement for Main Line of Potable Water Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Irrigation Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-IR-ML-A-110 | Approval Method Statement for Main Line of Irrigation Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-IR-ML-S-100 | Submission Method Statement for Main Line of Irrigation Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Medium Voltage Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-MV-A-110 | Approval Method Statement for Medium Voltage Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-MV-S-100 | Submission Method Statement for Medium Voltage Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Low Voltage Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-MV-A-120 | Approval Method Statement for Low Voltage Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-MV-S-110 | Submission Method Statement for Low Voltage Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Street Lighting Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-SL-A-110 | Approval Method Statement for Street Lighting Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-SL-S-100 | Submission Method Statement for Street Lighting Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Telecom Network** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-CTV-A-110 | Approval Method Statement for CCTV, Telephone, MSN, and Access Control | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-CTV-S-100 | Submission Method Statement for CCTV, Telephone, MSN, and Access Control | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-TE-A-110 | Approval Method Statement for Telecom Network | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-TE-S-100 | Submission Method Statement for Telecom Network | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Road Works** | | 11 | 18-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **General Road Works** | | 11 | 18-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-RD-A-10 | Approval Method Statement for Plan and Profile of Road Works | 4 | 21-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-A-20 | Approval Method Statement for Roads Typical Sections and Pavement Details | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-A-30 | Approval Method Statement of Extraover for Pedestrian ramps | 4 | 21-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-A-40 | Approval Method Statement for Intersections of Road Works | 4 | 21-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-S-10 | Submission Method Statement for Plan and Profile of Road Works | 4 | 18-Jan-26 A | 20-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-S-20 | Submission Method Statement for Roads Typical Sections and Pavement Details | 4 | 22-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-S-30 | Submission Method Statement of Extraover for Pedestrian ramps | 4 | 18-Jan-26 A | 20-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-RD-S-40 | Submission Method Statement for Intersections of Road Works | 4 | 18-Jan-26 A | 20-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Landscape Works** | | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-HS-A-10 | Approval Method Statement for Landscaping Works | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-HS-S-10 | Submission Method Statement for Landscaping Works | 4 | 22-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |

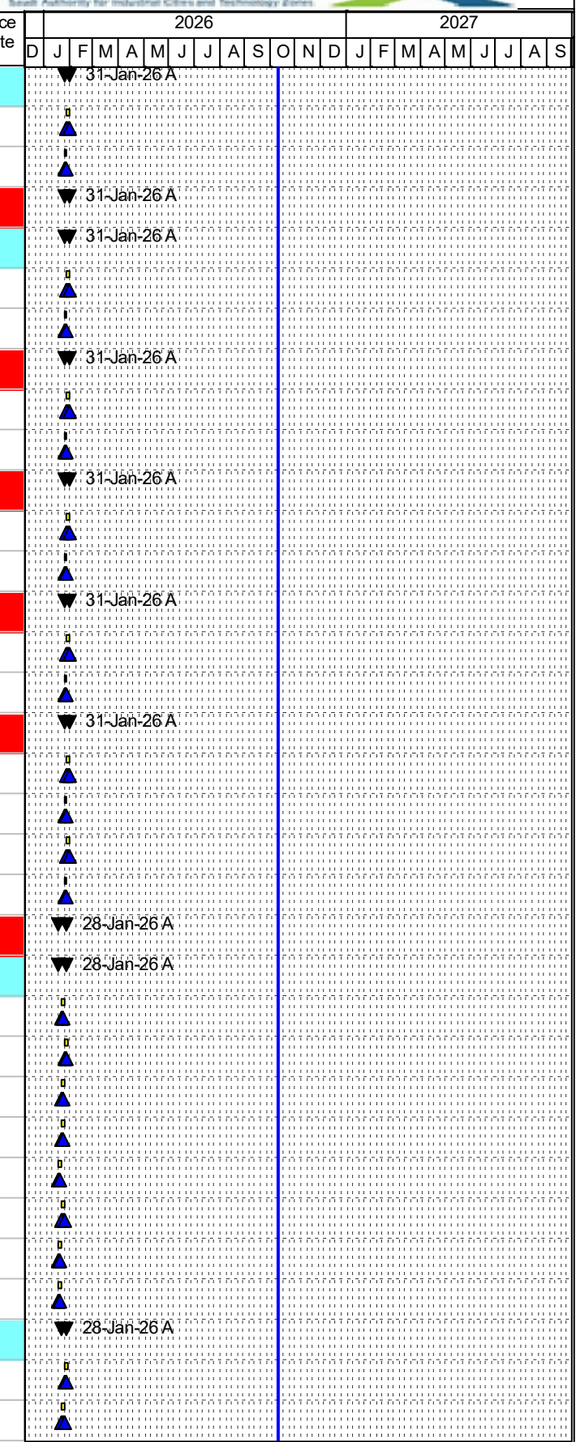



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Traffic Sign Boards and Road Marking** | | 7 | 22-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-MRK-A-10 | Approval Method Statement for Roads Markings | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-MRK-S-10 | Submission Method Statement for Roads Markings | 4 | 22-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-TSB-A-10 | Approval Method Statement for Traffic Signs Boards | 4 | 26-Jan-26 A | 28-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-TSB-S-10 | Submission Method Statement for Traffic Signs Boards | 4 | 22-Jan-26 A | 25-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Superstructure Works** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-LS-A-180 | Approval Method Statement Package for Water Pump Station | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-LS-S-170 | Submission Method Statement Package for Water Pump Station | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storage Tank (TSE)** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-ST-A-190 | Approval Method Statement Package for Storage Tank TSE | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-ST-S-180 | Submission Method Statement Package for Storage Tank TSE | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Control Room** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-ST-A-200 | Approval Method Statement Package for Control Room | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-ST-S-190 | Submission Method Statement Package for Control Room | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Pump Stations** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-SPS-A-170 | Approval Method Statement Package for Sewage Pump Station | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-SPS-S-160 | Submission Method Statement Package for Sewage Pump Station | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Gaurd Room** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-GR-A-210 | Approval Method Statement Package for Gaurd Room | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-GR-S-200 | Submission Method Statement Package for Gaurd Room | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Boundary Fence** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MS-GR-A-220 | Approval Method Statement Package for Boundary Fence | 4 | 28-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MS-GR-S-210 | Submission Method Statement Package for Boundary Fence | 4 | 25-Jan-26 A | 27-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Material Submittals and Approvals** | | 254 | 06-Jan-26 A | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Short Lead Time Items** | | 124 | 06-Jan-26 A | 13-Jun-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 23 | 06-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-ML-S-100 | Material Submittal for Manholes of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SD-ML-S-110 | Material Submittal for Main Line Pipes of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-CB-S-100 | Material Submittal for Catch Basins of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |

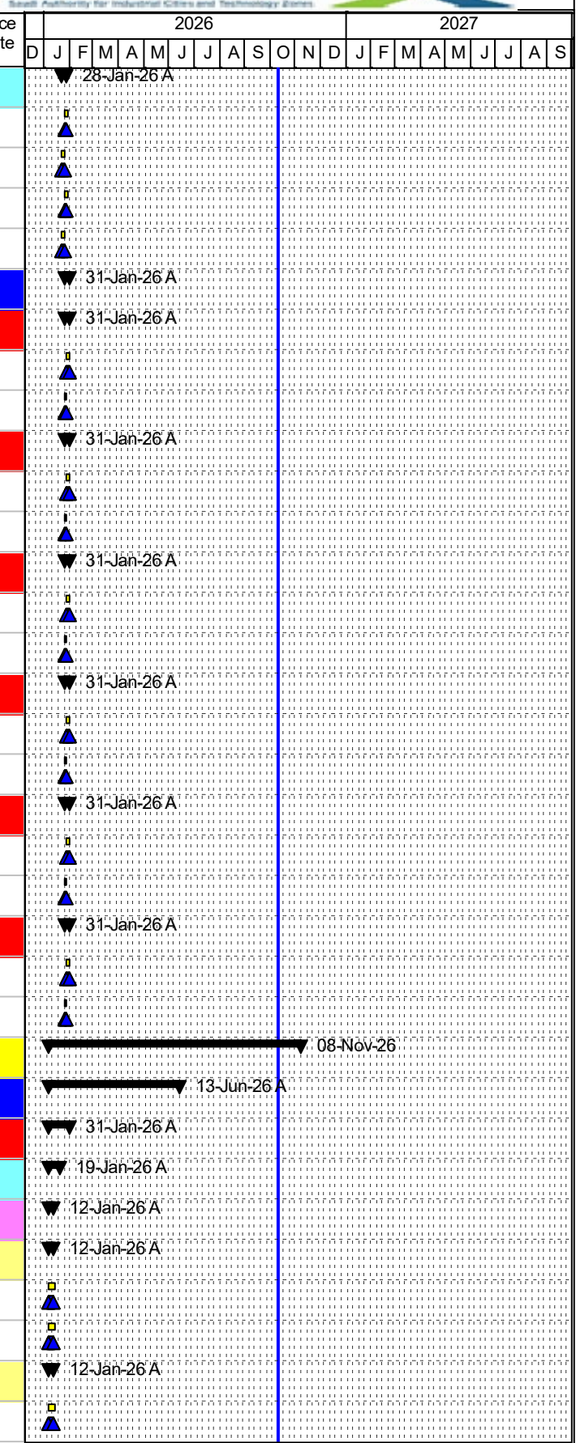



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| ENG-MT-SD-CB-S-110 | Material Submittal for Catch Basin Pipes of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storm Drainage Pond** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-DPO-CV-S-100 | Material Submittal for Materials of Storm Drainage Ponds | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-TF-S-100 | Material Submittal for Manhole Covers of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SD-TF-S-110 | Material Submittal for Catch Basin Covers of Storm Drainage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-ML-A-100 | Material Approval for Manholes of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SD-ML-A-110 | Material Approval for Main Line Pipes of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-CB-A-100 | Material Approval for Catch Basins of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SD-CB-A-110 | Material Approval for Catch Basin Pipes of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storm Drainage Pond** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-DPO-CV-A-110 | Material Approval for Materials of Storm Drainage Ponds | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SD-TF-A-100 | Material Approval for Manhole Covers of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SD-TF-A-110 | Material Approval for Catch Basin Covers of Storm Drainage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Network** | | 13 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SW-ML-S-100 | Material Submittal for Manholes of Sewage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SW-ML-S-110 | Material Submittal for Main Line Pipes of Sewage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SW-TF-S-100 | Material Submittal for Manhole Covers of Sewage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SW-ML-A-100 | Material Approval for Manholes of Sewage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SW-ML-A-110 | Material Approval for Main Line Pipes of Sewage Network | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SW-TF-A-100 | Material Approval for Manhole Covers of Sewage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Treated Sewage Effluent (Tse)** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-S-120 | Material Submittal for Materials of Treated Sewage Effluent (TSE) | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |

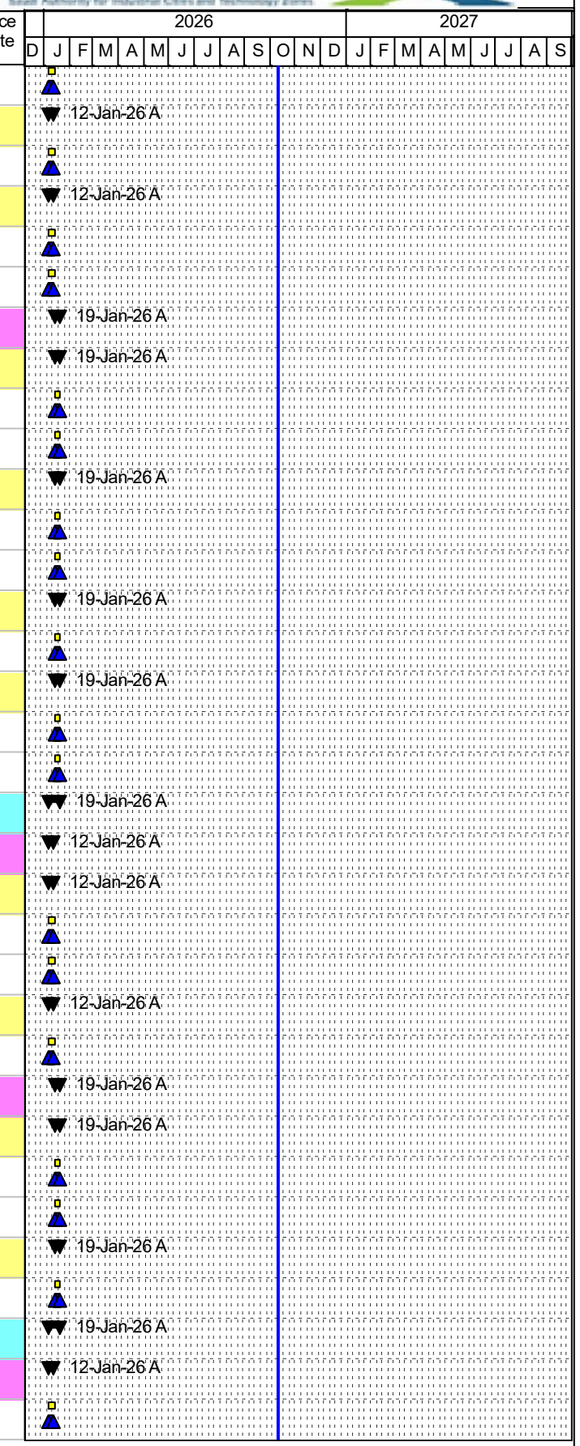



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-A-120 | Material Approval for Materials of Treated Sewage Effluent (TSE) | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Potable Water Network** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-ML-S-100 | Material Submittal for Main Line Pipes and Materials of Potable Water Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-PW-ML-S-110 | Material Submittal for Main Line Valves of Potable Water Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Fire Hydrant** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-FH-S-100 | Material Submittal for Fire Hydrant of Potable Water Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-TF-S-100 | Material Submittal for Surface Box of Potable Water Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-ML-A-100 | Material Approval for Main Line Pipes and Materials of Potable Water Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-PW-ML-A-110 | Material Approval for Valves of Potable Water Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Fire Hydrant** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-FH-A-100 | Material Approval for Fire Hydrants of Potable Water Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Testing and Finishes** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PW-TF-A-100 | Material Approval for Surface Box of Potable Water Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Irrigation Network** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-S-100 | Material Submittal for Main Line Pipes of Irrigation Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-IR-ML-S-110 | Material Submittal for Main Line Valves of Irrigation Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-A-100 | Material Approval for Main Line Pipes of Irrigation Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-IR-ML-A-110 | Material Approval for Valves of Irrigation Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Medium Voltage Network** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-MV-ML-S-100 | Material Submittal for Medium Voltage Materials of Medium Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-MV-ML-A-100 | Material Approval for Medium Voltage Materials of Medium Voltage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Low Voltage Network** | | 13 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

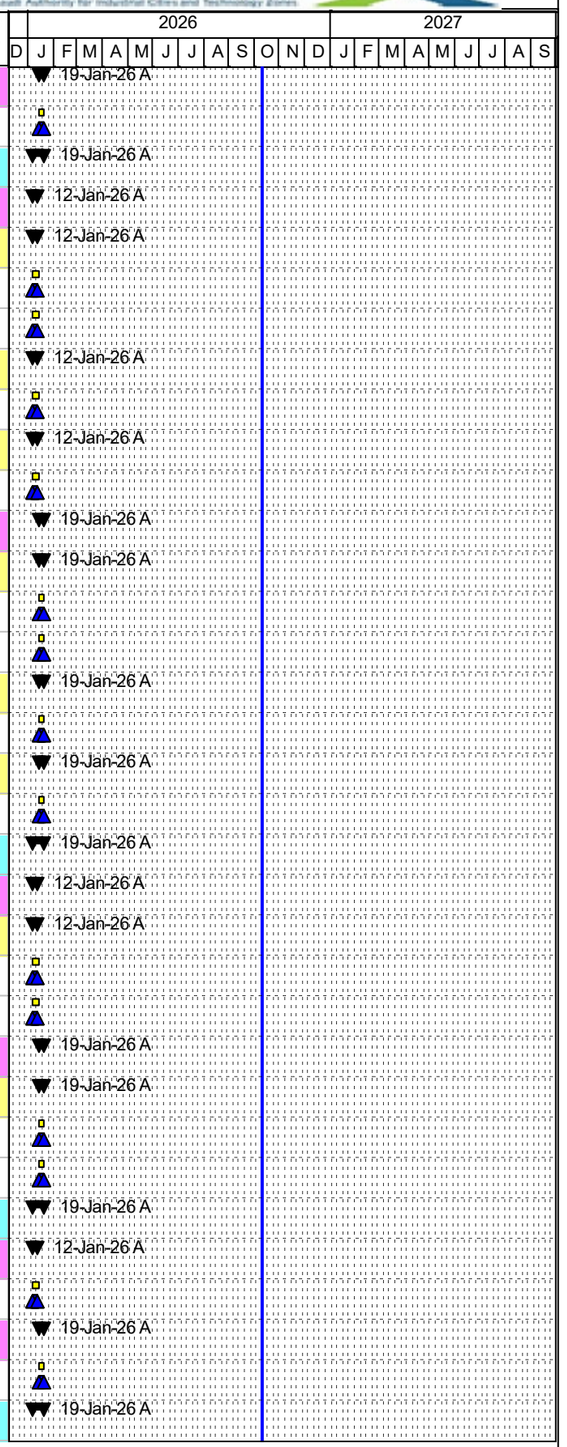



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-S-100 | Material Submittal for Main Low Voltage Cables of Low Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Service Low Voltage Cables Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-S-100 | Material Submittal for Service Low Voltage Cables of Low Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Distribution Pillars Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-S-100 | Material Submittal for Distribution Pillars of Low Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-LV-DP-S-110 | Material Submittal for Low Voltage Earthing of Low Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Termination and Testing Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-S-100 | Material Submittal for Cable Lugs of Low Voltage Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-A-100 | Material Approval for Main Low Voltage Cables of Low Voltage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Service Low Voltage Cables Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-A-100 | Material Approval for Service Low Voltage Cables of Low Voltage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Distribution Pillars Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-A-100 | Material Approval for Distribution Pillars of Low Voltage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-LV-DP-A-110 | Material Approval for Low Voltage Earthing of Low Voltage Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Termination and Testing Works** | | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-A-100 | Material Approval for Cable Lugs of Low Voltage Network | 7 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Street Lighting Network** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-ML-S-100 | Material Submittal for Lighting Cables of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Lighting Poles Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-S-100 | Material Submittal for Lighting Poles Concrete Foundations of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-S-110 | Material Submittal for Lighting Poles of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-S-120 | Material Submittal for Lighting Fixtures of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Distribution Panel Board** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-DB-S-100 | Material Submittal for Lighting Distrubution Panel Boards of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Termination and Testing Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-TF-S-100 | Material Submittal for Fuse Boxes of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-TF-S-110 | Material Submittal for Cable Lugs of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Earthing System Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

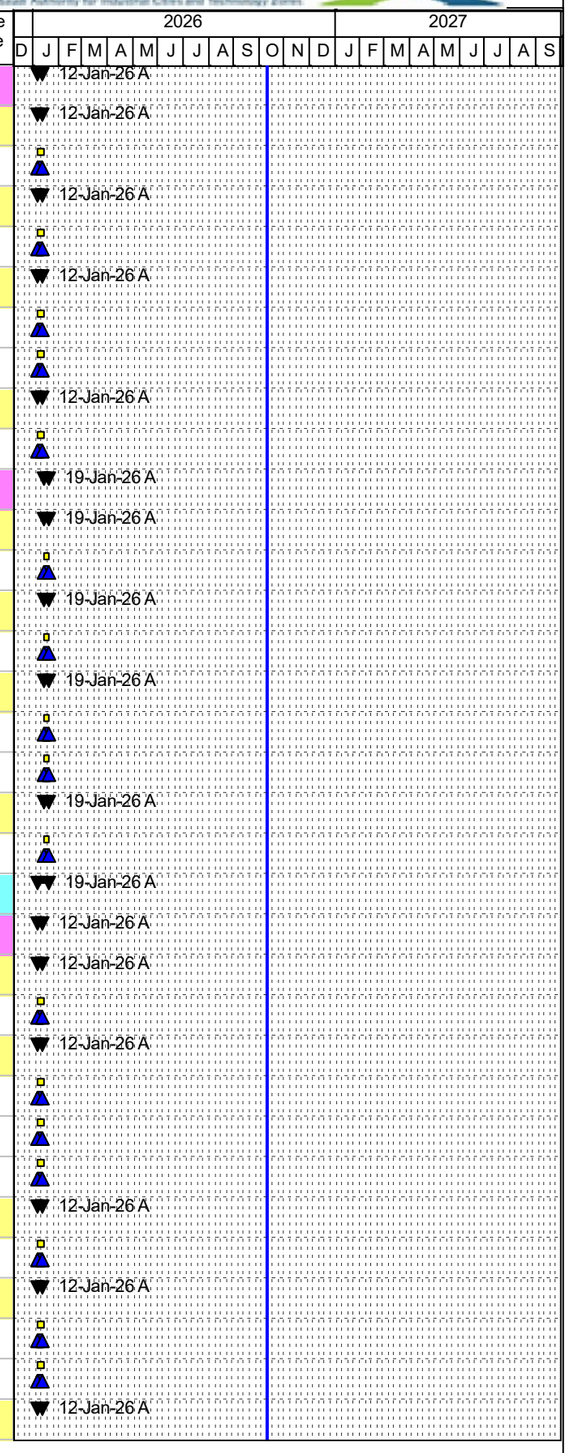



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| ENG-MT-SL-ES-S-100 | Material Submittal for Lighting Earthing of Street Lighting Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-ML-A-100 | Material Approval for Lighting Cables of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Lighting Poles Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-A-100 | Material Approval for Lighting Poles Concrete Foundations of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-A-110 | Material Approval for Lighting Poles of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-A-120 | Material Approval for Lighting Fixtures of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Distribution Panel Board** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-DB-A-100 | Material Approval for Distrubution Panel Boards of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Termination and Testing Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-TF-A-100 | Material Approval for Fuse Boxes of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-SL-TF-A-110 | Material Approval for Cable Lugs of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Earthing System Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SL-ES-A-100 | Material Approval for Lighting Earthing of Street Lighting Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Telecom and Light Current Networks** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TE-S-100 | Material Submittal for Ducts of Telecom Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Manholes Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TE-S-110 | Material Submittal for Manholes of Telecom Network | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **CCTV, Telephone, MSN, ACs System Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-CTV-S-100 | Material Submittal for Materials of CCTV, Telephone, MSN, and Access Control | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TE-A-100 | Material Approval for Ducts of Telecom Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Manholes Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TE-A-110 | Material Approval for Manholes of Telecom Network | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **CCTV, Telephone, MSN, ACs System Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-CTV-A-100 | Material Approval for for Materials of CCTV, Telephone, MSN, and Access Control | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Road Works** | | 23 | 06-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 17 | 06-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **General Road Works** | | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-RD-S-100 | Material Submittal for Subgrade of Road Works | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |

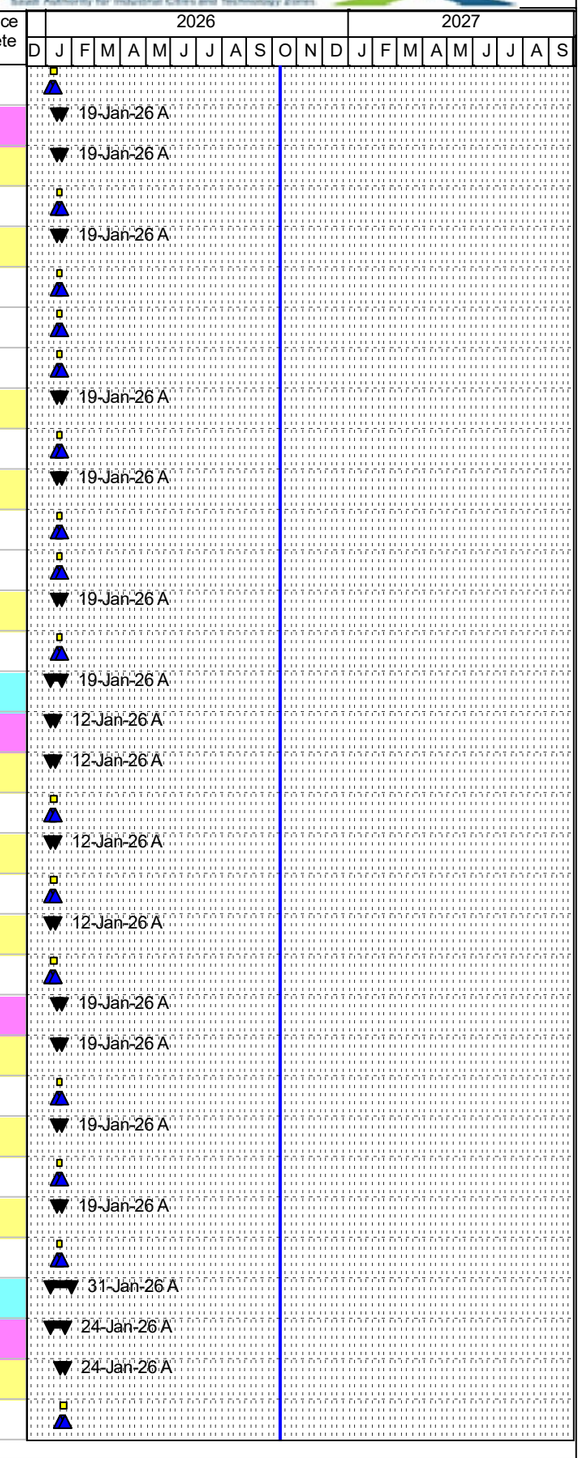



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| ENG-MT-RD-S-110 | Material Submittal for Aggregate Base Course of Road Works | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-S-120 | Material Submittal for Prime Coat of Road Works | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-S-130 | Material Submittal for Asphaltic Base Course Laver of Road Works | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-S-160 | Material Submittal for Asphaltic Wearing Course Laver for Roads Network | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-S-170 | Material Submittal for Tack Coat Layer for Roads Network | 7 | 18-Jan-26 A | 24-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Landscape Works** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-RD-S-140 | Material Submittal for Interlock Tiles of Landscaping | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-S-150 | Material Submittal for Curbstones of Landscaping | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Traffic Signs Boards and Roads Marking** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TS-S-100 | Material Submittal for Traffic Signs Boards of Road Works | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-TS-S-110 | Material Submittal for Road Markings of Road Works | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 17 | 13-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **General Road Works** | | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-RD-A-100 | Material Approval for Subgrade of Road Works | 6 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-110 | Material Approval for Aggregate Base Course of Road Works | 6 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-120 | Material Approval for Prime Coat of Road Works | 6 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-130 | Material Approval for Asphaltic Base Course Layer of Road Works | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-160 | Material Approval for Asphaltic Wearing Course Laver for Roads Network | 7 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-170 | Material Approval for Tack Coat Layer for Roads Network | 6 | 25-Jan-26 A | 31-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Landscape Works** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-RD-A-140 | Material Approval of Interlock Tiles for Landscaping | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-RD-A-150 | Material Approval of Curbstones for Landscaping | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Traffic Signs Boards and Roads Marking** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TS-A-100 | Material Approval for Traffic Signs Boards of Road Works | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-TS-A-110 | Material Approval for Road Markings of Road Works | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Softscape and Planting Works** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-S-140 | Material Submittal for Softscape and Planting Works | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-IR-ML-S-150 | Material Submittal for Site Furnishings (Seating Bench,Stone Boulders and Gravel) | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-IR-ML-A-140 | Material Approval for Softscape and Planting Works | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| ENG-MT-IR-ML-A-150 | Material Approval for Site Furnishings (Seating Bench,Stone Boulders and Gravel) | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Superstructure Works** | | 124 | 06-Jan-26 A | 13-Jun-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |

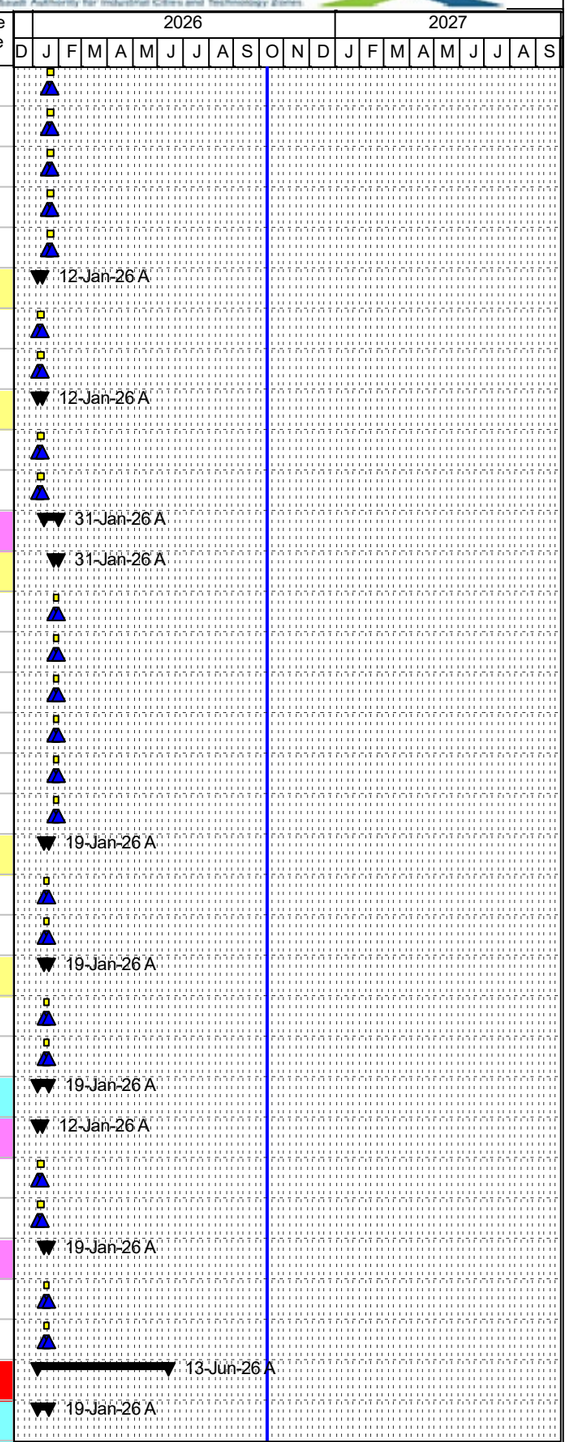



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SLS-CV-S-100 | Material Submittal for Works for Water Pump Station | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SLS-CV-A-110 | Material Approval for Works for Water Pump Station | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Storage Tank (TSE)** | | 12 | 06-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-CV-S-130 | Material Submittal for Works for Storage Tank (TSE) | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-CV-A-140 | Material Approval for Works for Storage Tank (TSE) | 6 | 13-Jan-26 A | 19-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Control Room** | | 7 | 03-Feb-26 A | 10-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 3 | 03-Feb-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-CV-S-140 | Material Submittal for Works for Control Room | 3 | 03-Feb-26 A | 04-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 6 | 04-Feb-26 A | 10-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-CV-A-150 | Material Approval for Works for Control Room | 6 | 04-Feb-26 A | 10-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Sewage Pump Stations** | | 36 | 06-Jan-26 A | 16-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PS-CV-S-140 | Material Submittal for Works of Sewage Pump Station | 7 | 06-Jan-26 A | 12-Jan-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 5 | 11-Feb-26 A | 16-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-PS-CV-A-150 | Material Approval for Works of Sewage Pump Station | 5 | 11-Feb-26 A | 16-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Gaurd Room** | | 8 | 18-Feb-26 A | 02-Mar-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 0 | 18-Feb-26 A | 19-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-GR-CV-S-120 | Material Submittal for Materials for Gaurd Room | 0 | 18-Feb-26 A | 19-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 7 | 19-Feb-26 A | 02-Mar-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-GR-CV-A-130 | Material Approval for Materials for Gaurd Room | 7 | 19-Feb-26 A | 02-Mar-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Boundary Fence** | | 82 | 25-Feb-26 A | 13-Jun-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 0 | 25-Feb-26 A | 26-Feb-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-FE-CV-S-110 | Material Submittal for Materials for Boundary Fence | 0 | 25-Feb-26 A | 26-Feb-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Approval of Material** | | 80 | 28-Feb-26 A | 13-Jun-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-FE-CV-A-120 | Material Approval for Materials for Boundary Fence | 80 | 28-Feb-26 A | 13-Jun-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Long Lead Time Items** | | 24 | 12-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Superstructure Works** | | 24 | 12-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Pump Stations** | | 12 | 12-Oct-26 | 25-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 6 | 12-Oct-26 | 18-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SPS-MC-S-100 | Material Submittal for Electromechanical Works for Pump Station | 6 | 12-Oct-26 | 18-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |

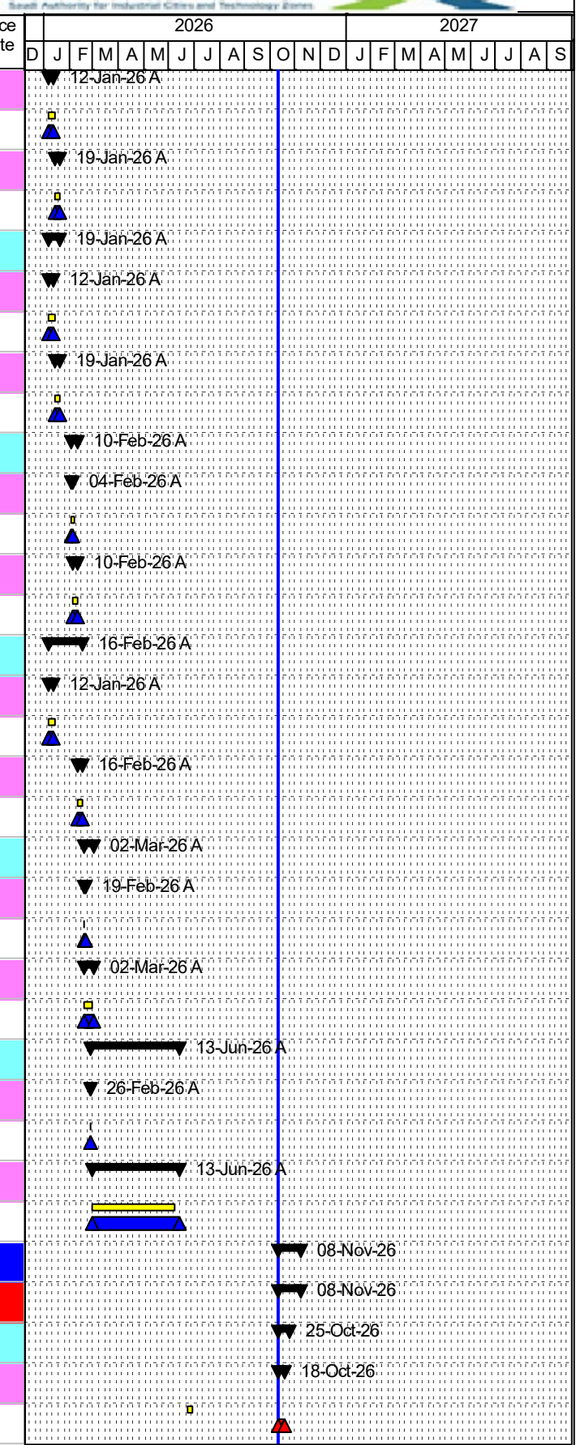



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Approval of Material** | | 6 | 19-Oct-26 | 25-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-SPS-MC-A-110 | Material Approval for Electromechanical Works for Pump Station | 6 | 19-Oct-26 | 25-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storage Tank (TSE)** | | 24 | 12-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Submission of Material** | | 12 | 12-Oct-26 | 25-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-MC-S-110 | Material Submittal for Electromechanical Works for Storage Tank (TSE) | 12 | 12-Oct-26 | 25-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Approval of Material** | | 12 | 26-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| ENG-MT-TSE-MC-A-120 | Material Approval for Electromechanical Works for Storage Tank (TSE) | 12 | 26-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Procurement Cycle** | | 331 | 02-May-26 A | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Short Lead Time Items** | | 294 | 02-May-26 A | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 294 | 02-May-26 A | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 123 | 01-Jul-26 A | 20-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 41 | 01-Jul-26 A | 16-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 12 | 01-Jul-26 A | 13-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-PO-100 | Issuance of Purchase Order for Manholes of Storm Drainage Network | 2 | 12-Oct-26 | 13-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-PO-110 | Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network | 2 | 01-Jul-26 A | 02-Jul-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 11 | 14-Oct-26 | 26-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-PO-130 | Issuance of Purchase Order for Catch Basins of Storm Drainage Network | 5 | 14-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-PO-150 | Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network | 6 | 20-Oct-26 | 26-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 12 | 27-Oct-26 | 09-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-PO-120 | Issuance of Purchase Order for Manhole Covers of Storm Drainage Network | 6 | 27-Oct-26 | 02-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-PO-140 | Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network | 6 | 03-Nov-26 | 09-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storm Drainage Ponds** | | 6 | 10-Nov-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-DPO-CV-PO-10 | Issuance of Purchase Order for Materials of Storm Drainage Ponds | 6 | 10-Nov-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 103 | 05-Jul-26 A | 30-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 24 | 05-Jul-26 A | 22-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-MF-100 | Manufacturing of Materials for Manholes of Storm Drainage Network | 8 | 14-Oct-26 | 22-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-MF-110 | Manufacturing of Materials for Main Line Pipes of Storm Drainage Network | 24 | 05-Jul-26 A | 07-Jul-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 31 | 20-Oct-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-MF-130 | Manufacturing of Materials for Catch Basins of Storm Drainage Network | 25 | 20-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-MF-150 | Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network | 25 | 27-Oct-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 50 | 25-Nov-26 | 21-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-MF-120 | Manufacturing of Materials for Manhole Covers of Storm Drainage Network | 20 | 25-Nov-26 | 17-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-MF-140 | Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network | 30 | 19-Dec-26 | 21-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storm Drainage Ponds** | | 64 | 17-Nov-26 | 30-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |

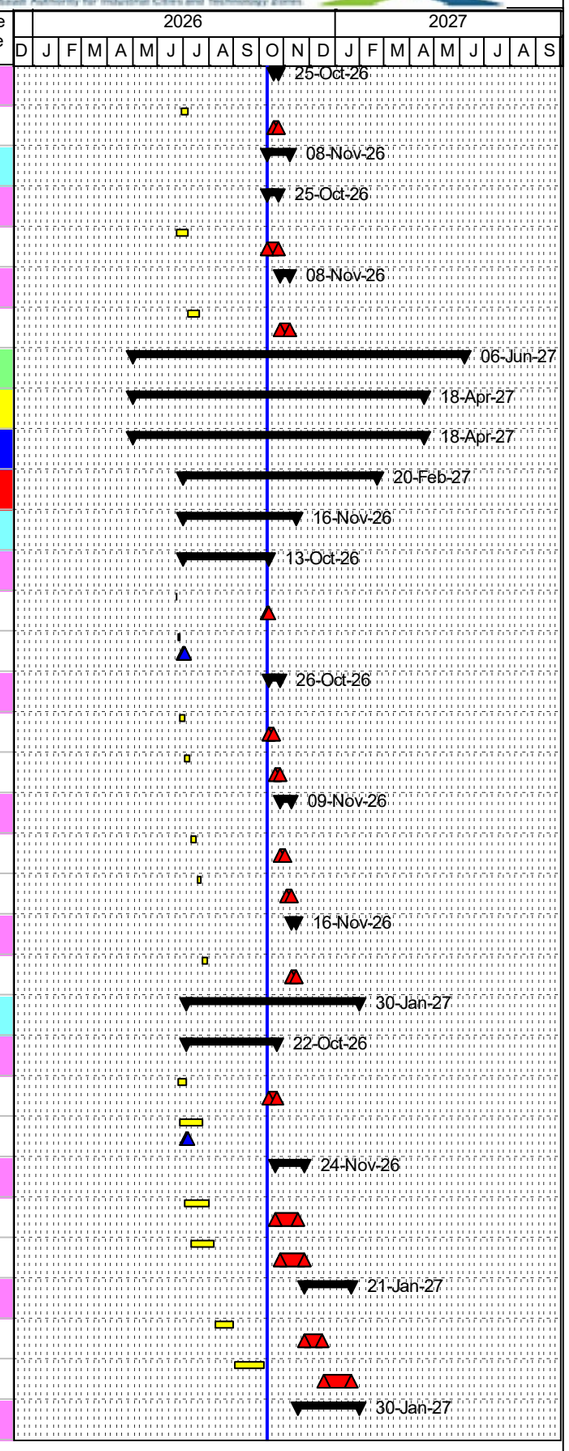



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-DPO-CV-MF-10 | Manufacturing of Materials of Storm Drainage Ponds | 64 | 17-Nov-26 | 30-Jan-27 | 0 | 0 | 0 | 0 | 95.31% | 0% |
| **1st Material Delivery & Site Inspection** | | 89 | 08-Jul-26 A | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 10 | 08-Jul-26 A | 27-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-1DL-100 | 1ST Material Delivery for Manholes of Storm Drainage Network | 4 | 24-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-1DL-110 | 1ST Material Delivery for Main Line Pipes of Storm Drainage Network | 4 | 08-Jul-26 A | 12-Jul-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Catch Basin Sections** | | 10 | 18-Nov-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-1DL-120 | 1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network | 4 | 25-Nov-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-1DL-130 | 1ST Material Delivery for Catch Basins of Storm Drainage Network | 4 | 18-Nov-26 | 22-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 34 | 19-Dec-26 | 26-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SD-1DL-140 | 1ST Material Delivery for Manholes Covers of Storm Drainage Network | 4 | 19-Dec-26 | 22-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SD-1DL-150 | 1ST Material Delivery for Catch Basin Covers of Storm Drainage Network | 4 | 23-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storm Drainage Ponds** | | 4 | 31-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-DPO-CV-1DL-10 | 1ST Material Delivery for Materials of Drainage Ponds | 4 | 31-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Delivery & Site Inspection** | | 99 | 20-Jul-26 A | 20-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 21 | 20-Jul-26 A | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SD-DL-100 | Material Delivery & Site Inspection of Manholes of Storm Drainage Network | 10 | 28-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-SD-DL-120 | Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network | 15 | 20-Jul-26 A | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 95% |
| **Catch Basin Sections** | | 15 | 23-Nov-26 | 09-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SD-DL-110 | Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network | 7 | 02-Dec-26 | 09-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-SD-DL-130 | Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network | 8 | 23-Nov-26 | 01-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 44 | 23-Dec-26 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SD-DL-140 | Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network | 20 | 23-Dec-26 | 14-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-SD-DL-150 | Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network | 14 | 27-Jan-27 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Ponds** | | 14 | 04-Feb-27 | 20-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-DPO-CV-DL-10 | Material Delivery & Site Inspection for Materials of Storm Drainage Ponds | 14 | 04-Feb-27 | 20-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Network** | | 41 | 12-Oct-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 21 | 12-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 14 | 12-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SW-PO-100 | Issuance of Purchase Order for Main Line Pipes of Sewage Network | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SW-PO-110 | Issuance of Purchase Order for Manhole of Sewage Network | 7 | 20-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 7 | 28-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SW-PO-120 | Issuance of Purchase Order for Manhole Covers of Sewage Network | 7 | 28-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 20 | 20-Oct-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 17 | 20-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |

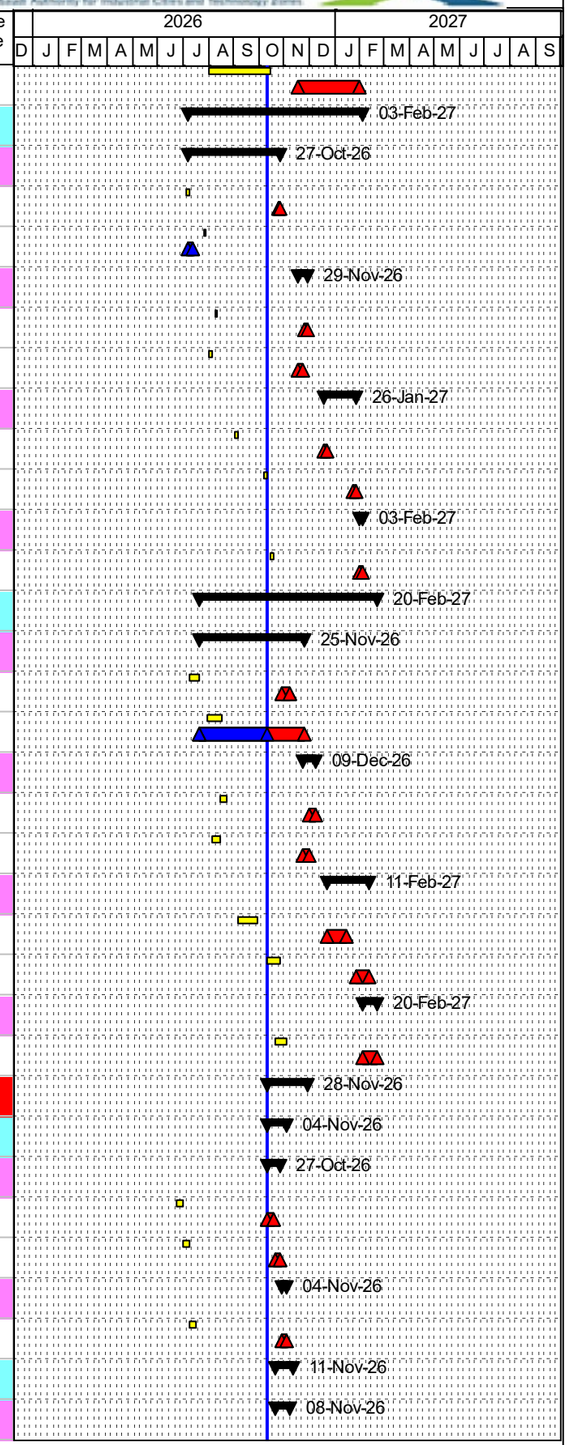



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-SW-MF-100 | Manufacturing of Main Line Pipes for Sewage Network | 10 | 20-Oct-26 | 31-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SW-MF-110 | Manufacturing of Manholes for Sewage Network | 10 | 28-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 6 | 05-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SW-MF-120 | Manufacturing of Manhole Covers for Sewage Network | 6 | 05-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 16 | 01-Nov-26 | 18-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 14 | 01-Nov-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SW-1DL-100 | 1ST Material Delivery for Main Line Pipes of Sewage Network | 4 | 01-Nov-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SW-1DL-110 | 1ST Material Delivery for Manholes of Sewage Network | 4 | 12-Nov-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 2 | 17-Nov-26 | 18-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SW-1DL-120 | 1ST Material Delivery for Manholes Covers of Sewage Network | 2 | 17-Nov-26 | 18-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 10 | 17-Nov-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 10 | 17-Nov-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SW-DL-100 | Material Delivery & Site Inspection of Main Line Pipes for Sewage Network | 4 | 24-Nov-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-SW-DL-110 | Material Delivery & Site Inspection of Manholes for Sewage Network | 4 | 17-Nov-26 | 21-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 4 | 19-Nov-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SW-DL-120 | Material Delivery & Site Inspection of Manholes Covers for Sewage Network | 4 | 19-Nov-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Treated Sewage Effluent (Tse)** | | 52 | 12-Oct-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-PO-120 | Issuance of Purchase Order for Materials of Treated Sewage Effluent (Tse) | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 24 | 20-Oct-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-MF-120 | Manufacturing of Materials for Treated Sewage Effluent (Tse) | 24 | 20-Oct-26 | 16-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 7 | 17-Nov-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-1DL-120 | 1ST Material Delivery for Materials of Treated Sewage Effluent (Tse) | 7 | 17-Nov-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 14 | 25-Nov-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-TSE-DL-120 | Material Delivery & Site Inspection of Materials for Treated Sewage Effluent (Tse) | 14 | 25-Nov-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Potable Water Network** | | 269 | 02-May-26 A | 20-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 146 | 02-May-26 A | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 11 | 02-May-26 A | 12-May-26 A | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-PO-100 | Issuance of Purchase Order for Main Line Pipes and Materials of Potable Water Network | 11 | 02-May-26 A | 12-May-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-PW-PO-110 | Issuance of Purchase Order for Valves of Potable Water Network | 11 | 02-May-26 A | 12-May-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| **Fire Hydrant** | | 5 | 12-Oct-26 | 17-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-PO-120 | Issuance of Purchase Order for Fire Hydrants of Potable Water Network | 5 | 12-Oct-26 | 17-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 6 | 18-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-PO-130 | Issuance of Purchase Order for Surface Box of Potable Water Network | 6 | 18-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |

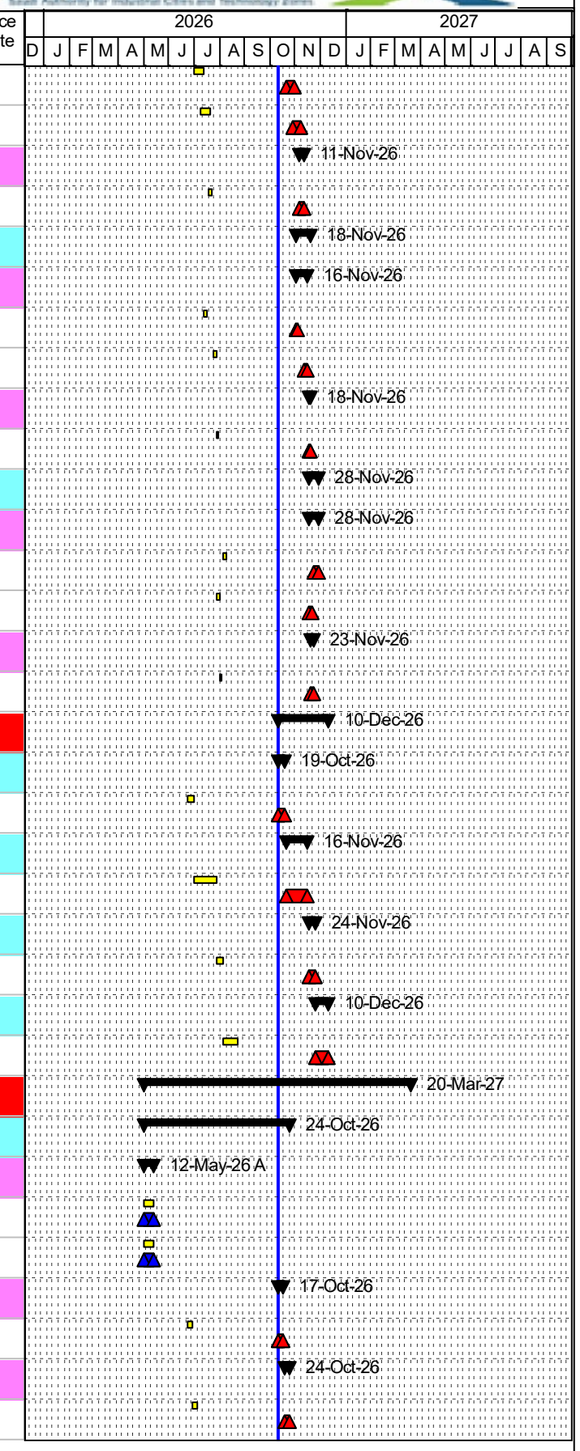



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Manufacturing of Material** | | 73 | 05-Jul-26 A | 21-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 36 | 05-Jul-26 A | 08-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-MF-100 | Manufacturing of Main Line Pipes and Materials for Potable Water Network | 34 | 05-Jul-26 A | 07-Jul-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-PW-MF-110 | Manufacturing of Valves for Potable Water Network | 24 | 12-Oct-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Fire Hydrant** | | 15 | 09-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-MF-120 | Manufacturing of Fire Hydrants for Potable Water Network | 15 | 09-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 50 | 25-Oct-26 | 21-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-MF-130 | Manufacturing for Surface Box of Potable Water Network | 50 | 25-Oct-26 | 21-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 19 | 12-Jul-26 A | 29-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 19 | 12-Jul-26 A | 29-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-1DL-100 | 1ST Material Delivery for Main Line Pipes and Materials of Potable Water Network | 7 | 12-Jul-26 A | 16-Jul-26 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-PW-1DL-110 | 1ST Material Delivery for Valves of Potable Water Network | 7 | 22-Dec-26 | 29-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Fire Hydrant** | | 7 | 22-Dec-26 | 29-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-1DL-120 | 1ST Material Delivery for Fire Hydrants of Potable Water Network | 7 | 22-Dec-26 | 29-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 7 | 22-Dec-26 | 29-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-PW-1DL-130 | 1ST Material Delivery for Finishes of Potable Water Network | 7 | 22-Dec-26 | 29-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 78 | 10-Oct-26 A | 20-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 33 | 10-Oct-26 A | 23-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-PW-DL-100 | Material Delivery & Site Inspection of Main Line Pipes and Materials for Potable Water | 21 | 10-Oct-26 A | 09-Jan-27 A | 0 | 0 | 0 | 0 | 100% | 100% |
| PRO-R25-PW-DL-110 | Material Delivery & Site Inspection of Valves for Potable Water Network | 21 | 30-Dec-26 | 23-Jan-27 | 0 | 0 | 0 | 0 | 23.81% | 0% |
| **Fire Hydrant** | | 6 | 30-Dec-26 | 05-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-PW-DL-120 | Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network | 6 | 30-Dec-26 | 05-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Testing and Finishes** | | 66 | 30-Dec-26 | 20-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-PW-DL-130 | Material Delivery & Site Inspection for Finishes of Potable Water Network | 66 | 30-Dec-26 | 20-Mar-27 | 0 | 0 | 0 | 0 | 39.39% | 0% |
| **Irrigation Network** | | 75 | 25-Oct-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 9 | 25-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 9 | 25-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-PO-100 | Issuance of Purchase Order for Main Line Pipes of Irrigation Network | 5 | 25-Oct-26 | 29-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-PO-110 | Issuance of Purchase Order for Valves of Irrigation Network | 4 | 31-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 42 | 31-Oct-26 | 17-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 42 | 31-Oct-26 | 17-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-MF-100 | Manufacturing of Main Line Pipes for Irrigation Network | 21 | 31-Oct-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-MF-110 | Manufacturing of Valves for Irrigation Network | 21 | 24-Nov-26 | 17-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 28 | 24-Nov-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |

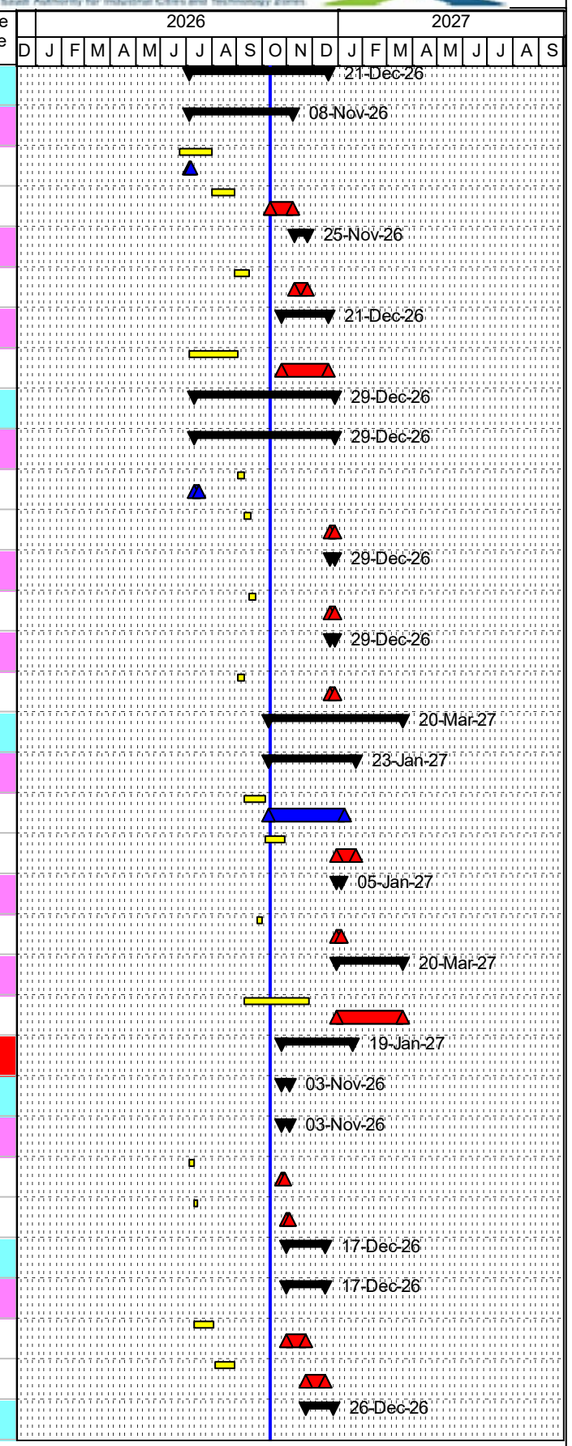



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Main Line Pipes** | | 28 | 24-Nov-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-1DL-100 | 1ST Material Delivery for Main Line Pipes of Irrigation Network | 7 | 24-Nov-26 | 01-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-1DL-110 | 1ST Material Delivery for Valves of Irrigation Network | 7 | 19-Dec-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 42 | 02-Dec-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 42 | 02-Dec-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-IR-DL-100 | Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network | 21 | 02-Dec-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-IR-DL-110 | Material Delivery & Site Inspection of Valves for Irrigation Network | 21 | 27-Dec-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Medium Voltage Network** | | 66 | 04-Nov-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 6 | 04-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-MV-PO-100 | Issuance of Purchase Order for Medium Voltage Materials of Medium Voltage Network | 6 | 04-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 21 | 11-Nov-26 | 05-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-MV-MF-100 | Manufacturing of Medium Voltage Materials for Medium Voltage Network | 21 | 11-Nov-26 | 05-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 7 | 06-Dec-26 | 13-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-MV-1DL-100 | 1ST Material Delivery for Medium Voltage Materials of Medium Voltage Network | 7 | 06-Dec-26 | 13-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 21 | 27-Dec-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-MV-DL-100 | Material Delivery & Site Inspection of Medium Voltage Materials for Medium Voltage Network | 21 | 27-Dec-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Low Voltage Network** | | 136 | 12-Oct-26 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 28 | 12-Oct-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-PO-100 | Issuance of Purchase Order for Main Low Voltage Cables of Low Voltage Network | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Service Low Voltage Cables Works** | | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-PO-100 | Issuance of Purchase Order for Service Low Voltage Cables of Low Voltage Network | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Pillar Works** | | 14 | 20-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-PO-100 | Issuance of Purchase Order for Distribution Pillars of Low Voltage Network | 7 | 20-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-LV-DP-PO-110 | Issuance of Purchase Order for Low Voltage Earthing of Low Voltage Network | 7 | 28-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Termination and Testing Works** | | 7 | 05-Nov-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-PO-100 | Issuance of Purchase Order for Cable Lugs of Low Voltage Network | 7 | 05-Nov-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 91 | 20-Oct-26 | 02-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 30 | 20-Oct-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-MF-100 | Manufacturing of Main Low Voltage Cables for Low Voltage Network | 30 | 20-Oct-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Service Low Voltage Cables Works** | | 30 | 20-Oct-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-MF-100 | Manufacturing of Service Low Voltage Cables for Low Voltage Network | 30 | 20-Oct-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Pillar Works** | | 47 | 28-Oct-26 | 21-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-MF-100 | Manufacturing of Distribution Pillars for Low Voltage Network | 40 | 28-Oct-26 | 13-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |

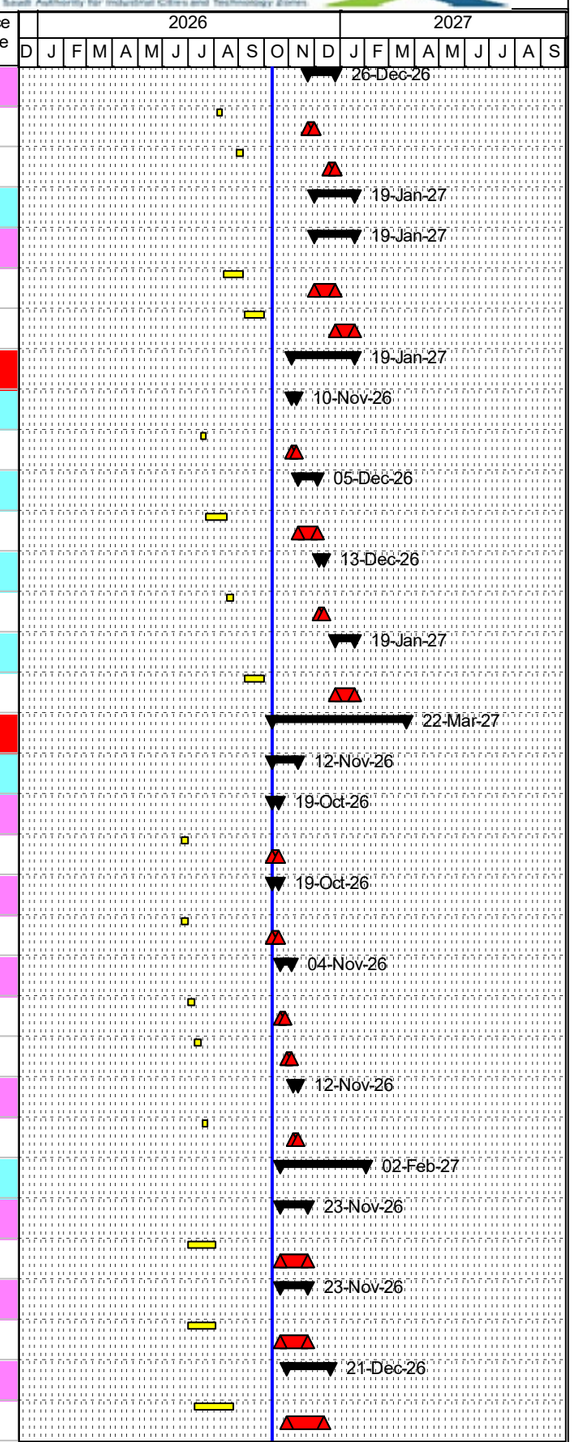



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-LV-DP-MF-110 | Manufacturing of Low Voltage Earthing for Low Voltage Network | 40 | 05-Nov-26 | 21-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Termination and Testing Works** | | 70 | 14-Nov-26 | 02-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-MF-100 | Manufacturing of Cable Lugs for Low Voltage Network | 70 | 14-Nov-26 | 02-Feb-27 | 0 | 0 | 0 | 0 | 94.29% | 0% |
| **1st Delivery of Material to Site** | | 62 | 24-Nov-26 | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 34 | 24-Nov-26 | 02-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-1DL-100 | 1ST Material Delivery for Main Low Voltage Cables of Low Voltage Network | 34 | 24-Nov-26 | 02-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Service Low Voltage Cables Works** | | 7 | 03-Jan-27 | 10-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-1DL-100 | 1ST Material Delivery for Service Low Voltage Cables of Low Voltage Network | 7 | 03-Jan-27 | 10-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Pillar Works** | | 14 | 11-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-1DL-100 | 1ST Material Delivery for Distribution Pillars of Low Voltage Network | 7 | 11-Jan-27 | 18-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-LV-DP-1DL-110 | 1ST Material Delivery for Low Voltage Earthing of Low Voltage Network | 7 | 19-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Termination and Testing Works** | | 7 | 27-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-1DL-100 | 1ST Material Delivery for Cable Lugs of Low Voltage Network | 7 | 27-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 28.57% | 0% |
| **Delivery of Material to Site** | | 65 | 03-Jan-27 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works** | | 7 | 03-Jan-27 | 10-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-ML-DL-100 | Material Delivery of Main Low Voltage Cables for Low Voltage Network | 7 | 03-Jan-27 | 10-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Service Low Voltage Cables Works** | | 21 | 11-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-HC-DL-100 | Material Delivery of Service Low Voltage Cables for Low Voltage Network | 21 | 11-Jan-27 | 03-Feb-27 | 0 | 0 | 0 | 0 | 76.19% | 0% |
| **Distribution Pillar Works** | | 20 | 03-Feb-27 | 25-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-DL-100 | Material Delivery of Distribution Pillars for Low Voltage Network | 19 | 04-Feb-27 | 25-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-DP-DL-120 | Material Delivery of Low Voltage Earthing for Low Voltage Network | 20 | 03-Feb-27 | 25-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 18 | 27-Feb-27 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LV-TT-DL-100 | Material Delivery of Cable Lugs for Low Voltage Network | 18 | 27-Feb-27 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 130 | 05-Nov-26 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 17 | 05-Nov-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-PO-100 | Issuance of Purchase Order for Lighting Cables of Street Lighting Network | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Lighting Poles Works** | | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-PO-110 | Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Network | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-PO-120 | Issuance of Purchase Order for Lighting Poles of Street Lighting Network | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-PO-140 | Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network | 5 | 05-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Panel Board** | | 6 | 05-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-PO-160 | Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network | 6 | 05-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Termination and Testing Works** | | 7 | 11-Nov-26 | 18-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |

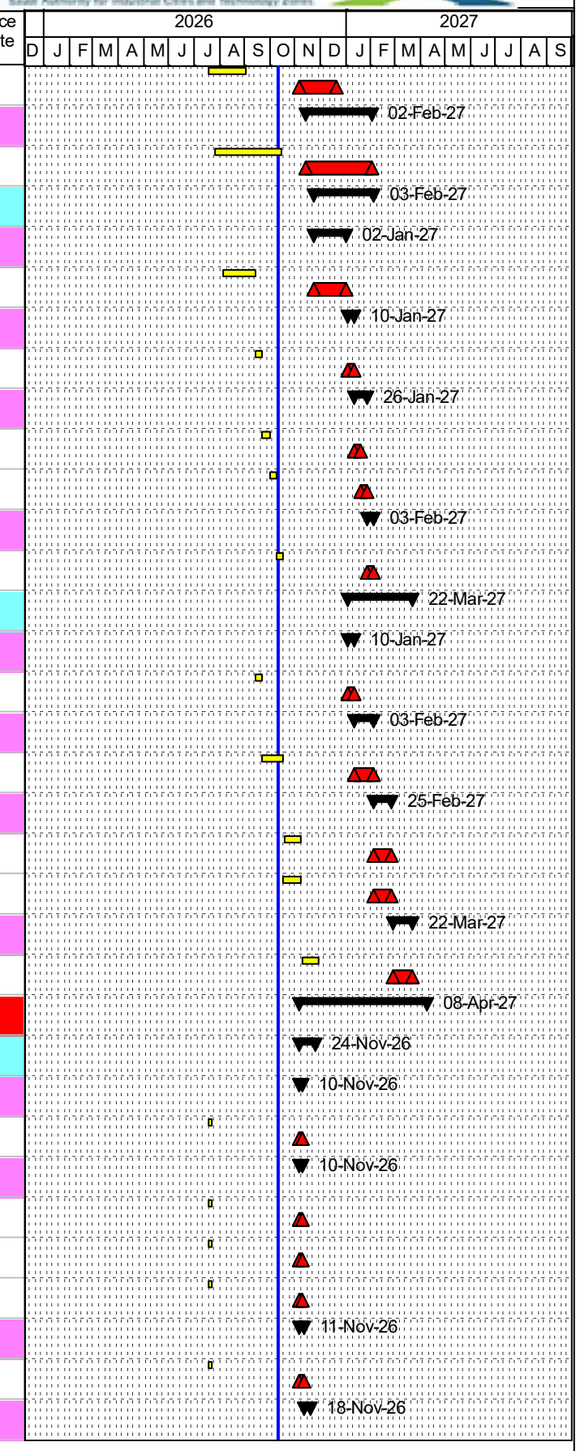



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-SL-PO-130 | Issuance of Purchase Order for Fuse Boxes of Street Lighting Network | 6 | 12-Nov-26 | 18-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-PO-170 | Issuance of Purchase Order for Cable Lugs of Street Lighting Network | 6 | 11-Nov-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Earthing System Works** | | 6 | 18-Nov-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-PO-150 | Issuance of Purchase Order for Lighting Earthing of Street Lighting Network | 6 | 18-Nov-26 | 24-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 98 | 11-Nov-26 | 04-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 20 | 11-Nov-26 | 03-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-MF-100 | Manufacturing of Lighting Cables for Street Lighting Network | 20 | 11-Nov-26 | 03-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Lighting Poles Works** | | 21 | 05-Dec-26 | 28-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-MF-110 | Manufacturing of Lighting Poles Foundations for Street Lighting Network | 21 | 05-Dec-26 | 28-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-MF-120 | Manufacturing of Lighting Poles for Street Lighting Network | 21 | 05-Dec-26 | 28-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-MF-140 | Manufacturing of Lighting Fixtures for Street Lighting Network | 21 | 05-Dec-26 | 28-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Panel Board** | | 30 | 29-Dec-26 | 01-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-MF-160 | Manufacturing of Distrubution Panel Boards for Street Lighting Network | 30 | 29-Dec-26 | 01-Feb-27 | 0 | 0 | 0 | 0 | 90% | 0% |
| **Termination and Testing Works** | | 91 | 19-Nov-26 | 04-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-MF-130 | Manufacturing of Fuse Boxes for Street Lighting Network | 70 | 19-Nov-26 | 08-Feb-27 | 0 | 0 | 0 | 0 | 87.14% | 0% |
| PRO-SL-MF-170 | Manufacturing of Cable Lugs for Street Lighting Network | 21 | 09-Feb-27 | 04-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 40 | 25-Nov-26 | 10-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-MF-150 | Manufacturing of Lighting Earthing for Street Lighting Network | 40 | 25-Nov-26 | 10-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 90 | 05-Dec-26 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 6 | 05-Dec-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-100 | 1ST Material Delivery for Lighting Cables of Street Lighting Network | 6 | 05-Dec-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Lighting Poles Works** | | 18 | 29-Dec-26 | 18-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-110 | 1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network | 6 | 29-Dec-26 | 04-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-1DL-120 | 1ST Material Delivery for Lighting Poles of Street Lighting Network | 6 | 05-Jan-27 | 11-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-SL-1DL-140 | 1ST Material Delivery for Lighting Fixtures of Street Lighting Network | 6 | 12-Jan-27 | 18-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Distribution Panel Board** | | 6 | 02-Feb-27 | 08-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-160 | 1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network | 6 | 02-Feb-27 | 08-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 27 | 09-Feb-27 | 15-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-130 | 1ST Material Delivery for Fuse Boxes of Street Lighting Network | 6 | 09-Feb-27 | 15-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-170 | 1ST Material Delivery for Cable Lugs of Street Lighting Network | 6 | 06-Mar-27 | 15-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 6 | 16-Mar-27 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SL-1DL-150 | 1ST Material Delivery for Lighting Earthing of Street Lighting Network | 6 | 16-Mar-27 | 22-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Delivery & Site Inspection** | | 99 | 12-Dec-26 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 21 | 12-Dec-26 | 04-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |

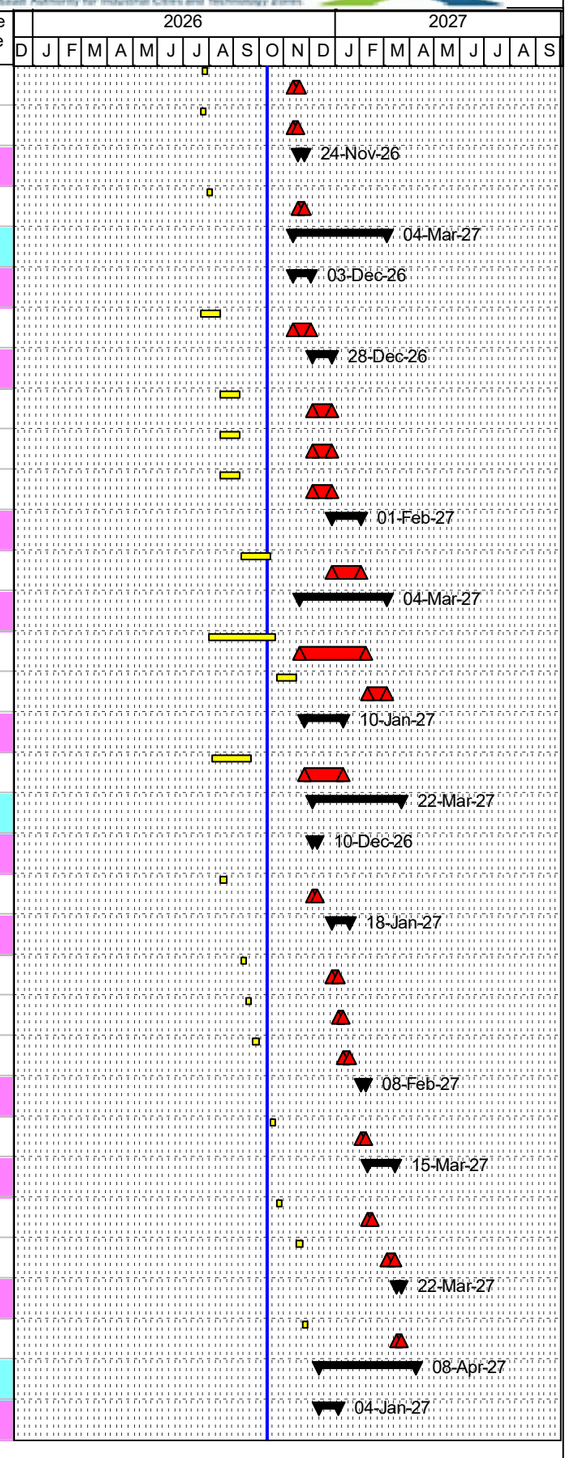



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-R25-SL-DL-100 | Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network | 21 | 12-Dec-26 | 04-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Lighting Poles Works** | | 42 | 29-Dec-26 | 15-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SL-DL-110 | Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network | 21 | 29-Dec-26 | 21-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-SL-DL-120 | Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network | 21 | 23-Jan-27 | 15-Feb-27 | 0 | 0 | 0 | 0 | 28.57% | 0% |
| PRO-R25-SL-DL-140 | Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network | 21 | 23-Jan-27 | 15-Feb-27 | 0 | 0 | 0 | 0 | 28.57% | 0% |
| **Distribution Panel Board** | | 21 | 16-Feb-27 | 15-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SL-DL-160 | Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting | 21 | 16-Feb-27 | 15-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 21 | 16-Mar-27 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SL-DL-130 | Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network | 21 | 16-Mar-27 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SL-DL-170 | Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network | 21 | 16-Mar-27 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 21 | 16-Mar-27 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-SL-DL-150 | Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network | 21 | 16-Mar-27 | 08-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 93 | 18-Nov-26 | 06-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 20 | 18-Nov-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-PO-100 | Issuance of Purchase Order for Ducts forTelecom Network | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manholes Works** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-PO-110 | Issuance of Purchase Order for Manholes forTelecom Network | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 20 | 18-Nov-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-CTV-PO-100 | Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System | 20 | 18-Nov-26 | 10-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 70 | 26-Nov-26 | 15-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 20 | 26-Nov-26 | 19-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-MF-100 | Manufacturing of Ducts for Telecom Network | 20 | 26-Nov-26 | 19-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manholes Works** | | 20 | 20-Dec-26 | 11-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-MF-110 | Manufacturing of Manholes for Telecom Network | 20 | 20-Dec-26 | 11-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 30 | 12-Jan-27 | 15-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-CTV-MF-100 | Manufacturing of Civil and Finishes Works for CCTV Complete System | 30 | 12-Jan-27 | 15-Feb-27 | 0 | 0 | 0 | 0 | 50% | 0% |
| **1st Material Delivery & Site Inspection** | | 56 | 20-Dec-26 | 22-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 6 | 20-Dec-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-1DL-100 | 1ST Material Delivery for Ducts of Telecom Network | 6 | 20-Dec-26 | 26-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manholes Works** | | 6 | 12-Jan-27 | 18-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TE-1DL-110 | 1ST Material Delivery for Manholes of Telecom Network | 6 | 12-Jan-27 | 18-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 6 | 16-Feb-27 | 22-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-CTV-1DL-100 | 1ST Material Delivery for Civil and Finishes Works of CCTV Complete System | 6 | 16-Feb-27 | 22-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |

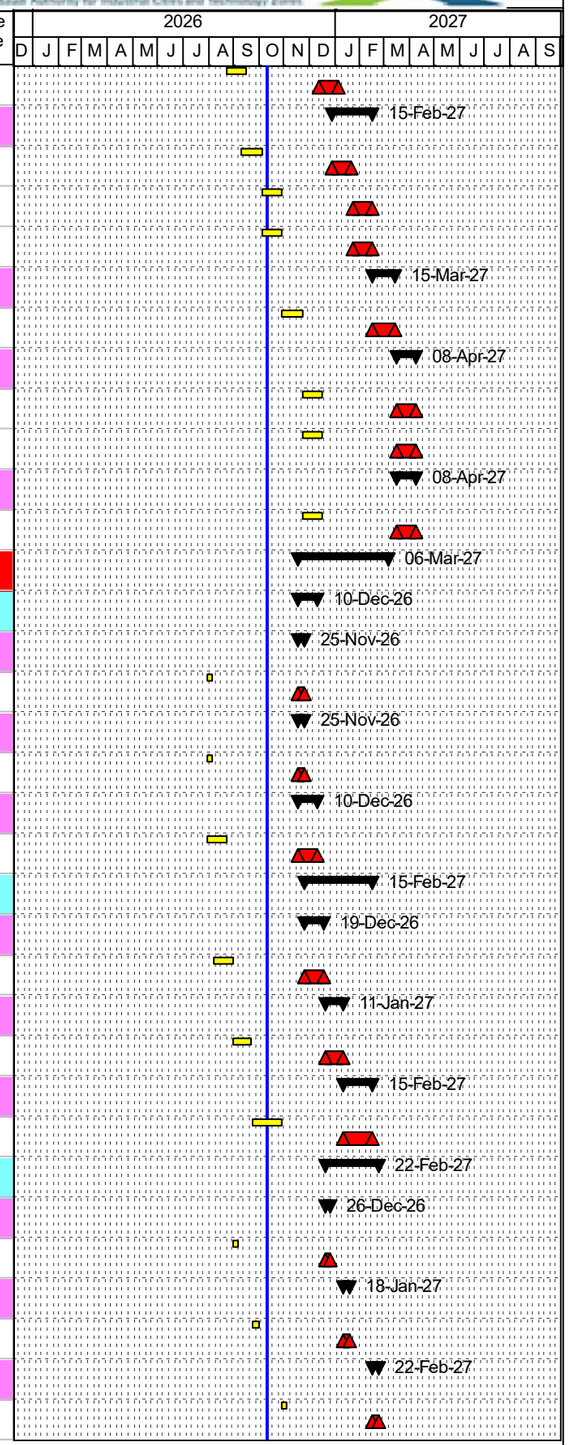



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Material Delivery & Site Inspection** | | 60 | 27-Dec-26 | 06-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 15 | 27-Dec-26 | 12-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-TE-DL-100 | Material Delivery & Site Inspection for Ducts of Telecom Network | 15 | 27-Dec-26 | 12-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manholes Works** | | 15 | 19-Jan-27 | 04-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-TE-DL-110 | Material Delivery & Site Inspection of Manholes for Telecom Network | 15 | 19-Jan-27 | 04-Feb-27 | 0 | 0 | 0 | 0 | 60% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 10 | 23-Feb-27 | 06-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-CTV-DL-100 | Material Delivery & Site Inspection of for Civil and Finishes Works of CCTV Complete | 10 | 23-Feb-27 | 06-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 159 | 12-Oct-26 | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 42 | 12-Oct-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 42 | 12-Oct-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-PO-100 | Issuance of Purchase Order for Subgrade of Road Works | 7 | 12-Oct-26 | 19-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-110 | Issuance of Purchase Order for Aggregate Base Course of Road Works | 7 | 20-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-120 | Issuance of Purchase Order for Prime Coat of Road Works | 7 | 28-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-130 | Issuance of Purchase Order for Asphaltic Base Course Laver of Road Works | 7 | 05-Nov-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-180 | Issuance of Purchase Order for Asphaltic Wearing Course Laver for Roads Network | 7 | 14-Nov-26 | 21-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-190 | Issuance of Purchase Order for Tack Coat Layer for Roads Network | 7 | 22-Nov-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Pavement Works** | | 14 | 28-Oct-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-PO-140 | Issuance of Purchase Order for Interlock Tiles of Landscaping | 7 | 28-Oct-26 | 04-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-150 | Issuance of Purchase Order for Curbstones of Landscaping | 7 | 05-Nov-26 | 12-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 14 | 14-Nov-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-PO-160 | Issuance of Purchase Order for Traffic Signs Boards of Road Works | 7 | 14-Nov-26 | 21-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-PO-170 | Issuance of Purchase Order for Road Markings of Road Works | 7 | 22-Nov-26 | 29-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 115 | 20-Oct-26 | 02-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 90 | 20-Oct-26 | 01-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-MF-100 | Manufacturing of Subgrade for Road Works | 10 | 20-Oct-26 | 31-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-MF-110 | Manufacturing of Aggregate Base Course for Road Works | 20 | 01-Nov-26 | 23-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-MF-120 | Manufacturing of Prime Coat for Road Works | 20 | 24-Nov-26 | 16-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-MF-130 | Manufacturing of Asphaltic Base Course Layer for Road Works | 20 | 17-Dec-26 | 09-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-MF-180 | Manufacturing of Asphaltic Wearing Course Layer for Roads Network | 20 | 10-Jan-27 | 01-Feb-27 | 0 | 0 | 0 | 0 | 85% | 0% |
| PRO-RD-MF-190 | Manufacturing of Tack Coat Layer for Roads Network | 50 | 30-Nov-26 | 26-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Pavement Works** | | 21 | 27-Jan-27 | 20-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-MF-140 | Manufacturing of Interlock Tiles for Landscaping | 21 | 27-Jan-27 | 20-Feb-27 | 0 | 0 | 0 | 0 | 9.52% | 0% |
| PRO-RD-MF-150 | Manufacturing of Curbstones for Landscaping | 20 | 27-Jan-27 | 18-Feb-27 | 0 | 0 | 0 | 0 | 10% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 87 | 22-Nov-26 | 02-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |

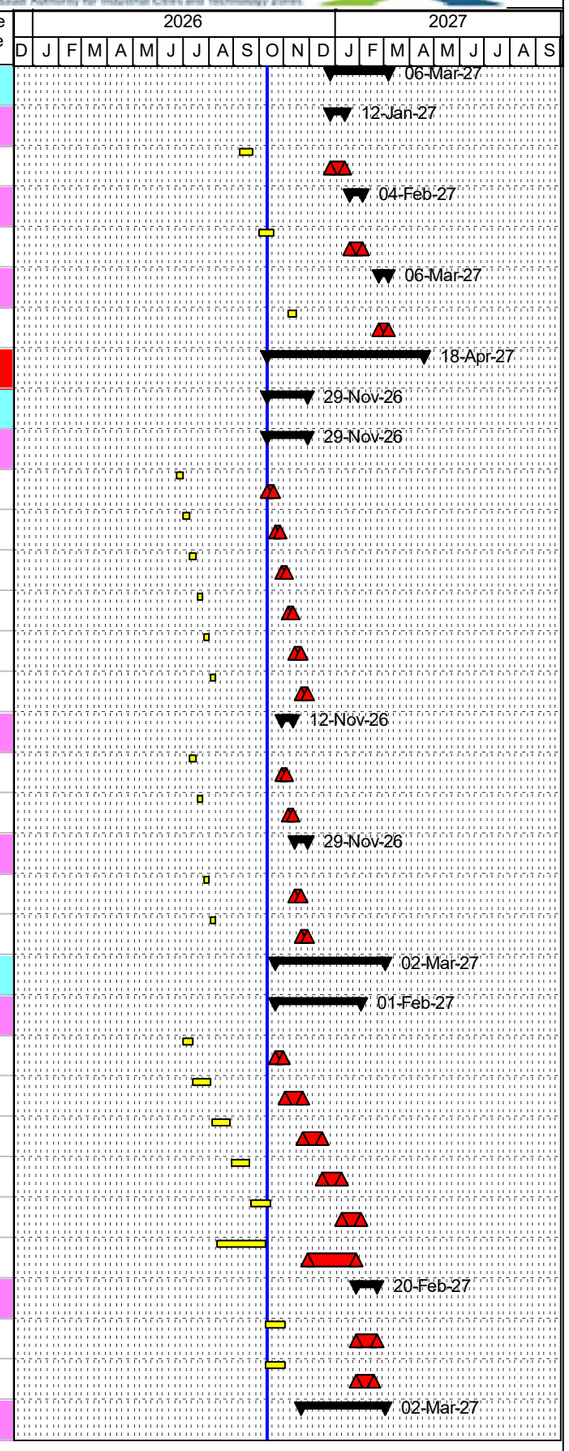



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-RD-MF-160 | Manufacturing of Traffic Signs Boards for Road Works | 80 | 22-Nov-26 | 22-Feb-27 | 0 | 0 | 0 | 0 | 73.75% | 0% |
| PRO-RD-MF-170 | Manufacturing of Road Markings for Road Works | 80 | 30-Nov-26 | 02-Mar-27 | 0 | 0 | 0 | 0 | 65% | 0% |
| **1st Material Delivery & Site Inspection** | | 124 | 01-Nov-26 | 28-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 94 | 01-Nov-26 | 17-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-100 | 1ST Material Delivery for Subgrade of Road Works | 7 | 01-Nov-26 | 08-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-1DL-110 | 1ST Material Delivery for Aggregate Base Course of Road Works | 7 | 24-Nov-26 | 01-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-1DL-120 | 1ST Material Delivery for Prime Coat of Road Works | 15 | 17-Dec-26 | 03-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-1DL-130 | 1ST Material Delivery for Asphaltic Base Course Layer of Road Works | 7 | 10-Jan-27 | 17-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-RD-1DL-180 | 1ST Material Delivery for Asphaltic Wearing Course Layer for Roads Network | 7 | 02-Feb-27 | 09-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-190 | 1ST Material Delivery for Tack Coat Layer for Roads Network | 7 | 10-Feb-27 | 17-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 14 | 21-Feb-27 | 08-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-140 | 1ST Material Delivery for Interlock Tiles of Landscaping | 7 | 21-Feb-27 | 28-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-150 | 1ST Material Delivery for Curbstones of Landscaping | 7 | 01-Mar-27 | 08-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 14 | 13-Mar-27 | 28-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-160 | 1ST Material Delivery for Traffic Signs Boards of Road Works | 7 | 21-Mar-27 | 28-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-1DL-170 | 1ST Material Delivery for Road Markings of Road Works | 7 | 13-Mar-27 | 20-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Delivery & Site Inspection** | | 135 | 09-Nov-26 | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 42 | 09-Nov-26 | 27-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-100 | Material Delivery & Site Inspection for Subgrade of Road Works | 21 | 09-Nov-26 | 02-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-RD-DL-110 | Material Delivery & Site Inspection for Aggregate Base Course of Road Works | 21 | 03-Dec-26 | 27-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Bituminous Construction** | | 54 | 04-Jan-27 | 07-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-160 | Material Delivery & Site Inspection for Prime Coat Layer of Road Works | 11 | 04-Jan-27 | 16-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-R25-RD-DL-170 | Material Delivery & Site Inspection for Asphaltic Base Course Layer of Road Works | 11 | 18-Jan-27 | 30-Jan-27 | 0 | 0 | 0 | 0 | 90.91% | 0% |
| PRO-RD-DL-200 | Material Delivery for Asphaltic Wearing Course Layer for Roads Network | 11 | 10-Feb-27 | 22-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-RD-DL-210 | Material Delivery for Tack Coat Layer for Roads Network | 11 | 23-Feb-27 | 07-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 22 | 08-Mar-27 | 05-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-120 | Material Delivery & Site Inspection of Interlock Tiles for Landscaping | 11 | 08-Mar-27 | 23-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-130 | Material Delivery & Site Inspection of Curbstones for Landscaping | 11 | 24-Mar-27 | 05-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 22 | 24-Mar-27 | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-140 | Material Delivery & Site Inspection of Traffic Signs Boards For Road Works | 11 | 06-Apr-27 | 18-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-RD-DL-150 | Material Delivery & Site Inspection of Road Markings For Road Works | 11 | 24-Mar-27 | 05-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Superstructure Works** | | 53 | 12-Oct-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 11 | 12-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 4 | 12-Oct-26 | 15-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |

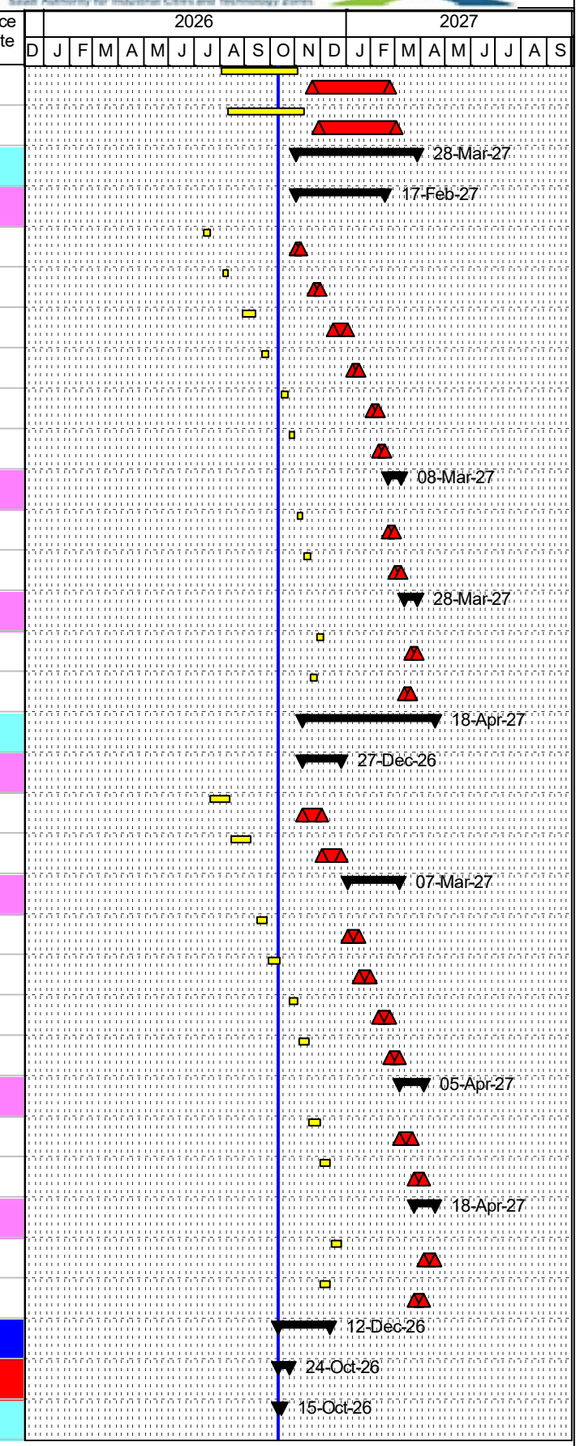



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-LS-CV-PO-20 | Issuance of Purchase Order for Works for Water Pump Station | 4 | 12-Oct-26 | 15-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storage Tank (TSE)** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-PO-30 | Issuance of Purchase Order for Works for Storage Tank (TSE) | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Control Room** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-PO-40 | Issuance of Purchase Order for Works for Control Room | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Sewage Pump Stations** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-CV-PO-10 | Issuance of Purchase Order for Works of Sewage Pump Station | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Gaurd Room** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-GR-CV-PO-40 | Issuance of Purchase Order for Materials for Gaurd Room | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Boundary Fence** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-FE-CV-PO-50 | Issuance of Purchase Order for Materials for Boundary Fence | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 28 | 17-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-CV-MF-30 | Manufacturing of Works for Works for Water Pump Station | 7 | 17-Oct-26 | 24-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storage Tank (TSE)** | | 14 | 25-Oct-26 | 09-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-MF-40 | Manufacturing of Works for Storage Tank (TSE) | 14 | 25-Oct-26 | 09-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Control Room** | | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-MF-50 | Manufacturing of Works for Control Room | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Sewage Pump Stations** | | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-CV-MF-10 | Manufacturing of Works of Sewage Pump Station | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Gaurd Room** | | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-GR-CV-MF-50 | Manufacturing of Materials for Gaurd Room | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Boundary Fence** | | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-FE-CV-MF-60 | Manufacturing of Materials for Boundary Fence | 21 | 25-Oct-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 35 | 17-Oct-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 6 | 17-Oct-26 | 22-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-CV-1DL-40 | 1ST Material Delivery for Works of Water Pump Station | 6 | 17-Oct-26 | 22-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storage Tank (TSE)** | | 7 | 10-Nov-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-1DL-50 | 1ST Material Delivery for Works for Storage Tank (TSE) | 7 | 10-Nov-26 | 17-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Control Room** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-1DL-60 | 1ST Material Delivery for Works for Control Room | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Sewage Pump Stations** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-CV-1DL-10 | 1ST Material Delivery for Works of Sewage Pump Station | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Gaurd Room** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |

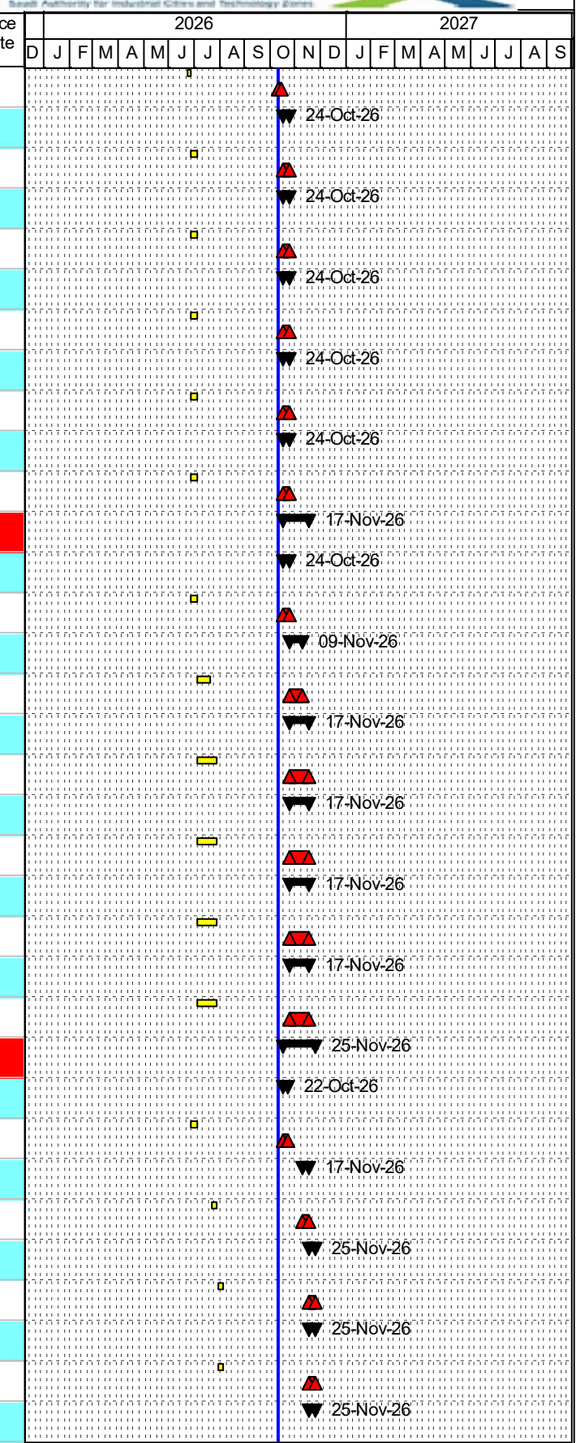



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| PRO-GR-CV-1DL-60 | 1ST Material Delivery for Materials for Gaurd Room | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Boundary Fence** | | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-FE-CV-1DL-70 | 1ST Material Delivery for Materials for Boundary Fence | 7 | 18-Nov-26 | 25-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 49 | 17-Oct-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 10 | 17-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-CV-DL-50 | Material Delivery & Site Inspection for Works for Water Pump Station | 10 | 17-Oct-26 | 27-Oct-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Storage Tank (TSE)** | | 27 | 28-Oct-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-DL-60 | Material Delivery & Site Inspection for Works for Storage Tank (TSE) | 27 | 28-Oct-26 | 28-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Control Room** | | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-CV-DL-70 | Material Delivery & Site Inspection for Works for Control Room | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Sewage Pump Stations** | | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-CV-DL-10 | Material Delivery & Site Inspection for Works for Pump Station | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Gaurd Room** | | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-GR-CV-DL-70 | Material Delivery & Site Inspection for Materials for Gaurd Room | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Boundary Fence** | | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-FE-CV-DL-80 | Material Delivery & Site Inspection for Materials for Boundary Fence | 14 | 26-Nov-26 | 12-Dec-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Softscape and Planting Works** | | 92 | 28-Oct-26 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 12 | 28-Oct-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 12 | 28-Oct-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-PO-140 | Issuance of Purchase Order for Softscape and Planting Works | 6 | 28-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-PO-150 | Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders | 6 | 04-Nov-26 | 10-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 66 | 04-Nov-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 66 | 04-Nov-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-MF-140 | Manufacturing of Softscape and Planting Works | 60 | 04-Nov-26 | 12-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-MF-150 | Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel) | 60 | 11-Nov-26 | 19-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **1st Material Delivery & Site Inspection** | | 12 | 13-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 12 | 13-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-IR-1DL-140 | 1ST Material Delivery for Softscape and Planting Works | 6 | 13-Jan-27 | 19-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| PRO-IR-1DL-150 | 1ST Material Delivery for Site Furnishings (Seating Bench,Stone Boulders and Gravel) | 6 | 20-Jan-27 | 26-Jan-27 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Material Delivery & Site Inspection** | | 20 | 20-Jan-27 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 20 | 20-Jan-27 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-R25-IR-DL-140 | Material Delivery & Site Inspection of Softscape and Planting Works | 10 | 20-Jan-27 | 31-Jan-27 | 0 | 0 | 0 | 0 | 80% | 0% |
| PRO-R25-IR-DL-150 | Material Delivery & Site Inspection of Site Furnishings (Seating Bench,Stone Boulders | 10 | 01-Feb-27 | 11-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Long Lead Time Items** | | 182 | 28-Oct-26 | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |

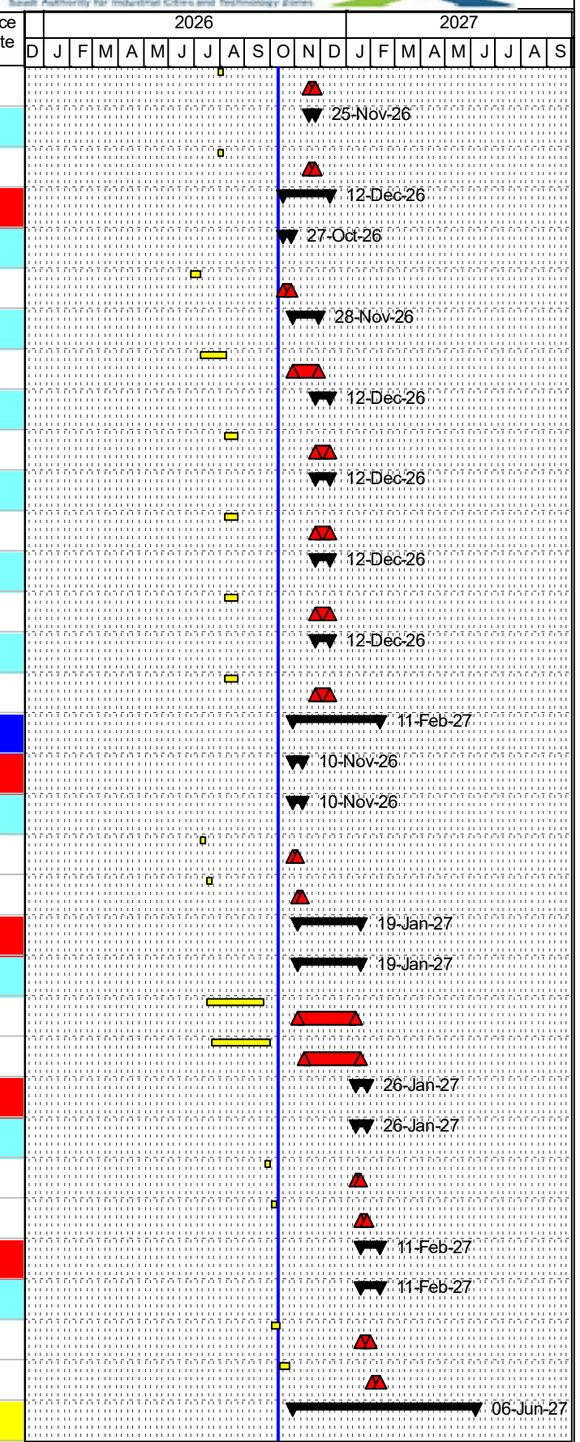



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Superstructure Works** | | 182 | 28-Oct-26 | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Pump Station** | | 149 | 28-Oct-26 | 22-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 6 | 28-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-LL-PO-10 | Issuance of Purchase Order for Electromechanical Works for Pump Station | 6 | 28-Oct-26 | 03-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 100 | 04-Nov-26 | 28-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-LL-MF-10 | Manufacturing of Electromechanical Works for Pump Station | 100 | 04-Nov-26 | 28-Feb-27 | 0 | 0 | 0 | 0 | 74% | 0% |
| **Material Shipping/Custom Clearance/Delivery** | | 21 | 01-Mar-27 | 28-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-LL-SH/DL-10 | Material Delivery for Electromechanical Works for Pump Station | 21 | 01-Mar-27 | 28-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Site Inspection** | | 22 | 29-Mar-27 | 22-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-SPS-LL-MSI-10 | Material Site Inspection for Electromechanical Works for Pump Station | 22 | 29-Mar-27 | 22-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Water Pump Station** | | 119 | 04-Nov-26 | 25-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 7 | 04-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-LL-PO-20 | Issuance of Purchase Order for Electromechanical Works for Water Pump | 7 | 04-Nov-26 | 11-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 70 | 12-Nov-26 | 01-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-LL-MF-20 | Manufacturing of Electromechanical Works for Water Pump Station | 70 | 12-Nov-26 | 01-Feb-27 | 0 | 0 | 0 | 0 | 95.71% | 0% |
| **Material Shipping/Custom Clearance/Delivery** | | 21 | 02-Feb-27 | 25-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-LL-SH/DL-20 | Material Delivery for Electromechanical Works for Water Pump Station | 21 | 02-Feb-27 | 25-Feb-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Site Inspection** | | 21 | 27-Feb-27 | 25-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-LS-LL-MSI-20 | Material Site Inspection for Electromechanical Works for Water Pump Station | 21 | 27-Feb-27 | 25-Mar-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storage Tank (TSE)** | | 169 | 12-Nov-26 | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Issuance of Purchase Orders** | | 7 | 12-Nov-26 | 19-Nov-26 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-LL-PO-30 | Issuance of Purchase Order for Electromechanical Works for Storage Tank | 7 | 12-Nov-26 | 19-Nov-26 | 0 | 0 | 0 | 0 | 100% | 0% |
| **Manufacturing of Material** | | 120 | 21-Nov-26 | 12-Apr-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-LL-MF-30 | Manufacturing of Electromechanical Works for Storage Tank (TSE) | 120 | 21-Nov-26 | 12-Apr-27 | 0 | 0 | 0 | 0 | 50% | 0% |
| **Material Shipping/Custom Clearance/Delivery** | | 21 | 13-Apr-27 | 06-May-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-LL-SH/DL-30 | Material Delivery for Electromechanical Works for Storage Tank (TSE) | 21 | 13-Apr-27 | 06-May-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Material Site Inspection** | | 21 | 08-May-27 | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| PRO-TSE-LL-MSI-30 | Material Site Inspection for Electromechanical Works for Storage Tank (TSE) | 21 | 08-May-27 | 06-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Construction Works** | | 376 | 10-Mar-26 A | 09-Jun-27 | 93,388,698 | 31,926,434 | 22,116,233 | 19,232,277 | 34.19% | 23.68% |
| **Infrastructure Networks** | | 374 | 10-Mar-26 A | 07-Jun-27 | 57,696,530 | 29,804,234 | 13,535,825 | 10,701,773 | 51.66% | 23.46% |
| **Internal** | | 374 | 10-Mar-26 A | 07-Jun-27 | 32,508,953 | 16,471,322 | 3,055,456 | 3,055,656 | 50.67% | 9.4% |
| **Alignment-RD-01** | | 357 | 10-Mar-26 A | 12-May-27 | 15,199,337 | 8,113,094 | 3,055,456 | 3,055,656 | 53.38% | 20.1% |
| **Earthworks** | | 222 | 10-Mar-26 A | 23-Dec-26 | 4,697,995 | 4,697,995 | 3,055,456 | 3,055,656 | 100% | 65.04% |
| **Earthworks** | | 222 | 10-Mar-26 A | 23-Dec-26 | 4,697,995 | 4,697,995 | 3,055,456 | 3,055,656 | 100% | 65.04% |

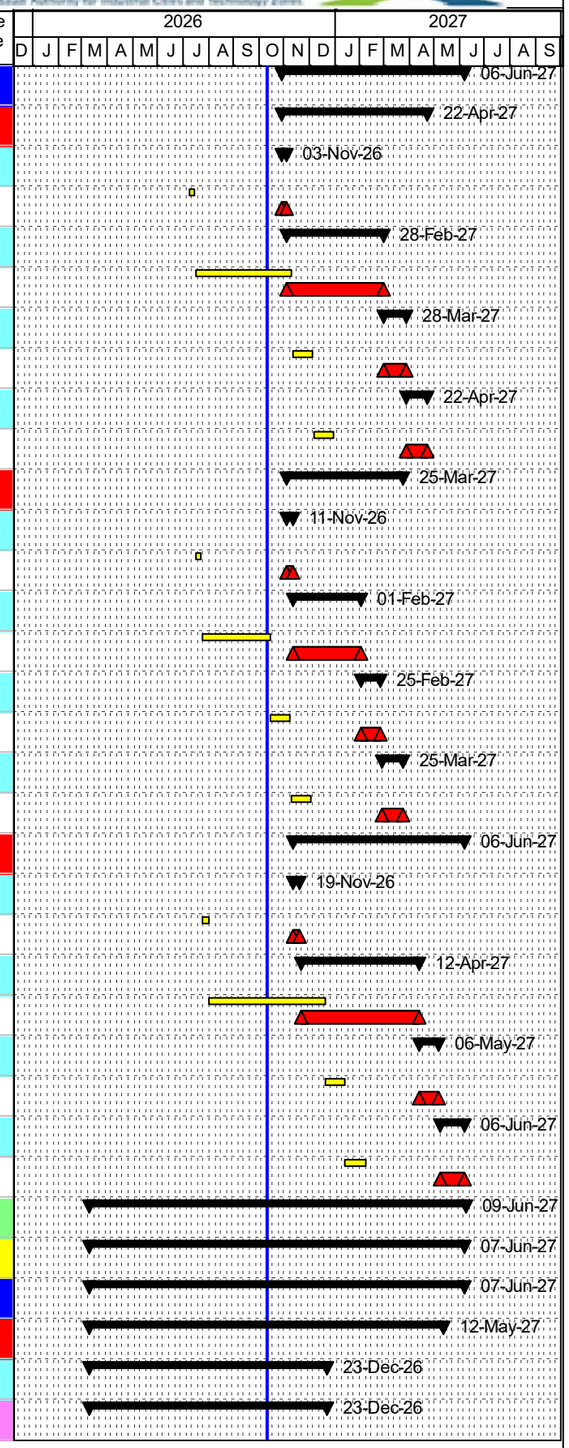



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-EW-210 | Excavation and Backfilling Works Upto Design Level for Earthworks for | 81 | 10-Mar-26 A | 22-Jun-26 A | 379,596 | 379,596 | 379,596 | 379,596 | 100% | 100% |
| CO-EW-210_R | Excavation and Backfilling Works Upto Design Level for Earthworks for | 20 | 01-Jul-26 A | 15-Jul-26 A | 1,772,616 | 1,772,616 | 1,772,616 | 1,772,616 | 100% | 100% |
| CO-EW-210_R01 | Excavation and Backfilling Works Upto Design Level for Earthworks for | 20 | 31-Aug-26 A | 23-Dec-26 | 2,545,782 | 2,545,782 | 903,244 | 903,443 | 100% | 35.48% |
| **Storm Drainage Network** | | 61 | 12-Oct-26 | 21-Dec-26 | 2,292,989 | 2,292,989 | 0 | 0 | 100% | 0% |
| **Manholes** | | 41 | 12-Oct-26 | 28-Nov-26 | 340,545 | 340,545 | 0 | 0 | 100% | 0% |
| CO-SD-MH-230 | Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for | 12 | 12-Oct-26 | 25-Oct-26 | 22,703 | 22,703 | 0 | 0 | 100% | 0% |
| CO-SD-MH-240 | Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-01 | 9 | 29-Oct-26 | 08-Nov-26 | 113,515 | 113,515 | 0 | 0 | 100% | 0% |
| CO-SD-MH-250 | Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for | 7 | 09-Nov-26 | 16-Nov-26 | 136,218 | 136,218 | 0 | 0 | 100% | 0% |
| CO-SD-MH-260 | Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-01 | 10 | 17-Nov-26 | 28-Nov-26 | 68,109 | 68,109 | 0 | 0 | 100% | 0% |
| **Main Line Sections** | | 23 | 09-Nov-26 | 05-Dec-26 | 1,523,566 | 1,523,566 | 0 | 0 | 100% | 0% |
| CO-SD-ML-140 | Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for | 8 | 09-Nov-26 | 17-Nov-26 | 209,385 | 209,385 | 0 | 0 | 100% | 0% |
| CO-SD-ML-150 | Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-01 | 8 | 17-Nov-26 | 25-Nov-26 | 933,291 | 933,291 | 0 | 0 | 100% | 0% |
| CO-SD-ML-160 | Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for | 8 | 26-Nov-26 | 05-Dec-26 | 380,890 | 380,890 | 0 | 0 | 100% | 0% |
| **Catch Basin Sections** | | 22 | 26-Nov-26 | 21-Dec-26 | 428,877 | 428,877 | 0 | 0 | 100% | 0% |
| CO-SD-CB-180 | Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for | 8 | 26-Nov-26 | 05-Dec-26 | 107,219 | 107,219 | 0 | 0 | 100% | 0% |
| CO-SD-CB-190 | Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage | 7 | 06-Dec-26 | 13-Dec-26 | 250,178 | 250,178 | 0 | 0 | 100% | 0% |
| CO-SD-CB-200 | Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for | 7 | 14-Dec-26 | 21-Dec-26 | 71,479 | 71,479 | 0 | 0 | 100% | 0% |
| **Sewage Network** | | 60 | 06-Dec-26 | 13-Feb-27 | 801,144 | 605,264 | 0 | 0 | 75.55% | 0% |
| **Manholes** | | 60 | 06-Dec-26 | 13-Feb-27 | 264,213 | 202,563 | 0 | 0 | 76.67% | 0% |
| CO-SW-MH-210 | Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-01 | 12 | 06-Dec-26 | 19-Dec-26 | 17,614 | 17,614 | 0 | 0 | 100% | 0% |
| CO-SW-MH-220 | Installation RC Footing Works for Main Line Manholes of Sewage Network for | 12 | 20-Dec-26 | 02-Jan-27 | 88,071 | 88,071 | 0 | 0 | 100% | 0% |
| CO-SW-MH-230 | Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for | 12 | 03-Jan-27 | 16-Jan-27 | 52,843 | 52,843 | 0 | 0 | 100% | 0% |
| CO-SW-MH-240 | Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for | 12 | 17-Jan-27 | 30-Jan-27 | 52,843 | 44,036 | 0 | 0 | 83.33% | 0% |
| CO-SW-MH-250 | Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-01 | 12 | 31-Jan-27 | 13-Feb-27 | 52,843 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 46 | 22-Dec-26 | 13-Feb-27 | 536,930 | 402,701 | 0 | 0 | 75% | 0% |
| CO-SW-ML-140 | Trench Excavation and Bedding Works for Main Lines of Sewage Network for | 8 | 22-Dec-26 | 30-Dec-26 | 79,139 | 79,139 | 0 | 0 | 100% | 0% |
| CO-SW-ML-150 | Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-01 | 8 | 31-Dec-26 | 09-Jan-27 | 323,562 | 323,562 | 0 | 0 | 100% | 0% |
| CO-SW-ML-160 | Trench Backfilling and Compaction Works for Main Lines of Sewage Network for | 6 | 07-Feb-27 | 13-Feb-27 | 134,230 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 42 | 29-Nov-26 | 16-Jan-27 | 94,795 | 94,795 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-200 | Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse) | 7 | 29-Nov-26 | 06-Dec-26 | 11,940 | 11,940 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-210 | Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-01 | 17 | 12-Dec-26 | 30-Dec-26 | 59,156 | 59,156 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-230 | Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for | 14 | 31-Dec-26 | 16-Jan-27 | 23,699 | 23,699 | 0 | 0 | 100% | 0% |
| **Potable Water Network** | | 32 | 29-Nov-26 | 04-Jan-27 | 373,599 | 373,599 | 0 | 0 | 100% | 0% |
| **Main Line Sections** | | 32 | 29-Nov-26 | 04-Jan-27 | 248,155 | 248,155 | 0 | 0 | 100% | 0% |

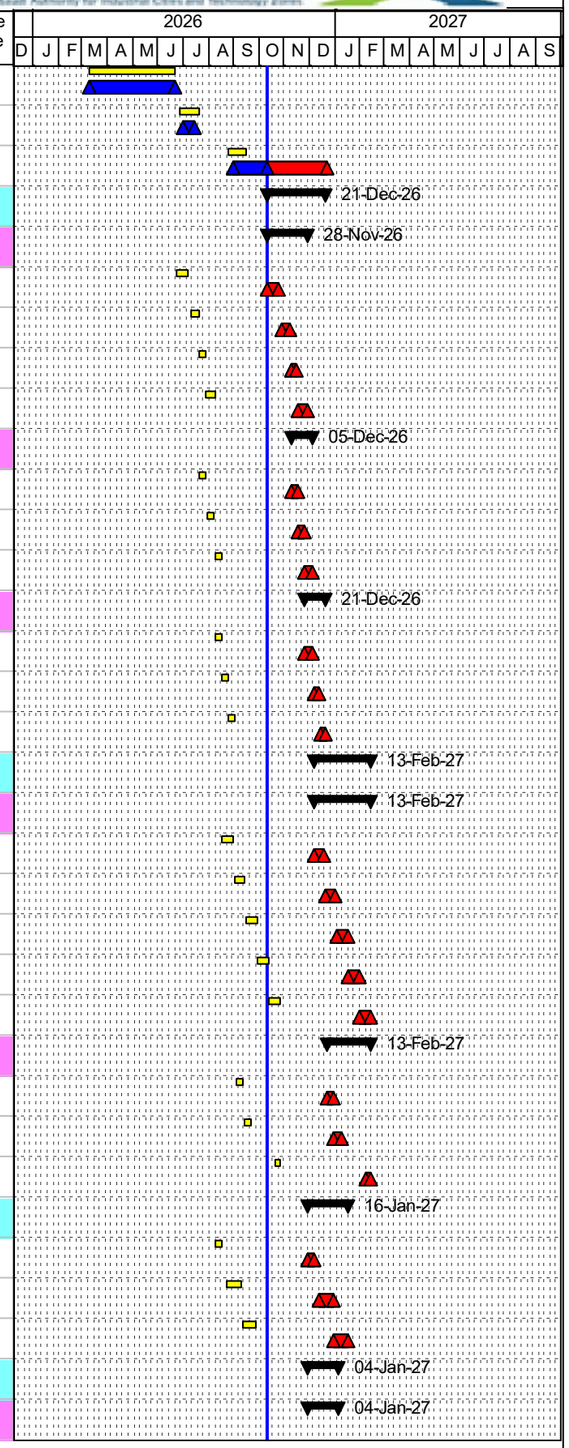



Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-PW-ML-140 | Trench Excavation and Bedding Works for Main Lines of Potable Water Network for | 6 | 29-Nov-26 | 05-Dec-26 | 45,473 | 45,473 | 0 | 0 | 100% | 0% |
| CO-PW-ML-150 | Pipes Laying and accessories for Main Lines of Potable Water Network for | 6 | 22-Dec-26 | 28-Dec-26 | 112,515 | 112,515 | 0 | 0 | 100% | 0% |
| CO-PW-ML-160 | Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for | 6 | 29-Dec-26 | 04-Jan-27 | 90,167 | 90,167 | 0 | 0 | 100% | 0% |
| **Valve Chamber** | | 30 | 01-Dec-26 | 04-Jan-27 | 62,485 | 62,485 | 0 | 0 | 100% | 0% |
| CO-PW-VC-230 | Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for | 4 | 01-Dec-26 | 05-Dec-26 | 3,905 | 3,905 | 0 | 0 | 100% | 0% |
| CO-PW-VC-240 | Installation Works for Valves of Potable Water Network for Alignment-RD-01 | 4 | 10-Dec-26 | 14-Dec-26 | 10,154 | 10,154 | 0 | 0 | 100% | 0% |
| CO-PW-VC-250 | Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for | 4 | 31-Dec-26 | 04-Jan-27 | 7,811 | 7,811 | 0 | 0 | 100% | 0% |
| CO-PW-VC190 | Installation of Valve Chambers of Potable Water Network for Alignment-RD-01 | 4 | 06-Dec-26 | 09-Dec-26 | 40,615 | 40,615 | 0 | 0 | 100% | 0% |
| **Fire Hydrant** | | 26 | 06-Dec-26 | 04-Jan-27 | 62,959 | 62,959 | 0 | 0 | 100% | 0% |
| CO-PW-FH-170 | Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-01 | 15 | 06-Dec-26 | 22-Dec-26 | 3,935 | 3,935 | 0 | 0 | 100% | 0% |
| CO-PW-FH-180 | Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-01 | 3 | 29-Dec-26 | 31-Dec-26 | 51,154 | 51,154 | 0 | 0 | 100% | 0% |
| CO-PW-FH-190 | Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for | 3 | 02-Jan-27 | 04-Jan-27 | 7,870 | 7,870 | 0 | 0 | 100% | 0% |
| **Irrigation Network** | | 36 | 17-Jan-27 | 27-Feb-27 | 601,521 | 48,452 | 0 | 0 | 8.05% | 0% |
| **Main Line Pipes** | | 36 | 17-Jan-27 | 27-Feb-27 | 601,521 | 48,452 | 0 | 0 | 8.05% | 0% |
| CO-IR-ML-150 | Trench Excavation and Bedding Works for Main Lines of Irrigation Network for | 7 | 17-Jan-27 | 24-Jan-27 | 13,844 | 13,844 | 0 | 0 | 100% | 0% |
| CO-IR-ML-160 | Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-01 | 8 | 25-Jan-27 | 02-Feb-27 | 69,218 | 34,609 | 0 | 0 | 50% | 0% |
| CO-IR-ML-170 | Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-01 | 7 | 03-Feb-27 | 10-Feb-27 | 21,302 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-180 | Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for | 4 | 23-Feb-27 | 27-Feb-27 | 27,687 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-190 | Installation Works for Bulbblers And Sprinklers and Irrigation Control System of Irrigation | 10 | 11-Feb-27 | 22-Feb-27 | 469,471 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 18 | 14-Feb-27 | 06-Mar-27 | 153,221 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 18 | 14-Feb-27 | 06-Mar-27 | 153,221 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-280 | Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-01 | 6 | 14-Feb-27 | 20-Feb-27 | 29,351 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-290 | Duct Laying Works for Medium Voltage Network for Alignment-RD-01 | 6 | 21-Feb-27 | 27-Feb-27 | 85,162 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-300 | Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-01 | 6 | 28-Feb-27 | 06-Mar-27 | 38,709 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 25 | 07-Mar-27 | 07-Apr-27 | 158,103 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works ( Cable 300 MM )** | | 18 | 07-Mar-27 | 30-Mar-27 | 81,711 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-130 | Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for | 6 | 07-Mar-27 | 16-Mar-27 | 15,956 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-140 | Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-01 | 6 | 17-Mar-27 | 23-Mar-27 | 45,209 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-150 | Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for | 6 | 24-Mar-27 | 30-Mar-27 | 20,546 | 0 | 0 | 0 | 0% | 0% |
| **Service Low Voltage Cables Works ( Cable 70 MM )** | | 19 | 17-Mar-27 | 07-Apr-27 | 73,733 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-130 | Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for | 6 | 17-Mar-27 | 23-Mar-27 | 7,978 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-140 | Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-01 | 7 | 24-Mar-27 | 31-Mar-27 | 45,209 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-150 | Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for | 6 | 01-Apr-27 | 07-Apr-27 | 20,546 | 0 | 0 | 0 | 0% | 0% |
| **Distribution Pillars Works** | | 7 | 17-Mar-27 | 24-Mar-27 | 2,659 | 0 | 0 | 0 | 0% | 0% |

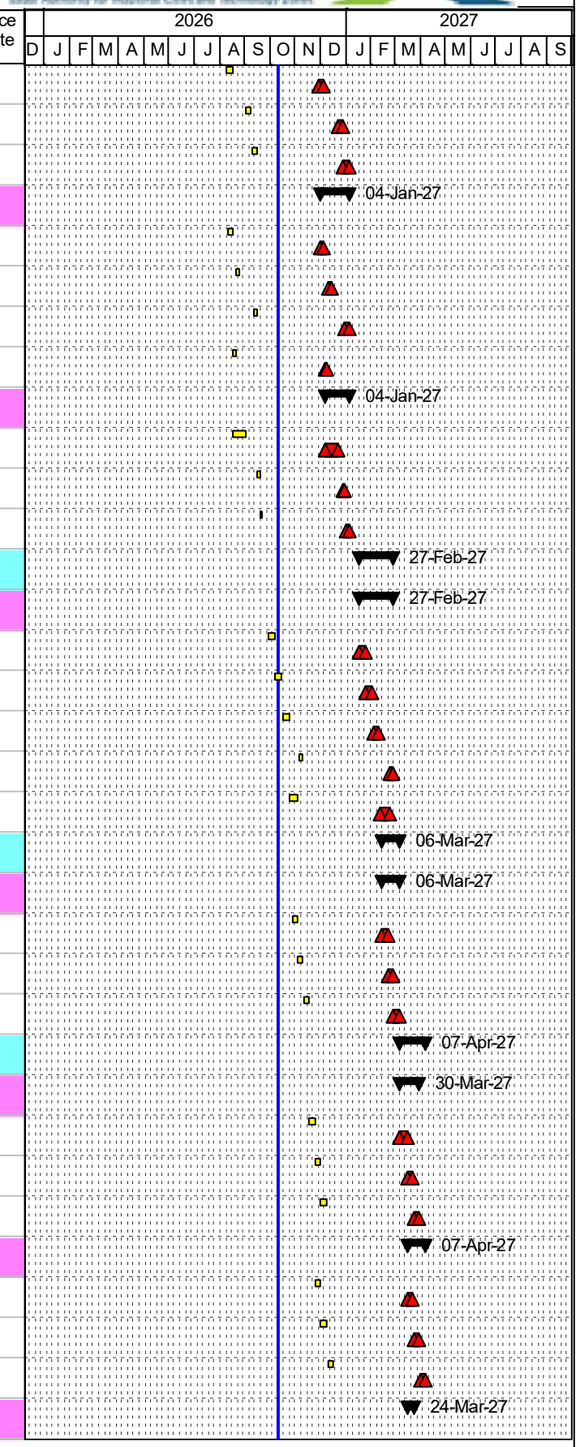



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CON-LV-DP-130 | Foundation Excavation Works for Distribution Pillars of Low Voltage Network for | 7 | 17-Mar-27 | 24-Mar-27 | 2,659 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 23 | 21-Feb-27 | 22-Mar-27 | 80,615 | 0 | 0 | 0 | 0% | 0% |
| **Lighting Poles Works** | | 19 | 21-Feb-27 | 17-Mar-27 | 33,194 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-350 | Installation Works for Lighting Poles Foundation of Street Lighting Network for | 8 | 21-Feb-27 | 01-Mar-27 | 7,113 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-360 | Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-01 | 5 | 02-Mar-27 | 07-Mar-27 | 23,710 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-380 | Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-01 | 6 | 08-Mar-27 | 17-Mar-27 | 2,371 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 10 | 08-Mar-27 | 22-Mar-27 | 47,420 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-290 | Cable Laying Works for Street Lighting Network for Alignment-RD-01 | 5 | 08-Mar-27 | 16-Mar-27 | 26,081 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-300 | Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-01 | 5 | 17-Mar-27 | 22-Mar-27 | 21,339 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 21 | 23-Mar-27 | 15-Apr-27 | 1,517,343 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 7 | 08-Apr-27 | 15-Apr-27 | 94,908 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-150 | Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-01 | 4 | 08-Apr-27 | 12-Apr-27 | 65,249 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-160 | Trench Backfilling and Compaction Works for Ducts of Telecom Network for | 3 | 13-Apr-27 | 15-Apr-27 | 29,659 | 0 | 0 | 0 | 0% | 0% |
| **Manholes Works** | | 8 | 23-Mar-27 | 31-Mar-27 | 36,239 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-170 | Excavation Works for Manholes of Telecom Network for Alignment-RD-01 | 4 | 23-Mar-27 | 27-Mar-27 | 2,416 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-180 | Installation Works for Manholes of Telecom Network for Alignment-RD-01 | 4 | 23-Mar-27 | 27-Mar-27 | 26,575 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-190 | Backfilling Works for Manholes of Telecom Network for Alignment-RD-01 | 4 | 28-Mar-27 | 31-Mar-27 | 7,248 | 0 | 0 | 0 | 0% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 8 | 01-Apr-27 | 10-Apr-27 | 1,386,196 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-150 | Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-01 | 8 | 01-Apr-27 | 10-Apr-27 | 1,386,196 | 0 | 0 | 0 | 0% | 0% |
| **Road Network** | | 10 | 17-Apr-27 | 27-Apr-27 | 2,662,858 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 10 | 17-Apr-27 | 27-Apr-27 | 2,607,263 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-180 | Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-01 | 10 | 17-Apr-27 | 27-Apr-27 | 263,715 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-190 | Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-01 | 10 | 17-Apr-27 | 27-Apr-27 | 2,343,548 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 8 | 17-Apr-27 | 25-Apr-27 | 55,595 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-190 | Application of Road Marking Works For Road Works for Alignment-RD-01 | 4 | 17-Apr-27 | 20-Apr-27 | 35,713 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-130 | Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-01 | 4 | 21-Apr-27 | 25-Apr-27 | 19,882 | 0 | 0 | 0 | 0% | 0% |
| **Finishes for Infrastructure Networks** | | 55 | 07-Mar-27 | 12-May-27 | 1,765,154 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 23 | 17-Apr-27 | 12-May-27 | 780,323 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 23 | 17-Apr-27 | 12-May-27 | 780,323 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-170 | Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-01 | 7 | 28-Apr-27 | 05-May-27 | 71,479 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-180 | Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for | 6 | 06-May-27 | 12-May-27 | 107,219 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-190 | Catch Basin Internal Finishes (Benching ) for Storm Drainage Network for Alignment-RD-01 | 6 | 17-Apr-27 | 22-Apr-27 | 107,219 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-MH-TF-230 | Testing Works for Manholes of Storm Drainage Network for Alignment-RD-01 | 2 | 26-Apr-27 | 27-Apr-27 | 113,515 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-ML-TF-110 | Testing Work for Pipes of Storm Drainage Network for Alignment-RD-01 | 2 | 24-Apr-27 | 25-Apr-27 | 380,890 | 0 | 0 | 0 | 0% | 0% |

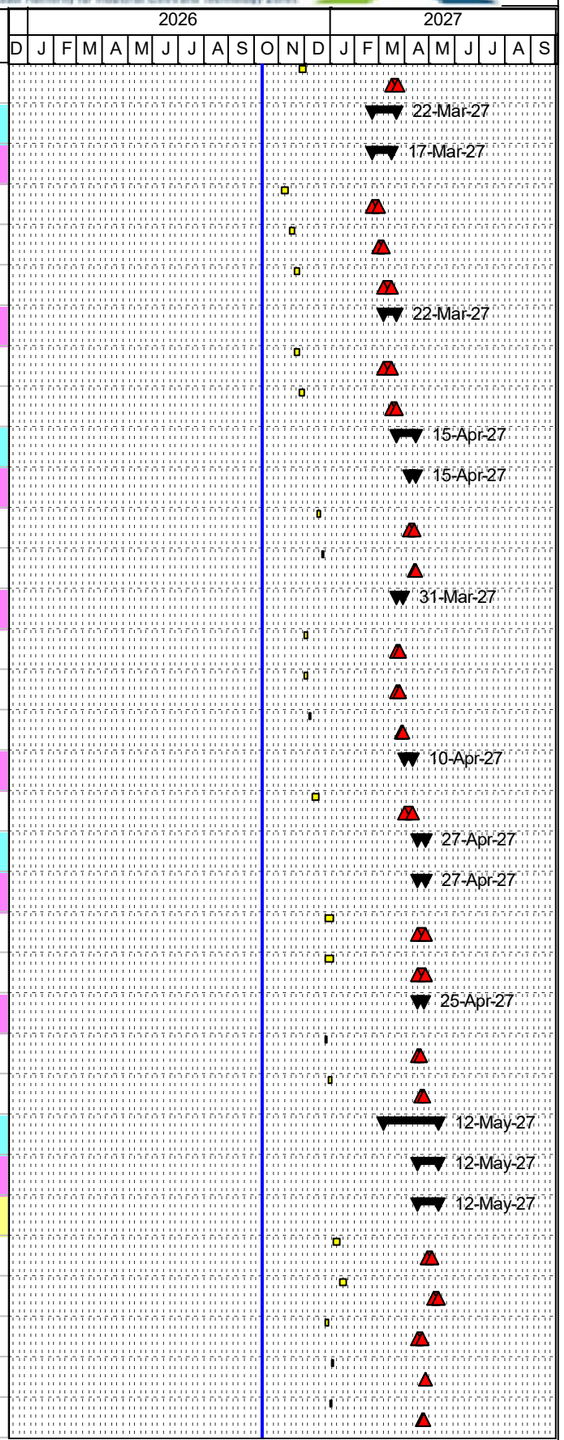



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Sewage Network** | | 7 | 17-Apr-27 | 24-Apr-27 | 222,301 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 7 | 17-Apr-27 | 24-Apr-27 | 222,301 | 0 | 0 | 0 | 0% | 0% |
| CO-SW-TF-230 | Final Testing For Main Line of Sewage Network for Alignment-RD-01 | 4 | 20-Apr-27 | 24-Apr-27 | 134,230 | 0 | 0 | 0 | 0% | 0% |
| CO-SW-TF-250 | Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-01 | 3 | 17-Apr-27 | 19-Apr-27 | 88,071 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 8 | 17-Apr-27 | 25-Apr-27 | 234,043 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 8 | 17-Apr-27 | 25-Apr-27 | 234,043 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-140 | Fire Hydrant Finishies (S.Box + Safety + Marker Post ) of Potable Water Network for | 4 | 17-Apr-27 | 20-Apr-27 | 15,740 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-150 | Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-01 | 2 | 21-Apr-27 | 22-Apr-27 | 128,136 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-220 | Testing of Potable Water Network for Alignment-RD-01 | 2 | 24-Apr-27 | 25-Apr-27 | 90,167 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 2 | 26-Apr-27 | 27-Apr-27 | 27,687 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 2 | 26-Apr-27 | 27-Apr-27 | 27,687 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-TF-170 | Final Testing (pressure tests) of Irrigation Network for Alignment-RD-01 | 2 | 26-Apr-27 | 27-Apr-27 | 27,687 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 2 | 26-Apr-27 | 27-Apr-27 | 23,699 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 2 | 26-Apr-27 | 27-Apr-27 | 23,699 | 0 | 0 | 0 | 0% | 0% |
| CO-TSE-TF-210 | Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-01 | 2 | 26-Apr-27 | 27-Apr-27 | 23,699 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 2 | 07-Mar-27 | 08-Mar-27 | 30,971 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 2 | 07-Mar-27 | 08-Mar-27 | 30,971 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-TF-230 | Testing and Termination Works of Medium Voltage Network for Alignment-RD-01 | 2 | 07-Mar-27 | 08-Mar-27 | 30,971 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 4 | 08-Apr-27 | 12-Apr-27 | 32,877 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 4 | 08-Apr-27 | 12-Apr-27 | 32,877 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-120 | Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage | 4 | 08-Apr-27 | 12-Apr-27 | 32,877 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 23 | 23-Mar-27 | 18-Apr-27 | 30,897 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 23 | 23-Mar-27 | 18-Apr-27 | 27,118 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-370 | Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for | 6 | 23-Mar-27 | 29-Mar-27 | 12,892 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-410 | Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-01 | 3 | 15-Apr-27 | 18-Apr-27 | 14,226 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 5 | 10-Apr-27 | 14-Apr-27 | 3,779 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-240 | Install Earthing System Works for Lighting Poles of Street Lighting Network for | 3 | 10-Apr-27 | 12-Apr-27 | 1,890 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-250 | Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for | 2 | 13-Apr-27 | 14-Apr-27 | 1,890 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 6 | 17-Apr-27 | 22-Apr-27 | 382,356 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 17-Apr-27 | 22-Apr-27 | 382,356 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-180 | Testing and Interface modules with Telecom for Alignment-RD-01 | 3 | 17-Apr-27 | 19-Apr-27 | 35,807 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-310 | Testing and Interface modules with CCTV, Telephone, MSN and Access Control for | 3 | 20-Apr-27 | 22-Apr-27 | 346,549 | 0 | 0 | 0 | 0% | 0% |
| **Alignment-RD-02** | | 174 | 08-Nov-26 | 07-Jun-27 | 7,655,882 | 3,830,987 | 0 | 0 | 50.04% | 0% |
| **Earthworks** | | 12 | 08-Nov-26 | 21-Nov-26 | 2,314,449 | 2,314,449 | 0 | 0 | 100% | 0% |

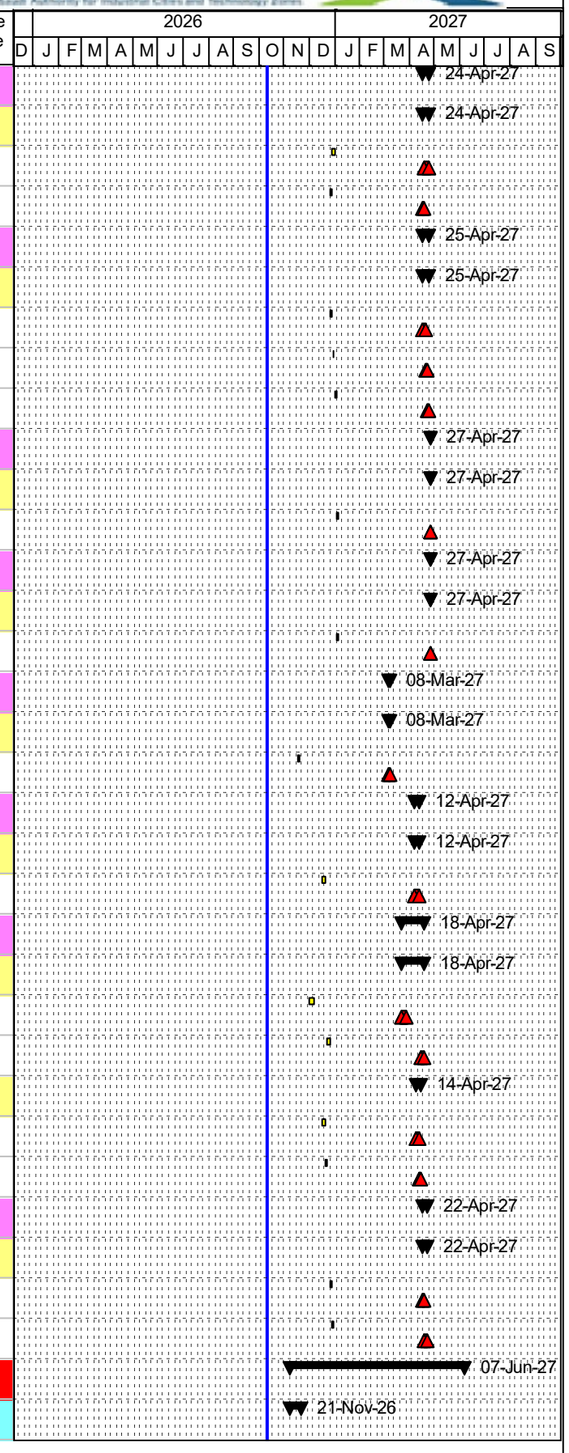



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Earthworks** | | 12 | 08-Nov-26 | 21-Nov-26 | 2,314,449 | 2,314,449 | 0 | 0 | 100% | 0% |
| CO-EW-220 | Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-02 | 12 | 08-Nov-26 | 21-Nov-26 | 2,314,449 | 2,314,449 | 0 | 0 | 100% | 0% |
| **Storm Drainage Network** | | 93 | 22-Nov-26 | 13-Mar-27 | 1,062,822 | 1,028,976 | 0 | 0 | 96.82% | 0% |
| **Manholes** | | 13 | 22-Nov-26 | 06-Dec-26 | 114,795 | 114,795 | 0 | 0 | 100% | 0% |
| CO-SD-MH-270 | Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for | 4 | 22-Nov-26 | 25-Nov-26 | 7,653 | 7,653 | 0 | 0 | 100% | 0% |
| CO-SD-MH-280 | Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-02 | 3 | 26-Nov-26 | 29-Nov-26 | 38,265 | 38,265 | 0 | 0 | 100% | 0% |
| CO-SD-MH-290 | Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for | 3 | 30-Nov-26 | 02-Dec-26 | 45,918 | 45,918 | 0 | 0 | 100% | 0% |
| CO-SD-MH-300 | Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-02 | 3 | 03-Dec-26 | 06-Dec-26 | 22,959 | 22,959 | 0 | 0 | 100% | 0% |
| **Main Line Sections** | | 9 | 03-Dec-26 | 13-Dec-26 | 744,950 | 744,950 | 0 | 0 | 100% | 0% |
| CO-SD-ML-170 | Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for | 3 | 03-Dec-26 | 06-Dec-26 | 106,954 | 106,954 | 0 | 0 | 100% | 0% |
| CO-SD-ML-180 | Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-02 | 3 | 07-Dec-26 | 09-Dec-26 | 451,755 | 451,755 | 0 | 0 | 100% | 0% |
| CO-SD-ML-190 | Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for | 3 | 10-Dec-26 | 13-Dec-26 | 186,241 | 186,241 | 0 | 0 | 100% | 0% |
| **Catch Basin Sections** | | 74 | 14-Dec-26 | 13-Mar-27 | 203,078 | 169,231 | 0 | 0 | 83.33% | 0% |
| CO-SD-CB-210 | Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for | 18 | 14-Dec-26 | 03-Jan-27 | 50,769 | 50,769 | 0 | 0 | 100% | 0% |
| CO-SD-CB-220 | Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage | 19 | 04-Jan-27 | 25-Jan-27 | 118,462 | 118,462 | 0 | 0 | 100% | 0% |
| CO-SD-CB-230 | Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for | 5 | 04-Mar-27 | 13-Mar-27 | 33,846 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Network** | | 58 | 14-Dec-26 | 18-Feb-27 | 276,597 | 202,710 | 0 | 0 | 73.29% | 0% |
| **Manholes** | | 58 | 14-Dec-26 | 18-Feb-27 | 94,811 | 66,368 | 0 | 0 | 70% | 0% |
| CO-SW-MH-260 | Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-02 | 11 | 14-Dec-26 | 26-Dec-26 | 6,321 | 6,321 | 0 | 0 | 100% | 0% |
| CO-SW-MH-270 | Installation RC Footing Works for Main Line Manholes of Sewage Network for | 11 | 27-Dec-26 | 07-Jan-27 | 31,604 | 31,604 | 0 | 0 | 100% | 0% |
| CO-SW-MH-280 | Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for | 12 | 09-Jan-27 | 21-Jan-27 | 18,962 | 18,962 | 0 | 0 | 100% | 0% |
| CO-SW-MH-290 | Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for | 12 | 23-Jan-27 | 04-Feb-27 | 18,962 | 9,481 | 0 | 0 | 25% | 0% |
| CO-SW-MH-300 | Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-02 | 12 | 06-Feb-27 | 18-Feb-27 | 18,962 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 58 | 14-Dec-26 | 18-Feb-27 | 181,786 | 136,343 | 0 | 0 | 75% | 0% |
| CO-SW-ML-170 | Trench Excavation and Bedding Works for Main Lines of Sewage Network for | 11 | 14-Dec-26 | 26-Dec-26 | 28,571 | 28,571 | 0 | 0 | 100% | 0% |
| CO-SW-ML-180 | Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-02 | 11 | 27-Dec-26 | 07-Jan-27 | 107,771 | 107,771 | 0 | 0 | 100% | 0% |
| CO-SW-ML-190 | Trench Backfilling and Compaction Works for Main Lines of Sewage Network for | 11 | 07-Feb-27 | 18-Feb-27 | 45,443 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 41 | 14-Dec-26 | 30-Jan-27 | 310,747 | 284,852 | 0 | 0 | 91.67% | 0% |
| CO-TSE-ML-250 | Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse) | 12 | 14-Dec-26 | 27-Dec-26 | 38,990 | 38,990 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-260 | Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-02 | 17 | 28-Dec-26 | 16-Jan-27 | 194,070 | 194,070 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-280 | Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for | 12 | 17-Jan-27 | 30-Jan-27 | 77,686 | 51,791 | 0 | 0 | 66.67% | 0% |
| **Potable Water Network** | | 18 | 31-Jan-27 | 20-Feb-27 | 232,618 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Sections** | | 17 | 31-Jan-27 | 18-Feb-27 | 77,824 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-ML-170 | Trench Excavation and Bedding Works for Main Lines of Potable Water Network for | 5 | 31-Jan-27 | 04-Feb-27 | 14,191 | 0 | 0 | 0 | 0% | 0% |

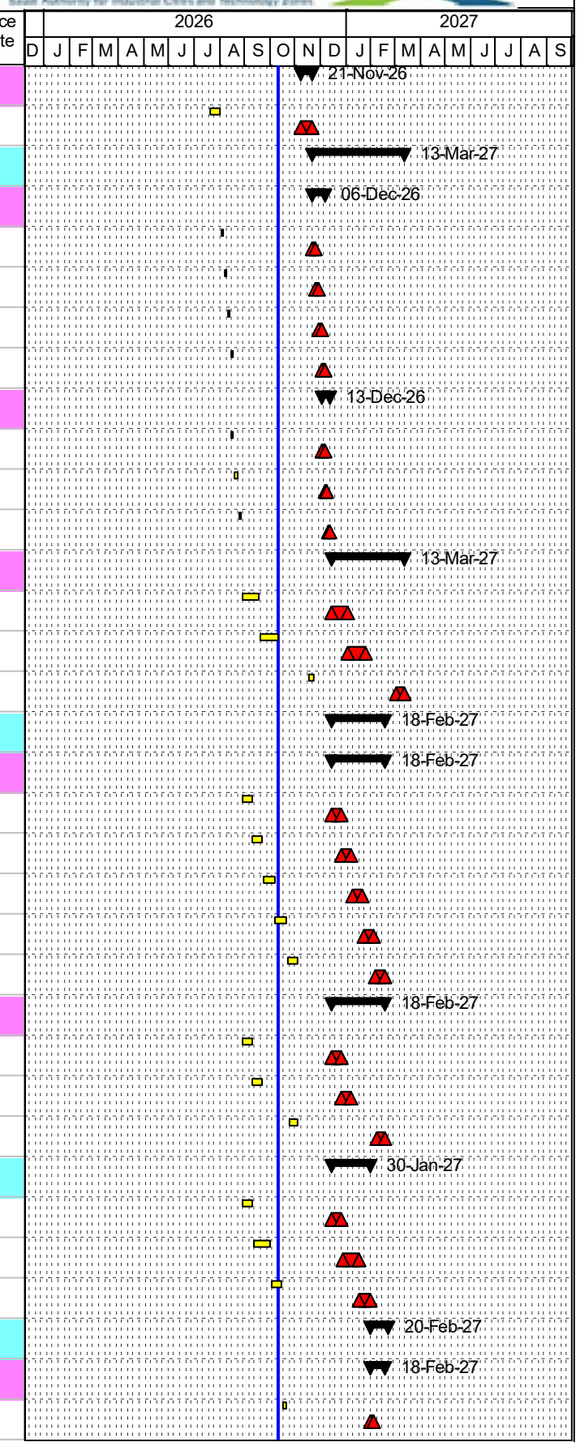



Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-PW-ML-180 | Pipes Laying and accessories for Main Lines of Potable Water Network for | 7 | 06-Feb-27 | 13-Feb-27 | 35,342 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-ML-190 | Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for | 5 | 14-Feb-27 | 18-Feb-27 | 28,291 | 0 | 0 | 0 | 0% | 0% |
| **Valve Chamber** | | 18 | 31-Jan-27 | 20-Feb-27 | 91,835 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC-260 | Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for | 5 | 31-Jan-27 | 04-Feb-27 | 5,740 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC-270 | Installation Works for Valves of Potable Water Network for Alignment-RD-02 | 5 | 09-Feb-27 | 14-Feb-27 | 14,923 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC-280 | Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for | 5 | 15-Feb-27 | 20-Feb-27 | 11,479 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC200 | Installation of Valve Chambers of Potable Water Network for Alignment-RD-02 | 3 | 06-Feb-27 | 08-Feb-27 | 59,693 | 0 | 0 | 0 | 0% | 0% |
| **Fire Hydrant** | | 13 | 06-Feb-27 | 20-Feb-27 | 62,959 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-200 | Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-02 | 3 | 06-Feb-27 | 08-Feb-27 | 3,935 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-210 | Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-02 | 3 | 14-Feb-27 | 16-Feb-27 | 51,154 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-220 | Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for | 3 | 17-Feb-27 | 20-Feb-27 | 7,870 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 18 | 07-Feb-27 | 27-Feb-27 | 267,506 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 18 | 07-Feb-27 | 27-Feb-27 | 267,506 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-200 | Trench Excavation and Bedding Works for Main Lines of Irrigation Network for | 3 | 07-Feb-27 | 09-Feb-27 | 6,922 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-210 | Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-02 | 3 | 14-Feb-27 | 16-Feb-27 | 34,609 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-220 | Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-02 | 3 | 17-Feb-27 | 20-Feb-27 | 9,941 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-230 | Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for | 3 | 24-Feb-27 | 27-Feb-27 | 13,844 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-240 | Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation | 3 | 21-Feb-27 | 23-Feb-27 | 202,191 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 12 | 14-Mar-27 | 27-Mar-27 | 28,138 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 12 | 14-Mar-27 | 27-Mar-27 | 28,138 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-310 | Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-02 | 4 | 14-Mar-27 | 17-Mar-27 | 6,170 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-320 | Duct Laying Works for Medium Voltage Network for Alignment-RD-02 | 4 | 18-Mar-27 | 22-Mar-27 | 15,103 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-330 | Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-02 | 4 | 23-Mar-27 | 27-Mar-27 | 6,865 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 40 | 28-Feb-27 | 18-Apr-27 | 139,309 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works ( Cable 300 MM )** | | 35 | 28-Feb-27 | 12-Apr-27 | 70,049 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-160 | Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for | 5 | 28-Mar-27 | 01-Apr-27 | 13,675 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-170 | Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-02 | 12 | 28-Feb-27 | 16-Mar-27 | 38,755 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-180 | Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for | 9 | 03-Apr-27 | 12-Apr-27 | 17,619 | 0 | 0 | 0 | 0% | 0% |
| **Service Low Voltage Cables Works ( Cable 70 MM )** | | 14 | 03-Apr-27 | 18-Apr-27 | 63,213 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-160 | Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for | 4 | 03-Apr-27 | 06-Apr-27 | 6,839 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-170 | Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-02 | 6 | 07-Apr-27 | 13-Apr-27 | 38,755 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-180 | Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for | 4 | 14-Apr-27 | 18-Apr-27 | 17,619 | 0 | 0 | 0 | 0% | 0% |
| **Distribution Pillars Works** | | 14 | 28-Mar-27 | 12-Apr-27 | 6,047 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-160 | Foundation Excavation Works for Distribution Pillars of Low Voltage Network for | 6 | 28-Mar-27 | 03-Apr-27 | 2,281 | 0 | 0 | 0 | 0% | 0% |

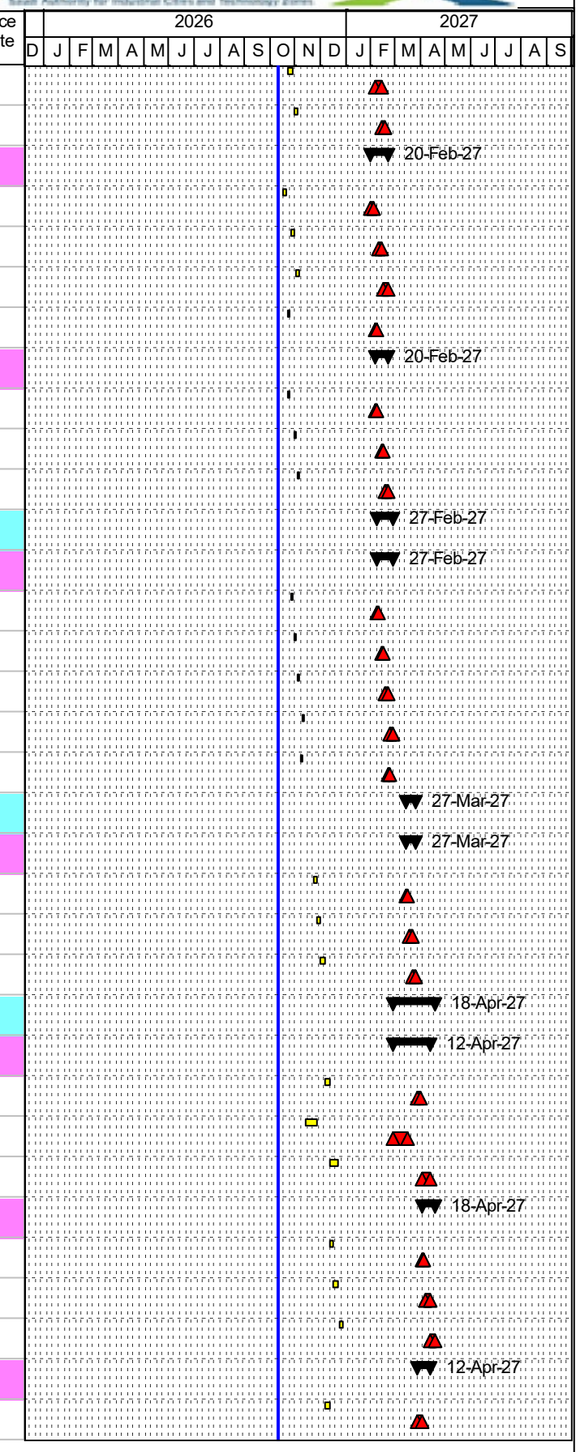



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CON-LV-DP-170 | Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for | 4 | 04-Apr-27 | 07-Apr-27 | 1,883 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-180 | Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-02 | 4 | 08-Apr-27 | 12-Apr-27 | 1,883 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 21 | 04-Apr-27 | 27-Apr-27 | 123,598 | 0 | 0 | 0 | 0% | 0% |
| **Lighting Poles Works** | | 11 | 04-Apr-27 | 15-Apr-27 | 44,088 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-400 | Installation Works for Lighting Poles Foundation of Street Lighting Network for | 4 | 04-Apr-27 | 07-Apr-27 | 9,458 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-410 | Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-02 | 4 | 08-Apr-27 | 12-Apr-27 | 31,466 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-430 | Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-02 | 3 | 13-Apr-27 | 15-Apr-27 | 3,165 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 7 | 04-Apr-27 | 11-Apr-27 | 62,968 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-320 | Cable Laying Works for Street Lighting Network for Alignment-RD-02 | 4 | 04-Apr-27 | 07-Apr-27 | 34,631 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-330 | Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-02 | 3 | 08-Apr-27 | 11-Apr-27 | 28,337 | 0 | 0 | 0 | 0% | 0% |
| **Distrubution Panel Boards** | | 10 | 17-Apr-27 | 27-Apr-27 | 16,541 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-DB-330 | Installation Works for Panel Board Concrete Foundations of Street Lighting Network for | 3 | 17-Apr-27 | 19-Apr-27 | 3,545 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-DB-340 | Installation Works for Lighting Panel Boards of Street Lighting Network for Alignment-RD-02 | 7 | 20-Apr-27 | 27-Apr-27 | 12,997 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 37 | 28-Mar-27 | 09-May-27 | 650,864 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 10 | 28-Apr-27 | 09-May-27 | 116,180 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-190 | Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-02 | 5 | 28-Apr-27 | 03-May-27 | 79,875 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-200 | Trench Backfilling and Compaction Works for Ducts of Telecom Network for | 5 | 04-May-27 | 09-May-27 | 36,306 | 0 | 0 | 0 | 0% | 0% |
| **Manholes Works** | | 9 | 28-Mar-27 | 06-Apr-27 | 30,612 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-200 | Excavation Works for Manholes of Telecom Network for Alignment-RD-02 | 3 | 28-Mar-27 | 30-Mar-27 | 2,041 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-210 | Installation Works for Manholes of Telecom Network for Alignment-RD-02 | 3 | 31-Mar-27 | 03-Apr-27 | 22,449 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-220 | Backfilling Works for Manholes of Telecom Network for Alignment-RD-02 | 3 | 04-Apr-27 | 06-Apr-27 | 6,122 | 0 | 0 | 0 | 0% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 6 | 07-Apr-27 | 13-Apr-27 | 504,071 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-180 | Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-02 | 6 | 07-Apr-27 | 13-Apr-27 | 504,071 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 26 | 19-Apr-27 | 24-May-27 | 1,365,735 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 14 | 19-Apr-27 | 04-May-27 | 1,338,540 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-200 | Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-02 | 5 | 19-Apr-27 | 24-Apr-27 | 131,137 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-210 | Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-02 | 9 | 25-Apr-27 | 04-May-27 | 1,207,402 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 8 | 10-May-27 | 24-May-27 | 27,195 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-200 | Application of Road Marking Works For Road Works for Alignment-RD-02 | 4 | 10-May-27 | 13-May-27 | 17,728 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-140 | Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-02 | 4 | 20-May-27 | 24-May-27 | 9,468 | 0 | 0 | 0 | 0% | 0% |
| **Finishes for Infrastructure Networks** | | 57 | 28-Mar-27 | 07-Jun-27 | 883,500 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 30 | 28-Apr-27 | 07-Jun-27 | 359,891 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 30 | 28-Apr-27 | 07-Jun-27 | 359,891 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-200 | Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-02 | 6 | 23-May-27 | 29-May-27 | 33,846 | 0 | 0 | 0 | 0% | 0% |

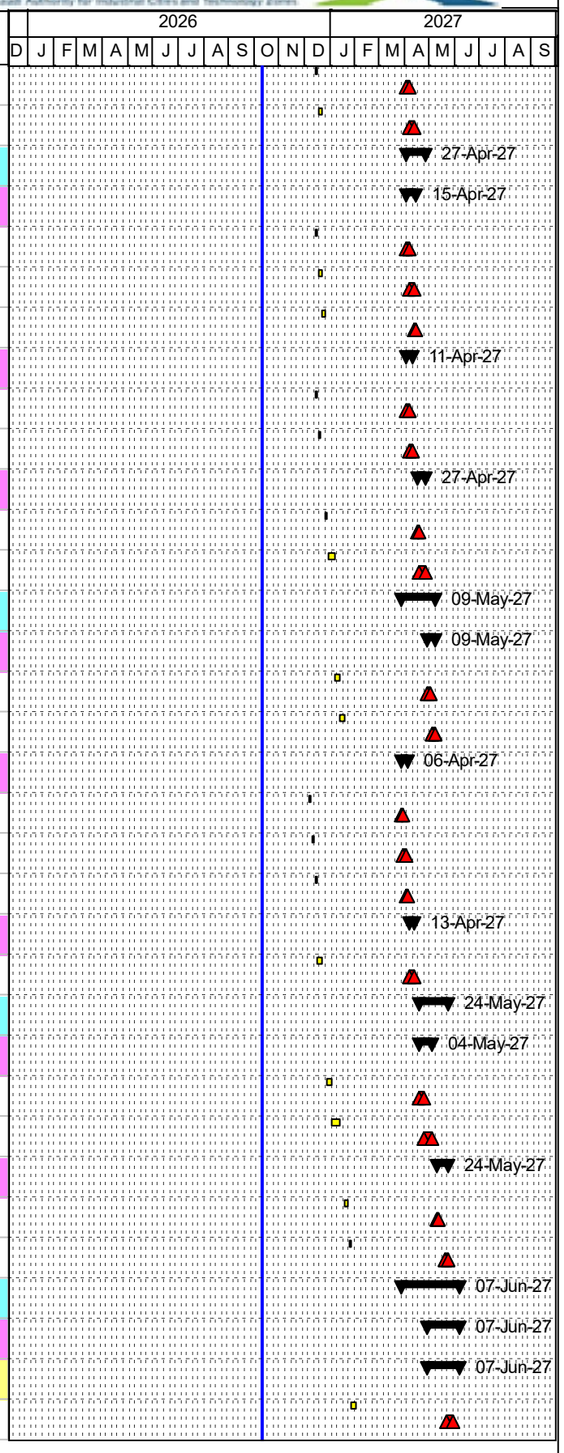



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-SD-CB-TF-210 | Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for | 8 | 30-May-27 | 07-Jun-27 | 50,769 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-220 | Catch Basin Internal Finishes (Benching ) for Storm Drainage Network for Alignment-RD-02 | 6 | 10-May-27 | 22-May-27 | 50,769 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-MH-TF-250 | Testing Works for Manholes of Storm Drainage Network for Alignment-RD-02 | 6 | 10-May-27 | 22-May-27 | 38,265 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-ML-TF-120 | Testing Work for Pipes of Storm Drainage Network for Alignment-RD-02 | 6 | 28-Apr-27 | 04-May-27 | 186,241 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Network** | | 18 | 17-Apr-27 | 06-May-27 | 77,047 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 18 | 17-Apr-27 | 06-May-27 | 77,047 | 0 | 0 | 0 | 0% | 0% |
| CO-SW-TF-270 | Final Testing For Main Line of Sewage Network for Alignment-RD-02 | 18 | 17-Apr-27 | 06-May-27 | 45,443 | 0 | 0 | 0 | 0% | 0% |
| CO-SW-TF-290 | Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-02 | 18 | 17-Apr-27 | 06-May-27 | 31,604 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 30 | 13-Apr-27 | 23-May-27 | 102,331 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 30 | 13-Apr-27 | 23-May-27 | 102,331 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-160 | Testing of Potable Water Network for Alignment-RD-02 | 8 | 09-May-27 | 23-May-27 | 28,291 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-170 | Fire Hydrant Finishies (S.Box + Safety + Marker Post ) of Potable Water Network for | 14 | 13-Apr-27 | 28-Apr-27 | 15,740 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-180 | Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-02 | 8 | 29-Apr-27 | 08-May-27 | 58,301 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 4 | 25-Apr-27 | 28-Apr-27 | 13,844 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 4 | 25-Apr-27 | 28-Apr-27 | 13,844 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-TF-180 | Final Testing (pressure tests) of Irrigation Network for Alignment-RD-02 | 4 | 25-Apr-27 | 28-Apr-27 | 13,844 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 6 | 10-May-27 | 22-May-27 | 77,686 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 10-May-27 | 22-May-27 | 77,686 | 0 | 0 | 0 | 0% | 0% |
| CO-TSE-TF-190 | Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-02 | 6 | 10-May-27 | 22-May-27 | 77,686 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 6 | 28-Mar-27 | 03-Apr-27 | 5,492 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 6 | 28-Mar-27 | 03-Apr-27 | 5,492 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-TF-240 | Testing and Termination Works of Medium Voltage Network for Alignment-RD-02 | 6 | 28-Mar-27 | 03-Apr-27 | 5,492 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 8 | 18-Apr-27 | 26-Apr-27 | 29,795 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 8 | 18-Apr-27 | 26-Apr-27 | 29,257 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-140 | Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage | 4 | 22-Apr-27 | 26-Apr-27 | 28,181 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-150 | Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for | 4 | 18-Apr-27 | 21-Apr-27 | 1,076 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 2 | 22-Apr-27 | 24-Apr-27 | 538 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ES-120 | Earthing System Works for Distribution Pillars Units of Low Voltage Network for | 2 | 22-Apr-27 | 24-Apr-27 | 538 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 16 | 20-Apr-27 | 08-May-27 | 52,148 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 16 | 20-Apr-27 | 08-May-27 | 46,478 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-420 | Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for | 2 | 20-Apr-27 | 21-Apr-27 | 20,510 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-440 | Termination Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02 | 6 | 28-Apr-27 | 04-May-27 | 4,726 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-450 | Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-02 | 2 | 06-May-27 | 08-May-27 | 18,880 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-460 | Testing Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02 | 2 | 06-May-27 | 08-May-27 | 2,363 | 0 | 0 | 0 | 0% | 0% |

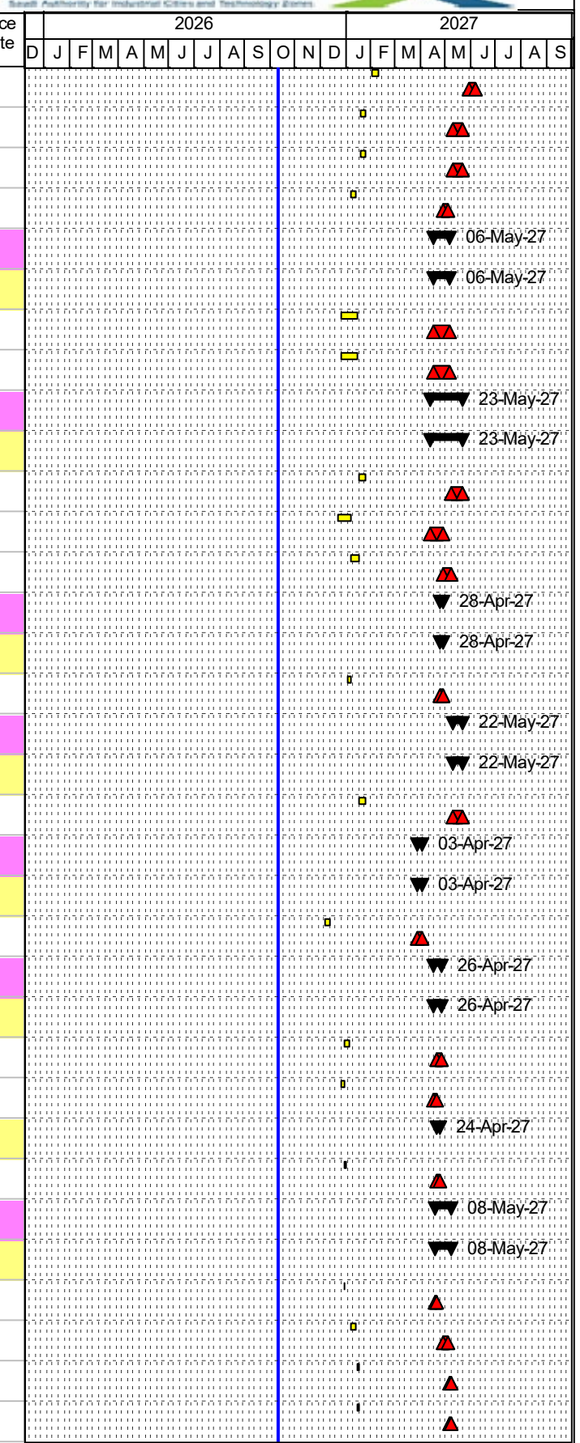



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Earthing System Works** | | 12 | 22-Apr-27 | 05-May-27 | 5,669 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-260 | Install Earthing System Works for Lighting Poles of Street Lighting Network for | 6 | 22-Apr-27 | 28-Apr-27 | 2,835 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-270 | Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for | 6 | 29-Apr-27 | 05-May-27 | 2,835 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 6 | 22-Apr-27 | 28-Apr-27 | 165,267 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 22-Apr-27 | 28-Apr-27 | 165,267 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-220 | Testing and Interface modules with Telecom for Alignment-RD-02 | 3 | 22-Apr-27 | 25-Apr-27 | 39,249 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-350 | Testing and Interface modules with CCTV, Telephone, MSN and Access Control for | 3 | 26-Apr-27 | 28-Apr-27 | 126,018 | 0 | 0 | 0 | 0% | 0% |
| **Alignment-RD-03-1** | | 171 | 12-Oct-26 | 02-May-27 | 3,448,486 | 1,263,997 | 0 | 0 | 36.65% | 0% |
| **Earthworks** | | 12 | 12-Oct-26 | 25-Oct-26 | 829,055 | 829,055 | 0 | 0 | 100% | 0% |
| **Earthworks** | | 12 | 12-Oct-26 | 25-Oct-26 | 829,055 | 829,055 | 0 | 0 | 100% | 0% |
| CO-EW-200 | Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-1 | 12 | 12-Oct-26 | 25-Oct-26 | 829,055 | 829,055 | 0 | 0 | 100% | 0% |
| **Storm Drainage Network** | | 33 | 26-Oct-26 | 02-Dec-26 | 122,202 | 122,202 | 0 | 0 | 100% | 0% |
| **Manholes** | | 33 | 26-Oct-26 | 02-Dec-26 | 48,644 | 48,644 | 0 | 0 | 100% | 0% |
| CO-SD-MH-180 | Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for | 10 | 26-Oct-26 | 05-Nov-26 | 3,243 | 3,243 | 0 | 0 | 100% | 0% |
| CO-SD-MH-190 | Install RC Footing Works for Manholes of Storm Drainage Network for | 3 | 07-Nov-26 | 09-Nov-26 | 16,215 | 16,215 | 0 | 0 | 100% | 0% |
| CO-SD-MH-200 | Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for | 10 | 10-Nov-26 | 21-Nov-26 | 19,458 | 19,458 | 0 | 0 | 100% | 0% |
| CO-SD-MH-220 | Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-1 | 10 | 22-Nov-26 | 02-Dec-26 | 9,729 | 9,729 | 0 | 0 | 100% | 0% |
| **Main Line Sections** | | 10 | 22-Nov-26 | 02-Dec-26 | 73,558 | 73,558 | 0 | 0 | 100% | 0% |
| CO-SD-ML-100 | Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for | 3 | 22-Nov-26 | 24-Nov-26 | 9,196 | 9,196 | 0 | 0 | 100% | 0% |
| CO-SD-ML-120 | Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-1 | 3 | 25-Nov-26 | 28-Nov-26 | 45,975 | 45,975 | 0 | 0 | 100% | 0% |
| CO-SD-ML-130 | Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for | 4 | 29-Nov-26 | 02-Dec-26 | 18,387 | 18,387 | 0 | 0 | 100% | 0% |
| **Treated Sewage Effluent (Tse)** | | 119 | 10-Dec-26 | 01-May-27 | 880,133 | 273,530 | 0 | 0 | 31.08% | 0% |
| CO-TSE-ML-150 | Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse) | 4 | 10-Dec-26 | 14-Dec-26 | 4,681 | 4,681 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-160 | Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-1 | 4 | 15-Dec-26 | 19-Dec-26 | 21,975 | 21,975 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-170 | Installation Works for Main Line Valves of Treated Sewage Effluent (Tse) for | 6 | 20-Dec-26 | 26-Dec-26 | 11,899 | 11,899 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-180 | Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for | 5 | 03-Jan-27 | 07-Jan-27 | 8,884 | 8,884 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-190 | Installation Works for Valve and Washout Chambers of Treated Sewage Effluent (Tse) | 6 | 27-Dec-26 | 02-Jan-27 | 226,089 | 226,089 | 0 | 0 | 100% | 0% |
| **Treated Sewage Effluent (Tse) Storage Tank** | | 6 | 25-Apr-27 | 01-May-27 | 606,604 | 0 | 0 | 0 | 0% | 0% |
| CO-TSE-TF-180 | Installation of Storage Tank of Treated Sewage Effluent (Tse) for Alignment-RD-03-1 | 6 | 25-Apr-27 | 01-May-27 | 606,604 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 88 | 09-Jan-27 | 24-Apr-27 | 671,455 | 39,211 | 0 | 0 | 5.84% | 0% |
| **Main Line Sections** | | 17 | 09-Jan-27 | 27-Jan-27 | 15,148 | 9,643 | 0 | 0 | 63.66% | 0% |
| CO-PW-ML-100 | Trench Excavation and Bedding Works for Main Lines of Potable Water Network for | 5 | 09-Jan-27 | 13-Jan-27 | 2,765 | 2,765 | 0 | 0 | 100% | 0% |
| CO-PW-ML-110 | Pipes Laying and accessories for Main Lines of Potable Water Network for | 5 | 14-Jan-27 | 19-Jan-27 | 6,878 | 6,878 | 0 | 0 | 100% | 0% |
| CO-PW-ML-130 | Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for | 7 | 20-Jan-27 | 27-Jan-27 | 5,505 | 0 | 0 | 0 | 0% | 0% |

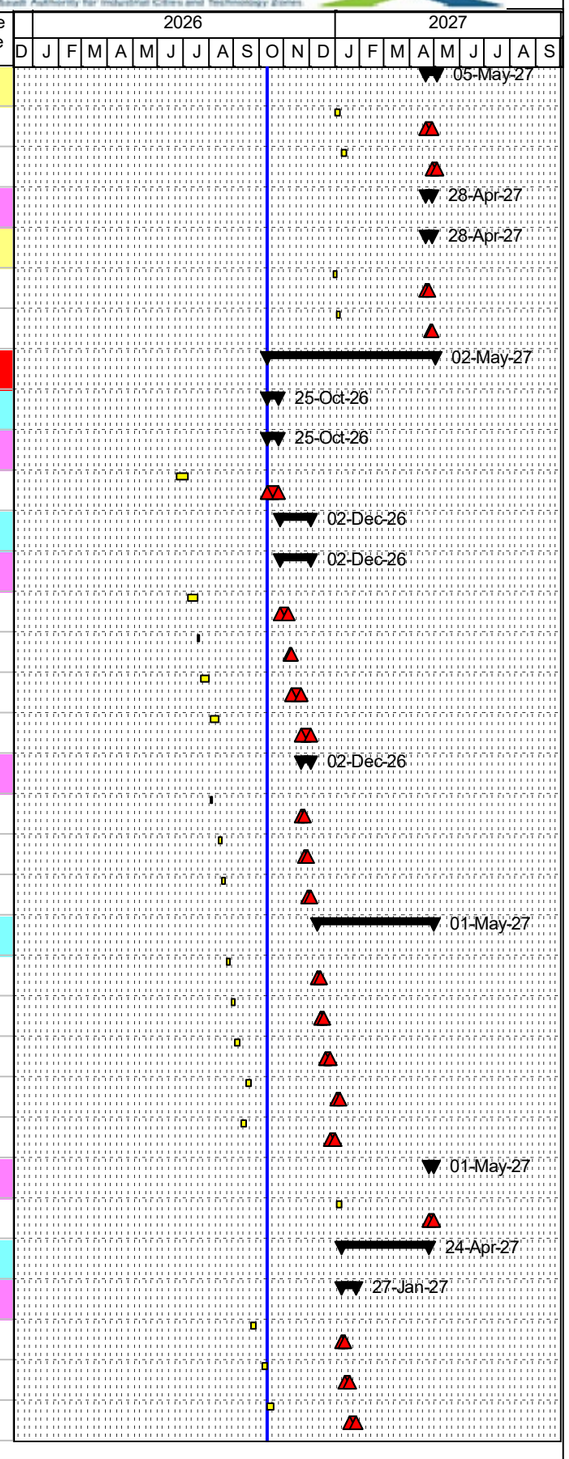



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Valve Chamber** | | 17 | 11-Jan-27 | 30-Jan-27 | 40,710 | 29,006 | 0 | 0 | 71.25% | 0% |
| CO-PW-VC-170 | Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for | 3 | 11-Jan-27 | 13-Jan-27 | 2,544 | 2,544 | 0 | 0 | 100% | 0% |
| CO-PW-VC-190 | Installation Works for Valves of Potable Water Network for Alignment-RD-03-1 | 3 | 24-Jan-27 | 26-Jan-27 | 6,615 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC-220 | Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for | 3 | 27-Jan-27 | 30-Jan-27 | 5,089 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC180 | Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-1 | 3 | 14-Jan-27 | 17-Jan-27 | 26,462 | 26,462 | 0 | 0 | 100% | 0% |
| **Fire Hydrant** | | 14 | 14-Jan-27 | 30-Jan-27 | 8,994 | 562 | 0 | 0 | 6.25% | 0% |
| CO-PW-FH-140 | Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-1 | 2 | 14-Jan-27 | 16-Jan-27 | 562 | 562 | 0 | 0 | 100% | 0% |
| CO-PW-FH-150 | Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-1 | 2 | 20-Jan-27 | 21-Jan-27 | 7,308 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-160 | Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for | 2 | 28-Jan-27 | 30-Jan-27 | 1,124 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network Storage Tank** | | 6 | 18-Apr-27 | 24-Apr-27 | 606,604 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-130 | Installation of Storage Tank of Potable Water Network for Alignment-RD-03-1 | 6 | 18-Apr-27 | 24-Apr-27 | 606,604 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 47 | 28-Jan-27 | 27-Mar-27 | 38,649 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works ( Cable 300 MM )** | | 19 | 28-Jan-27 | 18-Feb-27 | 18,678 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-100 | Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for | 8 | 28-Jan-27 | 06-Feb-27 | 3,648 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-110 | Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-1 | 7 | 07-Feb-27 | 14-Feb-27 | 10,333 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-120 | Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for | 4 | 15-Feb-27 | 18-Feb-27 | 4,697 | 0 | 0 | 0 | 0% | 0% |
| **Service Low Voltage Cables Works ( Cable 70 MM )** | | 27 | 07-Feb-27 | 13-Mar-27 | 16,853 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-100 | Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for | 4 | 07-Feb-27 | 10-Feb-27 | 1,823 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-110 | Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-1 | 7 | 27-Feb-27 | 06-Mar-27 | 10,333 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-120 | Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for | 3 | 07-Mar-27 | 13-Mar-27 | 4,697 | 0 | 0 | 0 | 0% | 0% |
| **Distribution Pillars Works** | | 12 | 14-Mar-27 | 27-Mar-27 | 3,119 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-100 | Foundation Excavation Works for Distribution Pillars of Low Voltage Network for | 4 | 14-Mar-27 | 17-Mar-27 | 608 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-110 | Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for | 4 | 18-Mar-27 | 22-Mar-27 | 1,255 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-120 | Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-1 | 4 | 23-Mar-27 | 27-Mar-27 | 1,255 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 20 | 27-Feb-27 | 24-Mar-27 | 24,454 | 0 | 0 | 0 | 0% | 0% |
| **Lighting Poles Works** | | 16 | 27-Feb-27 | 20-Mar-27 | 10,069 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-550 | Installation Works for Lighting Poles Foundation of Street Lighting Network for | 5 | 27-Feb-27 | 03-Mar-27 | 2,158 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-560 | Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1 | 5 | 04-Mar-27 | 13-Mar-27 | 7,192 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-570 | Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1 | 6 | 14-Mar-27 | 20-Mar-27 | 719 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 10 | 14-Mar-27 | 24-Mar-27 | 14,384 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-410 | Cable Laying Works for Street Lighting Network for Alignment-RD-03-1 | 5 | 14-Mar-27 | 18-Mar-27 | 7,911 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-420 | Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-1 | 5 | 20-Mar-27 | 24-Mar-27 | 6,473 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 12 | 21-Mar-27 | 03-Apr-27 | 234,558 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 8 | 25-Mar-27 | 03-Apr-27 | 30,845 | 0 | 0 | 0 | 0% | 0% |

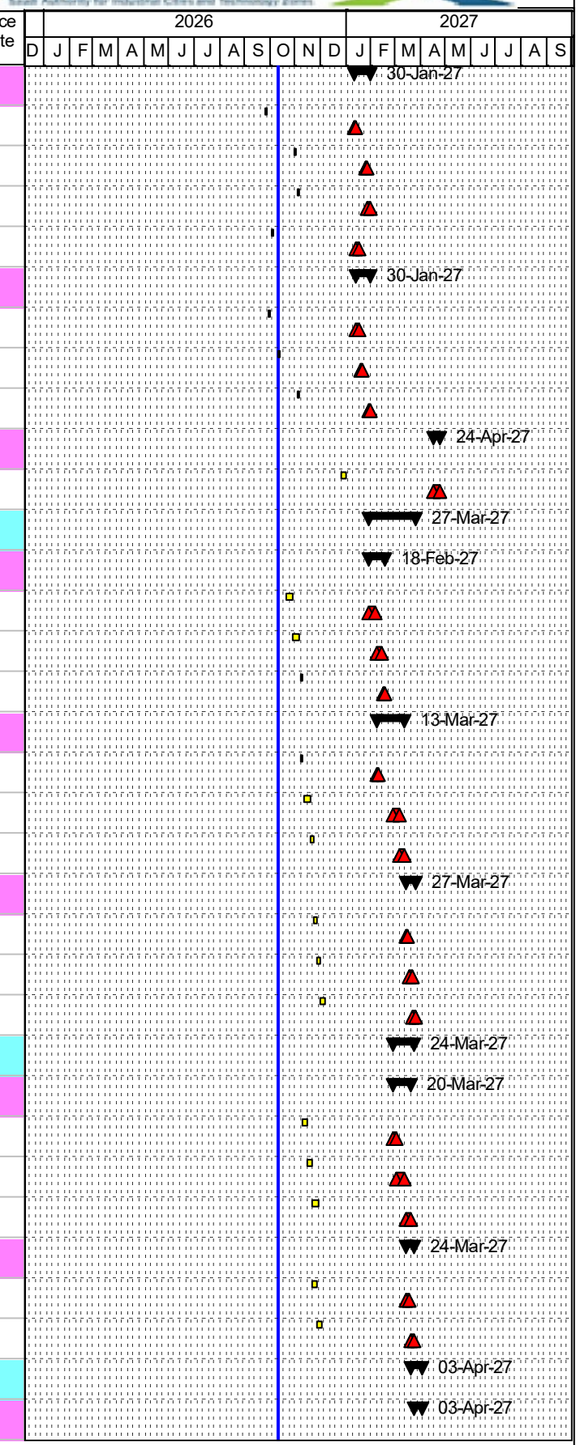



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-TE-DW-110 | Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-1 | 4 | 25-Mar-27 | 29-Mar-27 | 21,205 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-130 | Trench Backfilling and Compaction Works for Ducts of Telecom Network for | 4 | 30-Mar-27 | 03-Apr-27 | 9,640 | 0 | 0 | 0 | 0% | 0% |
| **Manholes Works** | | 6 | 21-Mar-27 | 27-Mar-27 | 14,687 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-140 | Excavation Works for Manholes of Telecom Network for Alignment-RD-03-1 | 2 | 21-Mar-27 | 22-Mar-27 | 979 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-150 | Installation Works for Manholes of Telecom Network for Alignment-RD-03-1 | 2 | 23-Mar-27 | 24-Mar-27 | 10,770 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-160 | Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-1 | 2 | 25-Mar-27 | 27-Mar-27 | 2,937 | 0 | 0 | 0 | 0% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 4 | 28-Mar-27 | 31-Mar-27 | 189,027 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-110 | Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-1 | 4 | 28-Mar-27 | 31-Mar-27 | 189,027 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 22 | 04-Apr-27 | 28-Apr-27 | 499,484 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 14 | 04-Apr-27 | 19-Apr-27 | 134,372 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-140 | Subgrade Layer for Road Works for Alignment-RD-03-1 | 7 | 04-Apr-27 | 11-Apr-27 | 65,548 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-150 | Aggregate Base Course Layer for Road Works for Alignment-RD-03-1 | 7 | 12-Apr-27 | 19-Apr-27 | 68,824 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 7 | 12-Apr-27 | 19-Apr-27 | 278,096 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-160 | Bituminous Base Courses Layers for Road Works for Alignment-RD-03-1 | 2 | 12-Apr-27 | 13-Apr-27 | 138,392 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-150 | Preparation of Asphaltic Wearing Course Layer for Roads Network for | 2 | 18-Apr-27 | 19-Apr-27 | 139,704 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 13 | 14-Apr-27 | 28-Apr-27 | 75,922 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-160 | Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-1 | 5 | 14-Apr-27 | 19-Apr-27 | 46,267 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-170 | Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-1 | 8 | 20-Apr-27 | 28-Apr-27 | 29,656 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 4 | 20-Apr-27 | 24-Apr-27 | 11,093 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-180 | Application of Road Marking Works For Road Works for Alignment-RD-03-1 | 2 | 20-Apr-27 | 21-Apr-27 | 6,360 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-120 | Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-1 | 2 | 22-Apr-27 | 24-Apr-27 | 4,734 | 0 | 0 | 0 | 0% | 0% |
| **Finishes for Infrastructure Networks** | | 31 | 28-Mar-27 | 02-May-27 | 148,496 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 6 | 17-Apr-27 | 22-Apr-27 | 34,602 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 17-Apr-27 | 22-Apr-27 | 34,602 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-MH-TF-210 | Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-1 | 3 | 20-Apr-27 | 22-Apr-27 | 16,215 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-ML-TF-100 | Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-1 | 3 | 17-Apr-27 | 19-Apr-27 | 18,387 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 4 | 13-Apr-27 | 17-Apr-27 | 24,809 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 4 | 13-Apr-27 | 17-Apr-27 | 24,809 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-100 | Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-1 | 4 | 13-Apr-27 | 17-Apr-27 | 17,055 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-110 | Testing of Potable Water Network for Alignment-RD-03-1 | 2 | 13-Apr-27 | 14-Apr-27 | 5,505 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-120 | Fire Hydrant Finishies (S.Box + Safety + Marker Post ) of Potable Water Network for | 3 | 13-Apr-27 | 15-Apr-27 | 2,249 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 1 | 02-May-27 | 02-May-27 | 8,884 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 1 | 02-May-27 | 02-May-27 | 8,884 | 0 | 0 | 0 | 0% | 0% |
| CO-TSE-TF-170 | Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-1 | 1 | 02-May-27 | 02-May-27 | 8,884 | 0 | 0 | 0 | 0% | 0% |

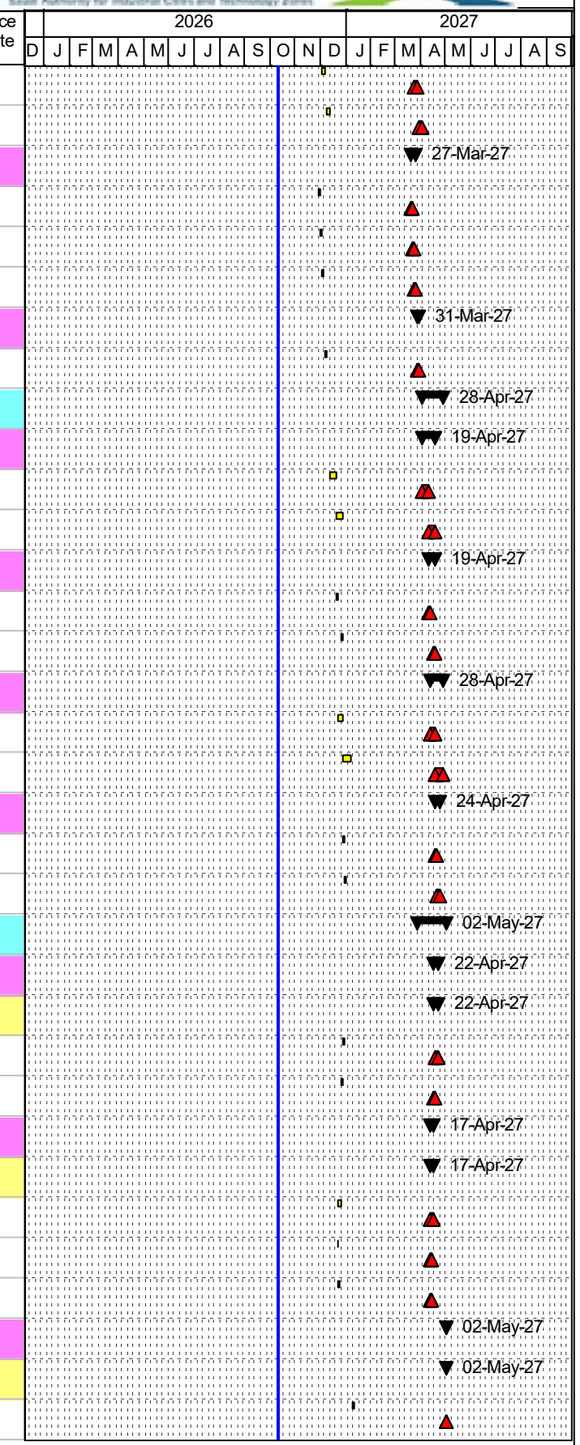



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Low Voltage Network** | | 4 | 28-Mar-27 | 31-Mar-27 | 8,591 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 4 | 28-Mar-27 | 31-Mar-27 | 8,232 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-100 | Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage | 2 | 30-Mar-27 | 31-Mar-27 | 7,515 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-110 | Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for | 2 | 28-Mar-27 | 29-Mar-27 | 717 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 2 | 30-Mar-27 | 31-Mar-27 | 359 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ES-100 | Earthing System Works for Distribution Pillars Units of Low Voltage Network for | 2 | 30-Mar-27 | 31-Mar-27 | 359 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 17 | 06-Apr-27 | 25-Apr-27 | 10,034 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 17 | 06-Apr-27 | 25-Apr-27 | 9,003 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-580 | Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for | 6 | 06-Apr-27 | 12-Apr-27 | 4,688 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-570 | Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1 | 6 | 19-Apr-27 | 25-Apr-27 | 4,315 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 5 | 13-Apr-27 | 18-Apr-27 | 1,031 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-320 | Install Earthing System Works for Lighting Poles of Street Lighting Network for | 3 | 13-Apr-27 | 15-Apr-27 | 515 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-330 | Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for | 2 | 17-Apr-27 | 18-Apr-27 | 515 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 6 | 01-Apr-27 | 07-Apr-27 | 61,576 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 01-Apr-27 | 07-Apr-27 | 61,576 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-140 | Testing and Interface modules with Telecom for Alignment-RD-03-1 | 6 | 01-Apr-27 | 07-Apr-27 | 12,607 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-330 | Testing and Interface modules with CCTV, Telephone, MSN and Access Control for | 6 | 01-Apr-27 | 07-Apr-27 | 48,969 | 0 | 0 | 0 | 0% | 0% |
| **Alignment-RD-03-2** | | 192 | 14-Oct-26 | 03-Jun-27 | 3,959,670 | 2,178,866 | 0 | 0 | 55.03% | 0% |
| **Earthworks** | | 12 | 14-Oct-26 | 27-Oct-26 | 1,830,833 | 1,830,833 | 0 | 0 | 100% | 0% |
| **Earthworks** | | 12 | 14-Oct-26 | 27-Oct-26 | 1,830,833 | 1,830,833 | 0 | 0 | 100% | 0% |
| CO-EW-240 | Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-2 | 12 | 14-Oct-26 | 27-Oct-26 | 1,830,833 | 1,830,833 | 0 | 0 | 100% | 0% |
| **Storm Drainage Network** | | 47 | 03-Dec-26 | 26-Jan-27 | 384,908 | 348,033 | 0 | 0 | 90.42% | 0% |
| **Manholes** | | 36 | 03-Dec-26 | 13-Jan-27 | 163,658 | 163,658 | 0 | 0 | 100% | 0% |
| CO-SD-MH-350 | Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for | 10 | 03-Dec-26 | 14-Dec-26 | 10,911 | 10,911 | 0 | 0 | 100% | 0% |
| CO-SD-MH-360 | Install RC Footing Works for Manholes of Storm Drainage Network for | 9 | 15-Dec-26 | 24-Dec-26 | 54,553 | 54,553 | 0 | 0 | 100% | 0% |
| CO-SD-MH-370 | Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for | 10 | 26-Dec-26 | 05-Jan-27 | 65,463 | 65,463 | 0 | 0 | 100% | 0% |
| CO-SD-MH-380 | Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-2 | 7 | 06-Jan-27 | 13-Jan-27 | 32,732 | 32,732 | 0 | 0 | 100% | 0% |
| **Main Line Sections** | | 18 | 06-Jan-27 | 26-Jan-27 | 221,251 | 184,376 | 0 | 0 | 83.33% | 0% |
| CO-SD-ML-230 | Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for | 7 | 06-Jan-27 | 13-Jan-27 | 39,655 | 39,655 | 0 | 0 | 100% | 0% |
| CO-SD-ML-240 | Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-2 | 5 | 14-Jan-27 | 19-Jan-27 | 126,283 | 126,283 | 0 | 0 | 100% | 0% |
| CO-SD-ML-250 | Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for | 6 | 20-Jan-27 | 26-Jan-27 | 55,313 | 18,438 | 0 | 0 | 33.33% | 0% |
| **Medium Voltage Network** | | 16 | 21-Feb-27 | 14-Mar-27 | 25,481 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 16 | 21-Feb-27 | 14-Mar-27 | 25,481 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-370 | Trench Excavation and Bedding Works for Medium Voltage Network for | 5 | 21-Feb-27 | 25-Feb-27 | 5,553 | 0 | 0 | 0 | 0% | 0% |

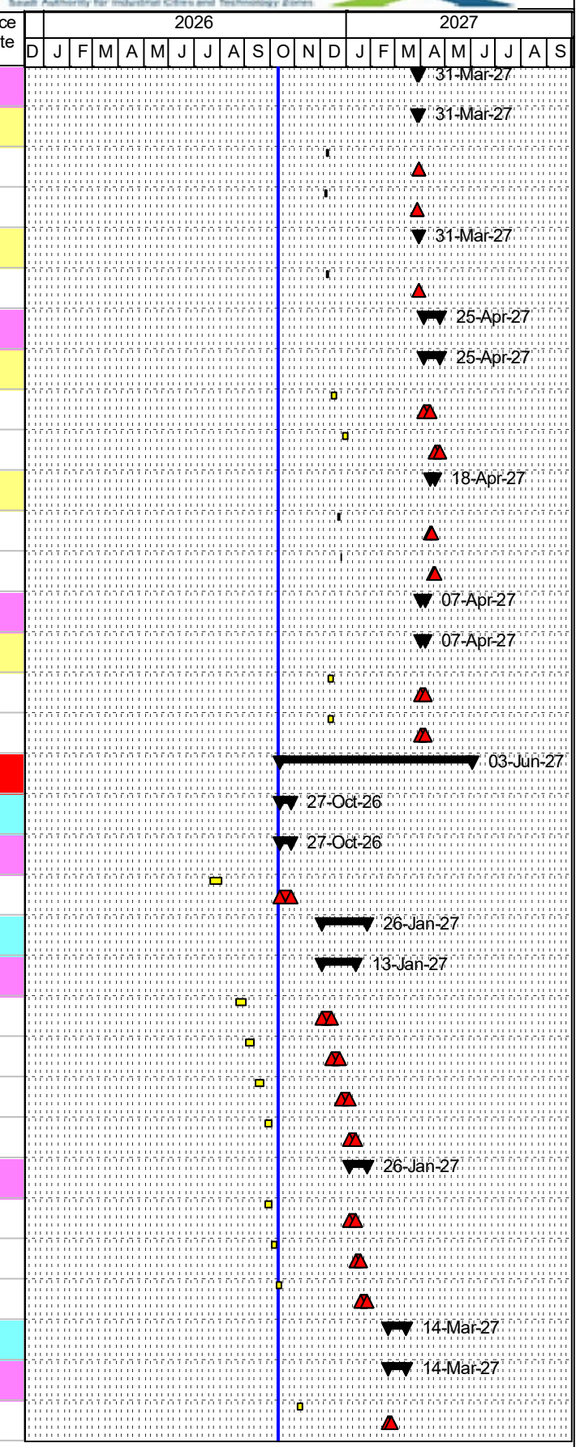



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-MV-ML-380 | Duct Laying Works for Medium Voltage Network for Alignment-RD-03-2 | 5 | 28-Feb-27 | 04-Mar-27 | 13,701 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-390 | Trench Backfilling and Compaction Works for Medium Voltage Network for | 4 | 07-Mar-27 | 14-Mar-27 | 6,228 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 30 | 17-Mar-27 | 20-Apr-27 | 82,593 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works ( Cable 300 MM )** | | 21 | 17-Mar-27 | 10-Apr-27 | 42,036 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-220 | Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for | 6 | 17-Mar-27 | 23-Mar-27 | 8,206 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-230 | Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-2 | 9 | 24-Mar-27 | 03-Apr-27 | 23,255 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-240 | Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for | 6 | 04-Apr-27 | 10-Apr-27 | 10,574 | 0 | 0 | 0 | 0% | 0% |
| **Service Low Voltage Cables Works ( Cable 70 MM )** | | 24 | 24-Mar-27 | 20-Apr-27 | 37,933 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-220 | Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for | 5 | 24-Mar-27 | 29-Mar-27 | 4,104 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-230 | Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-2 | 9 | 04-Apr-27 | 13-Apr-27 | 23,255 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-240 | Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for | 6 | 14-Apr-27 | 20-Apr-27 | 10,574 | 0 | 0 | 0 | 0% | 0% |
| **Distribution Pillars Works** | | 11 | 25-Mar-27 | 06-Apr-27 | 2,624 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-220 | Foundation Excavation Works for Distribution Pillars of Low Voltage Network for | 7 | 25-Mar-27 | 01-Apr-27 | 1,369 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-230 | Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for | 2 | 03-Apr-27 | 04-Apr-27 | 628 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-240 | Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-2 | 2 | 05-Apr-27 | 06-Apr-27 | 628 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 21 | 27-Feb-27 | 25-Mar-27 | 55,021 | 0 | 0 | 0 | 0% | 0% |
| **Lighting Poles Works** | | 16 | 27-Feb-27 | 20-Mar-27 | 22,656 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-500 | Installation Works for Lighting Poles Foundation of Street Lighting Network for | 5 | 27-Feb-27 | 03-Mar-27 | 4,855 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-510 | Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2 | 5 | 04-Mar-27 | 13-Mar-27 | 16,183 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-520 | Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2 | 6 | 14-Mar-27 | 20-Mar-27 | 1,618 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 10 | 15-Mar-27 | 25-Mar-27 | 32,365 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-380 | Cable Laying Works for Street Lighting Network for Alignment-RD-03-2 | 5 | 15-Mar-27 | 20-Mar-27 | 17,801 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-390 | Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-2 | 5 | 21-Mar-27 | 25-Mar-27 | 14,564 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 3 | 21-Apr-27 | 24-Apr-27 | 252,036 | 0 | 0 | 0 | 0% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 3 | 21-Apr-27 | 24-Apr-27 | 252,036 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-240 | Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-2 | 3 | 21-Apr-27 | 24-Apr-27 | 252,036 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 33 | 21-Apr-27 | 03-Jun-27 | 1,110,832 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 10 | 21-Apr-27 | 02-May-27 | 299,699 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-220 | Subgrade Layer for Road Works for Alignment-RD-03-2 | 5 | 21-Apr-27 | 26-Apr-27 | 146,196 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-230 | Installation of Aggregate Base Course Layer and Interlock Works for Road Works for | 5 | 27-Apr-27 | 02-May-27 | 153,503 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 15 | 03-May-27 | 25-May-27 | 620,266 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-240 | Bituminous Base Courses Layers for Road Works for Alignment-RD-03-2 | 3 | 03-May-27 | 05-May-27 | 308,669 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-230 | Preparation of Asphaltic Wearing Course Layer for Roads Network for | 3 | 23-May-27 | 25-May-27 | 311,597 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 14 | 06-May-27 | 27-May-27 | 169,336 | 0 | 0 | 0 | 0% | 0% |

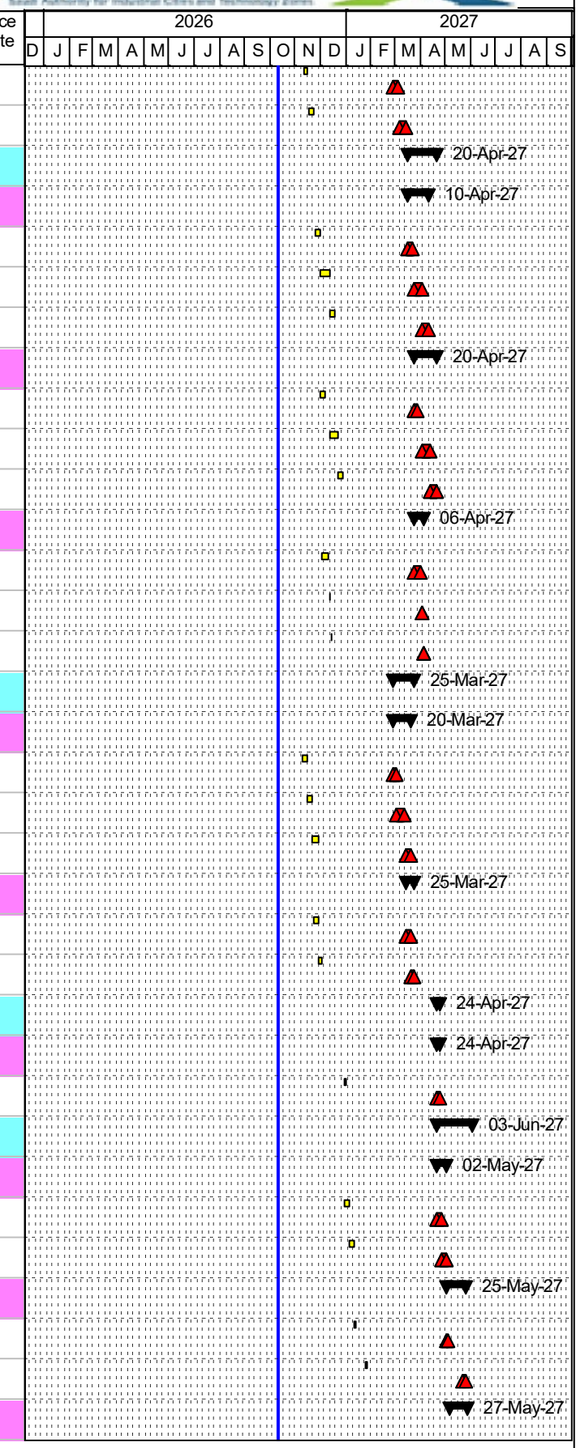



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-RD-PV-240 | Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-2 | 7 | 06-May-27 | 13-May-27 | 103,193 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-250 | Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-2 | 7 | 20-May-27 | 27-May-27 | 66,143 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 6 | 29-May-27 | 03-Jun-27 | 21,532 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-220 | Application of Road Marking Works For Road Works for Alignment-RD-03-2 | 3 | 29-May-27 | 31-May-27 | 13,958 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-160 | Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-2 | 3 | 01-Jun-27 | 03-Jun-27 | 7,574 | 0 | 0 | 0 | 0% | 0% |
| **Finishes for Infrastructure Networks** | | 54 | 15-Mar-27 | 22-May-27 | 217,965 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 16 | 28-Apr-27 | 22-May-27 | 109,865 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 16 | 28-Apr-27 | 22-May-27 | 109,865 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-CB-TF-260 | Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-03-2 | 9 | 06-May-27 | 22-May-27 | 55,313 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-MH-TF-290 | Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-2 | 6 | 28-Apr-27 | 04-May-27 | 54,553 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 6 | 15-Mar-27 | 21-Mar-27 | 4,982 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 6 | 15-Mar-27 | 21-Mar-27 | 4,982 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-TF-260 | Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-2 | 6 | 15-Mar-27 | 21-Mar-27 | 4,982 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 19 | 07-Apr-27 | 28-Apr-27 | 17,446 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 19 | 07-Apr-27 | 28-Apr-27 | 17,267 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-180 | Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage | 7 | 21-Apr-27 | 28-Apr-27 | 16,908 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-190 | Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for | 6 | 07-Apr-27 | 13-Apr-27 | 359 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 2 | 14-Apr-27 | 15-Apr-27 | 179 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ES-140 | Earthing System Works for Distribution Pillars Units of Low Voltage Network for | 2 | 14-Apr-27 | 15-Apr-27 | 179 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 15 | 30-Mar-27 | 15-Apr-27 | 22,662 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 15 | 30-Mar-27 | 15-Apr-27 | 20,257 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-530 | Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for | 6 | 30-Mar-27 | 05-Apr-27 | 10,548 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-530 | Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2 | 6 | 10-Apr-27 | 15-Apr-27 | 9,710 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 5 | 10-Apr-27 | 14-Apr-27 | 2,405 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-300 | Install Earthing System Works for Lighting Poles of Street Lighting Network for | 3 | 10-Apr-27 | 12-Apr-27 | 1,203 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-310 | Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for | 2 | 13-Apr-27 | 14-Apr-27 | 1,203 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 4 | 25-Apr-27 | 28-Apr-27 | 63,009 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 4 | 25-Apr-27 | 28-Apr-27 | 63,009 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-320 | Testing and Interface modules with CCTV, Telephone, MSN and Access Control for | 4 | 25-Apr-27 | 28-Apr-27 | 63,009 | 0 | 0 | 0 | 0% | 0% |
| **Alignment-RD-03-3** | | 165 | 26-Oct-26 | 09-May-27 | 2,245,578 | 1,084,377 | 0 | 0 | 48.29% | 0% |
| **Earthworks** | | 11 | 26-Oct-26 | 07-Nov-26 | 1,036,317 | 1,036,317 | 0 | 0 | 100% | 0% |
| **Earthworks** | | 11 | 26-Oct-26 | 07-Nov-26 | 1,036,317 | 1,036,317 | 0 | 0 | 100% | 0% |
| CO-EW-230 | Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-3 | 11 | 26-Oct-26 | 07-Nov-26 | 1,036,317 | 1,036,317 | 0 | 0 | 100% | 0% |
| **Storm Drainage Network** | | 10 | 25-Nov-26 | 06-Dec-26 | 38,627 | 38,627 | 0 | 0 | 100% | 0% |

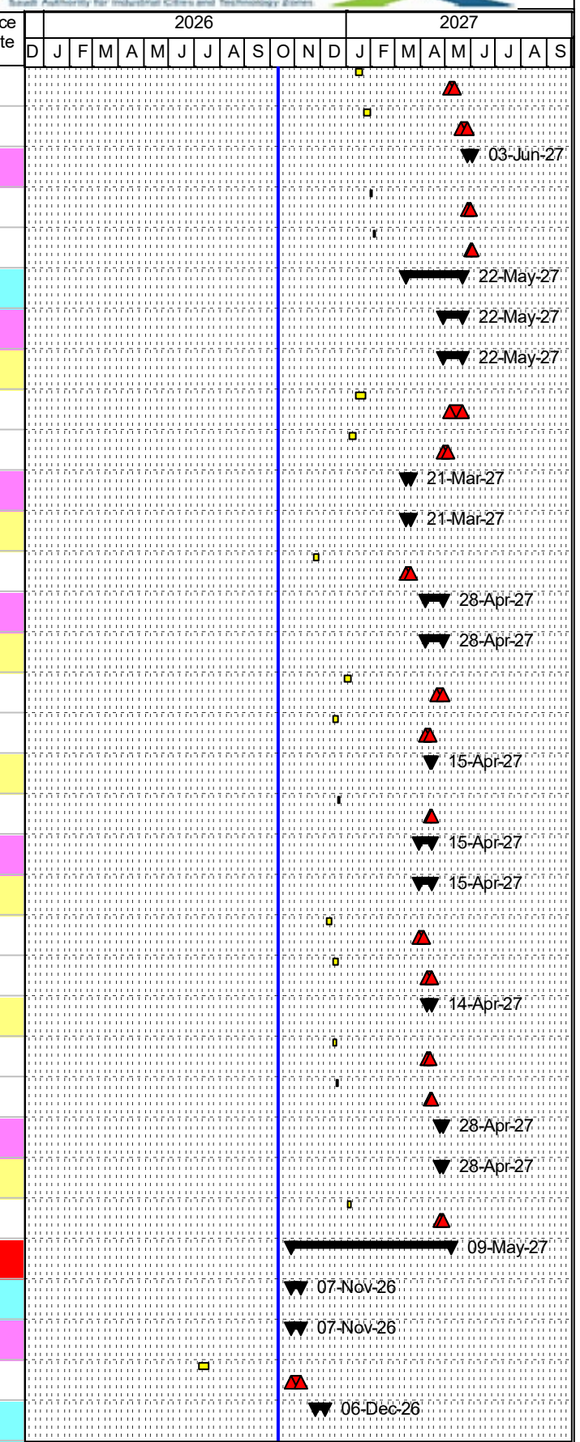



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Main Line Sections** | | 10 | 25-Nov-26 | 06-Dec-26 | 38,627 | 38,627 | 0 | 0 | 100% | 0% |
| CO-SD-ML-200 | Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for | 3 | 25-Nov-26 | 28-Nov-26 | 4,830 | 4,830 | 0 | 0 | 100% | 0% |
| CO-SD-ML-210 | Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-3 | 3 | 29-Nov-26 | 01-Dec-26 | 24,141 | 24,141 | 0 | 0 | 100% | 0% |
| CO-SD-ML-220 | Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for | 3 | 03-Dec-26 | 06-Dec-26 | 9,656 | 9,656 | 0 | 0 | 100% | 0% |
| **Treated Sewage Effluent (Tse)** | | 33 | 07-Dec-26 | 13-Jan-27 | 6,040 | 6,040 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-300 | Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse) | 11 | 07-Dec-26 | 19-Dec-26 | 755 | 755 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-310 | Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-3 | 11 | 20-Dec-26 | 31-Dec-26 | 3,775 | 3,775 | 0 | 0 | 100% | 0% |
| CO-TSE-ML-330 | Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for | 11 | 02-Jan-27 | 13-Jan-27 | 1,510 | 1,510 | 0 | 0 | 100% | 0% |
| **Potable Water Network** | | 32 | 14-Jan-27 | 20-Feb-27 | 53,061 | 3,394 | 0 | 0 | 6.4% | 0% |
| **Main Line Sections** | | 30 | 14-Jan-27 | 17-Feb-27 | 17,558 | 2,234 | 0 | 0 | 12.72% | 0% |
| CO-PW-ML-200 | Trench Excavation and Bedding Works for Main Lines of Potable Water Network for | 10 | 14-Jan-27 | 25-Jan-27 | 3,191 | 2,234 | 0 | 0 | 70% | 0% |
| CO-PW-ML-210 | Pipes Laying and accessories for Main Lines of Potable Water Network for | 10 | 26-Jan-27 | 06-Feb-27 | 7,981 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-ML-220 | Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for | 10 | 07-Feb-27 | 17-Feb-27 | 6,386 | 0 | 0 | 0 | 0% | 0% |
| **Valve Chamber** | | 32 | 14-Jan-27 | 20-Feb-27 | 26,509 | 1,160 | 0 | 0 | 4.38% | 0% |
| CO-PW-VC-290 | Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for | 10 | 14-Jan-27 | 25-Jan-27 | 1,657 | 1,160 | 0 | 0 | 70% | 0% |
| CO-PW-VC-300 | Installation Works for Valves of Potable Water Network for Alignment-RD-03-3 | 9 | 07-Feb-27 | 16-Feb-27 | 4,308 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC-310 | Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for | 3 | 17-Feb-27 | 20-Feb-27 | 3,314 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-VC210 | Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-3 | 10 | 26-Jan-27 | 06-Feb-27 | 17,231 | 0 | 0 | 0 | 0% | 0% |
| **Fire Hydrant** | | 22 | 26-Jan-27 | 20-Feb-27 | 8,994 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-230 | Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-3 | 10 | 26-Jan-27 | 06-Feb-27 | 562 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-240 | Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-3 | 10 | 07-Feb-27 | 17-Feb-27 | 7,308 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-FH-250 | Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for | 2 | 18-Feb-27 | 20-Feb-27 | 1,124 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 22 | 26-Jan-27 | 20-Feb-27 | 89,958 | 0 | 0 | 0 | 0% | 0% |
| **Main Line Pipes** | | 22 | 26-Jan-27 | 20-Feb-27 | 89,958 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-350 | Trench Excavation and Bedding Works for Main Lines of Irrigation Network for | 10 | 26-Jan-27 | 06-Feb-27 | 2,307 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-360 | Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-03-3 | 3 | 07-Feb-27 | 09-Feb-27 | 11,536 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-370 | Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-03-3 | 3 | 10-Feb-27 | 13-Feb-27 | 5,680 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-380 | Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for | 3 | 17-Feb-27 | 20-Feb-27 | 4,615 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-ML-390 | Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation | 3 | 14-Feb-27 | 16-Feb-27 | 65,819 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 12 | 27-Feb-27 | 15-Mar-27 | 2,657 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 12 | 27-Feb-27 | 15-Mar-27 | 2,657 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-340 | Trench Excavation and Bedding Works for Medium Voltage Network for | 3 | 27-Feb-27 | 01-Mar-27 | 617 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-350 | Duct Laying Works for Medium Voltage Network for Alignment-RD-03-3 | 3 | 06-Mar-27 | 08-Mar-27 | 1,402 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-ML-360 | Trench Backfilling and Compaction Works for Medium Voltage Network for | 3 | 13-Mar-27 | 15-Mar-27 | 637 | 0 | 0 | 0 | 0% | 0% |

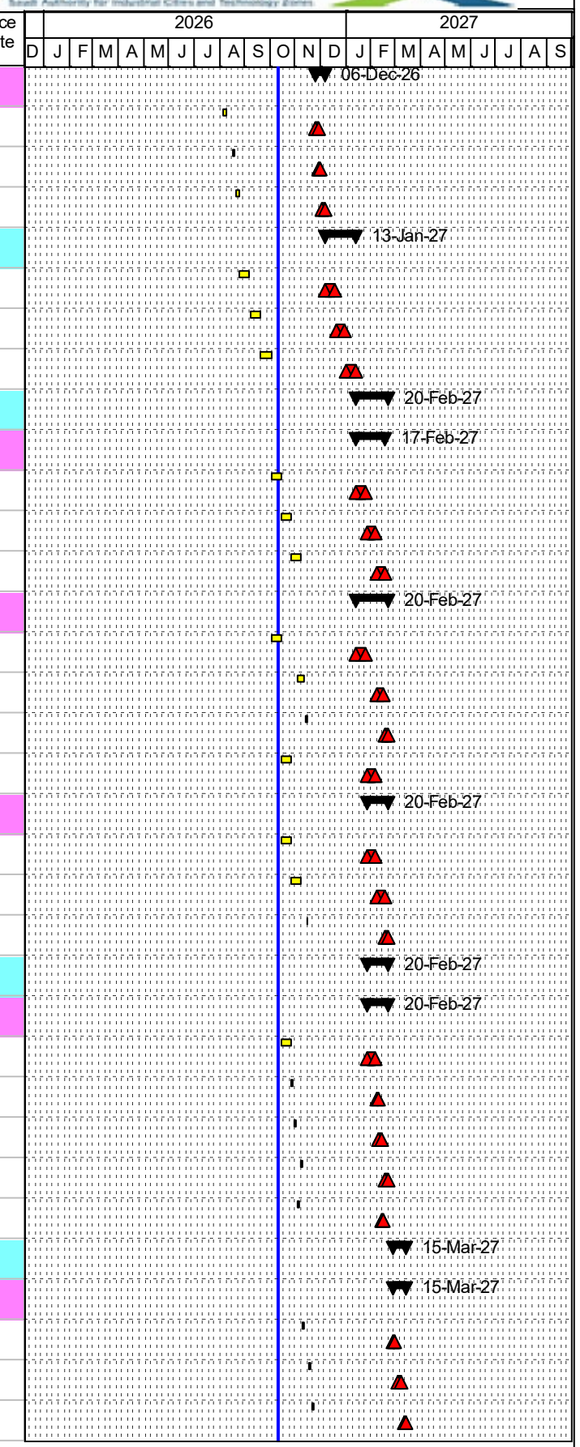



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Low Voltage Network** | | 28 | 16-Mar-27 | 17-Apr-27 | 40,657 | 0 | 0 | 0 | 0% | 0% |
| **Main Low Voltage Cables Works ( Cable 300 MM )** | | 18 | 16-Mar-27 | 05-Apr-27 | 21,013 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-190 | Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for | 7 | 16-Mar-27 | 23-Mar-27 | 4,104 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-200 | Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-3 | 7 | 24-Mar-27 | 31-Mar-27 | 11,622 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-ML-210 | Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for | 4 | 01-Apr-27 | 05-Apr-27 | 5,287 | 0 | 0 | 0 | 0% | 0% |
| **Service Low Voltage Cables Works ( Cable 70 MM )** | | 17 | 24-Mar-27 | 12-Apr-27 | 18,960 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-190 | Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for | 7 | 24-Mar-27 | 31-Mar-27 | 2,051 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-200 | Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-3 | 7 | 01-Apr-27 | 08-Apr-27 | 11,622 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-HC-210 | Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for | 3 | 10-Apr-27 | 12-Apr-27 | 5,287 | 0 | 0 | 0 | 0% | 0% |
| **Distribution Pillars Works** | | 4 | 13-Apr-27 | 17-Apr-27 | 684 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-DP-190 | Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-3 | 4 | 13-Apr-27 | 17-Apr-27 | 684 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 18 | 16-Mar-27 | 05-Apr-27 | 30,567 | 0 | 0 | 0 | 0% | 0% |
| **Lighting Poles Works** | | 18 | 16-Mar-27 | 05-Apr-27 | 12,586 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-450 | Installation Works for Lighting Poles Foundation of Street Lighting Network for | 6 | 16-Mar-27 | 22-Mar-27 | 2,697 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-460 | Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3 | 6 | 23-Mar-27 | 29-Mar-27 | 8,990 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-480 | Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3 | 6 | 30-Mar-27 | 05-Apr-27 | 899 | 0 | 0 | 0 | 0% | 0% |
| **Cabling Works** | | 6 | 30-Mar-27 | 05-Apr-27 | 17,981 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-350 | Cable Laying Works for Street Lighting Network for Alignment-RD-03-3 | 6 | 30-Mar-27 | 05-Apr-27 | 9,889 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-CL-360 | Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-3 | 6 | 30-Mar-27 | 05-Apr-27 | 8,091 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 26 | 25-Mar-27 | 24-Apr-27 | 232,186 | 0 | 0 | 0 | 0% | 0% |
| **Ducts Works** | | 10 | 13-Apr-27 | 24-Apr-27 | 28,472 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-230 | Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-3 | 6 | 13-Apr-27 | 19-Apr-27 | 19,575 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-DW-240 | Trench Backfilling and Compaction Works for Ducts of Telecom Network for | 4 | 20-Apr-27 | 24-Apr-27 | 8,898 | 0 | 0 | 0 | 0% | 0% |
| **Manholes Works** | | 8 | 25-Mar-27 | 03-Apr-27 | 14,687 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-230 | Excavation Works for Manholes of Telecom Network for Alignment-RD-03-3 | 2 | 25-Mar-27 | 27-Mar-27 | 979 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-240 | Installation Works for Manholes of Telecom Network for Alignment-RD-03-3 | 3 | 28-Mar-27 | 30-Mar-27 | 10,770 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-250 | Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-3 | 3 | 31-Mar-27 | 03-Apr-27 | 2,937 | 0 | 0 | 0 | 0% | 0% |
| **CCTV, Telephone, MSN, ACs System Works** | | 3 | 04-Apr-27 | 06-Apr-27 | 189,027 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-210 | Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-3 | 3 | 04-Apr-27 | 06-Apr-27 | 189,027 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 8 | 20-Apr-27 | 28-Apr-27 | 597,698 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 4 | 20-Apr-27 | 24-Apr-27 | 585,170 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-220 | Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-3 | 4 | 20-Apr-27 | 24-Apr-27 | 57,330 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-230 | Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-3 | 4 | 20-Apr-27 | 24-Apr-27 | 527,840 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 8 | 20-Apr-27 | 28-Apr-27 | 12,528 | 0 | 0 | 0 | 0% | 0% |

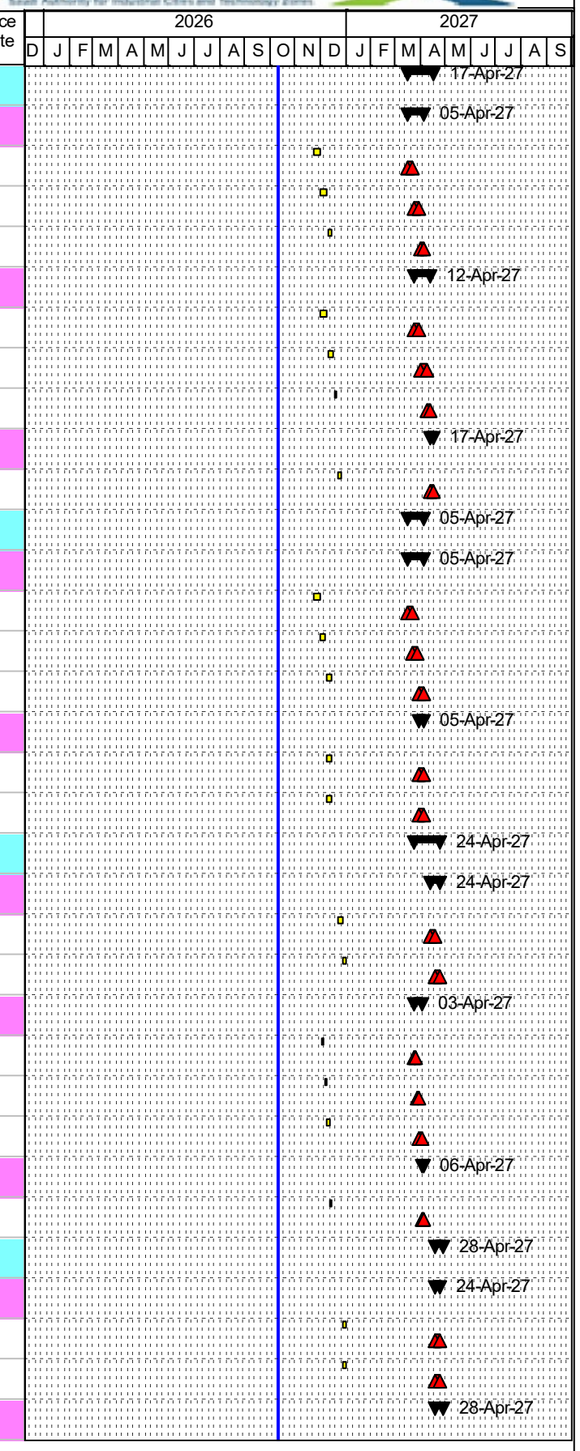



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-RD-F-RM-210 | Application of Road Marking Works For Road Works for Alignment-RD-03-3 | 3 | 20-Apr-27 | 22-Apr-27 | 7,795 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-150 | Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-3 | 4 | 25-Apr-27 | 28-Apr-27 | 4,734 | 0 | 0 | 0 | 0% | 0% |
| **Finishes for Infrastructure Networks** | | 47 | 16-Mar-27 | 09-May-27 | 117,812 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 5 | 22-Apr-27 | 27-Apr-27 | 9,656 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 5 | 22-Apr-27 | 27-Apr-27 | 9,656 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-ML-TF-130 | Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-3 | 5 | 22-Apr-27 | 27-Apr-27 | 9,656 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 7 | 13-Apr-27 | 20-Apr-27 | 23,243 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 7 | 13-Apr-27 | 20-Apr-27 | 23,243 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-190 | Testing of Potable Water Network for Alignment-RD-03-3 | 3 | 17-Apr-27 | 19-Apr-27 | 6,386 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-200 | Fire Hydrant Finishies (S.Box + Safety + Marker Post ) of Potable Water Network for | 3 | 13-Apr-27 | 15-Apr-27 | 2,249 | 0 | 0 | 0 | 0% | 0% |
| CO-PW-TF-210 | Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-3 | 4 | 17-Apr-27 | 20-Apr-27 | 14,609 | 0 | 0 | 0 | 0% | 0% |
| **Treated Sewage Effluent (Tse)** | | 6 | 03-May-27 | 09-May-27 | 1,510 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 03-May-27 | 09-May-27 | 1,510 | 0 | 0 | 0 | 0% | 0% |
| CO-TSE-TF-200 | Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-3 | 6 | 03-May-27 | 09-May-27 | 1,510 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 6 | 17-Apr-27 | 22-Apr-27 | 4,615 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 6 | 17-Apr-27 | 22-Apr-27 | 4,615 | 0 | 0 | 0 | 0% | 0% |
| CO-IR-TF-210 | Final Testing (pressure tests) of Irrigation Network for Alignment-RD-03-3 | 6 | 17-Apr-27 | 22-Apr-27 | 4,615 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 6 | 16-Mar-27 | 22-Mar-27 | 510 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 6 | 16-Mar-27 | 22-Mar-27 | 510 | 0 | 0 | 0 | 0% | 0% |
| CO-MV-TF-250 | Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-3 | 6 | 16-Mar-27 | 22-Mar-27 | 510 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 6 | 18-Apr-27 | 24-Apr-27 | 8,454 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 6 | 18-Apr-27 | 24-Apr-27 | 8,454 | 0 | 0 | 0 | 0% | 0% |
| CON-LV-TT-160 | Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage | 6 | 18-Apr-27 | 24-Apr-27 | 8,454 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 17 | 13-Apr-27 | 02-May-27 | 12,457 | 0 | 0 | 0 | 0% | 0% |
| **Termination and Testing Works** | | 17 | 13-Apr-27 | 02-May-27 | 11,254 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-LP-470 | Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for | 6 | 13-Apr-27 | 19-Apr-27 | 5,860 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-TF-490 | Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3 | 6 | 26-Apr-27 | 02-May-27 | 5,394 | 0 | 0 | 0 | 0% | 0% |
| **Earthing System Works** | | 11 | 13-Apr-27 | 25-Apr-27 | 1,203 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-280 | Install Earthing System Works for Lighting Poles of Street Lighting Network for | 6 | 13-Apr-27 | 19-Apr-27 | 601 | 0 | 0 | 0 | 0% | 0% |
| CO-SL-ES-290 | Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for | 6 | 19-Apr-27 | 25-Apr-27 | 601 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 12 | 08-Apr-27 | 21-Apr-27 | 57,368 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Finishes** | | 12 | 08-Apr-27 | 21-Apr-27 | 57,368 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-260 | Testing and Interface modules with Telecom for Alignment-RD-03-3 | 6 | 08-Apr-27 | 14-Apr-27 | 12,014 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-340 | Testing and Interface modules with CCTV, Telephone, MSN and Access Control for | 6 | 15-Apr-27 | 21-Apr-27 | 45,355 | 0 | 0 | 0 | 0% | 0% |

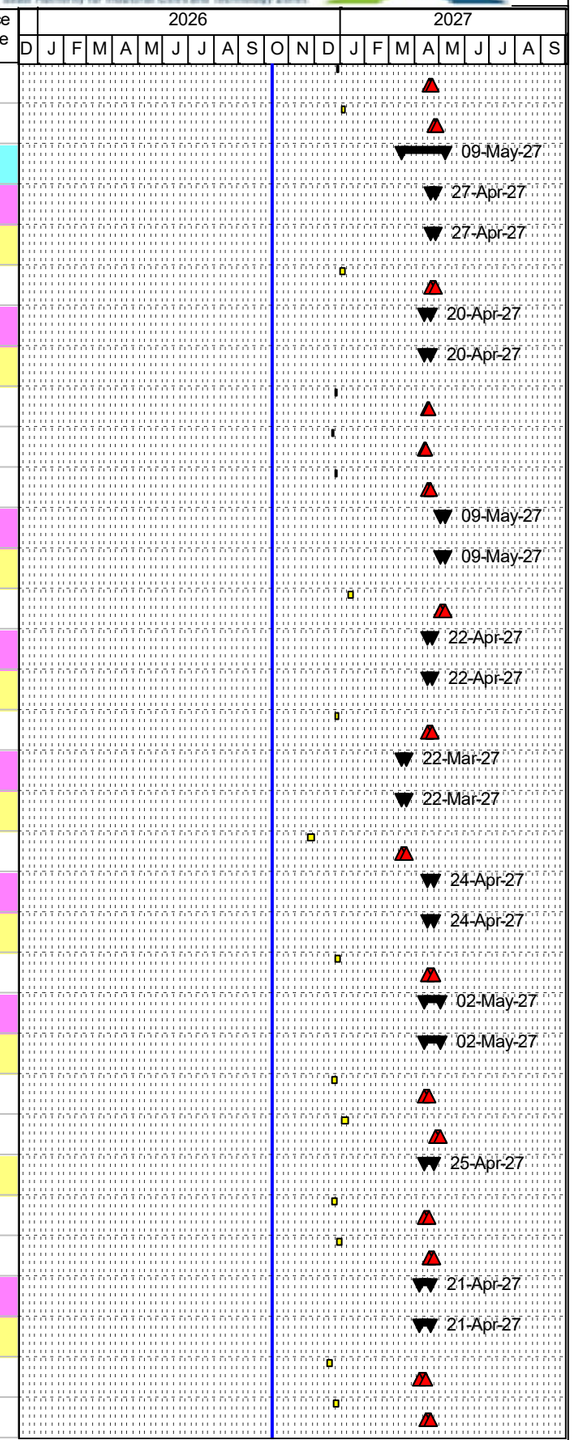



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **External** | | 328 | 01-Apr-26 A | 27-Apr-27 | 25,187,577 | 13,332,912 | 10,480,369 | 7,646,117 | 52.93% | 41.61% |
| **External Road - 1 - 1** | | 327 | 01-Apr-26 A | 26-Apr-27 | 5,221,714 | 3,247,135 | 2,608,226 | 1,170,237 | 62.19% | 49.95% |
| **Earthworks** | | 216 | 01-Apr-26 A | 14-Dec-26 | 3,247,135 | 3,247,135 | 2,608,226 | 1,170,237 | 100% | 80.32% |
| **Earthworks** | | 216 | 01-Apr-26 A | 14-Dec-26 | 3,247,135 | 3,247,135 | 2,608,226 | 1,170,237 | 100% | 80.32% |
| CO-EW-250 | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 - | 67 | 01-Apr-26 A | 22-Jun-26 A | 1,170,237 | 2,608,226 | 2,608,226 | 1,170,237 | 100% | 100% |
| CO-EW-250_R | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 - | 8 | 06-Dec-26 | 14-Dec-26 | 2,076,898 | 638,908 | 0 | 0 | 100% | 0% |
| **Road Works** | | 38 | 14-Mar-27 | 26-Apr-27 | 1,974,580 | 0 | 0 | 0 | 0% | 0% |
| **Road 01** | | 38 | 14-Mar-27 | 26-Apr-27 | 1,974,580 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 17 | 14-Mar-27 | 01-Apr-27 | 532,798 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-240 | Subgrade Layer for Road Works for External Road - 1 - 1 | 8 | 14-Mar-27 | 22-Mar-27 | 259,905 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-250 | Aggregate Base Course Layer for Road Works for External Road - 1 - 1 | 9 | 23-Mar-27 | 01-Apr-27 | 272,894 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 8 | 03-Apr-27 | 11-Apr-27 | 1,102,685 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-260 | Bituminous Base Courses Layers for Road Works for External Road - 1 - 1 | 4 | 03-Apr-27 | 06-Apr-27 | 548,740 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-250 | Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1 | 4 | 07-Apr-27 | 11-Apr-27 | 553,945 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 14 | 07-Apr-27 | 22-Apr-27 | 301,042 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-260 | Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 1 | 8 | 07-Apr-27 | 15-Apr-27 | 183,454 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-270 | Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 1 | 6 | 17-Apr-27 | 22-Apr-27 | 117,588 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 3 | 24-Apr-27 | 26-Apr-27 | 38,054 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-230 | Application of Road Marking Works For Road Works for External Road - 1 - 1 | 2 | 24-Apr-27 | 25-Apr-27 | 24,799 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-170 | Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 1 | 1 | 26-Apr-27 | 26-Apr-27 | 13,255 | 0 | 0 | 0 | 0% | 0% |
| **External Road - 1 - 2** | | 314 | 18-Apr-26 A | 27-Apr-27 | 7,651,591 | 4,767,067 | 1,790,191 | 1,214,285 | 62.3% | 23.4% |
| **Earthworks** | | 195 | 18-Apr-26 A | 04-Jan-27 | 4,767,067 | 4,767,067 | 1,790,191 | 1,214,285 | 100% | 37.55% |
| **Earthworks** | | 195 | 18-Apr-26 A | 04-Jan-27 | 4,767,067 | 4,767,067 | 1,790,191 | 1,214,285 | 100% | 37.55% |
| CO-EW-280 | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 - | 53 | 18-Apr-26 A | 22-Jun-26 A | 622,155 | 622,155 | 622,155 | 622,155 | 100% | 100% |
| CO-EW-280_R | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 - | 21 | 26-Sep-26 A | 04-Jan-27 | 4,144,912 | 4,144,912 | 1,168,036 | 592,130 | 100% | 28.18% |
| **Road Works** | | 39 | 14-Mar-27 | 27-Apr-27 | 2,884,524 | 0 | 0 | 0 | 0% | 0% |
| **Road 01** | | 39 | 14-Mar-27 | 27-Apr-27 | 2,884,524 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 12 | 14-Mar-27 | 27-Mar-27 | 778,172 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-300 | Subgrade Layer for Road Works for External Road - 1 - 2 | 6 | 14-Mar-27 | 20-Mar-27 | 379,600 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-310 | Aggregate Base Course Layer for Road Works for External Road - 1 - 2 | 6 | 21-Mar-27 | 27-Mar-27 | 398,572 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 11 | 28-Mar-27 | 08-Apr-27 | 1,610,525 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-320 | Bituminous Base Courses Layers for Road Works for External Road - 1 - 2 | 7 | 28-Mar-27 | 04-Apr-27 | 801,462 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-310 | Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1 | 4 | 05-Apr-27 | 08-Apr-27 | 809,064 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 12 | 06-Apr-27 | 19-Apr-27 | 439,683 | 0 | 0 | 0 | 0% | 0% |

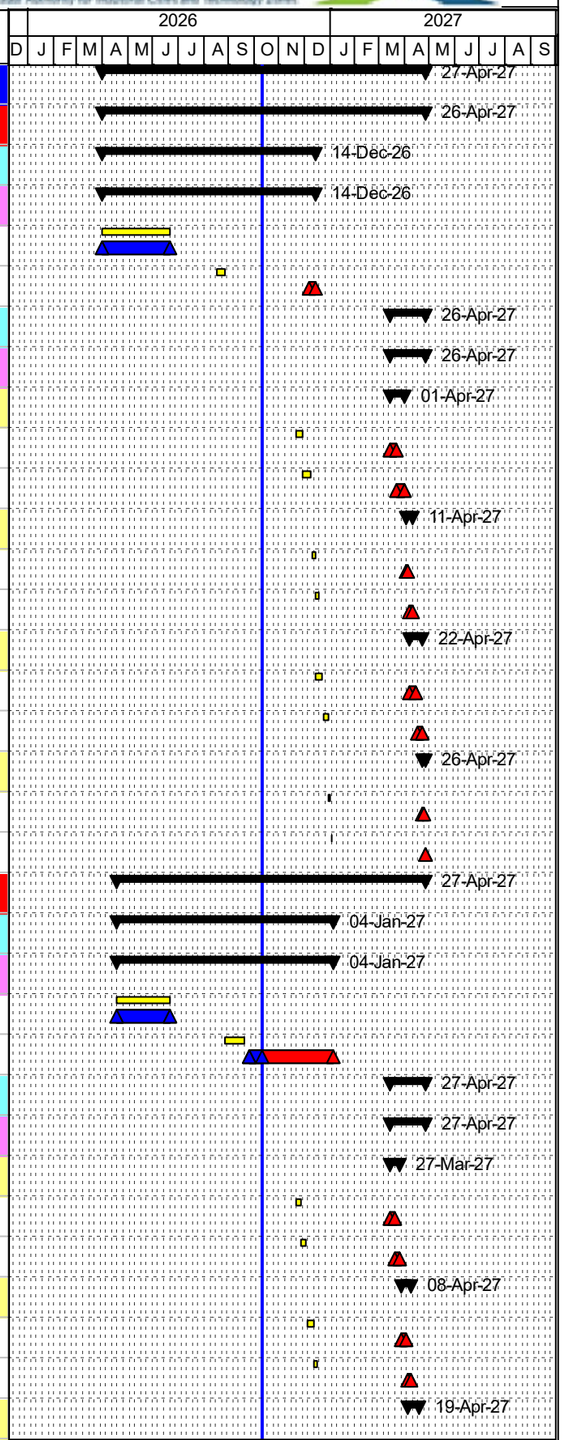



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-RD-PV-320 | Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 2 | 6 | 06-Apr-27 | 12-Apr-27 | 267,941 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-330 | Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 2 | 6 | 13-Apr-27 | 19-Apr-27 | 171,741 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 7 | 20-Apr-27 | 27-Apr-27 | 56,143 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-260 | Application of Road Marking Works For Road Works for External Road - 1 - 2 | 4 | 20-Apr-27 | 24-Apr-27 | 36,261 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-200 | Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 2 | 3 | 25-Apr-27 | 27-Apr-27 | 19,882 | 0 | 0 | 0 | 0% | 0% |
| **External Road - 2** | | 296 | 09-May-26 A | 27-Apr-27 | 3,781,297 | 2,348,995 | 1,330,763 | 212,860 | 62.12% | 35.19% |
| **Earthworks** | | 223 | 09-May-26 A | 28-Jan-27 | 2,348,995 | 2,348,995 | 1,330,763 | 212,860 | 100% | 56.65% |
| **Earthworks** | | 223 | 09-May-26 A | 28-Jan-27 | 2,348,995 | 2,348,995 | 1,330,763 | 212,860 | 100% | 56.65% |
| CO-EW-260 | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - | 35 | 09-May-26 A | 22-Jun-26 A | 212,860 | 1,330,763 | 1,330,763 | 212,860 | 100% | 100% |
| CO-EW-260_R | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - | 21 | 05-Jan-27 | 28-Jan-27 | 2,136,135 | 1,018,232 | 0 | 0 | 80.95% | 0% |
| **Road Works** | | 45 | 03-Mar-27 | 27-Apr-27 | 1,432,302 | 0 | 0 | 0 | 0% | 0% |
| **Road 01** | | 45 | 03-Mar-27 | 27-Apr-27 | 1,432,302 | 0 | 0 | 0 | 0% | 0% |
| **Pre-Bituminous Construction** | | 7 | 03-Mar-27 | 14-Mar-27 | 386,518 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-260 | Subgrade Layer for Road Works for External Road - 2 | 7 | 03-Mar-27 | 14-Mar-27 | 188,547 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PB-270 | Aggregate Base Course Layer for Road Works for External Road - 2 | 4 | 07-Mar-27 | 14-Mar-27 | 197,971 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 20 | 15-Mar-27 | 06-Apr-27 | 799,946 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-280 | Bituminous Base Courses Layers for Road Works for External Road - 2 | 10 | 15-Mar-27 | 25-Mar-27 | 398,085 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-270 | Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 2 | 10 | 27-Mar-27 | 06-Apr-27 | 401,861 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 9 | 06-Apr-27 | 15-Apr-27 | 218,390 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-280 | Fixing of Curbstone for Sidewalks Pavement for External Road - 2 | 9 | 06-Apr-27 | 15-Apr-27 | 133,086 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-290 | Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 2 | 9 | 06-Apr-27 | 15-Apr-27 | 85,304 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 10 | 17-Apr-27 | 27-Apr-27 | 27,448 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-240 | Application of Road Marking Works For Road Works for External Road - 2 | 10 | 17-Apr-27 | 27-Apr-27 | 17,980 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-180 | Installation Works of Traffic Signs Boards For Road Works for External Road - 2 | 2 | 19-Apr-27 | 20-Apr-27 | 9,468 | 0 | 0 | 0 | 0% | 0% |
| **External Road - 3** | | 296 | 09-May-26 A | 27-Apr-27 | 8,532,974 | 2,969,716 | 4,751,189 | 5,048,735 | 34.8% | 55.68% |
| **Earthworks** | | 219 | 09-May-26 A | 06-Feb-27 | 5,285,229 | 2,968,746 | 4,540,017 | 4,837,557 | 56.17% | 85.9% |
| **Earthworks** | | 219 | 09-May-26 A | 06-Feb-27 | 5,285,229 | 2,968,746 | 4,540,017 | 4,837,557 | 56.17% | 85.9% |
| CO-EW-270 | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - | 35 | 09-May-26 A | 22-Jun-26 A | 2,968,746 | 2,968,746 | 2,968,746 | 2,968,746 | 100% | 100% |
| CO-EW-270_R | Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - | 21 | 23-Aug-26 A | 06-Feb-27 | 2,316,484 | 0 | 1,571,271 | 1,868,812 | 0% | 67.83% |
| **Telecom and Light Current Network** | | 43 | 19-Jan-27 | 13-Mar-27 | 38,794 | 970 | 0 | 0 | 2.5% | 0% |
| **Manholes Works** | | 37 | 19-Jan-27 | 02-Mar-27 | 29,095 | 970 | 0 | 0 | 3.33% | 0% |
| CO-TE-MH-290 | Excavation Works for Manholes of Telecom Network for External Road - 3 | 18 | 19-Jan-27 | 08-Feb-27 | 1,940 | 970 | 0 | 0 | 50% | 0% |
| CO-TE-MH-300 | Installation Works for Manholes of Telecom Network for External Road - 3 | 19 | 09-Feb-27 | 02-Mar-27 | 21,337 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-MH-310 | Backfilling Works for Manholes of Telecom Network for External Road - 3 | 6 | 24-Feb-27 | 02-Mar-27 | 5,819 | 0 | 0 | 0 | 0% | 0% |

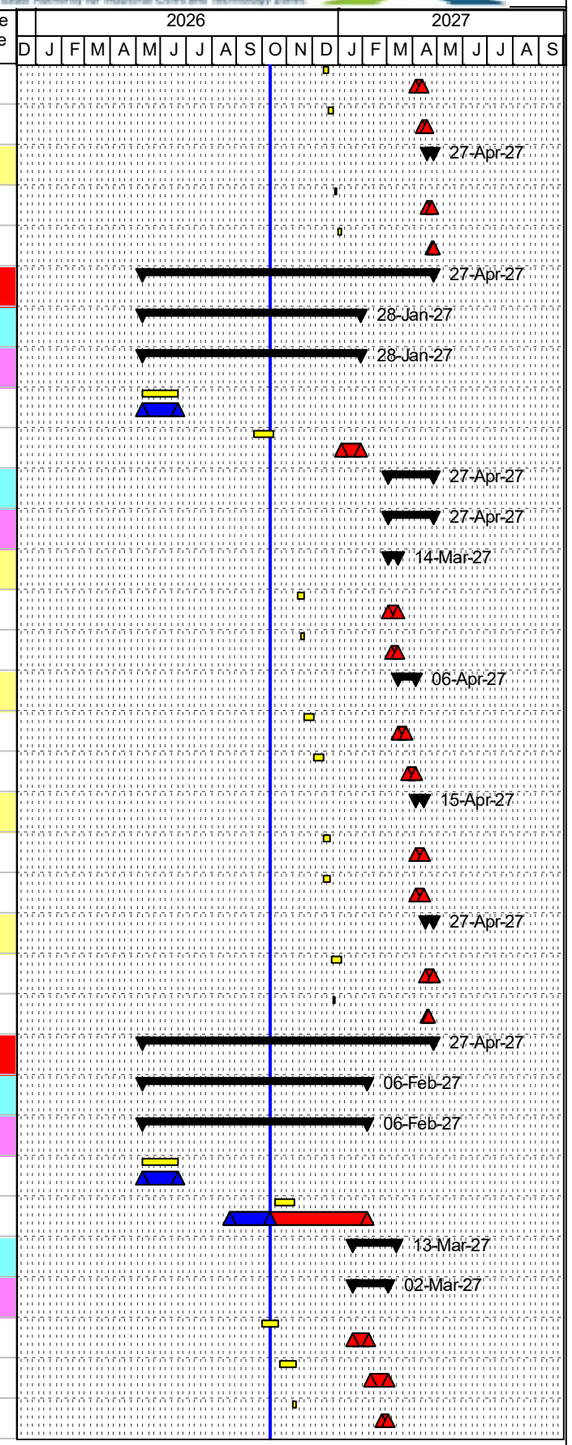



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Testing and Finishes** | | 6 | 03-Mar-27 | 13-Mar-27 | 9,698 | 0 | 0 | 0 | 0% | 0% |
| CO-TE-CTV-TF-360 | Testing and Interface modules with Telecom for External Road - 3 | 6 | 03-Mar-27 | 13-Mar-27 | 9,698 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 74 | 08-Sep-26 A | 27-Apr-27 | 3,208,951 | 0 | 211,172 | 211,178 | 0% | 6.58% |
| **Road 01** | | 74 | 08-Sep-26 A | 27-Apr-27 | 3,208,951 | 0 | 211,172 | 211,178 | 0% | 6.58% |
| **Pre-Bituminous Construction** | | 43 | 08-Sep-26 A | 22-Mar-27 | 865,798 | 0 | 211,172 | 211,178 | 0% | 24.39% |
| CO-RD-PB-280 | Subgrade Layer for Road Works for External Road - 3 | 6 | 08-Sep-26 A | 13-Mar-27 | 422,344 | 0 | 211,172 | 211,178 | 0% | 50% |
| CO-RD-PB-290 | Aggregate Base Course Layer for Road Works for External Road - 3 | 11 | 07-Mar-27 | 22-Mar-27 | 443,453 | 0 | 0 | 0 | 0% | 0% |
| **Bituminous Construction** | | 23 | 27-Mar-27 | 21-Apr-27 | 1,791,868 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-B-300 | Bituminous Base Courses Layers for Road Works for External Road - 3 | 12 | 27-Mar-27 | 08-Apr-27 | 891,705 | 0 | 0 | 0 | 0% | 0% |
| CON-RD-MR-290 | Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 3 | 11 | 10-Apr-27 | 21-Apr-27 | 900,163 | 0 | 0 | 0 | 0% | 0% |
| **Pavement Works** | | 3 | 17-Apr-27 | 19-Apr-27 | 489,192 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-300 | Fixing of Curbstone for Sidewalks Pavement for External Road - 3 | 3 | 17-Apr-27 | 19-Apr-27 | 298,112 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-PV-310 | Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 3 | 3 | 17-Apr-27 | 19-Apr-27 | 191,080 | 0 | 0 | 0 | 0% | 0% |
| **Traffic Signs Boards and Roads Marking** | | 5 | 22-Apr-27 | 27-Apr-27 | 62,093 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-RM-250 | Application of Road Marking Works For Road Works for External Road - 3 | 5 | 22-Apr-27 | 27-Apr-27 | 40,318 | 0 | 0 | 0 | 0% | 0% |
| CO-RD-F-TS-190 | Installation Works of Traffic Signs Boards For Road Works for External Road - 3 | 3 | 22-Apr-27 | 25-Apr-27 | 21,775 | 0 | 0 | 0 | 0% | 0% |
| **Superstructure Work** | | 214 | 01-Aug-26 A | 09-Jun-27 | 35,692,169 | 2,122,199 | 8,580,408 | 8,530,504 | 5.95% | 24.04% |
| **Utility Buildings** | | 214 | 29-Aug-26 A | 09-Jun-27 | 8,083,982 | 833,843 | 847,325 | 847,325 | 10.31% | 10.48% |
| **Water Pump Station** | | 214 | 15-Sep-26 A | 09-Jun-27 | 3,313,461 | 501,540 | 346,091 | 346,091 | 15.14% | 10.45% |
| **Civil work** | | 59 | 15-Sep-26 A | 01-Dec-26 | 445,078 | 445,078 | 346,091 | 346,091 | 100% | 77.76% |
| **SubStructure** | | 37 | 15-Sep-26 A | 01-Nov-26 | 318,456 | 318,456 | 314,735 | 314,735 | 100% | 98.83% |
| CO-UB-PS-100 | Excavation Work for Water Pump station building | 8 | 15-Sep-26 A | 17-Sep-26 A | 3,721 | 3,721 | 3,721 | 3,721 | 100% | 100% |
| CO-UB-PS-110 | pouring P.C Conceret for Water Pump station building | 2 | 19-Sep-26 A | 20-Sep-26 A | 296,132 | 296,132 | 296,132 | 296,132 | 100% | 100% |
| CO-UB-PS-120 | Formwork for Foundation for Water Pump station building | 7 | 26-Sep-26 A | 27-Sep-26 A | 3,721 | 3,721 | 3,721 | 3,721 | 100% | 100% |
| CO-UB-PS-130 | Steel fixing for Foundation for Water Pump station building | 6 | 27-Sep-26 A | 28-Sep-26 A | 3,721 | 3,721 | 3,721 | 3,721 | 100% | 100% |
| CO-UB-PS-140 | pouring for Foundation for Water Pump station building | 1 | 01-Oct-26 A | 03-Oct-26 A | 3,721 | 3,721 | 3,721 | 3,721 | 100% | 100% |
| CO-UB-PS-150 | curing and deshuttering formwork Pump station building | 7 | 06-Oct-26 A | 10-Oct-26 A | 3,721 | 3,721 | 3,721 | 3,721 | 100% | 100% |
| CO-UB-PS-160 | Backfilling and compaction work for pump station | 4 | 28-Oct-26 | 01-Nov-26 | 3,721 | 3,721 | 0 | 0 | 100% | 0% |
| **Super structure** | | 26 | 06-Oct-26 A | 01-Dec-26 | 126,623 | 126,623 | 31,356 | 31,356 | 100% | 24.76% |
| CO-UB-PS-170 | Formwork for Wall and columns for Water Pump station building | 5 | 06-Oct-26 A | 08-Oct-26 A | 10,452 | 10,452 | 10,452 | 10,452 | 100% | 100% |
| CO-UB-PS-180 | Steel fixing for Wall columns | 4 | 08-Oct-26 A | 10-Oct-26 A | 10,452 | 10,452 | 10,452 | 10,452 | 100% | 100% |
| CO-UB-PS-190 | pouring for Wall columns | 1 | 11-Oct-26 A | 12-Oct-26 A | 10,452 | 10,452 | 10,452 | 10,452 | 100% | 100% |
| CO-UB-PS-200 | curing and deshuttering formwork for Wall columns | 7 | 02-Nov-26 | 09-Nov-26 | 10,452 | 10,452 | 0 | 0 | 100% | 0% |
| CO-UB-PS-210 | Waterproofing for Walls columns | 2 | 10-Nov-26 | 11-Nov-26 | 10,452 | 10,452 | 0 | 0 | 100% | 0% |

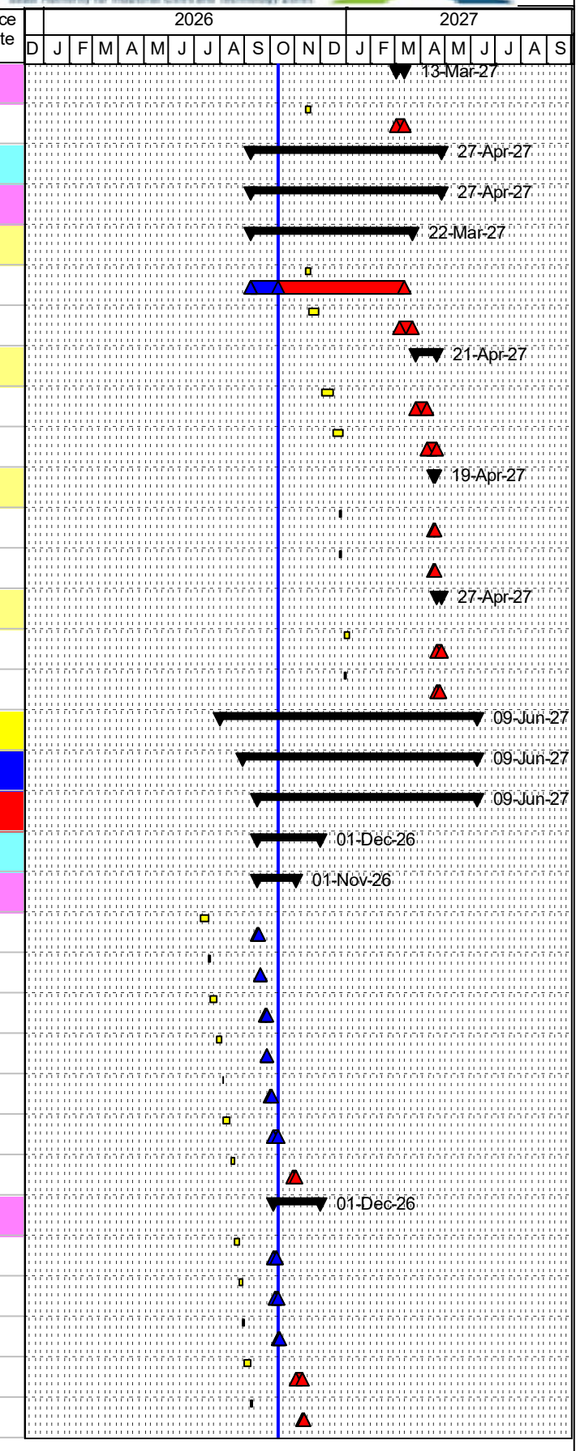



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-UB-PS-220 | Formwork for pump roof | 4 | 12-Nov-26 | 16-Nov-26 | 17,183 | 17,183 | 0 | 0 | 100% | 0% |
| CO-UB-PS-230 | Steel fixing for pump roof | 4 | 17-Nov-26 | 21-Nov-26 | 17,183 | 17,183 | 0 | 0 | 100% | 0% |
| CO-UB-PS-240 | pouring for pump roof | 2 | 22-Nov-26 | 23-Nov-26 | 17,183 | 17,183 | 0 | 0 | 100% | 0% |
| CO-UB-PS-250 | curing and deshuttering formwork for pump roof | 7 | 24-Nov-26 | 01-Dec-26 | 22,812 | 22,812 | 0 | 0 | 100% | 0% |
| **Architectural work** | | 30 | 02-Dec-26 | 05-Jan-27 | 152,986 | 56,462 | 0 | 0 | 36.91% | 0% |
| CO-UB-PS-260 | Executing Masonry Works for Water Pump station building | 7 | 02-Dec-26 | 09-Dec-26 | 44,161 | 44,161 | 0 | 0 | 100% | 0% |
| CO-UB-PS-270 | Executing Plastering Works for Pump station building | 7 | 10-Dec-26 | 17-Dec-26 | 43,051 | 12,300 | 0 | 0 | 28.57% | 0% |
| CO-UB-PS-280 | Executing Painting and Finishes Works for Pump station building | 8 | 19-Dec-26 | 27-Dec-26 | 55,593 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PS-320 | Doors and windows Fixing &Stair Tiles | 8 | 28-Dec-26 | 05-Jan-27 | 10,180 | 0 | 0 | 0 | 0% | 0% |
| **Mechanical work** | | 36 | 24-Apr-27 | 09-Jun-27 | 2,715,397 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PS-340 | Executing HVAC System for Water Pump station building | 10 | 24-Apr-27 | 04-May-27 | 88,142 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PS-360 | Executing Fire fighting institution works(piping and wire installation) for Water Pump station | 10 | 05-May-27 | 22-May-27 | 19,869 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PS-380 | Executing Plummbing works for Water Pump station building | 10 | 23-May-27 | 02-Jun-27 | 524,160 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PS-390 | Installation of pumps | 6 | 03-Jun-27 | 09-Jun-27 | 2,083,226 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Lift Station** | | 60 | 29-Aug-26 A | 06-Mar-27 | 564,483 | 0 | 228,618 | 228,618 | 0% | 40.5% |
| **Civil work** | | 60 | 29-Aug-26 A | 02-Mar-27 | 416,344 | 0 | 228,618 | 228,618 | 0% | 54.91% |
| **Sup Structure** | | 48 | 29-Aug-26 A | 10-Oct-26 A | 228,618 | 0 | 228,618 | 228,618 | 0% | 100% |
| CO-UB-LS-220 | Excavation Work for Sewage Lift Station | 9 | 29-Aug-26 A | 31-Aug-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| CO-UB-LS-230 | pouring P.C Conceret for Sewage Lift Station | 2 | 01-Sep-26 A | 02-Sep-26 A | 20,627 | 0 | 20,627 | 20,627 | 0% | 100% |
| CO-UB-LS-240 | Formwork for Foundation for Sewage Lift Station | 12 | 03-Sep-26 A | 03-Oct-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| CO-UB-LS-250 | Steel fixing for Foundation for Sewage Lift Station | 10 | 03-Sep-26 A | 06-Oct-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| CO-UB-LS-260 | pouring for Foundationfor Sewage Lift Station | 2 | 03-Sep-26 A | 08-Oct-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| CO-UB-LS-270 | curing and deshuttering formwork for Sewage Lift Station | 7 | 03-Sep-26 A | 10-Oct-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| CO-UB-LS-280 | Backfilling and compaction work for Sewage Lift Station | 6 | 03-Sep-26 A | 10-Oct-26 A | 34,665 | 0 | 34,665 | 34,665 | 0% | 100% |
| **Super structure** | | 56 | 28-Dec-26 | 02-Mar-27 | 187,726 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-290 | Formwork for Wall and columns for Sewage Lift Station | 10 | 28-Dec-26 | 07-Jan-27 | 14,769 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-300 | Steel fixing for Wall columns | 9 | 09-Jan-27 | 18-Jan-27 | 14,769 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-310 | pouring for Wall columns | 1 | 19-Jan-27 | 19-Jan-27 | 14,769 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-320 | curing and deshuttering formwork for Wall columns | 7 | 20-Jan-27 | 27-Jan-27 | 14,769 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-330 | Waterproofing for Walls columns | 4 | 28-Jan-27 | 01-Feb-27 | 14,769 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-340 | Formwork for pump roof | 6 | 02-Feb-27 | 08-Feb-27 | 24,170 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-350 | Steel fixing for pump roof | 6 | 09-Feb-27 | 15-Feb-27 | 24,170 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-360 | pouring for pump roof | 1 | 16-Feb-27 | 16-Feb-27 | 24,170 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-370 | curing and deshuttering formwork for pump roof | 12 | 17-Feb-27 | 02-Mar-27 | 41,368 | 0 | 0 | 0 | 0% | 0% |

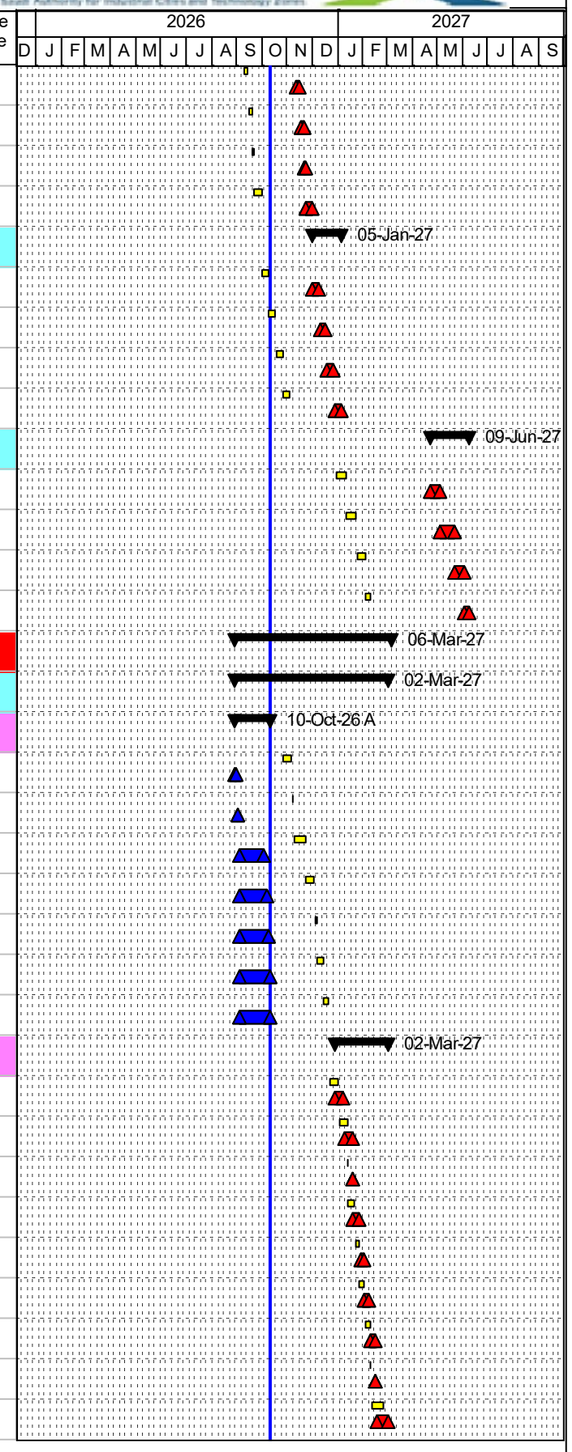



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **Architectural work** | | 3 | 03-Mar-27 | 06-Mar-27 | 148,139 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-LS-390 | Executing Plastering and Finishes Works for Sewage Lift Station | 3 | 03-Mar-27 | 06-Mar-27 | 148,139 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Tank** | | 77 | 19-Dec-26 | 21-Mar-27 | 314,972 | 0 | 0 | 0 | 0% | 0% |
| **Eearth Work** | | 22 | 19-Dec-26 | 12-Jan-27 | 99,522 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-100 | Excavation work for tank foundation tank formation level for Potable Water Tank | 12 | 19-Dec-26 | 31-Dec-26 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-110 | Soil replacement Up to tank formation level for Potable Water Tank | 10 | 02-Jan-27 | 12-Jan-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| **Structural Work** | | 41 | 13-Jan-27 | 01-Mar-27 | 168,191 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-120 | Plain Concrete works for Potable Water Tank | 7 | 13-Jan-27 | 20-Jan-27 | 18,908 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-130 | Form work for Tank Foundation for Potable Water Tank | 12 | 21-Jan-27 | 03-Feb-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-140 | Steel Reinforcement work for Tank Foundation for Potable Water Tank | 12 | 04-Feb-27 | 17-Feb-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-150 | Casting concrete for Tank Foundation for Potable Water Tank | 10 | 18-Feb-27 | 01-Mar-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| **Tank Shell Erection&Roof Installation** | | 14 | 02-Mar-27 | 21-Mar-27 | 47,259 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-PWT-170 | shell erection for Potable Water Tank | 14 | 02-Mar-27 | 21-Mar-27 | 47,259 | 0 | 0 | 0 | 0% | 0% |
| **IrrigationTank** | | 64 | 02-Jan-27 | 20-Mar-27 | 314,972 | 0 | 0 | 0 | 0% | 0% |
| **Eearth Work** | | 22 | 02-Jan-27 | 26-Jan-27 | 99,522 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-140 | Excavation work for tank foundation tank formation level for Irrigation Tank | 12 | 02-Jan-27 | 14-Jan-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-150 | Soil replacement Up to tank formation level for Irrigation Tank | 10 | 16-Jan-27 | 26-Jan-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| **Structural Work** | | 28 | 27-Jan-27 | 28-Feb-27 | 168,191 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-160 | Plain Concrete works for Irrigation Tank | 3 | 27-Jan-27 | 30-Jan-27 | 18,908 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-170 | Form work for Tank Foundation for Irrigation Tank | 10 | 31-Jan-27 | 10-Feb-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-180 | Steel Reinforcement work for Tank Foundation for Irrigation Tank | 11 | 11-Feb-27 | 23-Feb-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-190 | Casting concrete for Tank Foundation for Irrigation Tank | 4 | 24-Feb-27 | 28-Feb-27 | 49,761 | 0 | 0 | 0 | 0% | 0% |
| **Tank Shell Erection&Roof Installation** | | 14 | 01-Mar-27 | 20-Mar-27 | 47,259 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-IRT-210 | shell erection for Irrigation Tank | 14 | 01-Mar-27 | 20-Mar-27 | 47,259 | 0 | 0 | 0 | 0% | 0% |
| **Control Room** | | 138 | 03-Oct-26 A | 31-May-27 | 3,576,093 | 332,303 | 272,616 | 272,616 | 9.29% | 7.62% |
| **Civil Work** | | 43 | 03-Oct-26 A | 31-Jan-27 | 472,675 | 332,303 | 272,616 | 272,616 | 70.3% | 57.68% |
| CO-UB-CR-100 | Excavation Work For Control Room Foundation | 7 | 03-Oct-26 A | 04-Oct-26 A | 7,427 | 7,427 | 7,427 | 7,427 | 100% | 100% |
| CO-UB-CR-110 | Pouring for Plain Concrete | 5 | 05-Oct-26 A | 11-Oct-26 A | 265,188 | 265,188 | 265,188 | 265,188 | 100% | 100% |
| CO-UB-CR-120 | Pouring R.C Footing For Control Room | 21 | 13-Dec-26 | 05-Jan-27 | 7,427 | 7,427 | 0 | 0 | 100% | 0% |
| CO-UB-CR-130 | Pouring R.C Columns For Control Room | 12 | 06-Jan-27 | 19-Jan-27 | 78,391 | 52,260 | 0 | 0 | 66.67% | 0% |
| CO-UB-CR-140 | Pouring Beams and Slab For Control Room | 10 | 20-Jan-27 | 31-Jan-27 | 114,241 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 95 | 01-Feb-27 | 31-May-27 | 3,103,418 | 0 | 0 | 0 | 0% | 0% |
| **Architictural work** | | 42 | 01-Feb-27 | 24-Mar-27 | 362,218 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-150 | Brick Work For Control Room | 10 | 01-Feb-27 | 11-Feb-27 | 99,292 | 0 | 0 | 0 | 0% | 0% |

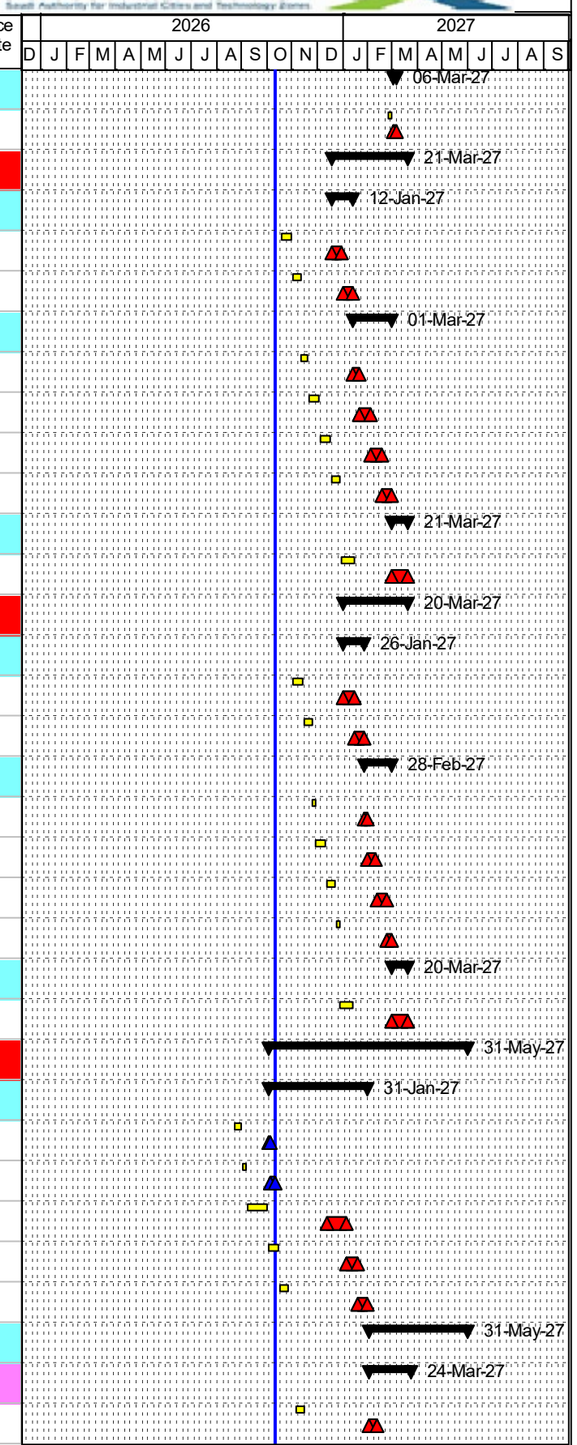



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-UB-CR-160 | Thermal & Moisture Protection Work for Control Room | 7 | 13-Feb-27 | 20-Feb-27 | 21,971 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-200 | Install For Curtian Wall and Windows and Doors | 7 | 21-Feb-27 | 28-Feb-27 | 91,926 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-240 | External Finshing Work (Walls and Floor) | 8 | 01-Mar-27 | 13-Mar-27 | 127,277 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-250 | Internal Finshing Work (Walls,Floor and Ceiling) | 10 | 14-Mar-27 | 24-Mar-27 | 21,751 | 0 | 0 | 0 | 0% | 0% |
| **Mechanical Work** | | 72 | 13-Feb-27 | 10-May-27 | 1,331,986 | 0 | 0 | 0 | 0% | 0% |
| **HVAC System** | | 72 | 13-Feb-27 | 10-May-27 | 137,139 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-170 | Install of Refrigerant Piping ( fabricated metal ducts with flanges complete with supports, | 21 | 13-Feb-27 | 08-Mar-27 | 68,570 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-260 | Install of Mini split actual and Ducted split | 20 | 25-Mar-27 | 17-Apr-27 | 30,178 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-310 | Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm | 20 | 18-Apr-27 | 10-May-27 | 38,392 | 0 | 0 | 0 | 0% | 0% |
| **Fire Fitting System** | | 17 | 13-Mar-27 | 31-Mar-27 | 434,599 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-180 | Installation & Testing of 2 hours Fire rated system for closing the openings between | 10 | 13-Mar-27 | 23-Mar-27 | 405,466 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-270 | Install Fire Extinguishers | 6 | 25-Mar-27 | 31-Mar-27 | 29,133 | 0 | 0 | 0 | 0% | 0% |
| **Plumbing System** | | 12 | 25-Mar-27 | 07-Apr-27 | 760,248 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-370 | Install of Sanitary Wares Including Relevant Pipes and Fittings | 12 | 25-Mar-27 | 07-Apr-27 | 760,248 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 47 | 25-Mar-27 | 24-May-27 | 965,706 | 0 | 0 | 0 | 0% | 0% |
| **LV Power** | | 43 | 25-Mar-27 | 13-May-27 | 874,883 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-190 | Install of Distribution board For Control Room | 10 | 25-Mar-27 | 05-Apr-27 | 87,096 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-220 | Install of Earting Cable for Control Room | 14 | 06-Apr-27 | 21-Apr-27 | 190,403 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-280 | Install of Socket outlet and LED Lighting | 19 | 22-Apr-27 | 13-May-27 | 597,384 | 0 | 0 | 0 | 0% | 0% |
| **Fire Detection And Alarm System** | | 35 | 08-Apr-27 | 24-May-27 | 90,824 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-210 | Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring | 4 | 08-Apr-27 | 12-Apr-27 | 35,785 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-230 | Install of Transmission Communication cable - Fiber Optics 12Core | 4 | 13-Apr-27 | 17-Apr-27 | 17,975 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-290 | Install of power supply system for fire alarm control panel | 4 | 18-Apr-27 | 21-Apr-27 | 11,246 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-300 | Install of Fire Alarm Control panel | 6 | 22-Apr-27 | 28-Apr-27 | 16,024 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-320 | Installation of the addressable manual call point with operation safety glass breaking | 3 | 29-Apr-27 | 02-May-27 | 243 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-330 | Install of the photoelectric heat & smoke detector | 5 | 03-May-27 | 08-May-27 | 4,229 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-340 | Install of Sounder With Beacon | 5 | 09-May-27 | 13-May-27 | 1,190 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-350 | Install of Addressable Control module | 4 | 20-May-27 | 24-May-27 | 4,131 | 0 | 0 | 0 | 0% | 0% |
| **Furnitures work** | | 6 | 25-May-27 | 31-May-27 | 443,507 | 0 | 0 | 0 | 0% | 0% |
| CO-UB-CR-360 | Office Chairs,Tables and Stand | 6 | 25-May-27 | 31-May-27 | 443,507 | 0 | 0 | 0 | 0% | 0% |
| **Softscape and Planting Works** | | 35 | 17-Apr-27 | 01-Jun-27 | 3,915,193 | 0 | 0 | 0 | 0% | 0% |
| CO-LS-PL-160 | Planting Works: Planting including plants, forming planting beds, suitable soil, supports, | 15 | 17-Apr-27 | 03-May-27 | 2,361,373 | 0 | 0 | 0 | 0% | 0% |
| CO-LS-SF-170 | Site Furnishings (Seating Bench,Stone Boulders and Gravel) | 20 | 04-May-27 | 01-Jun-27 | 1,553,820 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Ponds** | | 49 | 01-Oct-26 A | 21-Apr-27 | 8,820,044 | 0 | 3,969,020 | 3,969,053 | 0% | 45% |

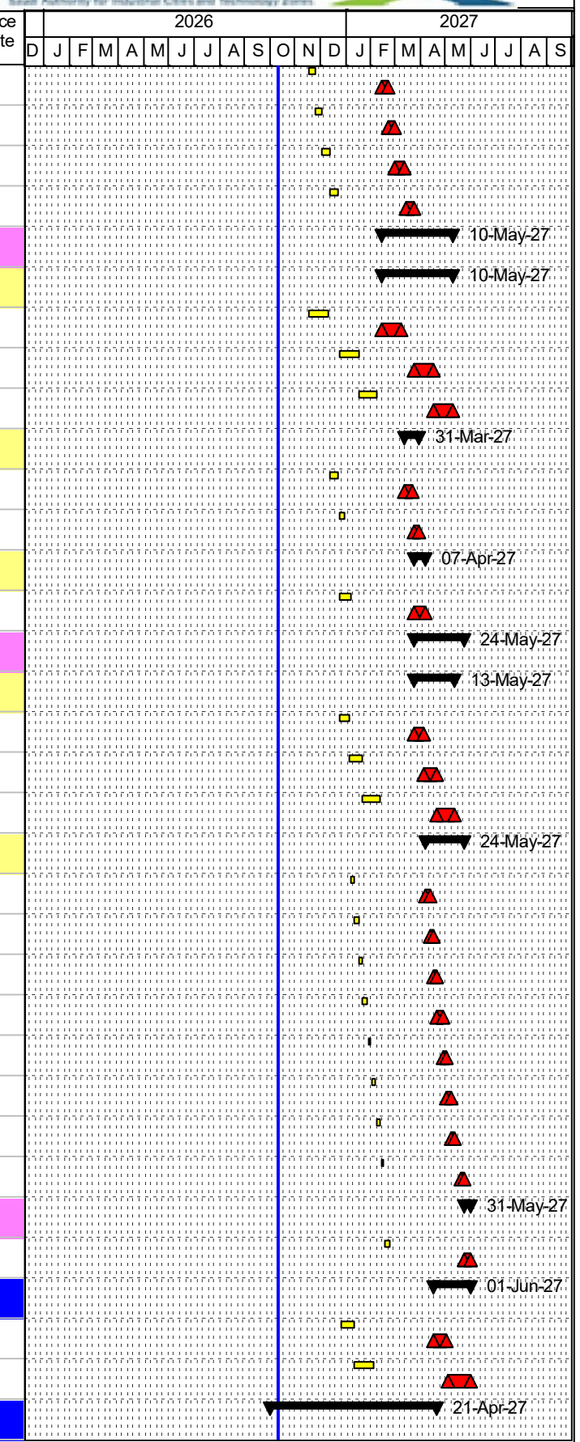



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-SD-PO-100-P1 | Excavation & Filling Works - PART 1 for Storm Drainage Ponds | 7 | 01-Oct-26 A | 28-Feb-27 | 4,093,463 | 0 | 3,684,116 | 3,684,116 | 0% | 90% |
| CO-SD-PO-100-P2 | Excavation & Filling Works - PART 2 for Storm Drainage Ponds | 17 | 14-Mar-27 | 01-Apr-27 | 4,093,463 | 0 | 0 | 0 | 0% | 0% |
| CO-SD-PO-110-P1 | Finished Grouted Riprap - PART 1 for Storm Drainage Ponds | 8 | 01-Mar-27 A | 13-Mar-27 | 316,560 | 0 | 284,904 | 284,937 | 0% | 90% |
| CO-SD-PO-110-P2 | Finished Grouted Riprap - PART 2 for Storm Drainage Ponds | 17 | 03-Apr-27 | 21-Apr-27 | 316,560 | 0 | 0 | 0 | 0% | 0% |
| **Boundary Fence and Gaurd Room** | | 180 | 01-Aug-26 A | 30-May-27 | 14,872,949 | 1,288,356 | 3,764,063 | 3,714,126 | 8.66% | 25.31% |
| **Gaurd Room Work** | | 44 | 04-Apr-27 | 30-May-27 | 1,497,270 | 0 | 0 | 0 | 0% | 0% |
| **Civil Work** | | 15 | 04-Apr-27 | 20-Apr-27 | 67,559 | 0 | 0 | 0 | 0% | 0% |
| A1000 | Excavation Work For Guard Room Foundation | 5 | 04-Apr-27 | 08-Apr-27 | 2,684 | 0 | 0 | 0 | 0% | 0% |
| A1010 | Pouring for Plain Concrete for Guard Room | 1 | 10-Apr-27 | 10-Apr-27 | 2,684 | 0 | 0 | 0 | 0% | 0% |
| A1020 | Pouring R.C Footing for Guard Room | 3 | 11-Apr-27 | 13-Apr-27 | 10,083 | 0 | 0 | 0 | 0% | 0% |
| A1030 | Pouring R.C Columns for Guard Room | 3 | 14-Apr-27 | 17-Apr-27 | 3,675 | 0 | 0 | 0 | 0% | 0% |
| A1040 | Pouring Beams and Slab for Guard Room | 3 | 18-Apr-27 | 20-Apr-27 | 48,433 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 29 | 21-Apr-27 | 30-May-27 | 1,429,712 | 0 | 0 | 0 | 0% | 0% |
| **Architectural work** | | 27 | 21-Apr-27 | 27-May-27 | 915,197 | 0 | 0 | 0 | 0% | 0% |
| A1050 | Brick Works for Architectural Works for Guard Rooms | 6 | 21-Apr-27 | 27-Apr-27 | 21,591 | 0 | 0 | 0 | 0% | 0% |
| A1060 | Thermal & Moisture Protection Work for Architectural Works for Guard Rooms | 5 | 28-Apr-27 | 03-May-27 | 12,891 | 0 | 0 | 0 | 0% | 0% |
| A1070 | Installation of Windows and Doors for Architectural Works for Guard Rooms | 5 | 23-May-27 | 27-May-27 | 49,349 | 0 | 0 | 0 | 0% | 0% |
| A1080 | External Finshing Work (Walls and Floor) for Architectural Works for Guard Rooms | 2 | 10-May-27 | 11-May-27 | 109,603 | 0 | 0 | 0 | 0% | 0% |
| A1090 | Internal Finshing Work (Walls,Floor and Ceiling) for Architectural Works for Guard | 6 | 10-May-27 | 22-May-27 | 721,763 | 0 | 0 | 0 | 0% | 0% |
| **Mechanical Work** | | 8 | 04-May-27 | 12-May-27 | 157,994 | 0 | 0 | 0 | 0% | 0% |
| **Drainage System** | | 8 | 04-May-27 | 12-May-27 | 44,607 | 0 | 0 | 0 | 0% | 0% |
| A1110 | Installation of Sewage Piping System complete with joints, angles, reducer etc. for | 4 | 04-May-27 | 08-May-27 | 33,221 | 0 | 0 | 0 | 0% | 0% |
| A1120 | Installation of all Sanitary Ware for Drainage System for Guard Rooms | 4 | 09-May-27 | 12-May-27 | 11,386 | 0 | 0 | 0 | 0% | 0% |
| **Water Supply System** | | 8 | 04-May-27 | 12-May-27 | 51,133 | 0 | 0 | 0 | 0% | 0% |
| A1140 | Installation of Water Piping System complete with joints, angles, reducer etc. for Water | 3 | 04-May-27 | 06-May-27 | 13,381 | 0 | 0 | 0 | 0% | 0% |
| A1180 | Installation oF Water Supply Wares (Water Heater, Faucets, Etc..) for Water Supply | 2 | 08-May-27 | 09-May-27 | 12,899 | 0 | 0 | 0 | 0% | 0% |
| A1240 | Installation of water tanks for Water Supply System for Guard Rooms | 1 | 12-May-27 | 12-May-27 | 24,852 | 0 | 0 | 0 | 0% | 0% |
| **HVAC System** | | 3 | 04-May-27 | 06-May-27 | 11,367 | 0 | 0 | 0 | 0% | 0% |
| A1190 | Installation of AC Units for HVAC System for Guard Rooms | 1 | 06-May-27 | 06-May-27 | 4,142 | 0 | 0 | 0 | 0% | 0% |
| A1200 | Installation of AC Piping for HVAC System for Guard Rooms | 2 | 04-May-27 | 05-May-27 | 7,225 | 0 | 0 | 0 | 0% | 0% |
| **Fire Fighting System** | | 3 | 04-May-27 | 06-May-27 | 50,888 | 0 | 0 | 0 | 0% | 0% |
| A1220 | Installation & Testing of 2 hours Fire Fighting system for Fire Fighting System for Guard | 2 | 04-May-27 | 05-May-27 | 29,586 | 0 | 0 | 0 | 0% | 0% |
| A1230 | Installation of Fire Extinguishers for Fire Fighting System for Guard Rooms | 1 | 06-May-27 | 06-May-27 | 21,302 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 11 | 04-May-27 | 22-May-27 | 335,219 | 0 | 0 | 0 | 0% | 0% |

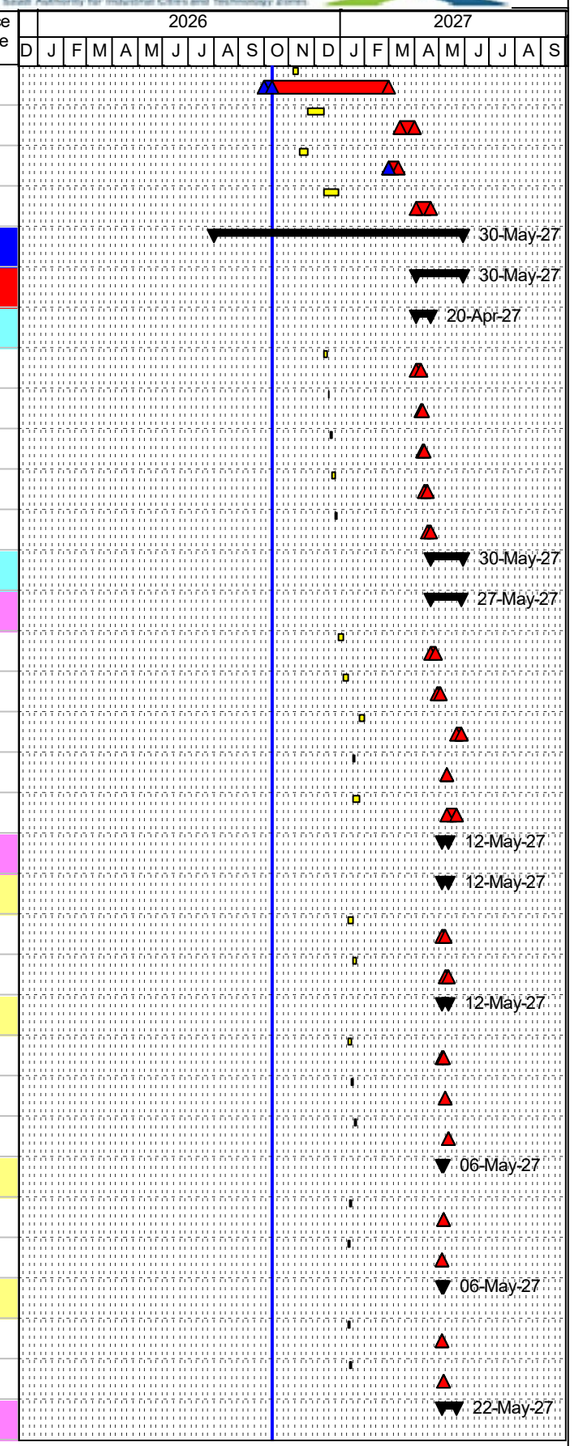



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| **LV Power** | | 9 | 04-May-27 | 13-May-27 | 107,021 | 0 | 0 | 0 | 0% | 0% |
| A1250 | Installation of Conduits and Cables for LV System for Gaurd Rooms | 5 | 04-May-27 | 09-May-27 | 58,313 | 0 | 0 | 0 | 0% | 0% |
| A1260 | Install of Eletrical Finishes (DBs, Sockets and Lightings) and Termination for LV System for | 4 | 10-May-27 | 13-May-27 | 48,708 | 0 | 0 | 0 | 0% | 0% |
| **Fire Detection And Alarm System** | | 11 | 04-May-27 | 22-May-27 | 228,198 | 0 | 0 | 0 | 0% | 0% |
| A1340 | Installation of Conduits and Cables for Fire Alarm System for Gaurd Rooms | 5 | 04-May-27 | 09-May-27 | 135,702 | 0 | 0 | 0 | 0% | 0% |
| A1350 | Installation of Fire Alarm Devices (AMCP, SD,HD, Sounder and Panels) for Fire Alarm | 6 | 10-May-27 | 22-May-27 | 92,496 | 0 | 0 | 0 | 0% | 0% |
| **Furniture work** | | 2 | 29-May-27 | 30-May-27 | 21,302 | 0 | 0 | 0 | 0% | 0% |
| A1100 | Office Chairs,Tables and Stand | 2 | 29-May-27 | 30-May-27 | 21,302 | 0 | 0 | 0 | 0% | 0% |
| **Boundary Fence** | | 171 | 01-Aug-26 A | 13-May-27 | 13,375,679 | 1,288,356 | 3,764,063 | 3,714,126 | 9.63% | 28.14% |
| **Boundary Fence - South** | | 132 | 01-Aug-26 A | 29-Mar-27 | 3,343,920 | 829,076 | 492,560 | 917,633 | 24.79% | 14.73% |
| **Civil Work** | | 55 | 01-Aug-26 A | 26-Dec-26 | 1,036,327 | 829,076 | 492,560 | 917,633 | 80% | 47.53% |
| CO-SU-FE-N-CI-100 | Excavation Work For Boundary Fence South | 16 | 01-Aug-26 A | 03-Aug-26 A | 66,380 | 66,380 | 66,380 | 66,380 | 100% | 100% |
| CO-SU-FE-N-CI-110 | Pouring for Plain Concrete For Boundary Fence South | 14 | 08-Aug-26 A | 13-Aug-26 A | 66,380 | 66,380 | 66,380 | 66,380 | 100% | 100% |
| CO-SU-FE-N-CI-120 | Pouring R.C Footing For Boundary Fence South | 12 | 15-Aug-26 A | 22-Aug-26 A | 312,570 | 312,570 | 312,570 | 312,570 | 100% | 100% |
| CO-SU-FE-N-CI-130 | Pouring R.C Columns For Boundary Fence South | 16 | 26-Sep-26 A | 13-Dec-26 | 472,304 | 383,747 | 47,230 | 472,304 | 81.25% | 10% |
| CO-SU-FE-N-CI-140 | Pouring Beams For Boundary Fence South | 12 | 13-Dec-26 | 26-Dec-26 | 118,694 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 77 | 27-Dec-26 | 29-Mar-27 | 2,307,593 | 0 | 0 | 0 | 0% | 0% |
| **Architictural work** | | 56 | 27-Dec-26 | 01-Mar-27 | 1,666,313 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-AR-100 | Install Brick Work For Boundary Fence South | 19 | 27-Dec-26 | 17-Jan-27 | 279,956 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-AR-110 | Insulation For Boundary Fence South | 15 | 02-Feb-27 | 18-Feb-27 | 109,999 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-AR-120 | Install all the Relevant Cladding and Finishes For Boundary Fence South | 9 | 20-Feb-27 | 01-Mar-27 | 1,276,358 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 58 | 18-Jan-27 | 29-Mar-27 | 641,279 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-240 | Installation of Conduits and Cables for Electricial Works For Boundary Fence South | 13 | 18-Jan-27 | 01-Feb-27 | 154,292 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-250 | Install, fixings, testing of all electrical finishes and lightings for Electricial Works For | 21 | 02-Mar-27 | 29-Mar-27 | 486,987 | 0 | 0 | 0 | 0% | 0% |
| **Boundary Fence - West** | | 125 | 01-Aug-26 A | 08-Apr-27 | 3,343,920 | 328,116 | 1,183,592 | 1,183,553 | 9.81% | 35.4% |
| **Civil Work** | | 51 | 01-Aug-26 A | 09-Jan-27 | 1,036,327 | 328,116 | 917,633 | 917,633 | 31.66% | 88.55% |
| CO-SU-FE-N-CI-150 | Excavation Work For Boundary Fence West | 16 | 01-Aug-26 A | 04-Aug-26 A | 66,380 | 66,380 | 66,380 | 66,380 | 100% | 100% |
| CO-SU-FE-N-CI-160 | Pouring for Plain Concrete For Boundary Fence West | 13 | 05-Aug-26 A | 10-Aug-26 A | 66,380 | 66,380 | 66,380 | 66,380 | 100% | 100% |
| CO-SU-FE-N-CI-170 | Pouring R.C Footing For Boundary Fence West | 16 | 11-Aug-26 A | 19-Aug-26 A | 312,570 | 195,356 | 312,570 | 312,570 | 62.5% | 100% |
| CO-SU-FE-N-CI-180 | Pouring R.C Columns For Boundary Fence West | 16 | 26-Sep-26 A | 12-Oct-26 A | 472,304 | 0 | 472,304 | 472,304 | 0% | 100% |
| CO-SU-FE-N-CI-190 | Pouring Beams For Boundary Fence West | 12 | 27-Dec-26 | 09-Jan-27 | 118,694 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 73 | 01-Oct-26 A | 08-Apr-27 | 2,307,593 | 0 | 265,958 | 265,919 | 0% | 11.53% |
| **Architictural work** | | 58 | 01-Oct-26 A | 22-Mar-27 | 1,666,313 | 0 | 265,958 | 265,919 | 0% | 15.96% |
| CO-SU-FE-N-AR-130 | Install Brick Work For Boundary Fence West | 16 | 01-Oct-26 A | 28-Jan-27 | 279,956 | 0 | 265,958 | 265,919 | 0% | 95% |

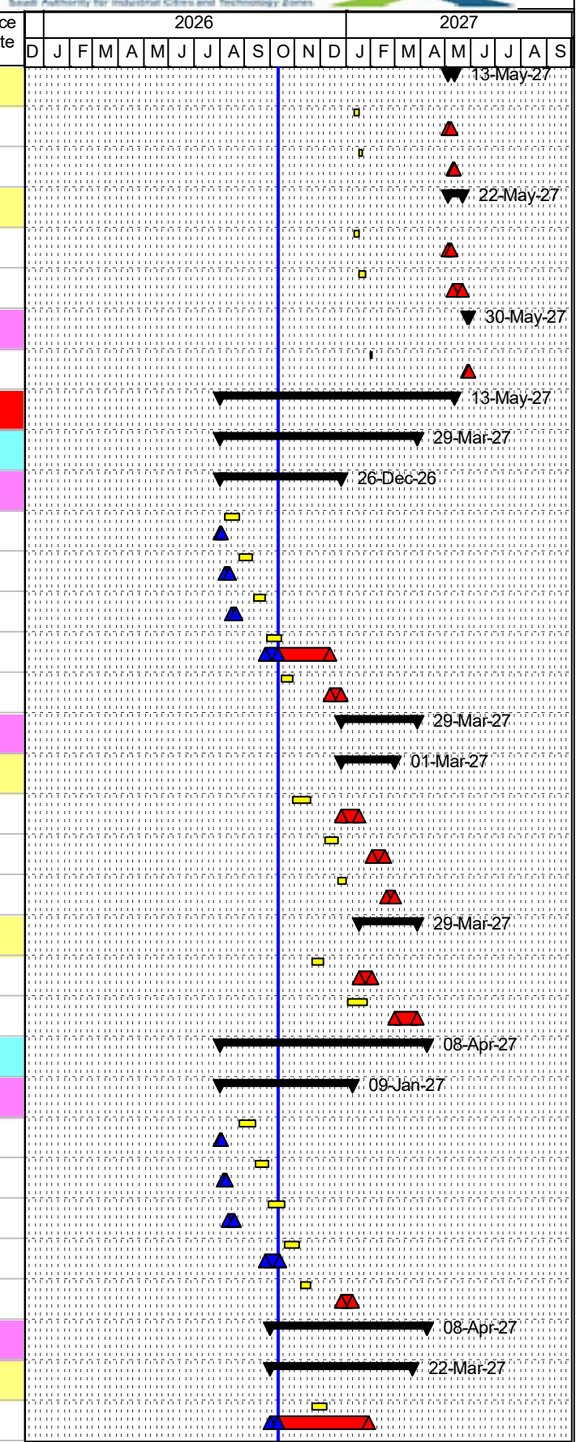



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-SU-FE-N-AR-140 | Insulation For Boundary Fence West | 12 | 20-Feb-27 | 04-Mar-27 | 109,999 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-AR-150 | Install all the Relevant Cladding and Finishes For Boundary Fence West | 12 | 06-Mar-27 | 22-Mar-27 | 1,276,358 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 54 | 02-Feb-27 | 08-Apr-27 | 641,279 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-260 | Installation of Conduits and Cables for Electricial Works For Boundary Fence West | 8 | 02-Feb-27 | 10-Feb-27 | 154,292 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-270 | Install, fixings, testing of all electrical finishes and lightings for Electricial Works For | 9 | 30-Mar-27 | 08-Apr-27 | 486,987 | 0 | 0 | 0 | 0% | 0% |
| **Boundary Fence - North** | | 106 | 01-Aug-26 A | 05-Apr-27 | 3,343,920 | 102,123 | 1,183,592 | 1,057,611 | 3.05% | 35.4% |
| **Civil Work** | | 47 | 01-Aug-26 A | 23-Jan-27 | 1,036,327 | 102,123 | 917,633 | 917,633 | 9.85% | 88.55% |
| CO-SU-FE-N-CI-200 | Excavation Work For Boundary Fence North | 16 | 01-Aug-26 A | 04-Aug-26 A | 66,380 | 66,380 | 66,380 | 66,380 | 100% | 100% |
| CO-SU-FE-N-CI-210 | Pouring for Plain Concrete For Boundary Fence North | 13 | 05-Aug-26 A | 11-Aug-26 A | 66,380 | 35,743 | 66,380 | 66,380 | 53.85% | 100% |
| CO-SU-FE-N-CI-220 | Pouring R.C Footing For Boundary Fence North | 16 | 11-Aug-26 A | 02-Sep-26 A | 312,570 | 0 | 312,570 | 312,570 | 0% | 100% |
| CO-SU-FE-N-CI-230 | Pouring R.C Columns For Boundary Fence North | 16 | 26-Sep-26 A | 12-Oct-26 A | 472,304 | 0 | 472,304 | 472,304 | 0% | 100% |
| CO-SU-FE-N-CI-240 | Pouring Beams For Boundary Fence North | 12 | 10-Jan-27 | 23-Jan-27 | 118,694 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 54 | 01-Oct-26 A | 05-Apr-27 | 2,307,593 | 0 | 265,958 | 139,978 | 0% | 11.53% |
| **Architictural work** | | 48 | 01-Oct-26 A | 29-Mar-27 | 1,666,313 | 0 | 265,958 | 139,978 | 0% | 15.96% |
| CO-SU-FE-N-AR-160 | Install Brick Work For Boundary Fence North | 14 | 01-Oct-26 A | 06-Feb-27 | 279,956 | 0 | 265,958 | 139,978 | 0% | 95% |
| CO-SU-FE-N-AR-170 | Insulation For Boundary Fence North | 11 | 06-Mar-27 | 21-Mar-27 | 109,999 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-AR-180 | Install all the Relevant Cladding and Finishes For Boundary Fence North | 6 | 23-Mar-27 | 29-Mar-27 | 1,276,358 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 43 | 11-Feb-27 | 05-Apr-27 | 641,279 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-280 | Installation of Conduits and Cables for Electricial Works For Boundary Fence North | 7 | 11-Feb-27 | 18-Feb-27 | 154,292 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-290 | Install, fixings, testing of all electrical finishes and lightings for Electricial Works For | 6 | 30-Mar-27 | 05-Apr-27 | 486,987 | 0 | 0 | 0 | 0% | 0% |
| **Boundary Fence - East** | | 123 | 06-Sep-26 A | 13-May-27 | 3,343,920 | 29,041 | 904,319 | 555,328 | 0.87% | 27.04% |
| **Civil Work** | | 45 | 06-Sep-26 A | 03-Feb-27 | 1,036,327 | 29,041 | 752,327 | 445,330 | 2.8% | 72.6% |
| CO-SU-FE-N-CI-250 | Excavation Work For Boundary Fence East | 16 | 19-Dec-26 A | 19-Dec-26 A | 66,380 | 29,041 | 66,380 | 66,380 | 43.75% | 100% |
| CO-SU-FE-N-CI-260 | Pouring for Plain Concrete For Boundary Fence East | 13 | 06-Sep-26 A | 20-Sep-26 A | 66,380 | 0 | 66,380 | 66,380 | 0% | 100% |
| CO-SU-FE-N-CI-270 | Pouring R.C Footing For Boundary Fence East | 16 | 21-Sep-26 A | 12-Oct-26 A | 312,570 | 0 | 312,570 | 312,570 | 0% | 100% |
| CO-SU-FE-N-CI-280 | Pouring R.C Columns For Boundary Fence East | 16 | 26-Sep-26 A | 02-Jan-27 | 472,304 | 0 | 306,997 | 0 | 0% | 65% |
| CO-SU-FE-N-CI-290 | Pouring Beams For Boundary Fence East | 10 | 24-Jan-27 | 03-Feb-27 | 118,694 | 0 | 0 | 0 | 0% | 0% |
| **Finishing Work** | | 41 | 01-Oct-26 A | 13-May-27 | 2,307,593 | 0 | 151,992 | 109,999 | 0% | 6.59% |
| **Architictural work** | | 36 | 01-Oct-26 A | 08-May-27 | 1,666,313 | 0 | 151,992 | 109,999 | 0% | 9.12% |
| CO-SU-FE-N-AR-190 | Install Brick Work For Boundary Fence East | 11 | 08-Oct-26 A | 15-Apr-27 | 279,956 | 0 | 41,993 | 0 | 0% | 15% |
| CO-SU-FE-N-AR-200 | Insulation For Boundary Fence East | 8 | 01-Oct-26 A | 12-Oct-26 A | 109,999 | 0 | 109,999 | 109,999 | 0% | 100% |
| CO-SU-FE-N-AR-210 | Install all the Relevant Cladding and Finishes For Boundary Fence East | 9 | 28-Apr-27 | 08-May-27 | 1,276,358 | 0 | 0 | 0 | 0% | 0% |
| **Electrical Work** | | 24 | 17-Apr-27 | 13-May-27 | 641,279 | 0 | 0 | 0 | 0% | 0% |
| CO-SU-FE-N-EL-300 | Installation of Conduits and Cables for Electricial Works For Boundary Fence East | 10 | 17-Apr-27 | 27-Apr-27 | 154,292 | 0 | 0 | 0 | 0% | 0% |

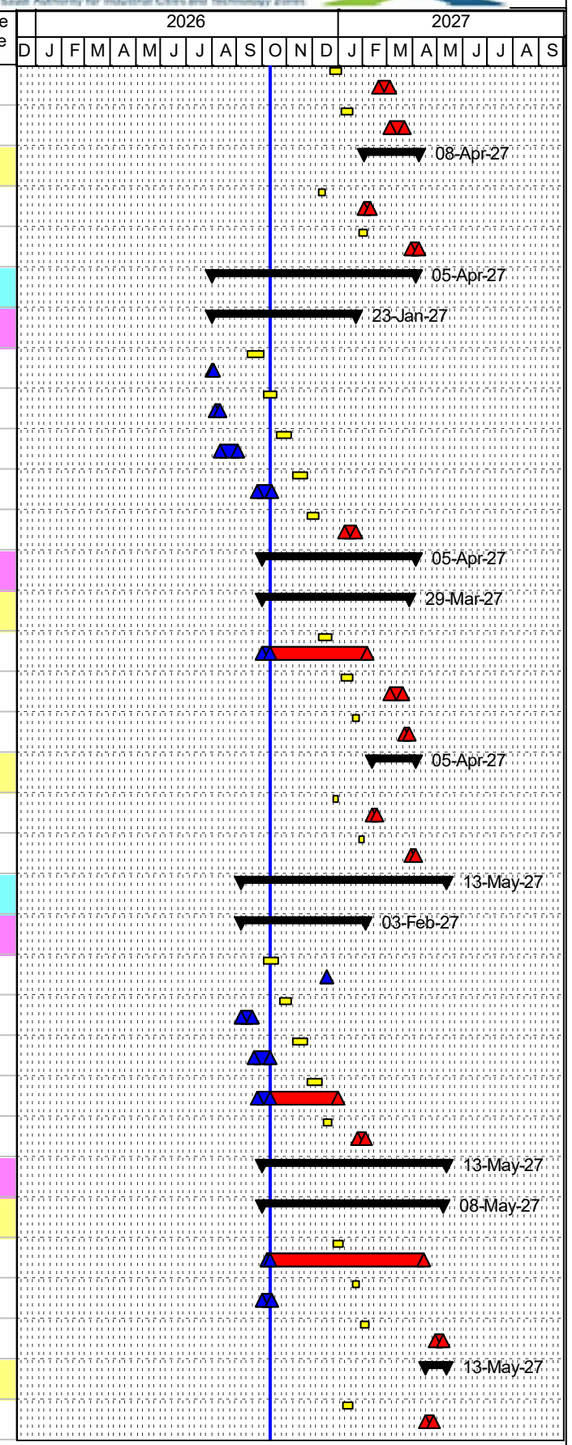



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| CO-SU-FE-N-EL-310 | Install, fixings, testing of all electrical finishes and lightings for Electricial Works For | 5 | 09-May-27 | 13-May-27 | 486,987 | 0 | 0 | 0 | 0% | 0% |
| **Testing and Comissioning** | | 25 | 31-May-27 | 28-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Infrastructure Networks** | | 17 | 05-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Low Voltage Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| TC-LV-100 | Testing and Commissioning of Low Voltage Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Irrigation Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-IR | Testing and Commissioning of Irrigation Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **TSE Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-TSE-10 | Testing and Commissioning of TSE Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Potable Water Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-PW | Testing and Commissioning of Potable Water Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Sewage Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-SW | Testing and Commissioning of Sewage Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Storm Drainage Network** | | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-DPO | Testing and Commissioning of Storm Drainage Ponds | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-SD | Testing and Commissioning of Storm Drainage Ponds and Storm Drainage Network | 12 | 10-Jun-27 | 23-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Street Lighting Network** | | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-SL | Testing and Commissioning of Street Lighting Network | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Telecom and Light Current Network** | | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-TE | Testing and Commissioning of Telecom and Light Current Networks | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Medium Voltage Network** | | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-MV | Testing and Commissioning of Medium Voltage Network | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Road Works** | | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-RD | Testing and Commissioning of Road Works | 12 | 05-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Utility Buildings** | | 25 | 31-May-27 | 28-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-CTV | Testing and Commissioning of Guard Room and Boundary Fence | 16 | 31-May-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-CTV10 | Testing and Commissioning of Utility Buildings | 16 | 10-Jun-27 | 28-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| T/C-CTV20 | Testing and Commissioning of Softscape And Planting | 16 | 02-Jun-27 | 20-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Handing over and close out** | | 24 | 05-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **As-Built** | | 24 | 05-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-100 | Submission As-Built Drawing For Sewage Network | 10 | 10-Jun-27 | 21-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-130 | Submission As-Built Drawing For Pond | 10 | 10-Jun-27 | 21-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-140 | Submission As-Built Drawing For Roads Network | 10 | 05-Jun-27 | 15-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-150 | Submission As-Built Drawing For Street Lighting Network | 10 | 05-Jun-27 | 15-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |

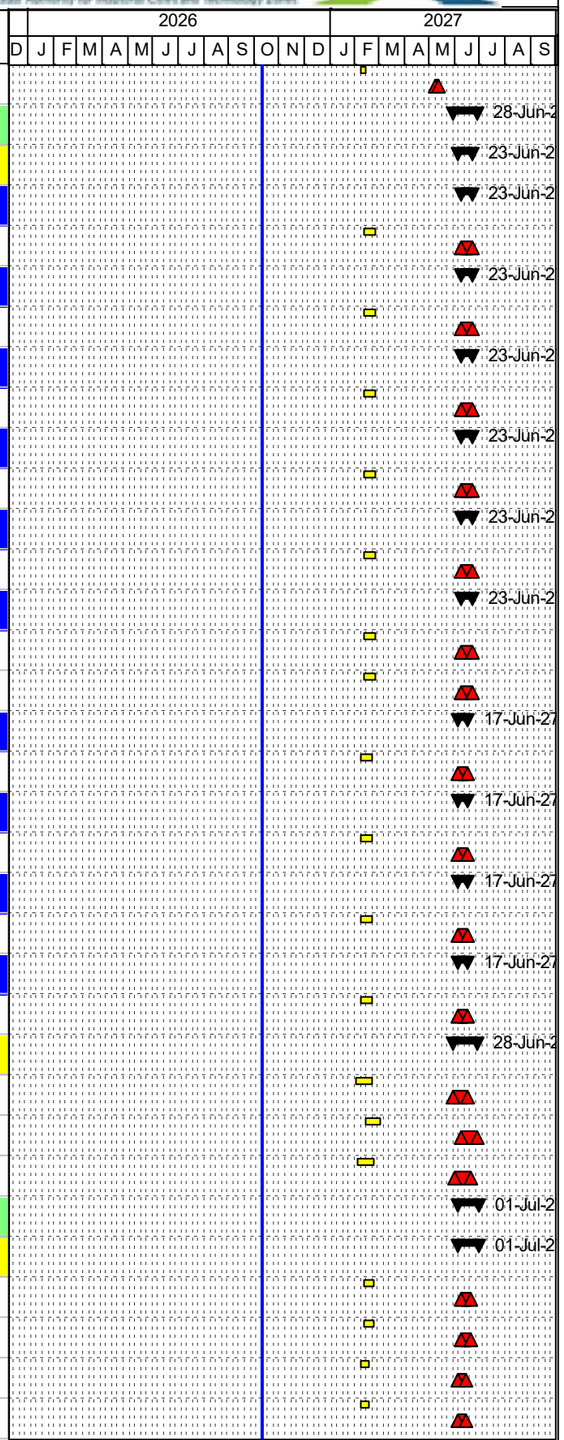



Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |

Development of the Technology City in Dharan Project
BL-Update 12-10-2026
WPR UPS LEVEL 5

| Activity ID | Activity Name | Original Duration | Start | Finish | Budgeted Total Cost | Planned Value Cost | Earned Value Cost | Actual Total Cost | Schedule % Complete | Performance % Complete |
|---|---|---|---|---|---|---|---|---|---|---|
| HO-160 | Submission As-Built Drawing For Telecom and Light Current Networks | 10 | 05-Jun-27 | 15-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-170 | Submission As-Built Drawing For Medium Voltage Network | 7 | 24-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-180 | Submission As-Built Drawing For Irrigation Network | 10 | 10-Jun-27 | 21-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-190 | As-Built Drawing For Potable Water Network | 7 | 24-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-200 | Submission As-Built Drawing For Storm Network | 10 | 10-Jun-27 | 21-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-210 | Submission As-Built Drawing For Utility Buildings | 8 | 20-Jun-27 | 28-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **De-Mobilization Works** | | 18 | 07-Jun-27 | 27-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-120 | Remove material stock & Storage area | 8 | 19-Jun-27 | 27-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-220 | Removing Portable Caravan | 7 | 10-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-230 | Remove Temporary Car Shades | 10 | 07-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| **Handing Over** | | 20 | 09-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-110 | Final Testing Work | 7 | 24-Jun-27 | 01-Jul-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-240 | Final Walkthrough and Inspection | 8 | 09-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-250 | Review B.O.Q Qty. to ensure compliance with the actual status | 8 | 09-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-260 | Review FIR Approval to ensure compliance with the actual status | 8 | 09-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-270 | Review the sample drawing to ensure compliance with the actual status | 8 | 09-Jun-27 | 17-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |
| HO-280 | Punch List Completion | 8 | 19-Jun-27 | 27-Jun-27 | 0 | 0 | 0 | 0 | 0% | 0% |

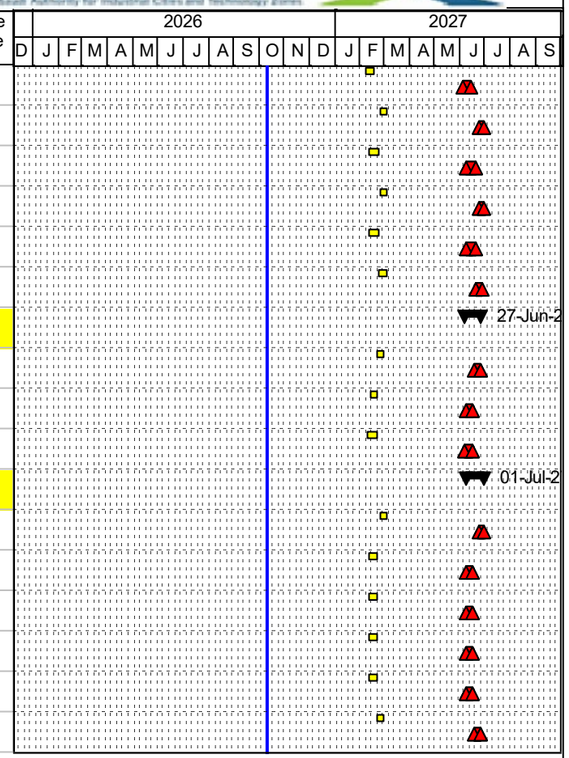


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary



| Date | Revision | Checked | Approved |
|---|---|---|---|
| 12-Oct-26 | Third Industrial City | | |
