
Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
DEVELOPMENT OF SUDAIR INDUSTRIAL CITY PHASE 2 - 09/11/2026.		244	08-Jul-26	26-May-27	18-May-26 A	14-Dec-26	61.37%	39.84%
Construction		244	08-Jul-26	26-May-27	18-May-26	14-Dec-26	61.37%	39.84%
ROAD WORKS		90	23-Aug-26	12-Jan-27	18-May-26	13-Dec-26	74.69%	48.74%
ZONE A		90	26-Aug-26	12-Jan-27	01-Jun-26 A	08-Dec-26	73.84%	47.4%
ROAD WORKS IN (PH2-COL-MC20)		18	16-Nov-26	06-Dec-26	09-Nov-26	29-Nov-26	0%	0%
Asphalt Works		18	16-Nov-26	06-Dec-26	09-Nov-26	29-Nov-26	0%	0%
SDR-2-CON-RW-ZA-	Asphalt works 2nd layer with RC-01	18	16-Nov-26	06-Dec-26	09-Nov-26	29-Nov-26	0%	0%
ROAD WORKS IN (PH2-A-MCI0)		48	26-Aug-26	10-Oct-26	05-Oct-26 A	01-Dec-26	100%	47.31%
Subgrade		20	26-Aug-26	17-Sep-26	05-Oct-26 A	01-Dec-26	100%	50%
SDR-2-CON-RW-ZA-	Subgrade layer works	20	26-Aug-26	17-Sep-26	05-Oct-26 A	01-Dec-26	100%	50%
Kerbstone Installation		18	19-Sep-26	10-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	19-Sep-26	10-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-A-MCA0)		84	31-Aug-26	07-Dec-26	01-Sep-26	07-Dec-26	96.96%	66.34%
Subgrade		21	31-Aug-26	24-Sep-26	01-Sep-26	12-Nov-26	100%	75%
SDR-2-CON-RW-ZA-	Subgrade layer works	21	31-Aug-26	24-Sep-26	01-Sep-26	12-Nov-26	100%	75%
Earth Works Plot		47	26-Sep-26	07-Dec-26	30-Sep-26	07-Dec-26	67.49%	47.24%
SDR-2-CON-RW-ZA-	Plot Excavation for cuttings (all types of soil)	21	26-Sep-26	19-Oct-26	30-Sep-26	07-Dec-26	100%	70%
SDR-2-CON-RW-ZA-	Embankments to the Plot 2 Layer	21	14-Nov-26	07-Dec-26	09-Nov-26	02-Dec-26	0%	0%
Base Course		15	26-Sep-26	12-Oct-26	20-Oct-26 A	30-Nov-26	100%	30%
SDR-2-CON-RW-ZA-	Aggregate base course layer	15	26-Sep-26	12-Oct-26	20-Oct-26 A	30-Nov-26	100%	30%
Kerbstone Installation		21	26-Sep-26	19-Oct-26	14-Nov-26	07-Dec-26	100%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	21	26-Sep-26	19-Oct-26	14-Nov-26	07-Dec-26	100%	0%
ROAD WORKS IN (PH2-A-MCB0)		81	12-Sep-26	14-Dec-26	08-Jun-26 A	02-Dec-26	96.96%	47.87%
Subgrade		16	12-Sep-26	30-Sep-26	01-Sep-26	09-Nov-26	100%	50%
SDR-2-CON-RW-ZA-	Subgrade layer works	16	12-Sep-26	30-Sep-26	01-Sep-26	09-Nov-26	100%	50%
Earth Works Plot		65	01-Oct-26	14-Dec-26	08-Jun-26 A	09-Nov-26	67.49%	65.49%
SDR-2-CON-RW-ZA-	Plot Excavation for cuttings (all types of soil)	21	01-Oct-26	25-Oct-26	08-Jun-26 A	09-Nov-26	100%	85%
SDR-2-CON-RW-ZA-	Embankments to the Plot 2 Layer	21	21-Nov-26	14-Dec-26	30-Jun-26 A	09-Nov-26	0%	25%
Base Course		20	01-Oct-26	24-Oct-26	27-Oct-26 A	02-Dec-26	100%	25%
SDR-2-CON-RW-ZA-	Aggregate base course layer	20	01-Oct-26	24-Oct-26	27-Oct-26 A	02-Dec-26	100%	25%
Kerbstone Installation		20	01-Oct-26	24-Oct-26	10-Nov-26	02-Dec-26	100%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	20	01-Oct-26	24-Oct-26	10-Nov-26	02-Dec-26	100%	0%
ROAD WORKS IN (PH2-A-MCC0)		63	04-Oct-26	20-Dec-26	08-Jun-26 A	29-Nov-26	74.4%	65.65%
Earth Works Plot		63	10-Oct-26	20-Dec-26	08-Jun-26 A	10-Nov-26	67.49%	83.37%
SDR-2-CON-RW-ZA-	Plot Excavation for cuttings (all types of soil)	20	10-Oct-26	01-Nov-26	08-Jun-26 A	09-Nov-26	100%	85%
SDR-2-CON-RW-ZA-	Embankments to the Plot 2 Layer	21	26-Nov-26	20-Dec-26	18-Jul-26 A	10-Nov-26	0%	80%
Kerbstone Installation		18	04-Oct-26	24-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	04-Oct-26	24-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-A-MCD0)		18	08-Oct-26	28-Oct-26	31-Oct-26 A	29-Nov-26	100%	25%
Kerbstone Installation		18	08-Oct-26	28-Oct-26	31-Oct-26 A	29-Nov-26	100%	25%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	08-Oct-26	28-Oct-26	31-Oct-26 A	29-Nov-26	100%	25%
ROAD WORKS IN (PH2-A-MCE0)		20	16-Sep-26	10-Oct-26	05-Oct-26 A	01-Dec-26	100%	75%
Subgrade		20	16-Sep-26	10-Oct-26	05-Oct-26 A	01-Dec-26	100%	75%
SDR-2-CON-RW-ZA-	Subgrade layer works	20	16-Sep-26	10-Oct-26	05-Oct-26 A	01-Dec-26	100%	75%
ROAD WORKS IN (PH2-A-MCF0)		18	05-Nov-26	25-Nov-26	09-Nov-26	29-Nov-26	16.67%	0%
Kerbstone Installation		18	05-Nov-26	25-Nov-26	09-Nov-26	29-Nov-26	16.67%	0%

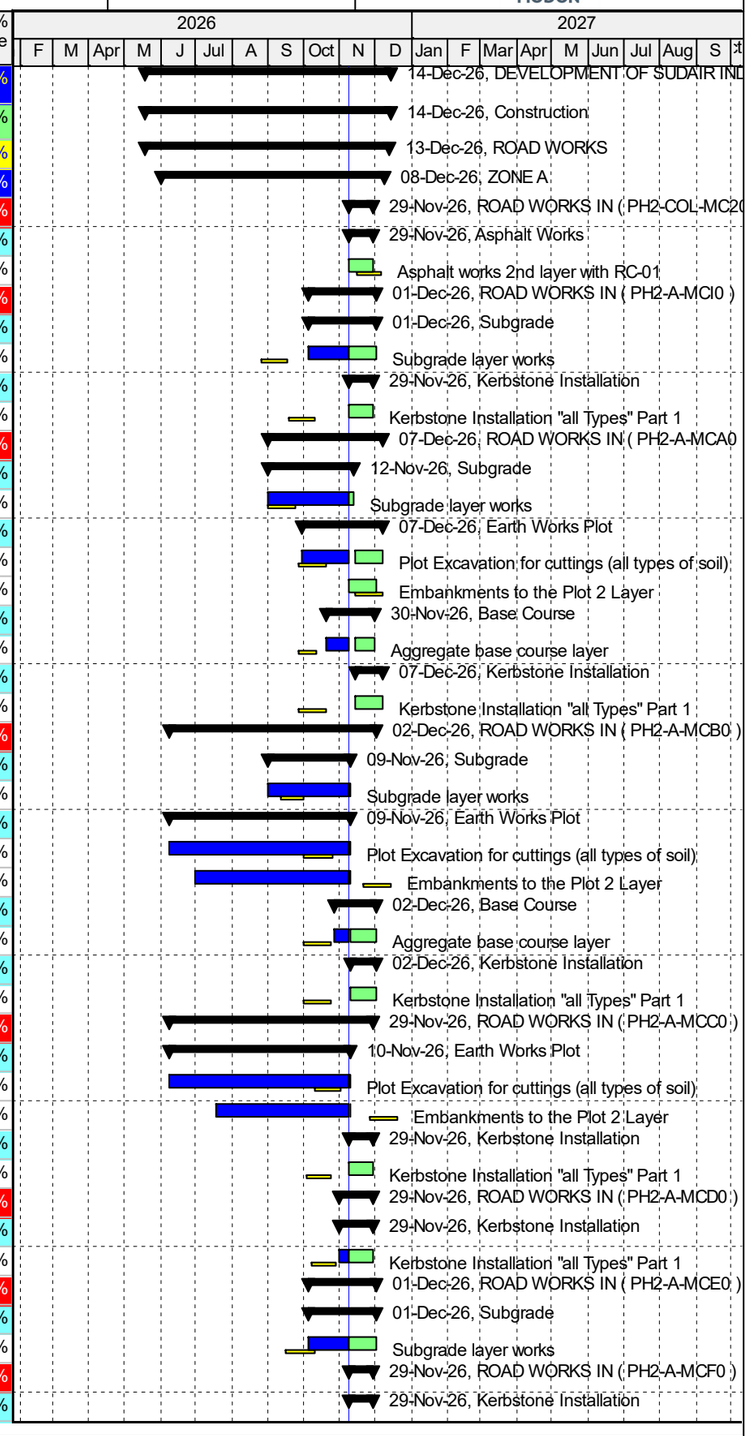

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	05-Nov-26	25-Nov-26	09-Nov-26	29-Nov-26	16.67%	0%
ROAD WORKS IN (PH2-A-MCG0)		18	07-Nov-26	19-Dec-26	09-Nov-26	29-Nov-26	1.01%	0%
Demolition Work		2	15-Nov-26	16-Nov-26	09-Nov-26	10-Nov-26	0%	0%
SDR-2-CON-RW-ZA-	Milling of wearing course	2	15-Nov-26	16-Nov-26	09-Nov-26	10-Nov-26	0%	0%
Asphalt Works		11	07-Dec-26	19-Dec-26	11-Nov-26	23-Nov-26	0%	0%
SDR-2-CON-RW-ZA-	Asphalt works 2nd layer with RC-02	11	07-Dec-26	19-Dec-26	11-Nov-26	23-Nov-26	0%	0%
Kerbstone Installation		18	07-Nov-26	26-Nov-26	09-Nov-26	29-Nov-26	11.11%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	07-Nov-26	26-Nov-26	09-Nov-26	29-Nov-26	11.11%	0%
ROAD WORKS IN (PH2-A-MCH0)		56	22-Oct-26	12-Jan-27	01-Jun-26 A	08-Dec-26	83.81%	23.99%
Subgrade		8	22-Oct-26	31-Oct-26	05-Oct-26 A	17-Nov-26	100%	25%
SDR-2-CON-RW-ZA-	Subgrade layer works	8	22-Oct-26	31-Oct-26	05-Oct-26 A	17-Nov-26	100%	25%
Earth Works Plot		43	25-Nov-26	12-Jan-27	01-Jun-26 A	03-Dec-26	0%	57.5%
SDR-2-CON-RW-ZA-	Embankments to the Plot 1 Layer	21	25-Nov-26	19-Dec-26	01-Jun-26 A	09-Nov-26	0%	85%
SDR-2-CON-RW-ZA-	Embankments to the Plot 2 Layer	21	20-Dec-26	12-Jan-27	05-Oct-26 A	03-Dec-26	0%	30%
Base Course		15	07-Nov-26	23-Nov-26	18-Nov-26	05-Dec-26	13.33%	0%
SDR-2-CON-RW-ZA-	Aggregate base course layer	15	07-Nov-26	23-Nov-26	18-Nov-26	05-Dec-26	13.33%	0%
Kerbstone Installation		18	01-Nov-26	21-Nov-26	18-Nov-26	08-Dec-26	38.89%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	01-Nov-26	21-Nov-26	18-Nov-26	08-Dec-26	38.89%	0%
ROAD WORKS IN (PH2-ART-MC00)		18	08-Nov-26	19-Dec-26	20-Oct-26 A	29-Nov-26	0.55%	50%
Asphalt Works		11	07-Dec-26	19-Dec-26	20-Oct-26 A	21-Nov-26	0%	50%
SDR-2-CON-RW-ZA-	Asphalt works 2nd layer with RC-02	11	07-Dec-26	19-Dec-26	20-Oct-26 A	21-Nov-26	0%	50%
Kerbstone Installation		18	08-Nov-26	28-Nov-26	25-Oct-26 A	29-Nov-26	5.56%	50%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	08-Nov-26	28-Nov-26	25-Oct-26 A	29-Nov-26	5.56%	50%
ROAD WORKS IN (PH2-ART-MC10)		36	11-Nov-26	23-Dec-26	24-Oct-26 A	08-Dec-26	0%	46.42%
Demolition Work		2	24-Nov-26	25-Nov-26	26-Oct-26 A	10-Nov-26	0%	75%
SDR-2-CON-RW-ZA-	Milling of wearing course	2	24-Nov-26	25-Nov-26	26-Oct-26 A	10-Nov-26	0%	75%
Asphalt Works		36	26-Nov-26	23-Dec-26	24-Oct-26 A	08-Dec-26	0%	47.5%
SDR-2-CON-RW-ZA-	Asphalt works 1st Layer with MC-01	10	26-Nov-26	07-Dec-26	24-Oct-26 A	22-Nov-26	0%	95%
SDR-2-CON-RW-ZA-	Asphalt works 2nd layer with RC-02	14	08-Dec-26	23-Dec-26	23-Nov-26	08-Dec-26	0%	0%
Kerbstone Installation		18	11-Nov-26	01-Dec-26	09-Nov-26	29-Nov-26	0%	0%
SDR-2-CON-RW-ZA-	Kerbstone Installation "all Types" Part 1	18	11-Nov-26	01-Dec-26	09-Nov-26	29-Nov-26	0%	0%
ZONE G		77	23-Aug-26	30-Nov-26	18-May-26	13-Dec-26	78.08%	54.14%
ROAD WORKS IN (PH2-COL-MC50)		25	21-Sep-26	14-Oct-26	26-Oct-26 A	29-Nov-26	100%	23.15%
Demolition Work		9	05-Oct-26	14-Oct-26	26-Oct-26 A	18-Nov-26	100%	50%
SDR-2-CON-RW-ZG-	Milling of wearing course	9	05-Oct-26	14-Oct-26	26-Oct-26 A	18-Nov-26	100%	50%
Kerbstone Installation		18	21-Sep-26	12-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	21-Sep-26	12-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-ART-MC00)		18	23-Aug-26	12-Sep-26	26-Oct-26 A	29-Nov-26	100%	75%
Kerbstone Installation		18	23-Aug-26	12-Sep-26	26-Oct-26 A	29-Nov-26	100%	75%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	23-Aug-26	12-Sep-26	26-Oct-26 A	29-Nov-26	100%	75%
ROAD WORKS IN (PH2-G-MCA0)		60	27-Oct-26	30-Nov-26	05-Oct-26 A	13-Dec-26	56.51%	45.36%
Demolition Work		16	27-Oct-26	14-Nov-26	09-Nov-26	26-Nov-26	30.48%	0%
SDR-2-CON-RW-ZG-	Removal of curbstone	9	27-Oct-26	05-Nov-26	09-Nov-26	18-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Milling of wearing course	7	07-Nov-26	14-Nov-26	19-Nov-26	26-Nov-26	28.57%	0%
Asphalt Works		60	27-Oct-26	30-Nov-26	05-Oct-26 A	13-Dec-26	57.45%	47.01%
SDR-2-CON-RW-ZG-	Asphalt works 1st Layer with MC-01	12	27-Oct-26	09-Nov-26	05-Oct-26 A	22-Nov-26	91.67%	75%
SDR-2-CON-RW-ZG-	Asphalt works 2nd layer with RC-02	18	10-Nov-26	30-Nov-26	23-Nov-26	13-Dec-26	0%	0%

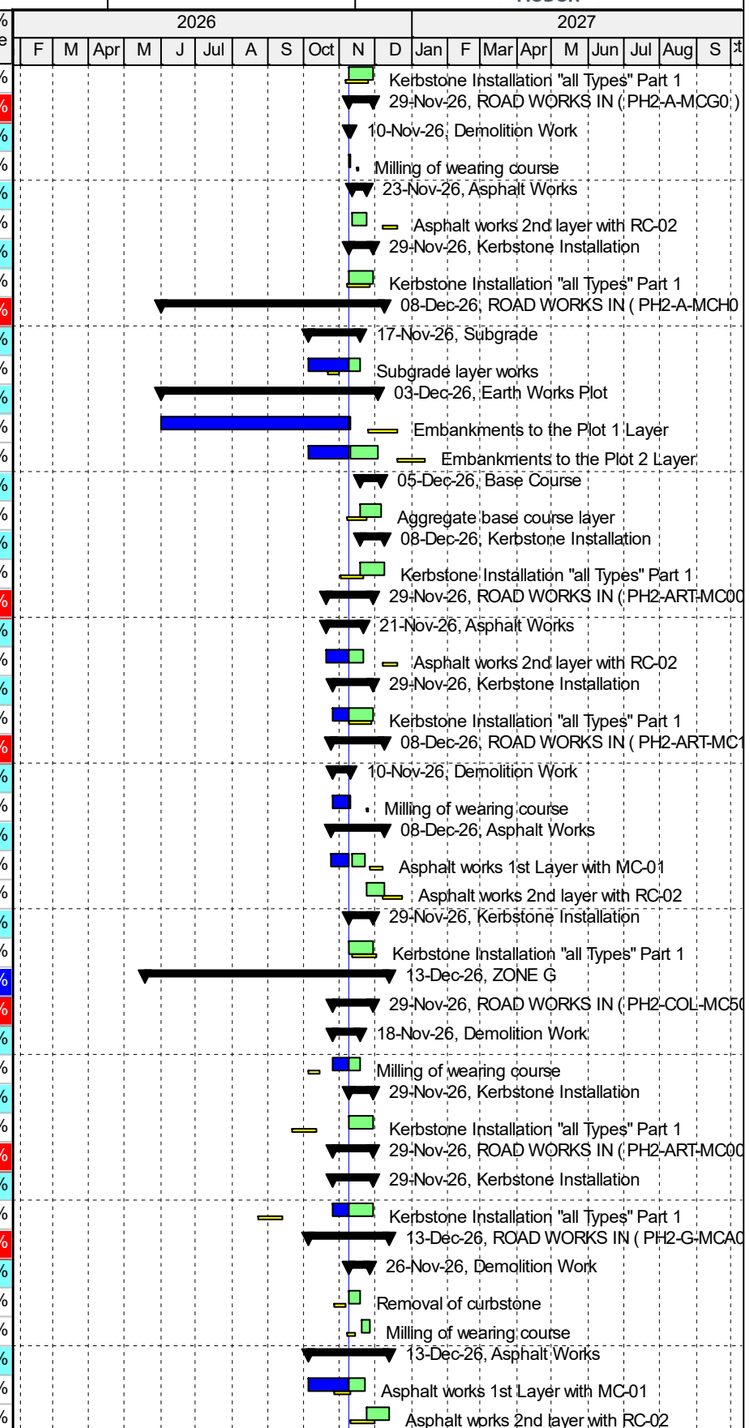

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
ROAD WORKS IN (PH2-G-MCE0)		18	19-Sep-26	14-Oct-26	09-Nov-26	29-Nov-26	100%	0%
Demolition Work		4	11-Oct-26	14-Oct-26	09-Nov-26	12-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Removal of curbstone	4	11-Oct-26	14-Oct-26	09-Nov-26	12-Nov-26	100%	0%
Kerbstone Installation		18	19-Sep-26	10-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	19-Sep-26	10-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-G-MCD0)		33	17-Sep-26	07-Nov-26	11-Oct-26 A	05-Dec-26	100%	82.76%
Demolition Work		5	12-Oct-26	17-Oct-26	26-Oct-26 A	14-Nov-26	100%	50%
SDR-2-CON-RW-ZG-	Milling of wearing course	5	12-Oct-26	17-Oct-26	26-Oct-26 A	14-Nov-26	100%	50%
Asphalt Works		18	18-Oct-26	07-Nov-26	11-Oct-26 A	05-Dec-26	100%	90%
SDR-2-CON-RW-ZG-	Asphalt works 1st Layer with MC-01	18	18-Oct-26	07-Nov-26	11-Oct-26 A	05-Dec-26	100%	90%
Kerbstone Installation		18	17-Sep-26	08-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	17-Sep-26	08-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-G-MCF0)		18	08-Sep-26	11-Oct-26	09-Nov-26	29-Nov-26	100%	0%
Demolition Work		7	04-Oct-26	11-Oct-26	09-Nov-26	16-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Removal of curbstone	7	04-Oct-26	11-Oct-26	09-Nov-26	16-Nov-26	100%	0%
Kerbstone Installation		18	08-Sep-26	29-Sep-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	08-Sep-26	29-Sep-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-G-MCG0)		65	14-Sep-26	30-Nov-26	18-May-26	29-Nov-26	81.64%	50.59%
Earth Works Plot		63	14-Sep-26	30-Nov-26	18-May-26	10-Nov-26	77.81%	61.13%
SDR-2-CON-RW-ZG-	Plot Excavation for cuttings (all types of soil)	21	14-Sep-26	08-Oct-26	18-May-26	09-Nov-26	100%	55%
SDR-2-CON-RW-ZG-	Embankments to the Plot 1 Layer	21	13-Oct-26	05-Nov-26	11-Jun-26 A	09-Nov-26	100%	80%
SDR-2-CON-RW-ZG-	Embankments to the Plot 2 Layer	21	07-Nov-26	30-Nov-26	22-Jun-26 A	10-Nov-26	9.52%	55%
Demolition Work		8	10-Oct-26	18-Oct-26	09-Nov-26	17-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Removal of curbstone	8	10-Oct-26	18-Oct-26	09-Nov-26	17-Nov-26	100%	0%
Kerbstone Installation		18	14-Sep-26	05-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	14-Sep-26	05-Oct-26	09-Nov-26	29-Nov-26	100%	0%
ROAD WORKS IN (PH2-G-MCZ0)		18	05-Oct-26	31-Oct-26	02-Nov-26	29-Nov-26	100%	0.63%
Demolition Work		15	14-Oct-26	31-Oct-26	02-Nov-26	25-Nov-26	100%	1.33%
SDR-2-CON-RW-ZG-	Removal of curbstone	5	14-Oct-26	19-Oct-26	02-Nov-26	14-Nov-26	100%	50%
SDR-2-CON-RW-ZG-	Milling of wearing course	10	20-Oct-26	31-Oct-26	15-Nov-26	25-Nov-26	100%	0%
Kerbstone Installation		18	05-Oct-26	25-Oct-26	09-Nov-26	29-Nov-26	100%	0%
SDR-2-CON-RW-ZG-	Kerbstone Installation "all Types" Part 1	18	05-Oct-26	25-Oct-26	09-Nov-26	29-Nov-26	100%	0%
Storm Water Drainage Network		175	08-Jul-26	28-Jan-27	06-Jul-26 A	09-Dec-26	74.88%	41.7%
ZONE A		138	08-Jul-26	10-Jan-27	06-Jul-26 A	09-Dec-26	75.31%	41.8%
STORM WATER LINE IN (PH2-A-MCB0)		44	23-Nov-26	10-Jan-27	16-Aug-26	03-Dec-26	0%	35%
Catch basin		44	23-Nov-26	10-Jan-27	16-Aug-26	03-Dec-26	0%	35%
Excavation		44	23-Nov-26	10-Jan-27	16-Aug-26	03-Dec-26	0%	35%
SDR-2-CON-ST-Z	Excavation for Catch basin Section 1	21	23-Nov-26	16-Dec-26	16-Aug-26	09-Nov-26	0%	60%
SDR-2-CON-ST-Z	Excavation for Catch basin Section 2	21	17-Dec-26	10-Jan-27	19-Oct-26 A	03-Dec-26	0%	10%
STORM WATER LINE IN (PH2-A-MCD0)		63	28-Sep-26	03-Jan-27	16-Aug-26	05-Dec-26	60.55%	63.61%
Pipes Works		58	28-Sep-26	09-Dec-26	20-Aug-26	03-Dec-26	62.16%	66.67%
bedding Works		21	28-Sep-26	21-Oct-26	20-Aug-26	09-Nov-26	100%	80%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	28-Sep-26	21-Oct-26	20-Aug-26	09-Nov-26	100%	80%
Pipes Laying		21	22-Oct-26	15-Nov-26	26-Aug-26	09-Nov-26	71.77%	80%
SDR-2-CON-ST-Z	Install ST GRP Pipes	21	22-Oct-26	15-Nov-26	26-Aug-26	09-Nov-26	71.43%	80%
Testing		21	16-Nov-26	09-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-ST-Z	Testing ST GRP Pipes	21	16-Nov-26	09-Dec-26	10-Nov-26	03-Dec-26	0%	0%

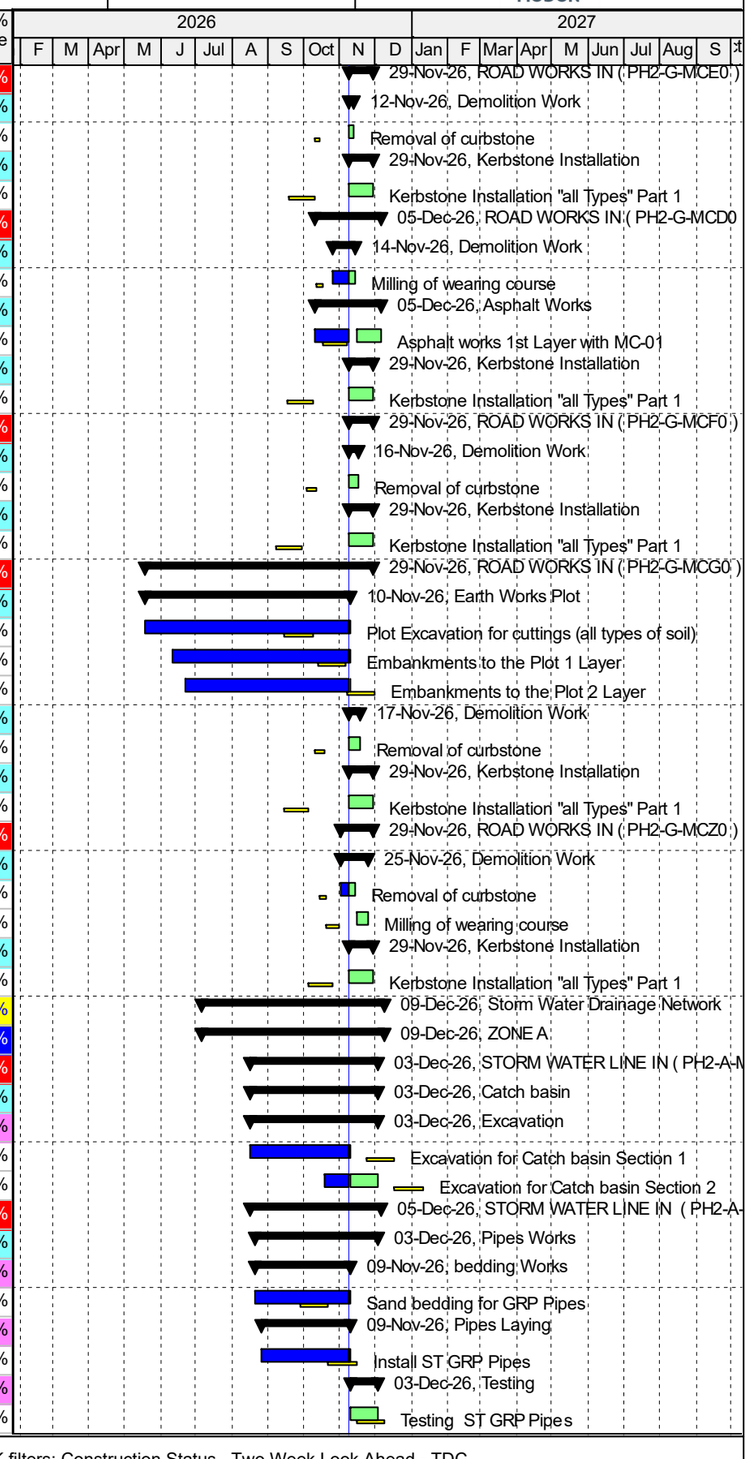

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Manholes		59	28-Sep-26	09-Dec-26	27-Aug-26	05-Dec-26	64.84%	63.46%
bedding Works		21	28-Sep-26	21-Oct-26	27-Aug-26	09-Nov-26	100%	75%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	28-Sep-26	21-Oct-26	27-Aug-26	09-Nov-26	100%	75%
Install Manholes		21	22-Oct-26	15-Nov-26	30-Aug-26	10-Nov-26	71.43%	75%
SDR-2-CON-ST-Z	Manholes Installation	21	22-Oct-26	15-Nov-26	30-Aug-26	10-Nov-26	71.43%	75%
Testing		21	16-Nov-26	09-Dec-26	11-Nov-26	05-Dec-26	0%	0%
SDR-2-CON-ST-Z	Testing for Manholes	21	16-Nov-26	09-Dec-26	11-Nov-26	05-Dec-26	0%	0%
Catch basin		25	16-Nov-26	03-Jan-27	16-Aug-26	05-Dec-26	0%	25%
Excavation		25	16-Nov-26	03-Jan-27	16-Aug-26	05-Dec-26	0%	25%
SDR-2-CON-ST-Z	Excavation for Catch basin Section 1	21	16-Nov-26	09-Dec-26	16-Aug-26	10-Nov-26	0%	50%
SDR-2-CON-ST-Z	Excavation for Catch basin Section 2	21	10-Dec-26	03-Jan-27	11-Nov-26	05-Dec-26	0%	0%
STORM WATER LINE IN (PH2-A-MCE0)		45	13-Oct-26	26-Dec-26	20-Aug-26	03-Dec-26	17.5%	51.31%
Pipes Works		44	14-Oct-26	26-Dec-26	20-Aug-26	03-Dec-26	11.92%	62.5%
bedding Works		21	14-Oct-26	07-Nov-26	20-Aug-26	09-Nov-26	100%	75%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	14-Oct-26	07-Nov-26	20-Aug-26	09-Nov-26	100%	75%
Pipes Laying		21	08-Nov-26	01-Dec-26	27-Aug-26	09-Nov-26	4.78%	75%
SDR-2-CON-ST-Z	Install ST GRP Pipes	21	08-Nov-26	01-Dec-26	27-Aug-26	09-Nov-26	4.76%	75%
Testing		21	02-Dec-26	26-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-ST-Z	Testing ST GRP Pipes	21	02-Dec-26	26-Dec-26	10-Nov-26	03-Dec-26	0%	0%
Manholes		45	13-Oct-26	24-Dec-26	20-Aug-26	03-Dec-26	21.98%	42.31%
bedding Works		21	13-Oct-26	05-Nov-26	20-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	13-Oct-26	05-Nov-26	20-Aug-26	09-Nov-26	100%	50%
Install Manholes		21	07-Nov-26	30-Nov-26	27-Aug-26	09-Nov-26	9.52%	50%
SDR-2-CON-ST-Z	Manholes Installation	21	07-Nov-26	30-Nov-26	27-Aug-26	09-Nov-26	9.52%	50%
Testing		21	01-Dec-26	24-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-ST-Z	Testing for Manholes	21	01-Dec-26	24-Dec-26	10-Nov-26	03-Dec-26	0%	0%
STORM WATER LINE IN (PH2-A-MCF0)		84	25-Aug-26	01-Dec-26	06-Jul-26 A	03-Dec-26	38.87%	67.83%
Pipes Works		32	14-Oct-26	01-Dec-26	21-Sep-26	02-Dec-26	14.31%	75%
bedding Works		21	14-Oct-26	07-Nov-26	21-Sep-26	02-Dec-26	100%	75%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	14-Oct-26	07-Nov-26	21-Sep-26	02-Dec-26	100%	75%
Pipes Laying		21	08-Nov-26	01-Dec-26	01-Oct-26 A	02-Dec-26	4.78%	75%
SDR-2-CON-ST-Z	Install ST GRP Pipes	21	08-Nov-26	01-Dec-26	01-Oct-26 A	02-Dec-26	4.76%	75%
Manholes		62	25-Aug-26	13-Oct-26	06-Jul-26 A	03-Dec-26	100%	50%
Excavation		21	25-Aug-26	17-Sep-26	06-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-ST-Z	Excavation Manholes Section 2	21	25-Aug-26	17-Sep-26	06-Jul-26 A	09-Nov-26	100%	50%
bedding Works		21	19-Sep-26	13-Oct-26	08-Oct-26 A	03-Dec-26	100%	50%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	19-Sep-26	13-Oct-26	08-Oct-26 A	03-Dec-26	100%	50%
STORM WATER LINE IN (PH2-A-MCG0)		54	03-Sep-26	22-Oct-26	29-Jul-26 A	03-Dec-26	100%	64.17%
Pipes Works		21	26-Sep-26	19-Oct-26	08-Oct-26 A	02-Dec-26	100%	75%
bedding Works		21	26-Sep-26	19-Oct-26	08-Oct-26 A	02-Dec-26	100%	75%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	26-Sep-26	19-Oct-26	08-Oct-26 A	02-Dec-26	100%	75%
Manholes		54	03-Sep-26	22-Oct-26	29-Jul-26 A	03-Dec-26	100%	60.71%
Excavation		21	03-Sep-26	28-Sep-26	29-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-ST-Z	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	29-Jul-26 A	09-Nov-26	100%	75%
bedding Works		21	29-Sep-26	22-Oct-26	07-Oct-26 A	03-Dec-26	100%	50%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	07-Oct-26 A	03-Dec-26	100%	50%
STORM WATER LINE IN (PH2-A-MCH0)		78	03-Sep-26	22-Oct-26	13-Jul-26 A	03-Dec-26	100%	26.65%

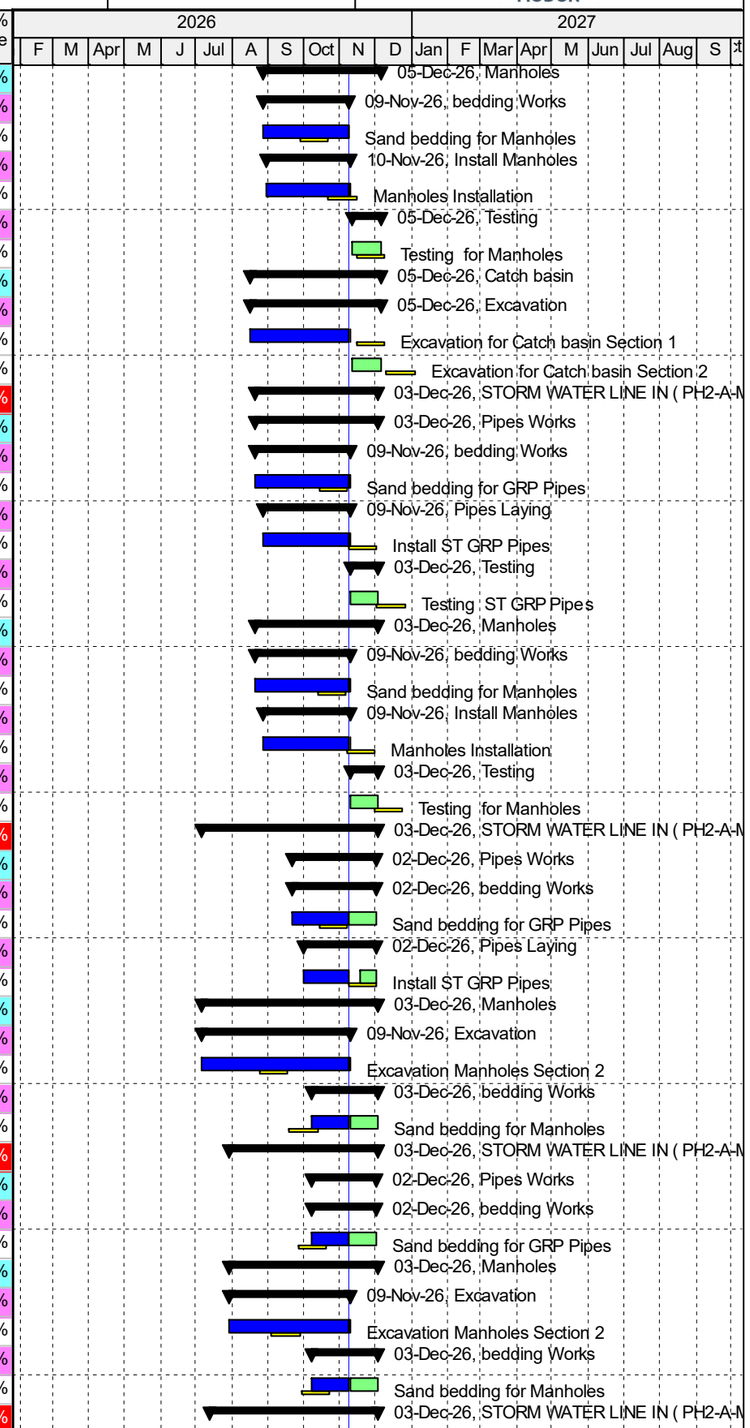

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Pipes Works		21	26-Sep-26	19-Oct-26	10-Oct-26 A	02-Dec-26	100%	30%
bedding Works		21	26-Sep-26	19-Oct-26	10-Oct-26 A	02-Dec-26	100%	30%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	26-Sep-26	19-Oct-26	10-Oct-26 A	02-Dec-26	100%	30%
Manholes		78	03-Sep-26	22-Oct-26	13-Jul-26 A	03-Dec-26	100%	25.71%
Excavation		21	03-Sep-26	28-Sep-26	13-Jul-26 A	09-Nov-26	100%	60%
SDR-2-CON-ST-Z	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	13-Jul-26 A	09-Nov-26	100%	60%
bedding Works		21	29-Sep-26	22-Oct-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	10-Nov-26	03-Dec-26	100%	0%
STORM WATER LINE IN (PH2-A-MCA0)		69	30-Aug-26	11-Nov-26	14-Jul-26 A	03-Dec-26	88.21%	25.6%
Pipes Works		39	24-Sep-26	11-Nov-26	01-Oct-26 A	02-Dec-26	87.51%	25%
bedding Works		21	24-Sep-26	18-Oct-26	01-Oct-26 A	02-Dec-26	100%	25%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	24-Sep-26	18-Oct-26	01-Oct-26 A	02-Dec-26	100%	25%
Pipes Laying		21	19-Oct-26	11-Nov-26	22-Oct-26 A	02-Dec-26	86.12%	25%
SDR-2-CON-ST-Z	Install ST GRP Pipes	21	19-Oct-26	11-Nov-26	22-Oct-26 A	02-Dec-26	85.71%	25%
Manholes		58	30-Aug-26	18-Oct-26	14-Jul-26 A	03-Dec-26	100%	35.71%
Excavation		21	30-Aug-26	22-Sep-26	14-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-ST-Z	Excavation Manholes Section 2	21	30-Aug-26	22-Sep-26	14-Jul-26 A	09-Nov-26	100%	50%
bedding Works		21	24-Sep-26	18-Oct-26	07-Oct-26 A	03-Dec-26	100%	25%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	24-Sep-26	18-Oct-26	07-Oct-26 A	03-Dec-26	100%	25%
STORM WATER LINE IN (PH2-A-MCI0)		78	03-Sep-26	22-Oct-26	30-Jul-26 A	03-Dec-26	100%	38.92%
Pipes Works		21	29-Sep-26	22-Oct-26	17-Oct-26 A	02-Dec-26	100%	50%
bedding Works		21	29-Sep-26	22-Oct-26	17-Oct-26 A	02-Dec-26	100%	50%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	29-Sep-26	22-Oct-26	17-Oct-26 A	02-Dec-26	100%	50%
Manholes		78	03-Sep-26	22-Oct-26	30-Jul-26 A	03-Dec-26	100%	21.43%
Excavation		21	03-Sep-26	28-Sep-26	30-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-ST-Z	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	30-Jul-26 A	09-Nov-26	100%	50%
bedding Works		21	29-Sep-26	22-Oct-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-ST-Z	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	10-Nov-26	03-Dec-26	100%	0%
STORM WATER LINE From STA-A2/10 TO STA-A2/1		21	15-Aug-26	27-Oct-26	27-Oct-26 A	02-Dec-26	100%	13.13%
Pipes Works		21	04-Oct-26	27-Oct-26	27-Oct-26 A	02-Dec-26	100%	15%
bedding Works		21	04-Oct-26	27-Oct-26	27-Oct-26 A	02-Dec-26	100%	15%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	04-Oct-26	27-Oct-26	27-Oct-26 A	02-Dec-26	100%	15%
Manholes		21	15-Aug-26	07-Sep-26	09-Nov-26	02-Dec-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SDR-2-CON-ST-Z	Excavation Manholes Section 1	21	15-Aug-26	07-Sep-26	09-Nov-26	02-Dec-26	100%	0%
STORM WATER LINE From IP A7 To Pond A		91	19-Aug-26	04-Nov-26	12-Aug-26	03-Dec-26	100%	70%
Pipes Works		91	19-Aug-26	04-Nov-26	12-Aug-26	03-Dec-26	100%	72%
Excavation		45	19-Aug-26	11-Oct-26	12-Aug-26	09-Nov-26	100%	90%
SDR-2-CON-ST-Z	Excavation for GRP Pipes Section 1	21	19-Aug-26	12-Sep-26	12-Aug-26	09-Nov-26	100%	90%
SDR-2-CON-ST-Z	Excavation for GRP Pipes Section 2	21	16-Sep-26	11-Oct-26	12-Aug-26	09-Nov-26	100%	90%
bedding Works		21	12-Oct-26	04-Nov-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-ST-Z	Sand bedding for GRP Pipes	21	12-Oct-26	04-Nov-26	10-Nov-26	03-Dec-26	100%	0%
Manholes		21	19-Aug-26	12-Sep-26	09-Nov-26	02-Dec-26	100%	0%
Excavation		21	19-Aug-26	12-Sep-26	09-Nov-26	02-Dec-26	100%	0%
SDR-2-CON-ST-Z	Excavation Manholes Section 1	21	19-Aug-26	12-Sep-26	09-Nov-26	02-Dec-26	100%	0%
Concrete Box culverts		14	25-Jul-26	15-Oct-26	09-Nov-26	24-Nov-26	100%	0%
For Pond A		14	30-Sep-26	15-Oct-26	09-Nov-26	24-Nov-26	100%	0%

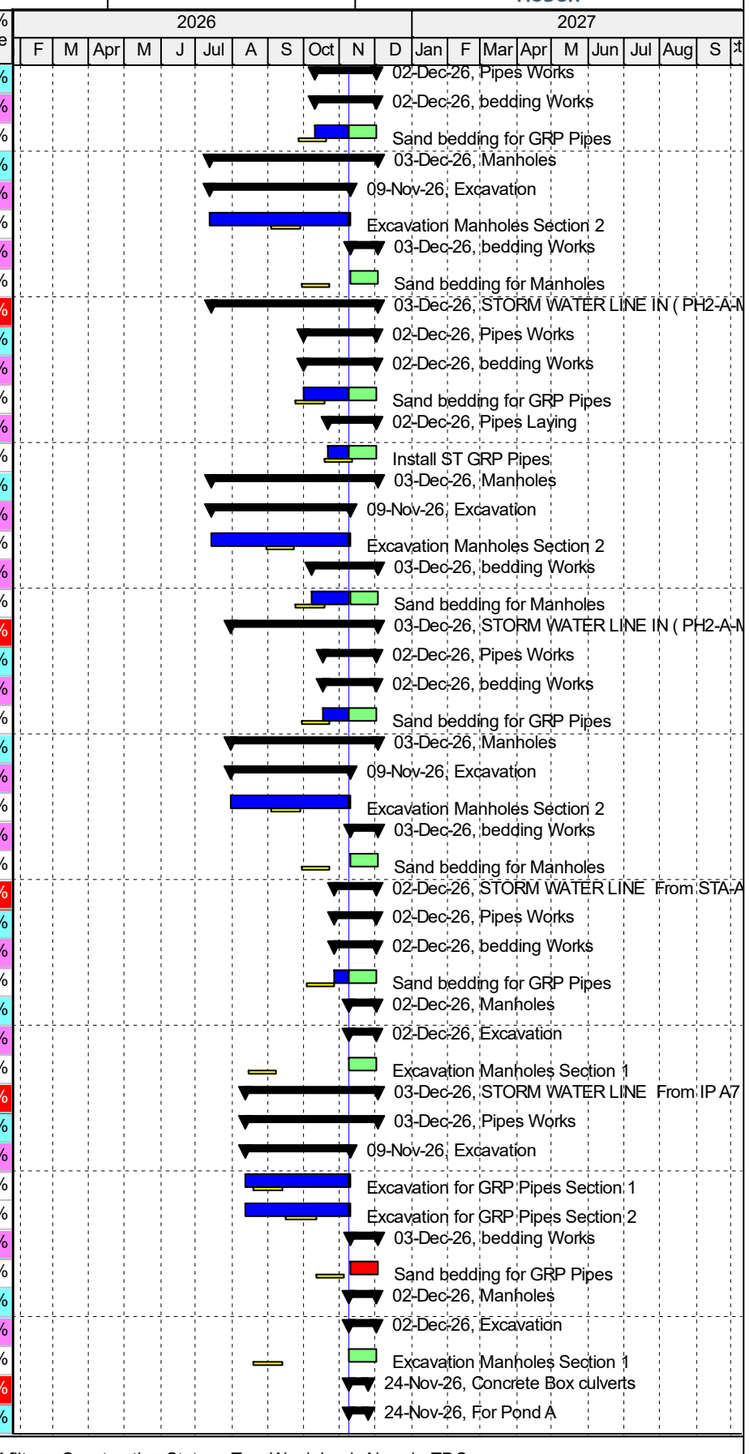

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Plain Concrete		6	30-Sep-26	06-Oct-26	09-Nov-26	15-Nov-26	100%	0%
SDR-2-CON-ST-Z	Plain Concrete for box culvert	6	30-Sep-26	06-Oct-26	09-Nov-26	15-Nov-26	100%	0%
Steel Reinforcement		8	07-Oct-26	15-Oct-26	16-Nov-26	24-Nov-26	100%	0%
SDR-2-CON-ST-Z	Steel Reinforcement for box culverts	8	07-Oct-26	15-Oct-26	16-Nov-26	24-Nov-26	100%	0%
For Pond B		14	25-Jul-26	09-Aug-26	09-Nov-26	24-Nov-26	100%	0%
Backfilling with common / suitable excavated material		8	25-Jul-26	02-Aug-26	09-Nov-26	17-Nov-26	100%	0%
SDR-2-CON-ST-Z	Backfilling with common / suitable excavated material or with suitabl	8	25-Jul-26	02-Aug-26	09-Nov-26	17-Nov-26	100%	0%
Plain Concrete		6	03-Aug-26	09-Aug-26	18-Nov-26	24-Nov-26	100%	0%
SDR-2-CON-ST-Z	Plain Concrete for box culvert	6	03-Aug-26	09-Aug-26	18-Nov-26	24-Nov-26	100%	0%
For Pond C		10	06-Aug-26	17-Aug-26	12-Nov-26	23-Nov-26	100%	0%
Excavation		10	06-Aug-26	17-Aug-26	12-Nov-26	23-Nov-26	100%	0%
SDR-2-CON-ST-Z	Excavation for Box Culvert.	10	06-Aug-26	17-Aug-26	12-Nov-26	23-Nov-26	100%	0%
Drainage works for ponds and open canals		132	08-Jul-26	14-Sep-26	31-Aug-26	09-Dec-26	100%	14.96%
Pond A		118	25-Jul-26	14-Sep-26	31-Aug-26	09-Dec-26	100%	15%
Sand lining for pond bed		118	25-Jul-26	14-Sep-26	31-Aug-26	09-Dec-26	100%	15%
SDR-2-CON-ST-Z	Sand lining for pond bed Section 1 & Section 2	21	25-Jul-26	17-Aug-26	31-Aug-26	11-Nov-26	100%	30%
SDR-2-CON-ST-Z	Sand lining for pond bed Section 3 & Section 4	21	22-Aug-26	14-Sep-26	16-Nov-26	09-Dec-26	100%	0%
Pond C		129	08-Jul-26	30-Aug-26	31-Aug-26	06-Dec-26	100%	11.67%
Excavation		129	08-Jul-26	30-Aug-26	31-Aug-26	06-Dec-26	100%	11.67%
SDR-2-CON-ST-Z	Excavation for cutting material. Section 2	21	08-Jul-26	01-Aug-26	31-Aug-26	11-Nov-26	100%	25%
SDR-2-CON-ST-Z	Excavation for cutting material. Section 3	21	06-Aug-26	30-Aug-26	12-Nov-26	06-Dec-26	100%	0%
ZONE G		60	21-Nov-26	28-Jan-27	31-Aug-26	18-Nov-26	0%	25%
STORM WATER LINE IN (PH2-G-MCE0)		21	05-Jan-27	28-Jan-27	31-Aug-26	11-Nov-26	0%	25%
Manholes		21	05-Jan-27	28-Jan-27	31-Aug-26	11-Nov-26	0%	25%
Testing		21	05-Jan-27	28-Jan-27	31-Aug-26	11-Nov-26	0%	25%
SDR-2-CON-ST-Z	Testing for Manholes	21	05-Jan-27	28-Jan-27	31-Aug-26	11-Nov-26	0%	25%
STORM WATER LINE IN (PH2-G-MCF0)		21	22-Nov-26	15-Dec-26	31-Aug-26	11-Nov-26	0%	25%
Manholes		21	22-Nov-26	15-Dec-26	31-Aug-26	11-Nov-26	0%	25%
Testing		21	22-Nov-26	15-Dec-26	31-Aug-26	11-Nov-26	0%	25%
SDR-2-CON-ST-Z	Testing for Manholes	21	22-Nov-26	15-Dec-26	31-Aug-26	11-Nov-26	0%	25%
STORM WATER LINE IN (PH2-G-MCG0)		21	21-Nov-26	14-Dec-26	07-Sep-26	18-Nov-26	0%	25%
Manholes		21	21-Nov-26	14-Dec-26	07-Sep-26	18-Nov-26	0%	25%
Testing		21	21-Nov-26	14-Dec-26	07-Sep-26	18-Nov-26	0%	25%
SDR-2-CON-ST-Z	Testing for Manholes	21	21-Nov-26	14-Dec-26	07-Sep-26	18-Nov-26	0%	25%
Sewerage Network		91	09-Dec-26	03-Apr-27	22-Jun-26 A	09-Dec-26	0%	56.28%
ZONE A		86	09-Dec-26	03-Apr-27	22-Jun-26 A	09-Dec-26	0%	59.86%
LINE 1 (PH2-A-MCA0)		67	09-Dec-26	04-Mar-27	22-Jun-26 A	05-Dec-26	0%	52.71%
Pipes Work		66	09-Dec-26	20-Feb-27	22-Jun-26 A	05-Dec-26	0%	61.33%
Pipes Laying		21	09-Dec-26	02-Jan-27	22-Jun-26 A	09-Nov-26	0%	90%
SDR-2-CON-SE-Z	200 mm GRP Pipe Laying	21	09-Dec-26	02-Jan-27	22-Jun-26 A	09-Nov-26	0%	90%
Testing		21	03-Jan-27	26-Jan-27	16-Aug-26	10-Nov-26	0%	55%
SDR-2-CON-SE-Z	Testing of 200 mm GRP Pipe.	21	03-Jan-27	26-Jan-27	16-Aug-26	10-Nov-26	0%	55%
Backfilling		21	27-Jan-27	20-Feb-27	11-Nov-26	05-Dec-26	0%	0%
SDR-2-CON-SE-Z	Backfilling of 200 mm GRP Pipe.	21	27-Jan-27	20-Feb-27	11-Nov-26	05-Dec-26	0%	0%
Manholes		65	14-Jan-27	04-Mar-27	09-Jul-26 A	03-Dec-26	0%	20%
Testing		21	14-Jan-27	07-Feb-27	09-Jul-26 A	09-Nov-26	0%	60%
SDR-2-CON-SE-Z	Testing	21	14-Jan-27	07-Feb-27	09-Jul-26 A	09-Nov-26	0%	60%

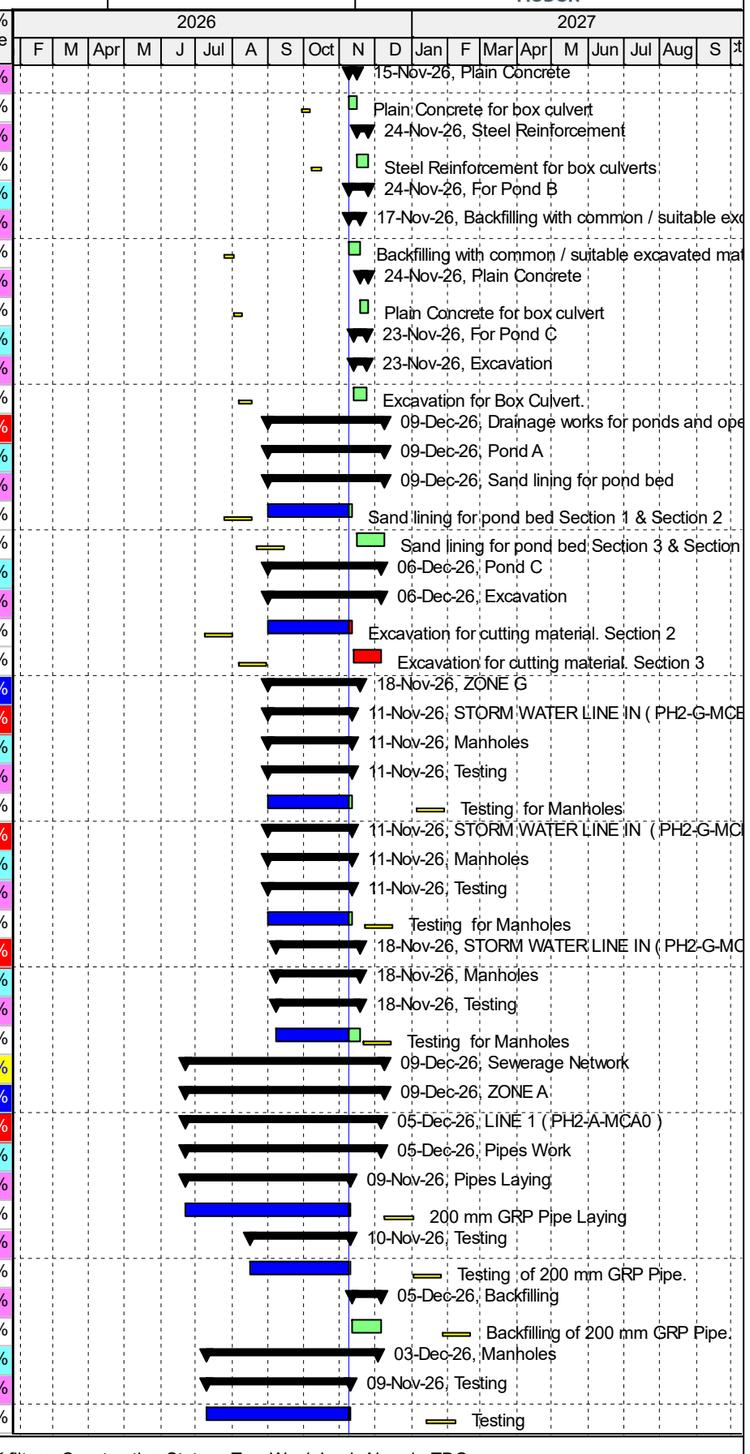

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Backfilling		21	08-Feb-27	04-Mar-27	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-SE-Z	Backfilling	21	08-Feb-27	04-Mar-27	10-Nov-26	03-Dec-26	0%	0%
LINE 4 AND LINE 5 (PH2-A-MCD0)		21	27-Dec-26	19-Jan-27	21-Jul-26 A	09-Nov-26	0%	90%
Pipes Work		21	27-Dec-26	19-Jan-27	21-Jul-26 A	09-Nov-26	0%	90%
Pipes Laying		21	27-Dec-26	19-Jan-27	21-Jul-26 A	09-Nov-26	0%	90%
SDR-2-CON-SE-Z	200 mm GRP Pipe Laying	21	27-Dec-26	19-Jan-27	21-Jul-26 A	09-Nov-26	0%	90%
LINE 8 AND LINE 9 (PH2-A-MCF0)		85	14-Jan-27	03-Apr-27	27-Jul-26 A	09-Dec-26	0%	44.03%
Pipes Work		85	14-Jan-27	03-Apr-27	27-Jul-26 A	03-Dec-26	0%	53%
Pipes Laying		21	14-Jan-27	07-Feb-27	27-Jul-26 A	09-Nov-26	0%	75%
SDR-2-CON-SE-Z	200 mm GRP Pipe Laying	21	14-Jan-27	07-Feb-27	27-Jul-26 A	09-Nov-26	0%	75%
Testing		21	08-Feb-27	04-Mar-27	18-Aug-26	09-Nov-26	0%	60%
SDR-2-CON-SE-Z	Testing of 200 mm GRP Pipe.	21	08-Feb-27	04-Mar-27	18-Aug-26	09-Nov-26	0%	60%
Backfilling		21	06-Mar-27	03-Apr-27	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-SE-Z	Backfilling of 200 mm GRP Pipe.	21	06-Mar-27	03-Apr-27	10-Nov-26	03-Dec-26	0%	0%
Manholes		77	24-Jan-27	25-Mar-27	27-Aug-26	09-Dec-26	0%	10%
Testing		21	24-Jan-27	16-Feb-27	27-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-SE-Z	Testing	21	24-Jan-27	16-Feb-27	27-Aug-26	09-Nov-26	0%	30%
Backfilling		18	01-Mar-27	25-Mar-27	19-Nov-26	09-Dec-26	0%	0%
SDR-2-CON-SE-Z	Backfilling	18	01-Mar-27	25-Mar-27	19-Nov-26	09-Dec-26	0%	0%
LINE 10 AND LINE 11 (PH2-A-MCG0)		21	17-Dec-26	10-Jan-27	27-Jul-26 A	09-Nov-26	0%	75%
Pipes Work		21	17-Dec-26	10-Jan-27	27-Jul-26 A	09-Nov-26	0%	75%
Pipes Laying		21	17-Dec-26	10-Jan-27	27-Jul-26 A	09-Nov-26	0%	75%
SDR-2-CON-SE-Z	200 mm GRP Pipe Laying	21	17-Dec-26	10-Jan-27	27-Jul-26 A	09-Nov-26	0%	75%
LINE 12 AND LINE 13 (PH2-A-MCH0)		59	24-Dec-26	03-Mar-27	25-Jul-26 A	03-Dec-26	0%	62.11%
Pipes Work		58	24-Dec-26	10-Feb-27	25-Jul-26 A	03-Dec-26	0%	69.55%
Pipes Laying		21	24-Dec-26	17-Jan-27	25-Jul-26 A	09-Nov-26	0%	85%
SDR-2-CON-SE-Z	200 mm GRP Pipe Laying	21	24-Dec-26	17-Jan-27	25-Jul-26 A	09-Nov-26	0%	85%
Testing		21	18-Jan-27	10-Feb-27	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-SE-Z	Testing of 200 mm GRP Pipe.	21	18-Jan-27	10-Feb-27	10-Nov-26	03-Dec-26	0%	0%
Manholes		21	07-Feb-27	03-Mar-27	09-Nov-26	02-Dec-26	0%	0%
Testing		21	07-Feb-27	03-Mar-27	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-SE-Z	Testing	21	07-Feb-27	03-Mar-27	09-Nov-26	02-Dec-26	0%	0%
ZONE G		43	04-Jan-27	23-Feb-27	07-Sep-26	18-Nov-26	0%	10%
LINE 49 AND LINE 51 (PH2-G-MCE0)		21	24-Jan-27	16-Feb-27	07-Sep-26	18-Nov-26	0%	10%
Manholes		21	24-Jan-27	16-Feb-27	07-Sep-26	18-Nov-26	0%	10%
Testing		21	24-Jan-27	16-Feb-27	07-Sep-26	18-Nov-26	0%	10%
SDR-2-CON-SE-Z	Testing	21	24-Jan-27	16-Feb-27	07-Sep-26	18-Nov-26	0%	10%
LINE 50 (PH2-G-MCD0)		21	30-Jan-27	23-Feb-27	07-Sep-26	18-Nov-26	0%	10%
Manholes		21	30-Jan-27	23-Feb-27	07-Sep-26	18-Nov-26	0%	10%
Testing		21	30-Jan-27	23-Feb-27	07-Sep-26	18-Nov-26	0%	10%
SDR-2-CON-SE-Z	Testing	21	30-Jan-27	23-Feb-27	07-Sep-26	18-Nov-26	0%	10%
LINE 52 AND LINE 53 (PH2-G-MCF0)		21	04-Jan-27	27-Jan-27	07-Sep-26	18-Nov-26	0%	10%
Manholes		21	04-Jan-27	27-Jan-27	07-Sep-26	18-Nov-26	0%	10%
Testing		21	04-Jan-27	27-Jan-27	07-Sep-26	18-Nov-26	0%	10%
SDR-2-CON-SE-Z	Testing	21	04-Jan-27	27-Jan-27	07-Sep-26	18-Nov-26	0%	10%
LINE 54 AND LINE 55 (PH2-G-MCG0)		21	18-Jan-27	10-Feb-27	07-Sep-26	18-Nov-26	0%	10%
Manholes		21	18-Jan-27	10-Feb-27	07-Sep-26	18-Nov-26	0%	10%

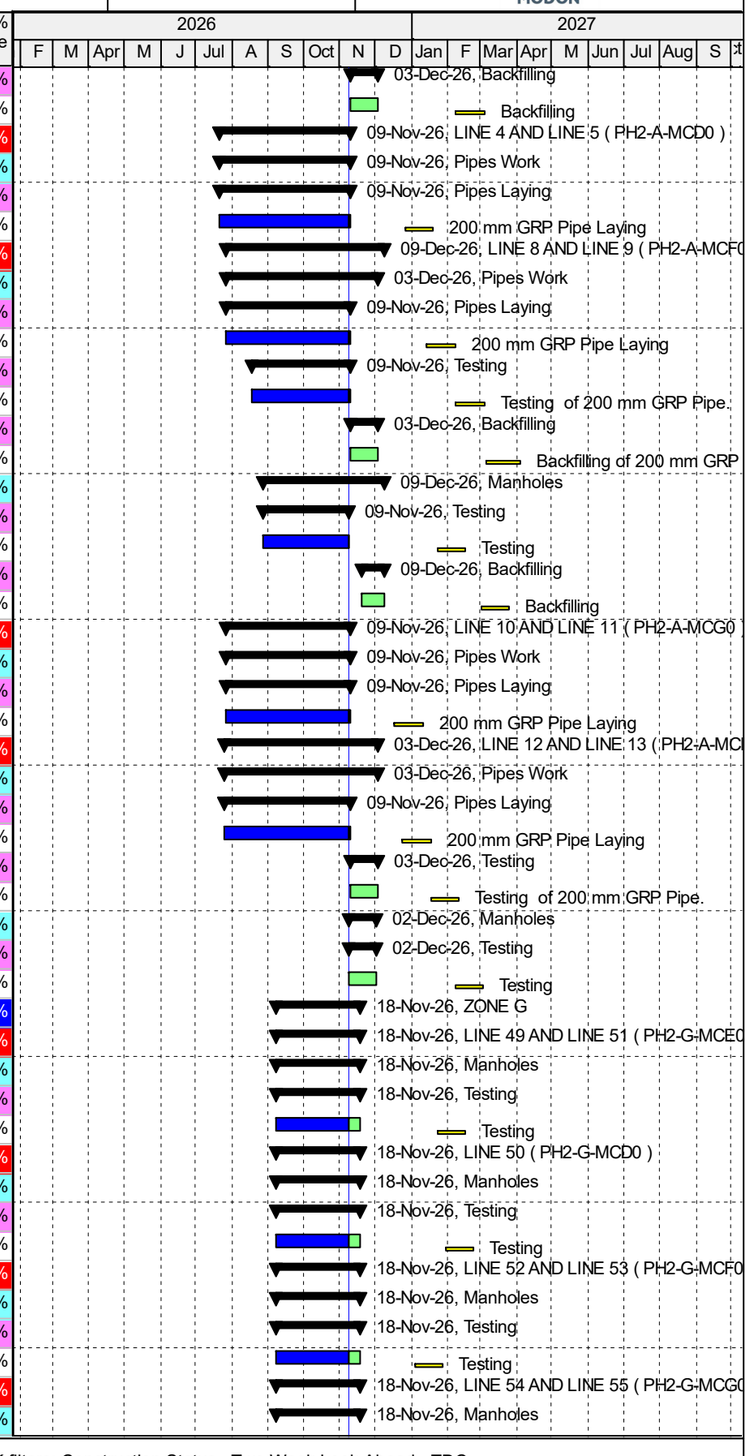

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Testing		21	18-Jan-27	10-Feb-27	07-Sep-26	18-Nov-26	0%	10%
SDR-2-CON-SE-Z	Testing	21	18-Jan-27	10-Feb-27	07-Sep-26	18-Nov-26	0%	10%
TSE Network		138	16-Nov-26	28-Mar-27	12-Aug-26	03-Dec-26	0%	20.72%
ZONE A		76	23-Nov-26	01-Mar-27	04-Oct-26 A	02-Dec-26	0%	19.83%
TSE NETWORK IN (PH2-A-MCC0)		57	02-Dec-26	26-Dec-26	04-Oct-26 A	02-Dec-26	0%	54.67%
Pipes Work		21	02-Dec-26	26-Dec-26	04-Oct-26 A	09-Nov-26	0%	75%
Excavation		21	02-Dec-26	26-Dec-26	04-Oct-26 A	09-Nov-26	0%	75%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 125 mm Section 2	21	02-Dec-26	26-Dec-26	04-Oct-26 A	09-Nov-26	0%	75%
Valve Chambers & Valves		21	02-Dec-26	26-Dec-26	09-Nov-26	02-Dec-26	0%	0%
Excavation		21	02-Dec-26	26-Dec-26	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	21	02-Dec-26	26-Dec-26	09-Nov-26	02-Dec-26	0%	0%
TSE NETWORK IN (PH2-A-MCD0)		57	02-Dec-26	06-Feb-27	04-Oct-26 A	01-Dec-26	0%	20.47%
Pipes Work		57	02-Dec-26	06-Feb-27	04-Oct-26 A	29-Nov-26	0%	43.33%
Excavation		20	02-Dec-26	24-Dec-26	04-Oct-26 A	09-Nov-26	0%	50%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 90 mm Section 2	20	02-Dec-26	24-Dec-26	04-Oct-26 A	09-Nov-26	0%	50%
bedding Works		18	17-Jan-27	06-Feb-27	22-Oct-26 A	29-Nov-26	0%	30%
SDR-2-CON-TS-Z	Sand bedding for TSE HDPE Pipes 90 mm	18	17-Jan-27	06-Feb-27	22-Oct-26 A	29-Nov-26	0%	30%
Valve Chambers & Valves		20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	02-Dec-26	24-Dec-26	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-A-MCE0)		21	13-Dec-26	05-Jan-27	09-Nov-26	02-Dec-26	0%	0%
Valve Chambers & Valves		21	13-Dec-26	05-Jan-27	09-Nov-26	02-Dec-26	0%	0%
Excavation		21	13-Dec-26	05-Jan-27	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	21	13-Dec-26	05-Jan-27	09-Nov-26	02-Dec-26	0%	0%
TSE NETWORK IN (PH2-A-MCF0)		24	21-Dec-26	01-Mar-27	10-Oct-26 A	01-Dec-26	0%	17.24%
Pipes Work		20	06-Feb-27	01-Mar-27	10-Oct-26 A	01-Dec-26	0%	75%
bedding Works		20	06-Feb-27	01-Mar-27	10-Oct-26 A	01-Dec-26	0%	75%
SDR-2-CON-TS-Z	Sand bedding for TSE HDPE Pipes 90 mm	20	06-Feb-27	01-Mar-27	10-Oct-26 A	01-Dec-26	0%	75%
Valve Chambers & Valves		20	21-Dec-26	12-Jan-27	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	21-Dec-26	12-Jan-27	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	21-Dec-26	12-Jan-27	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-A-MCG0)		20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Pipes Work		20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 90 mm Section 1	20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Valve Chambers & Valves		20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	23-Nov-26	15-Dec-26	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-A-MCH0)		20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Pipes Work		20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 250 mm Section 1	20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Valve Chambers & Valves		20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	29-Nov-26	21-Dec-26	09-Nov-26	01-Dec-26	0%	0%
ZONE G		102	16-Nov-26	28-Mar-27	12-Aug-26	03-Dec-26	0%	20.96%
TSE NETWORK IN (PH2-G-MCA0)		102	30-Nov-26	28-Mar-27	12-Aug-26	01-Dec-26	0%	19.35%

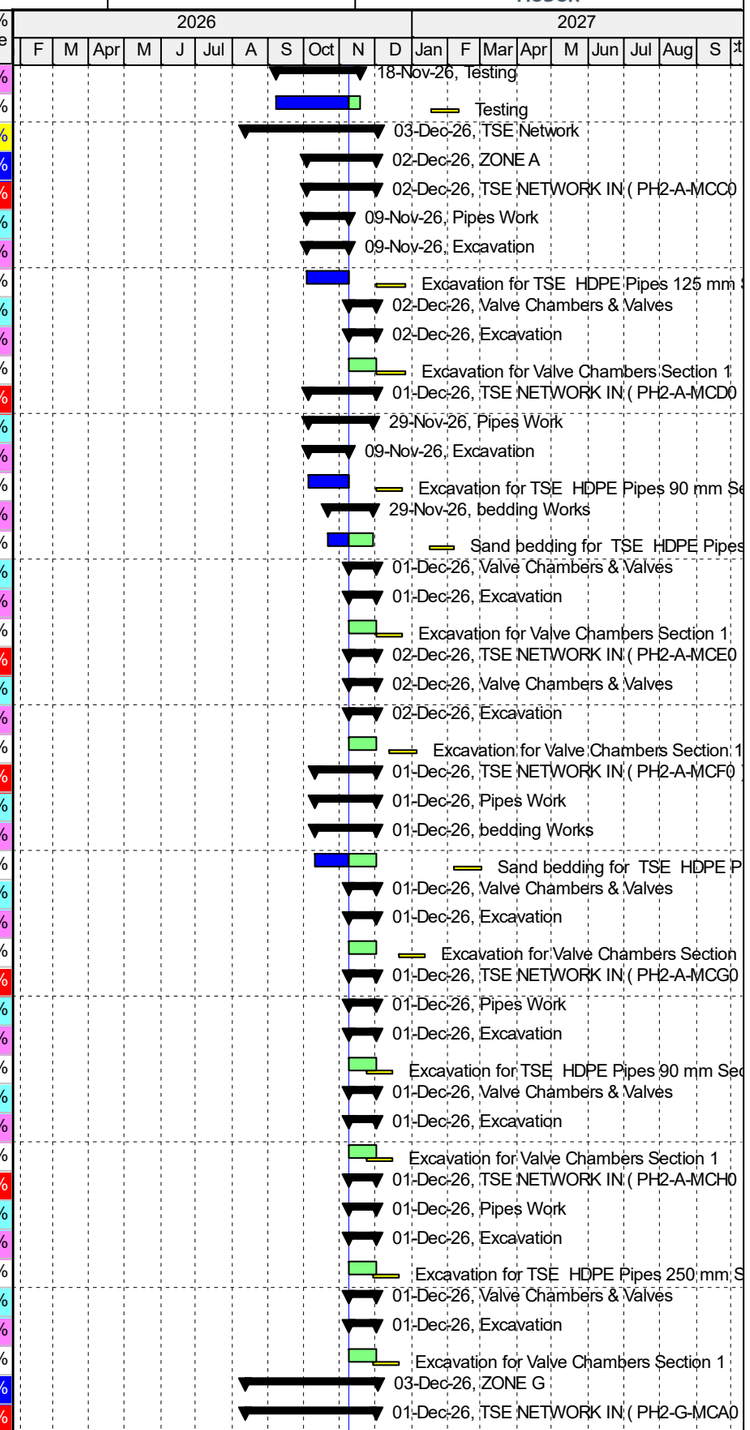

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Pipes Work		101	30-Nov-26	28-Mar-27	12-Aug-26	24-Nov-26	0%	20%
Excavation		42	30-Nov-26	17-Jan-27	12-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 225 mm Section 1	21	30-Nov-26	23-Dec-26	12-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 225 mm Section 2	21	24-Dec-26	17-Jan-27	12-Aug-26	09-Nov-26	0%	30%
bedding Works		21	18-Jan-27	10-Feb-27	24-Aug-26	09-Nov-26	0%	20%
SDR-2-CON-TS-Z	Sand bedding for TSE HDPE Pipes 225 mm	21	18-Jan-27	10-Feb-27	24-Aug-26	09-Nov-26	0%	20%
Pipes Laying		21	11-Feb-27	08-Mar-27	25-Aug-26	09-Nov-26	0%	20%
SDR-2-CON-TS-Z	Install TSE 225 mm HDPE Pipe	21	11-Feb-27	08-Mar-27	25-Aug-26	09-Nov-26	0%	20%
Testing		13	14-Mar-27	28-Mar-27	10-Nov-26	24-Nov-26	0%	0%
SDR-2-CON-TS-Z	Testing of TSE HDPE Pipe 225 mm.	13	14-Mar-27	28-Mar-27	10-Nov-26	24-Nov-26	0%	0%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-G-MCE0)		60	02-Dec-26	11-Feb-27	12-Aug-26	03-Dec-26	0%	20.89%
Pipes Work		60	02-Dec-26	11-Feb-27	12-Aug-26	03-Dec-26	0%	24%
Excavation		41	02-Dec-26	18-Jan-27	12-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 125 mm Section 1	21	02-Dec-26	26-Dec-26	12-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 125 mm Section 2	20	27-Dec-26	18-Jan-27	12-Aug-26	09-Nov-26	0%	30%
bedding Works		21	19-Jan-27	11-Feb-27	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TS-Z	Sand bedding for TSE HDPE Pipes 125 mm	21	19-Jan-27	11-Feb-27	10-Nov-26	03-Dec-26	0%	0%
Valve Chambers & Valves		21	02-Dec-26	26-Dec-26	10-Nov-26	03-Dec-26	0%	0%
Excavation		21	02-Dec-26	26-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	21	02-Dec-26	26-Dec-26	10-Nov-26	03-Dec-26	0%	0%
TSE NETWORK IN (PH2-G-MCF0)		27	16-Nov-26	09-Dec-26	13-Aug-26	01-Dec-26	0%	11.22%
Pipes Work		21	16-Nov-26	09-Dec-26	13-Aug-26	09-Nov-26	0%	30%
Excavation		21	16-Nov-26	09-Dec-26	13-Aug-26	09-Nov-26	0%	30%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 90 mm Section 1	21	16-Nov-26	09-Dec-26	13-Aug-26	09-Nov-26	0%	30%
Valve Chambers & Valves		20	16-Nov-26	08-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	16-Nov-26	08-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	16-Nov-26	08-Dec-26	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-G-MCG0)		58	30-Nov-26	08-Feb-27	13-Aug-26	03-Dec-26	0%	12.6%
Pipes Work		57	23-Dec-26	08-Feb-27	13-Aug-26	03-Dec-26	0%	26.67%
Excavation		20	23-Dec-26	14-Jan-27	13-Aug-26	09-Nov-26	0%	40%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 90 mm Section 2	20	23-Dec-26	14-Jan-27	13-Aug-26	09-Nov-26	0%	40%
bedding Works		21	16-Jan-27	08-Feb-27	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TS-Z	Sand bedding for TSE HDPE Pipes 90 mm	21	16-Jan-27	08-Feb-27	10-Nov-26	03-Dec-26	0%	0%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
TSE NETWORK IN (PH2-G-MCZ0)		59	30-Nov-26	16-Jan-27	13-Aug-26	01-Dec-26	0%	33.73%
Pipes Work		41	30-Nov-26	16-Jan-27	13-Aug-26	09-Nov-26	0%	40%
Excavation		41	30-Nov-26	16-Jan-27	13-Aug-26	09-Nov-26	0%	40%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 125 mm Section 1	21	30-Nov-26	23-Dec-26	13-Aug-26	09-Nov-26	0%	40%
SDR-2-CON-TS-Z	Excavation for TSE HDPE Pipes 125 mm Section 2	20	24-Dec-26	16-Jan-27	13-Aug-26	09-Nov-26	0%	40%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TS-Z	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	09-Nov-26	01-Dec-26	0%	0%

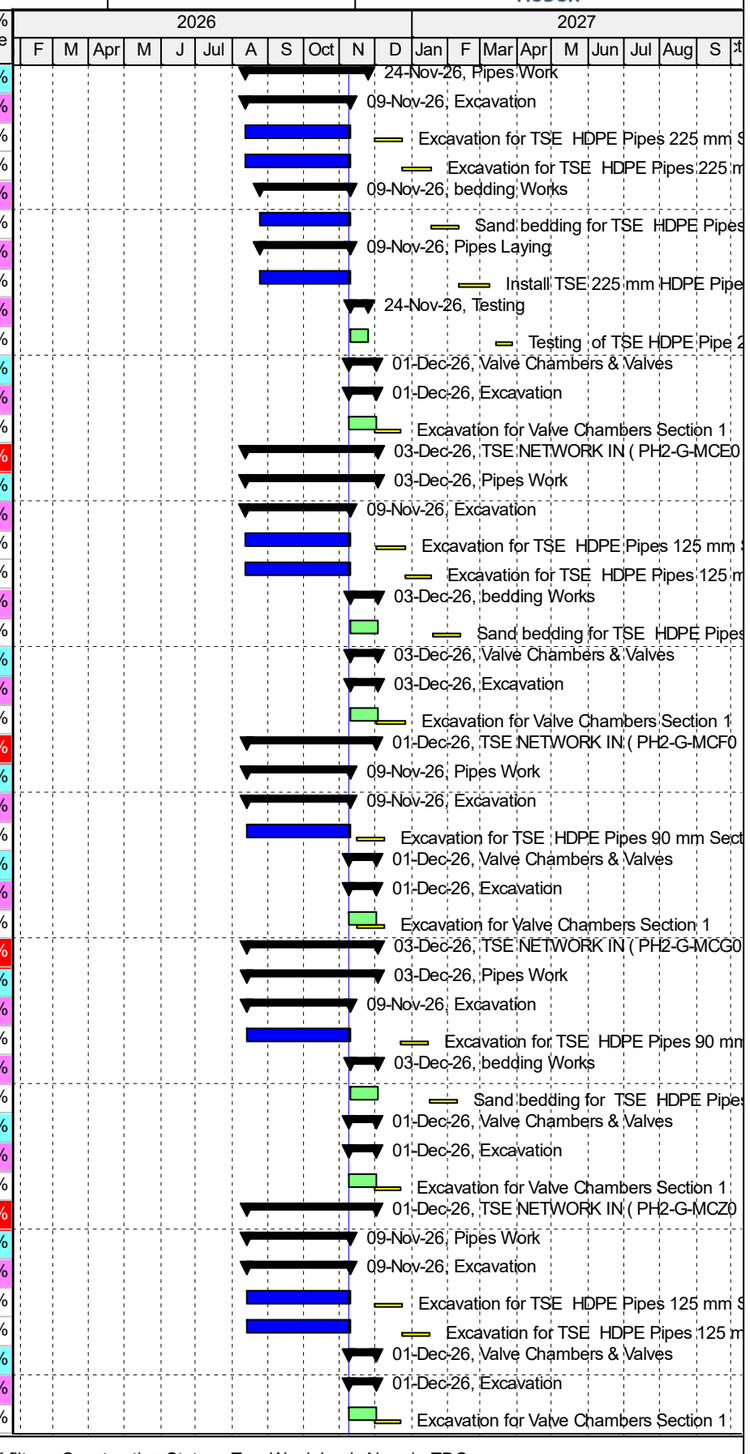

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Portable Water		139	07-Jan-27	26-May-27	01-Aug-26	07-Dec-26	0%	51.97%
ZONE A		20	07-Jan-27	30-Jan-27	09-Nov-26	01-Dec-26	0%	0%
PORTABLE WATER IN (PH2-A-MCE0)		20	07-Jan-27	30-Jan-27	09-Nov-26	01-Dec-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		20	07-Jan-27	30-Jan-27	09-Nov-26	01-Dec-26	0%	0%
Excavation		20	07-Jan-27	30-Jan-27	09-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-PW-...	Excavation for Valve Chambers Section 1	20	07-Jan-27	30-Jan-27	09-Nov-26	01-Dec-26	0%	0%
ZONE G		139	16-Jan-27	26-May-27	01-Aug-26	07-Dec-26	0%	52.58%
PORTABLE WATER IN (PH2-G-MCA0)		134	18-Jan-27	15-May-27	01-Aug-26	05-Dec-26	0%	56.25%
Pipes Work		133	14-Mar-27	15-May-27	01-Aug-26	05-Dec-26	0%	57.5%
bedding Works		16	14-Mar-27	31-Mar-27	01-Aug-26	09-Nov-26	0%	92%
SDR-2-CON-PW-...	Sand bedding for PW HDPE Pipes 400 mm	16	14-Mar-27	31-Mar-27	01-Aug-26	09-Nov-26	0%	92%
Pipes Laying		16	01-Apr-27	19-Apr-27	13-Aug-26	09-Nov-26	0%	92%
SDR-2-CON-PW-...	Install PW 400 mm HDPE Pipe	16	01-Apr-27	19-Apr-27	13-Aug-26	09-Nov-26	0%	92%
Testing		10	20-Apr-27	01-May-27	10-Nov-26	21-Nov-26	0%	0%
SDR-2-CON-PW-...	Testing of PW HDPE Pipe 400 mm.	10	20-Apr-27	01-May-27	10-Nov-26	21-Nov-26	0%	0%
Backfilling		12	02-May-27	15-May-27	22-Nov-26	05-Dec-26	0%	0%
SDR-2-CON-PW-...	Backfilling of PW HDPE Pipe 400 mm.	12	02-May-27	15-May-27	22-Nov-26	05-Dec-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	18-Jan-27	10-Feb-27	09-Nov-26	02-Dec-26	0%	0%
Excavation		21	18-Jan-27	10-Feb-27	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-PW-...	Excavation for Valve Chambers Section 1	21	18-Jan-27	10-Feb-27	09-Nov-26	02-Dec-26	0%	0%
PORTABLE WATER IN (PH2-G-MCE0)		138	15-Mar-27	24-May-27	13-Aug-26	02-Dec-26	0%	57.94%
Pipes Work		138	15-Mar-27	24-May-27	13-Aug-26	02-Dec-26	0%	57.94%
bedding Works		18	15-Mar-27	04-Apr-27	26-Aug-26	09-Nov-26	0%	45%
SDR-2-CON-PW-...	Sand bedding for PW HDPE Pipe 225 mm.	18	15-Mar-27	04-Apr-27	26-Aug-26	09-Nov-26	0%	45%
Pipes Laying		18	05-Apr-27	25-Apr-27	13-Aug-26	09-Nov-26	0%	98%
SDR-2-CON-PW-...	Install PW 225 mm HDPE Pipe	18	05-Apr-27	25-Apr-27	13-Aug-26	09-Nov-26	0%	98%
Testing		7	26-Apr-27	03-May-27	10-Nov-26	17-Nov-26	0%	0%
SDR-2-CON-PW-...	Testing of PW HDPE Pipe 225 mm.	7	26-Apr-27	03-May-27	10-Nov-26	17-Nov-26	0%	0%
Backfilling		13	04-May-27	24-May-27	18-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-PW-...	Backfilling of PW HDPE Pipe 225 mm.	13	04-May-27	24-May-27	18-Nov-26	02-Dec-26	0%	0%
PORTABLE WATER IN (PH2-G-MCG0)		118	16-Jan-27	22-May-27	26-Aug-26	07-Dec-26	0%	5.85%
Pipes Work		118	07-Mar-27	22-May-27	26-Aug-26	07-Dec-26	0%	7.14%
bedding Works		18	07-Mar-27	31-Mar-27	26-Aug-26	09-Nov-26	0%	50%
SDR-2-CON-PW-...	Sand bedding for PW HDPE Pipe 225 mm.	18	07-Mar-27	31-Mar-27	26-Aug-26	09-Nov-26	0%	50%
Testing		8	18-Apr-27	26-Apr-27	09-Nov-26	17-Nov-26	0%	0%
SDR-2-CON-PW-...	Testing of PW HDPE Pipe 225 mm.	8	18-Apr-27	26-Apr-27	09-Nov-26	17-Nov-26	0%	0%
Backfilling		17	27-Apr-27	22-May-27	18-Nov-26	07-Dec-26	0%	0%
SDR-2-CON-PW-...	Backfilling of PW HDPE Pipe 225 mm.	17	27-Apr-27	22-May-27	18-Nov-26	07-Dec-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	16-Jan-27	08-Feb-27	09-Nov-26	02-Dec-26	0%	0%
Excavation		21	16-Jan-27	08-Feb-27	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-PW-...	Excavation for Valve Chambers Section 1	21	16-Jan-27	08-Feb-27	09-Nov-26	02-Dec-26	0%	0%
PORTABLE WATER IN (PH2-G-MCZ0)		138	19-Jan-27	26-May-27	13-Aug-26	06-Dec-26	0%	54.09%
Pipes Work		137	15-Mar-27	26-May-27	13-Aug-26	06-Dec-26	0%	56.56%
bedding Works		19	15-Mar-27	05-Apr-27	26-Aug-26	09-Nov-26	0%	50%
SDR-2-CON-PW-...	Sand bedding for PW HDPE Pipes 315 mm	19	15-Mar-27	05-Apr-27	26-Aug-26	09-Nov-26	0%	50%
Pipes Laying		16	06-Apr-27	24-Apr-27	13-Aug-26	09-Nov-26	0%	95%
SDR-2-CON-PW-...	Install PW 315 mm HDPE Pipe	16	06-Apr-27	24-Apr-27	13-Aug-26	09-Nov-26	0%	95%

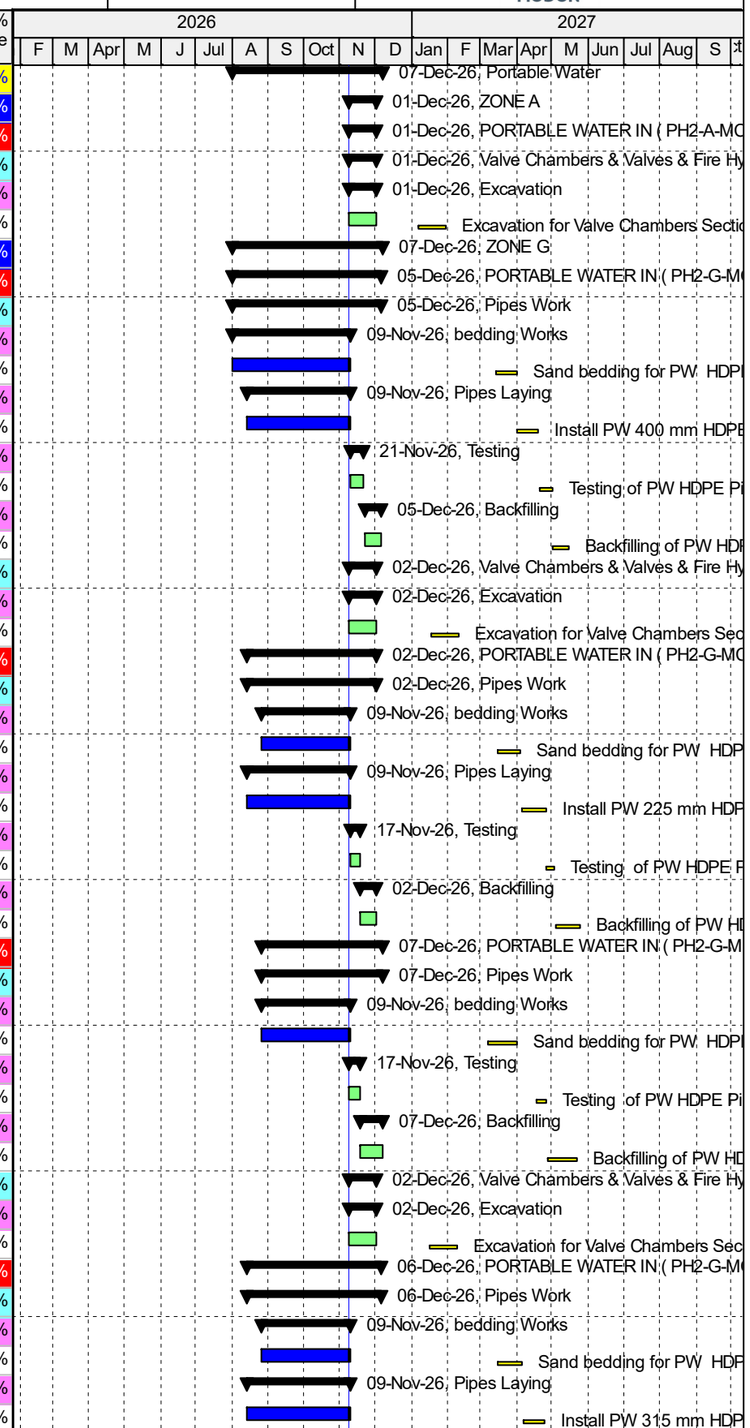

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Testing		6	25-Apr-27	01-May-27	10-Nov-26	16-Nov-26	0%	0%
SDR-2-CON-PW-Z	Testing of PW HDPE Pipe 315 mm.	6	25-Apr-27	01-May-27	10-Nov-26	16-Nov-26	0%	0%
Backfilling		17	02-May-27	26-May-27	17-Nov-26	06-Dec-26	0%	0%
SDR-2-CON-PW-Z	Backfilling of PW HDPE Pipe 315 mm.	17	02-May-27	26-May-27	17-Nov-26	06-Dec-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	19-Jan-27	11-Feb-27	09-Nov-26	02-Dec-26	0%	0%
Excavation		21	19-Jan-27	11-Feb-27	09-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-PW-Z	Excavation for Valve Chambers Section 1	21	19-Jan-27	11-Feb-27	09-Nov-26	02-Dec-26	0%	0%
Electrical Works		159	19-Jul-26	20-Jan-27	01-Jul-26 A	14-Dec-26	61.32%	29.01%
ZONE A		128	19-Jul-26	17-Dec-26	01-Jul-26 A	13-Dec-26	86.47%	34.75%
Street Lighting Network		126	19-Jul-26	13-Dec-26	01-Jul-26 A	13-Dec-26	83.68%	32.4%
Street Lighting Network IN (PH2-COL-MC10)		21	03-Aug-26	26-Aug-26	12-Aug-26	09-Nov-26	100%	20%
Excavation		21	03-Aug-26	26-Aug-26	12-Aug-26	09-Nov-26	100%	20%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	03-Aug-26	26-Aug-26	12-Aug-26	09-Nov-26	100%	20%
Street Lighting Network IN (PH2-COL-MC20)		21	06-Aug-26	30-Aug-26	13-Jul-26 A	09-Nov-26	100%	50%
Excavation		21	06-Aug-26	30-Aug-26	13-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	06-Aug-26	30-Aug-26	13-Jul-26 A	09-Nov-26	100%	50%
Street Lighting Network IN (PH2-A-MCA0)		42	19-Jul-26	05-Sep-26	01-Aug-26	09-Nov-26	100%	60%
Excavation		42	19-Jul-26	05-Sep-26	01-Aug-26	09-Nov-26	100%	60%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	19-Jul-26	11-Aug-26	01-Aug-26	09-Nov-26	100%	70%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	12-Aug-26	05-Sep-26	12-Aug-26	09-Nov-26	100%	50%
Street Lighting Network IN (PH2-A-MCB0)		115	25-Jul-26	31-Oct-26	04-Aug-26	06-Dec-26	100%	35%
Excavation		42	25-Jul-26	10-Sep-26	04-Aug-26	09-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	25-Jul-26	17-Aug-26	04-Aug-26	09-Nov-26	100%	80%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	18-Aug-26	10-Sep-26	12-Aug-26	09-Nov-26	100%	50%
Install Footings		21	12-Sep-26	06-Oct-26	31-Aug-26	11-Nov-26	100%	40%
SDR-2-CON-SL-Z	Install Footings	21	12-Sep-26	06-Oct-26	31-Aug-26	11-Nov-26	100%	40%
Backfilling		21	07-Oct-26	31-Oct-26	12-Nov-26	06-Dec-26	100%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	21	07-Oct-26	31-Oct-26	12-Nov-26	06-Dec-26	100%	0%
Street Lighting Network IN (PH2-A-MCC0)		113	30-Jul-26	05-Nov-26	20-Jul-26 A	09-Dec-26	100%	35%
Excavation		42	30-Jul-26	16-Sep-26	20-Jul-26 A	09-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	30-Jul-26	23-Aug-26	20-Jul-26 A	09-Nov-26	100%	80%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	24-Aug-26	16-Sep-26	01-Aug-26	09-Nov-26	100%	50%
Install Footings		21	17-Sep-26	12-Oct-26	03-Sep-26	15-Nov-26	100%	40%
SDR-2-CON-SL-Z	Install Footings	21	17-Sep-26	12-Oct-26	03-Sep-26	15-Nov-26	100%	40%
Backfilling		21	13-Oct-26	05-Nov-26	16-Nov-26	09-Dec-26	100%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	21	13-Oct-26	05-Nov-26	16-Nov-26	09-Dec-26	100%	0%
Street Lighting Network IN (PH2-A-MCD0)		108	05-Aug-26	11-Nov-26	20-Jul-26 A	09-Dec-26	95.24%	36.67%
Excavation		42	05-Aug-26	22-Sep-26	20-Jul-26 A	09-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	05-Aug-26	29-Aug-26	20-Jul-26 A	09-Nov-26	100%	80%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	30-Aug-26	22-Sep-26	01-Aug-26	09-Nov-26	100%	50%
Install Footings		21	24-Sep-26	18-Oct-26	03-Sep-26	15-Nov-26	100%	45%
SDR-2-CON-SL-Z	Install Footings	21	24-Sep-26	18-Oct-26	03-Sep-26	15-Nov-26	100%	45%
Backfilling		21	19-Oct-26	11-Nov-26	16-Nov-26	09-Dec-26	85.71%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	21	19-Oct-26	11-Nov-26	16-Nov-26	09-Dec-26	85.71%	0%
Street Lighting Network IN (PH2-A-MCE0)		103	11-Aug-26	17-Nov-26	02-Jul-26 A	09-Dec-26	87.3%	29.17%
Excavation		42	11-Aug-26	29-Sep-26	02-Jul-26 A	09-Nov-26	100%	57.5%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	11-Aug-26	03-Sep-26	02-Jul-26 A	09-Nov-26	100%	65%

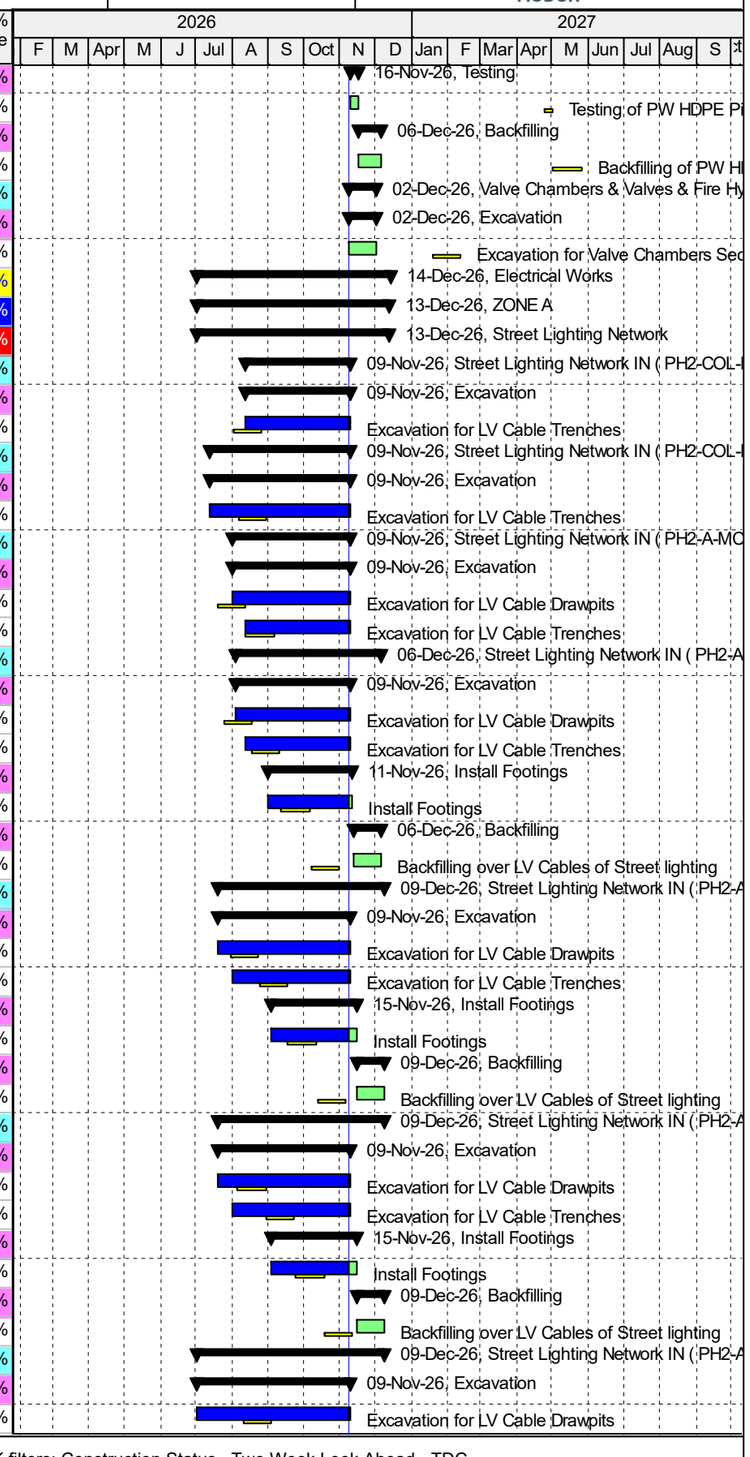

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	05-Sep-26	29-Sep-26	14-Jul-26 A	09-Nov-26	100%	50%
Install Footings		21	30-Sep-26	24-Oct-26	03-Sep-26	15-Nov-26	100%	30%
SDR-2-CON-SL-Z	Install Footings	21	30-Sep-26	24-Oct-26	03-Sep-26	15-Nov-26	100%	30%
Backfilling		21	25-Oct-26	17-Nov-26	16-Nov-26	09-Dec-26	61.9%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	21	25-Oct-26	17-Nov-26	16-Nov-26	09-Dec-26	61.9%	0%
Street Lighting Network IN (PH2-A-MCF0)		100	17-Aug-26	21-Nov-26	01-Jul-26 A	12-Dec-26	81.67%	29.17%
Excavation		42	17-Aug-26	05-Oct-26	01-Jul-26 A	18-Nov-26	100%	57.5%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	17-Aug-26	09-Sep-26	01-Jul-26 A	18-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	10-Sep-26	05-Oct-26	14-Jul-26 A	18-Nov-26	100%	50%
Install Footings		20	06-Oct-26	28-Oct-26	31-Aug-26	18-Nov-26	100%	30%
SDR-2-CON-SL-Z	Install Footings	20	06-Oct-26	28-Oct-26	31-Aug-26	18-Nov-26	100%	30%
Backfilling		20	29-Oct-26	21-Nov-26	19-Nov-26	12-Dec-26	45%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	20	29-Oct-26	21-Nov-26	19-Nov-26	12-Dec-26	45%	0%
Street Lighting Network IN (PH2-A-MCG0)		94	23-Aug-26	25-Nov-26	06-Jul-26 A	10-Dec-26	73.68%	29.17%
Excavation		42	23-Aug-26	11-Oct-26	06-Jul-26 A	18-Nov-26	100%	57.5%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	23-Aug-26	15-Sep-26	06-Jul-26 A	18-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	16-Sep-26	11-Oct-26	16-Jul-26 A	18-Nov-26	100%	50%
Install Footings		20	12-Oct-26	03-Nov-26	03-Sep-26	18-Nov-26	100%	30%
SDR-2-CON-SL-Z	Install Footings	20	12-Oct-26	03-Nov-26	03-Sep-26	18-Nov-26	100%	30%
Backfilling		19	04-Nov-26	25-Nov-26	19-Nov-26	10-Dec-26	21.05%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	19	04-Nov-26	25-Nov-26	19-Nov-26	10-Dec-26	21.05%	0%
Street Lighting Network IN (PH2-A-MCH0)		88	30-Aug-26	02-Dec-26	20-Jul-26 A	10-Dec-26	63.33%	29.17%
Excavation		42	30-Aug-26	18-Oct-26	20-Jul-26 A	18-Nov-26	100%	57.5%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	30-Aug-26	22-Sep-26	20-Jul-26 A	18-Nov-26	100%	65%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	24-Sep-26	18-Oct-26	01-Aug-26	18-Nov-26	100%	50%
Install Footings		20	19-Oct-26	10-Nov-26	03-Sep-26	18-Nov-26	90%	30%
SDR-2-CON-SL-Z	Install Footings	20	19-Oct-26	10-Nov-26	03-Sep-26	18-Nov-26	90%	30%
Backfilling		19	11-Nov-26	02-Dec-26	19-Nov-26	10-Dec-26	0%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	19	11-Nov-26	02-Dec-26	19-Nov-26	10-Dec-26	0%	0%
Street Lighting Network IN (PH2-ART-MC10)		84	06-Sep-26	13-Dec-26	20-Jul-26 A	13-Dec-26	52.38%	30%
Excavation		42	06-Sep-26	25-Oct-26	20-Jul-26 A	18-Nov-26	100%	60%
SDR-2-CON-SL-Z	Excavation for LV Cable Drawpits	21	06-Sep-26	30-Sep-26	20-Jul-26 A	18-Nov-26	100%	70%
SDR-2-CON-SL-Z	Excavation for LV Cable Trenches	21	01-Oct-26	25-Oct-26	01-Aug-26	18-Nov-26	100%	50%
Install Footings		21	26-Oct-26	18-Nov-26	03-Sep-26	18-Nov-26	57.14%	30%
SDR-2-CON-SL-Z	Install Footings	21	26-Oct-26	18-Nov-26	03-Sep-26	18-Nov-26	57.14%	30%
Backfilling		21	19-Nov-26	13-Dec-26	19-Nov-26	13-Dec-26	0%	0%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	21	19-Nov-26	13-Dec-26	19-Nov-26	13-Dec-26	0%	0%
Lighting Pole Panels		21	12-Sep-26	06-Oct-26	19-Nov-26	13-Dec-26	100%	0%
Excavation		21	12-Sep-26	06-Oct-26	19-Nov-26	13-Dec-26	100%	0%
SDR-2-CON-SL-Z	Street Lighting Panels Excavation	21	12-Sep-26	06-Oct-26	19-Nov-26	13-Dec-26	100%	0%
Ring Main Unit		20	12-Sep-26	05-Oct-26	19-Nov-26	12-Dec-26	100%	0%
Leveling		20	12-Sep-26	05-Oct-26	19-Nov-26	12-Dec-26	100%	0%
SDR-2-CON-SL-Z	Ring Main Unit leveling	20	12-Sep-26	05-Oct-26	19-Nov-26	12-Dec-26	100%	0%
Feeder Pillars		20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
Leveling		20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
SDR-2-CON-SL-Z	Feeder Pillars Leveling	20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
MV Network		100	09-Aug-26	21-Nov-26	14-Jul-26 A	03-Dec-26	90.26%	35.18%

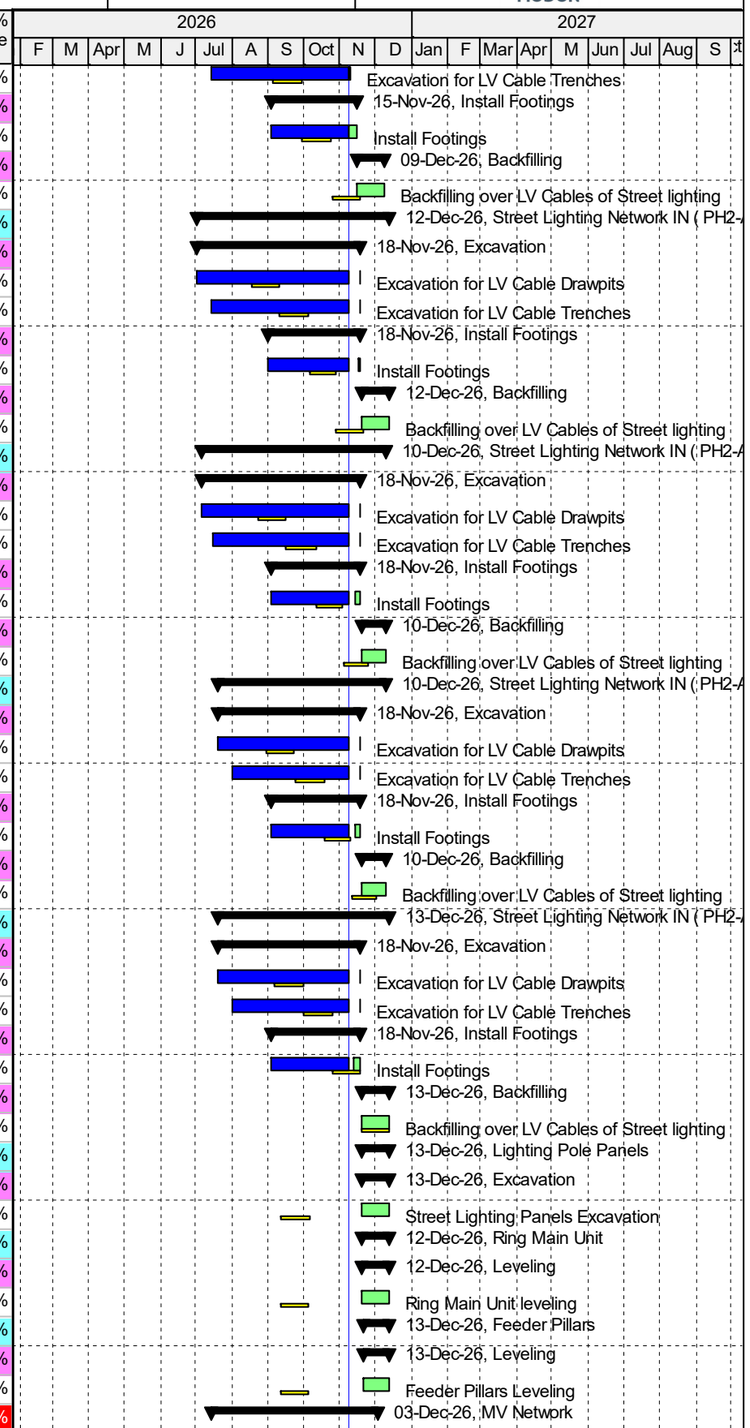

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
LOOP 3		100	09-Aug-26	14-Nov-26	14-Jul-26 A	03-Dec-26	85.71%	28%
Excavation		21	09-Aug-26	01-Sep-26	14-Jul-26 A	09-Nov-26	100%	70%
SDR-2-CON-MV-Z	Excavation Works	21	09-Aug-26	01-Sep-26	14-Jul-26 A	09-Nov-26	100%	70%
Pipe laying		20	02-Sep-26	26-Sep-26	25-Jul-26 A	09-Nov-26	100%	70%
SDR-2-CON-MV-Z	Pipe Laying	20	02-Sep-26	26-Sep-26	25-Jul-26 A	09-Nov-26	100%	70%
Backfilling		21	27-Sep-26	20-Oct-26	03-Aug-26	09-Nov-26	100%	70%
SDR-2-CON-MV-Z	Backfilling Works	21	27-Sep-26	20-Oct-26	03-Aug-26	09-Nov-26	100%	70%
Pulling Cable		21	21-Oct-26	14-Nov-26	10-Nov-26	03-Dec-26	76.19%	0%
SDR-2-CON-MV-Z	Pulling Cable	21	21-Oct-26	14-Nov-26	10-Nov-26	03-Dec-26	76.19%	0%
LOOP 4		90	20-Aug-26	02-Nov-26	25-Jul-26 A	03-Dec-26	100%	48.5%
Excavation		21	20-Aug-26	13-Sep-26	25-Jul-26 A	09-Nov-26	100%	70%
SDR-2-CON-MV-Z	Excavation Works	21	20-Aug-26	13-Sep-26	25-Jul-26 A	09-Nov-26	100%	70%
Pipe laying		21	14-Sep-26	08-Oct-26	13-Aug-26	09-Nov-26	100%	62%
SDR-2-CON-MV-Z	Pipe Laying	21	14-Sep-26	08-Oct-26	13-Aug-26	09-Nov-26	100%	62%
Backfilling		21	10-Oct-26	02-Nov-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-MV-Z	Backfilling Works	21	10-Oct-26	02-Nov-26	10-Nov-26	03-Dec-26	100%	0%
LOOP 5		81	31-Aug-26	12-Nov-26	13-Aug-26	03-Dec-26	95.24%	37.5%
Excavation		21	31-Aug-26	24-Sep-26	13-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Excavation Works	21	31-Aug-26	24-Sep-26	13-Aug-26	09-Nov-26	100%	50%
Pipe laying		21	26-Sep-26	19-Oct-26	13-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Pipe Laying	21	26-Sep-26	19-Oct-26	13-Aug-26	09-Nov-26	100%	50%
Backfilling		21	20-Oct-26	12-Nov-26	10-Nov-26	03-Dec-26	80.95%	0%
SDR-2-CON-MV-Z	Backfilling Works	21	20-Oct-26	12-Nov-26	10-Nov-26	03-Dec-26	80.95%	0%
LOOP 6		73	09-Sep-26	21-Nov-26	13-Aug-26	03-Dec-26	86.9%	37.5%
Excavation		21	09-Sep-26	04-Oct-26	13-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Excavation Works	21	09-Sep-26	04-Oct-26	13-Aug-26	09-Nov-26	100%	50%
Pipe laying		20	05-Oct-26	27-Oct-26	13-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Pipe Laying	20	05-Oct-26	27-Oct-26	13-Aug-26	09-Nov-26	100%	50%
Backfilling		21	28-Oct-26	21-Nov-26	10-Nov-26	03-Dec-26	47.62%	0%
SDR-2-CON-MV-Z	Backfilling Works	21	28-Oct-26	21-Nov-26	10-Nov-26	03-Dec-26	47.62%	0%
TELECOMMUNICATIONS Works		94	27-Aug-26	17-Dec-26	09-Jul-26 A	07-Dec-26	59.39%	36.24%
TELECOMMUNICATION IN (PH2-COL-MC10)		21	27-Aug-26	20-Sep-26	13-Sep-26	24-Nov-26	100%	50%
Ducts		21	27-Aug-26	20-Sep-26	13-Sep-26	24-Nov-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	13-Sep-26	24-Nov-26	100%	50%
SDR-2-CON-TI	Excavation for telecom crossing ducts	21	27-Aug-26	20-Sep-26	13-Sep-26	24-Nov-26	100%	50%
TELECOMMUNICATION IN (PH2-COL-MC20)		79	02-Sep-26	07-Dec-26	14-Jul-26 A	03-Dec-26	48.73%	41.66%
Ducts		79	02-Sep-26	07-Dec-26	14-Jul-26 A	03-Dec-26	38%	29%
Excavation		21	02-Sep-26	27-Sep-26	14-Jul-26 A	09-Nov-26	100%	80%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	02-Sep-26	27-Sep-26	14-Jul-26 A	09-Nov-26	100%	80%
Pipe laying		20	28-Sep-26	20-Oct-26	21-Jul-26 A	09-Nov-26	100%	70%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	28-Sep-26	20-Oct-26	21-Jul-26 A	09-Nov-26	100%	70%
Backfilling		20	21-Oct-26	12-Nov-26	01-Aug-26	09-Nov-26	80%	70%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	21-Oct-26	12-Nov-26	01-Aug-26	09-Nov-26	80%	70%
Pulling Cable		21	14-Nov-26	07-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TI	Pulling Cable	21	14-Nov-26	07-Dec-26	10-Nov-26	03-Dec-26	0%	0%
Manholes		56	28-Sep-26	29-Nov-26	03-Sep-26	01-Dec-26	70.77%	67.69%
Bedding Work		20	28-Sep-26	20-Oct-26	05-Sep-26	15-Nov-26	100%	80%

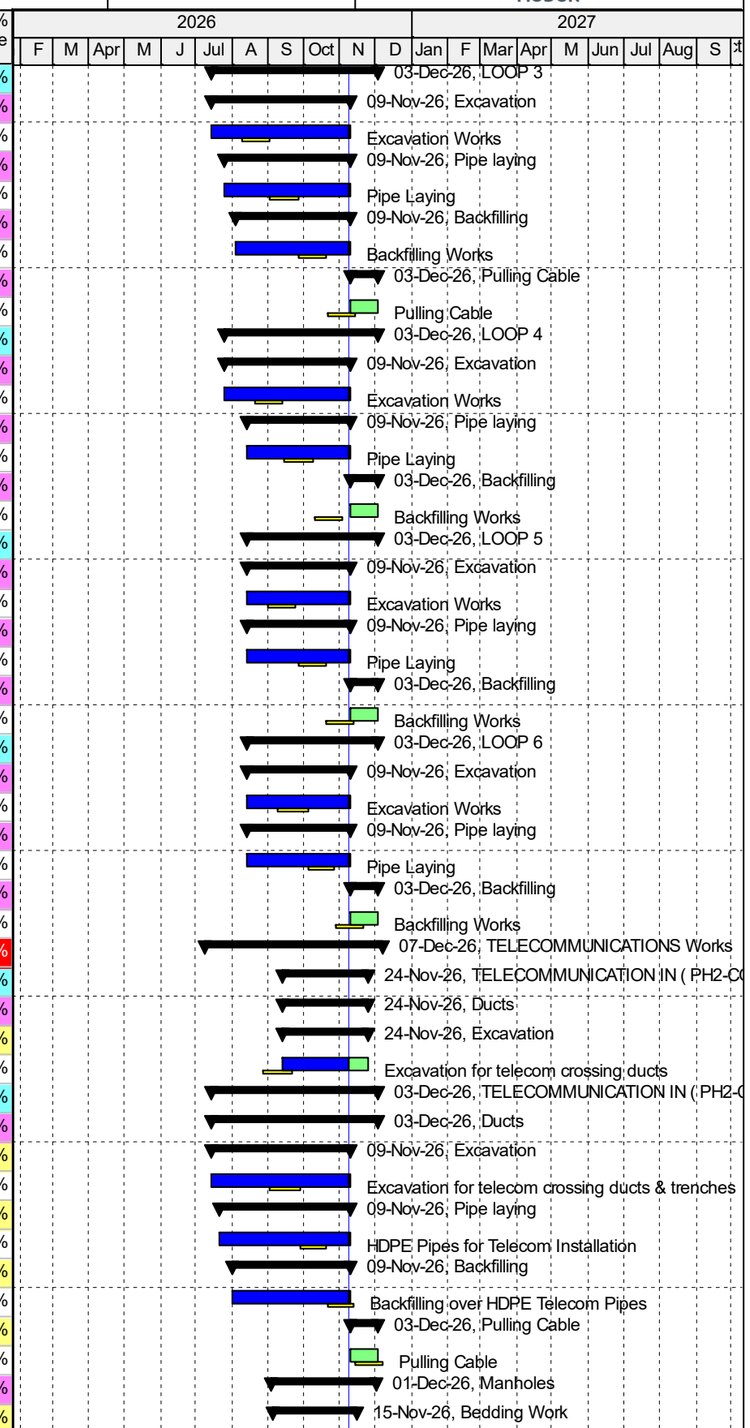

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	28-Sep-26	20-Oct-26	05-Sep-26	15-Nov-26	100%	80%
Install Manholes		20	21-Oct-26	12-Nov-26	03-Sep-26	15-Nov-26	80%	80%
SDR-2-CON-TI	Installation of Telecom Manhole	20	21-Oct-26	12-Nov-26	03-Sep-26	15-Nov-26	80%	80%
Testting		14	14-Nov-26	29-Nov-26	16-Nov-26	01-Dec-26	0%	0%
SDR-2-CON-TI	Telecom Manhole finishing works	14	14-Nov-26	29-Nov-26	16-Nov-26	01-Dec-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCA0)		74	06-Sep-26	24-Oct-26	01-Aug-26	02-Dec-26	100%	25.99%
Ducts		74	06-Sep-26	22-Oct-26	01-Aug-26	01-Dec-26	100%	20%
Excavation		21	06-Sep-26	30-Sep-26	01-Aug-26	09-Nov-26	100%	60%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	06-Sep-26	30-Sep-26	01-Aug-26	09-Nov-26	100%	60%
Pipe laying		19	01-Oct-26	22-Oct-26	10-Nov-26	01-Dec-26	100%	0%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	19	01-Oct-26	22-Oct-26	10-Nov-26	01-Dec-26	100%	0%
Manholes		20	01-Oct-26	24-Oct-26	14-Oct-26 A	02-Dec-26	100%	50%
Bedding Work		20	01-Oct-26	24-Oct-26	14-Oct-26 A	02-Dec-26	100%	50%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	01-Oct-26	24-Oct-26	14-Oct-26 A	02-Dec-26	100%	50%
TELECOMMUNICATION IN (PH2-A-MCB0)		71	12-Sep-26	31-Oct-26	08-Aug-26	03-Dec-26	100%	27.7%
Ducts		71	12-Sep-26	31-Oct-26	08-Aug-26	03-Dec-26	100%	10%
Excavation		21	12-Sep-26	06-Oct-26	08-Aug-26	09-Nov-26	100%	30%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	12-Sep-26	06-Oct-26	08-Aug-26	09-Nov-26	100%	30%
Pipe laying		21	07-Oct-26	31-Oct-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	21	07-Oct-26	31-Oct-26	10-Nov-26	03-Dec-26	100%	0%
Manholes		21	12-Sep-26	06-Oct-26	13-Sep-26	25-Nov-26	100%	75%
Excavation		21	12-Sep-26	06-Oct-26	13-Sep-26	25-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	12-Sep-26	06-Oct-26	13-Sep-26	25-Nov-26	100%	75%
TELECOMMUNICATION IN (PH2-A-MCC0)		69	17-Sep-26	13-Dec-26	20-Jul-26 A	07-Dec-26	66.34%	26.32%
Ducts		69	17-Sep-26	28-Nov-26	20-Jul-26 A	07-Dec-26	78.75%	31.25%
Excavation		21	17-Sep-26	12-Oct-26	20-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	17-Sep-26	12-Oct-26	20-Jul-26 A	09-Nov-26	100%	75%
Pipe laying		20	13-Oct-26	04-Nov-26	03-Sep-26	14-Nov-26	100%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	13-Oct-26	04-Nov-26	03-Sep-26	14-Nov-26	100%	25%
Backfilling		20	05-Nov-26	28-Nov-26	15-Nov-26	07-Dec-26	15%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	05-Nov-26	28-Nov-26	15-Nov-26	07-Dec-26	15%	0%
Manholes		14	28-Nov-26	13-Dec-26	10-Nov-26	25-Nov-26	0%	0%
Testting		14	28-Nov-26	13-Dec-26	10-Nov-26	25-Nov-26	0%	0%
SDR-2-CON-TI	Telecom Manhole finishing works	14	28-Nov-26	13-Dec-26	10-Nov-26	25-Nov-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCD0)		62	24-Sep-26	01-Dec-26	20-Jul-26 A	05-Dec-26	73.15%	39.2%
Ducts		62	24-Sep-26	01-Dec-26	20-Jul-26 A	05-Dec-26	70%	32.5%
Excavation		21	24-Sep-26	18-Oct-26	20-Jul-26 A	09-Nov-26	100%	80%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	24-Sep-26	18-Oct-26	20-Jul-26 A	09-Nov-26	100%	80%
Pipe laying		20	19-Oct-26	10-Nov-26	03-Sep-26	14-Nov-26	90%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	19-Oct-26	10-Nov-26	03-Sep-26	14-Nov-26	90%	25%
Backfilling		18	11-Nov-26	01-Dec-26	15-Nov-26	05-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	18	11-Nov-26	01-Dec-26	15-Nov-26	05-Dec-26	0%	0%
Manholes		20	19-Oct-26	10-Nov-26	15-Sep-26	26-Nov-26	90%	75%
Bedding Work		20	19-Oct-26	10-Nov-26	15-Sep-26	26-Nov-26	90%	75%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	19-Oct-26	10-Nov-26	15-Sep-26	26-Nov-26	90%	75%
TELECOMMUNICATION IN (PH2-A-MCE0)		57	29-Sep-26	06-Dec-26	14-Jul-26 A	03-Dec-26	73.59%	29.88%
Ducts		57	29-Sep-26	06-Dec-26	14-Jul-26 A	03-Dec-26	66.18%	31.25%

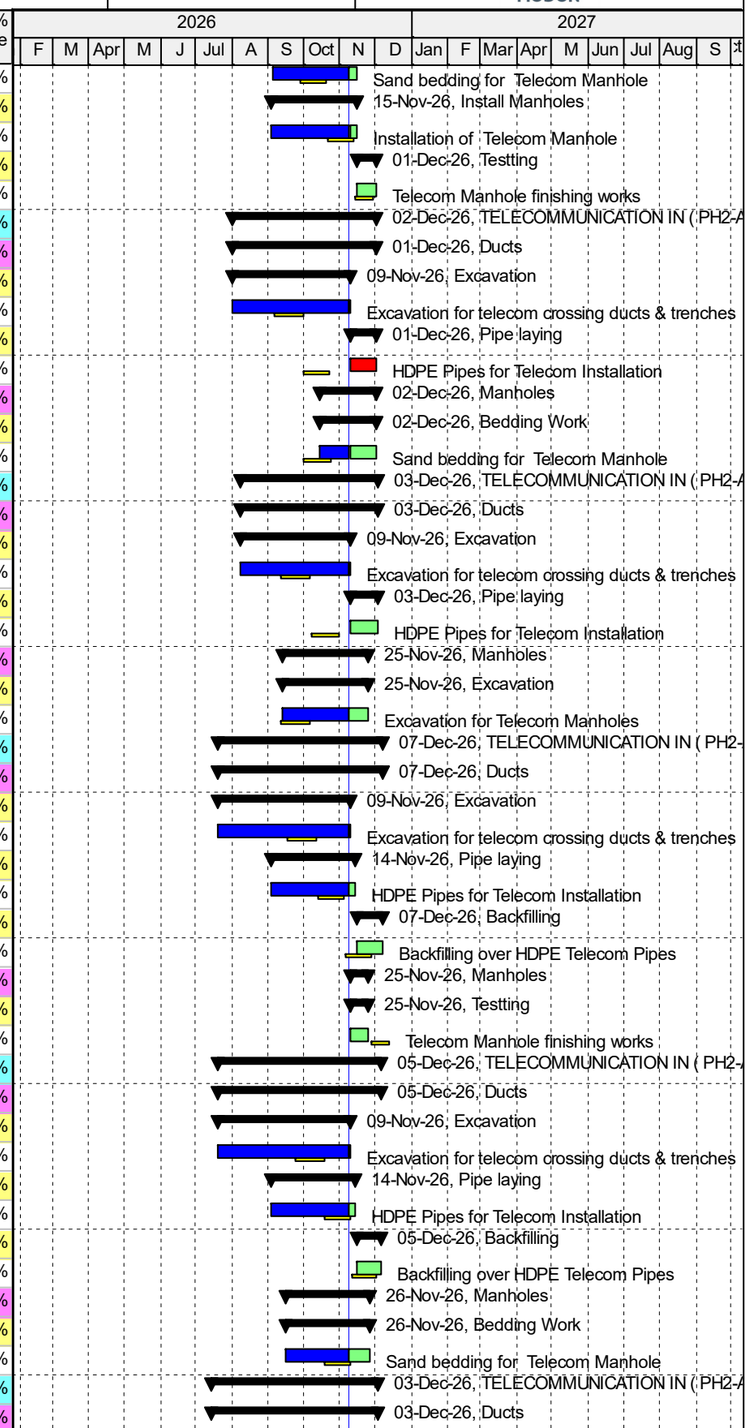

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	29-Sep-26	22-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	29-Sep-26	22-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
Pipe laying		17	24-Oct-26	11-Nov-26	21-Jul-26 A	09-Nov-26	82.35%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	17	24-Oct-26	11-Nov-26	21-Jul-26 A	09-Nov-26	82.35%	25%
Backfilling		21	12-Nov-26	06-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	21	12-Nov-26	06-Dec-26	10-Nov-26	03-Dec-26	0%	0%
Manholes		21	29-Sep-26	22-Oct-26	19-Oct-26 A	02-Dec-26	100%	25%
Excavation		21	29-Sep-26	22-Oct-26	19-Oct-26 A	02-Dec-26	100%	25%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	29-Sep-26	22-Oct-26	19-Oct-26 A	02-Dec-26	100%	25%
TELECOMMUNICATION IN (PH2-A-MCF0)		61	03-Oct-26	13-Dec-26	14-Jul-26 A	03-Dec-26	52.89%	38.15%
Ducts		54	03-Oct-26	13-Dec-26	14-Jul-26 A	03-Dec-26	52.5%	31.25%
Excavation		21	03-Oct-26	26-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	03-Oct-26	26-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
Pipe laying		20	27-Oct-26	18-Nov-26	21-Jul-26 A	09-Nov-26	55%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	27-Oct-26	18-Nov-26	21-Jul-26 A	09-Nov-26	55%	25%
Backfilling		21	19-Nov-26	13-Dec-26	10-Nov-26	03-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	21	19-Nov-26	13-Dec-26	10-Nov-26	03-Dec-26	0%	0%
Manholes		20	27-Oct-26	18-Nov-26	22-Oct-26 A	01-Dec-26	55%	75%
Bedding Work		20	27-Oct-26	18-Nov-26	22-Oct-26 A	01-Dec-26	55%	75%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	27-Oct-26	18-Nov-26	22-Oct-26 A	01-Dec-26	55%	75%
TELECOMMUNICATION IN (PH2-A-MCG0)		50	06-Oct-26	15-Dec-26	14-Jul-26 A	02-Dec-26	57.06%	43.03%
Ducts		50	06-Oct-26	15-Dec-26	14-Jul-26 A	02-Dec-26	45%	31.25%
Excavation		21	06-Oct-26	29-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	06-Oct-26	29-Oct-26	14-Jul-26 A	09-Nov-26	100%	75%
Pipe laying		20	31-Oct-26	22-Nov-26	21-Jul-26 A	09-Nov-26	40%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	31-Oct-26	22-Nov-26	21-Jul-26 A	09-Nov-26	40%	25%
Backfilling		20	23-Nov-26	15-Dec-26	10-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	23-Nov-26	15-Dec-26	10-Nov-26	02-Dec-26	0%	0%
Manholes		21	06-Oct-26	29-Oct-26	20-Oct-26 A	02-Dec-26	100%	85%
Excavation		21	06-Oct-26	29-Oct-26	20-Oct-26 A	02-Dec-26	100%	85%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	06-Oct-26	29-Oct-26	20-Oct-26 A	02-Dec-26	100%	85%
TELECOMMUNICATION IN (PH2-A-MCH0)		48	08-Oct-26	24-Nov-26	30-Jul-26 A	02-Dec-26	66.04%	26.21%
Ducts		48	08-Oct-26	24-Nov-26	30-Jul-26 A	02-Dec-26	53.33%	26.67%
Excavation		21	08-Oct-26	01-Nov-26	30-Jul-26 A	09-Nov-26	100%	80%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	30-Jul-26 A	09-Nov-26	100%	80%
Pipe laying		20	02-Nov-26	24-Nov-26	10-Nov-26	02-Dec-26	30%	0%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	10-Nov-26	02-Dec-26	30%	0%
Manholes		21	08-Oct-26	01-Nov-26	20-Oct-26 A	02-Dec-26	100%	25%
Excavation		21	08-Oct-26	01-Nov-26	20-Oct-26 A	02-Dec-26	100%	25%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	08-Oct-26	01-Nov-26	20-Oct-26 A	02-Dec-26	100%	25%
TELECOMMUNICATION IN (PH2-ART-MC00)		48	08-Oct-26	24-Nov-26	09-Jul-26 A	02-Dec-26	48.67%	28.66%
Ducts		48	08-Oct-26	24-Nov-26	09-Jul-26 A	02-Dec-26	53.33%	23.33%
Excavation		21	08-Oct-26	01-Nov-26	09-Jul-26 A	09-Nov-26	100%	70%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	09-Jul-26 A	09-Nov-26	100%	70%
Pipe laying		20	02-Nov-26	24-Nov-26	10-Nov-26	02-Dec-26	30%	0%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	10-Nov-26	02-Dec-26	30%	0%
Manholes		20	02-Nov-26	24-Nov-26	19-Oct-26 A	01-Dec-26	30%	50%

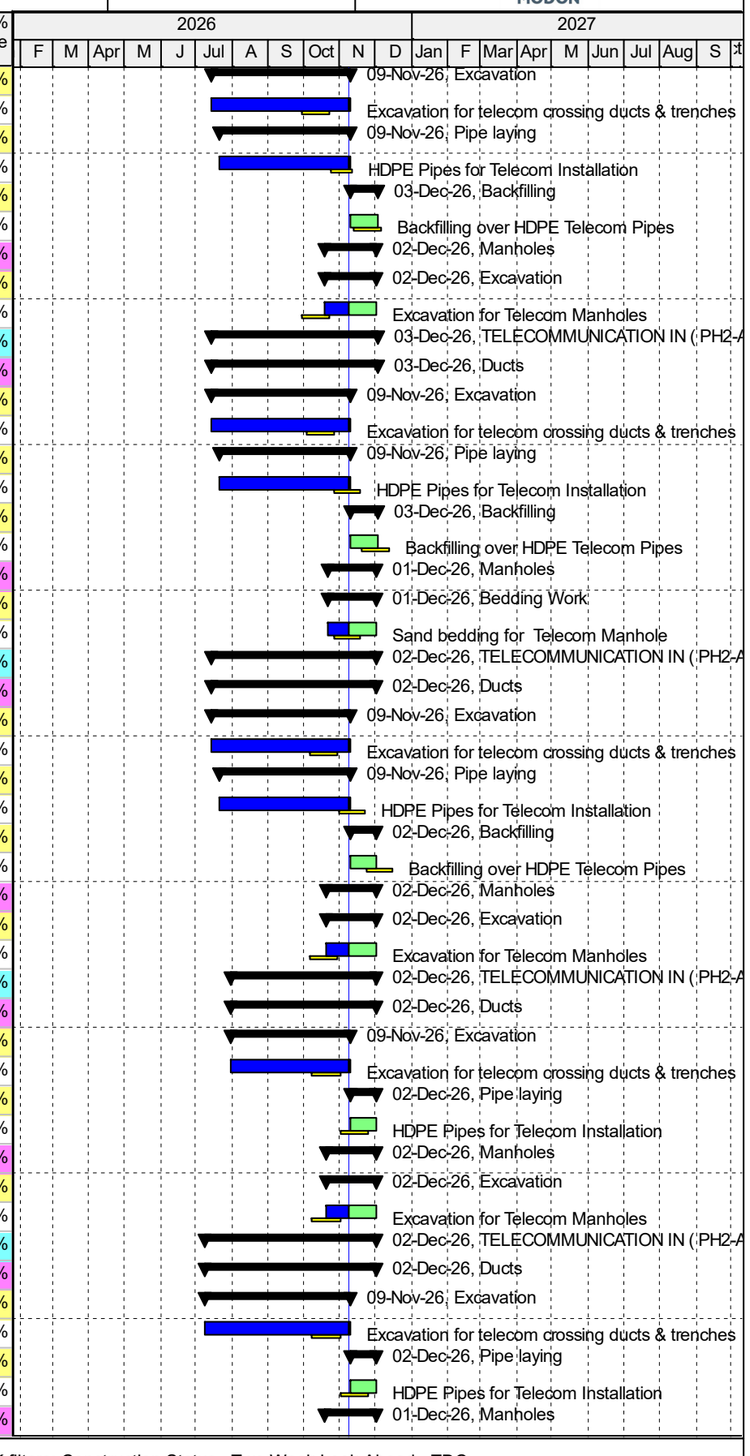

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Bedding Work		20	02-Nov-26	24-Nov-26	19-Oct-26 A	01-Dec-26	30%	50%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	02-Nov-26	24-Nov-26	19-Oct-26 A	01-Dec-26	30%	50%
TELECOMMUNICATION IN (PH2-ART-MC10)		59	08-Oct-26	17-Dec-26	14-Jul-26 A	02-Dec-26	22.79%	45.83%
Ducts		48	08-Oct-26	17-Dec-26	14-Jul-26 A	02-Dec-26	40%	31.25%
Excavation		21	08-Oct-26	01-Nov-26	14-Jul-26 A	09-Nov-26	100%	75%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	14-Jul-26 A	09-Nov-26	100%	75%
Pipe laying		20	02-Nov-26	24-Nov-26	21-Jul-26 A	09-Nov-26	30%	25%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	21-Jul-26 A	09-Nov-26	30%	25%
Backfilling		20	25-Nov-26	17-Dec-26	10-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	25-Nov-26	17-Dec-26	10-Nov-26	02-Dec-26	0%	0%
Manholes		38	02-Nov-26	15-Dec-26	13-Sep-26	25-Nov-26	6.06%	60%
Bedding Work		18	02-Nov-26	22-Nov-26	16-Sep-26	25-Nov-26	33.33%	60%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	18	02-Nov-26	22-Nov-26	16-Sep-26	25-Nov-26	33.33%	60%
Install Manholes		20	23-Nov-26	15-Dec-26	13-Sep-26	25-Nov-26	0%	60%
SDR-2-CON-TI	Installation of Telecom Manhole	20	23-Nov-26	15-Dec-26	13-Sep-26	25-Nov-26	0%	60%
ZONE G		125	27-Aug-26	20-Jan-27	01-Jul-26 A	14-Dec-26	35.07%	23.02%
Street Lighting Network		112	12-Sep-26	20-Jan-27	04-Jul-26 A	13-Dec-26	19.12%	31.31%
Street Lighting IN (PH2-G-MCA0)		55	30-Sep-26	10-Dec-26	13-Aug-26	02-Dec-26	53.97%	55.33%
Excavation		21	30-Sep-26	24-Oct-26	13-Aug-26	09-Nov-26	100%	76%
SDR-2-CON-SL-Z	Excavation for LV Cable drawpits & trenches	21	30-Sep-26	24-Oct-26	13-Aug-26	09-Nov-26	100%	76%
Install Footings		21	25-Oct-26	17-Nov-26	13-Aug-26	09-Nov-26	61.9%	60%
SDR-2-CON-SL-Z	Install Footings	21	25-Oct-26	17-Nov-26	13-Aug-26	09-Nov-26	61.9%	60%
Backfilling		20	18-Nov-26	10-Dec-26	25-Oct-26 A	02-Dec-26	0%	30%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	20	18-Nov-26	10-Dec-26	25-Oct-26 A	02-Dec-26	0%	30%
Street Lighting IN (PH2-G-MCE0)		70	12-Sep-26	23-Nov-26	04-Jul-26 A	02-Dec-26	78.33%	66.67%
Excavation		21	12-Sep-26	06-Oct-26	04-Jul-26 A	09-Nov-26	100%	90%
SDR-2-CON-SL-Z	Excavation for LV Cable drawpits & trenches	21	12-Sep-26	06-Oct-26	04-Jul-26 A	09-Nov-26	100%	90%
Install Footings		21	07-Oct-26	31-Oct-26	13-Aug-26	09-Nov-26	100%	60%
SDR-2-CON-SL-Z	Install Footings	21	07-Oct-26	31-Oct-26	13-Aug-26	09-Nov-26	100%	60%
Backfilling		20	01-Nov-26	23-Nov-26	27-Oct-26 A	02-Dec-26	35%	50%
SDR-2-CON-SL-Z	Backfilling over LV Cables of Street lighting	20	01-Nov-26	23-Nov-26	27-Oct-26 A	02-Dec-26	35%	50%
Street Lighting IN (PH2-G-MCF0)		38	25-Oct-26	14-Jan-27	13-Aug-26	07-Dec-26	8.13%	10%
Install Footings		20	25-Oct-26	16-Nov-26	13-Aug-26	09-Nov-26	65%	80%
SDR-2-CON-SL-Z	Install Footings	20	25-Oct-26	16-Nov-26	13-Aug-26	09-Nov-26	65%	80%
Install pole		21	22-Dec-26	14-Jan-27	14-Nov-26	07-Dec-26	0%	0%
SDR-2-CON-SL-Z	Install Pole	21	22-Dec-26	14-Jan-27	14-Nov-26	07-Dec-26	0%	0%
Street Lighting IN (PH2-G-MCG0)		38	25-Oct-26	14-Jan-27	13-Aug-26	07-Dec-26	8.13%	11.88%
Install Footings		20	25-Oct-26	16-Nov-26	13-Aug-26	09-Nov-26	65%	95%
SDR-2-CON-SL-Z	Install Footings	20	25-Oct-26	16-Nov-26	13-Aug-26	09-Nov-26	65%	95%
Install pole		21	22-Dec-26	14-Jan-27	14-Nov-26	07-Dec-26	0%	0%
SDR-2-CON-SL-Z	Install Pole	21	22-Dec-26	14-Jan-27	14-Nov-26	07-Dec-26	0%	0%
Street Lighting IN (PH2-G-MCZ0)		73	28-Oct-26	20-Jan-27	30-Jul-26 A	09-Nov-26	5.95%	51.25%
Install Footings		21	28-Oct-26	21-Nov-26	13-Aug-26	09-Nov-26	47.62%	60%
SDR-2-CON-SL-Z	Install Footings	21	28-Oct-26	21-Nov-26	13-Aug-26	09-Nov-26	47.62%	60%
Install pole		21	28-Dec-26	20-Jan-27	30-Jul-26 A	09-Nov-26	0%	50%
SDR-2-CON-SL-Z	Install Pole	21	28-Dec-26	20-Jan-27	30-Jul-26 A	09-Nov-26	0%	50%
Lighting Pole Panels		21	10-Oct-26	02-Nov-26	10-Nov-26	03-Dec-26	100%	0%

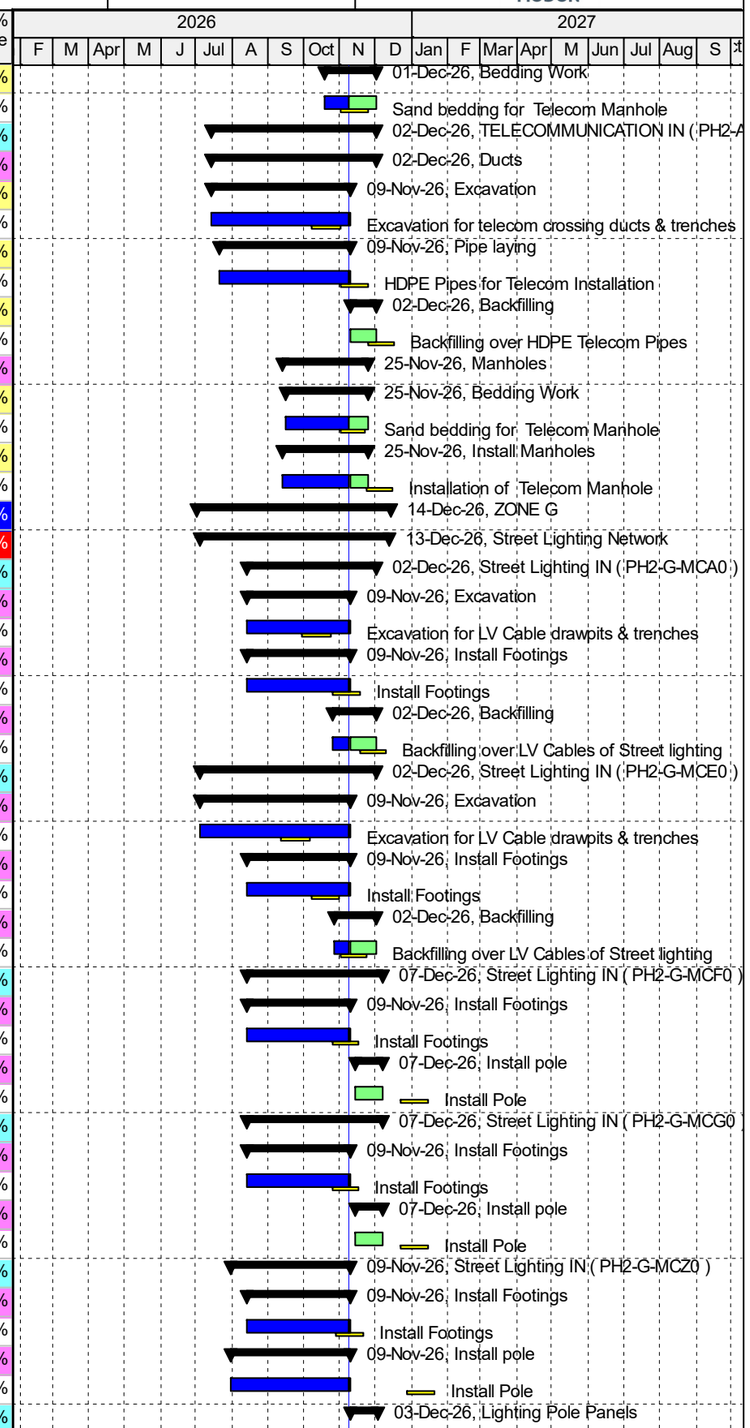

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	10-Oct-26	02-Nov-26	10-Nov-26	03-Dec-26	100%	0%
SDR-2-CON-SL-Z	Street Lighting Panels Excavation	21	10-Oct-26	02-Nov-26	10-Nov-26	03-Dec-26	100%	0%
Feeder Pillars		20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
Leveling		20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
SDR-2-CON-SL-Z	Feeder Pillars Leveling	20	12-Sep-26	05-Oct-26	21-Nov-26	13-Dec-26	100%	0%
MV Network		93	27-Aug-26	12-Dec-26	19-Jul-26 A	14-Dec-26	40%	17.5%
LOOP 1		93	27-Aug-26	03-Dec-26	19-Jul-26 A	14-Dec-26	40%	17.5%
Excavation		21	27-Aug-26	20-Sep-26	19-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Excavation Works	21	27-Aug-26	20-Sep-26	19-Jul-26 A	09-Nov-26	100%	50%
Pipe laying		21	21-Sep-26	15-Oct-26	04-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Pipe Laying	21	21-Sep-26	15-Oct-26	04-Aug-26	09-Nov-26	100%	50%
Backfilling		12	17-Oct-26	29-Oct-26	08-Aug-26	09-Nov-26	100%	25%
SDR-2-CON-MV-Z	Backfilling Works	12	17-Oct-26	29-Oct-26	08-Aug-26	09-Nov-26	100%	25%
Pulling Cable		20	11-Nov-26	03-Dec-26	22-Nov-26	14-Dec-26	0%	0%
SDR-2-CON-MV-Z	Pulling Cable	20	11-Nov-26	03-Dec-26	22-Nov-26	14-Dec-26	0%	0%
LOOP 2		93	27-Aug-26	12-Dec-26	01-Aug-26	14-Dec-26	40%	17.5%
Excavation		21	27-Aug-26	20-Sep-26	01-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Excavation Works	21	27-Aug-26	20-Sep-26	01-Aug-26	09-Nov-26	100%	50%
Pipe laying		20	21-Sep-26	14-Oct-26	04-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-MV-Z	Pipe Laying	20	21-Sep-26	14-Oct-26	04-Aug-26	09-Nov-26	100%	50%
Backfilling		20	15-Oct-26	07-Nov-26	08-Aug-26	09-Nov-26	100%	25%
SDR-2-CON-MV-Z	Backfilling Works	20	15-Oct-26	07-Nov-26	08-Aug-26	09-Nov-26	100%	25%
Pulling Cable		20	19-Nov-26	12-Dec-26	22-Nov-26	14-Dec-26	0%	0%
SDR-2-CON-MV-Z	Pulling Cable	20	19-Nov-26	12-Dec-26	22-Nov-26	14-Dec-26	0%	0%
TELECOMMUNICATIONS Works		102	14-Sep-26	18-Jan-27	01-Jul-26 A	12-Dec-26	37.35%	46.48%
TELECOMMUNICATION IN (PH2-G-MCA0)		68	14-Sep-26	21-Dec-26	01-Jul-26 A	02-Dec-26	59.79%	37.46%
Ducts		68	14-Sep-26	22-Nov-26	01-Jul-26 A	02-Dec-26	85%	39.25%
Excavation		21	14-Sep-26	08-Oct-26	01-Jul-26 A	09-Nov-26	100%	53%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	14-Sep-26	08-Oct-26	01-Jul-26 A	09-Nov-26	100%	53%
Pipe laying		18	10-Oct-26	29-Oct-26	13-Aug-26	09-Nov-26	100%	52%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	18	10-Oct-26	29-Oct-26	13-Aug-26	09-Nov-26	100%	52%
Backfilling		20	31-Oct-26	22-Nov-26	10-Nov-26	02-Dec-26	40%	0%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	31-Oct-26	22-Nov-26	10-Nov-26	02-Dec-26	40%	0%
Manholes		68	14-Sep-26	21-Dec-26	15-Aug-26	02-Dec-26	46.32%	36.5%
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	60%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	60%
Bedding Work		17	10-Oct-26	28-Oct-26	24-Aug-26	09-Nov-26	100%	25%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	17	10-Oct-26	28-Oct-26	24-Aug-26	09-Nov-26	100%	25%
Install Manholes		19	29-Oct-26	19-Nov-26	15-Aug-26	09-Nov-26	47.37%	50%
SDR-2-CON-TI	Installation of Telecom Manhole	19	29-Oct-26	19-Nov-26	15-Aug-26	09-Nov-26	47.37%	50%
Testting		7	21-Nov-26	28-Nov-26	02-Sep-26	09-Nov-26	0%	25%
SDR-2-CON-TI	Telecom Manhole finishing works	7	21-Nov-26	28-Nov-26	02-Sep-26	09-Nov-26	0%	25%
Backfilling		20	29-Nov-26	21-Dec-26	10-Nov-26	02-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over Telecom Manhole	20	29-Nov-26	21-Dec-26	10-Nov-26	02-Dec-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCE0)		81	14-Sep-26	20-Dec-26	16-Jul-26 A	12-Dec-26	37.13%	43.53%
Ducts		60	10-Oct-26	17-Dec-26	16-Jul-26 A	09-Nov-26	25.56%	50%
Pipe laying		20	10-Oct-26	01-Nov-26	16-Jul-26 A	09-Nov-26	100%	50%

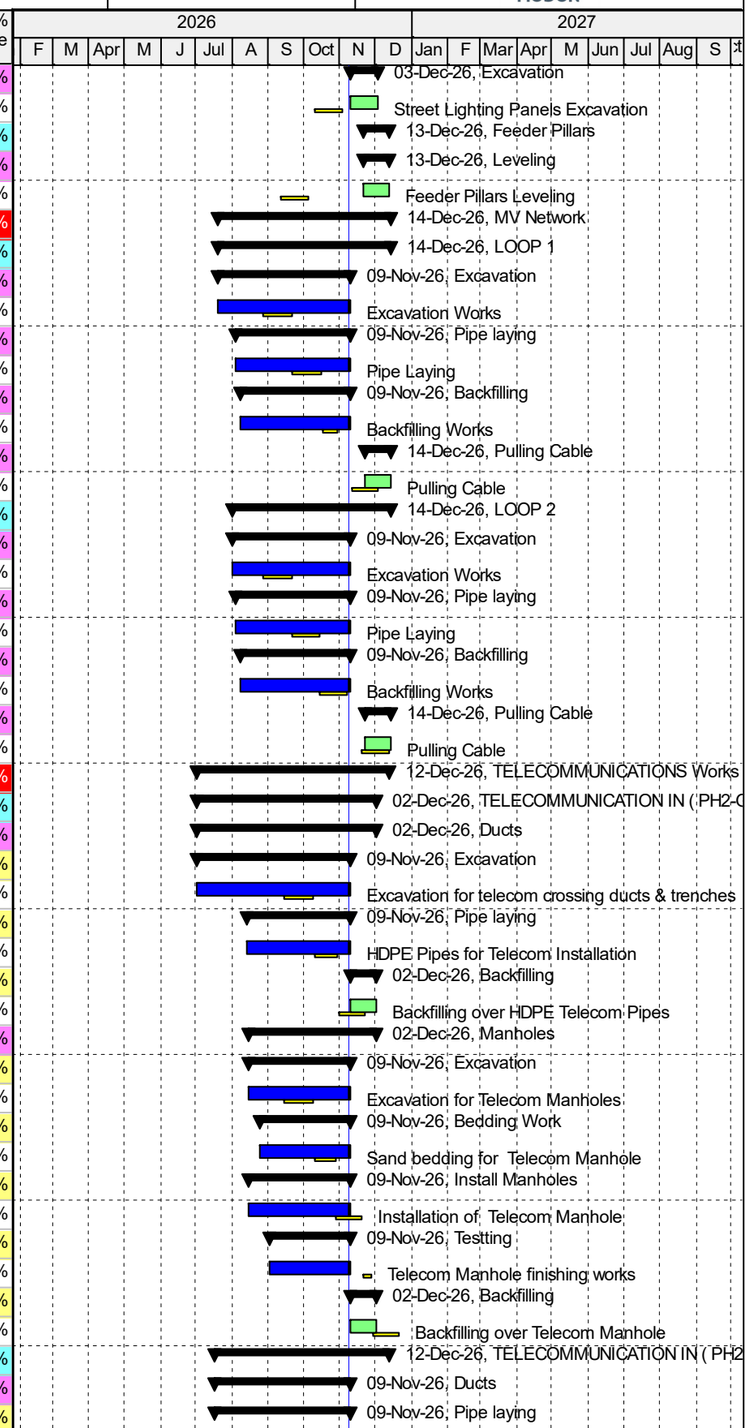

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	20	10-Oct-26	01-Nov-26	16-Jul-26 A	09-Nov-26	100%	50%
Backfilling		20	02-Nov-26	24-Nov-26	20-Jul-26 A	09-Nov-26	30%	50%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	02-Nov-26	24-Nov-26	20-Jul-26 A	09-Nov-26	30%	50%
Pulling Cable		20	25-Nov-26	17-Dec-26	16-Jul-26 A	09-Nov-26	0%	50%
SDR-2-CON-TI	Pulling Cable	20	25-Nov-26	17-Dec-26	16-Jul-26 A	09-Nov-26	0%	50%
Manholes		76	14-Sep-26	20-Dec-26	15-Aug-26	12-Dec-26	51.05%	35.75%
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	55%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	55%
Bedding Work		15	10-Oct-26	26-Oct-26	17-Aug-26	09-Nov-26	100%	50%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	15	10-Oct-26	26-Oct-26	17-Aug-26	09-Nov-26	100%	50%
Install Manholes		19	27-Oct-26	17-Nov-26	19-Aug-26	09-Nov-26	57.89%	50%
SDR-2-CON-TI	Installation of Telecom Manhole	19	27-Oct-26	17-Nov-26	19-Aug-26	09-Nov-26	57.89%	50%
Testting		7	18-Nov-26	25-Nov-26	10-Nov-26	17-Nov-26	0%	0%
SDR-2-CON-TI	Telecom Manhole finishing works	7	18-Nov-26	25-Nov-26	10-Nov-26	17-Nov-26	0%	0%
Backfilling		21	26-Nov-26	20-Dec-26	18-Nov-26	12-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over Telecom Manhole	21	26-Nov-26	20-Dec-26	18-Nov-26	12-Dec-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCF0)		81	10-Oct-26	18-Jan-27	06-Jul-26 A	10-Dec-26	16.22%	43.96%
Ducts		81	10-Oct-26	11-Jan-27	06-Jul-26 A	09-Nov-26	15.26%	50%
Excavation		21	10-Oct-26	02-Nov-26	06-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	10-Oct-26	02-Nov-26	06-Jul-26 A	09-Nov-26	100%	50%
Pipe laying		19	03-Nov-26	24-Nov-26	16-Jul-26 A	09-Nov-26	26.32%	50%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	19	03-Nov-26	24-Nov-26	16-Jul-26 A	09-Nov-26	26.32%	50%
Backfilling		20	25-Nov-26	17-Dec-26	16-Aug-26	09-Nov-26	0%	50%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	25-Nov-26	17-Dec-26	16-Aug-26	09-Nov-26	0%	50%
Pulling Cable		21	19-Dec-26	11-Jan-27	16-Jul-26 A	09-Nov-26	0%	50%
SDR-2-CON-TI	Pulling Cable	21	19-Dec-26	11-Jan-27	16-Jul-26 A	09-Nov-26	0%	50%
Manholes		60	10-Oct-26	18-Jan-27	15-Aug-26	10-Dec-26	17.5%	35.9%
Excavation		21	10-Oct-26	02-Nov-26	15-Aug-26	09-Nov-26	100%	56%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	10-Oct-26	02-Nov-26	15-Aug-26	09-Nov-26	100%	56%
Bedding Work		20	03-Nov-26	25-Nov-26	17-Aug-26	09-Nov-26	25%	50%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	20	03-Nov-26	25-Nov-26	17-Aug-26	09-Nov-26	25%	50%
Install Manholes		19	26-Nov-26	17-Dec-26	19-Aug-26	09-Nov-26	0%	50%
SDR-2-CON-TI	Installation of Telecom Manhole	19	26-Nov-26	17-Dec-26	19-Aug-26	09-Nov-26	0%	50%
Testting		7	19-Dec-26	26-Dec-26	10-Nov-26	17-Nov-26	0%	0%
SDR-2-CON-TI	Telecom Manhole finishing works	7	19-Dec-26	26-Dec-26	10-Nov-26	17-Nov-26	0%	0%
Backfilling		20	27-Dec-26	18-Jan-27	18-Nov-26	10-Dec-26	0%	0%
SDR-2-CON-TI	Backfilling over Telecom Manhole	20	27-Dec-26	18-Jan-27	18-Nov-26	10-Dec-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCG0)		79	14-Sep-26	15-Dec-26	06-Jul-26 A	17-Nov-26	44.56%	58.74%
Ducts		79	14-Sep-26	15-Dec-26	06-Jul-26 A	09-Nov-26	34%	54.5%
Excavation		21	14-Sep-26	08-Oct-26	06-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-TI	Excavation for telecom crossing ducts & trenches	21	14-Sep-26	08-Oct-26	06-Jul-26 A	09-Nov-26	100%	50%
Pipe laying		18	10-Oct-26	29-Oct-26	15-Jul-26 A	09-Nov-26	100%	55%
SDR-2-CON-TI	HDPE Pipes for Telecom Installation	18	10-Oct-26	29-Oct-26	15-Jul-26 A	09-Nov-26	100%	55%
Backfilling		20	31-Oct-26	22-Nov-26	16-Aug-26	09-Nov-26	40%	55%
SDR-2-CON-TI	Backfilling over HDPE Telecom Pipes	20	31-Oct-26	22-Nov-26	16-Aug-26	09-Nov-26	40%	55%
Pulling Cable		20	23-Nov-26	15-Dec-26	14-Jul-26 A	09-Nov-26	0%	55%
SDR-2-CON-TI	Pulling Cable	20	23-Nov-26	15-Dec-26	14-Jul-26 A	09-Nov-26	0%	55%

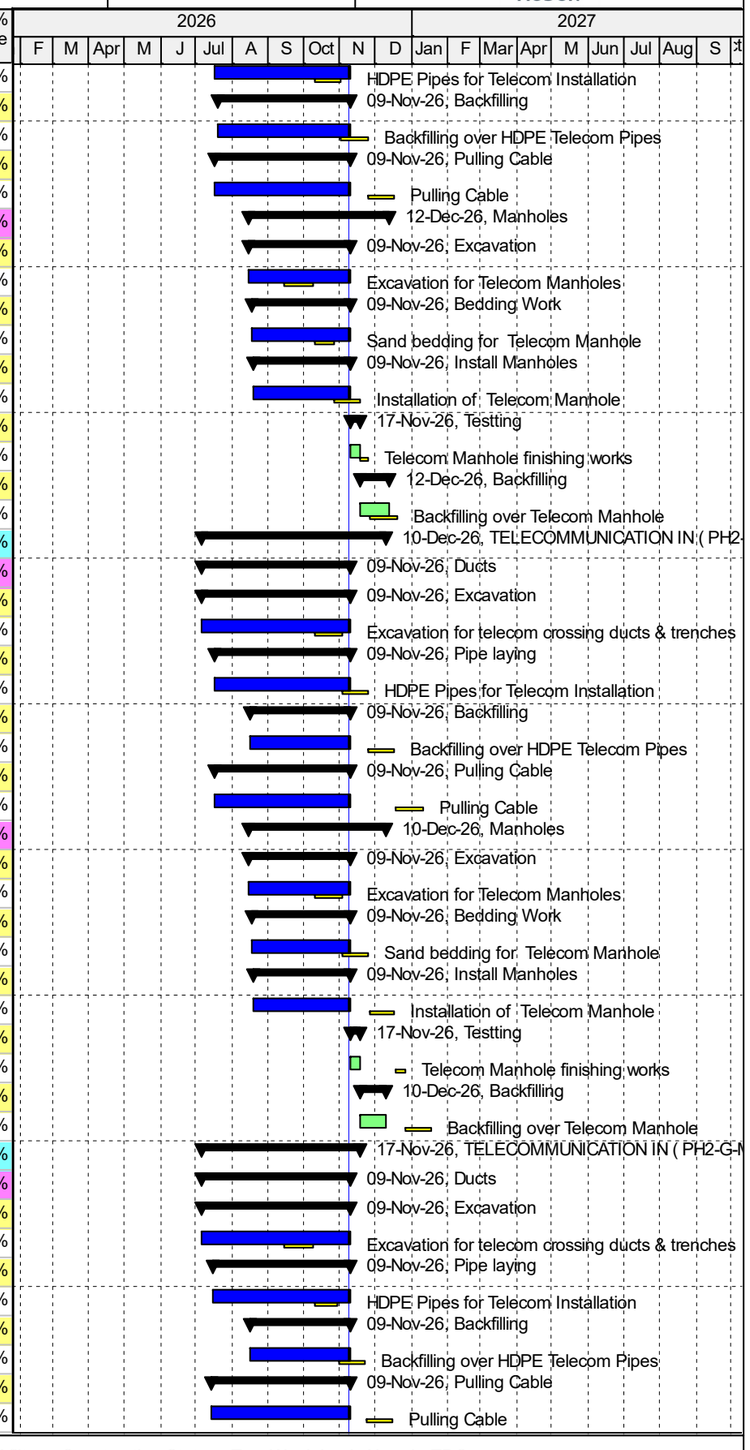

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Manholes		56	14-Sep-26	26-Nov-26	15-Aug-26	17-Nov-26	62.19%	65.81%
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	76%
SDR-2-CON-TI	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	09-Nov-26	100%	76%
Bedding Work		15	10-Oct-26	26-Oct-26	17-Aug-26	09-Nov-26	100%	75%
SDR-2-CON-TI	Sand bedding for Telecom Manhole	15	10-Oct-26	26-Oct-26	17-Aug-26	09-Nov-26	100%	75%
Install Manholes		20	27-Oct-26	18-Nov-26	19-Aug-26	09-Nov-26	55%	75%
SDR-2-CON-TI	Installation of Telecom Manhole	20	27-Oct-26	18-Nov-26	19-Aug-26	09-Nov-26	55%	75%
Testting		7	19-Nov-26	26-Nov-26	10-Nov-26	17-Nov-26	0%	0%
SDR-2-CON-TI	Telecom Manhole finishing works	7	19-Nov-26	26-Nov-26	10-Nov-26	17-Nov-26	0%	0%
CCTV Works		73	02-Sep-26	23-Nov-26	30-Jul-26 A	26-Nov-26	95.95%	30.18%
ZONE G		73	02-Sep-26	23-Nov-26	30-Jul-26 A	26-Nov-26	95.95%	30.18%
Poles 1st and 2nd Fix Works		73	02-Sep-26	06-Oct-26	30-Jul-26 A	26-Nov-26	100%	8%
Excavation		7	02-Sep-26	09-Sep-26	30-Jul-26 A	09-Nov-26	100%	50%
SDR-2-CON-CC-ZA-1	Excavation 1Sst & 2nd Fix Works	7	02-Sep-26	09-Sep-26	30-Jul-26 A	09-Nov-26	100%	50%
Install Footings		7	10-Sep-26	17-Sep-26	03-Sep-26	09-Nov-26	100%	30%
SDR-2-CON-CC-ZA-1	Install Footings	7	10-Sep-26	17-Sep-26	03-Sep-26	09-Nov-26	100%	30%
Backfilling		7	19-Sep-26	27-Sep-26	10-Nov-26	17-Nov-26	100%	0%
SDR-2-CON-CC-ZA-1	Backfilling 1Sst & 2nd Fix Works	7	19-Sep-26	27-Sep-26	10-Nov-26	17-Nov-26	100%	0%
Install pole		8	28-Sep-26	06-Oct-26	18-Nov-26	26-Nov-26	100%	0%
SDR-2-CON-CC-ZA-1	Install Pole	8	28-Sep-26	06-Oct-26	18-Nov-26	26-Nov-26	100%	0%
25m Pole Package		20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
Excavation		20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
SDR-2-CON-CC-ZA-1	25 Meters Pole Excavation	20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
7m Pole Package		20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
Excavation		20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
SDR-2-CON-CC-ZA-1	7m Meters Pole Excavation	20	07-Oct-26	29-Oct-26	03-Sep-26	26-Nov-26	100%	50%
35m Pole Package		21	31-Oct-26	23-Nov-26	03-Sep-26	26-Nov-26	38.1%	50%
Excavation		21	31-Oct-26	23-Nov-26	03-Sep-26	26-Nov-26	38.1%	50%
SDR-2-CON-CC-ZA-1	35m Meters Pole Excavation	21	31-Oct-26	23-Nov-26	03-Sep-26	26-Nov-26	38.1%	50%

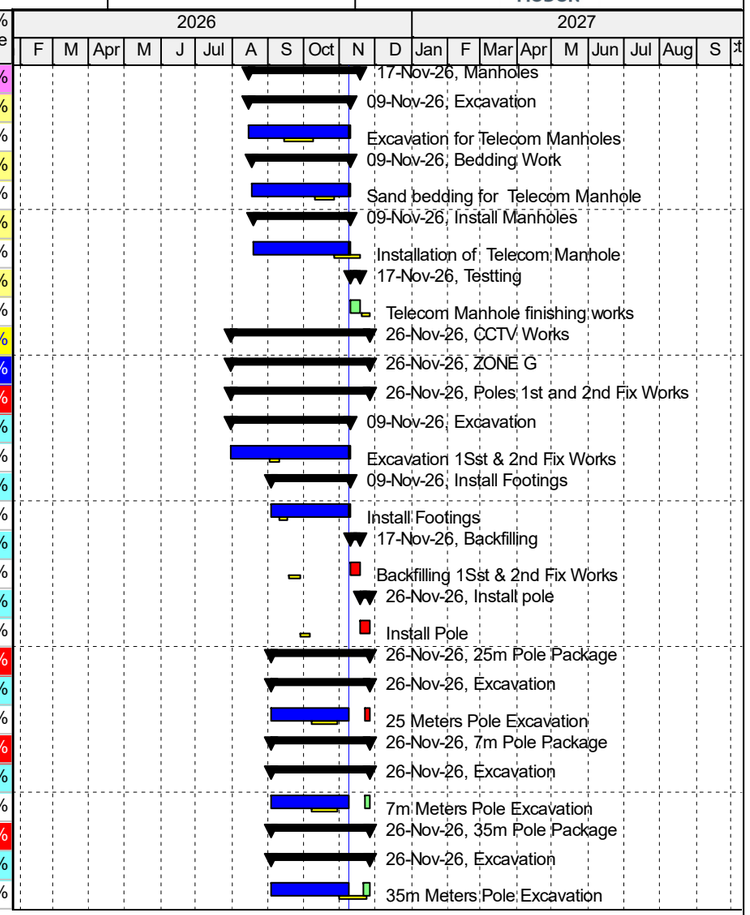

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone

TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation
