
ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Certificate # 02

Activity ID	Activity Name	Budget At Completion	Original Duration	BL Project Start	BL Project Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
3066	ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY	$140,467,862.00	654	04-Sep-25	03-Sep-27	38.96%	50.12%	$54,726,862.18	$70,404,065.68
3066.GENERAL	MILESTONS	$0.00	654	04-Sep-25	03-Sep-27	0%	0%	$0.00	$0.00
3066.5	MOBILIZATION	$0.00	632	04-Sep-25	23-Aug-27	0%	0%	$0.00	$0.00
3066.6	ENGINEERING	$4,214,035.86	208	04-Oct-25	02-Jun-26	100%	100%	$4,214,035.86	$4,214,035.86
3066.17	PROCUREMENT	$28,093,572.39	604	27-Oct-25	02-Sep-27	56.21%	64.32%	$15,790,681.52	$18,068,599.86
3066.1	CONSTRUCTION WORKS	$94,113,467.75	652	04-Sep-25	03-Sep-27	36.89%	51.13%	$34,722,144.80	$48,121,429.95
3066.22	CLOSE OUT	$14,046,786.00	221	17-Apr-27	03-Sep-27	0%	0%	$0.00	$0.00

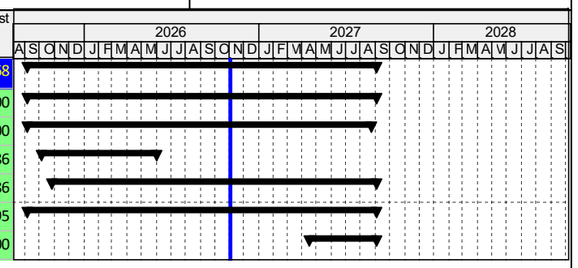

© Oracle Corporation
