
ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY		654	$140,467,862.00	04-Sep-25	03-Sep-27	04-Sep-25		$54,726,862.18	$70,404,065.68	1.29
MILESTONS		654	$0.00	04-Sep-25	03-Sep-27	04-Sep-25		$0.00	$0.00	0.00
CONTRACTUAL MILESTONES		654	$0.00	04-Sep-25	03-Sep-27	04-Sep-25		$0.00	$0.00	0.00
TAGNCM0001	Project Start	0	$0.00	04-Sep-25		04-Sep-25		$0.00	$0.00	0.00
TAGNCM0002	Site Hand Over	0	$0.00	04-Sep-25		04-Sep-25		$0.00	$0.00	0.00
TAGNCM0003	Project finish	0	$0.00		03-Sep-27			$0.00	$0.00	0.00
NET WORK MILESTONES		621	$0.00	11-Oct-25	03-Sep-27	11-Oct-25		$0.00	$0.00	0.00
TAGNML0004	Start Road Works	0	$0.00	11-Oct-25		11-Oct-25		$0.00	$0.00	0.00
TAGNML0011	Start Sewerage Networks	0	$0.00	22-Nov-25		22-Nov-25		$0.00	$0.00	0.00
TAGNML0012	Start Storm Water Drainage Networks	0	$0.00	31-Dec-25		31-Dec-25		$0.00	$0.00	0.00
TAGNML0022	Start works for Amana Road	0	$0.00	15-Mar-26		15-Mar-26		$0.00	$0.00	0.00
TAGNML0009	Start Potable Water Networks	0	$0.00	01-Apr-26		01-Apr-26		$0.00	$0.00	0.00
TAGNML0010	Start TSE Networks	0	$0.00	01-Apr-26		01-Apr-26		$0.00	$0.00	0.00
TAGNML0005	Start Electrical Works	0	$0.00	12-May-26		12-May-26		$0.00	$0.00	0.00
TAGNML0006	Start Teleommunications Works	0	$0.00	03-Jun-26		18-Jun-26		$0.00	$0.00	0.00
TAGNML0008	Start CCTV Works	0	$0.00	03-Jun-26				$0.00	$0.00	0.00
TAGNML0018	Finish TSE Networks	0	$0.00		21-Jul-27			$0.00	$0.00	0.00
TAGNML0019	Finish Sewerage Networks	0	$0.00		14-Aug-27			$0.00	$0.00	0.00
TAGNML0020	Finish Storm Water Drainage Networks	0	$0.00		14-Aug-27			$0.00	$0.00	0.00
TAGNML0015	Finish Teleommunications Works	0	$0.00		16-Aug-27			$0.00	$0.00	0.00
TAGNML0017	Finish Potable Water Networks	0	$0.00		21-Aug-27			$0.00	$0.00	0.00
TAGNML0032	Finish works for Amana Road	0	$0.00		23-Aug-27			$0.00	$0.00	0.00
TAGNML0013	Finish Road Works	0	$0.00		02-Sep-27			$0.00	$0.00	0.00
TAGNML0014	Finish Electrical Works	0	$0.00		03-Sep-27			$0.00	$0.00	0.00
TAGNML0016	Finish CCTV Works	0	$0.00		03-Sep-27			$0.00	$0.00	0.00
ZONES MILESTONES		563	$0.00	04-Sep-25	15-Aug-27	04-Sep-25		$0.00	$0.00	0.00
TAGNZM0003	Start Zone 3	0	$0.00	04-Sep-25		04-Sep-25		$0.00	$0.00	0.00
TAGNZM0002	Start Zone 2	0	$0.00	11-Oct-25		11-Oct-25		$0.00	$0.00	0.00
TAGNZM0001	Start Zone 1	0	$0.00	14-Oct-25		14-Oct-25		$0.00	$0.00	0.00
TAGNZM0004	Finish Zone 1	0	$0.00		05-Jun-27			$0.00	$0.00	0.00
TAGNZM0005	Finish Zone 2	0	$0.00		25-Jul-27			$0.00	$0.00	0.00
TAGNZM0006	Finish Zone 3	0	$0.00		15-Aug-27			$0.00	$0.00	0.00
PRELIMINARY SUBMITTALS		229	$0.00	09-Sep-25	02-Jun-26	09-Sep-25		$0.00	$0.00	0.00
TAGNPS0001	Initial survying Review and approval	28	$0.00	09-Sep-25	11-Oct-25	09-Sep-25	11-Oct-25	$0.00	$0.00	0.00
TAGNPS0005	HSE & Qui;ity Plan	44	$0.00	01-Oct-25	20-Nov-25	01-Oct-25	20-Nov-25	$0.00	$0.00	0.00
TAGNPS0003	Base line Schedule Review and approval	21	$0.00	09-Oct-25	02-Nov-25	09-Oct-25	02-Nov-25	$0.00	$0.00	0.00
TAGNPS0002	Shop drawing complete	167	$0.00	20-Nov-25	02-Jun-26	20-Nov-25		$0.00	$0.00	0.00
MOBILIZATION		632	$0.00	04-Sep-25	23-Aug-27	04-Sep-25		$0.00	$0.00	0.00
Site Facilites and Offices		632	$0.00	04-Sep-25	23-Aug-27	04-Sep-25		$0.00	$0.00	0.00
TAGNMZ0001	Mobilization works for Manpower and Equipment	112	$0.00	04-Sep-25	12-Jan-26	04-Sep-25	12-Jan-26	$0.00	$0.00	0.00
TAGNMZ0002	Office Ready	82	$0.00	07-Sep-25	10-Dec-25	07-Sep-25	10-Dec-25	$0.00	$0.00	0.00
TAGNMZ0007	Office Operation	231	$0.00	07-Sep-25	02-Jun-26	07-Sep-25	02-Jun-26	$0.00	$0.00	0.00
TAGNMZ0003	Housing portable cabins assembling	42	$0.00	10-Sep-25	28-Oct-25	10-Sep-25	28-Oct-25	$0.00	$0.00	0.00
TAGNMZ0004	laboratory and storage facilities	58	$0.00	08-Oct-25	14-Dec-25	08-Oct-25	14-Dec-25	$0.00	$0.00	0.00
TAGNMZ0006	Material Store with Fence	23	$0.00	12-Oct-25	06-Nov-25	12-Oct-25	07-Nov-25	$0.00	$0.00	0.00
TAGNMZ0005	Project Sign manufacturing and installation	35	$0.00	01-Nov-25	10-Dec-25	01-Nov-25	10-Dec-25	$0.00	$0.00	0.00
TAGNMZ9	Office Operation part 01	383	$0.00	03-Jun-26	23-Aug-27	21-Jun-26		$0.00	$0.00	0.00
Preliminaries		36	$0.00	25-Nov-25	05-Jan-26	25-Nov-25	05-Jan-26	$0.00	$0.00	0.00
TAGNMZ0008	Prepare & Submit Soil Investigation	34	$0.00	25-Nov-25	03-Jan-26	25-Nov-25	03-Jan-26	$0.00	$0.00	0.00
TAGNMZ0009	Review and Approval soil Investigation	33	$0.00	29-Nov-25	05-Jan-26	29-Nov-25	05-Jan-26	$0.00	$0.00	0.00
ENGINEERING		208	$4,214,035.86	04-Oct-25	02-Jun-26	04-Oct-25	02-Jun-26	$4,214,035.86	$4,214,035.86	1.00
Shop Drawings Submittls		193	$4,214,035.86	21-Oct-25	02-Jun-26	21-Oct-25	02-Jun-26	$4,214,035.86	$4,214,035.86	1.00
Shop Drawing for Roads		187	$737,443.24	28-Oct-25	02-Jun-26	28-Oct-25	02-Jun-26	$737,443.24	$737,443.24	1.00

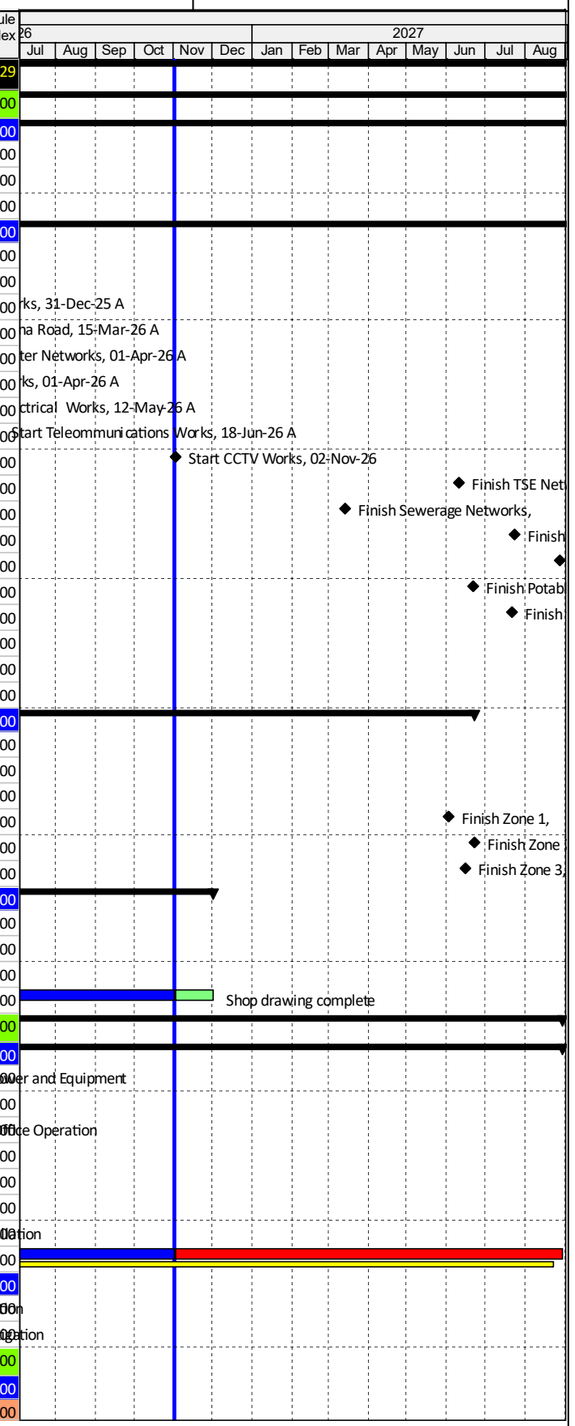


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAENSDRD0001	Roads Shop dwg. Prepare & Submit	187	$737,443.24	28-Oct-25	02-Jun-26	28-Oct-25	02-Jun-26	$737,443.24	$737,443.24	1.00
TAENSDRD0002	Roads Shop dwg. Review & Approval	132	$0.00	30-Dec-25	02-Jun-26	30-Dec-25	02-Jun-26	$0.00	$0.00	0.00
Shop Drawing for Electrical Works		19	$420,000.00	31-Dec-25	21-Jan-26	31-Dec-25	21-Jan-26	$420,000.00	$420,000.00	1.00
TAENSDEL0001	Shop dwg. Prepare ,submitt	19	$0.00	31-Dec-25	21-Jan-26	31-Dec-25	21-Jan-26	$0.00	$0.00	0.00
TAENSDEL0002	Shop dwg. Review and Approval	14	$420,000.00	06-Jan-26	21-Jan-26	06-Jan-26	21-Jan-26	$420,000.00	$420,000.00	1.00
Shop Drawing for Telecommunications		114	$120,000.00	21-Jan-26	02-Jun-26	21-Jan-26	02-Jun-26	$120,000.00	$120,000.00	1.00
TAENSDTL0001	Shop dwg. Prepare and submitt	113	$0.00	21-Jan-26	01-Jun-26	21-Jan-26	02-Jun-26	$0.00	$0.00	0.00
TAENSDTL0002	Shop dwg. Review and Approval	105	$120,000.00	01-Feb-26	02-Jun-26	01-Feb-26	02-Jun-26	$120,000.00	$120,000.00	1.00
Shop Drawing for CCTV Networks		5	$129,077.91	10-Jan-26	14-Jan-26	10-Jan-26	14-Jan-26	$129,077.91	$129,077.91	1.00
TAENSDCC0001	Shop Dwg Prepare and Submit	5	$0.00	10-Jan-26	14-Jan-26	10-Jan-26	14-Jan-26	$0.00	$0.00	0.00
TAENSDCC0002	Shop Dwg. Review and approval	2	$129,077.91	13-Jan-26	14-Jan-26	13-Jan-26	14-Jan-26	$129,077.91	$129,077.91	1.00
Shop Drawing for Potable Water		63	$222,841.39	02-Nov-25	13-Jan-26	02-Nov-25	13-Jan-26	$222,841.39	$222,841.39	1.00
TAENSDPT0001	Shop dwg. Prepare and submitt	63	$222,841.39	02-Nov-25	13-Jan-26	02-Nov-25	13-Jan-26	$222,841.39	$222,841.39	1.00
TAENSDPT0002	Shop dwg.Review and Approval	2	$0.00	12-Jan-26	13-Jan-26	12-Jan-26	13-Jan-26	$0.00	$0.00	0.00
Shop Drawing for TSE Networks		70	$202,254.99	02-Nov-25	21-Jan-26	02-Nov-25	21-Jan-26	$202,254.99	$202,254.99	1.00
TAENSDTS0001	Shop dwg. Prepare and submitt	70	$202,254.99	02-Nov-25	21-Jan-26	02-Nov-25	21-Jan-26	$202,254.99	$202,254.99	1.00
TAENSDTS0002	Shop dwg. Review and Approval	2	$0.00	20-Jan-26	21-Jan-26	20-Jan-26	21-Jan-26	$0.00	$0.00	0.00
Shop Drawing for Sewerage Networks		108	$1,192,635.06	26-Oct-25	28-Feb-26	26-Oct-25	28-Feb-26	$1,192,635.06	$1,192,635.06	1.00
TAENSDSW0001	Shop dwg. Prepare and Submitt	108	$1,192,635.06	26-Oct-25	28-Feb-26	26-Oct-25	28-Feb-26	$1,192,635.06	$1,192,635.06	1.00
TAENSDSW0002	Shop dwg. Review and Approval	59	$0.00	22-Dec-25	28-Feb-26	22-Dec-25	28-Feb-26	$0.00	$0.00	0.00
Shop Drawing for Storm Networks		86	$1,189,783.27	21-Oct-25	28-Jan-26	21-Oct-25	28-Jan-26	$1,189,783.27	$1,189,783.27	1.00
TAENSDST0003	Shop dwg. Prepare and submit For Ponds	77	$391,152.56	21-Oct-25	18-Jan-26	21-Oct-25	18-Jan-26	$391,152.56	$391,152.56	1.00
TAENSDST0005	Shop dwg. Prepare and submit For Dike	85	$29,365.10	22-Oct-25	28-Jan-26	22-Oct-25	28-Jan-26	$29,365.10	$29,365.10	1.00
TAENSDST0001	Shop dwg. Prepare and submit For Storm Networks	73	$769,265.61	26-Oct-25	18-Jan-26	26-Oct-25	18-Jan-26	$769,265.61	$769,265.61	1.00
TAENSDST0002	Shop Dwg.Review and approval for Storm Networks	14	$0.00	03-Jan-26	18-Jan-26	03-Jan-26	18-Jan-26	$0.00	$0.00	0.00
TAENSDST0004	Shop Dwg.Review and approval for Ponds	4	$0.00	14-Jan-26	18-Jan-26	14-Jan-26	18-Jan-26	$0.00	$0.00	0.00
TAENSDST0006	Shop Dwg.Review and approval for Dike	2	$0.00	27-Jan-26	28-Jan-26	27-Jan-26	28-Jan-26	$0.00	$0.00	0.00
Prequalification for Suppliers		174	$0.00	04-Oct-25	23-Apr-26	04-Oct-25	23-Apr-26	$0.00	$0.00	0.00
Submittle of Material and Prequalification Road Works		169	$0.00	04-Oct-25	18-Apr-26	04-Oct-25	18-Apr-26	$0.00	$0.00	0.00
TAENPQRD0005	Submit Prequalification for Laboratory testing	37	$0.00	04-Oct-25	15-Nov-25	04-Oct-25	15-Nov-25	$0.00	$0.00	0.00
TAENPQRD0006	Prequalification Approval for Laboratory testing	2	$0.00	16-Oct-25	18-Oct-25	16-Oct-25	18-Oct-25	$0.00	$0.00	0.00
TAENPQRD0001	Submit Prequalification for Supplier Kerbs and Interlocking	1	$0.00	22-Oct-25	22-Oct-25	22-Oct-25	22-Oct-25	$0.00	$0.00	0.00
TAENPQRD0002	Prequalification Approval for Kerps and Interlocking Suppliers	11	$0.00	22-Oct-25	03-Nov-25	22-Oct-25	03-Nov-25	$0.00	$0.00	0.00
TAENPQRD0003	Submit Prequalification for Supplier Road Marking	3	$0.00	15-Apr-26	18-Apr-26	15-Apr-26	18-Apr-26	$0.00	$0.00	0.00
TAENPQRD0004	Prequalification Approval for Road Marking	2	$0.00	16-Apr-26	18-Apr-26	16-Apr-26	18-Apr-26	$0.00	$0.00	0.00
Submittle of Material and Prequalification for Electrical Works		53	$0.00	14-Jan-26	16-Mar-26	14-Jan-26	16-Mar-26	$0.00	$0.00	0.00
TAENPQEL0004	Prequalification Approval for Unit Stations	28	$0.00	14-Jan-26	15-Feb-26	14-Jan-26	15-Feb-26	$0.00	$0.00	0.00
TAENPQEL0005	Submit Prequalification for Lighting Poles	2	$0.00	14-Jan-26	15-Jan-26	14-Jan-26	15-Jan-26	$0.00	$0.00	0.00
TAENPQEL0007	Submit Prequalification for Luminares	2	$0.00	14-Jan-26	15-Jan-26	14-Jan-26	15-Jan-26	$0.00	$0.00	0.00
TAENPQEL0008	Prequalification Approval for Luminares	2	$0.00	14-Jan-26	15-Jan-26	14-Jan-26	15-Jan-26	$0.00	$0.00	0.00
TAENPQEL0006	Prequalification Approval for Lighting Poles	1	$0.00	15-Jan-26	15-Jan-26	15-Jan-26	16-Jan-26	$0.00	$0.00	0.00
TAENPQEL0011	Submit Prequalification for Ducts	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQEL0012	Prequalification Approval for Ducts	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQEL0001	Submit Prequalification for Cables Suppliers	2	$0.00	12-Feb-26	14-Feb-26	12-Feb-26	14-Feb-26	$0.00	$0.00	0.00
TAENPQEL0003	Submit Prequalification for Unit Stations	2	$0.00	12-Feb-26	14-Feb-26	12-Feb-26	14-Feb-26	$0.00	$0.00	0.00
TAENPQEL0002	Prequalification Approval for Cables Suppliers	2	$0.00	14-Feb-26	15-Feb-26	14-Feb-26	15-Feb-26	$0.00	$0.00	0.00
TAENPQEL0009	Submit Prequalification for Precast Drawpits and Foundations	1	$0.00	15-Mar-26	15-Mar-26	15-Mar-26	15-Mar-26	$0.00	$0.00	0.00
TAENPQEL0010	Prequalification Approval for Precast Drawpits and Foundations	2	$0.00	15-Mar-26	16-Mar-26	15-Mar-26	16-Mar-26	$0.00	$0.00	0.00
Submittle of Material and Prequalification for Telecommunications		2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQTL0001	Submit Prequalification for Ducts	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQTL0002	Prequalification Approval for Ducts	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQTL0003	Submit Prequalification for Manholes	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
TAENPQTL0004	Prequalification Approval for Manholes	2	$0.00	22-Jan-26	24-Jan-26	22-Jan-26	24-Jan-26	$0.00	$0.00	0.00
Submittle of Material and Prequalification for CCTV Networks		76	$0.00	26-Jan-26	23-Apr-26	26-Jan-26	23-Apr-26	$0.00	$0.00	0.00
TAENPQCC0001	Prepare Material Submittle for CCTV System	76	$0.00	26-Jan-26	23-Apr-26	26-Jan-26	23-Apr-26	$0.00	$0.00	0.00

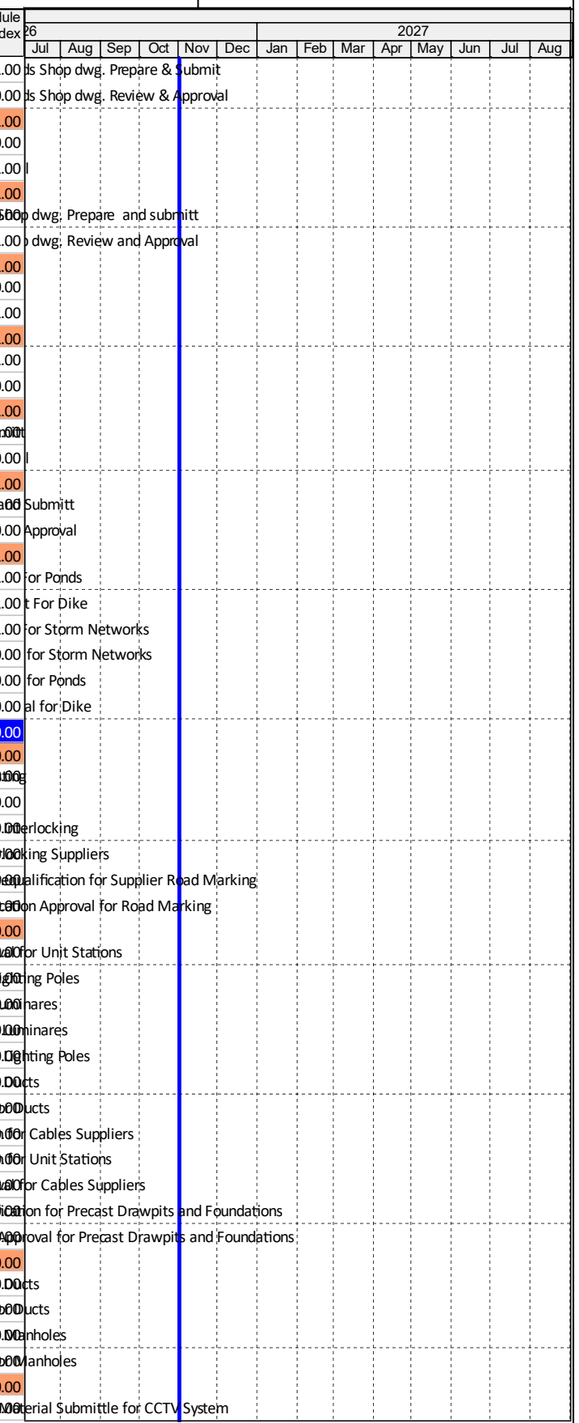


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAENPQCC0002	Review and Approval for Material Submittle for CCTV System	76	$0.00	26-Jan-26	23-Apr-26	26-Jan-26	23-Apr-26	$0.00	$0.00	0.00
Submittle of Material and Prequalification for Potable Water		6	$0.00	13-Nov-25	19-Nov-25	13-Nov-25	19-Nov-25	$0.00	$0.00	0.00
TAENPQPT0003	Prepare Material Submittle for Valves	1	$0.00	13-Nov-25	13-Nov-25	13-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQPT0004	Review and Approval of Material for Valves	5	$0.00	13-Nov-25	18-Nov-25	13-Nov-25	18-Nov-25	$0.00	$0.00	0.00
TAENPQPT0005	Prepare Material Submittle for Fire Hydrant	1	$0.00	13-Nov-25	13-Nov-25	13-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQPT0006	Review and Approval of Material for Fire Hydrant	6	$0.00	13-Nov-25	19-Nov-25	13-Nov-25	19-Nov-25	$0.00	$0.00	0.00
TAENPQPT0001	Prepare Material Submittle for HDPE Pipes	3	$0.00	15-Nov-25	17-Nov-25	15-Nov-25	17-Nov-25	$0.00	$0.00	0.00
TAENPQPT0002	Review and Approval of Material Submittle for HDPE Pipes	3	$0.00	15-Nov-25	17-Nov-25	15-Nov-25	17-Nov-25	$0.00	$0.00	0.00
Submittle of Material and Prequalification for TSE Networks		10	$0.00	13-Nov-25	24-Nov-25	13-Nov-25	24-Nov-25	$0.00	$0.00	0.00
TAENPQTS0003	Prepare Material Submittle for Valves	1	$0.00	13-Nov-25	13-Nov-25	13-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQTS0004	Review and Approval of Material for Valves	10	$0.00	13-Nov-25	24-Nov-25	13-Nov-25	24-Nov-25	$0.00	$0.00	0.00
TAENPQTS0001	Prepare Material Submittle for HDPE Pipes	1	$0.00	15-Nov-25	15-Nov-25	15-Nov-25	15-Nov-25	$0.00	$0.00	0.00
TAENPQTS0002	Review and Approval of Material Submittle for HDPE Pipes	3	$0.00	15-Nov-25	17-Nov-25	15-Nov-25	17-Nov-25	$0.00	$0.00	0.00
Submittle of Material and Prequalification for Sewerage Networks		6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQSW0001	Prepare Material Submittle for GRP Pipes	6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQSW0002	Review and Approval of Material Submittle for GRP Pipes	6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQSW0003	Prepare Material Submittle for Manhole	6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQSW0004	Review and Approval of Material Submittle for Manhole	6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
Submittle of Material and Prequalification for Storm Networks		23	$0.00	22-Oct-25	17-Nov-25	22-Oct-25	17-Nov-25	$0.00	$0.00	0.00
TAENPQST0011	Prepare Material Submittle for Concrete Works at Ponds	1	$0.00	22-Oct-25	22-Oct-25	22-Oct-25	22-Oct-25	$0.00	$0.00	0.00
TAENPQST0012	Review and Approval of Material Submittle for Concrete Works at Pond	11	$0.00	22-Oct-25	03-Nov-25	22-Oct-25	03-Nov-25	$0.00	$0.00	0.00
TAENPQST0001	Prepare Material Submittle for GRP Pipes	1	$0.00	08-Nov-25	08-Nov-25	08-Nov-25	08-Nov-25	$0.00	$0.00	0.00
TAENPQST0002	Review and Approval of Material Submittle for GRP Pipes	6	$0.00	08-Nov-25	13-Nov-25	08-Nov-25	13-Nov-25	$0.00	$0.00	0.00
TAENPQST0005	Prepare Material Submittle for Box Culvert	1	$0.00	15-Nov-25	15-Nov-25	15-Nov-25	15-Nov-25	$0.00	$0.00	0.00
TAENPQST0006	Review and Approval of Material Submittle for Box Culvert	3	$0.00	15-Nov-25	17-Nov-25	15-Nov-25	17-Nov-25	$0.00	$0.00	0.00
TAENPQST0007	Prepare Material Submittle for Catch Basin	1	$0.00	15-Nov-25	15-Nov-25	15-Nov-25	15-Nov-25	$0.00	$0.00	0.00
TAENPQST0008	Review and Approval of Material Submittle for Catch Basin	3	$0.00	15-Nov-25	17-Nov-25	15-Nov-25	17-Nov-25	$0.00	$0.00	0.00
TAENPQST0009	Prepare Material Submittle for Precast Manhole	1	$0.00	15-Nov-25	15-Nov-25	15-Nov-25	15-Nov-25	$0.00	$0.00	0.00
TAENPQST0010	Review and Approval of Material Submittle for Precast Manhole	2	$0.00	15-Nov-25	16-Nov-25	15-Nov-25	16-Nov-25	$0.00	$0.00	0.00
TAENPQST0003	Prepare Material Submittle for UPVC Pipes	1	$0.00	16-Nov-25	16-Nov-25	16-Nov-25	16-Nov-25	$0.00	$0.00	0.00
TAENPQST0004	Review and Approval of Material Submittle for UPVC Pipes	2	$0.00	16-Nov-25	17-Nov-25	16-Nov-25	17-Nov-25	$0.00	$0.00	0.00
Method Statement		124	$0.00	25-Nov-25	18-Apr-26	25-Nov-25	18-Apr-26	$0.00	$0.00	0.00
Earth Works (Excavation & Backfilling)		4	$0.00	25-Nov-25	29-Nov-25	25-Nov-25	29-Nov-25	$0.00	$0.00	0.00
TAENMSRD0001	Prepare and Submit MOS for Earth works	4	$0.00	25-Nov-25	29-Nov-25	25-Nov-25	29-Nov-25	$0.00	$0.00	0.00
TAENMSRD0002	Review and Approval MOS for Earth worksrs	1	$0.00	29-Nov-25	29-Nov-25	28-Nov-25	29-Nov-25	$0.00	$0.00	0.00
Asphalt works		38	$0.00	06-Dec-25	18-Jan-26	06-Dec-25	18-Jan-26	$0.00	$0.00	0.00
TAENMSRD0003	Prepare and Submit MOS for Asphalt works	36	$0.00	06-Dec-25	15-Jan-26	06-Dec-25	15-Jan-26	$0.00	$0.00	0.00
TAENMSRD0004	Revies and Approval MOS for Asphalt works	2	$0.00	17-Jan-26	18-Jan-26	17-Jan-26	18-Jan-26	$0.00	$0.00	0.00
Precast Concrete (Curbstone & Interlocking)		3	$0.00	15-Apr-26	18-Apr-26	15-Apr-26	18-Apr-26	$0.00	$0.00	0.00
TAENMSRD0005	Prepare and Submit MOS for Curbstone and Interlocking	2	$0.00	15-Apr-26	16-Apr-26	15-Apr-26	16-Apr-26	$0.00	$0.00	0.00
TAENMSRD0006	Review and Approval MOS for Curbstone and Interlocking	2	$0.00	16-Apr-26	18-Apr-26	16-Apr-26	18-Apr-26	$0.00	$0.00	0.00
Street Lighting		3	$0.00	19-Jan-26	21-Jan-26	19-Jan-26	21-Jan-26	$0.00	$0.00	0.00
TAENMSEL0001	Prepare and Submit MOS for Street Lighting	2	$0.00	19-Jan-26	20-Jan-26	19-Jan-26	20-Jan-26	$0.00	$0.00	0.00
TAENMSEL0002	Review and Approval MOS for Street Lighting	2	$0.00	20-Jan-26	21-Jan-26	20-Jan-26	21-Jan-26	$0.00	$0.00	0.00
Telecommunications		2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
TAENMSTC0001	Prepare and Submit MOS for TC	2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
TAENMSTC0002	Review and Approval MOS for TC	2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
CCTV Networks		2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
TAENMSCC0001	Prepare and Submit MOS for CCTV System	2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
TAENMSCC0002	Review and Approval MOS for CCTV Syestem	2	$0.00	07-Feb-26	08-Feb-26	07-Feb-26	08-Feb-26	$0.00	$0.00	0.00
Potable Water Networks		2	$0.00	25-Nov-25	26-Nov-25	25-Nov-25	26-Nov-25	$0.00	$0.00	0.00
TAENMSPT0001	Prepare and Submit MOS for Potable Network	2	$0.00	25-Nov-25	26-Nov-25	25-Nov-25	26-Nov-25	$0.00	$0.00	0.00
TAENMSPT0002	Review and Approval MOS for Potable Networks	2	$0.00	25-Nov-25	26-Nov-25	25-Nov-25	26-Nov-25	$0.00	$0.00	0.00
TSE Networks		7	$0.00	01-Mar-26	08-Mar-26	01-Mar-26	08-Mar-26	$0.00	$0.00	0.00
TAENMSTS0001	Prepare and Submit MOS for TSE Network	6	$0.00	01-Mar-26	07-Mar-26	01-Mar-26	07-Mar-26	$0.00	$0.00	0.00

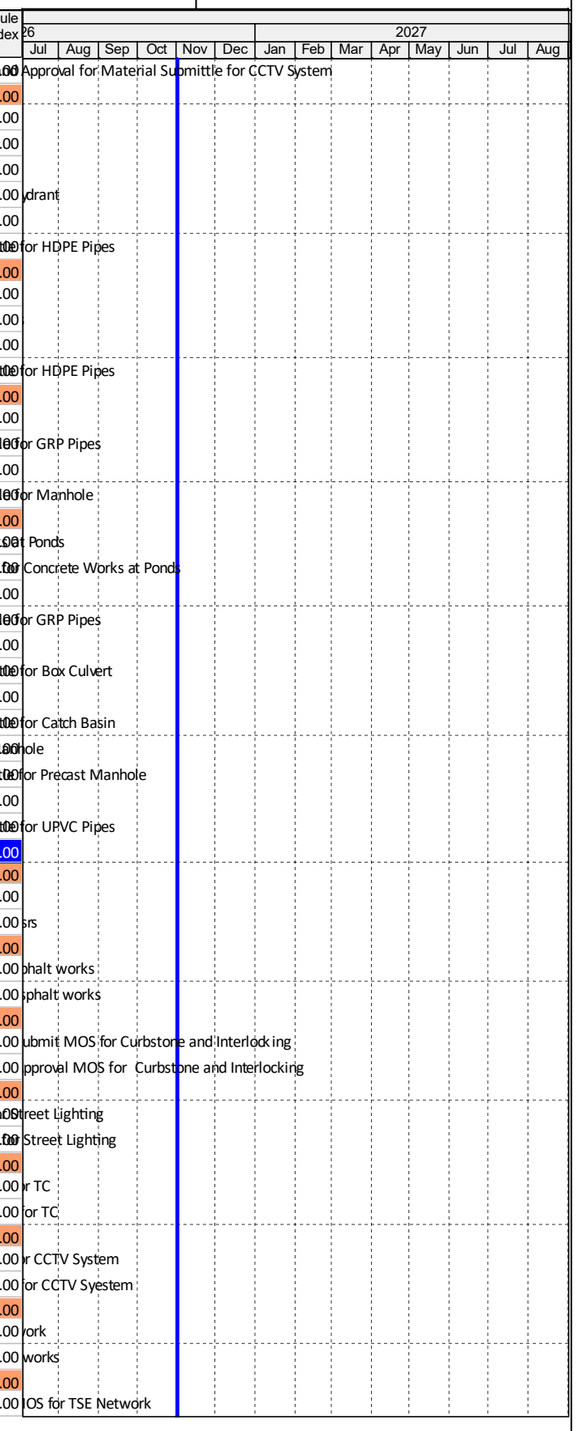


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAENMSTS0002	Review and Approval MOS for TSENetworks	7	$0.00	01-Mar-26	08-Mar-26	01-Mar-26	08-Mar-26	$0.00	$0.00	0.00
Sewerage Networks		3	$0.00	16-Dec-25	18-Dec-25	16-Dec-25	18-Dec-25	$0.00	$0.00	0.00
TAENMSSW0001	Prepare and Submit MOS for Sewer Network	3	$0.00	16-Dec-25	18-Dec-25	16-Dec-25	18-Dec-25	$0.00	$0.00	0.00
TAENMSSW0002	Review and Approval MOS for Sewer Networks	2	$0.00	17-Dec-25	18-Dec-25	17-Dec-25	18-Dec-25	$0.00	$0.00	0.00
Storm Networks		5	$0.00	20-Dec-25	24-Dec-25	20-Dec-25	24-Dec-25	$0.00	$0.00	0.00
TAENMSST0001	Prepare and Submit MOS for Storm Network	2	$0.00	20-Dec-25	21-Dec-25	20-Dec-25	21-Dec-25	$0.00	$0.00	0.00
TAENMSST0002	Review and Approval MOS for Storm Networks	5	$0.00	20-Dec-25	24-Dec-25	20-Dec-25	24-Dec-25	$0.00	$0.00	0.00
Precast Box Culvert		5	$0.00	20-Dec-25	24-Dec-25	20-Dec-25	24-Dec-25	$0.00	$0.00	0.00
TAENMSST0003	Prepare and Submit MOS for Box Culvert	2	$0.00	20-Dec-25	21-Dec-25	20-Dec-25	21-Dec-25	$0.00	$0.00	0.00
TAENMSST0004	Review and Approval MOS Box Culvert	5	$0.00	20-Dec-25	24-Dec-25	20-Dec-25	24-Dec-25	$0.00	$0.00	0.00
PROCUREMENT		604	$28,093,572.39	27-Oct-25	02-Sep-27	27-Oct-25		$15,790,681.52	$18,068,599.86	1.14
Material Purchase Order		283	$0.00	01-Nov-25	08-Sep-26	01-Nov-25	25-Jul-26	$0.00	$0.00	0.00
Material Purchase Order for Road Works		183	$0.00	01-Nov-25	02-Jun-26	01-Nov-25	02-Jun-26	$0.00	$0.00	0.00
TAPQPORD0001	Roads material Approved suppliers and issue po	183	$0.00	01-Nov-25	02-Jun-26	01-Nov-25	02-Jun-26	$0.00	$0.00	0.00
Material Purchase Order for Electrical Works		58	$0.00	23-Apr-26	10-Jun-26	23-Apr-26	02-Jul-26	$0.00	$0.00	0.00
TAPQPOEL0001	Electrical material Approved suppliers and issue po	35	$0.00	23-Apr-26	02-Jun-26	23-Apr-26	02-Jun-26	$0.00	$0.00	0.00
TAPQPOEL1	Electrical material Approved suppliers and issue po Part 01	7	$0.00	03-Jun-26	10-Jun-26	20-Jun-26	02-Jul-26	$0.00	$0.00	0.00
Material Purchase Order for Telecommunication		37	$0.00	03-Jun-26	15-Jul-26	20-Jun-26	22-Jul-26	$0.00	$0.00	0.00
TAPQPOTC0001	HDPE material Approved suppliers and issue po	37	$0.00	03-Jun-26	15-Jul-26	20-Jun-26	22-Jul-26	$0.00	$0.00	0.00
Material Purchase Order for CCTV Networks		62	$0.00	29-Jun-26	08-Sep-26	16-Jul-26	25-Jul-26	$0.00	$0.00	0.00
TAPQPOCC0001	CCTV material Approved suppliers and issue po	62	$0.00	29-Jun-26	08-Sep-26	16-Jul-26	25-Jul-26	$0.00	$0.00	0.00
Material Purchase Order for Potable Networks		122	$0.00	03-Jan-26	24-May-26	03-Jan-26	24-May-26	$0.00	$0.00	0.00
TAPQPOPT0001	Potable Water material Approved suppliers and issue po	122	$0.00	03-Jan-26	24-May-26	03-Jan-26	24-May-26	$0.00	$0.00	0.00
Material Purchase Order for TSE Networks		122	$0.00	03-Jan-26	24-May-26	03-Jan-26	24-May-26	$0.00	$0.00	0.00
TAPQPOTS0001	TSE material Approved suppliers and issue po	122	$0.00	03-Jan-26	24-May-26	03-Jan-26	24-May-26	$0.00	$0.00	0.00
Material Purchase Order for Sewrage Networks		62	$0.00	19-Nov-25	29-Jan-26	19-Nov-25	29-Jan-26	$0.00	$0.00	0.00
TAPQPOSW0001	Sanitary Sewerage material Approved suppliers and issue po	62	$0.00	19-Nov-25	29-Jan-26	19-Nov-25	29-Jan-26	$0.00	$0.00	0.00
Material Purchase Order for Storm Networks		148	$0.00	03-Dec-25	24-May-26	03-Dec-25	24-May-26	$0.00	$0.00	0.00
TAPQPOST0001	Storm Water material Approved suppliers and issue po	148	$0.00	03-Dec-25	24-May-26	03-Dec-25	24-May-26	$0.00	$0.00	0.00
Material Fabrication and Delivery		604	$28,093,572.39	27-Oct-25	02-Sep-27	27-Oct-25		$15,790,681.52	$18,068,599.86	1.14
Material Fabrication and Delivery for Road Works		604	$12,082,954.93	27-Oct-25	02-Sep-27	27-Oct-25		$2,796,728.97	$3,910,189.35	1.40
TAPQDVRD0007	Backfilling Material Delivery to Site	107	$1,244,052.99	27-Oct-25	28-Feb-26	27-Oct-25	28-Feb-26	$1,244,052.99	$1,244,052.99	1.00
TAPQDVRD0002	BBC Base Course Delivery to Site	6	$492,956.35	29-Mar-26	04-Apr-26	29-Mar-26	04-Apr-26	$492,956.35	$492,956.35	1.00
TAPQDVRD0004	Precast Concrete Curbstone Delivery to Site	10	$63,939.74	07-Apr-26	18-Apr-26	07-Apr-26	18-Apr-26	$63,939.74	$63,939.74	1.00
TAPQDVRD0001	ABC Delivery to Site	46	$8,581.85	09-Apr-26	01-Jun-26	09-Apr-26	02-Jun-26	$8,581.85	$8,581.85	1.00
TAPQDVRD0008	Marking for Road delivery to site	2	$130,360.33	22-Apr-26	23-Apr-26	22-Apr-26	23-Apr-26	$130,360.33	$130,360.33	1.00
TAPQDVRD0009	Trafic Sinage delivery to site	4	$7,235.06	28-Apr-26	02-May-26	28-Apr-26	02-May-26	$7,235.06	$7,235.06	1.00
TAPQDVRD00011	ABC Delivery to Site Part 01	71	$849,602.65	03-Jun-26	24-Aug-26	15-Jun-26		$849,602.65	$467,281.46	0.55
TAPQDVRD00041	Precast Concrete Curbstone Delivery to Site part 01	60	$1,214,855.00	28-Feb-27	08-May-27	29-Jul-26		$0.00	$194,376.80	0.00
TAPQDVRD00021	BBC Base Course Delivery to Site Part 01	74	$3,615,013.25	19-Apr-27	13-Jul-27	15-Jun-26		$0.00	$1,301,404.77	0.00
TAPQDVRD0003	BWC Asphalt Wearing Course Delivery to Site	35	$2,344,012.00	14-Jul-27	23-Aug-27			$0.00	$0.00	0.00
TAPQDVRD00081	Marking for Road delivery to site Part 01	5	$555,746.67	14-Jul-27	19-Jul-27			$0.00	$0.00	0.00
TAPQDVRD0005	Precast Concrete Interlocking Delivery to Site	40	$1,202,081.10	18-Jul-27	01-Sep-27			$0.00	$0.00	0.00
TAPQDVRD00091	Trafic Sinage delivery to site Part 01	9	$354,517.94	24-Aug-27	02-Sep-27			$0.00	$0.00	0.00
Material Fabrication and Delivery for Electrical Works		327	$3,224,132.68	29-Apr-26	21-Apr-27	29-Apr-26		$1,467,252.68	$1,633,447.67	1.11
TAPQDVEL0001	Pipes ,Fittings Delivery to Site	1	$296,510.21	29-Apr-26	29-Apr-26	29-Apr-26	29-Apr-26	$296,510.21	$296,510.21	1.00
TAPQDVEL00011	Pipes ,Fittings Delivery to Site Part 01	25	$127,075.80	11-Jun-26	09-Jul-26	18-Jul-26		$127,075.80	$113,097.46	0.89
TAPQDVEL0002	cables (LV,MV)Delivery to Site)	60	$1,002,000.00	20-Aug-26	28-Oct-26	09-Jun-26		$1,002,000.00	$581,160.00	0.58
TAPQDVEL0003	Poles & Luminares Delivery to Site	60	$833,333.33	29-Oct-26	06-Jan-27	21-Oct-26		$41,666.67	$250,000.00	6.00
TAPQDVEL0004	Substations & RMU ,ets.. Delivery to Site	90	$362,546.67	07-Jan-27	21-Apr-27	12-Jul-26	02-Sep-26	$0.00	$362,546.67	0.00
TAPQDVEL0005	Pre cast Drawpits and Pole Foundation Delivery	40	$602,666.67	14-Jan-27	01-Mar-27	24-Oct-26		$0.00	$30,133.33	0.00
Material Fabrication and Delivery for Telecommunication		60	$683,753.33	16-Jul-26	23-Sep-26	14-Jun-26		$683,753.33	$629,053.07	0.92
TAPQDVTC0001	Telecommunication Material (Pipes,,ets) Delivery	60	$683,753.33	16-Jul-26	23-Sep-26	14-Jun-26		$683,753.33	$629,053.07	0.92
Material Fabrication and Delivery for CCTV Networks		60	$552,633.38	24-Sep-26	02-Dec-26	19-Sep-26		$303,948.36	$469,738.37	1.55
TAPQDVCC0001	CCTV Material Cabls,Camera,Devices,ets) Delivery	60	$552,633.38	24-Sep-26	02-Dec-26	19-Sep-26		$303,948.36	$469,738.37	1.55
Material Fabrication and Delivery for Potable Networks		254	$1,485,609.25	18-Jan-26	21-Nov-26	18-Jan-26	13-Sep-26	$1,419,398.72	$1,485,609.25	1.05

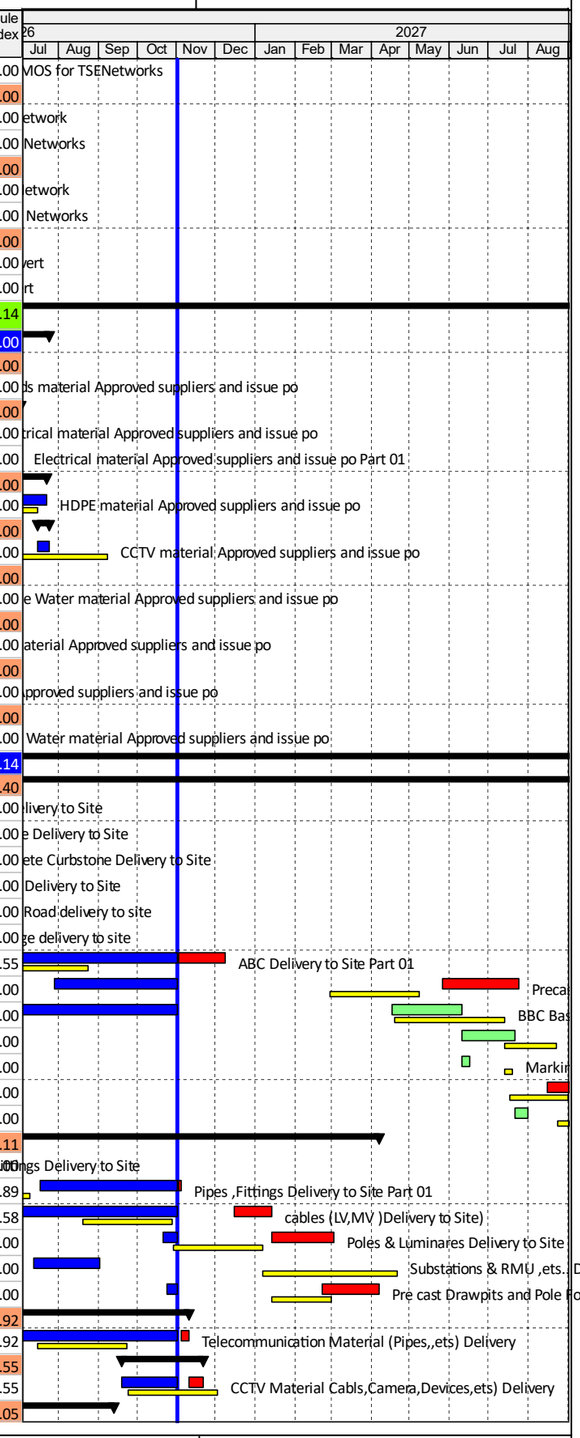


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAPQDVPT0001	PE Pipes Delivery	60	$535,645.48	18-Jan-26	28-Mar-26	18-Jan-26	03-May-26	$535,645.48	$535,645.48	1.00
TAPQDVPT0002	Valves Delivery to Site	74	$183,552.72	10-Feb-26	06-May-26	10-Feb-26	06-May-26	$183,552.72	$183,552.72	1.00
TAPQDVPT0003	Fire Hydrent Delivery to Site	65	$52,000.00	21-Feb-26	06-May-26	20-Feb-26	06-May-26	$52,000.00	$52,000.00	1.00
TAPQDVPT00011	PE Pipes Delivery Part 01	30	$514,639.77	13-Jul-26	16-Aug-26	15-Jun-26	30-Aug-26	$514,639.77	$514,639.77	1.00
TAPQDVPT00021	Valves Delivery to Site Part 01	45	$51,771.28	17-Aug-26	07-Oct-26	16-Jul-26	30-Aug-26	$51,771.28	$51,771.28	1.00
TAPQDVPT00031	Fire Hydrent Delivery to Site Part 01	38	$148,000.00	08-Oct-26	21-Nov-26	09-Jun-26	13-Sep-26	$81,789.47	$148,000.00	1.81
Material Fabrication and Delivery for TSE Networks		264	$1,348,366.62	22-Jan-26	14-Mar-27	22-Jan-26	30-Aug-26	$1,142,585.70	$1,348,366.62	1.18
TAPQDVTS0001	PE Pipes Delivery to Site	1	$518,714.18	22-Jan-26	22-Jan-26	22-Jan-26	22-Jan-26	$518,714.18	$518,714.18	1.00
TAPQDVTS0002	Valves Delivery to Site	7	$258,398.40	21-Feb-26	28-Feb-26	20-Feb-26	28-Feb-26	$258,398.40	$258,398.40	1.00
TAPQDVTS00011	PE Pipes Delivery to Site Part 01	90	$498,372.44	17-Aug-26	29-Nov-26	15-Jun-26	30-Aug-26	$365,473.12	$498,372.44	1.36
TAPQDVTS00021	Valves Delivery to Site Part 01	90	$72,881.60	30-Nov-26	14-Mar-27	16-Jul-26	30-Aug-26	$0.00	$72,881.60	0.00
Material Fabrication and Delivery for Sewerage Networks		316	$1,284,233.76	09-Dec-25	23-Aug-26	09-Dec-25		$1,284,233.76	$1,281,391.42	1.00
TAPQDVSW0001	GRP Pipes Delivery to Site	63	$840,000.00	09-Dec-25	19-Feb-26	09-Dec-25	19-Feb-26	$840,000.00	$840,000.00	1.00
TAPQDVSW0002	Fiberglass Manholes,ets) Delivery	102	$281,391.42	29-Jan-26	27-May-26	29-Jan-26	27-May-26	$281,391.42	$281,391.42	1.00
TAPQDVSW00011	GRP Pipes Delivery to Site Part 01	35	$160,000.00	03-Jun-26	13-Jul-26	16-Jul-26	31-Oct-26	$160,000.00	$160,000.00	1.00
TAPQDVSW00021	Fiberglass Manholes,ets) Delivery Part 01	35	$2,842.34	14-Jul-26	23-Aug-26			$2,842.34	$0.00	0.00
Material Fabrication and Delivery for Storm Networks		369	$7,431,888.44	29-Oct-25	02-Feb-27	29-Oct-25		$6,692,780.00	$7,310,804.12	1.09
TAPQDVST0008	Backfilling Material for Dike Delivery to Site	130	$39,916.80	29-Oct-25	29-Mar-26	29-Oct-25	29-Mar-26	$39,916.80	$39,916.80	1.00
TAPQDVST0002	GRP Pipes with Fittings Delivery Part 1	19	$1,442,324.77	09-Dec-25	30-Dec-25	09-Dec-25	30-Dec-25	$1,442,324.77	$1,442,324.77	1.00
TAPQDVST0003	GRP Pipes with Fittings Delivery Part 2	39	$1,333,333.13	31-Dec-25	14-Feb-26	31-Dec-25	14-Feb-26	$1,333,333.13	$1,333,333.13	1.00
TAPQDVST0001	UPVC Pipes with Fittings Delivery	28	$643,250.62	18-Jan-26	18-Feb-26	18-Jan-26	19-Feb-26	$643,250.62	$643,250.62	1.00
TAPQDVST0006	Manholes,ets Delivery	100	$482,588.71	07-Feb-26	02-Jun-26	07-Feb-26	02-Jun-26	$482,588.71	$482,588.71	1.00
TAPQDVST0004	GRP Pipes with Fittings Delivery Part 3	13	$1,133,333.05	14-Feb-26	28-Feb-26	14-Feb-26	28-Feb-26	$1,133,333.05	$1,133,333.05	1.00
TAPQDVST0005	Box Culvert Delivery	69	$855,241.72	04-Mar-26	23-May-26	04-Mar-26	23-May-26	$855,241.72	$855,241.72	1.00
TAPQDVST0007	RIprab,Sand,Marl gravel Delivery for Ponds	1	$43,763.00	22-Apr-26	22-Apr-26	22-Apr-26	22-Apr-26	$43,763.00	$43,763.00	1.00
TAPQDVST0010	Riprab for Dike Delivery to Site	6	$70,132.73	22-Apr-26	28-Apr-26	22-Apr-26	28-Apr-26	$70,132.73	$70,132.73	1.00
TAPQDVST00011	UPVC Pipes with Fittings Delivery Part 01	10	$6,497.48	03-Jun-26	14-Jun-26	02-Jul-26	05-Jul-26	$6,497.48	$6,497.48	1.00
TAPQDVST00101	Riprab for Dike Delivery to Site part 01	60	$85,717.78	03-Jun-26	11-Aug-26	15-Jun-26	02-Aug-26	$85,717.78	$85,717.78	1.00
TAPQDVST0009	Catchbasin Delivery to Site	60	$195,044.04	15-Jun-26	23-Aug-26	15-Jun-26		$195,044.04	$161,886.55	0.83
TAPQDVST00041	GRP Pipes with Fittings Delivery Part 4	60	$199,999.95	15-Jun-26	23-Aug-26	16-Jul-26	25-Oct-26	$199,999.95	$199,999.95	1.00
TAPQDVST00051	Box Culvert Delivery part 01	31	$64,373.03	24-Aug-26	28-Sep-26	15-Jun-26	25-Oct-26	$64,373.03	$64,373.03	1.00
TAPQDVST00061	Manholes,ets Delivery part 01	18	$4,874.63	29-Sep-26	19-Oct-26	12-Jul-26		$4,874.63	$97.49	0.02
TAPQDVST00071	RIprab,Sand,Marl gravel Delivery for Ponds part 01	90	$831,497.00	21-Oct-26	02-Feb-27	28-Jun-26		$92,388.56	$748,347.30	8.10
CONSTRUCTION WORKS		652	$94,113,467.75	04-Sep-25	03-Sep-27	04-Sep-25		$34,722,144.80	$48,121,429.95	1.39
ZONE 1		612	$19,581,738.06	21-Oct-25	03-Sep-27	21-Oct-25		$10,313,033.93	$12,531,966.44	1.22
Collector Road 02		482	$5,053,908.02	18-Nov-25	23-Jun-27	18-Nov-25		$2,083,114.68	$3,072,232.66	1.47
Road Works		482	$2,427,728.18	18-Nov-25	05-Jun-27	18-Nov-25		$709,671.06	$1,030,704.37	1.45
TAEXRDCC020001	Road Excavation and Disposal	38	$259,502.02	18-Nov-25	31-Dec-25	18-Nov-25	31-Dec-25	$259,502.02	$259,502.02	1.00
TAEXRDCC020002	Backfilling Works for Road	8	$214,217.40	20-Nov-25	29-Nov-25	20-Nov-25	29-Nov-25	$214,217.40	$214,217.40	1.00
TAEXRDCC020003	Subgrade Works	36	$235,951.64	10-Jan-26	19-Feb-26	10-Jan-26	19-Feb-26	$235,951.64	$235,951.64	1.00
TAEXRDCC0200021	Backfilling Works for Road Part 01	8	$11,274.60	07-Mar-27	15-Mar-27	25-Oct-26		$0.00	$2,254.92	0.00
TAEXRDCC0200031	Subgrade Works Part 01	8	$41,638.52	16-Mar-27	24-Mar-27	25-Oct-26		$0.00	$14,573.48	0.00
TAEXRDCC020004	ABC aggregate Base Course Works	16	$211,572.00	25-Mar-27	12-Apr-27	20-Sep-26		$0.00	$148,100.40	0.00
TAEXRDCC020005	MBC1 layer	1	$29,600.00	13-Apr-27	13-Apr-27	04-Oct-26		$0.00	$11,248.00	0.00
TAEXRDCC020006	BBC Base Course	4	$308,557.00	14-Apr-27	18-Apr-27	11-Oct-26		$0.00	$117,251.66	0.00
TAEXRDCC020008	Precast Concret Kerps	11	$394,355.00	19-Apr-27	01-May-27	31-Oct-26		$0.00	$27,604.85	0.00
TAEXRDCC020007	BWC Asphalt Wearing Course with RC	2	$211,511.00	02-May-27	03-May-27			$0.00	$0.00	0.00
TAEXRDCC020009	Precast Interlock Works	18	$402,199.00	04-May-27	24-May-27			$0.00	$0.00	0.00
TAEXRDCC020010	Stone Paving works	7	$47,000.00	25-May-27	01-Jun-27			$0.00	$0.00	0.00
TAEXRDCC020011	Road Marking	2	$7,850.00	02-Jun-27	03-Jun-27			$0.00	$0.00	0.00
TAEXRDCC020012	Traffic Sinage	1	$52,500.00	05-Jun-27	05-Jun-27			$0.00	$0.00	0.00
Electrical Works		111	$489,910.55	17-Sep-26	22-Mar-27	06-Sep-26		$78,072.55	$43,308.00	0.55
TAEXELCC020001	Trench Cut off	20	$78,072.55	17-Sep-26	10-Oct-26			$78,072.55	$0.00	0.00
TAEXELCC020002	Drawpit and PVC Pipes Installation	14	$32,120.00	14-Jan-27	30-Jan-27	20-Sep-26	01-Nov-26	$0.00	$32,120.00	0.00

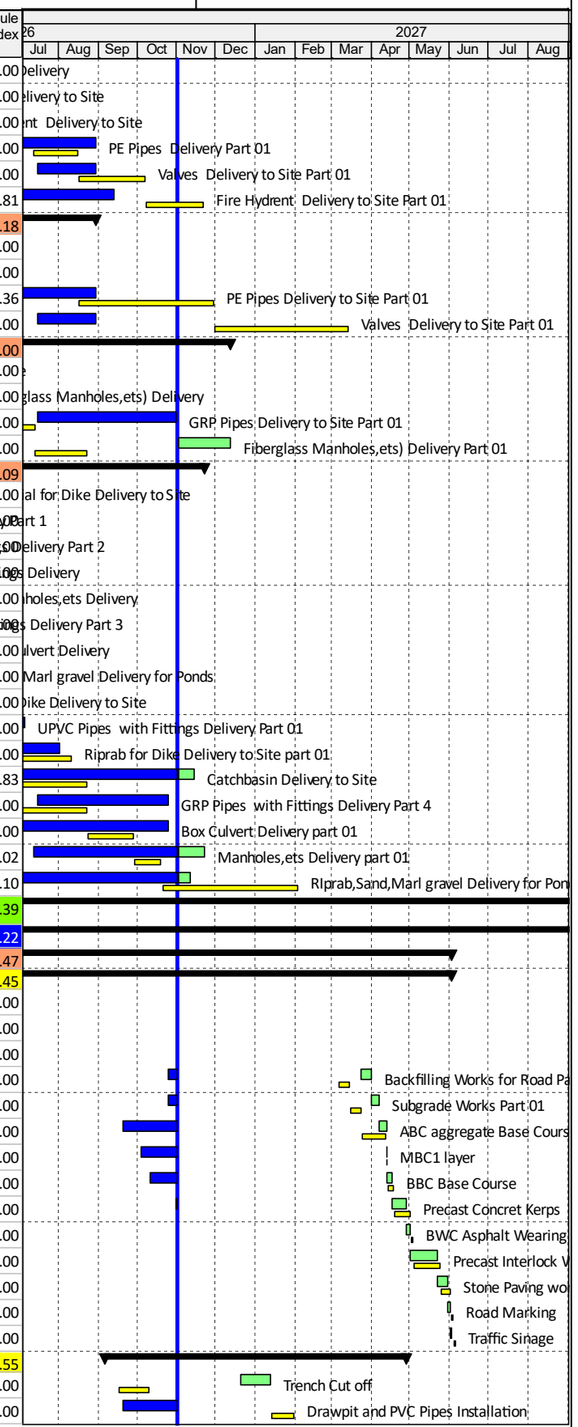


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXELCC020003	Road Crossing Ducts	4	$11,188.00	31-Jan-27	03-Feb-27	06-Sep-26	01-Nov-26	$0.00	$11,188.00	0.00
TAEXELCC020004	Trench Backfilling	18	$18,320.00	04-Feb-27	24-Feb-27			$0.00	$0.00	0.00
TAEXELCC020005	Cables Pulling	8	$248,000.00	25-Feb-27	06-Mar-27			$0.00	$0.00	0.00
TAEXELCC020006	Poles RC Foundation	6	$15,000.00	02-Mar-27	08-Mar-27			$0.00	$0.00	0.00
TAEXELCC020007	Earthing cables	10	$5,210.00	09-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCC020008	Lighting Pole Installation with Luminares	12	$82,000.00	09-Mar-27	22-Mar-27			$0.00	$0.00	0.00
Telecommunication Works		150	$171,388.23	09-Aug-26	05-Apr-27	20-Sep-26		$26,015.00	$92,425.23	3.55
TAEXTCCC020001	Trench Cut off	20	$26,015.00	09-Aug-26	31-Aug-26			$26,015.00	$0.00	0.00
TAEXTCCC020002	Drawpit and PVC Pipes Installation	8	$79,800.00	02-Mar-27	10-Mar-27	20-Sep-26	01-Nov-26	$0.00	$79,800.00	0.00
TAEXTCCC020003	Road Crossing Ducts	4	$12,625.23	11-Mar-27	15-Mar-27	20-Sep-26	01-Nov-26	$0.00	$12,625.23	0.00
TAEXTCCC020004	Trench Backfilling	18	$52,948.00	16-Mar-27	05-Apr-27			$0.00	$0.00	0.00
CCTV Works		60	$59,086.00	24-Jan-27	03-Apr-27			$0.00	$0.00	0.00
TAEXCCCC020001	Pipe Installation with manhole	10	$23,396.00	24-Jan-27	03-Feb-27			$0.00	$0.00	0.00
TAEXCCCC020002	CCTV Swiches Lighting panels Installation	18	$3,899.00	04-Feb-27	24-Feb-27			$0.00	$0.00	0.00
TAEXCCCC020003	Cable laying and connected with Panels	14	$25,974.00	25-Feb-27	13-Mar-27			$0.00	$0.00	0.00
TAEXCCCC020004	Pole Installation with IP Outdoor CCTV POE Camera	18	$5,817.00	14-Mar-27	03-Apr-27			$0.00	$0.00	0.00
Potable Networks		118	$307,045.54	14-Dec-26	16-Jun-27	30-Jun-26	17-Oct-26	$0.00	$307,045.54	0.00
TAEXPTCC020001	Excavation works for Trench	20	$54,010.00	14-Dec-26	05-Jan-27	30-Jun-26	19-Jul-26	$0.00	$54,010.00	0.00
TAEXPTCC020002	Bedding Works	2	$9,250.00	06-Jan-27	07-Jan-27	11-Jul-26	11-Aug-26	$0.00	$9,250.00	0.00
TAEXPTCC020003	Install Pipes & Fittings	16	$116,240.00	09-Jan-27	26-Jan-27	12-Jul-26	10-Aug-26	$0.00	$116,240.00	0.00
TAEXPTCC020004	Backfilling Works for Trench	18	$48,085.92	27-Jan-27	16-Feb-27	11-Aug-26	30-Aug-26	$0.00	$48,085.92	0.00
TAEXPTCC020005	Install Valves with fittings	8	$13,600.00	10-May-27	18-May-27	28-Jul-26	17-Oct-26	$0.00	$13,600.00	0.00
TAEXPTCC020006	Install fire hydrent	8	$26,200.00	19-May-27	27-May-27	02-Sep-26	17-Oct-26	$0.00	$26,200.00	0.00
TAEXPTCC020007	Valve Chamber works	11	$20,600.00	29-May-27	09-Jun-27	29-Aug-26	10-Oct-26	$0.00	$20,600.00	0.00
TAEXPTCC020008	Inspection Test	6	$19,059.62	10-Jun-27	16-Jun-27	03-Oct-26	04-Oct-26	$0.00	$19,059.62	0.00
TSE Networks		291	$198,873.34	19-Apr-26	23-Jun-27	19-Apr-26	17-Oct-26	$69,554.34	$198,873.34	2.86
TAEXTSCC020001	Excavation works for Trench	39	$29,753.34	19-Apr-26	02-Jun-26	19-Apr-26	02-Jun-26	$29,753.34	$29,753.34	1.00
TAEXTSCC020002	Bedding Works	2	$9,375.00	07-May-26	09-May-26	07-May-26	09-May-26	$9,375.00	$9,375.00	1.00
TAEXTSCC020003	Install Pipes & Fittings	4	$30,426.00	07-May-26	11-May-26	07-May-26	11-May-26	$30,426.00	$30,426.00	1.00
TAEXTSCC0200021	Bedding Works Part 01	2	$3,125.00	29-Dec-26	30-Dec-26	16-Jun-26	24-Jun-26	$0.00	$3,125.00	0.00
TAEXTSCC0200031	Install Pipes & Fittings Part 01	8	$24,894.00	31-Dec-26	09-Jan-27	16-Jun-26	24-Jun-26	$0.00	$24,894.00	0.00
TAEXTSCC020004	Backfilling Works for Trench	18	$31,500.00	10-Jan-27	30-Jan-27	18-Jun-26	09-Aug-26	$0.00	$31,500.00	0.00
TAEXTSCC020005	Install Valves with fittings	8	$12,800.00	21-Jan-27	30-Jan-27	29-Aug-26	17-Oct-26	$0.00	$12,800.00	0.00
TAEXTSCC020006	Valve Chamber works	20	$48,600.00	31-Jan-27	22-Feb-27	13-Aug-26	10-Oct-26	$0.00	$48,600.00	0.00
TAEXTSCC020007	Inspection Test	6	$8,400.00	17-Jun-27	23-Jun-27	06-Sep-26	04-Oct-26	$0.00	$8,400.00	0.00
Sewerage Networks		429	$316,685.69	22-Nov-25	22-Mar-27	22-Nov-25	29-Oct-26	$289,497.24	$316,685.69	1.09
TAEXSWCC020001	Excavation works for Trench	8	$52,558.84	22-Nov-25	30-Nov-25	22-Nov-25	30-Nov-25	$52,558.84	$52,558.84	1.00
TAEXSWCC020002	Bedding Works	4	$24,348.50	15-Dec-25	18-Dec-25	15-Dec-25	18-Dec-25	$24,348.50	$24,348.50	1.00
TAEXSWCC020003	Install GRP Pipes & Fittings	12	$71,820.00	20-Dec-25	01-Jan-26	20-Dec-25	01-Jan-26	$71,820.00	$71,820.00	1.00
TAEXSWCC020004	Backfilling Works for Trench	18	$58,839.34	30-Dec-25	19-Jan-26	30-Dec-25	19-Jan-26	$58,839.34	$58,839.34	1.00
TAEXSWCC020005	Manhole Installation with backfilling	16	$60,555.56	30-Mar-26	16-Apr-26	30-Mar-26	16-Apr-26	$60,555.56	$60,555.56	1.00
TAEXSWCC020006	Leakage Test	5	$21,375.00	18-Apr-26	22-Apr-26	18-Apr-26	22-Apr-26	$21,375.00	$21,375.00	1.00
TAEXSWCC0200011	Excavation works for Trench Part 01	5	$2,766.25	30-Nov-26	05-Dec-26	19-Aug-26	20-Aug-26	$0.00	$2,766.25	0.00
TAEXSWCC0200021	Bedding Works Part 01	2	$1,281.50	06-Dec-26	07-Dec-26	27-Aug-26	29-Aug-26	$0.00	$1,281.50	0.00
TAEXSWCC0200031	Install GRP Pipes & Fittings Part 01	4	$3,780.00	08-Feb-27	11-Feb-27	05-Sep-26	10-Sep-26	$0.00	$3,780.00	0.00
TAEXSWCC0200041	Backfilling Works for Trench Part 01	6	$3,096.81	23-Feb-27	01-Mar-27	07-Oct-26	10-Oct-26	$0.00	$3,096.81	0.00
TAEXSWCC0200051	Manhole Installation with backfilling Part 01	5	$15,138.89	14-Mar-27	18-Mar-27	18-Jun-26	10-Oct-26	$0.00	$15,138.89	0.00
TAEXSWCC0200061	Leakage Test Part 01	3	$1,125.00	20-Mar-27	22-Mar-27	01-Oct-26	29-Oct-26	$0.00	$1,125.00	0.00
Storm Networks		429	$1,083,190.49	29-Nov-25	25-Mar-27	29-Nov-25	25-Oct-26	$910,304.49	$1,083,190.49	1.19
TAEXSTCC020001	Excavation works for Trench	15	$251,256.00	29-Nov-25	15-Dec-25	29-Nov-25	15-Dec-25	$251,256.00	$251,256.00	1.00
TAEXSTCC020002	Bedding Works	4	$131,574.49	16-Dec-25	20-Dec-25	16-Dec-25	20-Dec-25	$131,574.49	$131,574.49	1.00
TAEXSTCC020003	Install GRP Pipes & Fittings	12	$273,250.00	21-Dec-25	03-Jan-26	21-Dec-25	03-Jan-26	$273,250.00	$273,250.00	1.00
TAEXSTCC020004	Backfilling Works for Trench	18	$101,032.50	31-Dec-25	20-Jan-26	31-Dec-25	20-Jan-26	$101,032.50	$101,032.50	1.00
TAEXSTCC020005	Manhole Installation with backfilling	16	$149,285.50	02-Mar-26	19-Mar-26	02-Mar-26	19-Mar-26	$149,285.50	$149,285.50	1.00

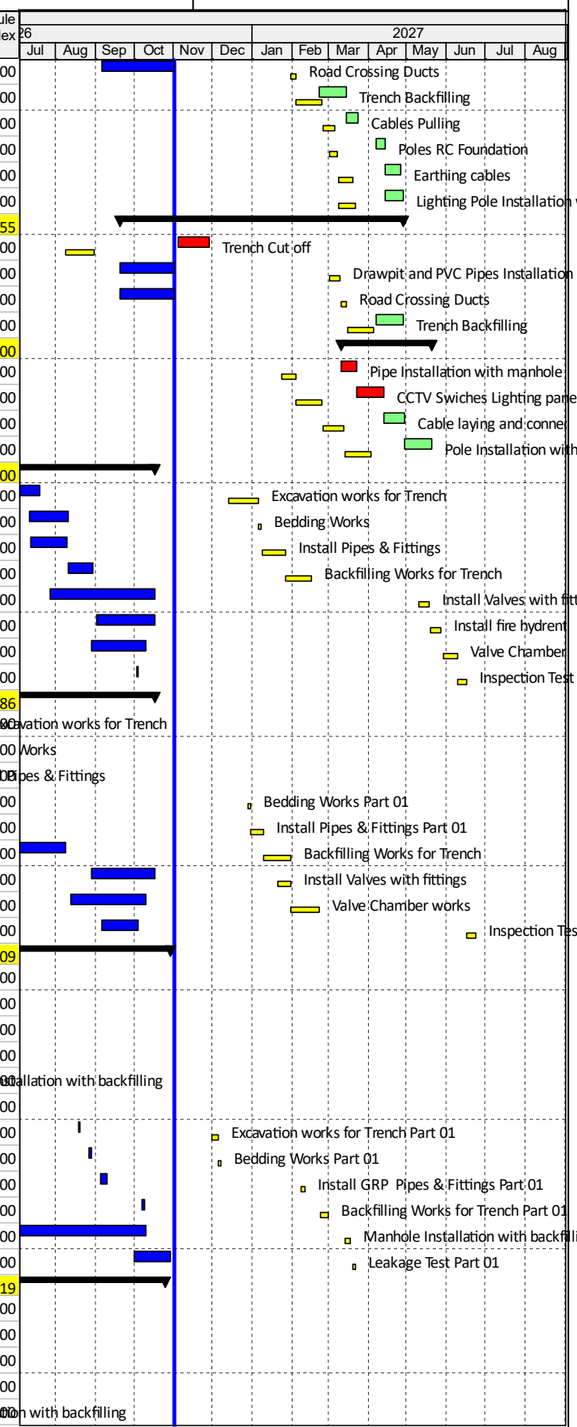


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXSTCC020007	Leakage Test	5	$3,906.00	18-Apr-26	22-Apr-26	18-Apr-26	22-Apr-26	$3,906.00	$3,906.00	1.00
TAEXSTCC0200041	Backfilling Works for Trench Part 01	5	$5,317.50	08-Dec-26	13-Dec-26	13-Sep-26	19-Sep-26	$0.00	$5,317.50	0.00
TAEXSTCC0200051	Manhole Installation with backfilling Part 01	6	$26,344.50	19-Dec-26	24-Dec-26	18-Jun-26	10-Oct-26	$0.00	$26,344.50	0.00
TAEXSTCC020006	Install Catch Basin with UPVC Pipes & Fittings	15	$126,530.00	21-Jan-27	07-Feb-27	08-Aug-26	25-Oct-26	$0.00	$126,530.00	0.00
TAEXSTCC0200071	Leakage Test Part 01	3	$14,694.00	23-Mar-27	25-Mar-27	17-Jun-26	04-Oct-26	$0.00	$14,694.00	0.00
Collector Road 03		419	$4,931,821.61	18-Jan-26	31-May-27	18-Jan-26		$3,543,378.61	$3,839,112.49	1.08
Road Works		413	$2,529,712.20	18-Jan-26	24-May-27	18-Jan-26		$1,499,197.20	$1,870,508.20	1.25
TAEXRDCC030003	Subgrade Works	14	$295,648.20	18-Jan-26	02-Feb-26	18-Jan-26	02-Feb-26	$295,648.20	$295,648.20	1.00
TAEXRDCC030001	Road Excavation and Disposal	14	$281,473.00	24-Mar-26	08-Apr-26	24-Mar-26	08-Apr-26	$281,473.00	$281,473.00	1.00
TAEXRDCC030002	Backfilling Works for Road	18	$340,932.00	09-Apr-26	29-Apr-26	09-Apr-26	29-Apr-26	$340,932.00	$340,932.00	1.00
TAEXRDCC030004	ABC aggregate Base Course Works	1	$22,236.60	21-May-26	21-May-26	21-May-26	21-May-26	$22,236.60	$22,236.60	1.00
TAEXRDCC0300041	ABC aggregate Base Course Works Part 01	5	$200,129.40	25-Aug-26	30-Aug-26	08-Jun-26	11-Jun-26	$200,129.40	$200,129.40	1.00
TAEXRDCC030005	MBC1 layer	1	$4,500.00	31-Aug-26	31-Aug-26	10-Jun-26	13-Jun-26	$4,500.00	$4,500.00	1.00
TAEXRDCC030006	BBC Base Course	4	$354,278.00	01-Sep-26	05-Sep-26	14-Jun-26	15-Jun-26	$354,278.00	$354,278.00	1.00
TAEXRDCC030008	Precast Concret Kerps	7	$371,311.00	02-May-27	09-May-27	02-Aug-26	16-Aug-26	$0.00	$371,311.00	0.00
TAEXRDCC030007	BWC Asphalt Wearing Course with RC	2	$251,511.00	10-May-27	11-May-27			$0.00	$0.00	0.00
TAEXRDCC030009	Precast Interlock Works	6	$349,143.00	12-May-27	18-May-27			$0.00	$0.00	0.00
TAEXRDCC030010	Stone Paving works	2	$21,000.00	19-May-27	20-May-27			$0.00	$0.00	0.00
TAEXRDCC030011	Road Marking	1	$4,100.00	22-May-27	22-May-27			$0.00	$0.00	0.00
TAEXRDCC030012	Traffic Sinage	2	$33,450.00	23-May-27	24-May-27			$0.00	$0.00	0.00
Electrical Works		323	$282,596.25	10-May-26	31-May-27	10-May-26		$89,030.25	$51,827.13	0.58
TAEXELCC030001	Trench Cut off	1	$37,203.13	10-May-26	10-May-26	10-May-26	10-May-26	$37,203.13	$37,203.13	1.00
TAEXELCC030002	Drawpit and PVC Pipes Installation	2	$7,000.00	11-May-26	12-May-26	11-May-26	12-May-26	$7,000.00	$7,000.00	1.00
TAEXELCC030003	Road Crossing Ducts	2	$2,600.00	11-May-26	12-May-26	11-May-26	12-May-26	$2,600.00	$2,600.00	1.00
TAEXELCC030004	Trench Backfilling	1	$5,024.00	12-May-26	12-May-26	12-May-26	12-May-26	$5,024.00	$5,024.00	1.00
TAEXELCC0300011	Trench Cut off Part 01	10	$37,203.12	06-Sep-26	16-Sep-26			$37,203.12	$0.00	0.00
TAEXELCC030005	Cables Pulling	4	$124,000.00	10-May-27	13-May-27			$0.00	$0.00	0.00
TAEXELCC0300041	Trench Backfilling Part 01	4	$7,536.00	15-May-27	18-May-27			$0.00	$0.00	0.00
TAEXELCC030006	Poles RC Foundation	3	$9,510.00	19-May-27	22-May-27			$0.00	$0.00	0.00
TAEXELCC030007	Earthing cables	2	$2,320.00	23-May-27	24-May-27			$0.00	$0.00	0.00
TAEXELCC030008	Lighting Pole Installation with Luminares	8	$50,200.00	23-May-27	31-May-27			$0.00	$0.00	0.00
Telecommunication Works		113	$142,360.00	24-Sep-26	04-Apr-27			$15,230.00	$0.00	0.00
TAEXTCCC030001	Trench Cut off	10	$15,230.00	24-Sep-26	05-Oct-26			$15,230.00	$0.00	0.00
TAEXTCCC030002	Drawpit and PVC Pipes Installation	7	$90,230.00	11-Mar-27	18-Mar-27			$0.00	$0.00	0.00
TAEXTCCC030003	Road Crossing Ducts	2	$8,600.00	20-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXTCCC030004	Trench Backfilling	12	$28,300.00	22-Mar-27	04-Apr-27			$0.00	$0.00	0.00
CCTV Works		162	$60,376.00	24-Sep-26	31-Mar-27			$23,144.00	$0.00	0.00
TAEXCCCC030001	Pipe Installation with manhole	7	$23,144.00	24-Sep-26	01-Oct-26			$23,144.00	$0.00	0.00
TAEXCCCC030002	CCTV Swiches Lighting panels Installation	12	$4,843.00	25-Feb-27	10-Mar-27			$0.00	$0.00	0.00
TAEXCCCC030003	Cable laying and connected with Panels	8	$25,943.00	11-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXCCCC030004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	21-Mar-27	31-Mar-27			$0.00	$0.00	0.00
Potable Networks		40	$269,163.54	31-Mar-26	16-May-26	31-Mar-26	16-May-26	$269,163.54	$269,163.54	1.00
TAEXPTCC030001	Excavation works for Trench	40	$56,114.62	31-Mar-26	16-May-26	31-Mar-26	16-May-26	$56,114.62	$56,114.62	1.00
TAEXPTCC030002	Bedding Works	24	$24,695.92	18-Apr-26	14-May-26	18-Apr-26	16-May-26	$24,695.92	$24,695.92	1.00
TAEXPTCC030003	Install Pipes & Fittings	23	$90,050.00	19-Apr-26	14-May-26	19-Apr-26	16-May-26	$90,050.00	$90,050.00	1.00
TAEXPTCC030004	Backfilling Works for Trench	22	$30,278.00	21-Apr-26	16-May-26	21-Apr-26	16-May-26	$30,278.00	$30,278.00	1.00
TAEXPTCC030006	Install fire hydrent	5	$50,520.00	05-May-26	10-May-26	05-May-26	10-May-26	$50,520.00	$50,520.00	1.00
TAEXPTCC030005	Install Valves with fittings	2	$13,500.00	09-May-26	10-May-26	09-May-26	10-May-26	$13,500.00	$13,500.00	1.00
TAEXPTCC030007	Inspection Test	3	$4,005.00	13-May-26	16-May-26	13-May-26	16-May-26	$4,005.00	$4,005.00	1.00
TSE Networks		18	$381,738.34	26-Apr-26	16-May-26	26-Apr-26	16-May-26	$381,738.34	$381,738.34	1.00
TAEXTSCC030001	Excavation works for Trench	18	$95,320.00	26-Apr-26	16-May-26	26-Apr-26	16-May-26	$95,320.00	$95,320.00	1.00
TAEXTSCC030002	Bedding Works	12	$26,000.00	03-May-26	16-May-26	03-May-26	16-May-26	$26,000.00	$26,000.00	1.00
TAEXTSCC030003	Install Pipes & Fittings	10	$150,215.00	05-May-26	16-May-26	05-May-26	16-May-26	$150,215.00	$150,215.00	1.00
TAEXTSCC030004	Backfilling Works for Trench	10	$30,150.00	05-May-26	16-May-26	05-May-26	16-May-26	$30,150.00	$30,150.00	1.00

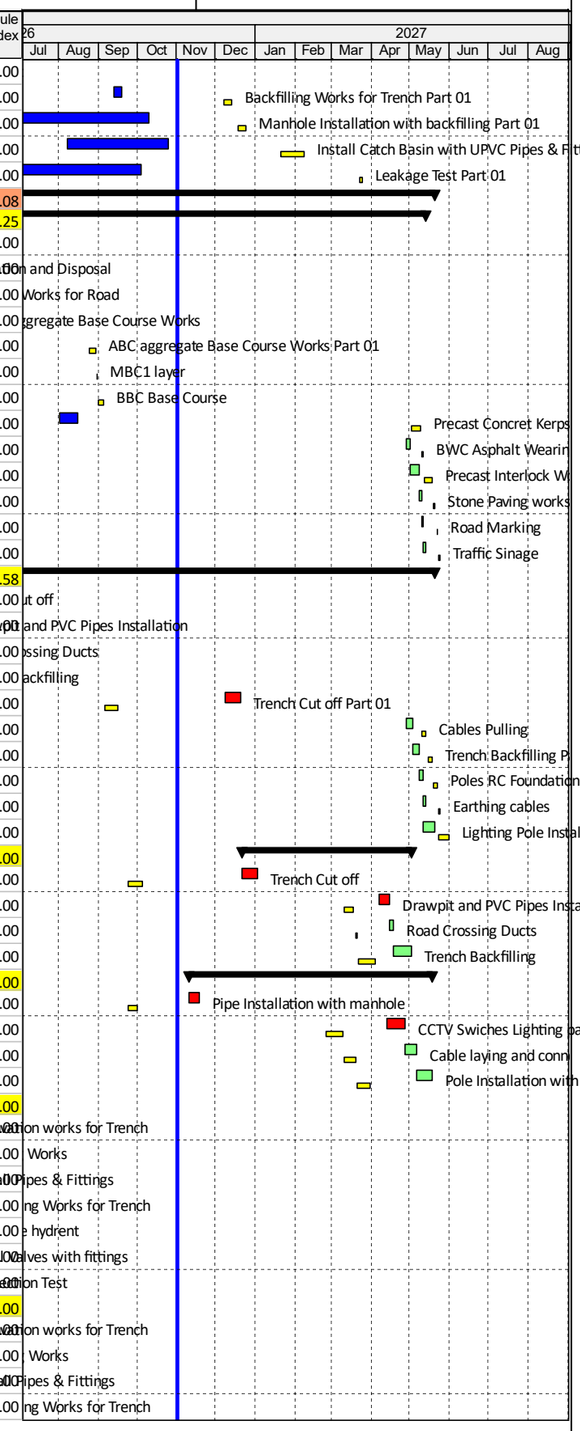


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTSCC030005	Inspection Test	4	$80,053.34	12-May-26	16-May-26	12-May-26	16-May-26	$80,053.34	$80,053.34	1.00
Storm Networks		75	$1,265,875.28	17-Feb-26	14-May-26	17-Feb-26	14-May-26	$1,265,875.28	$1,265,875.28	1.00
TAEXSTCC030001	Excavation works for Trench	11	$258,650.00	17-Feb-26	01-Mar-26	17-Feb-26	01-Mar-26	$258,650.00	$258,650.00	1.00
TAEXSTCC030002	Bedding Works	2	$97,545.28	12-Mar-26	14-Mar-26	12-Mar-26	14-Mar-26	$97,545.28	$97,545.28	1.00
TAEXSTCC030003	Install GRP Pipes & Fittings	37	$475,630.00	14-Mar-26	25-Apr-26	14-Mar-26	25-Apr-26	$475,630.00	$475,630.00	1.00
TAEXSTCC030004	Backfilling Works for Trench	40	$107,600.00	28-Mar-26	12-May-26	28-Mar-26	12-May-26	$107,600.00	$107,600.00	1.00
TAEXSTCC030005	Manhole Installation with backfilling	27	$178,200.00	12-Apr-26	12-May-26	12-Apr-26	12-May-26	$178,200.00	$178,200.00	1.00
TAEXSTCC030006	Install Catch Basin with UPVC Pipes & Fittings	9	$128,620.00	05-May-26	14-May-26	05-May-26	14-May-26	$128,620.00	$128,620.00	1.00
TAEXSTCC030007	Leakage Test	6	$19,630.00	06-May-26	12-May-26	06-May-26	12-May-26	$19,630.00	$19,630.00	1.00
Upgrade local 21		399	$3,626,292.58	12-Mar-26	08-Jun-27	12-Mar-26		$1,105,707.13	$1,363,155.99	1.23
Road Works		26	$982,585.00	10-May-27	08-Jun-27			$0.00	$0.00	0.00
TAEXRDCU210002	Precast Concret Kerps	9	$34,566.00	10-May-27	19-May-27			$0.00	$0.00	0.00
TAEXRDCU210001	BWC Asphalt Wearing Course with RC	1	$411,511.00	20-May-27	20-May-27			$0.00	$0.00	0.00
TAEXRDCU210003	Precast Interlock Works	7	$237,408.00	22-May-27	29-May-27			$0.00	$0.00	0.00
TAEXRDCU210004	Stone Paving works	5	$247,000.00	30-May-27	03-Jun-27			$0.00	$0.00	0.00
TAEXRDCU210005	Road Marking	1	$4,100.00	05-Jun-27	05-Jun-27			$0.00	$0.00	0.00
TAEXRDCU210006	Traffic Sinage	3	$48,000.00	06-Jun-27	08-Jun-27			$0.00	$0.00	0.00
Electrical Works		156	$461,815.70	17-Sep-26	29-May-27			$62,350.00	$0.00	0.00
TAEXELCU210001	Trench Cut off	13	$62,350.00	17-Sep-26	01-Oct-26			$62,350.00	$0.00	0.00
TAEXELCU210002	Drawpit and PVC Pipes Installation	12	$12,580.00	16-Mar-27	29-Mar-27			$0.00	$0.00	0.00
TAEXELCU210003	Road Crossing Ducts	6	$670.00	30-Mar-27	05-Apr-27			$0.00	$0.00	0.00
TAEXELCU210006	Poles RC Foundation	8	$24,510.00	30-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXELCU210004	Trench Backfilling	18	$11,250.00	06-Apr-27	26-Apr-27			$0.00	$0.00	0.00
TAEXELCU210008	Lighting Pole Installation with Luminares	10	$42,000.00	08-Apr-27	19-Apr-27			$0.00	$0.00	0.00
TAEXELCU210005	Cables Pulling	6	$123,932.70	27-Apr-27	03-May-27			$0.00	$0.00	0.00
TAEXELCU210009	Install Substation & RMU	9	$180,000.00	04-May-27	13-May-27			$0.00	$0.00	0.00
TAEXELCU210007	Earthing cables	4	$4,523.00	25-May-27	29-May-27			$0.00	$0.00	0.00
Telecommunication Works		125	$121,454.00	29-Oct-26	29-Apr-27			$4,331.57	$0.00	0.00
TAEXTCCU210001	Trench Cut off	14	$20,214.00	29-Oct-26	14-Nov-26			$4,331.57	$0.00	0.00
TAEXTCCU210002	Drawpit and PVC Pipes Installation	12	$20,240.00	20-Mar-27	01-Apr-27			$0.00	$0.00	0.00
TAEXTCCU210003	Road Crossing Ducts	6	$15,200.00	03-Apr-27	08-Apr-27			$0.00	$0.00	0.00
TAEXTCCU210004	Trench Backfilling	18	$65,800.00	10-Apr-27	29-Apr-27			$0.00	$0.00	0.00
CCTV Works		179	$55,102.00	03-Oct-26	28-Apr-27			$27,167.00	$0.00	0.00
TAEXCCCU210001	Pipe Installation with manhole	14	$27,167.00	03-Oct-26	18-Oct-26			$27,167.00	$0.00	0.00
TAEXCCCU210002	CCTV Swiches Lighting panels Installation	16	$3,647.00	11-Mar-27	29-Mar-27			$0.00	$0.00	0.00
TAEXCCCU210003	Cable laying and connected with Panels	12	$19,685.00	30-Mar-27	12-Apr-27			$0.00	$0.00	0.00
TAEXCCCU210004	Pole Installation with IP Outdoor CCTV POE Camera	14	$4,603.00	13-Apr-27	28-Apr-27			$0.00	$0.00	0.00
Potable Networks		162	$225,755.00	06-Dec-26	10-Mar-27	05-Sep-26		$0.00	$121,379.85	0.00
TAEXPTCU210001	Excavation works for Trench	20	$43,155.00	06-Dec-26	28-Dec-26	05-Sep-26		$0.00	$37,544.85	0.00
TAEXPTCU210002	Bedding Works	2	$7,050.00	29-Dec-26	30-Dec-26	14-Oct-26		$0.00	$5,287.50	0.00
TAEXPTCU210003	Install Pipes & Fittings	15	$92,350.00	31-Dec-26	17-Jan-27	17-Oct-26		$0.00	$69,262.50	0.00
TAEXPTCU210004	Backfilling Works for Trench	16	$24,100.00	18-Jan-27	04-Feb-27			$0.00	$0.00	0.00
TAEXPTCU210005	Install Valves with fittings	8	$9,600.00	27-Jan-27	04-Feb-27	27-Sep-26		$0.00	$1,440.00	0.00
TAEXPTCU210006	Install fire hydrent	8	$24,000.00	06-Feb-27	14-Feb-27	25-Oct-26		$0.00	$4,800.00	0.00
TAEXPTCU210007	Valve Chamber works	16	$20,300.00	15-Feb-27	04-Mar-27	27-Sep-26		$0.00	$3,045.00	0.00
TAEXPTCU210008	Inspection Test	5	$5,200.00	06-Mar-27	10-Mar-27			$0.00	$0.00	0.00
TSE Networks		81	$326,165.00	27-Oct-26	31-Jan-27	27-Sep-26		$9,173.28	$10,527.00	1.15
TAEXTSCU210001	Excavation works for Trench	29	$53,205.00	27-Oct-26	29-Nov-26			$9,173.28	$0.00	0.00
TAEXTSCU210002	Bedding Works	2	$10,500.00	30-Nov-26	01-Dec-26			$0.00	$0.00	0.00
TAEXTSCU210003	Install Pipes & Fittings	15	$155,630.00	02-Dec-26	19-Dec-26			$0.00	$0.00	0.00
TAEXTSCU210004	Backfilling Works for Trench	16	$30,150.00	20-Dec-26	06-Jan-27			$0.00	$0.00	0.00
TAEXTSCU210005	Install Valves with fittings	8	$11,580.00	29-Dec-26	06-Jan-27	27-Sep-26		$0.00	$1,737.00	0.00
TAEXTSCU210006	Valve Chamber works	16	$58,600.00	07-Jan-27	25-Jan-27	27-Sep-26		$0.00	$8,790.00	0.00
TAEXTSCU210007	Inspection Test	5	$6,500.00	26-Jan-27	31-Jan-27			$0.00	$0.00	0.00

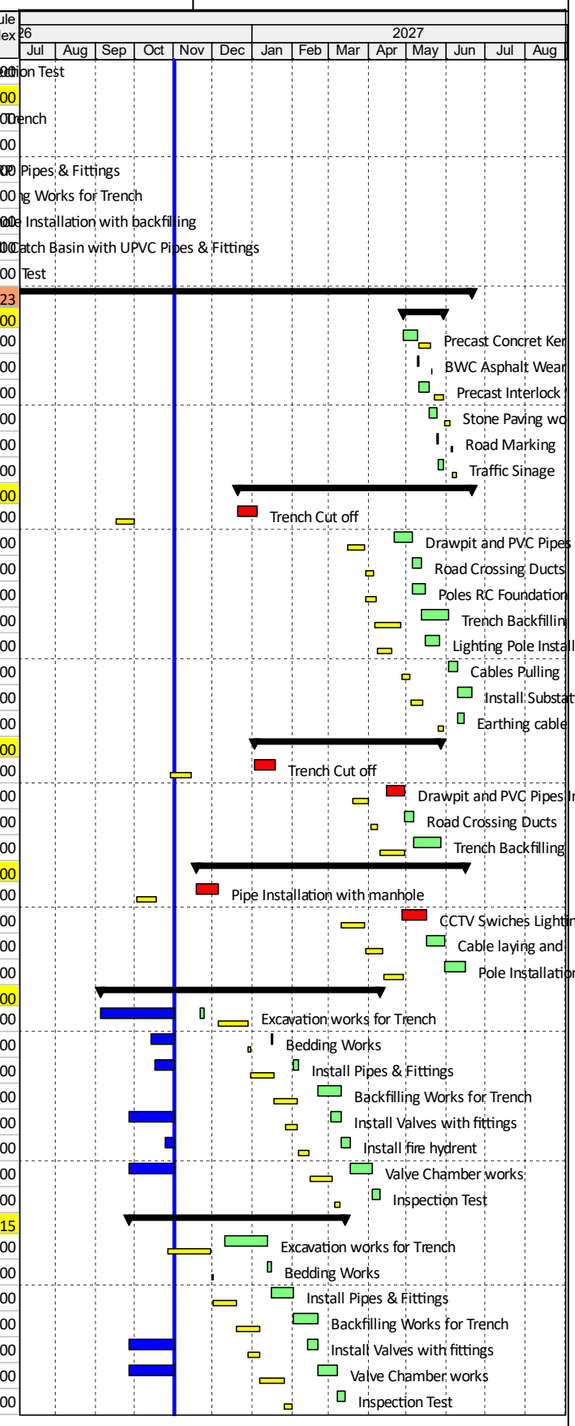


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Sewerage Networks		87	$326,630.60	21-Feb-27	09-May-27	09-Aug-26		$0.00	$243,549.12	0.00
TAEXSWCU210001	Excavation works for Trench	24	$54,350.00	21-Feb-27	20-Mar-27	09-Aug-26		$0.00	$47,284.50	0.00
TAEXSWCU210002	Bedding Works	3	$35,236.15	21-Mar-27	23-Mar-27	06-Sep-26		$0.00	$29,950.73	0.00
TAEXSWCU210003	Install GRP Pipes & Fittings	11	$70,250.00	24-Mar-27	05-Apr-27	09-Sep-26		$0.00	$59,712.50	0.00
TAEXSWCU210004	Backfilling Works for Trench	16	$44,700.00	05-Apr-27	22-Apr-27	18-Oct-26		$0.00	$35,760.00	0.00
TAEXSWCU210005	Manhole Installation with backfilling	15	$85,200.00	18-Apr-27	04-May-27	09-Sep-26		$0.00	$46,860.00	0.00
TAEXSWCU210006	Leakage Test	4	$36,894.45	05-May-27	09-May-27	31-Oct-26		$0.00	$23,981.39	0.00
Storm Networks		344	$1,126,785.28	12-Mar-26	30-Mar-27	12-Mar-26		$1,002,685.28	$987,700.02	0.99
TAEXSTCU210005	Manhole Installation with backfilling	36	$106,000.00	12-Mar-26	22-Apr-26	12-Mar-26	22-Apr-26	$106,000.00	$106,000.00	1.00
TAEXSTCU210001	Excavation works for Trench	42	$432,020.00	25-Mar-26	12-May-26	25-Mar-26	12-May-26	$432,020.00	$432,020.00	1.00
TAEXSTCU210002	Bedding Works	2	$83,168.02	09-Apr-26	11-Apr-26	09-Apr-26	11-Apr-26	$83,168.02	$83,168.02	1.00
TAEXSTCU210003	Install GRP Pipes & Fittings	6	$233,054.00	09-Apr-26	15-Apr-26	09-Apr-26	15-Apr-26	$233,054.00	$233,054.00	1.00
TAEXSTCU210004	Backfilling Works for Trench	9	$94,770.00	15-Apr-26	25-Apr-26	15-Apr-26	25-Apr-26	$94,770.00	$94,770.00	1.00
TAEXSTCU2100021	Bedding Works Part 01	1	$4,377.26	20-Sep-26	20-Sep-26			$4,377.26	$0.00	0.00
TAEXSTCU2100031	Install GRP Pipes & Fittings Part 01	3	$12,266.00	21-Sep-26	23-Sep-26	05-Jul-26		$12,266.00	$6,133.00	0.50
TAEXSTCU2100041	Backfilling Works for Trench Part 01	5	$10,530.00	06-Oct-26	11-Oct-26	05-Jul-26		$10,530.00	$5,265.00	0.50
TAEXSTCU2100051	Manhole Installation with backfilling Part 01	5	$26,500.00	20-Oct-26	25-Oct-26	15-Jun-26		$26,500.00	$13,250.00	0.50
TAEXSTCU210006	Install Catch Basin with UPVC Pipes & Fittings	14	$108,500.00	26-Dec-26	10-Jan-27			$0.00	$0.00	0.00
TAEXSTCU210007	Leakage Test	4	$15,600.00	27-Mar-27	30-Mar-27	11-Jun-26		$0.00	$14,040.00	0.00
Upgrade local 26		313	$255,196.00	03-Oct-26	03-Sep-27	12-Jul-26		$34,286.00	$62,717.40	1.83
Electrical Works		313	$204,663.00	03-Oct-26	03-Sep-27	12-Jul-26		$10,230.00	$62,717.40	6.13
TAEXELCU260001	Trench Cut off	14	$10,230.00	03-Oct-26	18-Oct-26	12-Jul-26		$10,230.00	$4,501.20	0.44
TAEXELCU260002	Drawpit and PVC Pipes Installation	12	$5,670.00	02-Mar-27	15-Mar-27	19-Aug-26	22-Aug-26	$0.00	$5,670.00	0.00
TAEXELCU260003	Road Crossing Ducts	4	$450.00	16-Mar-27	20-Mar-27	15-Aug-26	16-Aug-26	$0.00	$450.00	0.00
TAEXELCU260006	Poles RC Foundation	6	$18,210.00	16-Mar-27	22-Mar-27			$0.00	$0.00	0.00
TAEXELCU260004	Trench Backfilling	13	$9,580.00	21-Mar-27	04-Apr-27	03-Sep-26		$0.00	$3,736.20	0.00
TAEXELCU260008	Lighting Pole Installation with Luminares	8	$32,000.00	23-Mar-27	31-Mar-27			$0.00	$0.00	0.00
TAEXELCU260005	Cables Pulling	4	$124,000.00	05-Apr-27	08-Apr-27	01-Aug-26		$0.00	$48,360.00	0.00
TAEXELCU260007	Earthing cables	4	$4,523.00	31-Aug-27	03-Sep-27			$0.00	$0.00	0.00
CCTV Works		169	$50,533.00	19-Oct-26	03-May-27			$24,056.00	$0.00	0.00
TAEXCCCU260001	Pipe Installation with manhole	10	$24,056.00	19-Oct-26	29-Oct-26			$24,056.00	$0.00	0.00
TAEXCCCU260002	CCTV Swiches Lighting panels Installation	12	$2,264.00	30-Mar-27	12-Apr-27			$0.00	$0.00	0.00
TAEXCCCU260003	Cable laying and connected with Panels	8	$17,767.00	13-Apr-27	21-Apr-27			$0.00	$0.00	0.00
TAEXCCCU260004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	22-Apr-27	03-May-27			$0.00	$0.00	0.00
Local Road 10		528	$3,200,505.79	21-Oct-25	10-Jun-27	21-Oct-25		$1,198,853.45	$1,847,053.84	1.54
Road Works		496	$1,303,481.16	21-Oct-25	23-May-27	21-Oct-25		$382,580.00	$382,580.00	1.00
TAEXRDCL100001	Road Excavation and Disposal	19	$269,834.00	21-Oct-25	11-Nov-25	21-Oct-25	11-Nov-25	$269,834.00	$269,834.00	1.00
TAEXRDCL100002	Backfilling Works for Road	10	$112,746.00	13-Nov-25	24-Nov-25	13-Nov-25	24-Nov-25	$112,746.00	$112,746.00	1.00
TAEXRDCL100003	Subgrade Works	4	$75,432.16	16-Jan-27	19-Jan-27			$0.00	$0.00	0.00
TAEXRDCL100004	ABC aggregate Base Course Works	4	$37,893.00	21-Jan-27	25-Jan-27			$0.00	$0.00	0.00
TAEXRDCL100005	MBC1 layer	1	$2,458.00	26-Jan-27	26-Jan-27			$0.00	$0.00	0.00
TAEXRDCL100006	BBC Base Course	2	$204,278.00	27-Jan-27	28-Jan-27			$0.00	$0.00	0.00
TAEXRDCL100008	Precast Concret Kerps	14	$252,724.00	30-Jan-27	14-Feb-27			$0.00	$0.00	0.00
TAEXRDCL100007	BWC Asphalt Wearing Course with RC	1	$111,511.00	03-May-27	03-May-27			$0.00	$0.00	0.00
TAEXRDCL100009	Precast Interlock Works	13	$178,055.00	04-May-27	18-May-27			$0.00	$0.00	0.00
TAEXRDCL100010	Stone Paving works	2	$21,000.00	19-May-27	20-May-27			$0.00	$0.00	0.00
TAEXRDCL100011	Road Marking	1	$4,100.00	22-May-27	22-May-27			$0.00	$0.00	0.00
TAEXRDCL100012	Traffic Sinage	1	$33,450.00	23-May-27	23-May-27			$0.00	$0.00	0.00
Electrical Works		132	$432,836.25	19-Oct-26	31-May-27	01-Sep-26		$23,506.25	$180,000.00	7.66
TAEXELCL100001	Trench Cut off	12	$23,506.25	19-Oct-26	01-Nov-26			$23,506.25	$0.00	0.00
TAEXELCL100002	Drawpit and PVC Pipes Installation	10	$4,560.00	02-Mar-27	13-Mar-27			$0.00	$0.00	0.00
TAEXELCL100003	Road Crossing Ducts	2	$260.00	14-Mar-27	15-Mar-27			$0.00	$0.00	0.00
TAEXELCL100006	Poles RC Foundation	3	$9,510.00	14-Mar-27	16-Mar-27			$0.00	$0.00	0.00
TAEXELCL100004	Trench Backfilling	10	$5,630.00	16-Mar-27	27-Mar-27			$0.00	$0.00	0.00

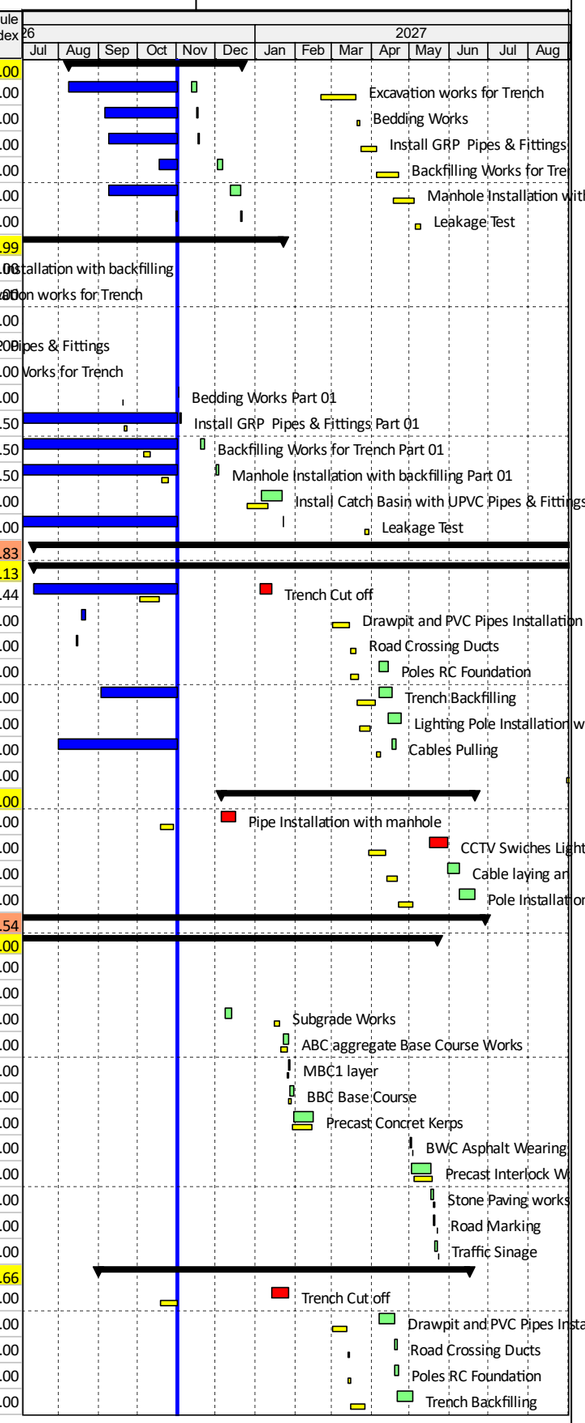


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXELCL100008	Lighting Pole Installation with Luminares	4	$91,050.00	17-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXELCL100005	Cables Pulling	2	$116,000.00	28-Mar-27	29-Mar-27			$0.00	$0.00	0.00
TAEXELCL100009	Install Substation & RMU	9	$180,000.00	22-Apr-27	02-May-27	01-Sep-26	02-Sep-26	$0.00	$180,000.00	0.00
TAEXELCL100007	Earthing cables	2	$2,320.00	30-May-27	31-May-27			$0.00	$0.00	0.00
Telecommunication Works		97	$122,780.00	22-Nov-26	20-Apr-27			$0.00	$0.00	0.00
TAEXTCCL100001	Trench Cut off	5	$7,500.00	22-Nov-26	26-Nov-26			$0.00	$0.00	0.00
TAEXTCCL100002	Drawpit and PVC Pipes Installation	4	$80,250.00	03-Apr-27	06-Apr-27			$0.00	$0.00	0.00
TAEXTCCL100003	Road Crossing Ducts	2	$8,600.00	07-Apr-27	08-Apr-27			$0.00	$0.00	0.00
TAEXTCCL100004	Trench Backfilling	10	$26,430.00	10-Apr-27	20-Apr-27			$0.00	$0.00	0.00
CCTV Works		166	$56,934.54	31-Oct-26	11-May-27			$5,963.39	$0.00	0.00
TAEXCCCL100001	Pipe Installation with manhole	8	$23,853.54	31-Oct-26	08-Nov-26			$5,963.39	$0.00	0.00
TAEXCCCL100002	CCTV Swiches Lighting panels Installation	10	$2,515.00	13-Apr-27	24-Apr-27			$0.00	$0.00	0.00
TAEXCCCL100003	Cable laying and connected with Panels	6	$24,655.00	25-Apr-27	01-May-27			$0.00	$0.00	0.00
TAEXCCCL100004	Pole Installation with IP Outdoor CCTV POE Camera	9	$5,911.00	02-May-27	11-May-27			$0.00	$0.00	0.00
Potable Networks		159	$236,062.54	26-Oct-26	30-May-27	01-Aug-26	01-Nov-26	$31,875.00	$236,062.54	7.41
TAEXPTCL100001	Excavation works for Trench	8	$42,500.00	26-Oct-26	03-Nov-26	01-Aug-26	16-Aug-26	$31,875.00	$42,500.00	1.33
TAEXPTCL100002	Bedding Works	2	$7,050.00	04-Nov-26	05-Nov-26	19-Aug-26	20-Aug-26	$0.00	$7,050.00	0.00
TAEXPTCL100003	Install Pipes & Fittings	8	$78,112.00	07-Nov-26	15-Nov-26	19-Aug-26	20-Sep-26	$0.00	$78,112.00	0.00
TAEXPTCL100004	Backfilling Works for Trench	12	$22,100.00	16-Nov-26	29-Nov-26	10-Oct-26	01-Nov-26	$0.00	$22,100.00	0.00
TAEXPTCL100006	Install fire hydrent	6	$24,000.00	03-May-27	09-May-27	04-Oct-26	25-Oct-26	$0.00	$24,000.00	0.00
TAEXPTCL100005	Install Valves with fittings	4	$25,285.92	05-May-27	09-May-27	17-Sep-26	25-Oct-26	$0.00	$25,285.92	0.00
TAEXPTCL100007	Valve Chamber works	14	$20,050.00	10-May-27	25-May-27	17-Sep-26	25-Oct-26	$0.00	$20,050.00	0.00
TAEXPTCL100008	Inspection Test	4	$16,964.62	26-May-27	30-May-27	22-Oct-26	25-Oct-26	$0.00	$16,964.62	0.00
TSE Networks		146	$208,473.34	30-Aug-26	03-Jun-27	15-Jul-26	18-Oct-26	$62,300.00	$208,473.34	3.35
TAEXTSCL100001	Excavation works for Trench	28	$62,300.00	30-Aug-26	30-Sep-26	15-Jul-26	18-Aug-26	$62,300.00	$62,300.00	1.00
TAEXTSCL100002	Bedding Works	2	$4,000.00	07-Nov-26	08-Nov-26	10-Aug-26	18-Aug-26	$0.00	$4,000.00	0.00
TAEXTSCL100003	Install Pipes & Fittings	8	$72,300.00	16-Nov-26	24-Nov-26	11-Aug-26	29-Aug-26	$0.00	$72,300.00	0.00
TAEXTSCL100004	Backfilling Works for Trench	12	$20,100.00	30-Nov-26	13-Dec-26	30-Aug-26	05-Sep-26	$0.00	$20,100.00	0.00
TAEXTSCL100005	Install Valves with fittings	4	$6,320.00	20-Feb-27	23-Feb-27	06-Sep-26	04-Oct-26	$0.00	$6,320.00	0.00
TAEXTSCL100006	Valve Chamber works	14	$35,200.00	24-Feb-27	11-Mar-27	29-Aug-26	04-Oct-26	$0.00	$35,200.00	0.00
TAEXTSCL100007	Inspection Test	4	$8,253.34	31-May-27	03-Jun-27	17-Oct-26	18-Oct-26	$0.00	$8,253.34	0.00
Sewerage Networks		445	$274,830.60	01-Dec-25	07-Jun-27	01-Dec-25	19-Sep-26	$229,620.84	$274,830.60	1.20
TAEXSWCL100001	Excavation works for Trench	6	$68,998.50	01-Dec-25	07-Dec-25	01-Dec-25	07-Dec-25	$68,998.50	$68,998.50	1.00
TAEXSWCL100002	Bedding Works	2	$22,311.84	27-Dec-25	28-Dec-25	27-Dec-25	28-Dec-25	$22,311.84	$22,311.84	1.00
TAEXSWCL100003	Install GRP Pipes & Fittings	5	$52,449.50	29-Dec-25	03-Jan-26	29-Dec-25	03-Jan-26	$52,449.50	$52,449.50	1.00
TAEXSWCL100004	Backfilling Works for Trench	8	$28,435.00	15-Jan-26	24-Jan-26	15-Jan-26	24-Jan-26	$28,435.00	$28,435.00	1.00
TAEXSWCL100005	Manhole Installation with backfilling	9	$57,426.00	09-Apr-26	19-Apr-26	09-Apr-26	19-Apr-26	$57,426.00	$57,426.00	1.00
TAEXSWCL1000011	Excavation works for Trench Part 01	3	$3,631.50	06-Dec-26	08-Dec-26	08-Sep-26	10-Sep-26	$0.00	$3,631.50	0.00
TAEXSWCL1000021	Bedding Works Part 01	2	$1,174.31	21-Jan-27	23-Jan-27	08-Sep-26	10-Sep-26	$0.00	$1,174.31	0.00
TAEXSWCL1000031	Install GRP Pipes & Fittings Part 01	5	$2,760.50	24-Jan-27	28-Jan-27	08-Sep-26	10-Sep-26	$0.00	$2,760.50	0.00
TAEXSWCL1000041	Backfilling Works for Trench Part 01	5	$1,815.00	10-Feb-27	15-Feb-27	08-Sep-26	10-Sep-26	$0.00	$1,815.00	0.00
TAEXSWCL1000051	Manhole Installation with backfilling Part 01	5	$10,134.00	16-Feb-27	21-Feb-27	10-Sep-26	13-Sep-26	$0.00	$10,134.00	0.00
TAEXSWCL100006	Leakage Test	3	$25,694.45	05-Jun-27	07-Jun-27	15-Jun-26	19-Sep-26	$0.00	$25,694.45	0.00
Storm Networks		169	$565,107.36	15-Aug-26	10-Jun-27	03-Aug-26	31-Oct-26	$463,007.97	$565,107.36	1.22
TAEXSTCL100001	Excavation works for Trench	13	$96,320.00	15-Aug-26	29-Aug-26	03-Aug-26	05-Aug-26	$96,320.00	$96,320.00	1.00
TAEXSTCL100002	Bedding Works	4	$28,900.00	30-Aug-26	02-Sep-26	16-Aug-26	19-Aug-26	$28,900.00	$28,900.00	1.00
TAEXSTCL100003	Install GRP Pipes & Fittings	7	$171,167.36	03-Sep-26	10-Sep-26	16-Aug-26	19-Aug-26	$171,167.36	$171,167.36	1.00
TAEXSTCL100004	Backfilling Works for Trench	14	$104,147.36	13-Sep-26	28-Sep-26	29-Aug-26	30-Aug-26	$104,147.36	$104,147.36	1.00
TAEXSTCL100005	Manhole Installation with backfilling	12	$68,152.64	20-Oct-26	02-Nov-26	22-Aug-26	06-Sep-26	$62,473.25	$68,152.64	1.09
TAEXSTCL100006	Install Catch Basin with UPVC Pipes & Fittings	9	$85,220.00	11-Jan-27	20-Jan-27	18-Oct-26	31-Oct-26	$0.00	$85,220.00	0.00
TAEXSTCL100007	Leakage Test	3	$11,200.00	08-Jun-27	10-Jun-27	03-Sep-26	06-Sep-26	$0.00	$11,200.00	0.00
AMANAH ROAD		424	$2,514,014.06	15-Mar-26	23-Aug-27	15-Mar-26		$2,347,694.06	$2,347,694.06	1.00
TAEXRDCA010001	Preperation Wprks for Existing layer	5	$100,000.00	15-Mar-26	19-Mar-26	15-Mar-26	19-Mar-26	$100,000.00	$100,000.00	1.00
TAEXRDCA020002	MBC1 LAYER	9	$2,458.00	21-Mar-26	30-Mar-26	21-Mar-26	30-Mar-26	$2,458.00	$2,458.00	1.00

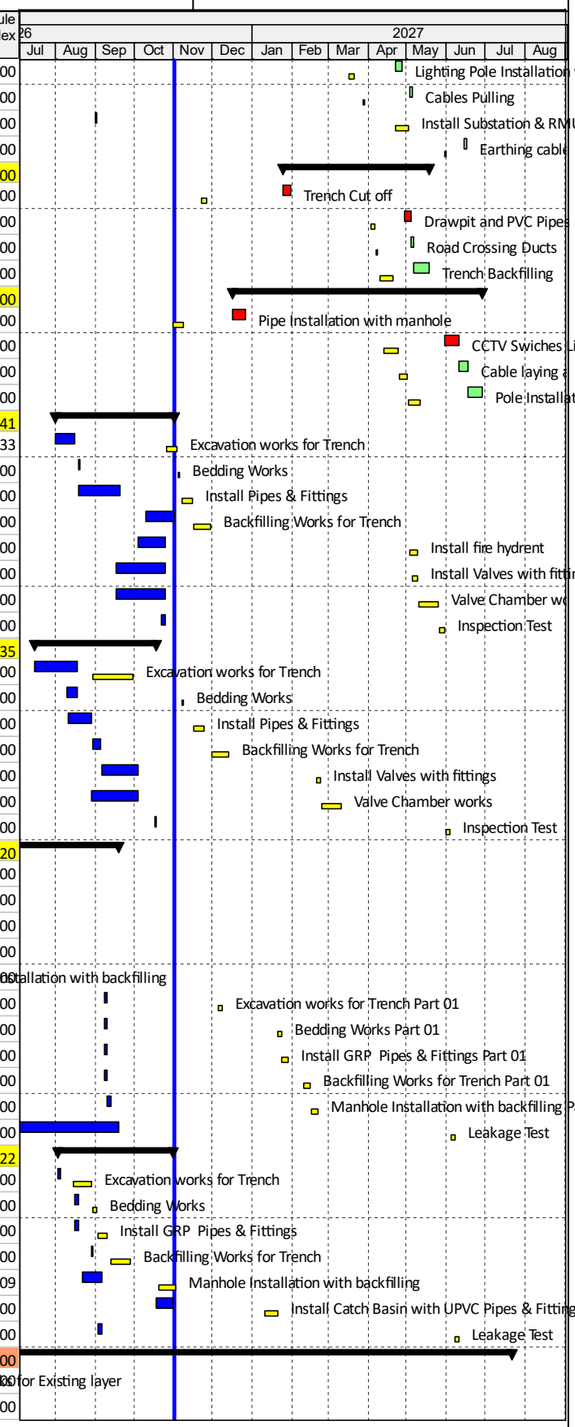


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXRDCA020003	BBC BASE COURSE	10	$1,639,606.40	24-Mar-26	04-Apr-26	24-Mar-26	04-Apr-26	$1,639,606.40	$1,639,606.40	1.00
TAEXRDCA030004	Precast Concret Kerps	22	$308,212.80	15-Apr-26	10-May-26	15-Apr-26	10-May-26	$308,212.80	$308,212.80	1.00
TAEXRDCA040005	Road Marking	18	$266,059.14	25-Apr-26	14-May-26	25-Apr-26	14-May-26	$266,059.14	$266,059.14	1.00
TAEXRDCA050006	Traffic Sinage	4	$31,357.72	21-May-26	25-May-26	21-May-26	25-May-26	$31,357.72	$31,357.72	1.00
TAEXRDCA050007	Backfilling Works for Road	25	$166,320.00	26-Jul-27	23-Aug-27			$0.00	$0.00	0.00
ZONE 2		603	$25,906,629.88	11-Oct-25	11-Aug-27	11-Oct-25		$9,858,647.82	$15,739,348.18	1.60
Collector Road 01		558	$5,451,723.31	21-Oct-25	12-Jul-27	21-Oct-25		$2,983,763.27	$3,098,832.56	1.04
Road Works		481	$1,922,967.04	21-Oct-25	13-Apr-27	21-Oct-25		$543,827.56	$543,827.56	1.00
TAEXRDCC010001	Road Excavation and Disposal	9	$256,598.97	21-Oct-25	30-Oct-25	21-Oct-25	31-Oct-25	$256,598.97	$256,598.97	1.00
TAEXRDCC010002	Backfilling Works for Road	9	$195,331.95	06-Nov-25	16-Nov-25	06-Nov-25	16-Nov-25	$195,331.95	$195,331.95	1.00
TAEXRDCC010003	Subgrade Works	10	$91,896.64	10-Feb-26	21-Feb-26	10-Feb-26	21-Feb-26	$91,896.64	$91,896.64	1.00
TAEXRDCC0100011	Road Excavation and Disposal Part 01	3	$2,591.91	17-Dec-26	20-Dec-26			$0.00	$0.00	0.00
TAEXRDCC0100021	Backfilling Works for Road Part 01	3	$1,973.05	21-Dec-26	23-Dec-26			$0.00	$0.00	0.00
TAEXRDCC0100031	Subgrade Works Part 01	13	$45,262.52	24-Dec-26	07-Jan-27			$0.00	$0.00	0.00
TAEXRDCC010004	ABC aggregate Base Course Works	18	$322,626.00	09-Jan-27	28-Jan-27			$0.00	$0.00	0.00
TAEXRDCC010005	MBC1 layer	2	$15,000.00	30-Jan-27	31-Jan-27			$0.00	$0.00	0.00
TAEXRDCC010006	BBC Base Course	4	$348,586.00	01-Feb-27	04-Feb-27			$0.00	$0.00	0.00
TAEXRDCC010008	Precast Concret Kerps	18	$187,181.00	15-Feb-27	07-Mar-27			$0.00	$0.00	0.00
TAEXRDCC010007	BWC Asphalt Wearing Course with RC	2	$311,511.00	08-Mar-27	09-Mar-27			$0.00	$0.00	0.00
TAEXRDCC010009	Precast Interlock Works	16	$57,408.00	10-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXRDCC010010	Stone Paving works	9	$35,000.00	29-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXRDCC010011	Road Marking	2	$6,500.00	08-Apr-27	10-Apr-27			$0.00	$0.00	0.00
TAEXRDCC010012	Traffic Sinage	3	$45,500.00	11-Apr-27	13-Apr-27			$0.00	$0.00	0.00
Electrical Works		122	$274,811.25	02-Nov-26	02-Jun-27	20-Sep-26		$0.00	$338.00	0.00
TAEXELCC010001	Trench Cut off	13	$69,026.25	02-Nov-26	16-Nov-26			$0.00	$0.00	0.00
TAEXELCC010002	Drawpit and PVC Pipes Installation	10	$10,250.00	02-Mar-27	13-Mar-27			$0.00	$0.00	0.00
TAEXELCC010003	Road Crossing Ducts	2	$2,600.00	14-Mar-27	15-Mar-27	20-Sep-26		$0.00	$338.00	0.00
TAEXELCC010006	Poles RC Foundation	3	$9,510.00	14-Mar-27	16-Mar-27			$0.00	$0.00	0.00
TAEXELCC010004	Trench Backfilling	15	$15,605.00	16-Mar-27	01-Apr-27			$0.00	$0.00	0.00
TAEXELCC010005	Cables Pulling	4	$124,000.00	03-Apr-27	06-Apr-27			$0.00	$0.00	0.00
TAEXELCC010008	Lighting Pole Installation with Luminares	10	$41,500.00	07-Apr-27	18-Apr-27			$0.00	$0.00	0.00
TAEXELCC010007	Earthing cables	2	$2,320.00	01-Jun-27	02-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		107	$134,911.00	28-Nov-26	08-May-27	20-Sep-26		$0.00	$1,720.00	0.00
TAEXTCCC010001	Trench Cut off	23	$23,581.00	28-Nov-26	23-Dec-26			$0.00	$0.00	0.00
TAEXTCCC010002	Drawpit and HDPE Pipes Installation	10	$70,230.00	07-Apr-27	18-Apr-27			$0.00	$0.00	0.00
TAEXTCCC010003	Road Crossing Ducts	2	$8,600.00	19-Apr-27	20-Apr-27	20-Sep-26		$0.00	$1,720.00	0.00
TAEXTCCC010004	Trench Backfilling	15	$32,500.00	21-Apr-27	08-May-27			$0.00	$0.00	0.00
CCTV Works		188	$60,237.00	09-Nov-26	15-Jun-27			$0.00	$0.00	0.00
TAEXCCCC010001	Pipe Installation with manhole	12	$24,088.00	09-Nov-26	22-Nov-26			$0.00	$0.00	0.00
TAEXCCCC010002	CCTV Swiches Lighting panels Installation	16	$3,647.00	25-Apr-27	12-May-27			$0.00	$0.00	0.00
TAEXCCCC010003	Cable laying and connected with Panels	12	$26,572.00	13-May-27	26-May-27			$0.00	$0.00	0.00
TAEXCCCC010004	Pole Installation with IP Outdoor CCTV POE Camera	17	$5,930.00	27-May-27	15-Jun-27			$0.00	$0.00	0.00
Potable Networks		278	$318,153.53	06-May-26	07-Jul-27	06-May-26		$197,340.49	$78,059.60	0.40
TAEXPTCC010001	Excavation works for Trench	9	$23,919.75	06-May-26	16-May-26	06-May-26	16-May-26	$23,919.75	$23,919.75	1.00
TAEXPTCC0100011	Excavation works for Trench Part 01	10	$29,235.25	26-Sep-26	06-Oct-26			$29,235.25	$0.00	0.00
TAEXPTCC010002	Bedding Works	2	$16,723.91	07-Oct-26	08-Oct-26	20-Jun-26		$16,723.91	$4,515.46	0.27
TAEXPTCC010003	Install Pipes & Fittings	14	$114,224.08	10-Oct-26	25-Oct-26	21-Jun-26		$114,224.08	$30,840.50	0.27
TAEXPTCC010004	Backfilling Works for Trench	16	$35,300.00	26-Oct-26	12-Nov-26	24-Jun-26		$13,237.50	$9,531.00	0.72
TAEXPTCC010006	Install fire hydrent	7	$20,100.00	11-Apr-27	18-Apr-27			$0.00	$0.00	0.00
TAEXPTCC010005	Install Valves with fittings	8	$29,185.92	17-Apr-27	25-Apr-27	26-Sep-26		$0.00	$4,377.89	0.00
TAEXPTCC010007	Valve Chamber works	20	$32,500.00	10-Jun-27	03-Jul-27	26-Sep-26		$0.00	$4,875.00	0.00
TAEXPTCC010008	Inspection Test	4	$16,964.62	04-Jul-27	07-Jul-27			$0.00	$0.00	0.00
TSE Networks		157	$249,302.09	09-Jul-26	12-Jul-27	06-Sep-26		$84,943.52	$101,291.26	1.19
TAEXTSCC010001	Excavation works for Trench	28	$39,693.34	09-Jul-26	10-Aug-26	06-Sep-26		$39,693.34	$35,724.01	0.90

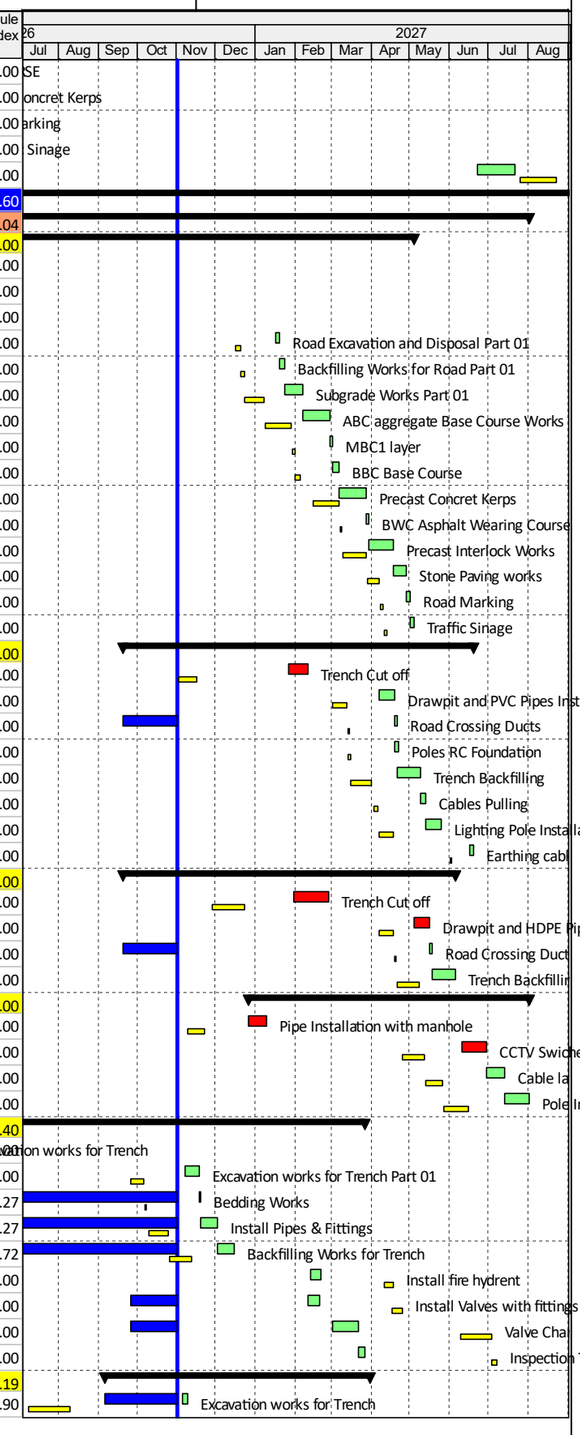


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTSCC010002	Bedding Works	2	$12,528.75	10-Oct-26	11-Oct-26	29-Oct-26		$12,528.75	$7,517.25	0.60
TAEXTSCC010003	Install Pipes & Fittings	14	$76,350.00	26-Oct-26	10-Nov-26	28-Oct-26		$32,721.43	$45,810.00	1.40
TAEXTSCC010004	Backfilling Works for Trench	16	$30,500.00	14-Nov-26	01-Dec-26			$0.00	$0.00	0.00
TAEXTSCC010005	Install Valves with fittings	8	$13,200.00	23-Nov-26	01-Dec-26	26-Sep-26		$0.00	$1,980.00	0.00
TAEXTSCC010006	Valve Chamber works	13	$68,400.00	02-Dec-26	16-Dec-26	26-Sep-26		$0.00	$10,260.00	0.00
TAEXTSCC010007	Inspection Test	4	$8,630.00	08-Jul-27	12-Jul-27			$0.00	$0.00	0.00
Sewerage Networks		210	$301,010.60	07-Apr-26	04-Feb-27	07-Apr-26		$110,724.00	$282,684.62	2.55
TAEXSWCC010001	Excavation works for Trench	7	$41,010.00	07-Apr-26	14-Apr-26	07-Apr-26	14-Apr-26	$41,010.00	$41,010.00	1.00
TAEXSWCC010002	Bedding Works	1	$4,110.00	06-May-26	06-May-26	06-May-26	06-May-26	$4,110.00	$4,110.00	1.00
TAEXSWCC010003	Install GRP Pipes & Fittings	4	$54,285.00	07-May-26	11-May-26	07-May-26	11-May-26	$54,285.00	$54,285.00	1.00
TAEXSWCC010004	Backfilling Works for Trench	8	$11,319.00	12-May-26	20-May-26	12-May-26	20-May-26	$11,319.00	$11,319.00	1.00
TAEXSWCC0100011	Excavation works for Trench Part 01	5	$27,340.00	09-Dec-26	14-Dec-26	06-Sep-26	28-Oct-26	$0.00	$27,340.00	0.00
TAEXSWCC0100021	Bedding Works Part 01	2	$2,740.00	15-Dec-26	16-Dec-26	26-Sep-26	01-Nov-26	$0.00	$2,740.00	0.00
TAEXSWCC0100031	Install GRP Pipes & Fittings Part 01	5	$44,415.00	17-Dec-26	22-Dec-26	01-Oct-26		$0.00	$42,194.25	0.00
TAEXSWCC0100041	Backfilling Works for Trench Part 01	8	$9,261.00	10-Jan-27	18-Jan-27	22-Oct-26		$0.00	$5,093.55	0.00
TAEXSWCC010005	Manhole Installation with backfilling	14	$80,836.15	14-Jan-27	30-Jan-27	26-Sep-26		$0.00	$72,752.54	0.00
TAEXSWCC010006	Leakage Test	5	$25,694.45	31-Jan-27	04-Feb-27	01-Oct-26		$0.00	$21,840.28	0.00
Storm Networks		314	$2,190,330.80	31-Dec-25	08-Feb-27	31-Dec-25		$2,046,927.70	$2,090,911.53	1.02
TAEXSTCC010001	Excavation works for Trench & Box Culvert	15	$223,373.70	31-Dec-25	17-Jan-26	31-Dec-25	17-Jan-26	$223,373.70	$223,373.70	1.00
TAEXSTCC010002	Bedding Works	2	$83,105.83	10-Feb-26	11-Feb-26	10-Feb-26	11-Feb-26	$83,105.83	$83,105.83	1.00
TAEXSTCC010003	Install GRP Pipes & Fittings	5	$252,054.00	28-Mar-26	01-Apr-26	28-Mar-26	01-Apr-26	$252,054.00	$252,054.00	1.00
TAEXSTCC010004	Backfilling Works for Trench & Box Culvert	14	$145,935.00	01-Apr-26	16-Apr-26	01-Apr-26	16-Apr-26	$145,935.00	$145,935.00	1.00
TAEXSTCC010008	Install Box Culvert Part 1	2	$303,207.76	15-Apr-26	16-Apr-26	15-Apr-26	16-Apr-26	$303,207.76	$303,207.76	1.00
TAEXSTCC010009	Install Box Culvert Part 2	14	$838,809.87	15-Apr-26	30-Apr-26	15-Apr-26	30-Apr-26	$838,809.87	$838,809.87	1.00
TAEXSTCC010005	Manhole Installation with backfilling	5	$76,657.50	21-Apr-26	26-Apr-26	21-Apr-26	26-Apr-26	$76,657.50	$76,657.50	1.00
TAEXSTCC0100011	Excavation works for Trench & Box Culvert Part 01	5	$2,256.30	03-Jun-26	08-Jun-26	10-Aug-26	16-Aug-26	$2,256.30	$2,256.30	1.00
TAEXSTCC0100021	Bedding Works Part 01	1	$839.45	09-Jun-26	09-Jun-26	20-Aug-26	22-Aug-26	$839.45	$839.45	1.00
TAEXSTCC0100031	Install GRP Pipes & Fittings Part 01	3	$13,266.00	10-Jun-26	13-Jun-26	29-Aug-26	30-Aug-26	$13,266.00	$13,266.00	1.00
TAEXSTCC0100041	Backfilling Works for Trench & Box Culvert Part 01	8	$9,315.00	01-Jul-26	09-Jul-26			$9,315.00	$0.00	0.00
TAEXSTCC0100051	Manhole Installation with backfilling Part 01	10	$93,692.50	20-Oct-26	31-Oct-26	16-Jun-26		$93,692.50	$79,638.63	0.85
TAEXSTCC0100091	Install Box Culvert Part 2 Part 01	10	$44,147.89	01-Nov-26	11-Nov-26	10-Oct-26		$4,414.79	$41,940.50	9.50
TAEXSTCC010006	Install Catch Basin with UPVC Pipes & Fittings	12	$85,220.00	12-Nov-26	25-Nov-26	17-Oct-26		$0.00	$29,827.00	0.00
TAEXSTCC010007	Leakage Test	3	$18,450.00	06-Feb-27	08-Feb-27			$0.00	$0.00	0.00
Upgrade Local 28		442	$3,039,340.64	14-Mar-26	24-Jun-27	14-Mar-26		$781,402.64	$929,928.24	1.19
Road Works		51	$948,680.00	08-Mar-27	05-May-27			$0.00	$0.00	0.00
TAEXRDCU280002	Precast Concret Kerps	15	$278,805.00	08-Mar-27	24-Mar-27			$0.00	$0.00	0.00
TAEXRDCU280001	BWC Asphalt Wearing Course with RC	1	$311,511.00	12-Apr-27	12-Apr-27			$0.00	$0.00	0.00
TAEXRDCU280003	Precast Interlock Works	13	$274,144.00	13-Apr-27	27-Apr-27			$0.00	$0.00	0.00
TAEXRDCU280004	Stone Paving works	4	$38,120.00	28-Apr-27	02-May-27			$0.00	$0.00	0.00
TAEXRDCU280005	Road Marking	1	$4,100.00	03-May-27	03-May-27			$0.00	$0.00	0.00
TAEXRDCU280006	Traffic Sinage	2	$42,000.00	04-May-27	05-May-27			$0.00	$0.00	0.00
Electrical Works		113	$607,403.00	17-Nov-26	07-Jun-27	28-Oct-26		$0.00	$140,502.60	0.00
TAEXELCU280001	Trench Cut off	10	$10,530.00	17-Nov-26	28-Nov-26	28-Oct-26		$0.00	$4,422.60	0.00
TAEXELCU280002	Drawpit and PVC Pipes Installation	11	$5,670.00	02-Mar-27	14-Mar-27			$0.00	$0.00	0.00
TAEXELCU280003	Road Crossing Ducts	4	$450.00	15-Mar-27	18-Mar-27			$0.00	$0.00	0.00
TAEXELCU280004	Trench Backfilling	17	$12,020.00	20-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXELCU280005	Cables Pulling	4	$324,000.00	08-Apr-27	12-Apr-27	29-Oct-26		$0.00	$136,080.00	0.00
TAEXELCU280006	Poles RC Foundation	6	$118,210.00	10-Apr-27	15-Apr-27			$0.00	$0.00	0.00
TAEXELCU280008	Lighting Pole Installation with Luminares	8	$82,000.00	17-Apr-27	25-Apr-27			$0.00	$0.00	0.00
TAEXELCU280007	Earthing cables	4	$54,523.00	03-Jun-27	07-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		92	$109,215.00	24-Dec-26	17-May-27			$0.00	$0.00	0.00
TAEXTCCU280001	Trench Cut off	10	$15,230.00	24-Dec-26	04-Jan-27			$0.00	$0.00	0.00
TAEXTCCU280002	Drawpit and PVC Pipes Installation	8	$50,235.00	19-Apr-27	27-Apr-27			$0.00	$0.00	0.00
TAEXTCCU280003	Road Crossing Ducts	4	$12,500.00	28-Apr-27	02-May-27			$0.00	$0.00	0.00

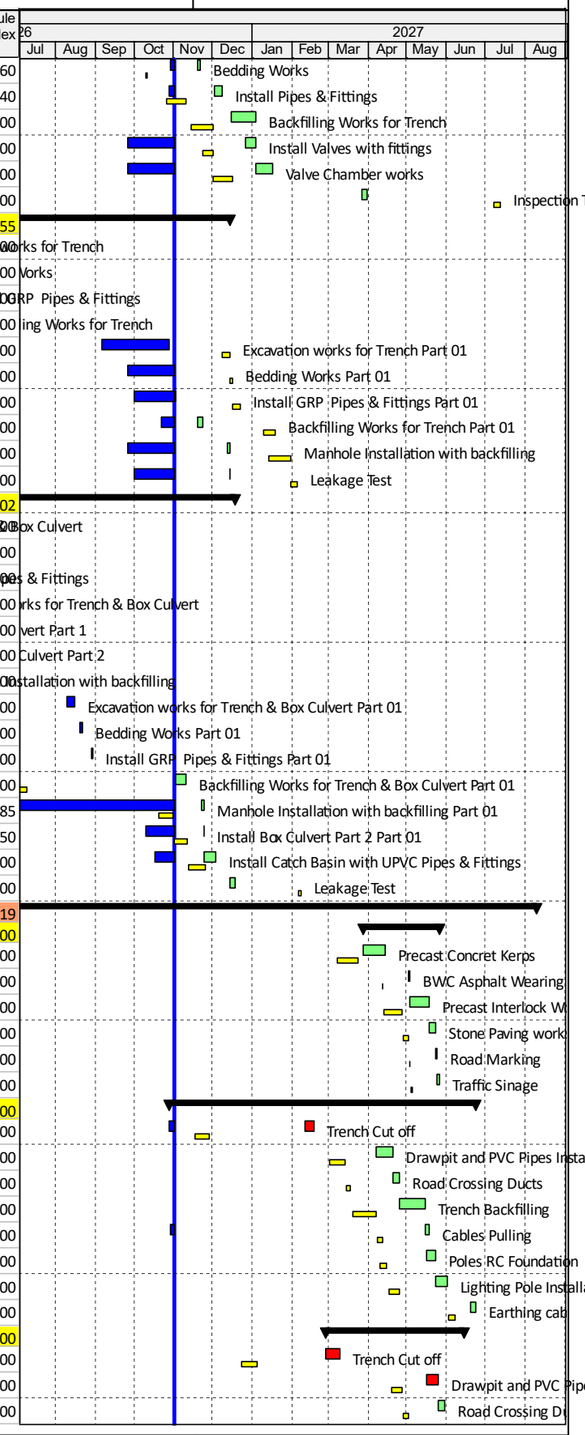


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTCCU280004	Trench Backfilling	13	$31,250.00	03-May-27	17-May-27			$0.00	$0.00	0.00
CCTV Works		183	$58,123.00	23-Nov-26	23-Jun-27			$0.00	$0.00	0.00
TAEXCCCU280001	Pipe Installation with manhole	12	$25,094.00	23-Nov-26	06-Dec-26			$0.00	$0.00	0.00
TAEXCCCU280002	CCTV Swiches Lighting panels Installation	14	$3,276.00	13-May-27	29-May-27			$0.00	$0.00	0.00
TAEXCCCU280003	Cable laying and connected with Panels	10	$25,974.00	30-May-27	09-Jun-27			$0.00	$0.00	0.00
TAEXCCCU280004	Pole Installation with IP Outdoor CCTV POE Camera	12	$3,779.00	10-Jun-27	23-Jun-27			$0.00	$0.00	0.00
Potable Networks		160	$231,617.00	04-Nov-26	16-Jun-27	23-Aug-26		$0.00	$199,117.00	0.00
TAEXPTCU280001	Excavation works for Trench	27	$52,100.00	04-Nov-26	05-Dec-26	23-Aug-26	28-Oct-26	$0.00	$52,100.00	0.00
TAEXPTCU280002	Bedding Works	2	$7,050.00	06-Dec-26	07-Dec-26	06-Sep-26	28-Oct-26	$0.00	$7,050.00	0.00
TAEXPTCU280003	Install Pipes & Fittings	8	$78,112.00	08-Dec-26	16-Dec-26	06-Sep-26	29-Oct-26	$0.00	$78,112.00	0.00
TAEXPTCU280004	Backfilling Works for Trench	14	$24,250.00	17-Dec-26	02-Jan-27	28-Oct-26	30-Oct-26	$0.00	$24,250.00	0.00
TAEXPTCU280005	Install Valves with fittings	4	$9,600.00	29-Dec-26	02-Jan-27	28-Oct-26	29-Oct-26	$0.00	$9,600.00	0.00
TAEXPTCU280006	Install fire hydrent	6	$24,000.00	03-Jan-27	09-Jan-27	28-Oct-26	29-Oct-26	$0.00	$24,000.00	0.00
TAEXPTCU280007	Valve Chamber works	15	$32,500.00	26-May-27	12-Jun-27			$0.00	$0.00	0.00
TAEXPTCU280008	Inspection Test	4	$4,005.00	13-Jun-27	16-Jun-27	28-Oct-26	29-Oct-26	$0.00	$4,005.00	0.00
TSE Networks		111	$214,990.00	01-Oct-26	21-Jun-27	10-Oct-26		$65,200.00	$6,741.00	0.10
TAEXTSCU280001	Excavation works for Trench	22	$65,200.00	01-Oct-26	26-Oct-26			$65,200.00	$0.00	0.00
TAEXTSCU280002	Bedding Works	2	$4,200.00	08-Dec-26	09-Dec-26			$0.00	$0.00	0.00
TAEXTSCU280003	Install Pipes & Fittings	8	$72,300.00	10-Dec-26	19-Dec-26			$0.00	$0.00	0.00
TAEXTSCU280004	Backfilling Works for Trench	14	$24,500.00	20-Dec-26	04-Jan-27			$0.00	$0.00	0.00
TAEXTSCU280005	Install Valves with fittings	4	$6,320.00	31-Dec-26	04-Jan-27	10-Oct-26		$0.00	$948.00	0.00
TAEXTSCU280006	Valve Chamber works	15	$38,620.00	05-Jan-27	21-Jan-27	10-Oct-26		$0.00	$5,793.00	0.00
TAEXTSCU280007	Inspection Test	4	$3,850.00	17-Jun-27	21-Jun-27			$0.00	$0.00	0.00
Storm Networks		354	$869,312.64	14-Mar-26	24-Jun-27	14-Mar-26		$716,202.64	$583,567.64	0.81
TAEXSTCU2100061	Excavation works for Trench	7	$90,255.41	14-Mar-26	21-Mar-26	14-Mar-26	21-Mar-26	$90,255.41	$90,255.41	1.00
TAEXSTCU2100071	Bedding Works	2	$82,266.37	09-Apr-26	11-Apr-26	09-Apr-26	11-Apr-26	$82,266.37	$82,266.37	1.00
TAEXSTCU2100081	Install GRP Pipes & Fittings	7	$188,698.50	11-Apr-26	18-Apr-26	11-Apr-26	18-Apr-26	$188,698.50	$188,698.50	1.00
TAEXSTCU2100091	Backfilling Works for Trench	10	$76,755.00	16-Apr-26	27-Apr-26	16-Apr-26	27-Apr-26	$76,755.00	$76,755.00	1.00
TAEXSTCU2100101	Manhole Installation with backfilling	10	$97,758.00	19-Apr-26	29-Apr-26	19-Apr-26	29-Apr-26	$97,758.00	$97,758.00	1.00
TAEXSTCU21000611	Excavation works for Trench Part 01	5	$1,841.95	09-Aug-26	13-Aug-26	05-Sep-26	06-Sep-26	$1,841.95	$1,841.95	1.00
TAEXSTCU21000711	Bedding Works Part 01	1	$1,678.91	15-Aug-26	15-Aug-26	10-Sep-26	13-Sep-26	$1,678.91	$1,678.91	1.00
TAEXSTCU21000811	Install GRP Pipes & Fittings Part 01	5	$9,931.50	16-Aug-26	20-Aug-26	10-Sep-26	13-Sep-26	$9,931.50	$9,931.50	1.00
TAEXSTCU21000911	Backfilling Works for Trench Part 01	7	$13,545.00	31-Aug-26	07-Sep-26	08-Oct-26	10-Oct-26	$13,545.00	$13,545.00	1.00
TAEXSTCU21001011	Manhole Installation with backfilling Part 01	5	$10,862.00	20-Oct-26	25-Oct-26	22-Oct-26	25-Oct-26	$10,862.00	$10,862.00	1.00
TAEXSTCU280006	Install Catch Basin with UPVC Pipes & Fittings	12	$285,220.00	26-Oct-26	08-Nov-26			$142,610.00	$0.00	0.00
TAEXSTCU280007	Leakage Test	3	$10,500.00	22-Jun-27	24-Jun-27	01-Aug-26		$0.00	$9,975.00	0.00
Local Road 02		517	$3,265,585.57	04-Jan-26	25-Jul-27	04-Jan-26		$1,707,359.92	$2,498,322.12	1.46
Road Works		459	$1,444,764.16	04-Jan-26	25-Jul-27	04-Jan-26		$449,774.16	$936,379.66	2.08
TAEXRDC L020001	Road Excavation and Disposal	52	$116,390.00	04-Jan-26	04-Mar-26	04-Jan-26	05-Mar-26	$116,390.00	$116,390.00	1.00
TAEXRDC L020002	Backfilling Works for Road	40	$197,305.00	18-Jan-26	04-Mar-26	18-Jan-26	04-Mar-26	$197,305.00	$197,305.00	1.00
TAEXRDC L020003	Subgrade Works	54	$136,079.16	08-Feb-26	11-Apr-26	08-Feb-26	11-Apr-26	$136,079.16	$136,079.16	1.00
TAEXRDC L020004	ABC aggregate Base Course Works	8	$35,786.00	30-Nov-26	08-Dec-26	21-Jun-26	09-Aug-26	$0.00	$35,786.00	0.00
TAEXRDC L020005	MBC1 layer	1	$5,000.00	09-Dec-26	09-Dec-26	05-Jul-26	09-Aug-26	$0.00	$5,000.00	0.00
TAEXRDC L020006	BBC Base Course	3	$406,417.00	10-Dec-26	13-Dec-26	08-Jul-26	16-Aug-26	$0.00	$406,417.00	0.00
TAEXRDC L020008	Precast Concret Kerps	9	$78,805.00	25-Mar-27	04-Apr-27	26-Sep-26		$0.00	$39,402.50	0.00
TAEXRDC L020007	BWC Asphalt Wearing Course with RC	1	$111,511.00	12-May-27	12-May-27			$0.00	$0.00	0.00
TAEXRDC L020009	Precast Interlock Works	9	$175,671.00	13-May-27	23-May-27			$0.00	$0.00	0.00
TAEXRDC L020010	Stone Paving works	4	$135,000.00	24-May-27	27-May-27			$0.00	$0.00	0.00
TAEXRDC L020011	Road Marking	3	$4,800.00	20-Jul-27	22-Jul-27			$0.00	$0.00	0.00
TAEXRDC L020012	Traffic Sinage	2	$42,000.00	24-Jul-27	25-Jul-27			$0.00	$0.00	0.00
Electrical Works		184	$361,210.25	29-Nov-26	09-Jun-27	11-Jun-26		$0.00	$186,260.30	0.00
TAEXELCL020001	Trench Cut off	9	$26,450.25	29-Nov-26	08-Dec-26	11-Jun-26		$0.00	$10,580.10	0.00
TAEXELCL020002	Drawpit and PVC Pipes Installation	8	$3,587.00	02-Mar-27	10-Mar-27	13-Jun-26	21-Jun-26	$0.00	$3,587.00	0.00
TAEXELCL020003	Road Crossing Ducts	2	$260.00	11-Mar-27	13-Mar-27	13-Jun-26	21-Jun-26	$0.00	$260.00	0.00

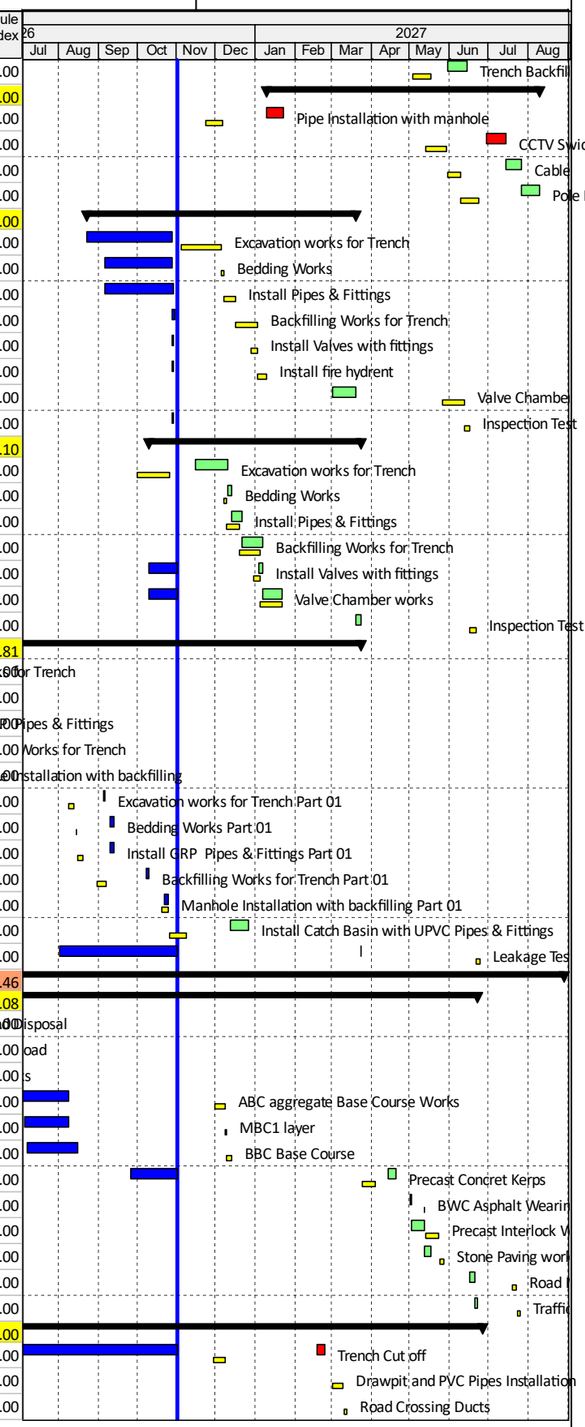


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXELCL020006	Poles RC Foundation	3	$59,510.00	11-Mar-27	14-Mar-27			$0.00	$0.00	0.00
TAEXELCL020004	Trench Backfilling	9	$9,583.00	14-Mar-27	23-Mar-27	16-Jun-26		$0.00	$3,833.20	0.00
TAEXELCL020008	Lighting Pole Installation with Luminares	4	$91,500.00	15-Mar-27	18-Mar-27			$0.00	$0.00	0.00
TAEXELCL020005	Cables Pulling	3	$168,000.00	24-Mar-27	27-Mar-27	20-Sep-26	26-Oct-26	$0.00	$168,000.00	0.00
TAEXELCL020007	Earthing cables	2	$2,320.00	08-Jun-27	09-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		114	$103,355.00	05-Jan-27	13-May-27	11-Jun-26		$0.00	$69,990.00	0.00
TAEXTCCL020001	Trench Cut off	6	$9,500.00	05-Jan-27	11-Jan-27	11-Jun-26		$0.00	$1,140.00	0.00
TAEXTCCL020002	Drawpit and PVC Pipes Installation	3	$60,250.00	28-Apr-27	01-May-27	13-Jun-26	23-Jun-26	$0.00	$60,250.00	0.00
TAEXTCCL020003	Road Crossing Ducts	2	$8,600.00	02-May-27	03-May-27	13-Jun-26	23-Jun-26	$0.00	$8,600.00	0.00
TAEXTCCL020004	Trench Backfilling	9	$25,005.00	04-May-27	13-May-27			$0.00	$0.00	0.00
CCTV Works		187	$50,564.00	07-Dec-26	12-Jul-27			$0.00	$0.00	0.00
TAEXCCCL020001	Pipe Installation with manhole	10	$25,094.00	07-Dec-26	17-Dec-26			$0.00	$0.00	0.00
TAEXCCCL020002	CCTV Swiches Lighting panels Installation	13	$2,578.00	30-May-27	13-Jun-27			$0.00	$0.00	0.00
TAEXCCCL020003	Cable laying and connected with Panels	10	$18,176.00	14-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TAEXCCCL020004	Pole Installation with IP Outdoor CCTV POE Camera	15	$4,716.00	26-Jun-27	12-Jul-27			$0.00	$0.00	0.00
Potable Networks		275	$258,012.54	12-May-26	04-Apr-27	12-May-26	25-Jun-26	$234,445.04	$258,012.54	1.10
TAEXPTCL020001	Excavation works for Trench	4	$65,059.62	12-May-26	16-May-26	12-May-26	16-May-26	$65,059.62	$65,059.62	1.00
TAEXPTCL020002	Bedding Works	3	$22,735.92	17-May-26	19-May-26	17-May-26	19-May-26	$22,735.92	$22,735.92	1.00
TAEXPTCL020003	Install Pipes & Fittings	2	$78,112.00	19-May-26	20-May-26	19-May-26	20-May-26	$78,112.00	$78,112.00	1.00
TAEXPTCL020004	Backfilling Works for Trench	4	$24,250.00	20-May-26	24-May-26	20-May-26	24-May-26	$24,250.00	$24,250.00	1.00
TAEXPTCL020005	Install Valves with fittings	3	$9,120.00	23-May-26	25-May-26	23-May-26	25-May-26	$9,120.00	$9,120.00	1.00
TAEXPTCL020007	Valve Chamber works	10	$22,687.50	23-May-26	02-Jun-26	23-May-26	02-Jun-26	$22,687.50	$22,687.50	1.00
TAEXPTCL020006	Install fire hydrent	3	$12,000.00	31-May-26	02-Jun-26	31-May-26	02-Jun-26	$12,000.00	$12,000.00	1.00
TAEXPTCL0200051	Install Valves with fittings Part 01	1	$480.00	08-Oct-26	08-Oct-26	06-Jun-26	09-Jun-26	$480.00	$480.00	1.00
TAEXPTCL0200061	Install fire hydrent Part 01	3	$12,000.00	22-Nov-26	24-Nov-26	06-Jun-26	09-Jun-26	$0.00	$12,000.00	0.00
TAEXPTCL0200071	Valve Chamber works Part 01	4	$7,562.50	25-Nov-26	29-Nov-26	06-Jun-26	20-Jun-26	$0.00	$7,562.50	0.00
TAEXPTCL020008	Inspection Test	4	$4,005.00	31-Mar-27	04-Apr-27	25-Jun-26	25-Jun-26	$0.00	$4,005.00	0.00
TSE Networks		302	$185,389.34	12-Apr-26	08-Apr-27	12-Apr-26	28-Jun-26	$171,350.44	$185,389.34	1.08
TAEXTSCL020001	Excavation works for Trench	30	$34,019.34	12-Apr-26	16-May-26	12-Apr-26	16-May-26	$34,019.34	$34,019.34	1.00
TAEXTSCL020002	Bedding Works	25	$4,150.00	05-May-26	02-Jun-26	05-May-26	02-Jun-26	$4,150.00	$4,150.00	1.00
TAEXTSCL020003	Install Pipes & Fittings	24	$72,300.00	06-May-26	02-Jun-26	06-May-26	02-Jun-26	$72,300.00	$72,300.00	1.00
TAEXTSCL020005	Install Valves with fittings	3	$6,193.60	10-May-26	12-May-26	10-May-26	12-May-26	$6,193.60	$6,193.60	1.00
TAEXTSCL020004	Backfilling Works for Trench	16	$24,500.00	16-May-26	02-Jun-26	16-May-26	02-Jun-26	$24,500.00	$24,500.00	1.00
TAEXTSCL020006	Valve Chamber works	10	$30,187.50	17-May-26	27-May-26	17-May-26	27-May-26	$30,187.50	$30,187.50	1.00
TAEXTSCL0200051	Install Valves with fittings Part 01	2	$126.40	15-Mar-27	16-Mar-27	06-Jun-26	09-Jun-26	$0.00	$126.40	0.00
TAEXTSCL0200061	Valve Chamber works Part 01	8	$10,062.50	17-Mar-27	25-Mar-27	04-Jun-26	20-Jun-26	$0.00	$10,062.50	0.00
TAEXTSCL020007	Inspection Test	4	$3,850.00	05-Apr-27	08-Apr-27	25-Jun-26	28-Jun-26	$0.00	$3,850.00	0.00
Storm Networks		348	$862,290.28	21-Feb-26	12-Apr-27	21-Feb-26	25-Oct-26	$851,790.28	$862,290.28	1.01
TAEXSTCL020001	Excavation works for Trench	88	$188,620.00	21-Feb-26	02-Jun-26	21-Feb-26	02-Jun-26	$188,620.00	$188,620.00	1.00
TAEXSTCL020002	Bedding Works	71	$83,945.28	12-Mar-26	02-Jun-26	12-Mar-26	02-Jun-26	$83,945.28	$83,945.28	1.00
TAEXSTCL020003	Install GRP Pipes & Fittings	70	$98,630.00	14-Mar-26	02-Jun-26	14-Mar-26	02-Jun-26	$98,630.00	$98,630.00	1.00
TAEXSTCL020004	Backfilling Works for Trench	60	$90,245.00	25-Mar-26	02-Jun-26	25-Mar-26	02-Jun-26	$90,245.00	$90,245.00	1.00
TAEXSTCL020005	Manhole Installation with backfilling	51	$101,230.00	05-Apr-26	02-Jun-26	05-Apr-26	02-Jun-26	$101,230.00	$101,230.00	1.00
TAEXSTCL020006	Install Catch Basin with UPVC Pipes & Fittings	6	$216,840.00	24-May-26	30-May-26	24-May-26	30-May-26	$216,840.00	$216,840.00	1.00
TAEXSTCL0200061	Install Catch Basin with UPVC Pipes & Fittings Part 01	4	$72,280.00	24-Aug-26	27-Aug-26	06-Jun-26	11-Jun-26	$72,280.00	$72,280.00	1.00
TAEXSTCL020007	Leakage Test	3	$10,500.00	10-Apr-27	12-Apr-27	23-Jun-26	25-Oct-26	$0.00	$10,500.00	0.00
Local Road 03		601	$4,139,196.17	12-Oct-25	26-Jul-27	12-Oct-25		$1,418,543.76	$3,028,377.41	2.13
Road Works		494	$2,371,280.16	12-Oct-25	02-May-27	12-Oct-25		$370,625.00	$1,646,361.86	4.44
TAEXRDCL030001	Road Excavation and Disposal	56	$293,112.00	12-Oct-25	15-Dec-25	12-Oct-25	15-Dec-25	$293,112.00	$293,112.00	1.00
TAEXRDCL030002	Backfilling Works for Road	9	$77,513.00	15-Apr-26	25-Apr-26	15-Apr-26	25-Apr-26	$77,513.00	$77,513.00	1.00
TAEXRDCL0300021	Backfilling Works for Road Part 01	9	$77,513.00	23-Dec-26	02-Jan-27	02-Aug-26		$0.00	$62,010.40	0.00
TAEXRDCL030003	Subgrade Works	8	$95,648.16	03-Jan-27	11-Jan-27	02-Aug-26	08-Aug-26	$0.00	$95,648.16	0.00
TAEXRDCL030004	ABC aggregate Base Course Works	15	$266,839.00	12-Jan-27	28-Jan-27	08-Aug-26	23-Aug-26	$0.00	$266,839.00	0.00
TAEXRDCL030005	MBC1 layer	2	$5,000.00	30-Jan-27	31-Jan-27	26-Aug-26	27-Aug-26	$0.00	$5,000.00	0.00

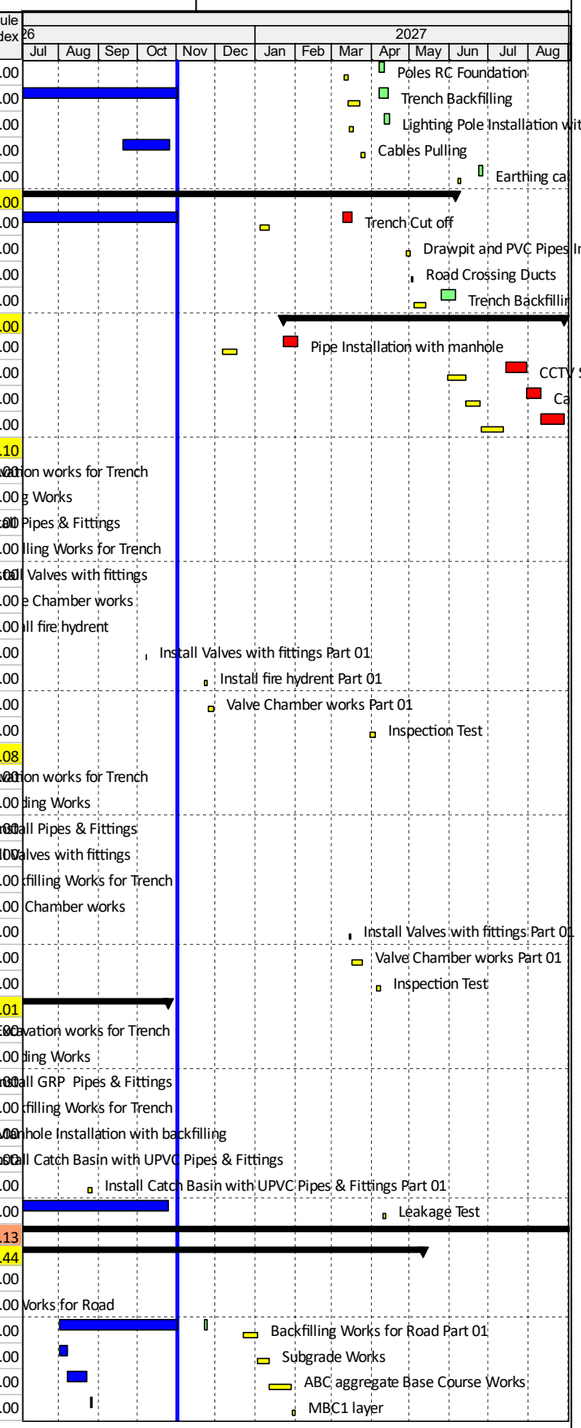


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXRDCL030006	BBC Base Course	2	$604,278.00	01-Feb-27	02-Feb-27	28-Aug-26	29-Aug-26	$0.00	$604,278.00	0.00
TAEXRDCL030008	Precast Concret Kerps	9	$345,659.00	05-Apr-27	14-Apr-27	10-Oct-26		$0.00	$241,961.30	0.00
TAEXRDCL030007	BWC Asphalt Wearing Course with RC	1	$311,511.00	15-Apr-27	15-Apr-27			$0.00	$0.00	0.00
TAEXRDCL030009	Precast Interlock Works	8	$212,407.00	17-Apr-27	25-Apr-27			$0.00	$0.00	0.00
TAEXRDCL030010	Stone Paving works	3	$35,000.00	26-Apr-27	28-Apr-27			$0.00	$0.00	0.00
TAEXRDCL030011	Road Marking	1	$4,800.00	29-Apr-27	29-Apr-27			$0.00	$0.00	0.00
TAEXRDCL030012	Traffic Sinage	2	$42,000.00	01-May-27	02-May-27			$0.00	$0.00	0.00
Electrical Works		142	$353,466.25	09-Dec-26	12-Jun-27	08-Aug-26		$0.00	$64,646.29	0.00
TAEXELCL030001	Trench Cut off	11	$26,786.25	09-Dec-26	21-Dec-26	06-Sep-26		$0.00	$13,660.99	0.00
TAEXELCL030002	Drawpit and PVC Pipes Installation	8	$4,560.00	02-Mar-27	10-Mar-27	08-Aug-26		$0.00	$3,420.00	0.00
TAEXELCL030003	Road Crossing Ducts	2	$260.00	11-Mar-27	13-Mar-27	08-Aug-26		$0.00	$195.00	0.00
TAEXELCL030006	Poles RC Foundation	3	$49,510.00	11-Mar-27	14-Mar-27			$0.00	$0.00	0.00
TAEXELCL030004	Trench Backfilling	10	$10,530.00	14-Mar-27	24-Mar-27	10-Oct-26		$0.00	$5,370.30	0.00
TAEXELCL030008	Lighting Pole Installation with Luminares	5	$91,500.00	15-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCL030005	Cables Pulling	3	$168,000.00	25-Mar-27	28-Mar-27	20-Sep-26		$0.00	$42,000.00	0.00
TAEXELCL030007	Earthing cables	2	$2,320.00	10-Jun-27	12-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		72	$125,530.00	12-Jan-27	19-May-27	08-Aug-26		$0.00	$59,529.50	0.00
TAEXTCCL030001	Trench Cut off	7	$10,250.00	12-Jan-27	19-Jan-27			$0.00	$0.00	0.00
TAEXTCCL030002	Drawpit and PVC Pipes Installation	4	$80,250.00	02-May-27	05-May-27	08-Aug-26		$0.00	$53,767.50	0.00
TAEXTCCL030003	Road Crossing Ducts	2	$8,600.00	06-May-27	08-May-27	08-Aug-26		$0.00	$5,762.00	0.00
TAEXTCCL030004	Trench Backfilling	10	$26,430.00	09-May-27	19-May-27			$0.00	$0.00	0.00
CCTV Works		189	$31,080.00	19-Dec-26	26-Jul-27			$0.00	$0.00	0.00
TAEXCCCL030001	Pipe Installation with manhole	11	$5,723.00	19-Dec-26	30-Dec-26			$0.00	$0.00	0.00
TAEXCCCL030002	CCTV Swiches Lighting panels Installation	13	$2,578.00	14-Jun-27	28-Jun-27			$0.00	$0.00	0.00
TAEXCCCL030003	Cable laying and connected with Panels	10	$18,176.00	29-Jun-27	10-Jul-27			$0.00	$0.00	0.00
TAEXCCCL030004	Pole Installation with IP Outdoor CCTV POE Camera	14	$4,603.00	11-Jul-27	26-Jul-27			$0.00	$0.00	0.00
Potable Networks		108	$232,550.54	17-Aug-26	25-Jan-27	09-Jun-26	16-Aug-26	$184,295.54	$232,550.54	1.26
TAEXPTCL030001	Excavation works for Trench	17	$57,309.62	17-Aug-26	05-Sep-26	09-Jun-26	25-Jul-26	$57,309.62	$57,309.62	1.00
TAEXPTCL030002	Bedding Works	2	$7,050.00	06-Sep-26	07-Sep-26	21-Jun-26	25-Jul-26	$7,050.00	$7,050.00	1.00
TAEXPTCL030003	Install Pipes & Fittings	7	$72,350.00	08-Sep-26	15-Sep-26	21-Jun-26	25-Jul-26	$72,350.00	$72,350.00	1.00
TAEXPTCL030004	Backfilling Works for Trench	10	$37,985.92	16-Sep-26	27-Sep-26	30-Jun-26	25-Jul-26	$37,985.92	$37,985.92	1.00
TAEXPTCL030005	Install Valves with fittings	4	$9,600.00	26-Oct-26	29-Oct-26	23-Jul-26	25-Jul-26	$9,600.00	$9,600.00	1.00
TAEXPTCL030006	Valve Chamber works	16	$20,250.00	05-Dec-26	22-Dec-26	25-Jun-26	11-Aug-26	$0.00	$20,250.00	0.00
TAEXPTCL030008	Install fire hydrent	6	$24,000.00	05-Dec-26	10-Dec-26	16-Jul-26	02-Aug-26	$0.00	$24,000.00	0.00
TAEXPTCL030007	Inspection Test	4	$4,005.00	21-Jan-27	25-Jan-27	15-Aug-26	16-Aug-26	$0.00	$4,005.00	0.00
TSE Networks		186	$202,553.34	09-Jun-26	20-Apr-27	09-Jun-26	16-Aug-26	$152,133.34	$202,553.34	1.33
TAEXTSCL030001	Excavation works for Trench	6	$66,703.34	09-Jun-26	15-Jun-26	09-Jun-26	25-Jul-26	$66,703.34	$66,703.34	1.00
TAEXTSCL030002	Bedding Works	2	$4,000.00	16-Jun-26	17-Jun-26	21-Jun-26	25-Jul-26	$4,000.00	$4,000.00	1.00
TAEXTSCL030003	Install Pipes & Fittings	7	$58,930.00	18-Jun-26	25-Jun-26	21-Jun-26	25-Jul-26	$58,930.00	$58,930.00	1.00
TAEXTSCL030004	Backfilling Works for Trench	13	$22,500.00	28-Sep-26	12-Oct-26	28-Jun-26	25-Jul-26	$22,500.00	$22,500.00	1.00
TAEXTSCL030005	Install Valves with fittings	4	$6,320.00	24-Mar-27	28-Mar-27	23-Jul-26	25-Jul-26	$0.00	$6,320.00	0.00
TAEXTSCL030006	Valve Chamber works	16	$40,250.00	29-Mar-27	15-Apr-27	25-Jun-26	12-Aug-26	$0.00	$40,250.00	0.00
TAEXTSCL030007	Inspection Test	4	$3,850.00	17-Apr-27	20-Apr-27	15-Aug-26	16-Aug-26	$0.00	$3,850.00	0.00
Sewerage Networks		129	$301,010.60	04-Jan-26	02-Jun-26	04-Jan-26	02-Jun-26	$301,010.60	$301,010.60	1.00
TAEXSWCL030001	Excavation works for Trench	19	$68,350.00	04-Jan-26	25-Jan-26	04-Jan-26	25-Jan-26	$68,350.00	$68,350.00	1.00
TAEXSWCL030002	Bedding Works	9	$23,486.15	27-Jan-26	05-Feb-26	27-Jan-26	05-Feb-26	$23,486.15	$23,486.15	1.00
TAEXSWCL030003	Install GRP Pipes & Fittings	75	$98,700.00	28-Jan-26	25-Apr-26	28-Jan-26	25-Apr-26	$98,700.00	$98,700.00	Install GRP Pipes & Fittings 1.00
TAEXSWCL030004	Backfilling Works for Trench	94	$20,580.00	04-Feb-26	24-May-26	04-Feb-26	24-May-26	$20,580.00	$20,580.00	1.00 lling Works for Trench
TAEXSWCL030005	Manhole Installation with backfilling	45	$64,200.00	12-Apr-26	02-Jun-26	12-Apr-26	02-Jun-26	$64,200.00	$64,200.00	1.00 nhole Installation with backfilling
TAEXSWCL030006	Leakage Test	10	$25,694.45	23-May-26	02-Jun-26	23-May-26	02-Jun-26	$25,694.45	$25,694.45	1.00 age Test
Storm Networks		257	$521,725.28	28-Jan-26	24-Apr-27	28-Jan-26	26-Sep-26	$410,479.28	$521,725.28	1.27
TAEXSTCL030001	Excavation works for Trench	72	$88,620.00	28-Jan-26	21-Apr-26	28-Jan-26	21-Apr-26	$88,620.00	$88,620.00	Excavation works for Trench 1.00
TAEXSTCL030002	Bedding Works	66	$83,945.28	15-Feb-26	02-May-26	15-Feb-26	02-May-26	$83,945.28	$83,945.28	1.00 orks
TAEXSTCL030003	Install GRP Pipes & Fittings	4	$93,698.50	18-Feb-26	22-Feb-26	18-Feb-26	22-Feb-26	$93,698.50	$93,698.50	Install GRP Pipes & Fittings 1.00

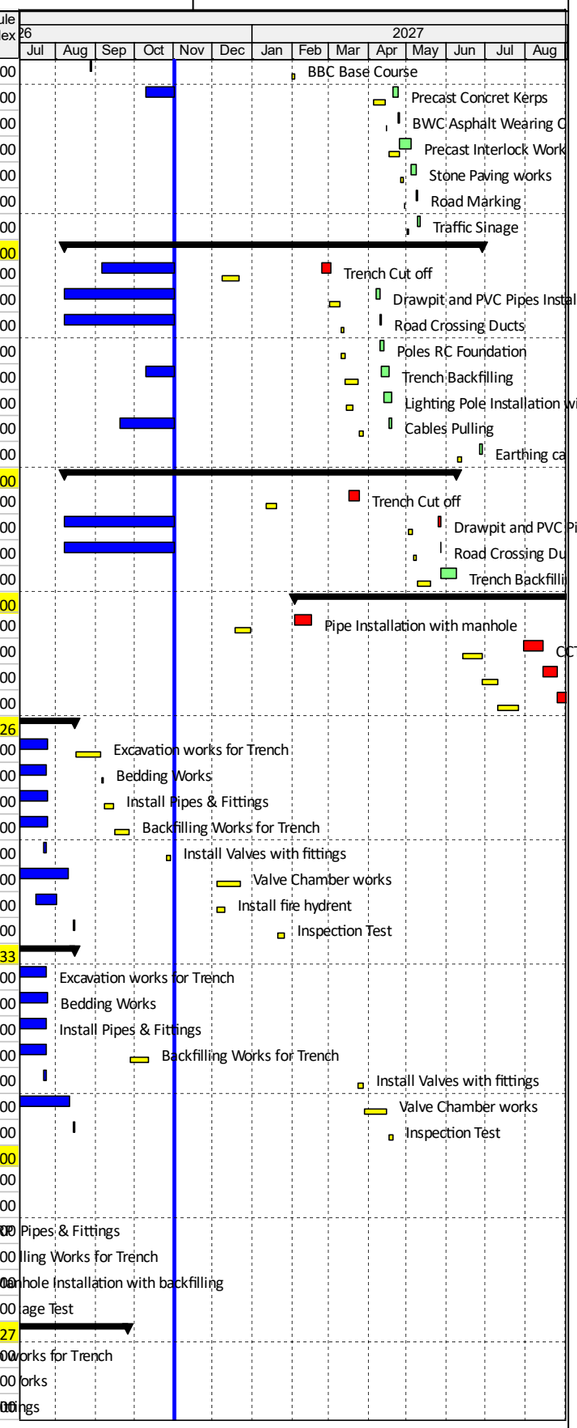


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXSTCL030004	Backfilling Works for Trench	11	$93,385.00	23-Mar-26	04-Apr-26	23-Mar-26	04-Apr-26	$93,385.00	$93,385.00	1.00
TAEXSTCL030005	Manhole Installation with backfilling	7	$40,984.00	23-May-26	30-May-26	23-May-26	30-May-26	$40,984.00	$40,984.00	1.00
TAEXSTCL0300031	Install GRP Pipes & Fittings Part 01	3	$4,931.50	03-Jun-26	06-Jun-26	23-Jul-26	25-Jul-26	$4,931.50	$4,931.50	1.00
TAEXSTCL0300041	Backfilling Works for Trench Part 01	4	$4,915.00	13-Oct-26	17-Oct-26	22-Jul-26	25-Jul-26	$4,915.00	$4,915.00	1.00
TAEXSTCL0300051	Manhole Installation with backfilling Part 01	3	$10,246.00	07-Nov-26	09-Nov-26	06-Jun-26	02-Aug-26	$0.00	$10,246.00	0.00
TAEXSTCL030006	Install Catch Basin with UPVC Pipes & Fittings	9	$89,800.00	10-Nov-26	19-Nov-26	05-Jul-26	02-Aug-26	$0.00	$89,800.00	0.00
TAEXSTCL030007	Leakage Test	3	$11,200.00	21-Apr-27	24-Apr-27	01-Aug-26	26-Sep-26	$0.00	$11,200.00	0.00
Local Road 04		548	$4,872,198.17	09-Dec-25	07-Aug-27	09-Dec-25		$1,319,837.84	$3,222,389.80	2.44
Road Works		330	$2,871,280.16	23-May-26	21-Jun-27	23-May-26		$161,942.58	$1,765,562.16	10.90
TAEXRDCL040001	Road Excavation and Disposal	6	$92,180.88	23-May-26	28-May-26	23-May-26	28-May-26	$92,180.88	$92,180.88	1.00
TAEXRDCL040002	Backfilling Works for Road	5	$69,761.70	24-May-26	28-May-26	24-May-26	29-May-26	$69,761.70	$69,761.70	1.00
TAEXRDCL0400011	Road Excavation and Disposal Part 01	3	$931.12	21-Nov-26	23-Nov-26	06-Jun-26	13-Jun-26	$0.00	$931.12	0.00
TAEXRDCL0400021	Backfilling Works for Road Part 01	8	$85,264.30	24-Nov-26	02-Dec-26	06-Jun-26	16-Jun-26	$0.00	$85,264.30	0.00
TAEXRDCL040003	Subgrade Works	5	$95,648.16	15-Dec-26	20-Dec-26	12-Jul-26	18-Jul-26	$0.00	$95,648.16	0.00
TAEXRDCL040004	ABC aggregate Base Course Works	6	$266,839.00	21-Dec-26	27-Dec-26	19-Jul-26	26-Jul-26	$0.00	$266,839.00	0.00
TAEXRDCL040005	MBC1 layer	1	$5,000.00	28-Dec-26	28-Dec-26	02-Aug-26	05-Aug-26	$0.00	$5,000.00	0.00
TAEXRDCL040006	BBC Base Course	2	$404,278.00	29-Dec-26	30-Dec-26	02-Aug-26	06-Aug-26	$0.00	$404,278.00	0.00
TAEXRDCL040008	Precast Concret Kerps	16	$745,659.00	15-Apr-27	03-May-27	20-Sep-26	25-Oct-26	$0.00	$745,659.00	0.00
TAEXRDCL040007	BWC Asphalt Wearing Course with RC	20	$411,511.00	04-May-27	26-May-27			$0.00	$0.00	0.00
TAEXRDCL040009	Precast Interlock Works	12	$112,407.00	27-May-27	09-Jun-27			$0.00	$0.00	0.00
TAEXRDCL040010	Stone Paving works	7	$535,000.00	10-Jun-27	17-Jun-27			$0.00	$0.00	0.00
TAEXRDCL040011	Road Marking	1	$4,800.00	19-Jun-27	19-Jun-27			$0.00	$0.00	0.00
TAEXRDCL040012	Traffic Sinage	2	$42,000.00	20-Jun-27	21-Jun-27			$0.00	$0.00	0.00
Electrical Works		166	$494,416.25	22-Dec-26	14-Jun-27	30-Jun-26		$0.00	$17,880.88	0.00
TAEXELCL040001	Trench Cut off	14	$27,686.25	22-Dec-26	06-Jan-27	30-Jun-26		$0.00	$8,305.88	0.00
TAEXELCL040002	Drawpit and PVC Pipes Installation	8	$4,560.00	02-Mar-27	10-Mar-27	04-Jul-26	27-Oct-26	$0.00	$4,560.00	0.00
TAEXELCL040003	Road Crossing Ducts	2	$260.00	11-Mar-27	13-Mar-27	04-Jul-26	27-Oct-26	$0.00	$260.00	0.00
TAEXELCL040006	Poles RC Foundation	3	$9,510.00	11-Mar-27	14-Mar-27	25-Oct-26		$0.00	$4,755.00	0.00
TAEXELCL040004	Trench Backfilling	10	$10,580.00	14-Mar-27	24-Mar-27			$0.00	$0.00	0.00
TAEXELCL040008	Lighting Pole Installation with Luminares	5	$91,500.00	15-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCL040005	Cables Pulling	3	$168,000.00	25-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXELCL040009	Install Substation & RMU	9	$180,000.00	22-Apr-27	02-May-27			$0.00	$0.00	0.00
TAEXELCL040007	Earthing cables	2	$2,320.00	13-Jun-27	14-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		122	$125,530.00	20-Jan-27	24-May-27	30-Jun-26		$0.00	$89,055.00	0.00
TAEXTCCL040001	Trench Cut off	7	$10,250.00	20-Jan-27	27-Jan-27	30-Jun-26		$0.00	$205.00	0.00
TAEXTCCL040002	Drawpit and PVC Pipes Installation	4	$80,250.00	06-May-27	10-May-27	04-Jul-26	05-Jul-26	$0.00	$80,250.00	0.00
TAEXTCCL040003	Road Crossing Ducts	2	$8,600.00	11-May-27	12-May-27	04-Jul-26	05-Jul-26	$0.00	$8,600.00	0.00
TAEXTCCL040004	Trench Backfilling	10	$26,430.00	13-May-27	24-May-27			$0.00	$0.00	0.00
CCTV Works		175	$31,080.00	31-Dec-26	07-Aug-27			$0.00	$0.00	0.00
TAEXCCCL040001	Pipe Installation with manhole	10	$5,723.00	31-Dec-26	11-Jan-27			$0.00	$0.00	0.00
TAEXCCCL040002	CCTV Swiches Lighting panels Installation	10	$2,578.00	29-Jun-27	10-Jul-27			$0.00	$0.00	0.00
TAEXCCCL040003	Cable laying and connected with Panels	10	$18,176.00	11-Jul-27	21-Jul-27			$0.00	$0.00	0.00
TAEXCCCL040004	Pole Installation with IP Outdoor CCTV POE Camera	14	$4,603.00	22-Jul-27	07-Aug-27			$0.00	$0.00	0.00
Potable Networks		120	$242,550.54	06-Sep-26	20-Jan-27	14-Jun-26	08-Jul-26	$184,295.54	$242,550.54	1.32
TAEXPTCL040001	Excavation works for Trench	6	$57,309.62	06-Sep-26	12-Sep-26	14-Jun-26	21-Jun-26	$57,309.62	$57,309.62	1.00
TAEXPTCL040002	Bedding Works	2	$7,050.00	13-Sep-26	14-Sep-26	22-Jun-26	23-Jun-26	$7,050.00	$7,050.00	1.00
TAEXPTCL040003	Install Pipes & Fittings	7	$72,350.00	26-Sep-26	03-Oct-26	22-Jun-26	23-Jun-26	$72,350.00	$72,350.00	1.00
TAEXPTCL040004	Backfilling Works for Trench	13	$37,985.92	11-Oct-26	25-Oct-26	25-Jun-26	28-Jun-26	$37,985.92	$37,985.92	1.00
TAEXPTCL040005	Install Valves with fittings	4	$9,600.00	21-Oct-26	25-Oct-26	27-Jun-26	30-Jun-26	$9,600.00	$9,600.00	1.00
TAEXPTCL040006	Install fire hydrent	6	$24,000.00	28-Nov-26	03-Dec-26	28-Jun-26	30-Jun-26	$0.00	$24,000.00	0.00
TAEXPTCL040007	Valve Chamber works	21	$30,250.00	23-Dec-26	16-Jan-27	23-Jun-26	02-Jul-26	$0.00	$30,250.00	0.00
TAEXPTCL040008	Inspection Test	4	$4,005.00	17-Jan-27	20-Jan-27	08-Jul-26	08-Jul-26	$0.00	$4,005.00	0.00
TSE Networks		221	$193,553.34	03-Jun-26	15-Apr-27	14-Jun-26	20-Aug-26	$143,133.34	$193,553.34	1.35
TAEXTSCL040001	Excavation works for Trench	5	$56,703.34	03-Jun-26	08-Jun-26	14-Jun-26	21-Jun-26	$56,703.34	$56,703.34	1.00

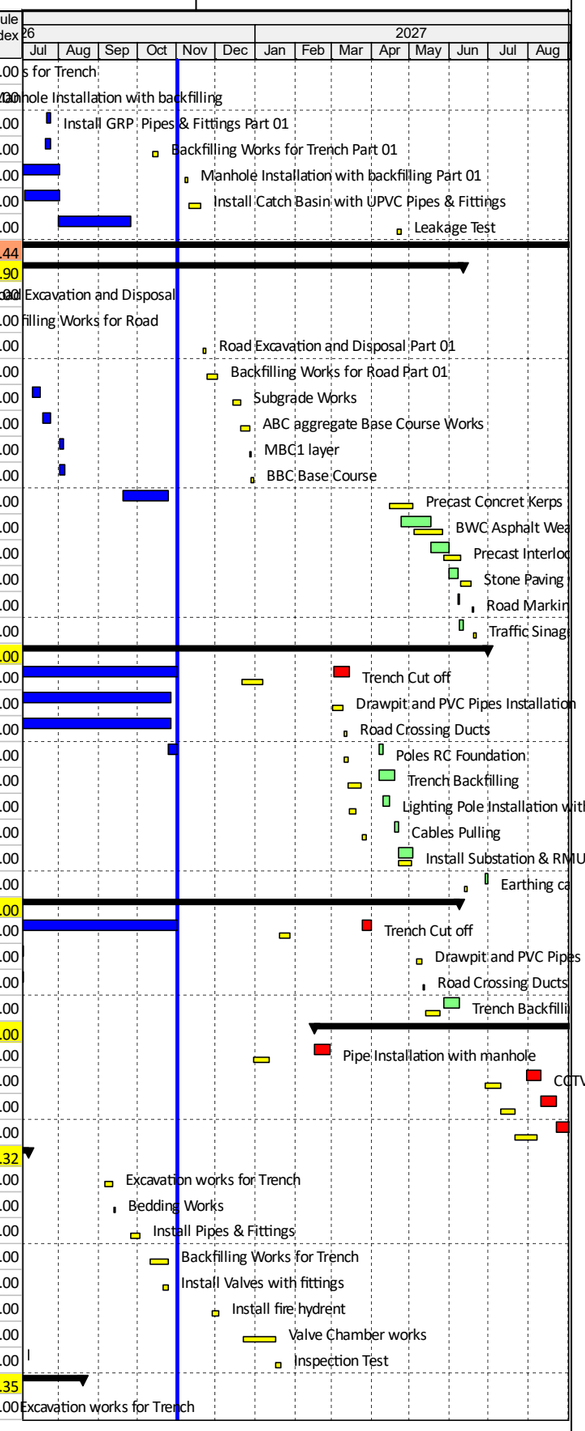


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTSCL040002	Bedding Works	2	$4,000.00	15-Sep-26	16-Sep-26	21-Jun-26	23-Jun-26	$4,000.00	$4,000.00	1.00
TAEXTSCL040003	Install Pipes & Fittings	7	$58,930.00	17-Sep-26	24-Sep-26	21-Jun-26	23-Jun-26	$58,930.00	$58,930.00	1.00
TAEXTSCL040004	Backfilling Works for Trench	13	$23,500.00	26-Sep-26	10-Oct-26	25-Jun-26	02-Jul-26	$23,500.00	$23,500.00	1.00
TAEXTSCL040005	Install Valves with fittings	4	$6,320.00	20-Mar-27	23-Mar-27	28-Jun-26	30-Jun-26	$0.00	$6,320.00	0.00
TAEXTSCL040006	Valve Chamber works	16	$40,250.00	24-Mar-27	11-Apr-27	23-Jun-26	02-Jul-26	$0.00	$40,250.00	0.00
TAEXTSCL040007	Inspection Test	4	$3,850.00	12-Apr-27	15-Apr-27	20-Aug-26	20-Aug-26	$0.00	$3,850.00	0.00
Sewerage Networks		142	$301,662.60	09-Dec-25	23-May-26	09-Dec-25	23-May-26	$301,662.60	$301,662.60	1.00
TAEXSWCL040001	Excavation works for Trench	18	$68,350.00	09-Dec-25	29-Dec-25	09-Dec-25	29-Dec-25	$68,350.00	$68,350.00	1.00
TAEXSWCL040002	Bedding Works	7	$23,486.15	30-Dec-25	06-Jan-26	30-Dec-25	06-Jan-26	$23,486.15	$23,486.15	1.00
TAEXSWCL040003	Install GRP Pipes & Fittings	94	$98,700.00	06-Jan-26	25-Apr-26	06-Jan-26	25-Apr-26	$98,700.00	$98,700.00	1.00
TAEXSWCL040004	Backfilling Works for Trench	102	$20,590.00	21-Jan-26	19-May-26	21-Jan-26	19-May-26	$20,590.00	$20,590.00	1.00
TAEXSWCL040005	Manhole Installation with backfilling	36	$64,200.00	12-Apr-26	23-May-26	12-Apr-26	23-May-26	$64,200.00	$64,200.00	1.00
TAEXSWCL040006	Leakage Test	10	$26,336.45	09-May-26	19-May-26	09-May-26	19-May-26	$26,336.45	$26,336.45	1.00
Storm Networks		266	$612,125.28	25-Jan-26	19-Apr-27	25-Jan-26	30-Aug-26	$528,803.78	$612,125.28	1.16
TAEXSTCL040001	Excavation works for Trench	7	$179,189.00	25-Jan-26	01-Feb-26	25-Jan-26	01-Feb-26	$179,189.00	$179,189.00	1.00
TAEXSTCL040002	Bedding Works	2	$79,748.02	21-Feb-26	22-Feb-26	21-Feb-26	22-Feb-26	$79,748.02	$79,748.02	1.00
TAEXSTCL040003	Install GRP Pipes & Fittings	6	$93,698.50	21-Feb-26	26-Feb-26	21-Feb-26	26-Feb-26	$93,698.50	$93,698.50	1.00
TAEXSTCL040005	Manhole Installation with backfilling	10	$48,668.50	21-Apr-26	02-May-26	21-Apr-26	02-May-26	$48,668.50	$48,668.50	1.00
TAEXSTCL040004	Backfilling Works for Trench	10	$93,385.00	25-Apr-26	05-May-26	25-Apr-26	05-May-26	$93,385.00	$93,385.00	1.00
TAEXSTCL040007	Leakage Test	2	$10,640.00	23-May-26	24-May-26	23-May-26	24-May-26	$10,640.00	$10,640.00	1.00
TAEXSTCL0400011	Excavation works for Trench Part 01	11	$9,431.00	03-Jun-26	15-Jun-26	06-Jun-26	20-Jun-26	$9,431.00	$9,431.00	1.00
TAEXSTCL0400021	Bedding Works Part 01	2	$4,197.26	17-Sep-26	19-Sep-26	06-Jun-26	21-Jun-26	$4,197.26	$4,197.26	1.00
TAEXSTCL0400031	Install GRP Pipes & Fittings Part 01	8	$4,931.50	20-Sep-26	28-Sep-26	23-Jun-26	24-Jun-26	$4,931.50	$4,931.50	1.00
TAEXSTCL0400041	Backfilling Works for Trench Part 01	15	$4,915.00	11-Oct-26	27-Oct-26	27-Jun-26	28-Jun-26	$4,915.00	$4,915.00	1.00
TAEXSTCL0400051	Manhole Installation with backfilling Part 01	13	$2,561.50	05-Nov-26	19-Nov-26	27-Jun-26	28-Jun-26	$0.00	$2,561.50	0.00
TAEXSTCL040006	Install Catch Basin with UPVC Pipes & Fittings	10	$80,200.00	21-Nov-26	01-Dec-26	26-Jun-26	05-Jul-26	$0.00	$80,200.00	0.00
TAEXSTCL0400071	Leakage Test Part 01	3	$560.00	17-Apr-27	19-Apr-27	08-Jul-26	30-Aug-26	$0.00	$560.00	0.00
Local Road 05		603	$5,138,586.02	11-Oct-25	11-Aug-27	11-Oct-25		$1,647,740.39	$2,961,498.06	1.80
Road Works		510	$2,919,230.16	11-Oct-25	07-Jun-27	11-Oct-25		$448,138.00	$1,510,755.57	3.37
TAEXRDCL050001	Road Excavation and Disposal	56	$293,112.00	11-Oct-25	14-Dec-25	11-Oct-25	14-Dec-25	$293,112.00	$293,112.00	1.00
TAEXRDCL050002	Backfilling Works for Road	3	$155,026.00	06-Dec-25	08-Dec-25	06-Dec-25	08-Dec-25	$155,026.00	$155,026.00	1.00
TAEXRDCL050003	Subgrade Works	5	$95,648.16	09-Dec-26	14-Dec-26	21-Jun-26	21-Jul-26	$0.00	$95,648.16	0.00
TAEXRDCL050004	ABC aggregate Base Course Works	6	$266,839.00	02-Jan-27	07-Jan-27	04-Jul-26	06-Aug-26	$0.00	$266,839.00	0.00
TAEXRDCL050005	MBC1 layer	1	$3,650.00	09-Jan-27	09-Jan-27	15-Jul-26	11-Aug-26	$0.00	$3,650.00	0.00
TAEXRDCL050006	BBC Base Course	2	$354,278.00	10-Jan-27	11-Jan-27	18-Jul-26	16-Aug-26	$0.00	$354,278.00	0.00
TAEXRDCL050008	Precast Concret Kerps	17	$345,659.00	12-Jan-27	31-Jan-27	20-Sep-26		$0.00	$342,202.41	0.00
TAEXRDCL050007	BWC Asphalt Wearing Course with RC	1	$1,011,511.00	13-May-27	13-May-27			$0.00	$0.00	0.00
TAEXRDCL050009	Precast Interlock Works	15	$312,407.00	15-May-27	31-May-27			$0.00	$0.00	0.00
TAEXRDCL050010	Stone Paving works	3	$35,000.00	01-Jun-27	03-Jun-27			$0.00	$0.00	0.00
TAEXRDCL050011	Road Marking	1	$4,100.00	05-Jun-27	05-Jun-27			$0.00	$0.00	0.00
TAEXRDCL050012	Traffic Sinage	2	$42,000.00	06-Jun-27	07-Jun-27			$0.00	$0.00	0.00
Electrical Works		156	$714,386.25	07-Jan-27	16-Jun-27	21-Jun-26		$0.00	$13,122.88	0.00
TAEXELCL050001	Trench Cut off	12	$27,676.25	07-Jan-27	20-Jan-27	22-Jun-26		$0.00	$8,302.88	0.00
TAEXELCL050002	Drawpit and PVC Pipes Installation	8	$4,560.00	02-Mar-27	10-Mar-27	23-Jun-26	24-Jun-26	$0.00	$4,560.00	0.00
TAEXELCL050003	Road Crossing Ducts	2	$260.00	11-Mar-27	13-Mar-27	21-Jun-26	24-Jun-26	$0.00	$260.00	0.00
TAEXELCL050006	Poles RC Foundation	3	$9,510.00	11-Mar-27	14-Mar-27			$0.00	$0.00	0.00
TAEXELCL050004	Trench Backfilling	10	$10,560.00	14-Mar-27	24-Mar-27			$0.00	$0.00	0.00
TAEXELCL050008	Lighting Pole Installation with Luminares	5	$91,500.00	15-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCL050005	Cables Pulling	3	$568,000.00	25-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXELCL050007	Earthing cables	2	$2,320.00	15-Jun-27	16-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		115	$125,530.00	28-Jan-27	29-May-27	20-Jun-26		$0.00	$89,260.00	0.00
TAEXTCCL050001	Trench Cut off	7	$10,250.00	28-Jan-27	04-Feb-27	22-Jun-26		$0.00	$410.00	0.00
TAEXTCCL050002	Drawpit and PVC Pipes Installation	4	$80,250.00	11-May-27	15-May-27	20-Jun-26	21-Jun-26	$0.00	$80,250.00	0.00
TAEXTCCL050003	Road Crossing Ducts	2	$8,600.00	16-May-27	17-May-27	22-Jun-26	24-Jun-26	$0.00	$8,600.00	0.00

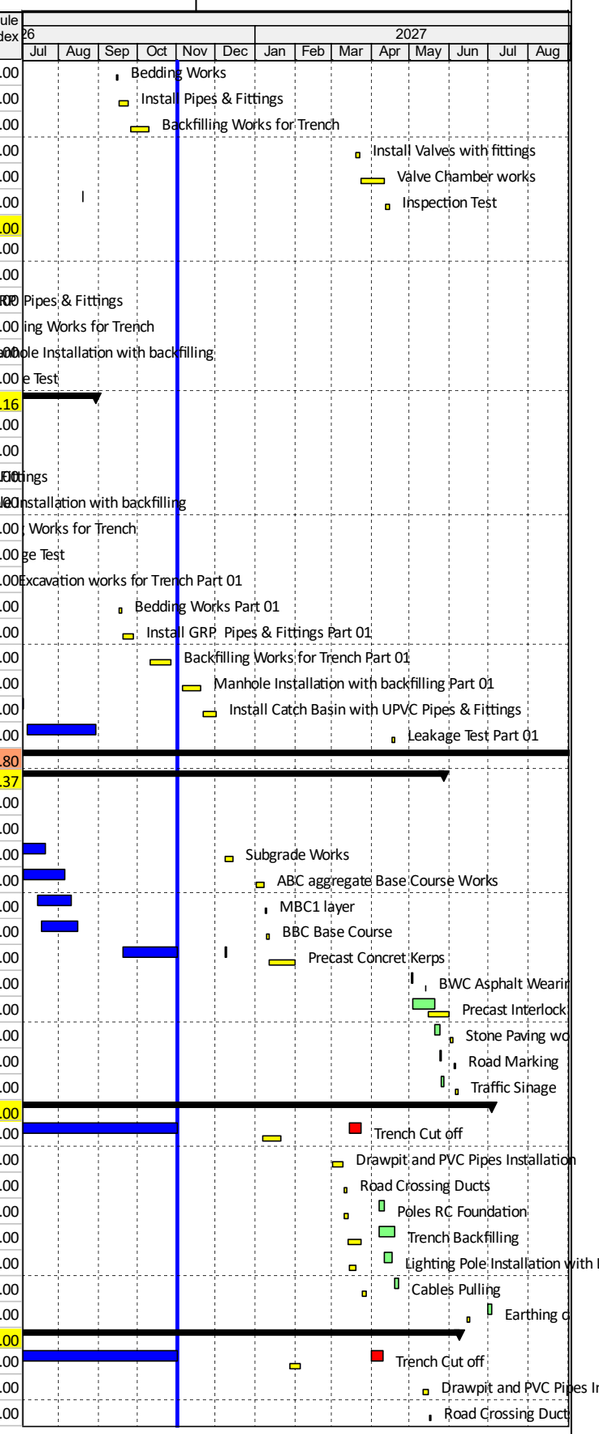


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTCCL050004	Trench Backfilling	10	$26,430.00	18-May-27	29-May-27			$0.00	$0.00	0.00
CCTV Works		169	$31,080.00	12-Jan-27	11-Aug-27			$0.00	$0.00	0.00
TAEXCCCL050001	Pipe Installation with manhole	10	$5,723.00	12-Jan-27	23-Jan-27			$0.00	$0.00	0.00
TAEXCCCL050002	CCTV Swiches Lighting panels Installation	10	$2,578.00	11-Jul-27	21-Jul-27			$0.00	$0.00	0.00
TAEXCCCL050003	Cable laying and connected with Panels	10	$18,176.00	22-Jul-27	02-Aug-27			$0.00	$0.00	0.00
TAEXCCCL050004	Pole Installation with IP Outdoor CCTV POE Camera	8	$4,603.00	03-Aug-27	11-Aug-27			$0.00	$0.00	0.00
Potable Networks		280	$272,350.54	30-Apr-26	08-Apr-27	30-Apr-26	05-Jul-26	$227,335.54	$272,350.54	1.20
TAEXPTCL050001	Excavation works for Trench	13	$57,309.62	30-Apr-26	14-May-26	30-Apr-26	15-May-26	$57,309.62	$57,309.62	1.00
TAEXPTCL050002	Bedding Works	7	$22,735.92	10-May-26	17-May-26	10-May-26	17-May-26	$22,735.92	$22,735.92	1.00
TAEXPTCL050003	Install Pipes & Fittings	8	$92,350.00	14-May-26	23-May-26	14-May-26	23-May-26	$92,350.00	$92,350.00	1.00
TAEXPTCL050004	Backfilling Works for Trench	13	$22,100.00	19-May-26	02-Jun-26	19-May-26	02-Jun-26	$22,100.00	$22,100.00	1.00
TAEXPTCL050005	Install Valves with fittings	3	$9,120.00	19-May-26	21-May-26	19-May-26	21-May-26	$9,120.00	$9,120.00	1.00
TAEXPTCL050007	Valve Chamber works	7	$16,100.00	24-May-26	31-May-26	24-May-26	31-May-26	$16,100.00	$16,100.00	1.00
TAEXPTCL050006	Install fire hydrent	2	$7,200.00	24-May-26	25-May-26	24-May-26	25-May-26	$7,200.00	$7,200.00	1.00
TAEXPTCL0500051	Install Valves with fittings Part 01	24	$480.00	08-Oct-26	04-Nov-26	06-Jun-26	20-Jun-26	$420.00	$480.00	1.14
TAEXPTCL0500061	Install fire hydrent Part 01	2	$16,800.00	25-Nov-26	26-Nov-26	06-Jun-26	14-Jun-26	$0.00	$16,800.00	0.00
TAEXPTCL0500071	Valve Chamber works Part 01	9	$24,150.00	28-Nov-26	07-Dec-26	06-Jun-26	20-Jun-26	$0.00	$24,150.00	0.00
TAEXPTCL050008	Inspection Test	4	$4,005.00	05-Apr-27	08-Apr-27	02-Jul-26	05-Jul-26	$0.00	$4,005.00	0.00
TSE Networks		277	$212,453.34	09-May-26	13-Apr-27	09-May-26	05-Jul-26	$186,149.84	$212,453.34	1.14
TAEXTSCL050001	Excavation works for Trench	4	$66,703.34	09-May-26	12-May-26	09-May-26	12-May-26	$66,703.34	$66,703.34	1.00
TAEXTSCL050002	Bedding Works	3	$4,000.00	17-May-26	19-May-26	17-May-26	19-May-26	$4,000.00	$4,000.00	1.00
TAEXTSCL050003	Install Pipes & Fittings	2	$68,930.00	19-May-26	20-May-26	19-May-26	20-May-26	$68,930.00	$68,930.00	1.00
TAEXTSCL050005	Install Valves with fittings	3	$6,004.00	19-May-26	21-May-26	19-May-26	21-May-26	$6,004.00	$6,004.00	1.00
TAEXTSCL050004	Backfilling Works for Trench	10	$22,400.00	23-May-26	02-Jun-26	23-May-26	02-Jun-26	$22,400.00	$22,400.00	1.00
TAEXTSCL050006	Valve Chamber works	8	$18,112.50	24-May-26	01-Jun-26	24-May-26	01-Jun-26	$18,112.50	$18,112.50	1.00
TAEXTSCL0500051	Install Valves with fittings Part 01	2	$316.00	17-Mar-27	18-Mar-27	06-Jun-26	20-Jun-26	$0.00	$316.00	0.00
TAEXTSCL0500061	Valve Chamber works Part 01	8	$22,137.50	20-Mar-27	28-Mar-27	06-Jun-26	20-Jun-26	$0.00	$22,137.50	0.00
TAEXTSCL050007	Inspection Test	4	$3,850.00	10-Apr-27	13-Apr-27	02-Jul-26	05-Jul-26	$0.00	$3,850.00	0.00
Sewerage Networks		393	$301,430.45	25-Dec-25	15-Apr-27	25-Dec-25	30-Jun-26	$291,331.73	$301,430.45	1.03
TAEXSWCL050001	Excavation works for Trench	23	$68,350.00	25-Dec-25	20-Jan-26	25-Dec-25	20-Jan-26	$68,350.00	$68,350.00	1.00
TAEXSWCL050002	Bedding Works	15	$23,486.00	04-Jan-26	20-Jan-26	04-Jan-26	20-Jan-26	$23,486.00	$23,486.00	1.00
TAEXSWCL050003	Install GRP Pipes & Fittings	5	$96,726.00	04-Jan-26	08-Jan-26	04-Jan-26	08-Jan-26	$96,726.00	$96,726.00	1.00
TAEXSWCL050004	Backfilling Works for Trench	13	$20,580.00	21-Jan-26	04-Feb-26	21-Jan-26	04-Feb-26	$20,580.00	$20,580.00	1.00
TAEXSWCL050005	Manhole Installation with backfilling	10	$57,780.00	11-Apr-26	21-Apr-26	11-Apr-26	21-Apr-26	$57,780.00	$57,780.00	1.00
TAEXSWCL050006	Leakage Test	2	$24,409.73	06-May-26	07-May-26	06-May-26	07-May-26	$24,409.73	$24,409.73	1.00
TAEXSWCL0500031	Install GRP Pipes & Fittings Part 01	5	$1,974.00	20-Mar-27	24-Mar-27	06-Jun-26	07-Jun-26	$0.00	$1,974.00	0.00
TAEXSWCL0500041	Backfilling Works for Trench Part 01	5	$420.00	25-Mar-27	30-Mar-27	27-Jun-26	28-Jun-26	$0.00	$420.00	0.00
TAEXSWCL0500051	Manhole Installation with backfilling Part 01	8	$6,420.00	03-Apr-27	11-Apr-27	06-Jun-26	24-Jun-26	$0.00	$6,420.00	0.00
TAEXSWCL0500061	Leakage Test Part 01	2	$1,284.72	14-Apr-27	15-Apr-27	29-Jun-26	30-Jun-26	$0.00	$1,284.72	0.00
Storm Networks		400	$562,125.28	24-Jan-26	19-Apr-27	24-Jan-26	30-Jun-26	$494,785.28	$562,125.28	1.14
TAEXSTCL050001	Excavation works for Trench	52	$88,620.00	24-Jan-26	24-Mar-26	24-Jan-26	24-Mar-26	$88,620.00	$88,620.00	1.00
TAEXSTCL050002	Bedding Works	30	$83,945.28	18-Feb-26	24-Mar-26	18-Feb-26	24-Mar-26	$83,945.28	$83,945.28	1.00
TAEXSTCL050003	Install GRP Pipes & Fittings	56	$98,630.00	19-Feb-26	25-Apr-26	19-Feb-26	25-Apr-26	$98,630.00	$98,630.00	1.00
TAEXSTCL050004	Backfilling Works for Trench	48	$98,300.00	23-Mar-26	17-May-26	23-Mar-26	17-May-26	$98,300.00	$98,300.00	1.00
TAEXSTCL050005	Manhole Installation with backfilling	11	$96,168.50	23-Mar-26	04-Apr-26	23-Mar-26	04-Apr-26	$96,168.50	$96,168.50	1.00
TAEXSTCL0500051	Manhole Installation with backfilling Part 01	8	$5,061.50	20-Oct-26	28-Oct-26	06-Jun-26	08-Jun-26	$5,061.50	$5,061.50	1.00
TAEXSTCL050006	Install Catch Basin with UPVC Pipes & Fittings	10	$80,200.00	29-Oct-26	09-Nov-26	09-Jun-26	20-Jun-26	$24,060.00	$80,200.00	3.33
TAEXSTCL050007	Leakage Test	3	$11,200.00	17-Apr-27	19-Apr-27	06-Jun-26	30-Jun-26	$0.00	$11,200.00	0.00
ZONE 3		648	$48,625,099.81	04-Sep-25	30-Aug-27	04-Sep-25		$14,550,463.05	$19,850,115.33	1.36
Local Road 01		476	$6,697,536.93	25-Jan-26	20-Jun-27	25-Jan-26		$3,007,235.46	$4,072,187.13	1.35
Road Works		436	$2,794,617.16	25-Jan-26	17-Jun-27	25-Jan-26		$344,362.29	$1,152,857.48	3.35
TAEXRDCL010001	Road Excavation and Disposal	111	$116,390.00	25-Jan-26	02-Jun-26	25-Jan-26	02-Jun-26	$116,390.00	$116,390.00	1.00
TAEXRDCL010002	Backfilling Works for Road	105	$197,305.00	01-Feb-26	02-Jun-26	01-Feb-26	02-Jun-26	$197,305.00	$197,305.00	1.00
TAEXRDCL010003	Subgrade Works	4	$30,667.29	12-Feb-26	16-Feb-26	12-Feb-26	16-Feb-26	$30,667.29	$30,667.29	1.00

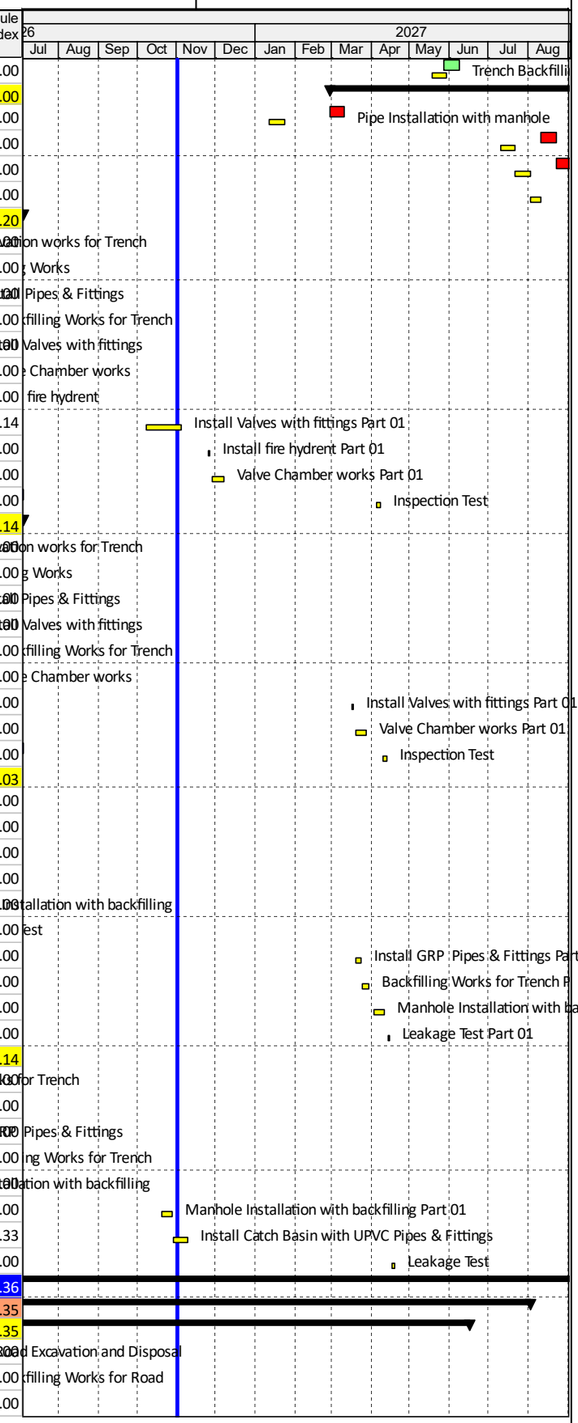


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXRDCL0100031	Subgrade Works Part 01	3	$5,411.87	12-Jan-27	14-Jan-27	23-Aug-26	30-Aug-26	$0.00	$5,411.87	0.00
TAEXRDCL010004	ABC aggregate Base Course Works	8	$355,786.00	16-Jan-27	24-Jan-27	23-Aug-26		$0.00	$298,860.24	0.00
TAEXRDCL010005	MBC1 layer	1	$7,120.00	25-Jan-27	25-Jan-27	06-Sep-26		$0.00	$5,980.80	0.00
TAEXRDCL010006	BBC Base Course	3	$306,417.00	26-Jan-27	28-Jan-27	10-Sep-26		$0.00	$257,390.28	0.00
TAEXRDCL010008	Precast Concret Kerps	14	$401,420.00	15-Apr-27	01-May-27	04-Oct-26		$0.00	$240,852.00	0.00
TAEXRDCL010007	BWC Asphalt Wearing Course with RC	1	$611,511.00	02-May-27	02-May-27			$0.00	$0.00	0.00
TAEXRDCL010009	Precast Interlock Works	15	$675,671.00	24-May-27	09-Jun-27			$0.00	$0.00	0.00
TAEXRDCL010010	Stone Paving works	4	$38,120.00	10-Jun-27	14-Jun-27			$0.00	$0.00	0.00
TAEXRDCL010011	Road Marking	1	$6,148.00	15-Jun-27	15-Jun-27			$0.00	$0.00	0.00
TAEXRDCL010012	Traffic Sinage	2	$42,650.00	16-Jun-27	17-Jun-27			$0.00	$0.00	0.00
Electrical Works		88	$549,066.25	15-Mar-27	20-Jun-27	29-Aug-26		$0.00	$2,072.60	0.00
TAEXELCL010001	Trench Cut off	12	$32,386.25	15-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXELCL010003	Drawpit and PVC Pipes Installation	8	$4,560.00	29-Mar-27	06-Apr-27	29-Aug-26		$0.00	$1,960.80	0.00
TAEXELCL010002	Road Crossing Ducts	4	$260.00	07-Apr-27	11-Apr-27	29-Aug-26		$0.00	$111.80	0.00
TAEXELCL010006	Poles RC Foundation	3	$39,510.00	07-Apr-27	10-Apr-27			$0.00	$0.00	0.00
TAEXELCL010008	Lighting Pole Installation with Luminares	5	$91,500.00	11-Apr-27	15-Apr-27			$0.00	$0.00	0.00
TAEXELCL010004	Trench Backfilling	10	$10,530.00	12-Apr-27	22-Apr-27			$0.00	$0.00	0.00
TAEXELCL010005	Cables Pulling	3	$368,000.00	15-Jun-27	17-Jun-27			$0.00	$0.00	0.00
TAEXELCL010007	Earthing cables	2	$2,320.00	19-Jun-27	20-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		35	$125,530.00	01-Mar-27	02-Jun-27	31-Oct-26		$0.00	$17,770.00	0.00
TAEXTCCL010001	Trench Cut off	7	$10,250.00	01-Mar-27	08-Mar-27			$0.00	$0.00	0.00
TAEXTCCL010002	Drawpit and PVC Pipes Installation	4	$80,250.00	16-May-27	19-May-27	31-Oct-26		$0.00	$16,050.00	0.00
TAEXTCCL010003	Road Crossing Ducts	2	$8,600.00	20-May-27	22-May-27	31-Oct-26		$0.00	$1,720.00	0.00
TAEXTCCL010004	Trench Backfilling	10	$26,430.00	23-May-27	02-Jun-27			$0.00	$0.00	0.00
CCTV Works		50	$52,063.00	22-Mar-27	18-May-27			$0.00	$0.00	0.00
TAEXCCCL010001	Pipe Installation with manhole	12	$25,094.00	22-Mar-27	04-Apr-27			$0.00	$0.00	0.00
TAEXCCCL010002	CCTV Swiches Lighting panels Installation	13	$2,578.00	05-Apr-27	19-Apr-27			$0.00	$0.00	0.00
TAEXCCCL010003	Cable laying and connected with Panels	10	$19,654.00	20-Apr-27	01-May-27			$0.00	$0.00	0.00
TAEXCCCL010004	Pole Installation with IP Outdoor CCTV POE Camera	15	$4,737.00	02-May-27	18-May-27			$0.00	$0.00	0.00
Potable Networks		256	$283,262.54	02-Jun-26	20-May-27	02-Jun-26		$114,045.54	$257,852.91	2.26
TAEXPTCL010001	Excavation works for Trench	1	$59,351.25	02-Jun-26	02-Jun-26	02-Jun-26	02-Jun-26	$59,351.25	$59,351.25	1.00
TAEXPTCL0100011	Excavation works for Trench Part 01	4	$31,958.37	13-Sep-26	16-Sep-26	15-Jul-26		$31,958.37	$28,762.53	0.90
TAEXPTCL010002	Bedding Works	2	$22,735.92	17-Sep-26	19-Sep-26	20-Jun-26		$22,735.92	$20,462.33	0.90
TAEXPTCL010003	Install Pipes & Fittings	8	$78,112.00	01-Mar-27	09-Mar-27	20-Jun-26		$0.00	$70,300.80	0.00
TAEXPTCL010004	Backfilling Works for Trench	15	$28,300.00	10-Mar-27	27-Mar-27	30-Jun-26		$0.00	$24,055.00	0.00
TAEXPTCL010006	Install fire hydrent	6	$24,000.00	10-Mar-27	16-Mar-27	08-Aug-26		$0.00	$22,800.00	0.00
TAEXPTCL010005	Install Valves with fittings	4	$12,500.00	25-Mar-27	29-Mar-27	08-Aug-26		$0.00	$11,250.00	0.00
TAEXPTCL010007	Valve Chamber works	15	$22,300.00	29-Apr-27	16-May-27	26-Jul-26		$0.00	$20,070.00	0.00
TAEXPTCL010008	Inspection Test	4	$4,005.00	17-May-27	20-May-27	23-Aug-26		$0.00	$801.00	0.00
TSE Networks		310	$228,303.34	02-Jun-26	17-May-27	02-Jun-26		$78,053.34	$173,606.59	2.22
TAEXTSCL010001	Excavation works for Trench	1	$54,677.51	02-Jun-26	02-Jun-26	02-Jun-26	02-Jun-26	$54,677.51	$54,677.51	1.00
TAEXTSCL0100011	Excavation works for Trench Part 01	4	$18,225.83	16-Jun-26	20-Jun-26	15-Jul-26		$18,225.83	$1,822.58	0.10
TAEXTSCL010002	Bedding Works	2	$5,150.00	21-Jun-26	22-Jun-26	15-Jun-26		$5,150.00	$3,553.50	0.69
TAEXTSCL010003	Install Pipes & Fittings	8	$72,300.00	29-Mar-27	06-Apr-27	20-Jun-26		$0.00	$49,887.00	0.00
TAEXTSCL010004	Backfilling Works for Trench	15	$25,300.00	07-Apr-27	24-Apr-27	27-Jun-26		$0.00	$17,457.00	0.00
TAEXTSCL010005	Install Valves with fittings	4	$6,800.00	20-Apr-27	24-Apr-27	08-Aug-26		$0.00	$6,120.00	0.00
TAEXTSCL010006	Valve Chamber works	16	$40,250.00	25-Apr-27	12-May-27	19-Jul-26		$0.00	$36,225.00	0.00
TAEXTSCL010007	Inspection Test	4	$5,600.00	13-May-27	17-May-27	23-Aug-26		$0.00	$3,864.00	0.00
Sewerage Networks		228	$248,780.60	28-Mar-26	07-Apr-27	28-Mar-26		$132,423.89	$152,217.99	1.15
TAEXSWCL010001	Excavation works for Trench	10	$35,490.00	28-Mar-26	07-Apr-26	28-Mar-26	07-Apr-26	$35,490.00	$35,490.00	1.00
TAEXSWCL010002	Bedding Works	2	$17,513.89	01-Apr-26	02-Apr-26	01-Apr-26	02-Apr-26	$17,513.89	$17,513.89	1.00
TAEXSWCL010003	Install GRP Pipes & Fittings	6	$31,620.00	04-Apr-26	09-Apr-26	04-Apr-26	10-Apr-26	$31,620.00	$31,620.00	1.00
TAEXSWCL010004	Backfilling Works for Trench	11	$13,500.00	11-Apr-26	22-Apr-26	11-Apr-26	22-Apr-26	$13,500.00	$13,500.00	1.00
TAEXSWCL010005	Manhole Installation with backfilling	7	$34,300.00	21-Apr-26	28-Apr-26	21-Apr-26	28-Apr-26	$34,300.00	$34,300.00	1.00

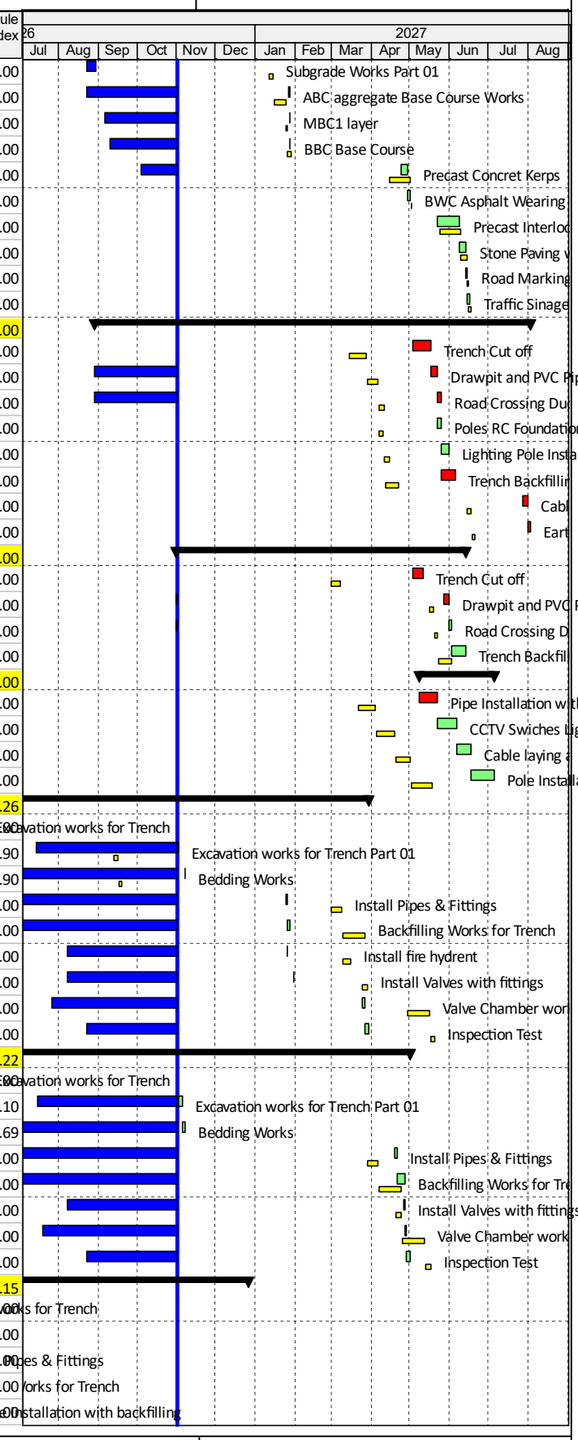

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities


© Oracle Corporation

03-Nov-26 10:40

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXSWCL0100011	Excavation works for Trench Part 01	10	$19,110.00	09-Feb-27	20-Feb-27	15-Jul-26		$0.00	$955.50	0.00
TAEXSWCL0100021	Bedding Works Part 01	2	$9,430.56	21-Feb-27	22-Feb-27	25-Jul-26		$0.00	$471.53	0.00
TAEXSWCL0100031	Install GRP Pipes & Fittings Part 01	10	$21,080.00	23-Feb-27	06-Mar-27	25-Jul-26		$0.00	$1,054.00	0.00
TAEXSWCL0100041	Backfilling Works for Trench Part 01	12	$9,000.00	10-Mar-27	23-Mar-27	08-Aug-26		$0.00	$450.00	0.00
TAEXSWCL0100051	Manhole Installation with backfilling Part 01	10	$34,300.00	24-Mar-27	04-Apr-27	28-Jul-26		$0.00	$5,145.00	0.00
TAEXSWCL010006	Leakage Test	3	$23,436.15	05-Apr-27	07-Apr-27	10-Oct-26		$0.00	$11,718.08	0.00
Storm Networks		266	$2,415,914.04	02-Feb-26	19-Nov-26	02-Feb-26		$2,338,350.40	$2,315,809.55	0.99
TAEXSTCL010001	Excavation works for Trench & Box Culvert	10	$200,172.19	02-Feb-26	12-Feb-26	02-Feb-26	12-Feb-26	$200,172.19	$200,172.19	1.00
TAEXSTCL010002	Bedding Works	2	$67,156.22	28-Feb-26	01-Mar-26	28-Feb-26	01-Mar-26	$67,156.22	$67,156.22	1.00
TAEXSTCL010003	Install GRP Pipes & Fittings	10	$301,993.50	31-Mar-26	11-Apr-26	31-Mar-26	11-Apr-26	$301,993.50	$301,993.50	1.00
TAEXSTCL010004	Backfilling Works for Trench and Boxculvert	12	$108,975.00	04-Apr-26	16-Apr-26	04-Apr-26	16-Apr-26	$108,975.00	$108,975.00	1.00
TAEXSTCL010008	Install Box Culvert Part 1	2	$843,187.76	16-Apr-26	18-Apr-26	16-Apr-26	18-Apr-26	$843,187.76	$843,187.76	1.00
TAEXSTCL010005	Manhole Installation with backfilling	1	$26,300.00	25-Apr-26	25-Apr-26	25-Apr-26	25-Apr-26	$26,300.00	$26,300.00	1.00
TAEXSTCL010009	Install Box Culvert Part 2	14	$458,809.87	25-Apr-26	10-May-26	25-Apr-26	10-May-26	$458,809.87	$458,809.87	1.00
TAEXSTCL0100091	Install Box Culvert Part 2 Part 01	10	$24,147.89	03-Jun-26	14-Jun-26	02-Aug-26	30-Aug-26	$24,147.89	$24,147.89	1.00
TAEXSTCL0100011	Excavation works for Trench & Box Culvert Part 01	25	$50,043.05	16-Jun-26	14-Jul-26	15-Jul-26		$50,043.05	$42,536.59	0.85
TAEXSTCL0100041	Backfilling Works for Trench and Boxculvert Part 01	12	$36,325.00	18-Jun-26	01-Jul-26	02-Aug-26		$36,325.00	$18,162.50	0.50
TAEXSTCL0100021	Bedding Works Part 01	5	$16,789.06	20-Sep-26	24-Sep-26	02-Aug-26		$16,789.06	$14,270.70	0.85
TAEXSTCL0100031	Install GRP Pipes & Fittings Part 01	10	$100,664.50	26-Sep-26	06-Oct-26	02-Aug-26		$100,664.50	$85,564.83	0.85
TAEXSTCL0100051	Manhole Installation with backfilling Part 01	8	$78,900.00	20-Oct-26	28-Oct-26	06-Jun-26		$78,900.00	$67,065.00	0.85
TAEXSTCL010006	Install Catch Basin with UPVC Pipes & Fittings	11	$91,250.00	29-Oct-26	10-Nov-26	26-Jul-26		$24,886.36	$50,187.50	2.02
TAEXSTCL010007	Leakage Test	3	$11,200.00	17-Nov-26	19-Nov-26	31-Oct-26		$0.00	$7,280.00	0.00
Local Road 06		522	$5,081,657.76	18-Dec-25	30-Jun-27	18-Dec-25		$1,038,330.15	$1,599,843.03	1.54
Road Works		476	$2,969,950.38	18-Dec-25	27-Jun-27	18-Dec-25		$413,032.79	$512,432.79	1.24
TAEXRDCL060001	Road Excavation and Disposal	24	$116,390.00	18-Dec-25	14-Jan-26	18-Dec-25	14-Jan-26	$116,390.00	$116,390.00	1.00
TAEXRDCL060002	Backfilling Works for Road	82	$197,305.00	28-Feb-26	02-Jun-26	28-Feb-26	02-Jun-26	$197,305.00	$197,305.00	1.00
TAEXRDCL060003	Subgrade Works	5	$99,337.79	08-Mar-26	12-Mar-26	08-Mar-26	12-Mar-26	$99,337.79	$99,337.79	1.00
TAEXRDCL060000	Asphalt Milling and Deisposal	4	$99,400.00	09-Mar-27	13-Mar-27	25-Jul-26	26-Jul-26	$0.00	$99,400.00	0.00
TAEXRDCL0600031	Subgrade Works Part 01	4	$36,741.37	14-Mar-27	17-Mar-27			$0.00	$0.00	0.00
TAEXRDCL060004	ABC aggregate Base Course Works	8	$355,786.00	18-Mar-27	27-Mar-27			$0.00	$0.00	0.00
TAEXRDCL060005	MBC1 layer	1	$9,874.00	05-Apr-27	05-Apr-27			$0.00	$0.00	0.00
TAEXRDCL060006	BBC Base Course	6	$475,686.00	06-Apr-27	12-Apr-27			$0.00	$0.00	0.00
TAEXRDCL060008	Precast Concret Kerps	18	$401,420.00	02-May-27	22-May-27			$0.00	$0.00	0.00
TAEXRDCL060007	BWC Asphalt Wearing Course with RC	2	$518,119.00	23-May-27	24-May-27			$0.00	$0.00	0.00
TAEXRDCL060009	Precast Interlock Works	14	$575,671.22	25-May-27	09-Jun-27			$0.00	$0.00	0.00
TAEXRDCL060010	Stone Paving works	12	$38,120.00	10-Jun-27	23-Jun-27			$0.00	$0.00	0.00
TAEXRDCL060011	Road Marking	1	$4,100.00	24-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TAEXRDCL060012	Traffic Sinage	2	$42,000.00	26-Jun-27	27-Jun-27			$0.00	$0.00	0.00
Electrical Works		81	$552,024.25	29-Mar-27	30-Jun-27			$0.00	$0.00	0.00
TAEXELCL060001	Trench Cut off	10	$27,356.25	29-Mar-27	08-Apr-27			$0.00	$0.00	0.00
TAEXELCL060002	Drawpit and PVC Pipes Installation	5	$5,280.00	10-Apr-27	14-Apr-27			$0.00	$0.00	0.00
TAEXELCL060003	Road Crossing Ducts	2	$260.00	15-Apr-27	17-Apr-27			$0.00	$0.00	0.00
TAEXELCL060006	Poles RC Foundation	4	$12,500.00	15-Apr-27	19-Apr-27			$0.00	$0.00	0.00
TAEXELCL060004	Trench Backfilling	14	$14,258.00	18-Apr-27	03-May-27			$0.00	$0.00	0.00
TAEXELCL060008	Lighting Pole Installation with Luminares	6	$122,050.00	20-Apr-27	26-Apr-27			$0.00	$0.00	0.00
TAEXELCL060005	Cables Pulling	3	$368,000.00	26-Jun-27	28-Jun-27			$0.00	$0.00	0.00
TAEXELCL060007	Earthing cables	2	$2,320.00	29-Jun-27	30-Jun-27			$0.00	$0.00	0.00
Telecommunication Works		38	$156,565.00	09-Mar-27	13-Jun-27			$0.00	$0.00	0.00
TAEXTCCL060001	Trench Cut off	10	$15,230.00	09-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXTCCL060002	Drawpit and PVC Pipes Installation	5	$100,235.00	20-May-27	25-May-27			$0.00	$0.00	0.00
TAEXTCCL060003	Road Crossing Ducts	2	$8,600.00	26-May-27	27-May-27			$0.00	$0.00	0.00
TAEXTCCL060004	Trench Backfilling	14	$32,500.00	29-May-27	13-Jun-27			$0.00	$0.00	0.00
CCTV Works		50	$52,061.00	05-Apr-27	01-Jun-27			$0.00	$0.00	0.00
TAEXCCCL060001	Pipe Installation with manhole	12	$25,094.00	05-Apr-27	18-Apr-27			$0.00	$0.00	0.00

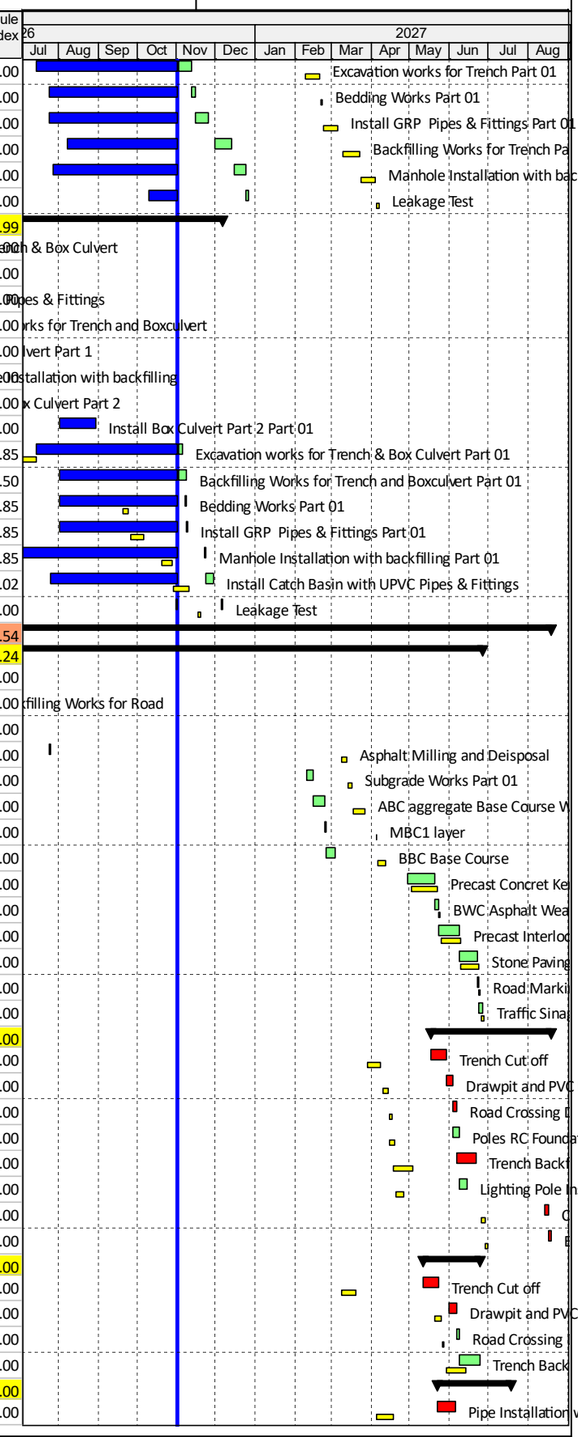


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXCCCL060002	CCTV Swiches Lighting panels Installation	13	$2,578.00	19-Apr-27	03-May-27			$0.00	$0.00	0.00
TAEXCCCL060003	Cable laying and connected with Panels	10	$19,654.00	04-May-27	15-May-27			$0.00	$0.00	0.00
TAEXCCCL060004	Pole Installation with IP Outdoor CCTV POE Camera	15	$4,735.00	16-May-27	01-Jun-27			$0.00	$0.00	0.00
Potable Networks		208	$260,452.92	07-Oct-26	08-Jun-27	18-Jul-26		$101,085.92	$218,080.02	2.16
TAEXPTCL060001	Excavation works for Trench	8	$78,350.00	07-Oct-26	15-Oct-26	18-Jul-26		$78,350.00	$75,999.50	0.97
TAEXPTCL060002	Bedding Works	2	$22,735.92	17-Oct-26	18-Oct-26	08-Aug-26		$22,735.92	$21,599.12	0.95
TAEXPTCL060003	Install Pipes & Fittings	8	$78,112.00	10-Mar-27	18-Mar-27	08-Aug-26		$0.00	$74,206.40	0.00
TAEXPTCL060004	Backfilling Works for Trench	15	$28,300.00	20-Mar-27	05-Apr-27	06-Sep-26		$0.00	$26,885.00	0.00
TAEXPTCL060006	Install fire hydrent	6	$24,000.00	19-Apr-27	25-Apr-27	01-Nov-26		$0.00	$14,400.00	0.00
TAEXPTCL060005	Install Valves with fittings	4	$4,600.00	26-Apr-27	29-Apr-27	27-Sep-26		$0.00	$920.00	0.00
TAEXPTCL060007	Valve Chamber works	16	$20,350.00	17-May-27	03-Jun-27	05-Sep-26		$0.00	$4,070.00	0.00
TAEXPTCL060008	Inspection Test	4	$4,005.00	05-Jun-27	08-Jun-27			$0.00	$0.00	0.00
TSE Networks		218	$228,733.34	11-Aug-26	13-Jun-27	25-Jul-26		$78,103.34	$137,908.87	1.77
TAEXTSCL060001	Excavation works for Trench	8	$72,903.34	11-Aug-26	19-Aug-26	25-Jul-26		$72,903.34	$58,322.67	0.80
TAEXTSCL060002	Bedding Works	2	$5,200.00	20-Aug-26	22-Aug-26	15-Aug-26		$5,200.00	$3,588.00	0.69
TAEXTSCL060003	Install Pipes & Fittings	8	$72,300.00	07-Apr-27	15-Apr-27	15-Aug-26		$0.00	$49,887.00	0.00
TAEXTSCL060004	Backfilling Works for Trench	15	$25,300.00	17-Apr-27	03-May-27	30-Aug-26		$0.00	$17,457.00	0.00
TAEXTSCL060005	Install Valves with fittings	4	$7,100.00	29-Apr-27	03-May-27	27-Sep-26		$0.00	$710.00	0.00
TAEXTSCL060006	Valve Chamber works	16	$40,250.00	04-May-27	22-May-27	05-Sep-26		$0.00	$4,025.00	0.00
TAEXTSCL060007	Inspection Test	4	$5,680.00	09-Jun-27	13-Jun-27	30-Aug-26		$0.00	$3,919.20	0.00
Sewerage Networks		369	$269,640.23	21-Dec-25	11-Mar-27	21-Dec-25		$166,363.26	$228,960.34	1.38
TAEXSWCL060001	Excavation works for Trench	10	$54,047.70	21-Dec-25	31-Dec-25	21-Dec-25	31-Dec-25	$54,047.70	$54,047.70	1.00
TAEXSWCL060002	Bedding Works	3	$21,555.56	30-Dec-25	01-Jan-26	30-Dec-25	01-Jan-26	$21,555.56	$21,555.56	1.00
TAEXSWCL060003	Install GRP Pipes & Fittings	12	$42,160.00	03-Jan-26	15-Jan-26	03-Jan-26	15-Jan-26	$42,160.00	$42,160.00	1.00
TAEXSWCL060004	Backfilling Works for Trench	10	$18,000.00	17-Jan-26	27-Jan-26	17-Jan-26	27-Jan-26	$18,000.00	$18,000.00	1.00
TAEXSWCL060005	Manhole Installation with backfilling	4	$30,600.00	14-Apr-26	18-Apr-26	14-Apr-26	18-Apr-26	$30,600.00	$30,600.00	1.00
TAEXSWCL0600011	Excavation works for Trench Part 01	10	$13,511.92	28-Jan-27	08-Feb-27	10-Sep-26	13-Sep-26	$0.00	$13,511.92	0.00
TAEXSWCL0600021	Bedding Works Part 01	2	$5,388.89	09-Feb-27	10-Feb-27	29-Sep-26	28-Oct-26	$0.00	$5,388.89	0.00
TAEXSWCL0600031	Install GRP Pipes & Fittings Part 01	5	$10,540.00	11-Feb-27	16-Feb-27	01-Oct-26		$0.00	$7,905.00	0.00
TAEXSWCL0600041	Backfilling Works for Trench Part 01	10	$4,500.00	23-Feb-27	06-Mar-27			$0.00	$0.00	0.00
TAEXSWCL0600051	Manhole Installation with backfilling Part 01	9	$45,900.00	24-Feb-27	06-Mar-27	10-Oct-26		$0.00	$25,245.00	0.00
TAEXSWCL060006	Leakage Test	3	$23,436.16	09-Mar-27	11-Mar-27	16-Jul-26		$0.00	$10,546.27	0.00
Storm Networks		167	$592,230.64	15-Jul-26	08-Mar-27	18-Jul-26		$279,744.84	$502,461.00	1.80
TAEXSTCL060001	Excavation works for Trench	21	$148,407.36	15-Jul-26	08-Aug-26	18-Jul-26		$148,407.36	$139,502.92	0.94
TAEXSTCL060002	Bedding Works	3	$83,945.28	19-Oct-26	21-Oct-26	25-Jul-26		$83,945.28	$78,908.56	0.94
TAEXSTCL060003	Install GRP Pipes & Fittings	10	$52,658.00	22-Oct-26	02-Nov-26	26-Jul-26		$47,392.20	$49,498.52	1.04
TAEXSTCL060004	Backfilling Works for Trench	15	$95,600.00	03-Nov-26	19-Nov-26	11-Aug-26		$0.00	$86,040.00	0.00
TAEXSTCL060005	Manhole Installation with backfilling	14	$105,200.00	16-Nov-26	01-Dec-26	28-Jul-26		$0.00	$89,420.00	0.00
TAEXSTCL060006	Install Catch Basin with UPVC Pipes & Fittings	12	$95,220.00	20-Feb-27	04-Mar-27	31-Oct-26		$0.00	$52,371.00	0.00
TAEXSTCL060007	Leakage Test	3	$11,200.00	06-Mar-27	08-Mar-27	28-Oct-26		$0.00	$6,720.00	0.00
Local Road 07		495	$5,890,150.17	21-Jan-26	01-Aug-27	21-Jan-26		$1,279,185.32	$1,551,582.60	1.21
Road Works		477	$3,418,038.16	21-Jan-26	01-Aug-27	21-Jan-26		$193,786.16	$193,786.16	1.00
TAEXRDCL070001	Road Excavation and Disposal	8	$93,112.00	21-Jan-26	29-Jan-26	21-Jan-26	29-Jan-26	$93,112.00	$93,112.00	1.00
TAEXRDCL070002	Backfilling Works for Road	66	$55,026.00	25-Jan-26	11-Apr-26	25-Jan-26	11-Apr-26	$55,026.00	$55,026.00	1.00
TAEXRDCL070003	Subgrade Works	54	$45,648.16	08-Feb-26	11-Apr-26	08-Feb-26	11-Apr-26	$45,648.16	$45,648.16	1.00
TAEXRDCL070004	ABC aggregate Base Course Works	3	$266,839.00	11-Apr-27	13-Apr-27			$0.00	$0.00	0.00
TAEXRDCL070005	MBC1 layer	1	$2,458.00	14-Apr-27	14-Apr-27			$0.00	$0.00	0.00
TAEXRDCL070006	BBC Base Course	2	$1,004,278.00	15-Apr-27	17-Apr-27			$0.00	$0.00	0.00
TAEXRDCL070008	Precast Concret Kerps	18	$345,659.00	23-May-27	12-Jun-27			$0.00	$0.00	0.00
TAEXRDCL070007	BWC Asphalt Wearing Course with RC	1	$811,511.00	13-Jun-27	13-Jun-27			$0.00	$0.00	0.00
TAEXRDCL070009	Precast Interlock Works	16	$712,407.00	23-Jun-27	11-Jul-27			$0.00	$0.00	0.00
TAEXRDCL070010	Stone Paving works	15	$35,000.00	12-Jul-27	28-Jul-27			$0.00	$0.00	0.00
TAEXRDCL070011	Road Marking	1	$4,100.00	29-Jul-27	29-Jul-27			$0.00	$0.00	0.00
TAEXRDCL070012	Traffic Sinage	2	$42,000.00	31-Jul-27	01-Aug-27			$0.00	$0.00	0.00

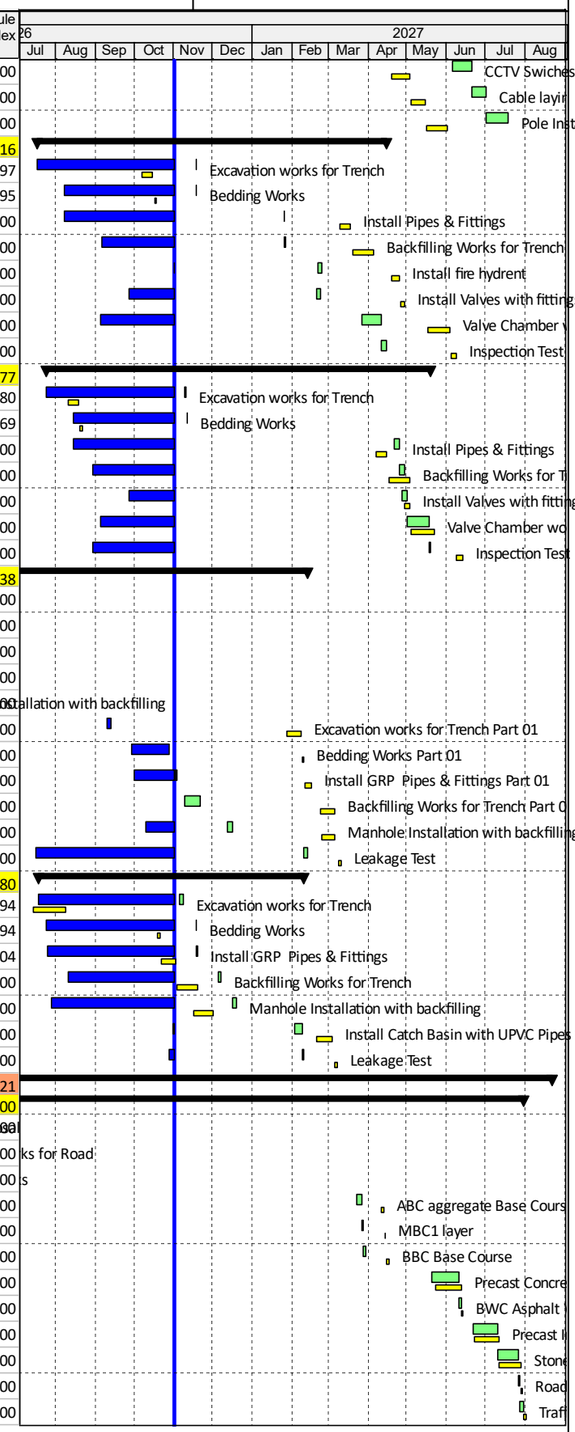


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Electrical Works		73	$516,856.25	10-Apr-27	03-Jul-27			$0.00	$0.00	0.00
TAEXELCL070001	Trench Cut off	12	$30,176.25	10-Apr-27	22-Apr-27			$0.00	$0.00	0.00
TAEXELCL070002	Drawpit and PVC Pipes Installation	8	$4,560.00	24-Apr-27	02-May-27			$0.00	$0.00	0.00
TAEXELCL070003	Road Crossing Ducts	2	$260.00	03-May-27	04-May-27			$0.00	$0.00	0.00
TAEXELCL070006	Poles RC Foundation	3	$9,510.00	03-May-27	05-May-27			$0.00	$0.00	0.00
TAEXELCL070004	Trench Backfilling	10	$10,530.00	05-May-27	16-May-27			$0.00	$0.00	0.00
TAEXELCL070008	Lighting Pole Installation with Luminares	5	$91,500.00	06-May-27	11-May-27			$0.00	$0.00	0.00
TAEXELCL070005	Cables Pulling	3	$368,000.00	17-May-27	19-May-27			$0.00	$0.00	0.00
TAEXELCL070007	Earthing cables	2	$2,320.00	01-Jul-27	03-Jul-27			$0.00	$0.00	0.00
Telecommunication Works		28	$124,780.00	21-Mar-27	13-Jun-27			$0.00	$0.00	0.00
TAEXTCCL070001	Trench Cut off	6	$9,500.00	21-Mar-27	27-Mar-27			$0.00	$0.00	0.00
TAEXTCCL070002	Drawpit and PVC Pipes Installation	4	$80,250.00	26-May-27	30-May-27			$0.00	$0.00	0.00
TAEXTCCL070003	Road Crossing Ducts	2	$8,600.00	31-May-27	01-Jun-27			$0.00	$0.00	0.00
TAEXTCCL070004	Trench Backfilling	10	$26,430.00	02-Jun-27	13-Jun-27			$0.00	$0.00	0.00
CCTV Works		44	$50,414.00	19-Apr-27	08-Jun-27			$0.00	$0.00	0.00
TAEXCCCL070001	Pipe Installation with manhole	9	$23,962.00	19-Apr-27	28-Apr-27			$0.00	$0.00	0.00
TAEXCCCL070002	CCTV Swiches Lighting panels Installation	12	$2,264.00	29-Apr-27	12-May-27			$0.00	$0.00	0.00
TAEXCCCL070003	Cable laying and connected with Panels	10	$19,654.00	13-May-27	24-May-27			$0.00	$0.00	0.00
TAEXCCCL070004	Pole Installation with IP Outdoor CCTV POE Camera	13	$4,534.00	25-May-27	08-Jun-27			$0.00	$0.00	0.00
Potable Networks		322	$238,312.54	22-Apr-26	24-Jun-27	22-Apr-26		$80,045.54	$109,959.22	1.37
TAEXPTCL070001	Excavation works for Trench	4	$54,444.14	22-Apr-26	26-Apr-26	22-Apr-26	26-Apr-26	$54,444.14	$54,444.14	1.00
TAEXPTCL0700011	Excavation works for Trench Part 01	4	$2,865.48	21-Sep-26	24-Sep-26			$2,865.48	$0.00	0.00
TAEXPTCL070002	Bedding Works	2	$22,735.92	26-Sep-26	27-Sep-26	29-Jun-26		$22,735.92	$10,003.80	0.44
TAEXPTCL070003	Install Pipes & Fittings	8	$78,112.00	20-Mar-27	28-Mar-27	30-Jun-26		$0.00	$34,369.28	0.00
TAEXPTCL070004	Backfilling Works for Trench	13	$22,050.00	29-Mar-27	12-Apr-27	30-Aug-26		$0.00	$9,702.00	0.00
TAEXPTCL070006	Install fire hydrent	5	$22,400.00	29-Mar-27	03-Apr-27			$0.00	$0.00	0.00
TAEXPTCL070005	Install Valves with fittings	4	$9,600.00	08-Apr-27	12-Apr-27	27-Sep-26		$0.00	$1,440.00	0.00
TAEXPTCL070007	Valve Chamber works	14	$22,100.00	05-Jun-27	20-Jun-27			$0.00	$0.00	0.00
TAEXPTCL070008	Inspection Test	4	$4,005.00	21-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TSE Networks		369	$217,273.34	23-Mar-26	02-Jun-27	23-Mar-26		$141,028.34	$167,101.34	1.18
TAEXTSCL070001	Excavation works for Trench	4	$50,027.51	23-Mar-26	26-Mar-26	23-Mar-26	27-Mar-26	$50,027.51	$50,027.51	1.00
TAEXTSCL070002	Bedding Works	1	$3,375.00	15-Apr-26	15-Apr-26	15-Apr-26	15-Apr-26	$3,375.00	$3,375.00	1.00
TAEXTSCL070003	Install Pipes & Fittings	5	$54,225.00	15-Apr-26	20-Apr-26	15-Apr-26	20-Apr-26	$54,225.00	$54,225.00	1.00
TAEXTSCL070004	Backfilling Works for Trench	9	$16,725.00	21-Apr-26	30-Apr-26	21-Apr-26	30-Apr-26	$16,725.00	$16,725.00	1.00
TAEXTSCL0700011	Excavation works for Trench Part 01	4	$16,675.83	21-Jun-26	24-Jun-26	29-Oct-26	31-Oct-26	$16,675.83	$16,675.83	1.00
TAEXTSCL0700021	Bedding Works Part 01	1	$1,125.00	17-Jan-27	17-Jan-27	31-Oct-26	31-Oct-26	$0.00	$1,125.00	0.00
TAEXTSCL0700031	Install Pipes & Fittings Part 01	5	$18,075.00	18-Jan-27	23-Jan-27	01-Nov-26	01-Nov-26	$0.00	$18,075.00	0.00
TAEXTSCL0700041	Backfilling Works for Trench Part 01	8	$5,575.00	24-Jan-27	01-Feb-27			$0.00	$0.00	0.00
TAEXTSCL070005	Install Valves with fittings	4	$7,200.00	08-May-27	11-May-27	27-Sep-26		$0.00	$1,080.00	0.00
TAEXTSCL070006	Valve Chamber works	15	$38,620.00	12-May-27	29-May-27	27-Sep-26		$0.00	$5,793.00	0.00
TAEXTSCL070007	Inspection Test	4	$5,650.00	30-May-27	02-Jun-27			$0.00	$0.00	0.00
Sewerage Networks		89	$358,750.60	15-Dec-26	02-Mar-27	09-Jun-26	31-Oct-26	$0.00	$358,750.60	0.00
TAEXSWCL070001	Excavation works for Trench	28	$64,670.00	15-Dec-26	16-Jan-27	09-Jun-26	10-Oct-26	$0.00	$64,670.00	0.00
TAEXSWCL070002	Bedding Works	3	$26,944.45	17-Jan-27	19-Jan-27	29-Aug-26	10-Oct-26	$0.00	$26,944.45	0.00
TAEXSWCL070003	Install GRP Pipes & Fittings	8	$98,700.00	20-Jan-27	28-Jan-27	30-Aug-26	17-Oct-26	$0.00	$98,700.00	0.00
TAEXSWCL070004	Backfilling Works for Trench	14	$70,350.00	31-Jan-27	15-Feb-27	22-Oct-26	25-Oct-26	$0.00	$70,350.00	0.00
TAEXSWCL070005	Manhole Installation with backfilling	12	$74,650.00	14-Feb-27	27-Feb-27	10-Sep-26	25-Oct-26	$0.00	$74,650.00	0.00
TAEXSWCL070006	Leakage Test	3	$23,436.15	28-Feb-27	02-Mar-27	27-Oct-26	31-Oct-26	$0.00	$23,436.15	0.00
Storm Networks		320	$965,725.28	15-Feb-26	22-Feb-27	15-Feb-26		$864,325.28	$721,985.28	0.84
TAEXSTCL070001	Excavation works for Trench	6	$150,896.00	15-Feb-26	21-Feb-26	15-Feb-26	21-Feb-26	$150,896.00	$150,896.00	1.00
TAEXSTCL070002	Bedding Works	1	$67,156.22	05-Mar-26	05-Mar-26	05-Mar-26	06-Mar-26	$67,156.22	$67,156.22	1.00
TAEXSTCL070003	Install GRP Pipes & Fittings	6	$223,972.50	14-Mar-26	19-Mar-26	14-Mar-26	19-Mar-26	$223,972.50	$223,972.50	1.00
TAEXSTCL070004	Backfilling Works for Trench	10	$145,125.00	04-Apr-26	14-Apr-26	04-Apr-26	14-Apr-26	$145,125.00	$145,125.00	1.00
TAEXSTCL070005	Manhole Installation with backfilling	10	$74,722.50	12-Apr-26	22-Apr-26	12-Apr-26	22-Apr-26	$74,722.50	$74,722.50	1.00

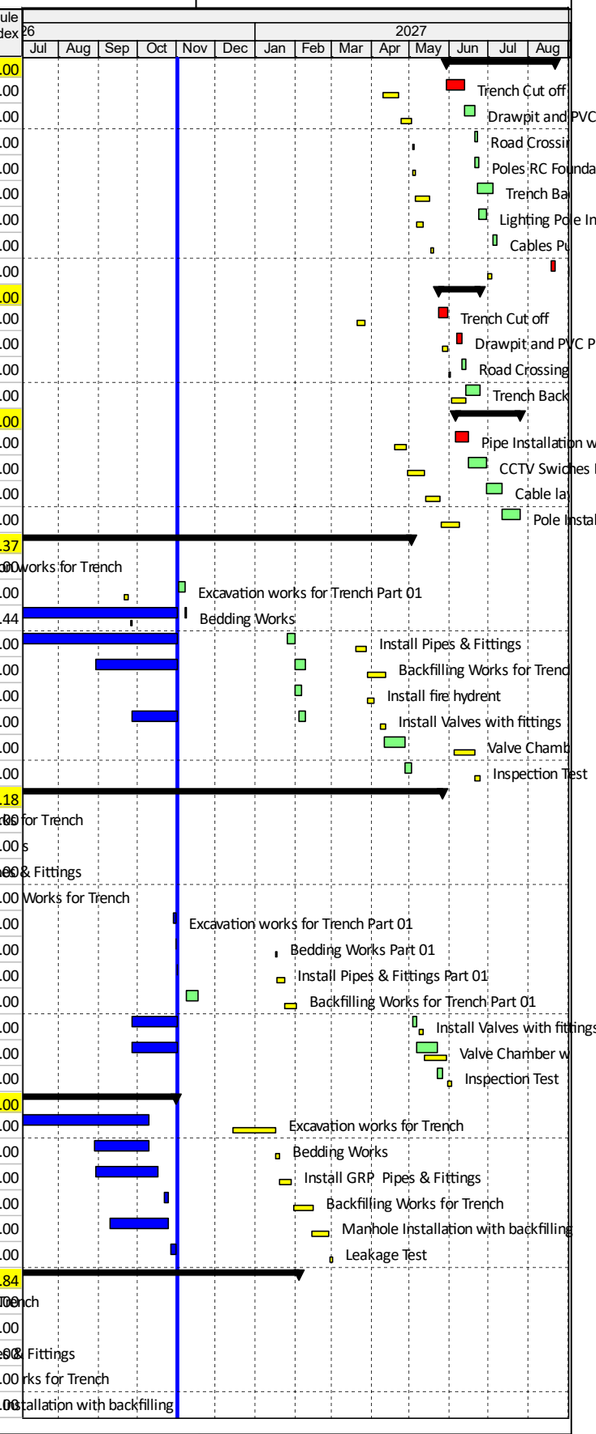


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXSTCL0700011	Excavation works for Trench Part 01	4	$37,724.00	15-Aug-26	18-Aug-26	29-Oct-26	31-Oct-26	$37,724.00	$37,724.00	1.00
TAEXSTCL0700021	Bedding Works Part 01	1	$16,789.06	19-Aug-26	19-Aug-26	01-Nov-26	01-Nov-26	$16,789.06	$16,789.06	1.00
TAEXSTCL0700031	Install GRP Pipes & Fittings Part 01	5	$74,657.50	20-Aug-26	25-Aug-26			$74,657.50	$0.00	0.00
TAEXSTCL0700041	Backfilling Works for Trench Part 01	8	$48,375.00	03-Sep-26	12-Sep-26			$48,375.00	$0.00	0.00
TAEXSTCL0700051	Manhole Installation with backfilling Part 01	5	$24,907.50	20-Oct-26	25-Oct-26			$24,907.50	$0.00	0.00
TAEXSTCL070006	Install Catch Basin with UPVC Pipes & Fittings	10	$90,200.00	08-Feb-27	18-Feb-27			$0.00	$0.00	0.00
TAEXSTCL070007	Leakage Test	3	$11,200.00	20-Feb-27	22-Feb-27	17-Oct-26		$0.00	$5,600.00	0.00
Local Road 08		505	$5,152,236.17	12-Jan-26	31-Jul-27	12-Jan-26		$1,343,762.72	$1,694,411.71	1.26
Road Works		484	$3,063,374.16	12-Jan-26	31-Jul-27	12-Jan-26		$364,786.28	$464,186.28	1.27
TAEXRDCL080001	Road Excavation and Disposal	8	$115,226.10	12-Jan-26	20-Jan-26	12-Jan-26	20-Jan-26	$115,226.10	$115,226.10	1.00
TAEXRDCL080002	Backfilling Works for Road	8	$181,520.60	29-Jan-26	07-Feb-26	29-Jan-26	07-Feb-26	$181,520.60	$181,520.60	1.00
TAEXRDCL080003	Subgrade Works	4	$68,039.58	08-Feb-26	11-Feb-26	08-Feb-26	11-Feb-26	$68,039.58	$68,039.58	1.00
TAEXRDCL080000	Asphalt Milling and Deisposal	4	$99,400.00	14-Mar-27	17-Mar-27	25-Jul-26	26-Jul-26	$0.00	$99,400.00	0.00
TAEXRDCL0800011	Road Excavation and Disposal Part 01	5	$1,163.90	18-Mar-27	23-Mar-27			$0.00	$0.00	0.00
TAEXRDCL0800021	Backfilling Works for Road Part 01	7	$15,784.40	24-Mar-27	31-Mar-27			$0.00	$0.00	0.00
TAEXRDCL0800031	Subgrade Works Part 01	4	$68,039.58	01-Apr-27	05-Apr-27			$0.00	$0.00	0.00
TAEXRDCL080004	ABC aggregate Base Course Works	4	$655,786.00	06-Apr-27	10-Apr-27			$0.00	$0.00	0.00
TAEXRDCL080005	MBC1 layer	1	$9,832.00	11-Apr-27	11-Apr-27			$0.00	$0.00	0.00
TAEXRDCL080006	BBC Base Course	4	$1,075,760.00	12-Apr-27	15-Apr-27			$0.00	$0.00	0.00
TAEXRDCL080008	Precast Concret Kerps	14	$401,420.00	13-Jun-27	28-Jun-27			$0.00	$0.00	0.00
TAEXRDCL080007	BWC Asphalt Wearing Course with RC	1	$111,511.00	29-Jun-27	29-Jun-27			$0.00	$0.00	0.00
TAEXRDCL080009	Precast Interlock Works	17	$175,671.00	30-Jun-27	19-Jul-27			$0.00	$0.00	0.00
TAEXRDCL080010	Stone Paving works	7	$38,120.00	20-Jul-27	27-Jul-27			$0.00	$0.00	0.00
TAEXRDCL080011	Road Marking	1	$4,100.00	28-Jul-27	28-Jul-27			$0.00	$0.00	0.00
TAEXRDCL080012	Traffic Sinage	2	$42,000.00	29-Jul-27	31-Jul-27			$0.00	$0.00	0.00
Electrical Works		63	$362,566.25	24-Apr-27	05-Jul-27	01-Sep-26		$0.00	$80,000.00	0.00
TAEXELCL080001	Trench Cut off	10	$27,926.25	24-Apr-27	04-May-27			$0.00	$0.00	0.00
TAEXELCL080002	Drawpit and PVC Pipes Installation	5	$5,280.00	05-May-27	10-May-27			$0.00	$0.00	0.00
TAEXELCL080003	Road Crossing Ducts	2	$260.00	11-May-27	12-May-27			$0.00	$0.00	0.00
TAEXELCL080006	Poles RC Foundation	4	$12,500.00	11-May-27	15-May-27			$0.00	$0.00	0.00
TAEXELCL080004	Trench Backfilling	14	$14,230.00	13-May-27	29-May-27			$0.00	$0.00	0.00
TAEXELCL080008	Lighting Pole Installation with Luminares	6	$52,050.00	16-May-27	22-May-27			$0.00	$0.00	0.00
TAEXELCL080005	Cables Pulling	3	$168,000.00	30-May-27	01-Jun-27			$0.00	$0.00	0.00
TAEXELCL080009	Install Substation & RMU	9	$80,000.00	02-Jun-27	12-Jun-27	01-Sep-26	02-Sep-26	$0.00	$80,000.00	0.00
TAEXELCL080007	Earthing cables	2	$2,320.00	04-Jul-27	05-Jul-27			$0.00	$0.00	0.00
Telecommunication Works		31	$156,215.00	28-Mar-27	23-Jun-27			$0.00	$0.00	0.00
TAEXTCCL080001	Trench Cut off	10	$15,230.00	28-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXTCCL080002	Drawpit and PVC Pipes Installation	5	$100,235.00	31-May-27	05-Jun-27			$0.00	$0.00	0.00
TAEXTCCL080003	Road Crossing Ducts	2	$8,600.00	06-Jun-27	07-Jun-27			$0.00	$0.00	0.00
TAEXTCCL080004	Trench Backfilling	14	$32,150.00	08-Jun-27	23-Jun-27			$0.00	$0.00	0.00
CCTV Works		46	$52,061.00	29-Apr-27	21-Jun-27			$0.00	$0.00	0.00
TAEXCCCL080001	Pipe Installation with manhole	8	$25,094.00	29-Apr-27	08-May-27			$0.00	$0.00	0.00
TAEXCCCL080002	CCTV Swiches Lighting panels Installation	13	$2,578.00	09-May-27	23-May-27			$0.00	$0.00	0.00
TAEXCCCL080003	Cable laying and connected with Panels	10	$19,654.00	24-May-27	03-Jun-27			$0.00	$0.00	0.00
TAEXCCCL080004	Pole Installation with IP Outdoor CCTV POE Camera	15	$4,735.00	05-Jun-27	21-Jun-27			$0.00	$0.00	0.00
Potable Networks		212	$251,192.54	17-Oct-26	13-Jul-27	23-Aug-26		$74,195.54	$123,836.66	1.67
TAEXPTCL080001	Excavation works for Trench	8	$51,459.62	17-Oct-26	25-Oct-26	23-Aug-26		$51,459.62	$38,594.71	0.75
TAEXPTCL080002	Bedding Works	2	$22,735.92	26-Oct-26	27-Oct-26	26-Sep-26		$22,735.92	$17,051.94	0.75
TAEXPTCL080003	Install Pipes & Fittings	8	$78,112.00	29-Mar-27	06-Apr-27	26-Sep-26		$0.00	$58,584.00	0.00
TAEXPTCL080004	Backfilling Works for Trench	15	$28,350.00	07-Apr-27	24-Apr-27			$0.00	$0.00	0.00
TAEXPTCL080006	Install fire hydrent	6	$24,000.00	26-Apr-27	02-May-27	27-Sep-26		$0.00	$3,600.00	0.00
TAEXPTCL080005	Install Valves with fittings	4	$12,500.00	01-May-27	04-May-27			$0.00	$0.00	0.00
TAEXPTCL080007	Valve Chamber works	16	$30,030.00	21-Jun-27	08-Jul-27	27-Sep-26		$0.00	$6,006.00	0.00
TAEXPTCL080008	Inspection Test	4	$4,005.00	10-Jul-27	13-Jul-27			$0.00	$0.00	0.00

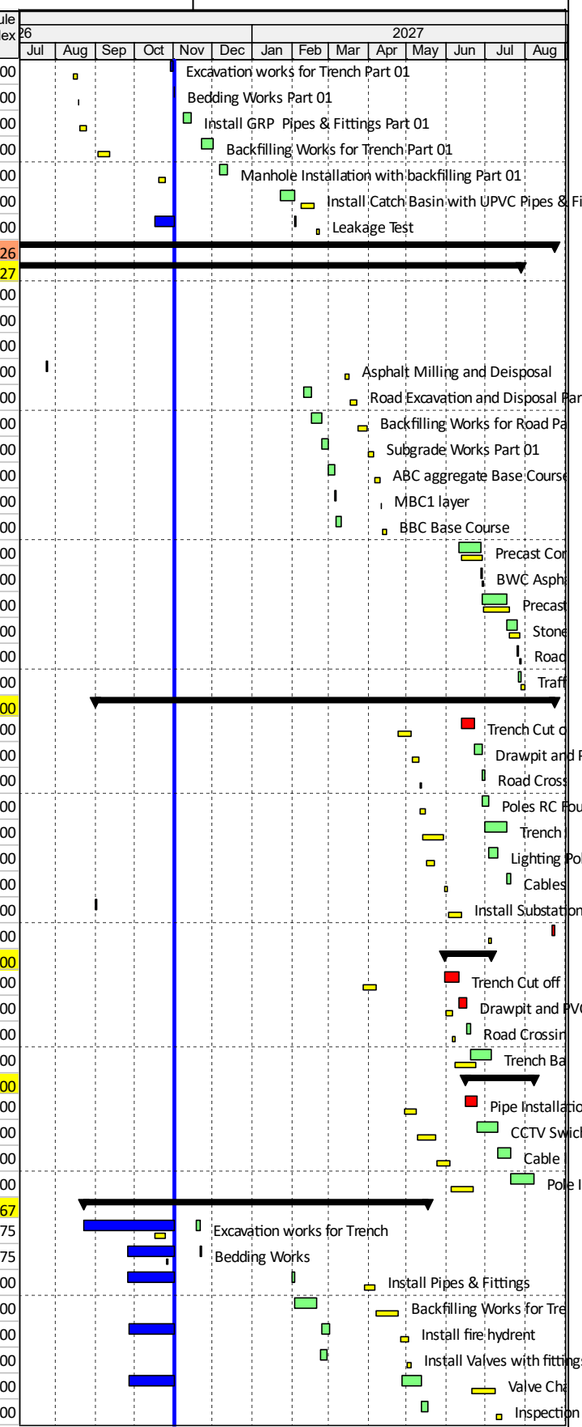


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TSE Networks		197	$228,923.34	20-Aug-26	18-Jul-27	04-Aug-26		$78,503.34	$97,592.00	1.24
TAEXTSCL080001	Excavation works for Trench	8	$72,903.34	20-Aug-26	29-Aug-26	04-Aug-26		$72,903.34	$43,742.00	0.60
TAEXTSCL080002	Bedding Works	2	$5,600.00	28-Oct-26	29-Oct-26	17-Oct-26		$5,600.00	$3,360.00	0.60
TAEXTSCL080003	Install Pipes & Fittings	8	$72,300.00	24-Jan-27	01-Feb-27	17-Oct-26		$0.00	$43,380.00	0.00
TAEXTSCL080004	Backfilling Works for Trench	15	$25,300.00	02-Feb-27	18-Feb-27			$0.00	$0.00	0.00
TAEXTSCL080005	Install Valves with fittings	4	$7,150.00	15-Feb-27	18-Feb-27	27-Sep-26		$0.00	$1,072.50	0.00
TAEXTSCL080006	Valve Chamber works	16	$40,250.00	20-Feb-27	09-Mar-27	27-Sep-26		$0.00	$6,037.50	0.00
TAEXTSCL080007	Inspection Test	4	$5,420.00	14-Jul-27	18-Jul-27			$0.00	$0.00	0.00
Sewerage Networks		278	$255,270.60	19-Feb-26	07-Mar-27	19-Feb-26		$146,094.28	$247,629.39	1.69
TAEXSWCL080001	Excavation works for Trench	8	$52,416.00	19-Feb-26	28-Feb-26	19-Feb-26	28-Feb-26	$52,416.00	$52,416.00	1.00
TAEXSWCL080002	Bedding Works	2	$22,987.78	31-Mar-26	01-Apr-26	31-Mar-26	01-Apr-26	$22,987.78	$22,987.78	1.00
TAEXSWCL080003	Install GRP Pipes & Fittings	6	$38,962.50	01-Apr-26	07-Apr-26	01-Apr-26	07-Apr-26	$38,962.50	$38,962.50	1.00
TAEXSWCL080004	Backfilling Works for Trench	6	$9,024.00	04-Apr-26	09-Apr-26	04-Apr-26	09-Apr-26	$9,024.00	$9,024.00	1.00
TAEXSWCL080005	Manhole Installation with backfilling	5	$22,704.00	11-Apr-26	15-Apr-26	11-Apr-26	15-Apr-26	$22,704.00	$22,704.00	1.00
TAEXSWCL0800011	Excavation works for Trench Part 01	10	$2,184.00	17-Jan-27	27-Jan-27	08-Jun-26	21-Jun-26	$0.00	$2,184.00	0.00
TAEXSWCL0800021	Bedding Works Part 01	1	$4,056.67	28-Jan-27	28-Jan-27	02-Jul-26	06-Sep-26	$0.00	$4,056.67	0.00
TAEXSWCL0800031	Install GRP Pipes & Fittings Part 01	4	$12,987.50	30-Jan-27	02-Feb-27	02-Jul-26	13-Sep-26	$0.00	$12,987.50	0.00
TAEXSWCL0800041	Backfilling Works for Trench Part 01	10	$13,536.00	09-Feb-27	20-Feb-27	06-Jun-26	04-Oct-26	$0.00	$13,536.00	0.00
TAEXSWCL0800051	Manhole Installation with backfilling Part 01	10	$52,976.00	21-Feb-27	03-Mar-27	28-Jul-26		$0.00	$47,678.40	0.00
TAEXSWCL080006	Leakage Test	3	$23,436.15	04-Mar-27	07-Mar-27	18-Jul-26		$0.00	$21,092.54	0.00
Storm Networks		276	$782,633.28	15-Feb-26	16-Jan-27	15-Feb-26		$680,183.28	$681,167.39	1.00
TAEXSTCL080001	Excavation works for Trench	10	$188,708.80	15-Feb-26	25-Feb-26	15-Feb-26	25-Feb-26	$188,708.80	$188,708.80	1.00
TAEXSTCL080002	Bedding Works	2	$82,266.37	05-Mar-26	07-Mar-26	05-Mar-26	07-Mar-26	$82,266.37	$82,266.37	1.00
TAEXSTCL080003	Install GRP Pipes & Fittings	7	$192,525.10	01-Apr-26	08-Apr-26	01-Apr-26	08-Apr-26	$192,525.10	$192,525.10	1.00
TAEXSTCL080004	Backfilling Works for Trench	6	$91,029.00	04-Apr-26	09-Apr-26	04-Apr-26	09-Apr-26	$91,029.00	$91,029.00	1.00
TAEXSTCL080005	Manhole Installation with backfilling	5	$31,560.00	11-Apr-26	15-Apr-26	11-Apr-26	15-Apr-26	$31,560.00	$31,560.00	1.00
TAEXSTCL0800011	Excavation works for Trench Part 01	5	$3,851.20	30-Aug-26	03-Sep-26	12-Sep-26	10-Oct-26	$3,851.20	$3,851.20	1.00
TAEXSTCL0800021	Bedding Works Part 01	1	$1,678.91	05-Sep-26	05-Sep-26	12-Sep-26	17-Oct-26	$1,678.91	$1,678.91	1.00
TAEXSTCL0800031	Install GRP Pipes & Fittings Part 01	7	$10,132.90	06-Sep-26	13-Sep-26	17-Oct-26		$10,132.90	$9,119.61	0.90
TAEXSTCL0800041	Backfilling Works for Trench Part 01	7	$4,791.00	23-Sep-26	30-Sep-26	17-Oct-26		$4,791.00	$4,311.90	0.90
TAEXSTCL0800051	Manhole Installation with backfilling Part 01	10	$73,640.00	20-Oct-26	31-Oct-26	06-Jun-26		$73,640.00	$62,594.00	0.85
TAEXSTCL080006	Install Catch Basin with UPVC Pipes & Fittings	11	$91,250.00	02-Dec-26	14-Dec-26	31-Oct-26		$0.00	$4,562.50	0.00
TAEXSTCL080007	Leakage Test	3	$11,200.00	13-Jan-27	16-Jan-27	12-Jul-26		$0.00	$8,960.00	0.00
Local Road 09		579	$3,820,653.17	20-Oct-25	02-Aug-27	20-Oct-25		$1,514,709.77	$1,654,208.92	1.09
Road Works		558	$2,037,671.16	20-Oct-25	02-Aug-27	20-Oct-25		$518,053.16	$518,053.16	1.00
TAEXRDCL090001	Road Excavation and Disposal	25	$281,473.00	20-Oct-25	17-Nov-25	20-Oct-25	17-Nov-25	$281,473.00	$281,473.00	1.00
TAEXRDCL090002	Backfilling Works for Road	2	$140,932.00	15-Dec-25	16-Dec-25	15-Dec-25	16-Dec-25	$140,932.00	$140,932.00	1.00
TAEXRDCL090003	Subgrade Works	15	$95,648.16	04-Jan-26	20-Jan-26	04-Jan-26	20-Jan-26	$95,648.16	$95,648.16	1.00
TAEXRDCL090004	ABC aggregate Base Course Works	5	$222,366.00	20-Feb-27	24-Feb-27			$0.00	$0.00	0.00
TAEXRDCL090005	MBC1 layer	1	$2,458.00	25-Feb-27	25-Feb-27			$0.00	$0.00	0.00
TAEXRDCL090006	BBC Base Course	2	$404,278.00	27-Feb-27	28-Feb-27			$0.00	$0.00	0.00
TAEXRDCL090008	Precast Concret Kerps	13	$271,311.00	29-Jun-27	13-Jul-27			$0.00	$0.00	0.00
TAEXRDCL090007	BWC Asphalt Wearing Course with RC	1	$111,511.00	14-Jul-27	14-Jul-27			$0.00	$0.00	0.00
TAEXRDCL090009	Precast Interlock Works	12	$449,144.00	15-Jul-27	28-Jul-27			$0.00	$0.00	0.00
TAEXRDCL090010	Stone Paving works	2	$21,000.00	29-Jul-27	31-Jul-27			$0.00	$0.00	0.00
TAEXRDCL090011	Road Marking	1	$4,100.00	01-Aug-27	01-Aug-27			$0.00	$0.00	0.00
TAEXRDCL090012	Traffic Sinage	1	$33,450.00	02-Aug-27	02-Aug-27			$0.00	$0.00	0.00
Electrical Works		55	$264,866.25	05-May-27	07-Jul-27			$0.00	$0.00	0.00
TAEXELCL090001	Trench Cut off	11	$30,186.25	05-May-27	17-May-27			$0.00	$0.00	0.00
TAEXELCL090002	Drawpit and PVC Pipes Installation	9	$4,560.00	18-May-27	27-May-27			$0.00	$0.00	0.00
TAEXELCL090003	Road Crossing Ducts	2	$260.00	29-May-27	30-May-27			$0.00	$0.00	0.00
TAEXELCL090006	Poles RC Foundation	3	$9,510.00	29-May-27	31-May-27			$0.00	$0.00	0.00
TAEXELCL090004	Trench Backfilling	10	$10,530.00	31-May-27	10-Jun-27			$0.00	$0.00	0.00
TAEXELCL090008	Lighting Pole Installation with Luminares	4	$91,500.00	01-Jun-27	05-Jun-27			$0.00	$0.00	0.00

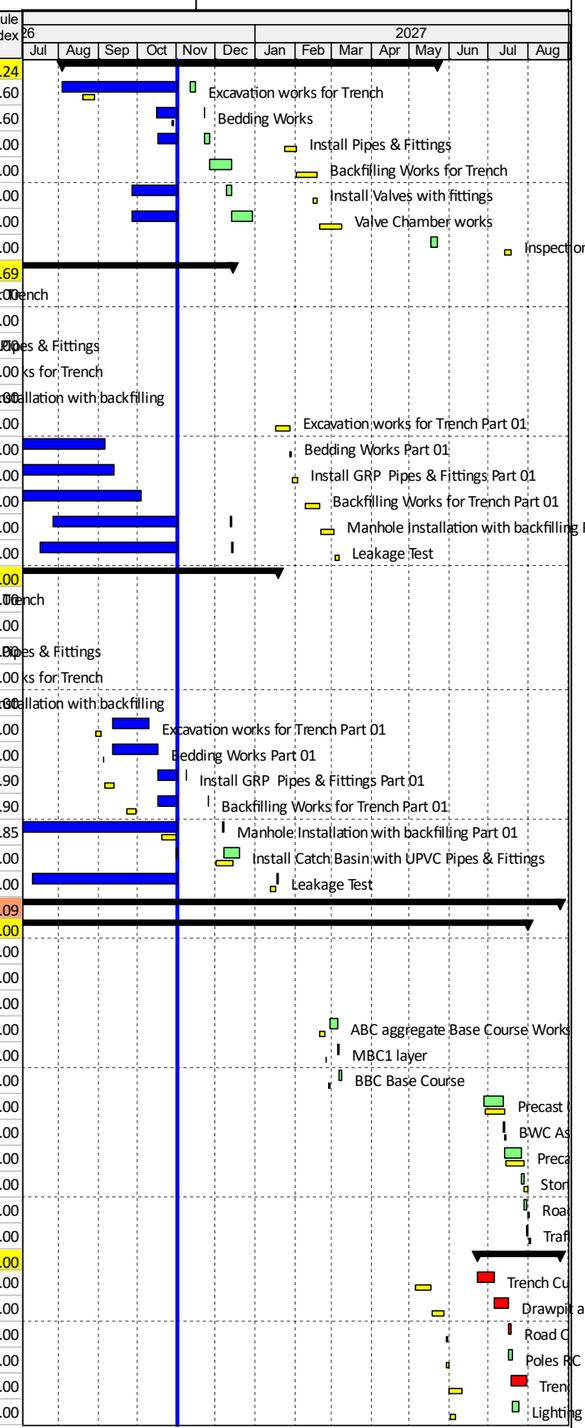


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXELCL090005	Cables Pulling	2	$116,000.00	12-Jun-27	13-Jun-27			$0.00	$0.00	0.00
TAEXELCL090007	Earthing cables	2	$2,320.00	06-Jul-27	07-Jul-27			$0.00	$0.00	0.00
Telecommunication Works		21	$122,780.00	08-Apr-27	23-Jun-27			$0.00	$0.00	0.00
TAEXTCCL090001	Trench Cut off	5	$7,500.00	08-Apr-27	13-Apr-27			$0.00	$0.00	0.00
TAEXTCCL090002	Drawpit and PVC Pipes Installation	4	$80,250.00	06-Jun-27	09-Jun-27			$0.00	$0.00	0.00
TAEXTCCL090003	Road Crossing Ducts	2	$8,600.00	10-Jun-27	12-Jun-27			$0.00	$0.00	0.00
TAEXTCCL090004	Trench Backfilling	10	$26,430.00	13-Jun-27	23-Jun-27			$0.00	$0.00	0.00
CCTV Works		37	$52,325.00	09-May-27	20-Jun-27			$0.00	$0.00	0.00
TAEXCCCL090001	Pipe Installation with manhole	7	$23,144.00	09-May-27	16-May-27			$0.00	$0.00	0.00
TAEXCCCL090002	CCTV Swiches Lighting panels Installation	10	$2,515.00	17-May-27	27-May-27			$0.00	$0.00	0.00
TAEXCCCL090003	Cable laying and connected with Panels	8	$22,767.00	29-May-27	06-Jun-27			$0.00	$0.00	0.00
TAEXCCCL090004	Pole Installation with IP Outdoor CCTV POE Camera	12	$3,899.00	07-Jun-27	20-Jun-27			$0.00	$0.00	0.00
Potable Networks		373	$246,105.54	23-Mar-26	28-Jul-27	23-Mar-26		$183,004.04	$189,430.54	1.04
TAEXPTCL090001	Excavation works for Trench	4	$61,806.64	23-Mar-26	26-Mar-26	23-Mar-26	26-Mar-26	$61,806.64	$61,806.64	1.00
TAEXPTCL090002	Bedding Works	1	$19,325.53	14-Apr-26	14-Apr-26	14-Apr-26	14-Apr-26	$19,325.53	$19,325.53	1.00
TAEXPTCL090003	Install Pipes & Fittings	2	$65,025.00	16-Apr-26	18-Apr-26	16-Apr-26	18-Apr-26	$65,025.00	$65,025.00	1.00
TAEXPTCL090004	Backfilling Works for Trench	9	$18,708.50	21-Apr-26	30-Apr-26	21-Apr-26	30-Apr-26	$18,708.50	$18,708.50	1.00
TAEXPTCL0900011	Excavation works for Trench Part 01	3	$3,252.98	17-Sep-26	20-Sep-26	06-Aug-26	09-Aug-26	$3,252.98	$3,252.98	1.00
TAEXPTCL0900021	Bedding Works Part 01	6	$3,410.39	21-Sep-26	27-Sep-26	06-Jun-26	09-Aug-26	$3,410.39	$3,410.39	1.00
TAEXPTCL0900031	Install Pipes & Fittings Part 01	6	$11,475.00	28-Sep-26	04-Oct-26	11-Jun-26	09-Aug-26	$11,475.00	$11,475.00	1.00
TAEXPTCL0900041	Backfilling Works for Trench Part 01	10	$3,301.50	23-Feb-27	06-Mar-27	15-Jun-26	09-Aug-26	$0.00	$3,301.50	0.00
TAEXPTCL090006	Install fire hydrent	6	$24,000.00	04-Apr-27	10-Apr-27			$0.00	$0.00	0.00
TAEXPTCL090005	Install Valves with fittings	3	$12,500.00	13-Apr-27	15-Apr-27	04-Oct-26		$0.00	$3,125.00	0.00
TAEXPTCL090007	Valve Chamber works	14	$20,050.00	10-Jul-27	25-Jul-27			$0.00	$0.00	0.00
TAEXPTCL090008	Inspection Test	3	$3,250.00	26-Jul-27	28-Jul-27			$0.00	$0.00	0.00
TSE Networks		347	$182,133.34	26-Apr-26	26-May-27	26-Apr-26		$62,603.34	$123,433.34	1.97
TAEXTSCL090001	Excavation works for Trench	4	$51,303.00	26-Apr-26	29-Apr-26	26-Apr-26	29-Apr-26	$51,303.00	$51,303.00	1.00
TAEXTSCL0900011	Excavation works for Trench Part 01	12	$5,700.34	25-Jun-26	08-Jul-26	29-Oct-26	29-Oct-26	$5,700.34	$5,700.34	1.00
TAEXTSCL090002	Bedding Works	2	$5,600.00	09-Jul-26	11-Jul-26	31-Oct-26	31-Oct-26	$5,600.00	$5,600.00	1.00
TAEXTSCL090003	Install Pipes & Fittings	6	$54,580.00	02-Feb-27	08-Feb-27	31-Oct-26	31-Oct-26	$0.00	$54,580.00	0.00
TAEXTSCL090004	Backfilling Works for Trench	12	$20,100.00	09-Feb-27	22-Feb-27			$0.00	$0.00	0.00
TAEXTSCL090005	Install Valves with fittings	3	$5,200.00	04-May-27	06-May-27	04-Oct-26		$0.00	$2,600.00	0.00
TAEXTSCL090006	Valve Chamber works	14	$36,000.00	08-May-27	23-May-27			$0.00	$0.00	0.00
TAEXTSCL090007	Inspection Test	3	$3,650.00	24-May-27	26-May-27	31-Oct-26	31-Oct-26	$0.00	$3,650.00	0.00
Sewerage Networks		259	$263,496.60	08-Feb-26	12-Apr-27	08-Feb-26	30-Oct-26	$209,076.45	$263,496.60	1.26
TAEXSWCL090001	Excavation works for Trench	43	$40,058.00	08-Feb-26	29-Mar-26	08-Feb-26	29-Mar-26	$40,058.00	$40,058.00	1.00
TAEXSWCL090002	Bedding Works	4	$24,294.45	29-Mar-26	01-Apr-26	29-Mar-26	01-Apr-26	$24,294.45	$24,294.45	1.00
TAEXSWCL090003	Install GRP Pipes & Fittings	21	$95,755.00	01-Apr-26	25-Apr-26	01-Apr-26	25-Apr-26	$95,755.00	$95,755.00	1.00
TAEXSWCL090004	Backfilling Works for Trench	10	$17,717.50	05-Apr-26	15-Apr-26	05-Apr-26	15-Apr-26	$17,717.50	$17,717.50	1.00
TAEXSWCL090005	Manhole Installation with backfilling	6	$31,251.50	11-Apr-26	16-Apr-26	11-Apr-26	17-Apr-26	$31,251.50	$31,251.50	1.00
TAEXSWCL0900041	Backfilling Works for Trench Part 01	8	$932.50	31-Mar-27	08-Apr-27	24-Oct-26	30-Oct-26	$0.00	$932.50	0.00
TAEXSWCL0900051	Manhole Installation with backfilling Part 01	6	$31,251.50	03-Apr-27	08-Apr-27	10-Oct-26	25-Oct-26	$0.00	$31,251.50	0.00
TAEXSWCL090006	Leakage Test	3	$22,236.15	10-Apr-27	12-Apr-27	18-Jul-26	17-Oct-26	$0.00	$22,236.15	0.00
Storm Networks		283	$651,275.28	10-Feb-26	28-Dec-26	10-Feb-26		$541,972.78	$559,795.28	1.03
TAEXSTCL090001	Excavation works for Trench	89	$182,520.00	10-Feb-26	24-May-26	10-Feb-26	24-May-26	$182,520.00	$182,520.00	1.00
TAEXSTCL090002	Bedding Works	1	$73,335.52	07-May-26	07-May-26	07-May-26	07-May-26	$73,335.52	$73,335.52	1.00
TAEXSTCL0900021	Bedding Works Part 01	1	$3,859.76	06-Sep-26	06-Sep-26	04-Jun-26	06-Jun-26	$3,859.76	$3,859.76	1.00
TAEXSTCL090003	Install GRP Pipes & Fittings	8	$98,630.00	07-Sep-26	15-Sep-26	04-Jun-26	06-Jun-26	$98,630.00	$98,630.00	1.00
TAEXSTCL090004	Backfilling Works for Trench	13	$92,300.00	19-Sep-26	03-Oct-26	24-Jun-26	08-Aug-26	$92,300.00	$92,300.00	1.00
TAEXSTCL090005	Manhole Installation with backfilling	12	$99,630.00	20-Oct-26	02-Nov-26	13-Jun-26	30-Oct-26	$91,327.50	$99,630.00	1.09
TAEXSTCL090006	Install Catch Basin with UPVC Pipes & Fittings	9	$89,800.00	15-Dec-26	24-Dec-26			$0.00	$0.00	0.00
TAEXSTCL090007	Leakage Test	3	$11,200.00	26-Dec-26	28-Dec-26	08-Aug-26		$0.00	$9,520.00	0.00
Upgrade Local 06		45	$440,739.00	02-Jun-27	20-Jul-27	10-Oct-26		$0.00	$2,425.50	0.00
Electrical Works		32	$388,980.00	10-Jun-27	20-Jul-27	10-Oct-26		$0.00	$2,425.50	0.00

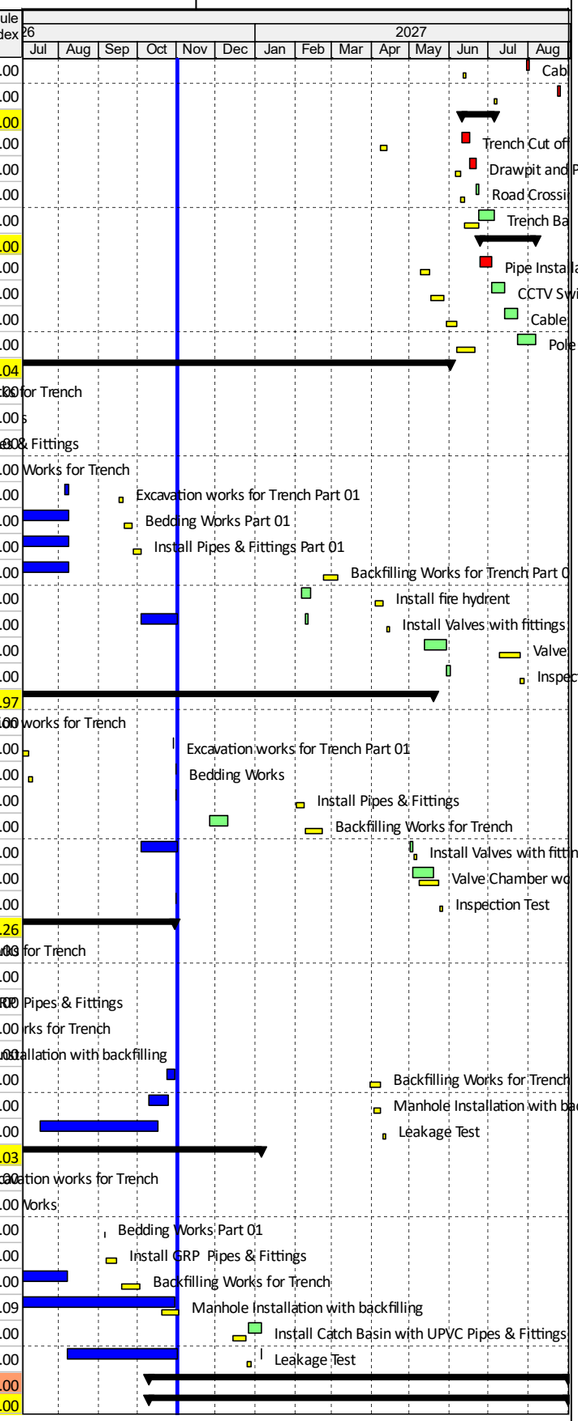


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXELCU060001	Trench Cut off	10	$10,530.00	10-Jun-27	21-Jun-27			$0.00	$0.00	0.00
TAEXELCU060002	Drawpit and PVC Pipes Installation	6	$7,000.00	22-Jun-27	28-Jun-27	10-Oct-26		$0.00	$2,310.00	0.00
TAEXELCU060003	Road Crossing Ducts	3	$350.00	29-Jun-27	01-Jul-27	10-Oct-26		$0.00	$115.50	0.00
TAEXELCU060006	Poles RC Foundation	4	$12,500.00	29-Jun-27	03-Jul-27			$0.00	$0.00	0.00
TAEXELCU060004	Trench Backfilling	10	$10,230.00	03-Jul-27	13-Jul-27			$0.00	$0.00	0.00
TAEXELCU060008	Lighting Pole Installation with Luminares	6	$122,050.00	04-Jul-27	10-Jul-27			$0.00	$0.00	0.00
TAEXELCU060005	Cables Pulling	4	$224,000.00	14-Jul-27	18-Jul-27			$0.00	$0.00	0.00
TAEXELCU060007	Earthing cables	2	$2,320.00	19-Jul-27	20-Jul-27			$0.00	$0.00	0.00
CCTV Works		37	$51,759.00	02-Jun-27	14-Jul-27			$0.00	$0.00	0.00
TAEXCCCU060001	Pipe Installation with manhole	8	$23,144.00	02-Jun-27	10-Jun-27			$0.00	$0.00	0.00
TAEXCCCU060002	CCTV Swiches Lighting panels Installation	10	$2,515.00	12-Jun-27	22-Jun-27			$0.00	$0.00	0.00
TAEXCCCU060003	Cable laying and connected with Panels	9	$19,654.00	23-Jun-27	03-Jul-27			$0.00	$0.00	0.00
TAEXCCCU060004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	04-Jul-27	14-Jul-27			$0.00	$0.00	0.00
Upgrade Local 07		44	$343,019.00	12-Jun-27	24-Jul-27	22-Aug-26		$0.00	$2,420.90	0.00
Electrical Works		44	$291,260.00	22-Jun-27	24-Jul-27	22-Aug-26		$0.00	$2,420.90	0.00
TAEXELCU070001	Trench Cut off	7	$7,950.00	22-Jun-27	29-Jun-27			$0.00	$0.00	0.00
TAEXELCU070002	Drawpit and PVC Pipes Installation	5	$5,280.00	30-Jun-27	05-Jul-27	22-Aug-26		$0.00	$2,270.40	0.00
TAEXELCU070003	Road Crossing Ducts	3	$350.00	06-Jul-27	08-Jul-27	22-Aug-26		$0.00	$150.50	0.00
TAEXELCU070006	Poles RC Foundation	3	$9,510.00	06-Jul-27	08-Jul-27			$0.00	$0.00	0.00
TAEXELCU070008	Lighting Pole Installation with Luminares	5	$91,500.00	10-Jul-27	14-Jul-27			$0.00	$0.00	0.00
TAEXELCU070004	Trench Backfilling	8	$6,350.00	10-Jul-27	18-Jul-27			$0.00	$0.00	0.00
TAEXELCU070005	Cables Pulling	3	$168,000.00	19-Jul-27	21-Jul-27			$0.00	$0.00	0.00
TAEXELCU070007	Earthing cables	2	$2,320.00	22-Jul-27	24-Jul-27			$0.00	$0.00	0.00
CCTV Works		37	$51,759.00	12-Jun-27	24-Jul-27			$0.00	$0.00	0.00
TAEXCCCU070001	Pipe Installation with manhole	8	$23,144.00	12-Jun-27	20-Jun-27			$0.00	$0.00	0.00
TAEXCCCU070002	CCTV Swiches Lighting panels Installation	10	$2,515.00	21-Jun-27	01-Jul-27			$0.00	$0.00	0.00
TAEXCCCU070003	Cable laying and connected with Panels	9	$19,654.00	03-Jul-27	12-Jul-27			$0.00	$0.00	0.00
TAEXCCCU070004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	13-Jul-27	24-Jul-27			$0.00	$0.00	0.00
Upgrade Local 08		56	$343,519.00	21-Jun-27	02-Aug-27	02-Aug-26		$0.00	$12,387.50	0.00
Electrical Works		56	$291,760.00	30-Jun-27	01-Aug-27	02-Aug-26		$0.00	$12,387.50	0.00
TAEXELCU080001	Trench Cut off	7	$7,950.00	30-Jun-27	07-Jul-27	02-Aug-26		$0.00	$6,757.50	0.00
TAEXELCU080002	Drawpit and PVC Pipes Installation	5	$5,280.00	08-Jul-27	13-Jul-27	29-Aug-26	18-Oct-26	$0.00	$5,280.00	0.00
TAEXELCU080003	Road Crossing Ducts	3	$350.00	14-Jul-27	17-Jul-27	29-Aug-26	18-Oct-26	$0.00	$350.00	0.00
TAEXELCU080006	Poles RC Foundation	3	$9,510.00	14-Jul-27	17-Jul-27			$0.00	$0.00	0.00
TAEXELCU080008	Lighting Pole Installation with Luminares	5	$91,500.00	18-Jul-27	22-Jul-27			$0.00	$0.00	0.00
TAEXELCU080004	Trench Backfilling	8	$6,850.00	18-Jul-27	26-Jul-27			$0.00	$0.00	0.00
TAEXELCU080005	Cables Pulling	3	$168,000.00	27-Jul-27	29-Jul-27			$0.00	$0.00	0.00
TAEXELCU080007	Earthing cables	2	$2,320.00	31-Jul-27	01-Aug-27			$0.00	$0.00	0.00
CCTV Works		37	$51,759.00	21-Jun-27	02-Aug-27			$0.00	$0.00	0.00
TAEXCCCU080001	Pipe Installation with manhole	8	$23,144.00	21-Jun-27	29-Jun-27			$0.00	$0.00	0.00
TAEXCCCU080002	CCTV Swiches Lighting panels Installation	10	$2,515.00	30-Jun-27	11-Jul-27			$0.00	$0.00	0.00
TAEXCCCU080003	Cable laying and connected with Panels	9	$19,654.00	12-Jul-27	21-Jul-27			$0.00	$0.00	0.00
TAEXCCCU080004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	22-Jul-27	02-Aug-27			$0.00	$0.00	0.00
Upgrade Local 09		37	$343,719.00	30-Jun-27	11-Aug-27	01-Oct-26		$0.00	$5,630.00	0.00
Electrical Works		21	$291,960.00	08-Jul-27	09-Aug-27	01-Oct-26		$0.00	$5,630.00	0.00
TAEXELCU090001	Trench Cut off	7	$7,950.00	08-Jul-27	15-Jul-27			$0.00	$0.00	0.00
TAEXELCU090002	Drawpit and PVC Pipes Installation	5	$5,280.00	17-Jul-27	21-Jul-27	01-Oct-26	03-Oct-26	$0.00	$5,280.00	0.00
TAEXELCU090003	Road Crossing Ducts	3	$350.00	22-Jul-27	25-Jul-27	01-Oct-26	03-Oct-26	$0.00	$350.00	0.00
TAEXELCU090006	Poles RC Foundation	4	$9,510.00	22-Jul-27	26-Jul-27			$0.00	$0.00	0.00
TAEXELCU090004	Trench Backfilling	8	$7,500.00	26-Jul-27	03-Aug-27			$0.00	$0.00	0.00
TAEXELCU090008	Lighting Pole Installation with Luminares	5	$91,050.00	27-Jul-27	01-Aug-27			$0.00	$0.00	0.00
TAEXELCU090005	Cables Pulling	3	$168,000.00	04-Aug-27	07-Aug-27			$0.00	$0.00	0.00
TAEXELCU090007	Earthing cables	2	$2,320.00	08-Aug-27	09-Aug-27			$0.00	$0.00	0.00
CCTV Works		37	$51,759.00	30-Jun-27	11-Aug-27			$0.00	$0.00	0.00
TAEXCCCU090001	Pipe Installation with manhole	7	$23,144.00	30-Jun-27	07-Jul-27			$0.00	$0.00	0.00

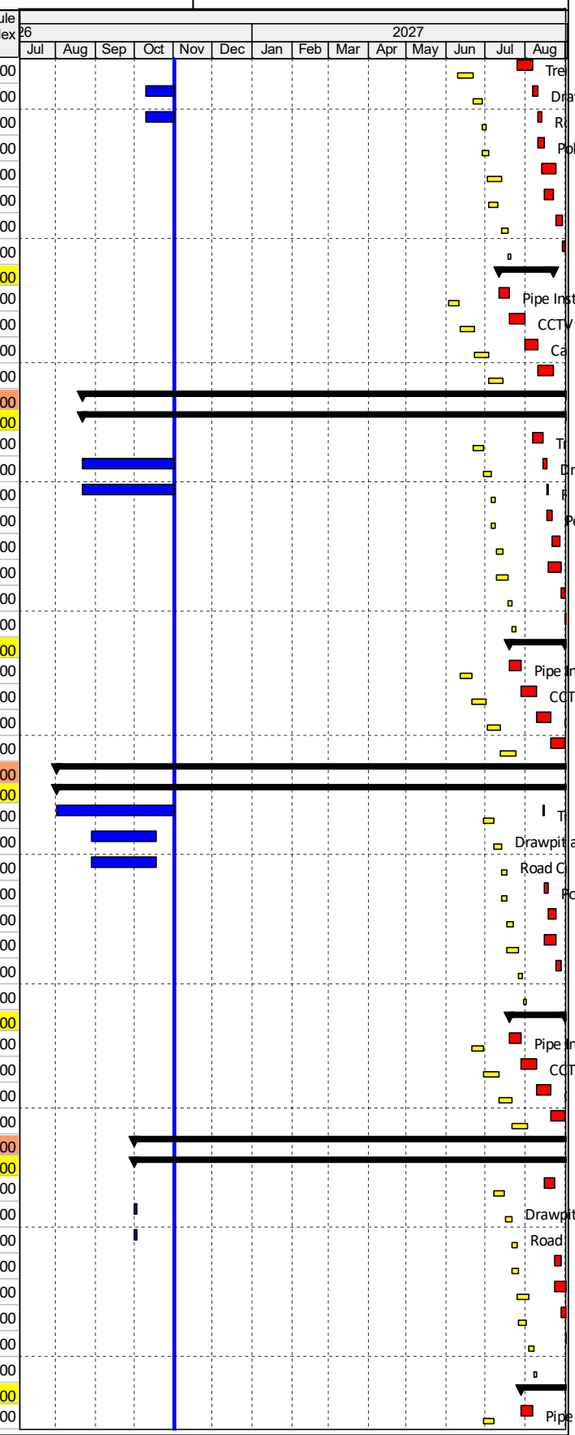


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXCCCU090002	CCTV Swiches Lighting panels Installation	10	$2,515.00	08-Jul-27	19-Jul-27			$0.00	$0.00	0.00
TAEXCCCU090003	Cable laying and connected with Panels	10	$19,654.00	20-Jul-27	31-Jul-27			$0.00	$0.00	0.00
TAEXCCCU090004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	01-Aug-27	11-Aug-27			$0.00	$0.00	0.00
Upgrade Local 12		258	$2,339,971.72	30-Nov-26	14-Aug-27	16-Jun-26		$0.00	$153,580.20	0.00
Road works		84	$212,585.00	10-Apr-27	15-Jul-27			$0.00	$0.00	0.00
TAEXRDCU120002	Precast Concret Kerps	18	$34,566.00	10-Apr-27	29-Apr-27			$0.00	$0.00	0.00
TAEXRDCU120001	BWC Asphalt Wearing Course with RC	1	$41,511.00	16-Jun-27	16-Jun-27			$0.00	$0.00	0.00
TAEXRDCU120003	Precast Interlock Works	16	$37,408.00	17-Jun-27	05-Jul-27			$0.00	$0.00	0.00
TAEXRDCU120004	Stone Paving works	5	$47,000.00	06-Jul-27	11-Jul-27			$0.00	$0.00	0.00
TAEXRDCU120005	Road Marking	1	$4,100.00	12-Jul-27	12-Jul-27			$0.00	$0.00	0.00
TAEXRDCU120006	Traffic Sinage	3	$48,000.00	13-Jul-27	15-Jul-27			$0.00	$0.00	0.00
Electrical Works		173	$563,653.00	01-Mar-27	14-Aug-27	16-Jun-26		$0.00	$136,107.70	0.00
TAEXELCU120001	Trench Cut off	12	$15,630.00	01-Mar-27	14-Mar-27	16-Jun-26		$0.00	$7,658.70	0.00
TAEXELCU120002	Drawpit and PVC Pipes Installation	9	$9,850.00	15-Mar-27	24-Mar-27	25-Jul-26		$0.00	$7,781.50	0.00
TAEXELCU120003	Road Crossing Ducts	4	$450.00	25-Mar-27	29-Mar-27	25-Jul-26		$0.00	$355.50	0.00
TAEXELCU120006	Poles RC Foundation	7	$21,500.00	25-Mar-27	01-Apr-27			$0.00	$0.00	0.00
TAEXELCU120008	Lighting Pole Installation with Luminares	10	$81,350.00	03-Apr-27	13-Apr-27			$0.00	$0.00	0.00
TAEXELCU120004	Trench Backfilling	17	$82,350.00	12-Apr-27	01-May-27	15-Aug-26		$0.00	$26,352.00	0.00
TAEXELCU120005	Cables Pulling	8	$348,000.00	02-May-27	10-May-27	26-Jul-26		$0.00	$93,960.00	0.00
TAEXELCU120007	Earthing cables	4	$4,523.00	10-Aug-27	14-Aug-27			$0.00	$0.00	0.00
Telecommunication Works		87	$124,980.00	11-Feb-27	14-Jul-27			$0.00	$0.00	0.00
TAEXTCCU120001	Trench Cut off	15	$24,530.00	11-Feb-27	28-Feb-27			$0.00	$0.00	0.00
TAEXTCCU120002	Drawpit and PVC Pipes Installation	9	$50,500.00	10-Jun-27	20-Jun-27			$0.00	$0.00	0.00
TAEXTCCU120003	Road Crossing Ducts	4	$12,500.00	21-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TAEXTCCU120004	Trench Backfilling	17	$37,450.00	26-Jun-27	14-Jul-27			$0.00	$0.00	0.00
CCTV Works		48	$53,584.00	09-Mar-27	03-May-27			$0.00	$0.00	0.00
TAEXCCCU120001	Pipe Installation with manhole	11	$22,767.00	09-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXCCCU120002	CCTV Swiches Lighting panels Installation	12	$2,264.00	22-Mar-27	04-Apr-27			$0.00	$0.00	0.00
TAEXCCCU120003	Cable laying and connected with Panels	11	$24,025.00	05-Apr-27	17-Apr-27			$0.00	$0.00	0.00
TAEXCCCU120004	Pole Installation with IP Outdoor CCTV POE Camera	14	$4,528.00	18-Apr-27	03-May-27			$0.00	$0.00	0.00
Potable Networks		109	$232,120.00	29-Dec-26	04-May-27			$0.00	$0.00	0.00
TAEXPTCU120001	Excavation works for Trench	12	$56,200.00	29-Dec-26	11-Jan-27			$0.00	$0.00	0.00
TAEXPTCU120002	Bedding Works	2	$7,050.00	12-Jan-27	13-Jan-27			$0.00	$0.00	0.00
TAEXPTCU120003	Install Pipes & Fittings	8	$78,112.00	20-Feb-27	28-Feb-27			$0.00	$0.00	0.00
TAEXPTCU120004	Backfilling Works for Trench	18	$24,158.00	01-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXPTCU120005	Install Valves with fittings	4	$4,600.00	17-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXPTCU120006	Install fire hydrent	9	$28,000.00	22-Mar-27	31-Mar-27			$0.00	$0.00	0.00
TAEXPTCU120007	Valve Chamber works	16	$28,900.00	11-Apr-27	28-Apr-27			$0.00	$0.00	0.00
TAEXPTCU120008	Inspection Test	5	$5,100.00	29-Apr-27	04-May-27			$0.00	$0.00	0.00
TSE Networks		119	$319,310.00	30-Nov-26	15-May-27	27-Sep-26		$0.00	$17,472.50	0.00
TAEXTSCU120001	Excavation works for Trench	22	$50,230.00	30-Nov-26	24-Dec-26			$0.00	$0.00	0.00
TAEXTSCU120002	Bedding Works	2	$10,530.00	26-Dec-26	27-Dec-26			$0.00	$0.00	0.00
TAEXTSCU120003	Install Pipes & Fittings	8	$152,340.00	20-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXTSCU120004	Backfilling Works for Trench	18	$29,800.00	29-Mar-27	18-Apr-27			$0.00	$0.00	0.00
TAEXTSCU120005	Install Valves with fittings	4	$11,490.00	14-Apr-27	18-Apr-27	27-Sep-26		$0.00	$2,872.50	0.00
TAEXTSCU120006	Valve Chamber works	18	$58,400.00	19-Apr-27	09-May-27	27-Sep-26		$0.00	$14,600.00	0.00
TAEXTSCU120007	Inspection Test	5	$6,520.00	10-May-27	15-May-27			$0.00	$0.00	0.00
Sewerage Networks		63	$328,050.60	21-Mar-27	01-Jun-27			$0.00	$0.00	0.00
TAEXSWCU120001	Excavation works for Trench	16	$72,600.00	21-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXSWCU120002	Bedding Works	4	$37,944.45	08-Apr-27	12-Apr-27			$0.00	$0.00	0.00
TAEXSWCU120003	Install GRP Pipes & Fittings	14	$62,510.00	13-Apr-27	28-Apr-27			$0.00	$0.00	0.00
TAEXSWCU120004	Backfilling Works for Trench	13	$85,200.00	02-May-27	16-May-27			$0.00	$0.00	0.00
TAEXSWCU120005	Manhole Installation with backfilling	12	$47,560.00	15-May-27	27-May-27			$0.00	$0.00	0.00
TAEXSWCU120006	Leakage Test	4	$22,236.15	29-May-27	01-Jun-27			$0.00	$0.00	0.00

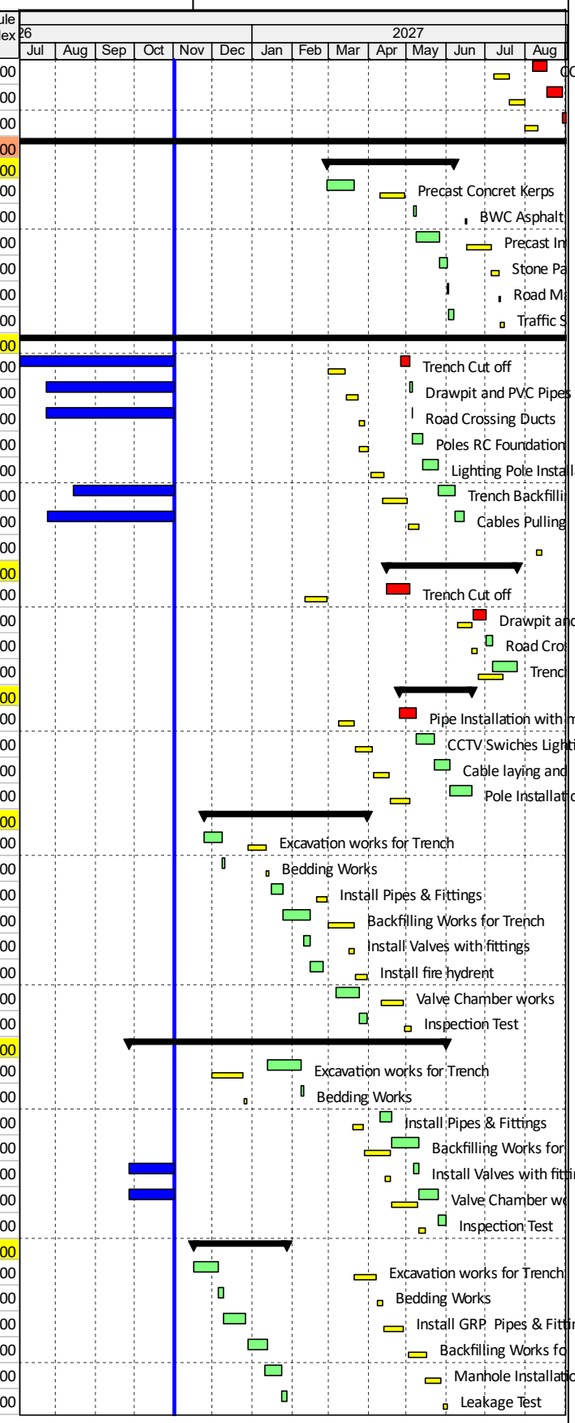


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Storm Networks		67	$505,689.12	30-Mar-27	15-Jun-27			$0.00	$0.00	0.00
TAEXSTCU120001	Excavation works for Trench	18	$136,005.36	30-Mar-27	19-Apr-27			$0.00	$0.00	0.00
TAEXSTCU120002	Bedding Works	4	$68,846.88	20-Apr-27	24-Apr-27			$0.00	$0.00	0.00
TAEXSTCU120003	Install GRP Pipes & Fittings	14	$82,556.88	25-Apr-27	10-May-27			$0.00	$0.00	0.00
TAEXSTCU120004	Backfilling Works for Trench	13	$55,600.00	13-May-27	27-May-27			$0.00	$0.00	0.00
TAEXSTCU120005	Manhole Installation with backfilling	12	$50,580.00	15-May-27	27-May-27			$0.00	$0.00	0.00
TAEXSTCU120006	Install Catch Basin with UPVC Pipes & Fittings	12	$96,500.00	29-May-27	10-Jun-27			$0.00	$0.00	0.00
TAEXSTCU120007	Leakage Test	4	$15,600.00	12-Jun-27	15-Jun-27			$0.00	$0.00	0.00
Upgrade Local 14		87	$441,338.00	25-May-27	16-Aug-27	31-Jul-26		$0.00	$68,013.70	0.00
Electrical Works		87	$388,950.00	30-May-27	16-Aug-27	31-Jul-26		$0.00	$68,013.70	0.00
TAEXELCU140001	Trench Cut off	10	$10,530.00	30-May-27	09-Jun-27	31-Jul-26		$0.00	$3,053.70	0.00
TAEXELCU140002	Drawpit and PVC Pipes Installation	6	$7,000.00	10-Jun-27	16-Jun-27			$0.00	$0.00	0.00
TAEXELCU140003	Road Crossing Ducts	3	$350.00	17-Jun-27	20-Jun-27			$0.00	$0.00	0.00
TAEXELCU140006	Poles RC Foundation	4	$12,500.00	17-Jun-27	21-Jun-27			$0.00	$0.00	0.00
TAEXELCU140004	Trench Backfilling	10	$10,200.00	21-Jun-27	01-Jul-27			$0.00	$0.00	0.00
TAEXELCU140008	Lighting Pole Installation with Luminares	6	$122,050.00	22-Jun-27	28-Jun-27			$0.00	$0.00	0.00
TAEXELCU140005	Cables Pulling	4	$224,000.00	03-Jul-27	06-Jul-27	02-Aug-26		$0.00	$64,960.00	0.00
TAEXELCU140007	Earthing cables	2	$2,320.00	15-Aug-27	16-Aug-27			$0.00	$0.00	0.00
CCTV Works		37	$52,388.00	25-May-27	06-Jul-27			$0.00	$0.00	0.00
TAEXCCCU140001	Pipe Installation with manhole	7	$23,773.00	25-May-27	01-Jun-27			$0.00	$0.00	0.00
TAEXCCCU140002	CCTV Swiches Lighting panels Installation	12	$2,515.00	02-Jun-27	15-Jun-27			$0.00	$0.00	0.00
TAEXCCCU140003	Cable laying and connected with Panels	8	$19,654.00	16-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TAEXCCCU140004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	26-Jun-27	06-Jul-27			$0.00	$0.00	0.00
Upgrade Local 18		29	$51,759.00	08-Jul-27	10-Aug-27			$0.00	$0.00	0.00
CCTV Works		29	$51,759.00	08-Jul-27	10-Aug-27			$0.00	$0.00	0.00
TAEXCCCU180001	Pipe Installation with manhole	8	$23,144.00	08-Jul-27	17-Jul-27			$0.00	$0.00	0.00
TAEXCCCU180002	CCTV Swiches Lighting panels Installation	9	$2,515.00	18-Jul-27	27-Jul-27			$0.00	$0.00	0.00
TAEXCCCU180003	Cable laying and connected with Panels	7	$19,654.00	28-Jul-27	04-Aug-27			$0.00	$0.00	0.00
TAEXCCCU180004	Pole Installation with IP Outdoor CCTV POE Camera	5	$6,446.00	05-Aug-27	10-Aug-27			$0.00	$0.00	0.00
Upgrade Local 20		277	$1,259,711.00	08-Dec-26	21-Aug-27	08-Aug-26		$0.00	$121,440.80	0.00
Electrical Works		198	$604,896.00	21-Jan-27	21-Aug-27	08-Aug-26		$0.00	$121,440.80	0.00
TAEXELCU200001	Trench Cut off	11	$11,250.00	21-Jan-27	02-Feb-27	08-Aug-26		$0.00	$5,625.00	0.00
TAEXELCU200002	Drawpit and PVC Pipes Installation	9	$29,850.00	02-Mar-27	11-Mar-27	29-Aug-26		$0.00	$7,462.50	0.00
TAEXELCU200003	Road Crossing Ducts	4	$50,450.00	13-Mar-27	16-Mar-27	29-Aug-26		$0.00	$12,612.50	0.00
TAEXELCU200006	Poles RC Foundation	7	$102,153.00	13-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCU200004	Trench Backfilling	14	$51,320.00	17-Mar-27	01-Apr-27	23-Aug-26		$0.00	$22,580.80	0.00
TAEXELCU200008	Lighting Pole Installation with Luminares	9	$51,350.00	21-Mar-27	30-Mar-27			$0.00	$0.00	0.00
TAEXELCU200005	Cables Pulling	4	$124,000.00	03-Apr-27	06-Apr-27	16-Aug-26		$0.00	$73,160.00	0.00
TAEXELCU200009	Install Substation & RMU	9	$180,000.00	22-Apr-27	02-May-27			$0.00	$0.00	0.00
TAEXELCU200007	Earthing cables	4	$4,523.00	17-Aug-27	21-Aug-27			$0.00	$0.00	0.00
CCTV Works		148	$49,263.00	04-Feb-27	26-Jul-27			$0.00	$0.00	0.00
TAEXCCCU200001	Pipe Installation with manhole	10	$24,591.00	04-Feb-27	15-Feb-27			$0.00	$0.00	0.00
TAEXCCCU200002	CCTV Swiches Lighting panels Installation	13	$2,578.00	16-Jun-27	30-Jun-27			$0.00	$0.00	0.00
TAEXCCCU200003	Cable laying and connected with Panels	10	$18,176.00	01-Jul-27	12-Jul-27			$0.00	$0.00	0.00
TAEXCCCU200004	Pole Installation with IP Outdoor CCTV POE Camera	12	$3,918.00	13-Jul-27	26-Jul-27			$0.00	$0.00	0.00
Potable Networks		72	$200,812.00	08-Dec-26	28-Feb-27			$0.00	$0.00	0.00
TAEXPTCU200007	Valve Chamber works	17	$22,500.00	08-Dec-26	27-Dec-26			$0.00	$0.00	0.00
TAEXPTCU200008	Inspection Test	5	$5,100.00	28-Dec-26	02-Jan-27			$0.00	$0.00	0.00
TAEXPTCU200001	Excavation works for Trench	9	$30,350.00	12-Jan-27	21-Jan-27			$0.00	$0.00	0.00
TAEXPTCU200002	Bedding Works	2	$7,050.00	23-Jan-27	24-Jan-27			$0.00	$0.00	0.00
TAEXPTCU200003	Install Pipes & Fittings	8	$78,112.00	25-Jan-27	02-Feb-27			$0.00	$0.00	0.00
TAEXPTCU200004	Backfilling Works for Trench	16	$24,100.00	03-Feb-27	21-Feb-27			$0.00	$0.00	0.00
TAEXPTCU200005	Install Valves with fittings	4	$9,600.00	17-Feb-27	21-Feb-27			$0.00	$0.00	0.00
TAEXPTCU200006	Install fire hydrent	6	$24,000.00	22-Feb-27	28-Feb-27			$0.00	$0.00	0.00
TSE Networks		68	$187,370.00	26-Dec-26	14-Mar-27			$0.00	$0.00	0.00

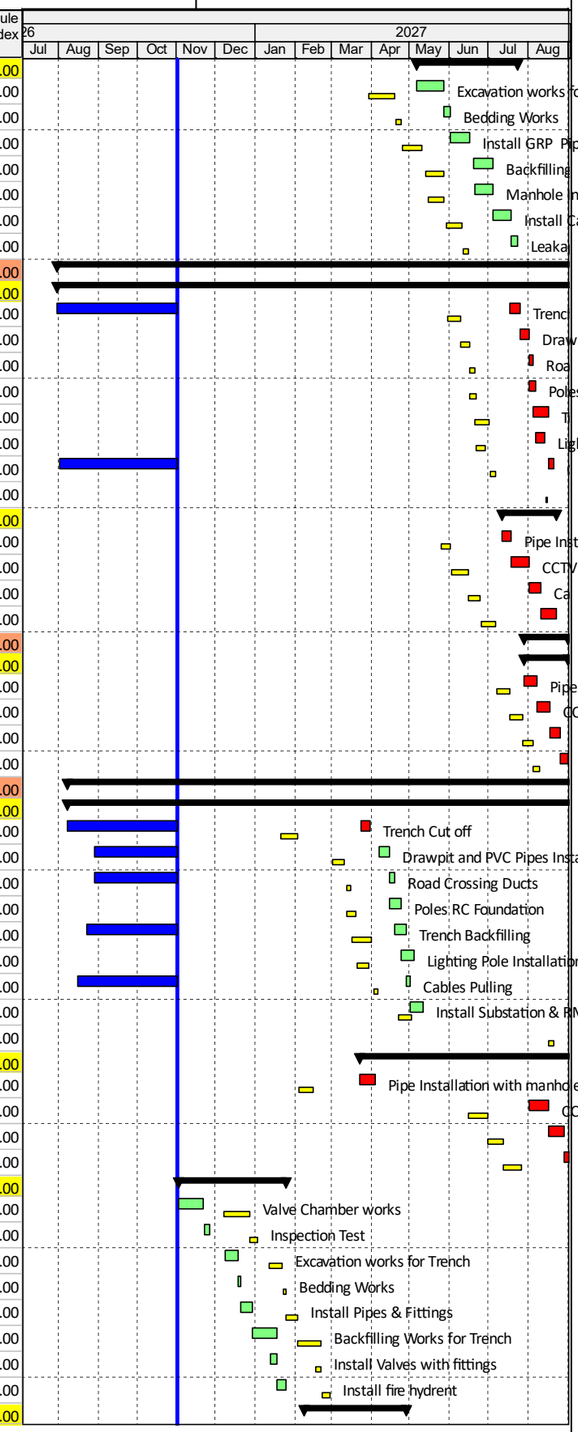


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTSCU200001	Excavation works for Trench	20	$30,150.00	26-Dec-26	17-Jan-27			$0.00	$0.00	0.00
TAEXTSCU200002	Bedding Works	2	$3,800.00	18-Jan-27	19-Jan-27			$0.00	$0.00	0.00
TAEXTSCU200003	Install Pipes & Fittings	8	$72,300.00	20-Jan-27	28-Jan-27			$0.00	$0.00	0.00
TAEXTSCU200004	Backfilling Works for Trench	16	$26,300.00	30-Jan-27	16-Feb-27			$0.00	$0.00	0.00
TAEXTSCU200005	Install Valves with fittings	4	$6,320.00	13-Feb-27	16-Feb-27			$0.00	$0.00	0.00
TAEXTSCU200006	Valve Chamber works	17	$44,300.00	17-Feb-27	08-Mar-27			$0.00	$0.00	0.00
TAEXTSCU200007	Inspection Test	5	$4,200.00	09-Mar-27	14-Mar-27			$0.00	$0.00	0.00
Sewerage Networks		59	$217,370.00	08-Apr-27	15-Jun-27			$0.00	$0.00	0.00
TAEXSWCU200001	Excavation works for Trench	15	$58,630.00	08-Apr-27	25-Apr-27			$0.00	$0.00	0.00
TAEXSWCU200002	Bedding Works	3	$6,850.00	26-Apr-27	28-Apr-27			$0.00	$0.00	0.00
TAEXSWCU200003	Install GRP Pipes & Fittings	12	$55,210.00	29-Apr-27	12-May-27			$0.00	$0.00	0.00
TAEXSWCU200004	Backfilling Works for Trench	17	$22,480.00	11-May-27	30-May-27			$0.00	$0.00	0.00
TAEXSWCU200005	Manhole Installation with backfilling	16	$68,600.00	24-May-27	10-Jun-27			$0.00	$0.00	0.00
TAEXSWCU200006	Leakage Test	4	$5,600.00	12-Jun-27	15-Jun-27			$0.00	$0.00	0.00
Upgrade Local 29		243	$2,105,445.00	07-Feb-27	23-Aug-27	05-Jul-26		$0.00	$427,130.00	0.00
Road Works		65	$1,201,076.00	18-Mar-27	06-Jun-27	25-Jul-26		$0.00	$99,400.00	0.00
TAEXRDCU290001	Asphalt Milling and Deisposal	4	$99,400.00	18-Mar-27	22-Mar-27	25-Jul-26	26-Jul-26	$0.00	$99,400.00	0.00
TAEXRDCU290002	MBC1 layer	1	$9,832.00	23-Mar-27	23-Mar-27			$0.00	$0.00	0.00
TAEXRDCU290003	BBC Base Course	4	$469,343.00	24-Mar-27	28-Mar-27			$0.00	$0.00	0.00
TAEXRDCU290005	Precast Concret Kerps	10	$185,870.00	29-Mar-27	08-Apr-27			$0.00	$0.00	0.00
TAEXRDCU290004	BWC Asphalt Wearing Course with RC	3	$209,377.00	10-Apr-27	12-Apr-27			$0.00	$0.00	0.00
TAEXRDCU290006	Precast Interlock Works	8	$168,704.00	24-May-27	01-Jun-27			$0.00	$0.00	0.00
TAEXRDCU290007	Stone Paving works	2	$21,000.00	02-Jun-27	03-Jun-27			$0.00	$0.00	0.00
TAEXRDCU290008	Road Marking	1	$4,100.00	05-Jun-27	05-Jun-27			$0.00	$0.00	0.00
TAEXRDCU290009	Traffic Sinage	1	$33,450.00	06-Jun-27	06-Jun-27			$0.00	$0.00	0.00
Electrical Works		68	$389,750.00	18-May-27	23-Aug-27			$0.00	$0.00	0.00
TAEXELCU290001	Trench Cut off	10	$10,530.00	18-May-27	29-May-27			$0.00	$0.00	0.00
TAEXELCU290002	Drawpit and PVC Pipes Installation	6	$7,000.00	30-May-27	05-Jun-27			$0.00	$0.00	0.00
TAEXELCU290003	Road Crossing Ducts	3	$350.00	06-Jun-27	08-Jun-27			$0.00	$0.00	0.00
TAEXELCU290006	Poles RC Foundation	4	$12,250.00	06-Jun-27	09-Jun-27			$0.00	$0.00	0.00
TAEXELCU290004	Trench Backfilling	10	$11,250.00	09-Jun-27	20-Jun-27			$0.00	$0.00	0.00
TAEXELCU290008	Lighting Pole Installation with Luminares	6	$122,050.00	10-Jun-27	16-Jun-27			$0.00	$0.00	0.00
TAEXELCU290005	Cables Pulling	4	$224,000.00	21-Jun-27	24-Jun-27			$0.00	$0.00	0.00
TAEXELCU290007	Earthing cables	2	$2,320.00	22-Aug-27	23-Aug-27			$0.00	$0.00	0.00
Telecommunication Works		32	$74,410.00	14-Apr-27	12-Jul-27			$0.00	$0.00	0.00
TAEXTCCU290001	Trench Cut off	10	$15,230.00	14-Apr-27	25-Apr-27			$0.00	$0.00	0.00
TAEXTCCU290002	Drawpit and PVC Pipes Installation	6	$22,250.00	21-Jun-27	27-Jun-27			$0.00	$0.00	0.00
TAEXTCCU290003	Road Crossing Ducts	3	$10,500.00	28-Jun-27	30-Jun-27			$0.00	$0.00	0.00
TAEXTCCU290004	Trench Backfilling	10	$26,430.00	01-Jul-27	12-Jul-27			$0.00	$0.00	0.00
CCTV Works		36	$51,759.00	17-May-27	27-Jun-27			$0.00	$0.00	0.00
TAEXCCCU290001	Pipe Installation with manhole	7	$23,144.00	17-May-27	24-May-27			$0.00	$0.00	0.00
TAEXCCCU290002	CCTV Swiches Lighting panels Installation	10	$2,515.00	25-May-27	05-Jun-27			$0.00	$0.00	0.00
TAEXCCCU290003	Cable laying and connected with Panels	9	$19,654.00	06-Jun-27	15-Jun-27			$0.00	$0.00	0.00
TAEXCCCU290004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	16-Jun-27	27-Jun-27			$0.00	$0.00	0.00
Potable Networks		157	$207,150.00	07-Feb-27	15-Aug-27	05-Jul-26		$0.00	$185,050.00	0.00
TAEXPTCU290001	Excavation works for Trench	4	$44,350.00	07-Feb-27	10-Feb-27	05-Jul-26	15-Jul-26	$0.00	$44,350.00	0.00
TAEXPTCU290002	Bedding Works	2	$7,050.00	11-Feb-27	13-Feb-27	15-Jul-26	16-Jul-26	$0.00	$7,050.00	0.00
TAEXPTCU290003	Install Pipes & Fittings	5	$76,300.00	14-Feb-27	18-Feb-27	16-Jul-26	29-Jul-26	$0.00	$76,300.00	0.00
TAEXPTCU290004	Backfilling Works for Trench	12	$22,150.00	20-Feb-27	04-Mar-27	09-Aug-26	23-Aug-26	$0.00	$22,150.00	0.00
TAEXPTCU290005	Install Valves with fittings	4	$9,600.00	01-Mar-27	04-Mar-27	23-Aug-26	23-Aug-26	$0.00	$9,600.00	0.00
TAEXPTCU290006	Install fire hydrent	5	$22,400.00	06-Mar-27	10-Mar-27	01-Oct-26	04-Oct-26	$0.00	$22,400.00	0.00
TAEXPTCU290007	Valve Chamber works	15	$22,100.00	26-Jul-27	11-Aug-27			$0.00	$0.00	0.00
TAEXPTCU290008	Inspection Test	3	$3,200.00	12-Aug-27	15-Aug-27	08-Oct-26	10-Oct-26	$0.00	$3,200.00	0.00
TSE Networks		33	$181,300.00	11-Mar-27	27-Apr-27	12-Jul-26		$0.00	$142,680.00	0.00

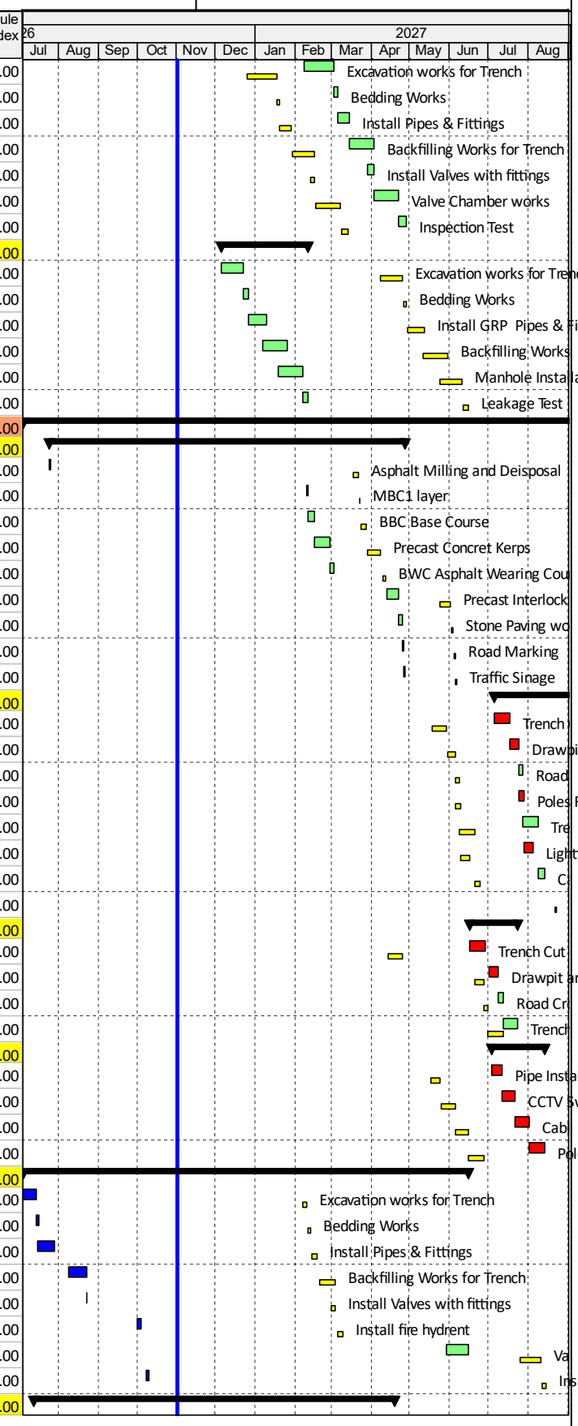

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities


© Oracle Corporation

03-Nov-26 10:40

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXTSCU290001	Excavation works for Trench	4	$48,360.00	11-Mar-27	15-Mar-27	12-Jul-26	16-Jul-26	$0.00	$48,360.00	0.00
TAEXTSCU290002	Bedding Works	2	$4,200.00	16-Mar-27	17-Mar-27	25-Jul-26	26-Jul-26	$0.00	$4,200.00	0.00
TAEXTSCU290003	Install Pipes & Fittings	5	$60,200.00	18-Mar-27	23-Mar-27	26-Jul-26	02-Aug-26	$0.00	$60,200.00	0.00
TAEXTSCU290004	Backfilling Works for Trench	12	$20,100.00	24-Mar-27	06-Apr-27	09-Aug-26	23-Aug-26	$0.00	$20,100.00	0.00
TAEXTSCU290005	Install Valves with fittings	4	$6,320.00	03-Apr-27	06-Apr-27	23-Aug-26	23-Aug-26	$0.00	$6,320.00	0.00
TAEXTSCU290006	Valve Chamber works	15	$38,620.00	07-Apr-27	24-Apr-27			$0.00	$0.00	0.00
TAEXTSCU290007	Inspection Test	3	$3,500.00	25-Apr-27	27-Apr-27	08-Oct-26	10-Oct-26	$0.00	$3,500.00	0.00
Upgrade Local 32		266	$2,463,549.71	28-Dec-26	28-Aug-27	11-Aug-26		$0.00	$108,214.00	0.00
Electrical Works		155	$728,178.00	03-Feb-27	28-Aug-27			$0.00	$0.00	0.00
TAEXELCU320001	Trench Cut off	11	$11,250.00	03-Feb-27	15-Feb-27			$0.00	$0.00	0.00
TAEXELCU320002	Drawpit and PVC Pipes Installation	4	$329,850.00	02-Mar-27	06-Mar-27			$0.00	$0.00	0.00
TAEXELCU320003	Road Crossing Ducts	12	$55,450.00	07-Mar-27	20-Mar-27			$0.00	$0.00	0.00
TAEXELCU320006	Poles RC Foundation	7	$21,520.00	07-Mar-27	14-Mar-27			$0.00	$0.00	0.00
TAEXELCU320008	Lighting Pole Installation with Luminares	9	$71,350.00	15-Mar-27	24-Mar-27			$0.00	$0.00	0.00
TAEXELCU320004	Trench Backfilling	16	$10,235.00	21-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXELCU320005	Cables Pulling	4	$224,000.00	08-Apr-27	12-Apr-27			$0.00	$0.00	0.00
TAEXELCU320007	Earthing cables	4	$4,523.00	24-Aug-27	28-Aug-27			$0.00	$0.00	0.00
Telecommunication Works		117	$49,263.00	16-Feb-27	07-Aug-27			$0.00	$0.00	0.00
TAEXCCCU320001	Pipe Installation with manhole	10	$24,591.00	16-Feb-27	27-Feb-27			$0.00	$0.00	0.00
TAEXCCCU320002	CCTV Swiches Lighting panels Installation	13	$2,578.00	28-Jun-27	12-Jul-27			$0.00	$0.00	0.00
TAEXCCCU320003	Cable laying and connected with Panels	10	$18,176.00	13-Jul-27	24-Jul-27			$0.00	$0.00	0.00
TAEXCCCU320004	Pole Installation with IP Outdoor CCTV POE Camera	12	$3,918.00	25-Jul-27	07-Aug-27			$0.00	$0.00	0.00
Potable Networks		64	$250,812.00	28-Dec-26	10-Mar-27			$0.00	$0.00	0.00
TAEXPTCU320007	Valve Chamber works	17	$42,500.00	28-Dec-26	16-Jan-27			$0.00	$0.00	0.00
TAEXPTCU320008	Inspection Test	5	$5,100.00	17-Jan-27	21-Jan-27			$0.00	$0.00	0.00
TAEXPTCU320001	Excavation works for Trench	9	$60,350.00	23-Jan-27	01-Feb-27			$0.00	$0.00	0.00
TAEXPTCU320002	Bedding Works	2	$7,050.00	02-Feb-27	03-Feb-27			$0.00	$0.00	0.00
TAEXPTCU320003	Install Pipes & Fittings	8	$78,112.00	04-Feb-27	13-Feb-27			$0.00	$0.00	0.00
TAEXPTCU320004	Backfilling Works for Trench	16	$24,100.00	14-Feb-27	03-Mar-27			$0.00	$0.00	0.00
TAEXPTCU320005	Install Valves with fittings	4	$9,600.00	28-Feb-27	03-Mar-27			$0.00	$0.00	0.00
TAEXPTCU320006	Install fire hydrent	6	$24,000.00	04-Mar-27	10-Mar-27			$0.00	$0.00	0.00
TSE Networks		58	$188,350.00	18-Jan-27	06-Apr-27	11-Aug-26		$0.00	$108,214.00	0.00
TAEXTSCU320001	Excavation works for Trench	20	$30,150.00	18-Jan-27	09-Feb-27	11-Aug-26	11-Aug-26	$0.00	$30,150.00	0.00
TAEXTSCU320002	Bedding Works	2	$4,500.00	10-Feb-27	11-Feb-27	16-Aug-26	23-Aug-26	$0.00	$4,500.00	0.00
TAEXTSCU320003	Install Pipes & Fittings	8	$72,300.00	13-Feb-27	21-Feb-27	16-Aug-26	23-Aug-26	$0.00	$72,300.00	0.00
TAEXTSCU320004	Backfilling Works for Trench	16	$26,480.00	22-Feb-27	11-Mar-27			$0.00	$0.00	0.00
TAEXTSCU320005	Install Valves with fittings	4	$6,320.00	08-Mar-27	11-Mar-27	04-Oct-26		$0.00	$1,264.00	0.00
TAEXTSCU320006	Valve Chamber works	17	$44,350.00	13-Mar-27	31-Mar-27			$0.00	$0.00	0.00
TAEXTSCU320007	Inspection Test	5	$4,250.00	01-Apr-27	06-Apr-27			$0.00	$0.00	0.00
Storm Networks		63	$1,246,946.71	16-Feb-27	29-Apr-27			$0.00	$0.00	0.00
TAEXSTCU320001	Excavation works for Trench	10	$288,364.24	16-Feb-27	27-Feb-27			$0.00	$0.00	0.00
TAEXSTCU320002	Bedding Works	3	$65,596.88	28-Feb-27	02-Mar-27			$0.00	$0.00	0.00
TAEXSTCU320003	Install GRP Pipes & Fittings	6	$268,197.08	03-Mar-27	09-Mar-27			$0.00	$0.00	0.00
TAEXSTCU320004	Backfilling Works for Trench	17	$106,921.51	08-Mar-27	27-Mar-27			$0.00	$0.00	0.00
TAEXSTCU320005	Manhole Installation with backfilling	16	$218,147.00	21-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXSTCU320006	Install Catch Basin with UPVC Pipes & Fittings	15	$285,220.00	08-Apr-27	25-Apr-27			$0.00	$0.00	0.00
TAEXSTCU320007	Leakage Test	4	$14,500.00	26-Apr-27	29-Apr-27			$0.00	$0.00	0.00
Upgrade Local 33		236	$2,636,509.24	02-Feb-27	30-Aug-27	20-Sep-26		$0.00	$539,180.24	0.00
Road Works		23	$824,635.00	05-Jun-27	30-Jun-27			$0.00	$0.00	0.00
TAEXRDCU330002	Precast Concret Kerps	10	$185,870.00	05-Jun-27	15-Jun-27			$0.00	$0.00	0.00
TAEXRDCU330001	BWC Asphalt Wearing Course with RC	1	$411,511.00	16-Jun-27	16-Jun-27			$0.00	$0.00	0.00
TAEXRDCU330003	Precast Interlock Works	8	$168,704.00	17-Jun-27	26-Jun-27			$0.00	$0.00	0.00
TAEXRDCU330004	Stone Paving works	2	$21,000.00	27-Jun-27	28-Jun-27			$0.00	$0.00	0.00
TAEXRDCU330005	Road Marking	1	$4,100.00	29-Jun-27	29-Jun-27			$0.00	$0.00	0.00

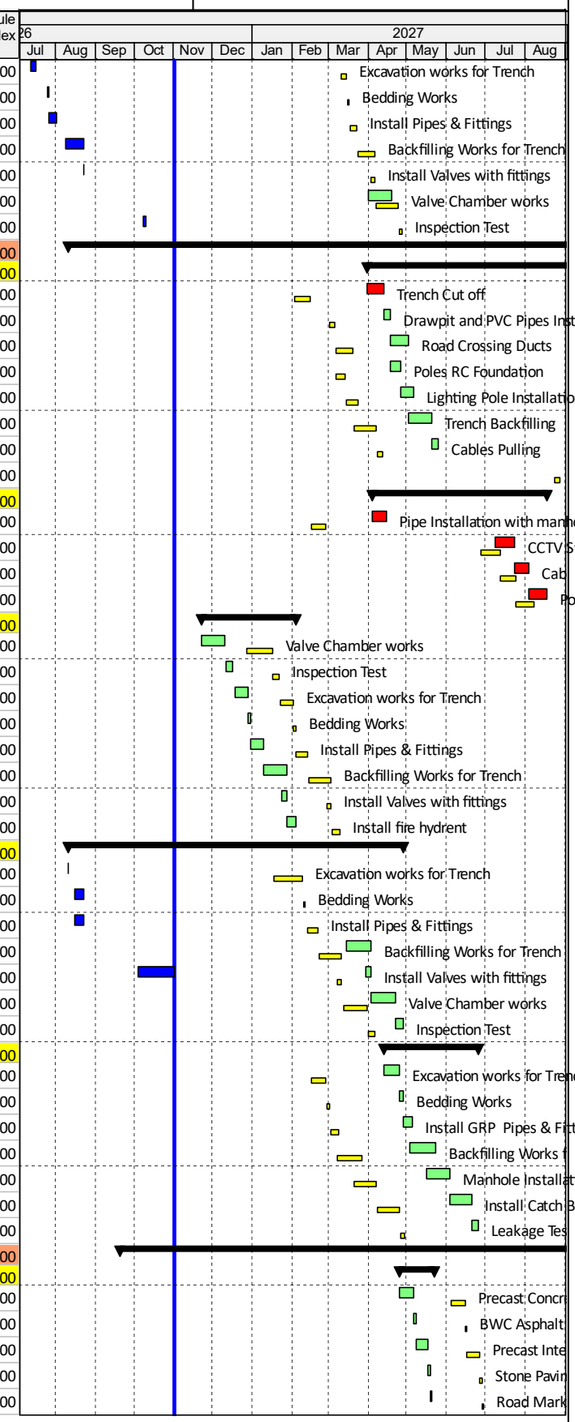


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXRDCU330006	Traffic Sinage	1	$33,450.00	30-Jun-27	30-Jun-27			$0.00	$0.00	0.00
Electrical Works		146	$419,960.00	16-Feb-27	30-Aug-27			$0.00	$0.00	0.00
TAEXELCU330001	Trench Cut off	11	$35,620.00	16-Feb-27	28-Feb-27			$0.00	$0.00	0.00
TAEXELCU330002	Drawpit and PVC Pipes Installation	9	$74,560.00	02-Mar-27	11-Mar-27			$0.00	$0.00	0.00
TAEXELCU330003	Road Crossing Ducts	10	$350.00	13-Mar-27	23-Mar-27			$0.00	$0.00	0.00
TAEXELCU330006	Poles RC Foundation	4	$12,500.00	13-Mar-27	16-Mar-27			$0.00	$0.00	0.00
TAEXELCU330008	Lighting Pole Installation with Luminares	4	$122,050.00	17-Mar-27	21-Mar-27			$0.00	$0.00	0.00
TAEXELCU330004	Trench Backfilling	13	$4,560.00	24-Mar-27	07-Apr-27			$0.00	$0.00	0.00
TAEXELCU330005	Cables Pulling	3	$168,000.00	08-Apr-27	11-Apr-27			$0.00	$0.00	0.00
TAEXELCU330007	Earthing cables	2	$2,320.00	29-Aug-27	30-Aug-27			$0.00	$0.00	0.00
Telecommunication Works		106	$123,255.00	06-Feb-27	31-Jul-27			$0.00	$0.00	0.00
TAEXTCCU330001	Trench Cut off	5	$7,500.00	06-Feb-27	10-Feb-27			$0.00	$0.00	0.00
TAEXTCCU330002	Drawpit and PVC Pipes Installation	4	$80,250.00	13-Jul-27	17-Jul-27			$0.00	$0.00	0.00
TAEXTCCU330003	Road Crossing Ducts	3	$10,500.00	18-Jul-27	20-Jul-27			$0.00	$0.00	0.00
TAEXTCCU330004	Trench Backfilling	9	$25,005.00	21-Jul-27	31-Jul-27			$0.00	$0.00	0.00
CCTV Works		113	$51,759.00	28-Feb-27	08-Jul-27			$0.00	$0.00	0.00
TAEXCCCU330001	Pipe Installation with manhole	8	$23,144.00	28-Feb-27	08-Mar-27			$0.00	$0.00	0.00
TAEXCCCU330002	CCTV Swiches Lighting panels Installation	10	$2,515.00	06-Jun-27	16-Jun-27			$0.00	$0.00	0.00
TAEXCCCU330003	Cable laying and connected with Panels	9	$19,654.00	17-Jun-27	27-Jun-27			$0.00	$0.00	0.00
TAEXCCCU330004	Pole Installation with IP Outdoor CCTV POE Camera	10	$6,446.00	28-Jun-27	08-Jul-27			$0.00	$0.00	0.00
Potable Networks		61	$200,350.00	02-Feb-27	13-Apr-27			$0.00	$0.00	0.00
TAEXPTCU330001	Excavation works for Trench	4	$48,350.00	02-Feb-27	06-Feb-27			$0.00	$0.00	0.00
TAEXPTCU330002	Bedding Works	2	$7,050.00	07-Feb-27	08-Feb-27			$0.00	$0.00	0.00
TAEXPTCU330003	Install Pipes & Fittings	5	$63,300.00	14-Feb-27	18-Feb-27			$0.00	$0.00	0.00
TAEXPTCU330004	Backfilling Works for Trench	12	$22,050.00	20-Feb-27	04-Mar-27			$0.00	$0.00	0.00
TAEXPTCU330005	Install Valves with fittings	4	$9,600.00	01-Mar-27	04-Mar-27			$0.00	$0.00	0.00
TAEXPTCU330006	Install fire hydrent	5	$22,400.00	11-Mar-27	16-Mar-27			$0.00	$0.00	0.00
TAEXPTCU330007	Valve Chamber works	21	$22,500.00	17-Mar-27	10-Apr-27			$0.00	$0.00	0.00
TAEXPTCU330008	Inspection Test	3	$5,100.00	11-Apr-27	13-Apr-27			$0.00	$0.00	0.00
TSE Networks		62	$181,840.00	10-Feb-27	22-Apr-27			$0.00	$0.00	0.00
TAEXTSCU330001	Excavation works for Trench	25	$48,560.00	10-Feb-27	10-Mar-27			$0.00	$0.00	0.00
TAEXTSCU330002	Bedding Works	2	$3,860.00	11-Mar-27	13-Mar-27			$0.00	$0.00	0.00
TAEXTSCU330003	Install Pipes & Fittings	5	$60,530.00	14-Mar-27	18-Mar-27			$0.00	$0.00	0.00
TAEXTSCU330004	Backfilling Works for Trench	12	$20,100.00	20-Mar-27	01-Apr-27			$0.00	$0.00	0.00
TAEXTSCU330005	Install Valves with fittings	4	$6,320.00	29-Mar-27	01-Apr-27			$0.00	$0.00	0.00
TAEXTSCU330006	Valve Chamber works	15	$38,620.00	03-Apr-27	19-Apr-27			$0.00	$0.00	0.00
TAEXTSCU330007	Inspection Test	3	$3,850.00	20-Apr-27	22-Apr-27			$0.00	$0.00	0.00
Sewerage Networks		36	$252,922.00	20-Jun-27	27-Jul-27	20-Sep-26	01-Nov-26	$0.00	$252,922.00	0.00
TAEXSWCU330001	Excavation works for Trench	10	$66,700.00	20-Jun-27	30-Jun-27	20-Sep-26	17-Oct-26	$0.00	$66,700.00	0.00
TAEXSWCU330004	Backfilling Works for Trench	12	$20,350.00	28-Jun-27	11-Jul-27	29-Oct-26	31-Oct-26	$0.00	$20,350.00	0.00
TAEXSWCU330002	Bedding Works	2	$5,600.00	01-Jul-27	03-Jul-27	03-Oct-26	18-Oct-26	$0.00	$5,600.00	0.00
TAEXSWCU330003	Install GRP Pipes & Fittings	7	$93,152.00	04-Jul-27	11-Jul-27	04-Oct-26	18-Oct-26	$0.00	$93,152.00	0.00
TAEXSWCU330005	Manhole Installation with backfilling	11	$61,520.00	12-Jul-27	24-Jul-27	22-Oct-26	25-Oct-26	$0.00	$61,520.00	0.00
TAEXSWCU330006	Leakage Test	3	$5,600.00	25-Jul-27	27-Jul-27	24-Oct-26	01-Nov-26	$0.00	$5,600.00	0.00
Storm Networks		49	$581,788.24	11-Mar-27	23-May-27	24-Oct-26		$0.00	$286,258.24	0.00
TAEXSTCU330001	Excavation works for Trench	16	$125,064.00	11-Mar-27	29-Mar-27	24-Oct-26	01-Nov-26	$0.00	$125,064.00	0.00
TAEXSTCU330002	Bedding Works	2	$61,826.88	30-Mar-27	31-Mar-27	31-Oct-26	01-Nov-26	$0.00	$61,826.88	0.00
TAEXSTCU330003	Install GRP Pipes & Fittings	7	$99,367.36	01-Apr-27	08-Apr-27	01-Nov-26	01-Nov-26	$0.00	$99,367.36	0.00
TAEXSTCU330004	Backfilling Works for Trench	12	$92,500.00	13-Apr-27	26-Apr-27			$0.00	$0.00	0.00
TAEXSTCU330005	Manhole Installation with backfilling	11	$99,630.00	26-Apr-27	08-May-27			$0.00	$0.00	0.00
TAEXSTCU330006	Install Catch Basin with UPVC Pipes & Fittings	10	$90,200.00	09-May-27	19-May-27			$0.00	$0.00	0.00
TAEXSTCU330007	Leakage Test	3	$13,200.00	20-May-27	23-May-27			$0.00	$0.00	0.00
Pond		526	$9,213,585.94	04-Sep-25	23-May-27	04-Sep-25		$6,367,239.63	$7,837,459.10	1.23
Storm Water Pond		526	$9,213,585.94	04-Sep-25	23-May-27	04-Sep-25		$6,367,239.63	$7,837,459.10	1.23

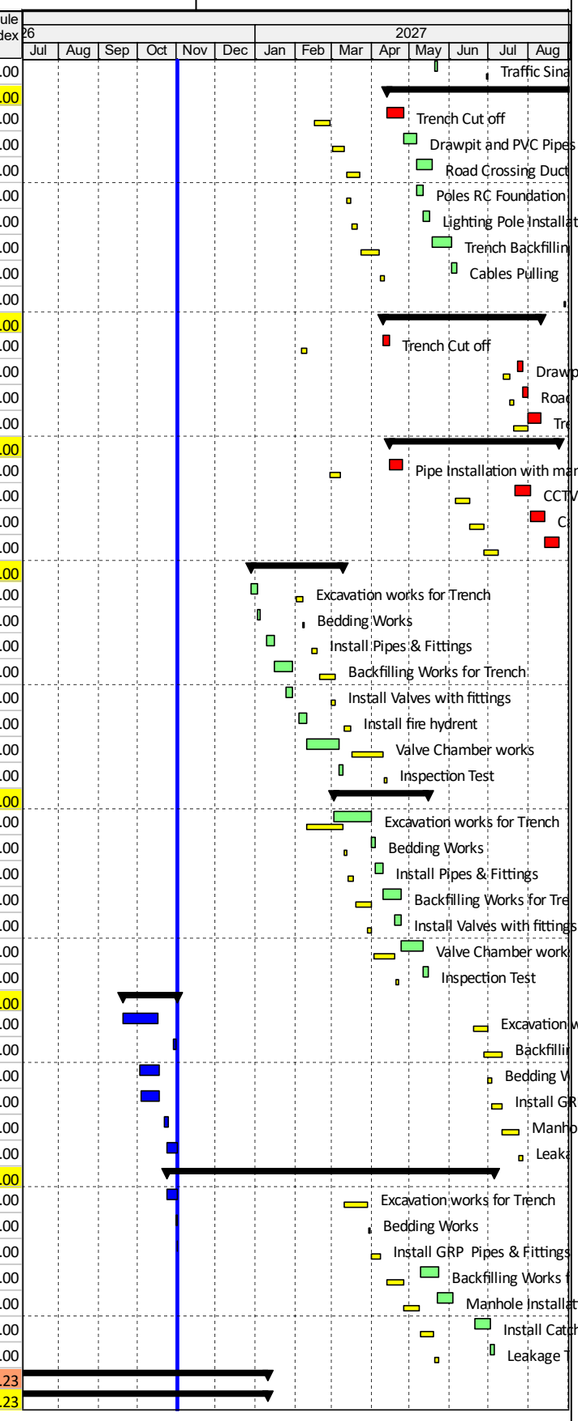


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
TAEXSTCSWP0001	Excavation works for Ponds 1st Part	27	$1,170,180.00	04-Sep-25	05-Oct-25	04-Sep-25	05-Oct-25	$1,170,180.00	$1,170,180.00	1.00
TAEXSTCSWP0002	Excavation works for Ponds 2nd Part	24	$1,170,180.00	06-Oct-25	02-Nov-25	06-Oct-25	02-Nov-25	$1,170,180.00	$1,170,180.00	1.00
TAEXSTCSWP0003	Excavation works for Ponds 3rd Part	26	$1,670,180.00	03-Nov-25	02-Dec-25	03-Nov-25	02-Dec-25	$1,670,180.00	$1,670,180.00	1.00
TAEXSTCSWP0008	Excavation works for Ponds slop	172	$570,167.00	15-Nov-25	02-Jun-26	15-Nov-25	02-Jun-26	$570,167.00	$570,167.00	1.00
TAEXSTCSWP0004	Excavation works for Ponds 4th Part	57	$570,180.10	02-Dec-25	05-Feb-26	02-Dec-25	05-Feb-26	$570,180.10	$570,180.10	1.00
TAEXSTCSWP0013	Filling with suitable and approved imported material for Dike	94	$133,721.28	14-Jan-26	03-May-26	14-Jan-26	03-May-26	$133,721.28	$133,721.28	1.00
TAEXSTCSWP0005	Excavation works for Ponds 5th Part	17	$70,180.00	08-Feb-26	26-Feb-26	08-Feb-26	26-Feb-26	$70,180.00	$70,180.00	1.00
TAEXSTCSWP0014	Loose Riprap, for protection	10	$234,944.65	11-May-26	21-May-26	11-May-26	21-May-26	$234,944.65	$234,944.65	1.00
TAEXSTCSWP0006	Excavation works for Ponds 6th part	30	$346,307.00	29-Aug-26	01-Oct-26	06-Jun-26	15-Jun-26	$346,307.00	$346,307.00	1.00
TAEXSTCSWP0007	Excavation works for ponds 7th part	45	$746,307.00	03-Oct-26	23-Nov-26	18-Jun-26		$431,199.60	$708,991.65	1.64
TAEXSTCSWP0009	Riprap Works part 1	12	$582,875.00	03-Feb-27	16-Feb-27	21-Jun-26		$0.00	$553,731.25	0.00
TAEXSTCSWP0010	Riprap Works Part 2	20	$409,255.00	17-Feb-27	11-Mar-27	08-Aug-26		$0.00	$347,866.75	0.00
TAEXSTCSWP0011	Sand Marl Mix Ballast layer	12	$1,227,455.34	13-Mar-27	25-Mar-27			$0.00	$0.00	0.00
TAEXSTCSWP0012	Outfall structure works	20	$24,499.00	13-Apr-27	05-May-27	05-Jul-26		$0.00	$3,674.85	0.00
TAEXSTCSWP00141	Loose Riprap, for protection Part 01	15	$287,154.57	06-May-27	23-May-27	17-Jun-26	22-Sep-26	$0.00	$287,154.57	0.00
CLOSE OUT		221	$14,046,786.00	17-Apr-27	03-Sep-27			$0.00	$0.00	0.00
Final Testing and Commmisionning		217	$13,562,866.00	17-Apr-27	03-Sep-27			$0.00	$0.00	0.00
Final Test & commisionning Zone 1		108	$2,642,004.00	01-May-27	28-Jun-27			$0.00	$0.00	0.00
TACOFTFT0003	Telecommunications Networks	4	$294,000.00	01-May-27	04-May-27			$0.00	$0.00	0.00
TACOFTFT0004	CCTV Networks	7	$399,630.00	12-May-27	19-May-27			$0.00	$0.00	0.00
TACOFTFT0002	Electrical NetWorks	7	$104,750.00	01-Jun-27	08-Jun-27			$0.00	$0.00	0.00
TACOFTFT0007	Sewerage Networks	6	$225,458.00	08-Jun-27	14-Jun-27			$0.00	$0.00	0.00
TACOFTFT0001	Road Works	4	$241,798.00	09-Jun-27	13-Jun-27			$0.00	$0.00	0.00
TACOFTFT0008	Storm Water Drainage Networks	7	$240,848.00	12-Jun-27	19-Jun-27			$0.00	$0.00	0.00
TACOFTFT0005	Potable Water Networks	4	$589,072.00	20-Jun-27	23-Jun-27			$0.00	$0.00	0.00
TACOFTFT0006	TSE Networks	4	$546,448.00	24-Jun-27	28-Jun-27			$0.00	$0.00	0.00
Final Test & commisionning Zone 2		208	$4,884,878.00	17-Apr-27	24-Aug-27			$0.00	$0.00	0.00
TACOFTFT0015	Sewerage Networks	6	$725,457.00	17-Apr-27	22-Apr-27			$0.00	$0.00	0.00
TACOFTFT0010	Electrical NetWorks	7	$961,120.00	26-Apr-27	03-May-27			$0.00	$0.00	0.00
TACOFTFT0011	Telecommunications Networks	7	$294,000.00	07-Jun-27	14-Jun-27			$0.00	$0.00	0.00
TACOFTFT0016	Storm Water Drainage Networks	7	$440,848.00	26-Jun-27	03-Jul-27			$0.00	$0.00	0.00
TACOFTFT0013	Potable Water Networks	4	$489,071.00	08-Jul-27	12-Jul-27			$0.00	$0.00	0.00
TACOFTFT0014	TSE Networks	4	$732,450.00	13-Jul-27	17-Jul-27			$0.00	$0.00	0.00
TACOFTFT0009	Road Works	7	$542,307.00	26-Jul-27	02-Aug-27			$0.00	$0.00	0.00
TACOFTFT0012	CCTV Networks	7	$699,625.00	17-Aug-27	24-Aug-27			$0.00	$0.00	0.00
Final Test & commisionning Zone 3		197	$6,035,984.00	04-Jul-27	03-Sep-27			$0.00	$0.00	0.00
TACOFTFT0024	Storm Water Drainage Networks	7	$1,240,848.00	04-Jul-27	11-Jul-27			$0.00	$0.00	0.00
TACOFTFT0022	TSE Networks	3	$732,449.00	19-Jul-27	21-Jul-27			$0.00	$0.00	0.00
TACOFTFT0023	Sewerage Networks	5	$725,457.00	28-Jul-27	02-Aug-27			$0.00	$0.00	0.00
TACOFTFT0019	Telecommunications Networks	7	$294,000.00	01-Aug-27	08-Aug-27			$0.00	$0.00	0.00
TACOFTFT0018	Electrical NetWorks	7	$562,725.00	02-Aug-27	09-Aug-27			$0.00	$0.00	0.00
TACOFTFT0017	Road Works	3	$541,798.00	03-Aug-27	05-Aug-27			$0.00	$0.00	0.00
TACOFTFT0021	Potable Water Networks	5	$1,239,072.00	16-Aug-27	21-Aug-27			$0.00	$0.00	0.00
TACOFTFT0020	CCTV Networks	9	$699,635.00	25-Aug-27	03-Sep-27			$0.00	$0.00	0.00
AS BUILT DRAWINGS		177	$483,920.00	19-Jul-27	16-Aug-27			$0.00	$0.00	0.00
AS BUILT DRAWN GS Zone 1		172	$120,980.00	19-Jul-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0006	TSE Networks	10	$15,500.00	19-Jul-27	29-Jul-27			$0.00	$0.00	0.00
TACOFTAD0007	Sewerage Networks	10	$22,300.00	03-Aug-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0008	Storm Water Drainage Networks	10	$25,480.00	03-Aug-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0005	Potable Water Networks	10	$16,500.00	04-Aug-27	15-Aug-27			$0.00	$0.00	0.00
TACOFTAD0001	Road Works	3	$12,000.00	07-Aug-27	09-Aug-27			$0.00	$0.00	0.00
TACOFTAD0003	Telecommunications Networks	7	$9,000.00	09-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0002	Electrical NetWorks	6	$12,000.00	10-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0004	CCTV Networks	4	$8,200.00	12-Aug-27	16-Aug-27			$0.00	$0.00	0.00

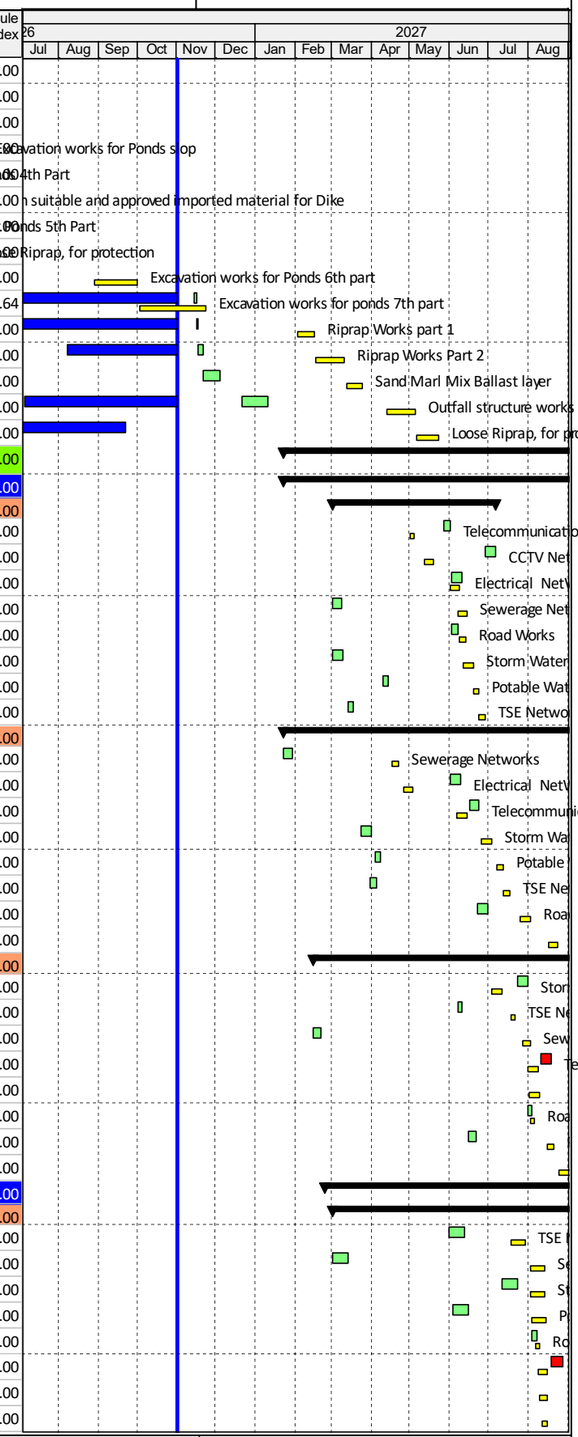


© Oracle Corporation

ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
AS BUILT DRAWN GS Zone 2		177	$181,470.00	19-Jul-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0014	TSE Networks	10	$23,250.00	19-Jul-27	29-Jul-27			$0.00	$0.00	0.00
TACOFTAD0015	Sewerage Networks	15	$33,450.00	28-Jul-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0016	Storm Water Drainage Networks	15	$38,220.00	28-Jul-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0013	Potable Water Networks	10	$24,750.00	04-Aug-27	15-Aug-27			$0.00	$0.00	0.00
TACOFTAD0010	Electrical NetWorks	7	$18,000.00	09-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0011	Telecommunications Networks	7	$13,500.00	09-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0009	Road Works	3	$18,000.00	10-Aug-27	12-Aug-27			$0.00	$0.00	0.00
TACOFTAD0012	CCTV Networks	4	$12,300.00	12-Aug-27	16-Aug-27			$0.00	$0.00	0.00
AS BUILT DRAWN GS Zone 3		172	$181,470.00	19-Jul-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0022	TSE Networks	10	$23,250.00	19-Jul-27	29-Jul-27			$0.00	$0.00	0.00
TACOFTAD0023	Sewerage Networks	10	$33,450.00	03-Aug-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0024	Storm Water Drainage Networks	10	$38,220.00	03-Aug-27	14-Aug-27			$0.00	$0.00	0.00
TACOFTAD0021	Potable Water Networks	10	$24,750.00	04-Aug-27	15-Aug-27			$0.00	$0.00	0.00
TACOFTAD0018	Electrical NetWorks	7	$18,000.00	09-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0019	Telecommunications Networks	7	$13,500.00	09-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0020	CCTV Networks	5	$12,300.00	11-Aug-27	16-Aug-27			$0.00	$0.00	0.00
TACOFTAD0017	Road Works	3	$18,000.00	14-Aug-27	16-Aug-27			$0.00	$0.00	0.00
DEMOBILIZATION		16	$0.00	17-Aug-27	03-Sep-27			$0.00	$0.00	0.00
TAPCDZ00000001	Demobilization Manpower	6	$0.00	17-Aug-27	23-Aug-27			$0.00	$0.00	0.00
TAPCDZ00000002	Remove Offices and Structures	5	$0.00	24-Aug-27	29-Aug-27			$0.00	$0.00	0.00
TAPCDZ00000022	Restore Ground Surfaces	6	$0.00	29-Aug-27	03-Sep-27			$0.00	$0.00	0.00
TAPCDZ00000012	Demobilize Equipment from Site	5	$0.00	30-Aug-27	03-Sep-27			$0.00	$0.00	0.00
TAPCDZ00000032	Final Handover	0	$0.00		03-Sep-27			$0.00	$0.00	0.00

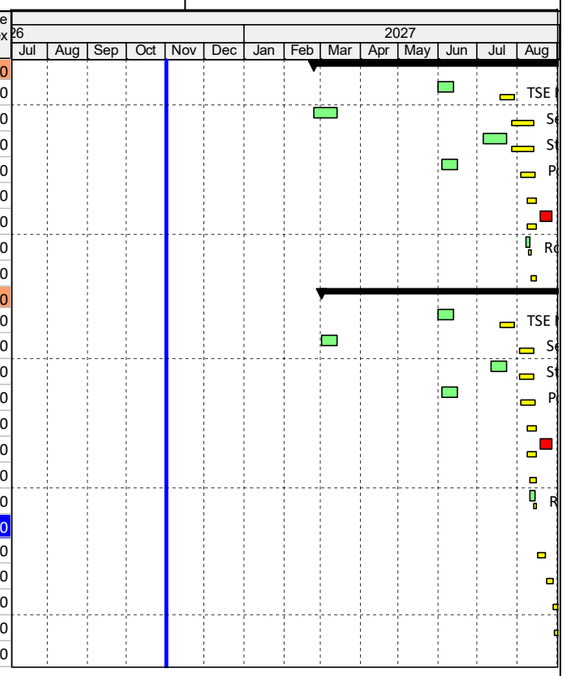

© Oracle Corporation
