
# ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY

| Activity Name | Schedule % Complete | Physical % Complete |
|---|---|---|
| **ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY** | | |
| **PROCUREMENT** | | |
| **Material Fabrication and Delivery** | | |
| **Material Fabrication and Delivery for Road Works** | | |
| Precast Concrete Curbstone Delivery to Site part 01 | 0% | 16% |
| **Material Fabrication and Delivery for Electrical Works** | | |
| Pipes ,Fittings Delivery to Site Part 01 | 100% | 89% |
| **Material Fabrication and Delivery for Storm Networks** | | |
| Manholes,ets Delivery part 01 | 100% | 2% |
| **CONSTRUCTION WORKS** | | |
| **ZONE 1** | | |
| **Upgrade local 21** | | |
| **Storm Networks** | | |
| Install GRP Pipes & Fittings Part 01 | 100% | 50% |
| Backfilling Works for Trench Part 01 | 100% | 50% |
| **Upgrade local 26** | | |
| **Electrical Works** | | |
| Trench Cut of | 100% | 44% |
| **ZONE 3** | | |
| **Local Road 01** | | |
| **Potable Networks** | | |
| Excavation works for Trench Part 01 | 100% | 90% |
| Valve Chamber works | 0% | 90% |
| **TSE Networks** | | |
| Excavation works for Trench Part 01 | 100% | 10% |
| Valve Chamber works | 0% | 90% |
| **Sewerage Networks** | | |
| Excavation works for Trench Part 01 | 0% | 5% |
| Bedding Works Part 01 | 0% | 5% |
| Install GRP Pipes & Fittings Part 01 | 0% | 5% |
| Manhole Installation with backfilling Part 01 | 0% | 15% |
| **Storm Networks** | | |
| Excavation works for Trench & Box Culvert Part 01 | 100% | 85% |
| Install Catch Basin with UPVC Pipes & Fittings | 27.27% | 55% |
| **Local Road 06** | | |
| **Potable Networks** | | |
| Excavation works for Trench | 100% | 97% |
| **TSE Networks** | | |
| Excavation works for Trench | 100% | 80% |
| **Sewerage Networks** | | |
| Leakage Test | 0% | 45% |
| **Storm Networks** | | |
| Excavation works for Trench | 100% | 94% |
| Bedding Works | 100% | 94% |
| Install GRP Pipes & Fittings | 90% | 94% |
| Manhole Installation with backfilling | 0% | 85% |
| **Local Road 08** | | |
| **Sewerage Networks** | | |
| Leakage Test | 0% | 90% |
| Manhole Installation with backfilling Part 01 | 0% | 90% |
| **Storm Networks** | | |
| Leakage Test | 0% | 80% |
| **Upgrade Local 12** | | |
| **Electrical Works** | | |
| Drawpit and PVC Pipes Installation | 0% | 79% |
| Road Crossing Ducts | 0% | 79% |
| Cables Pulling | 0% | 27% |
| **Pond** | | |
| **Storm Water Pond** | | |
| Outfall structure works | 0% | 15% |




Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

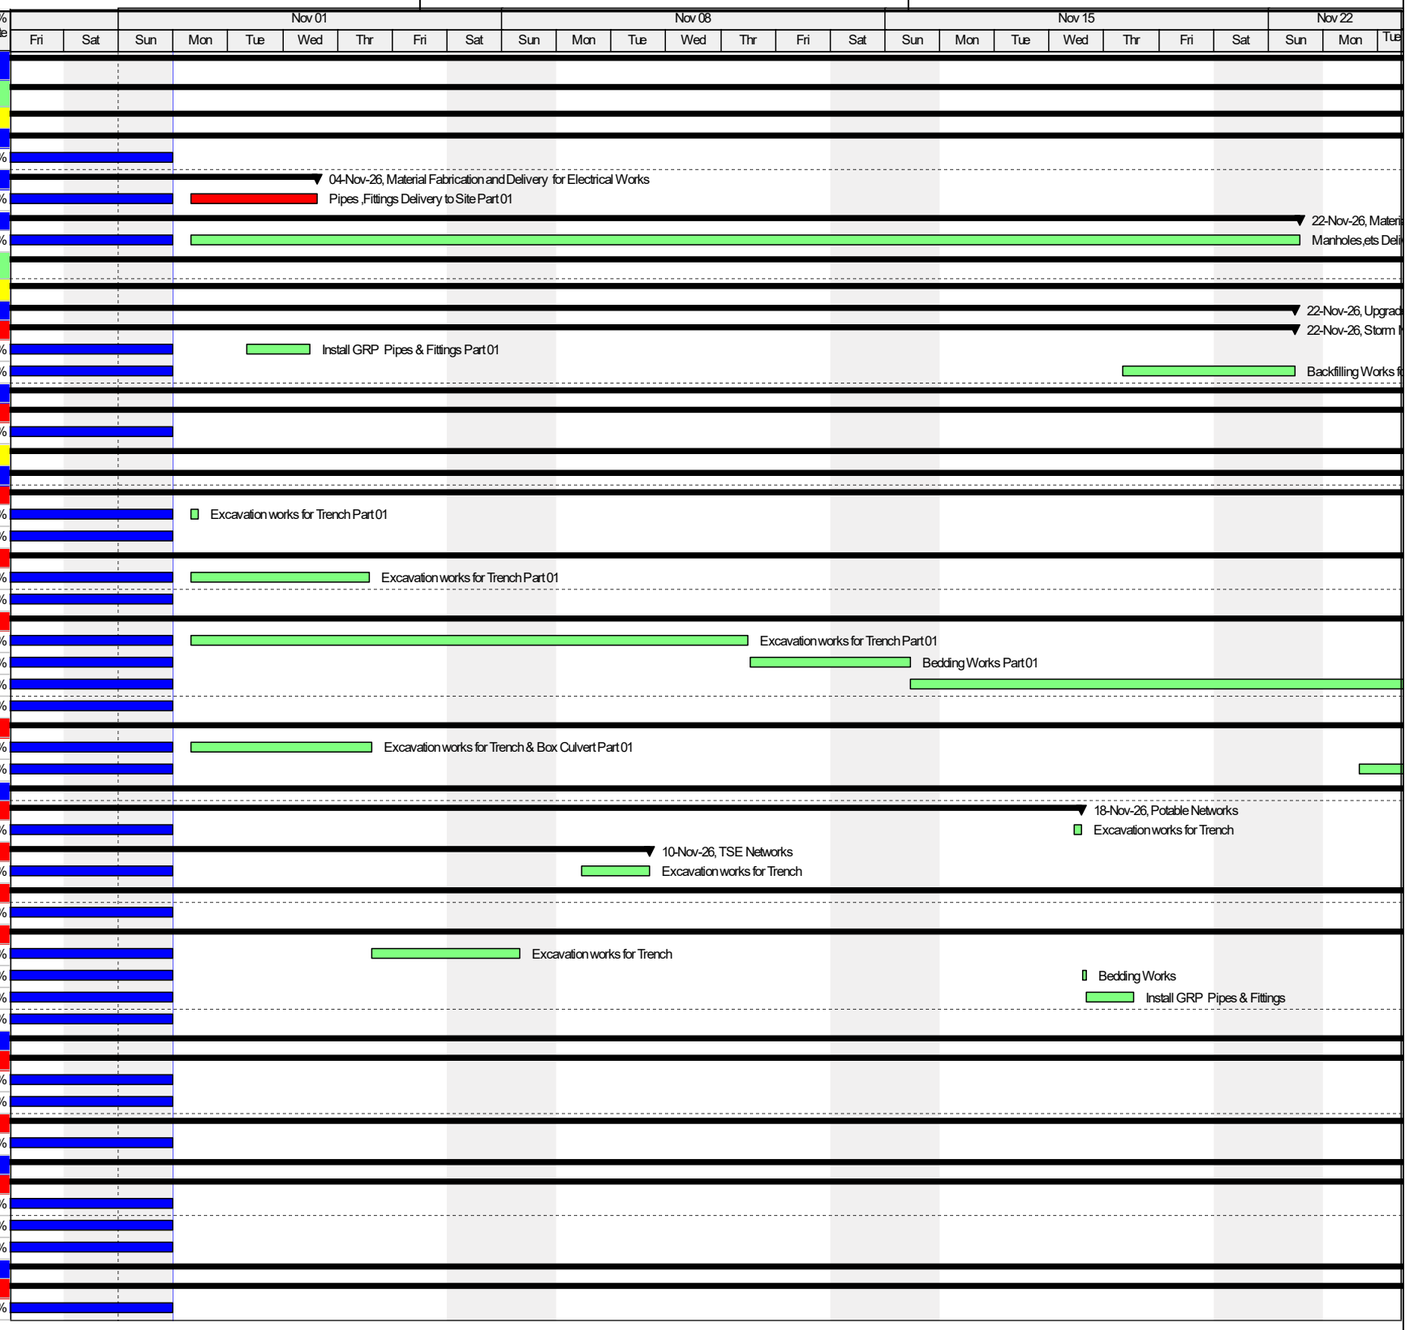

TASK filter: Three Weeks Lookahead -.

© Oracle Corporation
