
Development of the Technology City in Dammam-Projec
UPDATE 13-10-2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Development of the Technology City in Dammam-Project UPDATE 13-10-2(		196	22-Jul-26 A	19-Feb-27	23-Jun-26	28-Jan-27	19,364,870.12
Key Milestones		0	21-Oct-26	21-Oct-26	13-Jul-26	13-Jul-26	0.00
Contractual Milestones		0	21-Oct-26	21-Oct-26	13-Jul-26	13-Jul-26	0.00
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		21-Oct-26		13-Jul-26	0.00
Engineering Works		8	13-Oct-26	21-Oct-26	23-Jun-26	02-Jul-26	0.00
Material Submittals and Approvals		8	13-Oct-26	21-Oct-26	23-Jun-26	02-Jul-26	0.00
Short Lead Time Items		7	13-Oct-26	20-Oct-26	23-Jun-26	30-Jun-26	0.00
Superstructure Works		7	13-Oct-26	20-Oct-26	23-Jun-26	30-Jun-26	0.00
Storage Tank (TSE)		7	13-Oct-26	20-Oct-26	23-Jun-26	30-Jun-26	0.00
Submission of Material		7	13-Oct-26	20-Oct-26	23-Jun-26	30-Jun-26	0.00
ENG-MT-TSE-CV-S-	Material Submittal for Civil Works for Storage Tank (TSE)	7	13-Oct-26	20-Oct-26	23-Jun-26	30-Jun-26	0.00
Long Lead Time Items		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Superstructure Works		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Pump Stations		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Submission of Material		7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	0.00
ENG-MT-SPS-MC-S-	Material Submittal for Electromechanical Works for Pump Stations	7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	0.00
Approval of Material		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
ENG-MT-SPS-MC-A-	Material Approval for Electromechanical Works for Pump Stations	8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Storage Tank (TSE)		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Submission of Material		7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	0.00
ENG-MT-TSE-MC-S-	Material Submittal for Electromechanical Works for Storage Tank (TSE)	7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	0.00
Approval of Material		8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
ENG-MT-TSE-MC-A-	Material Approval for Electromechanical Works for Storage Tank (TSE)	8	13-Oct-26	21-Oct-26	24-Jun-26	02-Jul-26	0.00
Procurement Cycle		178	22-Jul-26 A	19-Feb-27	23-Jun-26	28-Jan-27	0.00
Short Lead Time Items		178	22-Jul-26 A	19-Feb-27	23-Jun-26	28-Jan-27	0.00
Infrastructure Networks		178	22-Jul-26 A	19-Feb-27	23-Jun-26	28-Jan-27	0.00
Road Works		17	02-Aug-26 A	13-Oct-26	02-Nov-26	05-Dec-26	0.00
Material Delivery & Site Inspection		17	02-Aug-26 A	13-Oct-26	02-Nov-26	05-Dec-26	0.00
Pre-Bituminous Construction		17	02-Aug-26 A	13-Oct-26	02-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-10	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	13-Oct-26	02-Nov-26	02-Nov-26	0.00
PRO-R25-RD-DL-11	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	13-Oct-26	13-Oct-26	12-Nov-26	12-Nov-26	0.00
Bituminous Construction		0	13-Oct-26	13-Oct-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-16	Material Delivery & Site Inspection for Prime Coat of Road Works	0	13-Oct-26	13-Oct-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-17	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	0	13-Oct-26	13-Oct-26	05-Dec-26	05-Dec-26	0.00
Pavement Works		0	13-Oct-26	13-Oct-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-12	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	13-Oct-26	13-Oct-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-13	Material Delivery & Site Inspection of Curbstones for Landscaping	0	13-Oct-26	13-Oct-26	12-Nov-26	12-Nov-26	0.00
Traffic Signs Boards and Roads Marking		0	13-Oct-26	13-Oct-26	08-Nov-26	25-Nov-26	0.00
PRO-R25-RD-DL-14	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	13-Oct-26	13-Oct-26	08-Nov-26	08-Nov-26	0.00
PRO-R25-RD-DL-15	Material Delivery & Site Inspection of Road Markings For Road Works	0	13-Oct-26	13-Oct-26	25-Nov-26	25-Nov-26	0.00
Softscape and Planting Works		83	13-Oct-26	17-Jan-27	11-Jul-26	17-Oct-26	0.00
Issuance of Purchase Orders		6	13-Oct-26	19-Oct-26	11-Jul-26	19-Jul-26	0.00
Main Line Pipes		6	13-Oct-26	19-Oct-26	11-Jul-26	19-Jul-26	0.00
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	13-Oct-26	19-Oct-26	12-Jul-26	19-Jul-26	0.00
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	13-Oct-26	19-Oct-26	11-Jul-26	18-Jul-26	0.00

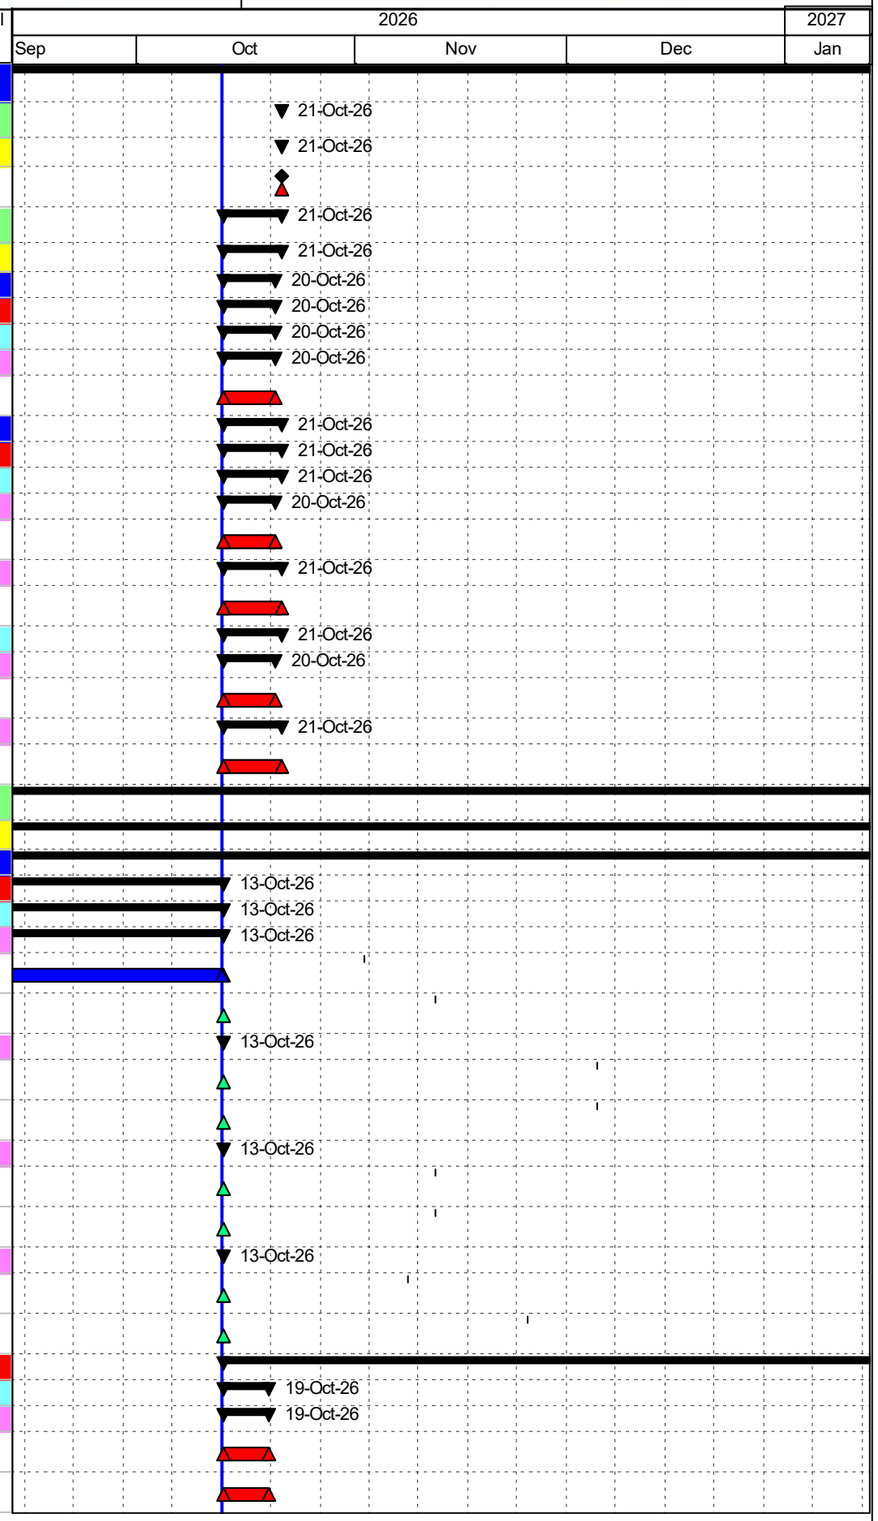

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Manufacturing of Material		90	20-Oct-26	17-Jan-27	18-Jul-26	17-Oct-26	0.00
Main Line Pipes		90	20-Oct-26	17-Jan-27	18-Jul-26	17-Oct-26	0.00
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	20-Oct-26	17-Jan-27	19-Jul-26	17-Oct-26	0.00
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	90	20-Oct-26	17-Jan-27	18-Jul-26	16-Oct-26	0.00
Sewage Network		109	13-Sep-26 A	19-Feb-27	15-Jul-26	21-Nov-26	0.00
Manufacturing of Material		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
Testing and Finishes		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
Material Delivery & Site Inspection		0	13-Sep-26 A	13-Oct-26	09-Aug-26	09-Aug-26	0.00
Main Line Sections		0	13-Sep-26 A	13-Oct-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SW-DL-11	Material Delivery & Site Inspection of Manholes for Sewage Network	0	13-Sep-26 A	13-Oct-26	09-Aug-26	09-Aug-26	0.00
Storm Drainage Network		152	02-Aug-26 A	20-Jan-27	15-Jul-26	22-Oct-26	0.00
Manufacturing of Material		100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
Testing and Finishes		100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
1st Material Delivery & Site Inspection		6	13-Sep-26 A	19-Oct-26	20-Jul-26	26-Jul-26	0.00
Catch Basin Sections		6	13-Sep-26 A	19-Oct-26	20-Jul-26	26-Jul-26	0.00
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	6	13-Sep-26 A	19-Oct-26	20-Jul-26	26-Jul-26	0.00
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	6	13-Sep-26 A	19-Oct-26	20-Jul-26	26-Jul-26	0.00
Material Delivery & Site Inspection		11	02-Aug-26 A	20-Oct-26	27-Jul-26	09-Aug-26	0.00
Main Line Sections		0	02-Aug-26 A	13-Oct-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SD-DL-10	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	13-Oct-26	09-Aug-26	09-Aug-26	0.00
Catch Basin Sections		0	02-Aug-26 A	20-Oct-26	27-Jul-26	27-Jul-26	0.00
PRO-R25-SD-DL-13	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	20-Oct-26	27-Jul-26	27-Jul-26	0.00
PRO-R25-SD-DL-11	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	20-Oct-26	27-Jul-26	27-Jul-26	0.00
Potable Water Network		116	30-Jul-26 A	11-Feb-27	07-Jul-26	06-Nov-26	0.00
Issuance of Purchase Orders		10	13-Oct-26	24-Oct-26	08-Jul-26	19-Jul-26	0.00
Main Line Sections		6	13-Oct-26	19-Oct-26	08-Jul-26	14-Jul-26	0.00
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	13-Oct-26	19-Oct-26	08-Jul-26	14-Jul-26	0.00
Fire Hydrant		10	13-Oct-26	24-Oct-26	08-Jul-26	19-Jul-26	0.00
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	13-Oct-26	24-Oct-26	08-Jul-26	19-Jul-26	0.00
Testing and Finishes		10	13-Oct-26	24-Oct-26	08-Jul-26	19-Jul-26	0.00
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	13-Oct-26	24-Oct-26	08-Jul-26	19-Jul-26	0.00
Manufacturing of Material		115	20-Oct-26	11-Feb-27	15-Jul-26	06-Nov-26	0.00
Main Line Sections		90	20-Oct-26	17-Jan-27	15-Jul-26	12-Oct-26	0.00
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	20-Oct-26	17-Jan-27	15-Jul-26	12-Oct-26	0.00
Fire Hydrant		60	25-Oct-26	23-Dec-26	20-Jul-26	17-Sep-26	0.00
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	25-Oct-26	23-Dec-26	20-Jul-26	17-Sep-26	0.00
Testing and Finishes		110	25-Oct-26	11-Feb-27	20-Jul-26	06-Nov-26	0.00
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	25-Oct-26	11-Feb-27	20-Jul-26	06-Nov-26	0.00
1st Material Delivery & Site Inspection		71	30-Jul-26 A	03-Jan-27	07-Jul-26	28-Sep-26	0.00
Main Line Sections		71	30-Jul-26 A	03-Jan-27	07-Jul-26	28-Sep-26	0.00
PRO-PW-1DL-100_F	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	30-Jul-26 A	03-Jan-27	07-Jul-26	28-Sep-26	0.00
Material Delivery & Site Inspection		0	02-Aug-26 A	03-Jan-27	29-Sep-26	29-Sep-26	0.00
Main Line Sections		0	02-Aug-26 A	03-Jan-27	29-Sep-26	29-Sep-26	0.00

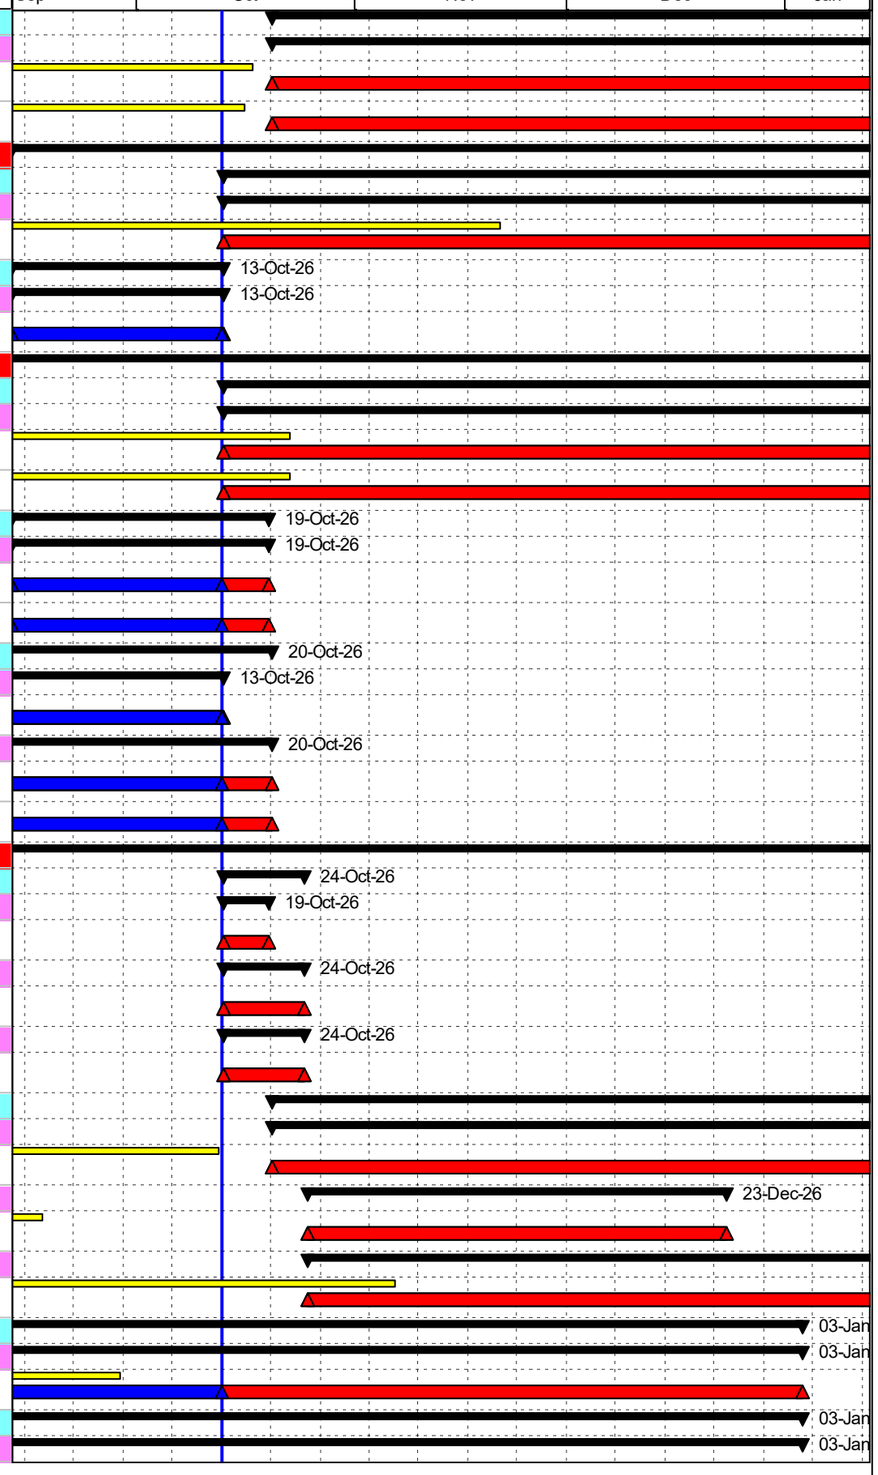

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R25-PW-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Remaining)	0	02-Aug-26 A	03-Jan-27	29-Sep-26	29-Sep-26	0.00
Irrigation Network		158	22-Jul-26 A	24-Jan-27	15-Jul-26	19-Oct-26	0.00
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	15-Jul-26	21-Jul-26	0.00
Main Line Pipes		6	20-Oct-26	26-Oct-26	15-Jul-26	21-Jul-26	0.00
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	20-Oct-26	26-Oct-26	15-Jul-26	21-Jul-26	0.00
Manufacturing of Material		90	27-Oct-26	24-Jan-27	22-Jul-26	19-Oct-26	0.00
Main Line Pipes		90	27-Oct-26	24-Jan-27	22-Jul-26	19-Oct-26	0.00
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	27-Oct-26	24-Jan-27	22-Jul-26	19-Oct-26	0.00
1st Material Delivery & Site Inspection		5	22-Jul-26 A	13-Oct-26	05-Oct-26	11-Oct-26	0.00
Main Line Pipes		5	22-Jul-26 A	13-Oct-26	05-Oct-26	11-Oct-26	0.00
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	22-Jul-26 A	13-Oct-26	05-Oct-26	11-Oct-26	0.00
Material Delivery & Site Inspection		0	13-Oct-26	13-Oct-26	11-Oct-26	11-Oct-26	0.00
Main Line Pipes		0	13-Oct-26	13-Oct-26	11-Oct-26	11-Oct-26	0.00
PRO-R25-IR-DL-100	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	13-Oct-26	13-Oct-26	11-Oct-26	11-Oct-26	0.00
Treated Sewage Effluent (Tse)		86	02-Aug-26 A	17-Jan-27	27-Jun-26	10-Oct-26	0.00
Issuance of Purchase Orders		6	13-Oct-26	19-Oct-26	27-Jun-26	04-Jul-26	0.00
Main Line Pipes		6	13-Oct-26	19-Oct-26	27-Jun-26	04-Jul-26	0.00
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	13-Oct-26	19-Oct-26	27-Jun-26	04-Jul-26	0.00
Manufacturing of Material		90	20-Oct-26	17-Jan-27	04-Jul-26	02-Oct-26	0.00
Main Line Pipes		90	20-Oct-26	17-Jan-27	04-Jul-26	02-Oct-26	0.00
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	20-Oct-26	17-Jan-27	04-Jul-26	02-Oct-26	0.00
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	03-Oct-26	08-Oct-26	0.00
Main Line Pipes		6	13-Oct-26	19-Oct-26	03-Oct-26	08-Oct-26	0.00
PRO-TSE-1DL-120	1ST Material Delivery for Main Line Pipes of Treated Sewage Effluent (Tse)	6	13-Oct-26	19-Oct-26	03-Oct-26	08-Oct-26	0.00
Material Delivery & Site Inspection		0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0.00
Main Line Pipes		0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0.00
PRO-R25-TSE-DL-1	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (Tse)(Remaining)	0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0.00
Medium Voltage Network		89	13-Oct-26	24-Jan-27	23-Jun-26	19-Oct-26	0.00
Issuance of Purchase Orders		12	13-Oct-26	26-Oct-26	23-Jun-26	21-Jul-26	0.00
Cabling Works		12	13-Oct-26	26-Oct-26	23-Jun-26	06-Jul-26	0.00
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	13-Oct-26	26-Oct-26	23-Jun-26	06-Jul-26	0.00
Termination and Testing Works		12	13-Oct-26	26-Oct-26	08-Jul-26	21-Jul-26	0.00
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Network	12	13-Oct-26	26-Oct-26	08-Jul-26	21-Jul-26	0.00
Manufacturing of Material		90	27-Oct-26	24-Jan-27	07-Jul-26	19-Oct-26	0.00
Cabling Works		60	27-Oct-26	25-Dec-26	07-Jul-26	04-Sep-26	0.00
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	27-Oct-26	25-Dec-26	07-Jul-26	04-Sep-26	0.00
Termination and Testing Works		90	27-Oct-26	24-Jan-27	22-Jul-26	19-Oct-26	0.00
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	27-Oct-26	24-Jan-27	22-Jul-26	19-Oct-26	0.00
Low Voltage and Street Lighting Network		41	13-Oct-26	29-Nov-26	28-Sep-26	28-Jan-27	0.00
1st Material Delivery & Site Inspection		15	13-Oct-26	29-Oct-26	28-Sep-26	29-Dec-26	0.00
Cabling Works		6	13-Oct-26	19-Oct-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	13-Oct-26	19-Oct-26	28-Sep-26	04-Oct-26	0.00
Lighting Poles Works		6	13-Oct-26	19-Oct-26	28-Sep-26	19-Dec-26	0.00
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	13-Oct-26	19-Oct-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	13-Oct-26	19-Oct-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	13-Oct-26	19-Oct-26	13-Dec-26	19-Dec-26	0.00
Distribution Panel Board		6	13-Oct-26	19-Oct-26	24-Oct-26	29-Oct-26	0.00

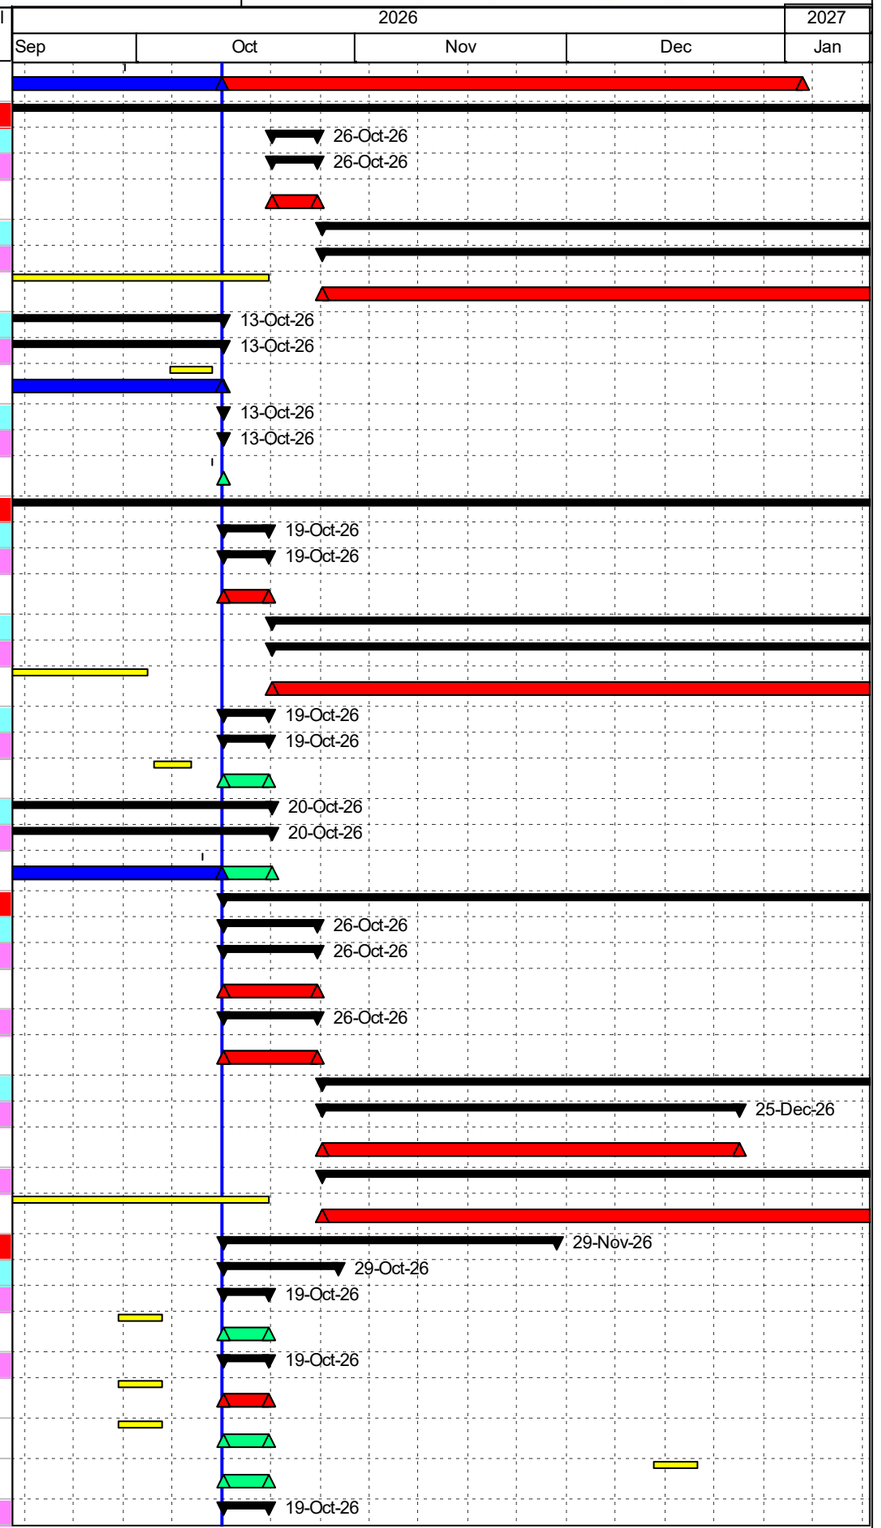


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	13-Oct-26	19-Oct-26	24-Oct-26	29-Oct-26	0.00
Termination and Testing Works		15	13-Oct-26	29-Oct-26	03-Nov-26	29-Dec-26	0.00
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	13-Oct-26	29-Oct-26	13-Dec-26	29-Dec-26	0.00
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	13-Oct-26	29-Oct-26	03-Nov-26	21-Nov-26	0.00
Earthing System Works		6	13-Oct-26	19-Oct-26	03-Dec-26	09-Dec-26	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	13-Oct-26	19-Oct-26	03-Dec-26	09-Dec-26	0.00
Material Delivery & Site Inspection		35	20-Oct-26	29-Nov-26	05-Oct-26	28-Jan-27	0.00
Cabling Works		0	20-Oct-26	20-Oct-26	05-Oct-26	05-Oct-26	0.00
PRO-R25-SL-DL-10(	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	20-Oct-26	20-Oct-26	05-Oct-26	05-Oct-26	0.00
Lighting Poles Works		18	20-Oct-26	09-Nov-26	05-Oct-26	20-Dec-26	0.00
PRO-R25-SL-DL-11(	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network	18	20-Oct-26	09-Nov-26	05-Oct-26	25-Oct-26	0.00
PRO-R25-SL-DL-12(	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	20-Oct-26	20-Oct-26	05-Oct-26	05-Oct-26	0.00
PRO-R25-SL-DL-14(	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	20-Oct-26	20-Oct-26	20-Dec-26	20-Dec-26	0.00
Distribution Panel Board		0	20-Oct-26	20-Oct-26	31-Oct-26	31-Oct-26	0.00
PRO-R25-SL-DL-16(	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	0	20-Oct-26	20-Oct-26	31-Oct-26	31-Oct-26	0.00
Termination and Testing Works		26	31-Oct-26	29-Nov-26	21-Nov-26	28-Jan-27	0.00
PRO-R25-SL-DL-13(	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	31-Oct-26	29-Nov-26	30-Dec-26	28-Jan-27	0.00
PRO-R25-SL-DL-17(	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	31-Oct-26	29-Nov-26	21-Nov-26	21-Dec-26	0.00
Earthing System Works		0	20-Oct-26	20-Oct-26	10-Dec-26	10-Dec-26	0.00
PRO-R25-SL-DL-15(	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	20-Oct-26	20-Oct-26	10-Dec-26	10-Dec-26	0.00
Telecom Network		83	13-Oct-26	17-Jan-27	07-Jul-26	11-Oct-26	0.00
Issuance of Purchase Orders		6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
Ducts Works		6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
Manholes Works		6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
CCTV System Wroks		6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	13-Oct-26	19-Oct-26	07-Jul-26	13-Jul-26	0.00
Manufacturing of Material		90	20-Oct-26	17-Jan-27	14-Jul-26	11-Oct-26	0.00
Ducts Works		60	20-Oct-26	18-Dec-26	14-Jul-26	11-Sep-26	0.00
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	20-Oct-26	18-Dec-26	14-Jul-26	11-Sep-26	0.00
Manholes Works		90	20-Oct-26	17-Jan-27	14-Jul-26	11-Oct-26	0.00
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	20-Oct-26	17-Jan-27	14-Jul-26	11-Oct-26	0.00
CCTV System Wroks		90	20-Oct-26	17-Jan-27	14-Jul-26	11-Oct-26	0.00
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	20-Oct-26	17-Jan-27	14-Jul-26	11-Oct-26	0.00
Superstructure Works		145	02-Aug-26 A	10-Jan-27	23-Jun-26	11-Oct-26	0.00
Issuance of Purchase Orders		18	13-Oct-26	02-Nov-26	23-Jun-26	13-Jul-26	0.00
Storage Tank (TSE)		11	21-Oct-26	02-Nov-26	01-Jul-26	13-Jul-26	0.00
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	21-Oct-26	02-Nov-26	01-Jul-26	13-Jul-26	0.00
Gaurd Room		11	13-Oct-26	25-Oct-26	23-Jun-26	05-Jul-26	0.00
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	13-Oct-26	25-Oct-26	23-Jun-26	05-Jul-26	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	23-Jun-26	11-Oct-26	0.00
Pump Stations		40	13-Oct-26	21-Nov-26	23-Jun-26	01-Aug-26	0.00
PRO-SPS-CV-MF-10	Manufacturing of Civil Works for Pump Stations	40	13-Oct-26	21-Nov-26	23-Jun-26	01-Aug-26	0.00
Lift Station		40	13-Oct-26	21-Nov-26	23-Jun-26	01-Aug-26	0.00

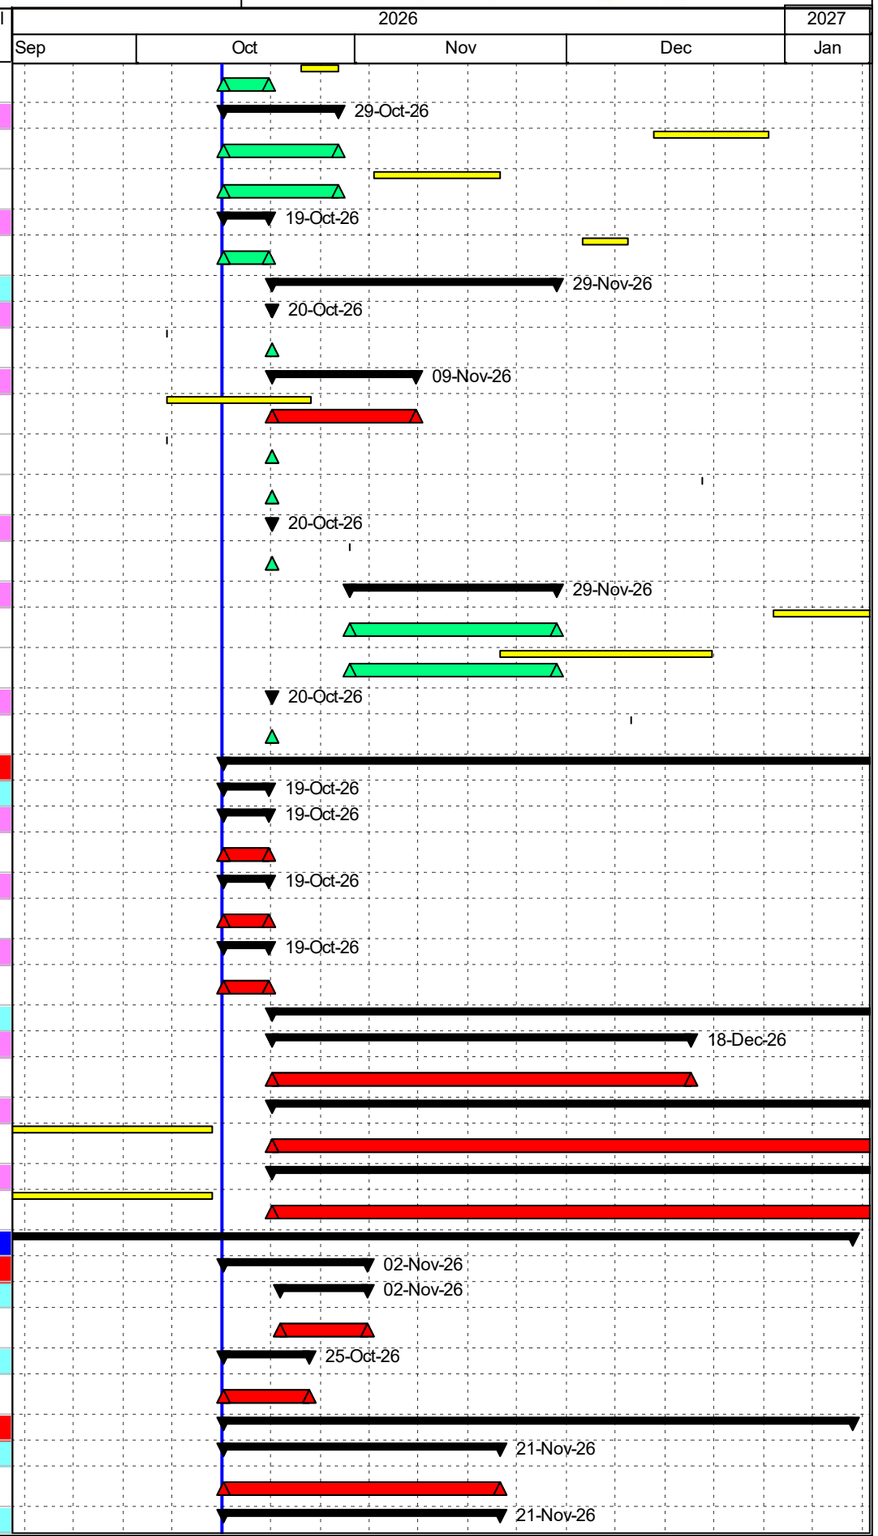


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-LS-CV-MF-30	Manufacturing of Civil Works for Civil Works for Lift Stations	40	13-Oct-26	21-Nov-26	23-Jun-26	01-Aug-26	0.00
Gaurd Room		40	25-Oct-26	04-Dec-26	05-Jul-26	14-Aug-26	0.00
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	25-Oct-26	04-Dec-26	05-Jul-26	14-Aug-26	0.00
Softscape and Planting Works		90	13-Oct-26	10-Jan-27	13-Jul-26	11-Oct-26	0.00
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	13-Oct-26	10-Jan-27	13-Jul-26	11-Oct-26	0.00
Material Delivery & Site Inspection		9	02-Aug-26 A	02-Dec-26	25-Jul-26	04-Aug-26	0.00
Pump Stations		0	02-Aug-26 A	02-Dec-26	04-Aug-26	04-Aug-26	0.00
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Pump Stations	0	02-Aug-26 A	02-Dec-26	04-Aug-26	04-Aug-26	0.00
Fence		0	02-Aug-26 A	13-Oct-26	25-Jul-26	25-Jul-26	0.00
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	13-Oct-26	25-Jul-26	25-Jul-26	0.00
Long Lead Time Items		89	01-Aug-26 A	20-Dec-26	23-Jun-26	05-Oct-26	0.00
Infrastructure Networks		20	13-Oct-26	04-Nov-26	23-Jun-26	15-Jul-26	0.00
CCTV System Wroks of Telecom Network		20	13-Oct-26	04-Nov-26	23-Jun-26	15-Jul-26	0.00
Issuance of Purchase Orders		20	13-Oct-26	04-Nov-26	23-Jun-26	15-Jul-26	0.00
PRO-CTV-LL-PO-10	Issuance of Purchase Order for Low Current Works of CCTV Complete System with All Accessories	20	13-Oct-26	04-Nov-26	23-Jun-26	15-Jul-26	0.00
Superstructure Works		81	01-Aug-26 A	20-Dec-26	04-Jul-26	05-Oct-26	0.00
Pump Stations		60	26-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
Manufacturing of Material		60	26-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	26-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
Lift Stations		60	01-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
Manufacturing of Material		60	01-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	01-Aug-26 A	20-Dec-26	07-Aug-26	05-Oct-26	0.00
Storage Tank (TSE)		30	22-Oct-26	25-Nov-26	04-Jul-26	06-Aug-26	0.00
Issuance of Purchase Orders		30	22-Oct-26	25-Nov-26	04-Jul-26	06-Aug-26	0.00
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	22-Oct-26	25-Nov-26	04-Jul-26	06-Aug-26	0.00
Construction Works		154	02-Aug-26 A	20-Dec-26	01-Jul-26	01-Dec-26	19,364,870.12
Infrastructure Networks		118	02-Aug-26 A	16-Nov-26	01-Jul-26	17-Aug-26	6,103,000.70
Earthworks		26	02-Aug-26 A	31-Oct-26	01-Jul-26	01-Aug-26	3,797,028.96
Earthworks		26	02-Aug-26 A	31-Oct-26	01-Jul-26	01-Aug-26	3,797,028.96
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	24-Oct-26	01-Jul-26	13-Jul-26	522,497.42
CO-EW-110_R	Embankments Works Upto Design Level for Earthworks(Remaining)	16	02-Aug-26 A	31-Oct-26	13-Jul-26	01-Aug-26	2,419,920.17
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	24-Oct-26	01-Jul-26	13-Jul-26	275,826.95
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	26-Oct-26	01-Jul-26	15-Jul-26	578,784.42
Storm Drainage Network		107	02-Aug-26 A	16-Nov-26	13-Jul-26	17-Aug-26	2,243,864.15
FROM MH-25:MH-12		100	02-Aug-26 A	08-Nov-26	13-Jul-26	16-Aug-26	1,837,506.72
Main Line Sections		18	02-Aug-26 A	24-Oct-26	13-Jul-26	03-Aug-26	1,787,972.67
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	15-Oct-26	13-Jul-26	16-Jul-26	496,659.08
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	18-Oct-26	16-Jul-26	22-Jul-26	893,986.33
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	24-Oct-26	22-Jul-26	03-Aug-26	397,327.26
Manholes		7	01-Nov-26	08-Nov-26	09-Aug-26	16-Aug-26	49,534.05
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	01-Nov-26	08-Nov-26	09-Aug-26	16-Aug-26	49,534.05
FROM MH-12:MH-01		14	01-Nov-26	16-Nov-26	01-Aug-26	17-Aug-26	406,357.43
Main Line Sections		14	01-Nov-26	16-Nov-26	01-Aug-26	17-Aug-26	406,357.43
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	01-Nov-26	16-Nov-26	01-Aug-26	17-Aug-26	406,357.43
Sewage Network		12	01-Nov-26	14-Nov-26	01-Aug-26	15-Aug-26	62,107.60
FROM MH-18:MH-10		12	01-Nov-26	14-Nov-26	01-Aug-26	15-Aug-26	62,107.60

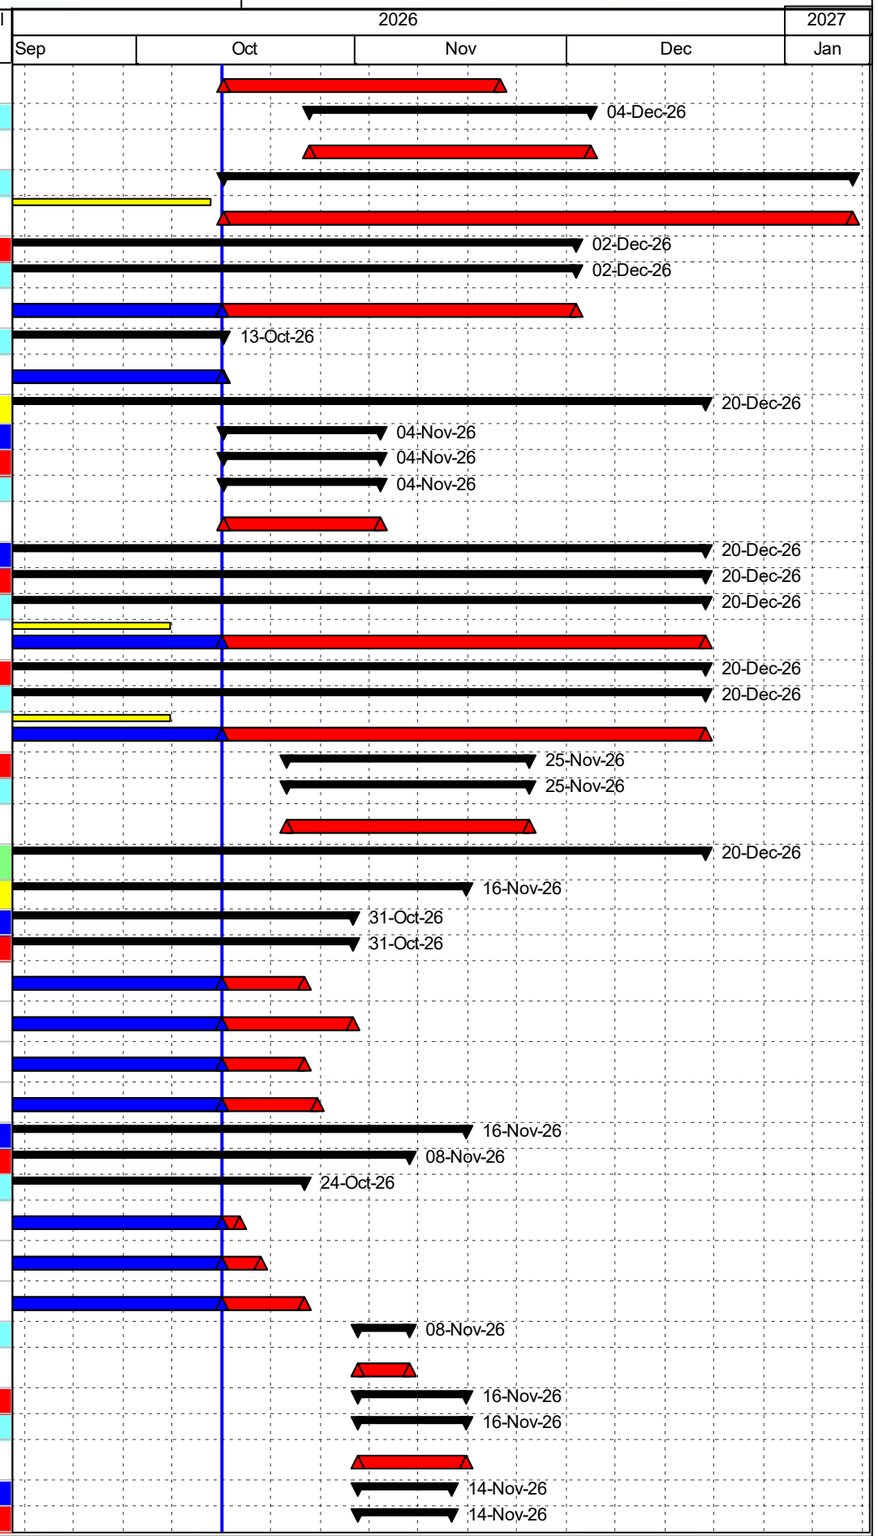


Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Main Line Sections		12	01-Nov-26	14-Nov-26	01-Aug-26	15-Aug-26	62,107.60
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	01-Nov-26	14-Nov-26	01-Aug-26	15-Aug-26	62,107.60
Superstructure Work		127	02-Aug-26 A	20-Dec-26	02-Aug-26	01-Dec-26	13,261,869.42
Utility Buildings		22	23-Sep-26 A	03-Dec-26	13-Oct-26	02-Nov-26	218,609.74
Lift Station		22	23-Sep-26 A	03-Dec-26	13-Oct-26	02-Nov-26	218,609.74
Civil work		22	23-Sep-26 A	03-Dec-26	13-Oct-26	02-Nov-26	218,609.74
Super structure		22	23-Sep-26 A	03-Dec-26	13-Oct-26	02-Nov-26	218,609.74
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	02-Dec-26	13-Oct-26	21-Oct-26	84,080.67
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	03-Dec-26	21-Oct-26	01-Nov-26	84,080.67
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	03-Dec-26	01-Nov-26	02-Nov-26	50,448.40
Fence and Gaurd Room		114	02-Aug-26 A	20-Dec-26	02-Aug-26	01-Dec-26	13,043,259.67
Fence Work		114	02-Aug-26 A	20-Dec-26	02-Aug-26	01-Dec-26	13,043,259.67
Northern Fence N01:N03		80	02-Aug-26 A	03-Nov-26	02-Aug-26	06-Sep-26	2,422,327.27
Civil Work		70	02-Aug-26 A	29-Oct-26	02-Aug-26	01-Sep-26	2,237,792.73
CO-SU-FE-N-CI-110	Pouring for Plain Concrete Northern Fence	4	02-Aug-26 A	17-Oct-26	02-Aug-26	05-Aug-26	53,454.55
CO-SU-FE-N-CI-120	Pouring R.C Footing For Northern Fence	6	02-Aug-26 A	19-Oct-26	05-Aug-26	12-Aug-26	1,494,000.00
CO-SU-FE-N-CI-130	Pouring R.C Columns For Northern Fence	5	01-Oct-26 A	25-Oct-26	12-Aug-26	18-Aug-26	649,407.27
CO-SU-FE-N-CI-140	Pouring Beams For Northern Fence	4	03-Oct-26 A	29-Oct-26	29-Aug-26	01-Sep-26	40,930.91
Finishing Work		20	29-Sep-26 A	03-Nov-26	18-Aug-26	06-Sep-26	184,534.55
Electrical Work		8	26-Oct-26	03-Nov-26	29-Aug-26	06-Sep-26	26,025.45
CO-SU-FE-N-EL-10	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	26-Oct-26	03-Nov-26	29-Aug-26	06-Sep-26	17,843.64
CO-SU-FE-N-EL-11	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	26-Oct-26	03-Nov-26	29-Aug-26	06-Sep-26	8,181.82
Architictural work		9	29-Sep-26 A	25-Oct-26	18-Aug-26	27-Aug-26	158,509.09
CO-SU-FE-N-AR-1(	Install Brick Work For Northern Fence	9	29-Sep-26 A	25-Oct-26	18-Aug-26	27-Aug-26	158,509.09
Western Fence P1 (W01:W06)		75	02-Aug-26 A	28-Nov-26	27-Aug-26	01-Nov-26	2,369,170.91
Civil Work		73	02-Aug-26 A	28-Nov-26	27-Aug-26	01-Nov-26	2,052,152.73
CO-SU-FE-WP1-CI-1	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	18-Oct-26	27-Aug-26	02-Sep-26	106,909.09
CO-SU-FE-WP1-CI-1	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	29-Oct-26	02-Sep-26	12-Sep-26	1,188,000.00
CO-SU-FE-WP1-CI-1	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	08-Nov-26	12-Sep-26	01-Oct-26	675,381.82
CO-SU-FE-WP1-CI-1	Pouring Beams For Northern Fence	17	05-Oct-26 A	28-Nov-26	12-Oct-26	01-Nov-26	81,861.82
Finishing Work		9	29-Sep-26 A	08-Nov-26	01-Oct-26	12-Oct-26	317,018.18
Architictural work		9	29-Sep-26 A	08-Nov-26	01-Oct-26	12-Oct-26	317,018.18
CO-SU-FE-WP1-AF	Install Brick Work For Northern Fence	9	29-Sep-26 A	08-Nov-26	01-Oct-26	12-Oct-26	317,018.18
Western Fence P2 (W07:W12)		58	02-Aug-26 A	06-Dec-26	22-Sep-26	09-Nov-26	2,313,014.83
Civil Work		58	02-Aug-26 A	06-Dec-26	22-Sep-26	09-Nov-26	1,943,945.73
CO-SU-FE-WP2-CI-2	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	26-Oct-26	22-Sep-26	29-Sep-26	106,909.09
CO-SU-FE-WP2-CI-2	Pouring R.C Footing For Northern Fence	7	02-Aug-26 A	28-Oct-26	29-Sep-26	07-Oct-26	1,188,000.00
CO-SU-FE-WP2-CI-2	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	31-Oct-26	07-Oct-26	18-Oct-26	567,174.83
CO-SU-FE-WP2-CI-2	Pouring Beams For Northern Fence	7	11-Oct-26 A	06-Dec-26	01-Nov-26	09-Nov-26	81,861.82
Finishing Work		12	29-Sep-26 A	07-Nov-26	18-Oct-26	03-Nov-26	369,069.09
Electrical Work		6	01-Nov-26	07-Nov-26	27-Oct-26	03-Nov-26	52,050.91
CO-SU-FE-WP2-EL	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	01-Nov-26	04-Nov-26	27-Oct-26	01-Nov-26	35,687.27
CO-SU-FE-WP2-EL	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	01-Nov-26	07-Nov-26	27-Oct-26	03-Nov-26	16,363.64
Architictural work		8	29-Sep-26 A	31-Oct-26	18-Oct-26	27-Oct-26	317,018.18

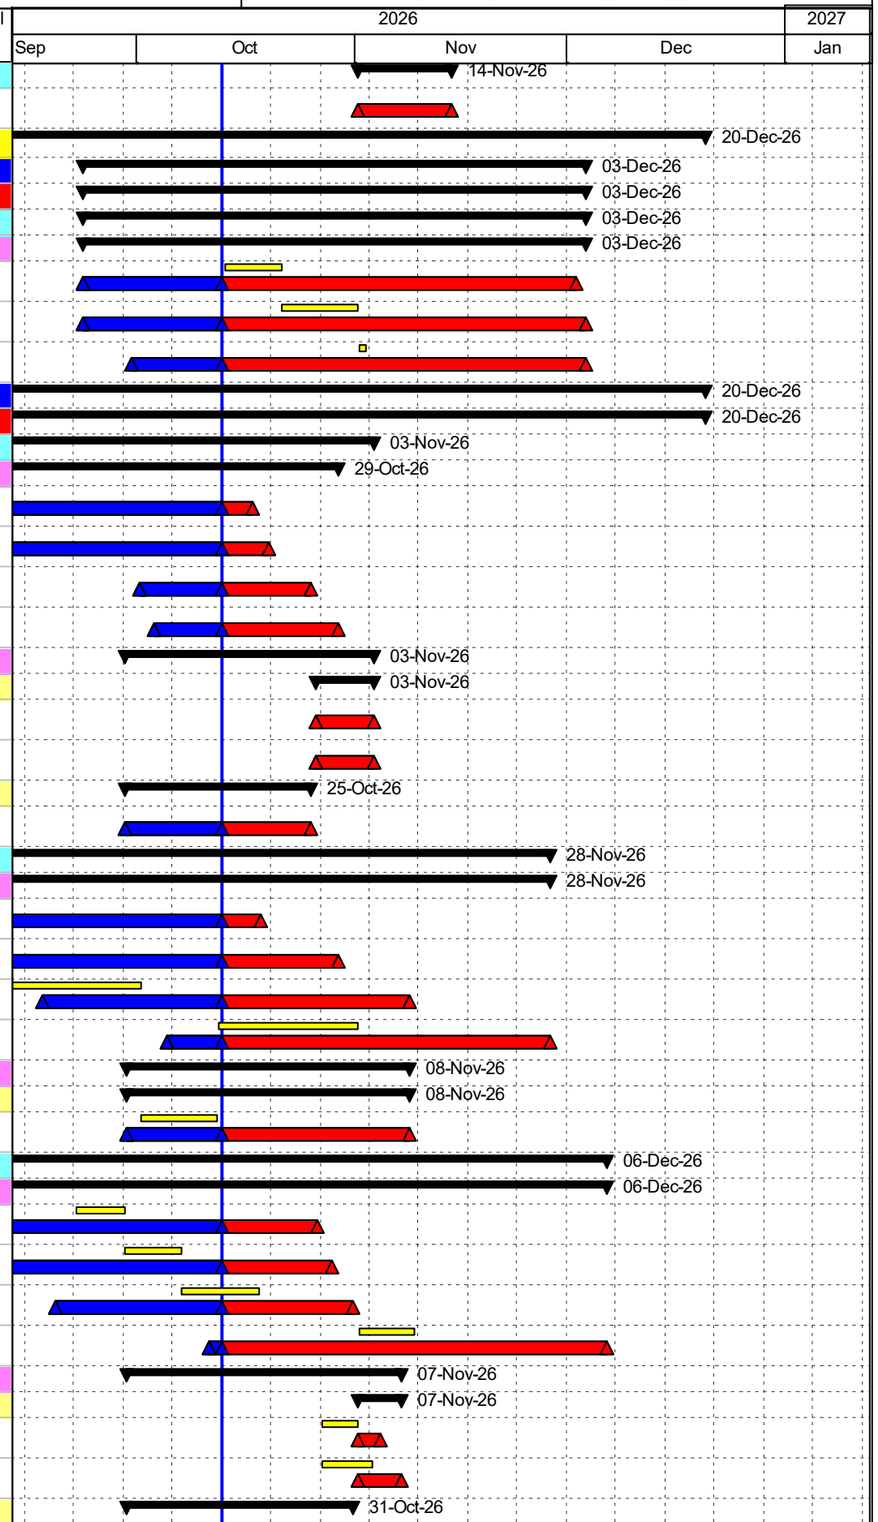


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-SU-FE-WP2-AF	Install Brick Work For Northern Fence	8	29-Sep-26 A	31-Oct-26	18-Oct-26	27-Oct-26	317,018.18
Southern Fence S01:S05		82	02-Aug-26 A	12-Nov-26	09-Aug-26	20-Sep-26	2,173,732.12
Civil Work		76	02-Aug-26 A	12-Nov-26	09-Aug-26	13-Sep-26	1,866,174.55
CO-SU-FE-S-CI-260	Pouring for Plain Concrete Northern Fence	3	02-Aug-26 A	15-Oct-26	09-Aug-26	12-Aug-26	89,090.91
CO-SU-FE-S-CI-270	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	21-Oct-26	12-Aug-26	22-Aug-26	990,000.00
CO-SU-FE-S-CI-280	Pouring R.C Columns For Northern Fence	10	05-Oct-26 A	02-Nov-26	22-Aug-26	02-Sep-26	718,865.45
CO-SU-FE-S-CI-290	Pouring Beams For Northern Fence	9	08-Oct-26 A	12-Nov-26	02-Sep-26	13-Sep-26	68,218.18
Finishing Work		21	29-Sep-26 A	12-Nov-26	02-Sep-26	20-Sep-26	307,557.58
Electrical Work		15	27-Oct-26	12-Nov-26	02-Sep-26	20-Sep-26	43,375.76
CO-SU-FE-S-EL-56	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	27-Oct-26	12-Nov-26	02-Sep-26	20-Sep-26	29,739.39
CO-SU-FE-S-EL-62	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	27-Oct-26	12-Nov-26	02-Sep-26	20-Sep-26	13,636.36
Architictural work		6	29-Sep-26 A	02-Nov-26	02-Sep-26	09-Sep-26	264,181.82
CO-SU-FE-S-AR-28	Install Brick Work For Northern Fence	6	29-Sep-26 A	02-Nov-26	02-Sep-26	09-Sep-26	264,181.82
Eastern Fence P1 (E01:E06)		68	02-Aug-26 A	21-Nov-26	26-Aug-26	25-Oct-26	2,212,603.64
Civil Work		68	02-Aug-26 A	21-Nov-26	26-Aug-26	25-Oct-26	1,895,585.45
CO-SU-FE-EP1-CI-3	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	21-Oct-26	26-Aug-26	05-Sep-26	106,909.09
CO-SU-FE-EP1-CI-3	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	26-Oct-26	05-Sep-26	19-Sep-26	1,188,000.00
CO-SU-FE-EP1-CI-3	Pouring R.C Columns For Northern Fence	15	06-Oct-26 A	12-Nov-26	19-Sep-26	07-Oct-26	518,814.55
CO-SU-FE-EP1-CI-3	Pouring Beams For Northern Fence	7	08-Oct-26 A	21-Nov-26	17-Oct-26	25-Oct-26	81,861.82
Finishing Work		8	29-Sep-26 A	12-Nov-26	07-Oct-26	17-Oct-26	317,018.18
Architictural work		8	29-Sep-26 A	12-Nov-26	07-Oct-26	17-Oct-26	317,018.18
CO-SU-FE-EP1-AR	Install Brick Work For Northern Fence	8	29-Sep-26 A	12-Nov-26	07-Oct-26	17-Oct-26	317,018.18
Eastern Fence P2 (E07:E13)		61	02-Aug-26 A	20-Dec-26	04-Oct-26	01-Dec-26	1,552,410.91
Civil Work		61	02-Aug-26 A	20-Dec-26	04-Oct-26	01-Dec-26	1,182,556.36
CO-SU-FE-EP2-CI-3	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	12-Nov-26	04-Oct-26	18-Oct-26	124,727.27
CO-SU-FE-EP2-CI-3	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	12-Nov-26	18-Oct-26	01-Nov-26	486,000.00
CO-SU-FE-EP2-CI-3	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	12-Nov-26	01-Nov-26	12-Nov-26	476,323.64
CO-SU-FE-EP2-CI-3	Pouring Beams For Northern Fence	10	01-Oct-26 A	20-Dec-26	19-Nov-26	01-Dec-26	95,505.45
Finishing Work		6	29-Sep-26 A	08-Dec-26	12-Nov-26	19-Nov-26	369,854.55
Architictural work		6	29-Sep-26 A	08-Dec-26	12-Nov-26	19-Nov-26	369,854.55
CO-SU-FE-EP2-AR	Install Brick Work For Northern Fence	6	29-Sep-26 A	08-Dec-26	12-Nov-26	19-Nov-26	369,854.55
Testing and Comissioning		0	13-Oct-26	13-Oct-26	04-Jan-27	04-Jan-27	0.00
Utility Buildings		0	13-Oct-26	13-Oct-26	04-Jan-27	04-Jan-27	0.00
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	13-Oct-26	13-Oct-26	04-Jan-27	04-Jan-27	0.00
Handing over and close out		14	13-Oct-26	28-Oct-26	04-Jan-27	19-Jan-27	0.00
As-Built		14	13-Oct-26	28-Oct-26	04-Jan-27	19-Jan-27	0.00
HO-130	Submission As-Built Drawing For Pond	14	13-Oct-26	28-Oct-26	04-Jan-27	19-Jan-27	0.00

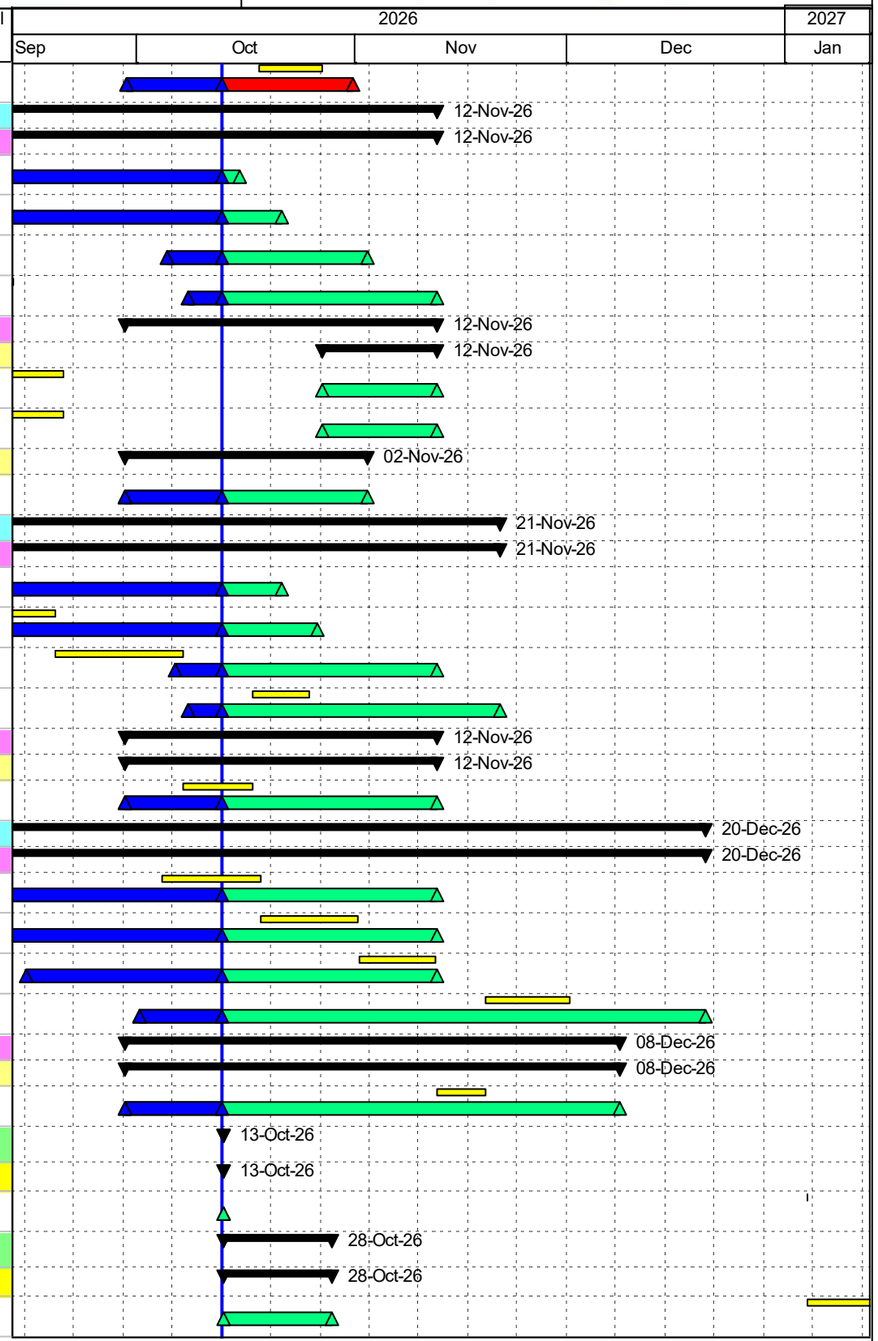

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
