Development of Infrastructure Networks, 3rd Industrial City in Dammam, Phase 2 Part 2, Zone J

تطوير شبكات البنية التحتية للمدينة الصناعية الثالثة بالدمام المرحلة الثانية الجزء الثاني - المنطقة J

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ANSAB General Contracting	EGIS	Eng. Mohammed Al-Aissa	12-Jan-2025	11-Jan-2027

Scope: collector and local roads, potable water, sewerage, storm drainage, irrigation, medium-voltage, street lighting and telecom networks, a sewage pump station and storm drainage ponds for Block J. Contract value 117.4M SAR excluding VAT, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 13-Oct-2026 data date the project is 54.8% complete against 85.3% planned, behind by 30.5% (SPI 0.64). The weekly report states 3.4% gained this week against 1.4% planned.

PHYSICAL % COMPLETE

54.8% / 85.3% plan

▼ SPI 0.64 –30.5%

PROGRESS THIS WEEK

+3.4% / +1.4% plan

▲ 2.0% above the weekly plan

CONTRACT TIME ELAPSED

87.7% · day 639 of 729

▼ Forecast finish 31-Aug-2027

INVOICED TO DATE (GROSS)

37.0% · 43.4M SAR

19 invoices, last period ends 31-Aug-2026

The project is forecast to finish about seven and a half months late.

The weekly report and the P6 update (data date 20-Oct-2026) both forecast completion on 31-Aug-2027, 232 days after the contract completion date of 11-Jan-2027. The P6 completion milestone has –189.5 days of float. With 87.7% of the contract time used, 45.2% of the physical work remains, and every network completion milestone is between 124 and 207 days negative in P6.

Site photos this week

Six photos uploaded with this week's report. Where the camera stamp is visible it reads 11-Oct-2026 or 15-Oct-2026, 3rd Industrial City, Dammam. Chambers on the twin storm lines, catch basins and road formation works are shown. Select a photo to view it larger, then use the arrows to move between photos.



Twin-line chamber reinforcement

Steel cage for a chamber over the twin GRP pipes. Stamped 11-Oct-2026, 10:26.



Chamber at a pipe junction

Reinforcement fixed around the GRP pipe junction, excavator working alongside. Stamped 11-Oct-2026, 10:13.



Catch basin installed

Precast catch basin CB-BJ1-SWD-18 with its connection pipe laid in the trench.



Trench excavation

Trench along the asphalted road, with a catch basin set further along.



Compaction in the road corridor

Plate compactor on the formation. GPS-stamped 15-Oct-2026, 11:29.




Road formation

Graded formation being watered, with lighting poles along the edge. Stamped 15-Oct-2026, 11:39.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

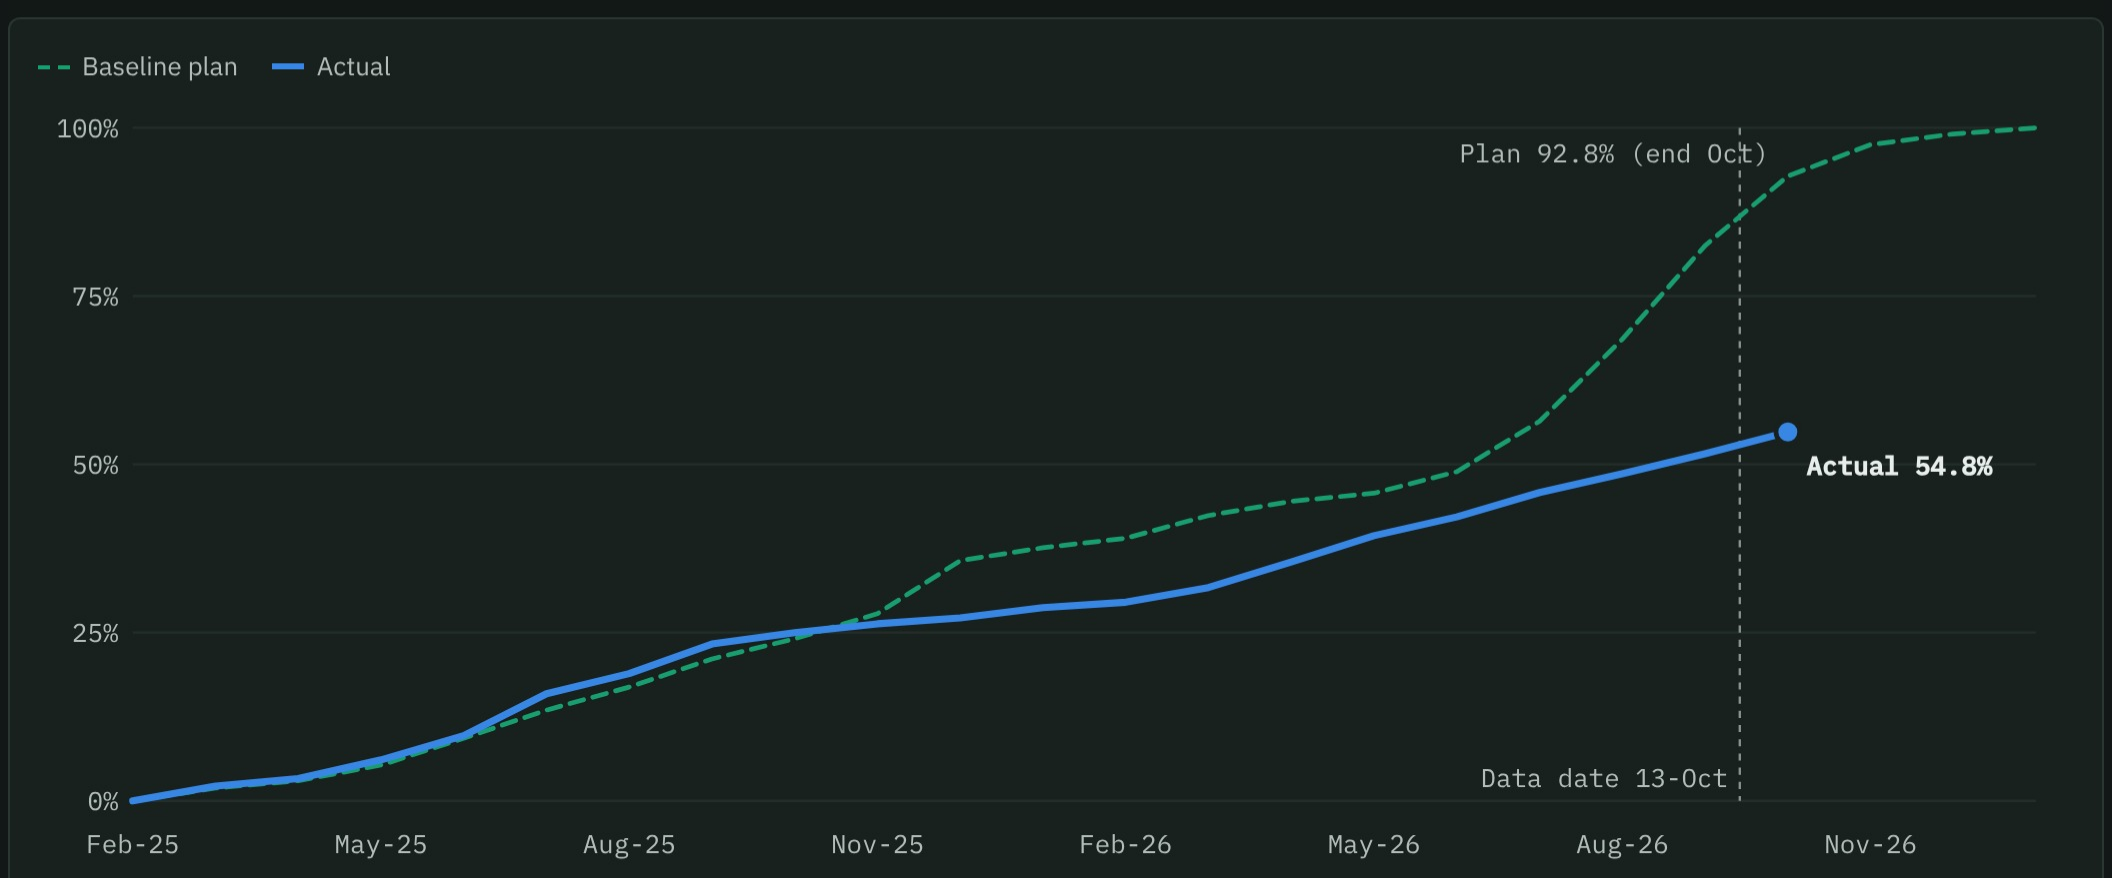

MONTH ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS MONTH	SPI
May-2026	45.7	39.4	−6.3	+3.9	0.86
Jun-2026	48.9	42.3	−6.6	+2.9	0.86
Jul-2026	56.4	45.8	−10.6	+3.6	0.81
Aug-2026	68.6	48.6	−20.0	+2.8	0.71
Sep-2026	82.5	51.6	−30.9	+3.0	0.63
13-Oct-2026	**85.3***	**54.8**	**−30.5**	**+3.2**	**0.64**

Only the latest weekly report is used, and it has no weekly history, so the table is monthly. * Planned value at the data date from the report cover; the plan for the end of October is 92.8%. The project has gained about 3% a month since May while the plan has been rising by 8–14% a month.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Earthworks network	8.3%	100.0%	100.0%	0.0	1.00	✓ Complete
Irrigation network	3.5%	94.9%	21.4%	−73.4	0.23	▼ Behind
Potable water network	4.1%	89.1%	33.8%	−55.3	0.38	▼ Behind
Medium-voltage network	3.6%	95.0%	76.8%	−18.3	0.81	▼ Behind
Street lighting network	12.5%	100.0%	26.3%	−73.7	0.26	▼ Behind
Telecom network	2.2%	100.0%	54.6%	−45.4	0.55	▼ Behind
Roads network	33.2%	68.7%	53.2%	−15.6	0.77	▼ Behind
Sewage network	17.6%	86.6%	54.9%	−31.7	0.63	▼ Behind
Storm drainage network	15.1%	92.4%	65.3%	−27.1	0.71	▼ Behind
Total	100%	**85.3%**	**54.8%**	**−30.5**	**0.64**	▼ Behind

Engineering, procurement and testing carry no man-hours in the physical measure and are not listed. By cost-based earned value the project is at 75.8% against 85.8% planned (SPI 0.88), but that is not the main progress measure. The P6 update (data date 20-Oct-2026) has 1,921 activities: 1,221 completed, 64 in progress and 636 not started. Its scheduled finish is 31-Aug-2027, 232 days after the contract date.

Scope of work: quantities

Total, executed and remaining length of each network, from the execution summary in the Arabic progress summary sheet. The report gives no previous cumulative quantities, so the "this week" column shows "–". The work done this week is listed in the second table, from the report's weekly activities sheet.

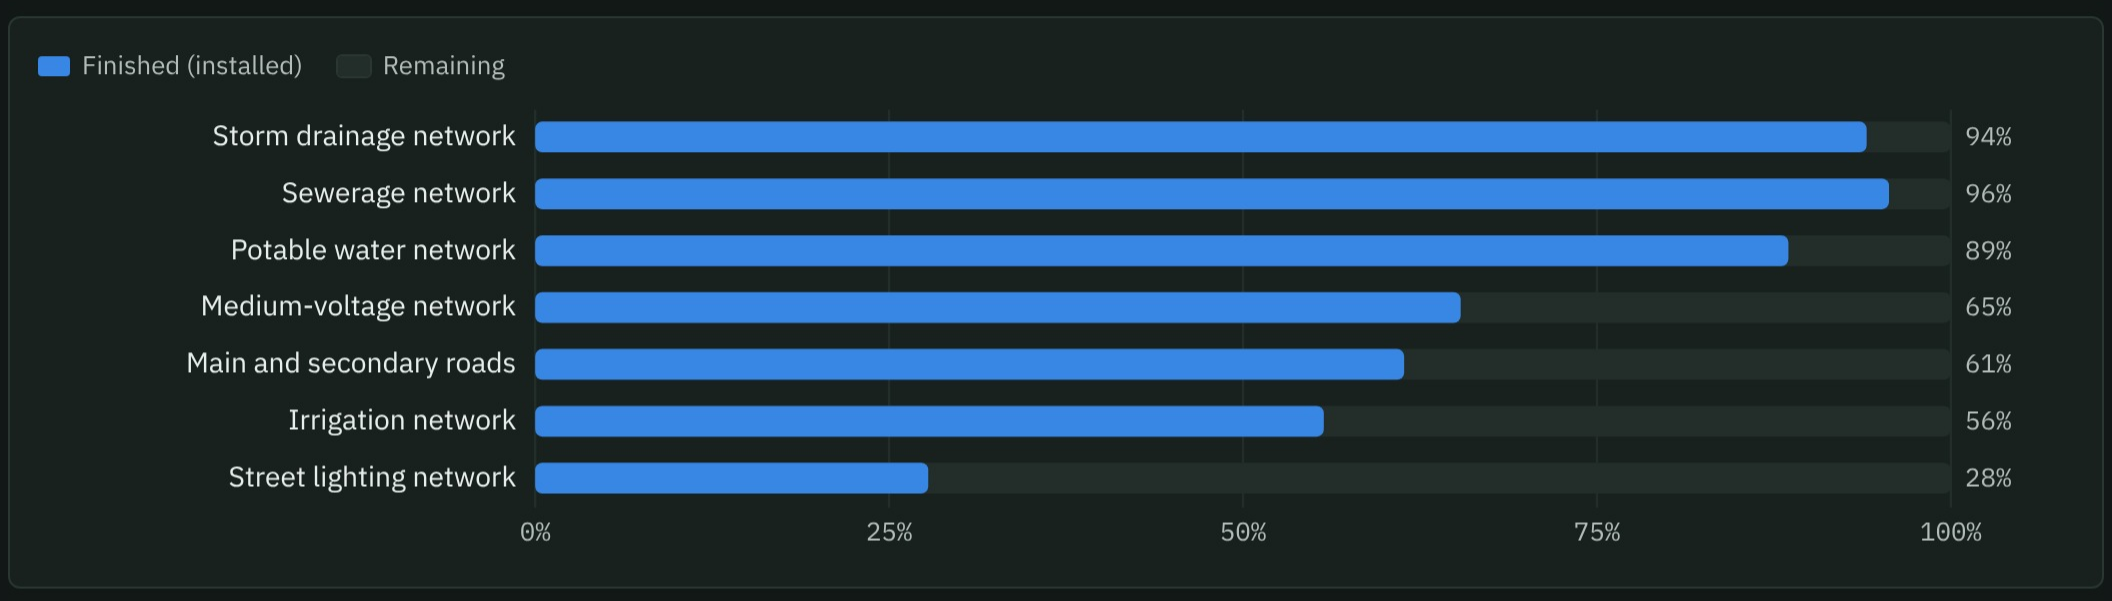

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Storm drainage network	Block J	LM	18,554	17,450	–	1,104	94.0%	–
Sewerage network	Block J	LM	9,152	8,752	–	400	95.6%	–
Potable water network	Block J	LM	12,200	10,800	–	1,400	88.5%	–
Medium-voltage network	Block J	LM	17,328	11,328	–	6,000	65.4%	–
Main and secondary roads	Block J	LM	8,146	5,000	–	3,146	61.4%	–
Irrigation network	Block J	LM	14,494	8,074	–	6,420	55.7%	–
Street lighting network	Block J	LM	12,786	3,550	–	9,236	27.8%	–

Work executed this week

NETWORK	ACTIVITY	LOCATION	UNIT	THIS WEEK	NEXT WEEK
Storm drainage	Branch pipe excavation and laying	RD 9	LM	155	500
Storm drainage	Twin-line chambers	RD 9	EA	2	4
Storm drainage	Manholes installed	RD 9, RD 10	EA	3	5
Storm drainage	Catch basins installed	RD 9, RD 10	EA	7	20
Sewerage	Main pipe excavation and laying	RD 9, RD EXT	LM	448	348
Potable water	Main pipe excavation and laying	RD 10, RD 14	LM	80	400
Irrigation	Main pipe excavation and laying	RD 10, RD EXT	LM	531	531
Medium voltage	Cable trench and cable laying	RD EXT	LM	1,500	1,500

Furthest behind

Street lighting is 27.8% executed (3,550 of 12,786 LM): no LED luminaires, earthing, road-crossing ducts or draw pits have been installed. Irrigation is 55.7% and roads 61.4%. Traffic markings, signs and fire hydrants (0 of 55) have not started.

Close to finished

Sewerage is 95.6% and storm drainage 94.1% executed by length, and potable water 88.5%. The storm box conduit (2,051 m) is complete. Catch basins remain at 207 of 505 and the storm drainage ponds and sewage pump station are still under construction.

Milestones

Baseline and forecast dates from the weekly report's milestone table, against the P6 update of 20-Oct-2026. Days in brackets are the delay the weekly report gives against the baseline.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	12-Jan-2025	12-Jan-2025	12-Jan-2025 (actual)	–	✓ Done
Complete mobilisation	12-Mar-2025	12-Mar-2025	09-Mar-2025 (actual)	–	✓ Done
Shop drawings and materials approved	10-Feb-2025	11-Feb-2025	24-May-2025 (actual)	–	✓ Done
Earthworks network	24-May-2026	31-May-2025	–	–	✓ Done
Telecom network	28-Sep-2026	07-Apr-2027 (+191 d)	13-Mar-2027	−160	▼ Late
Irrigation network	23-Aug-2026	05-May-2027 (+255 d)	05-May-2027	−158	▼ Late
Potable water network	05-Oct-2026	03-Jul-2027 (+271 d)	19-Jun-2027	−173	▼ Late
Sewage network	06-Oct-2026	29-Jun-2027 (+266 d)	15-Jun-2027	−179	▼ Late
Medium-voltage network	17-Oct-2026	17-Apr-2027 (+182 d)	27-Mar-2027	−124	▼ Late
Road works	21-Oct-2026	17-Aug-2027 (+300 d)	17-Aug-2027	−189.5	▼ Late
Street lighting network	20-Dec-2026	15-Jul-2027 (+207 d)	24-Jun-2027	−207	▼ Late
Storm drainage network	–	13-Jul-2027	05-Jul-2027	−167	▼ Late
Storm drainage ponds	–	–	25-Apr-2027	−104	▼ Late
Sewage pump station	–	–	30-May-2027	−129	▼ Late
Tie-in to existing networks	–	–	17-Aug-2027	−186.5	▼ Late
Project completion	11-Jan-2027	31-Aug-2027 (+232 d)	31-Aug-2027	−189.5	▼ Late

The two forecasts agree on completion but not on the network milestones.

Both give 31-Aug-2027 for project completion and the same dates for irrigation and road works. For telecom, potable water, sewage, medium voltage, street lighting and storm drainage the P6 update is 8 to 25 days earlier than the weekly report. The Employer's NOC for the medium-voltage network is the only control milestone not yet achieved; P6 schedules it for 14-Dec-2026 with −39 days of float.

Procurement of key materials

Share of the required quantity delivered to site. Source: Procurement sheet, weekly report 13-Oct-2026. All listed materials are approved.

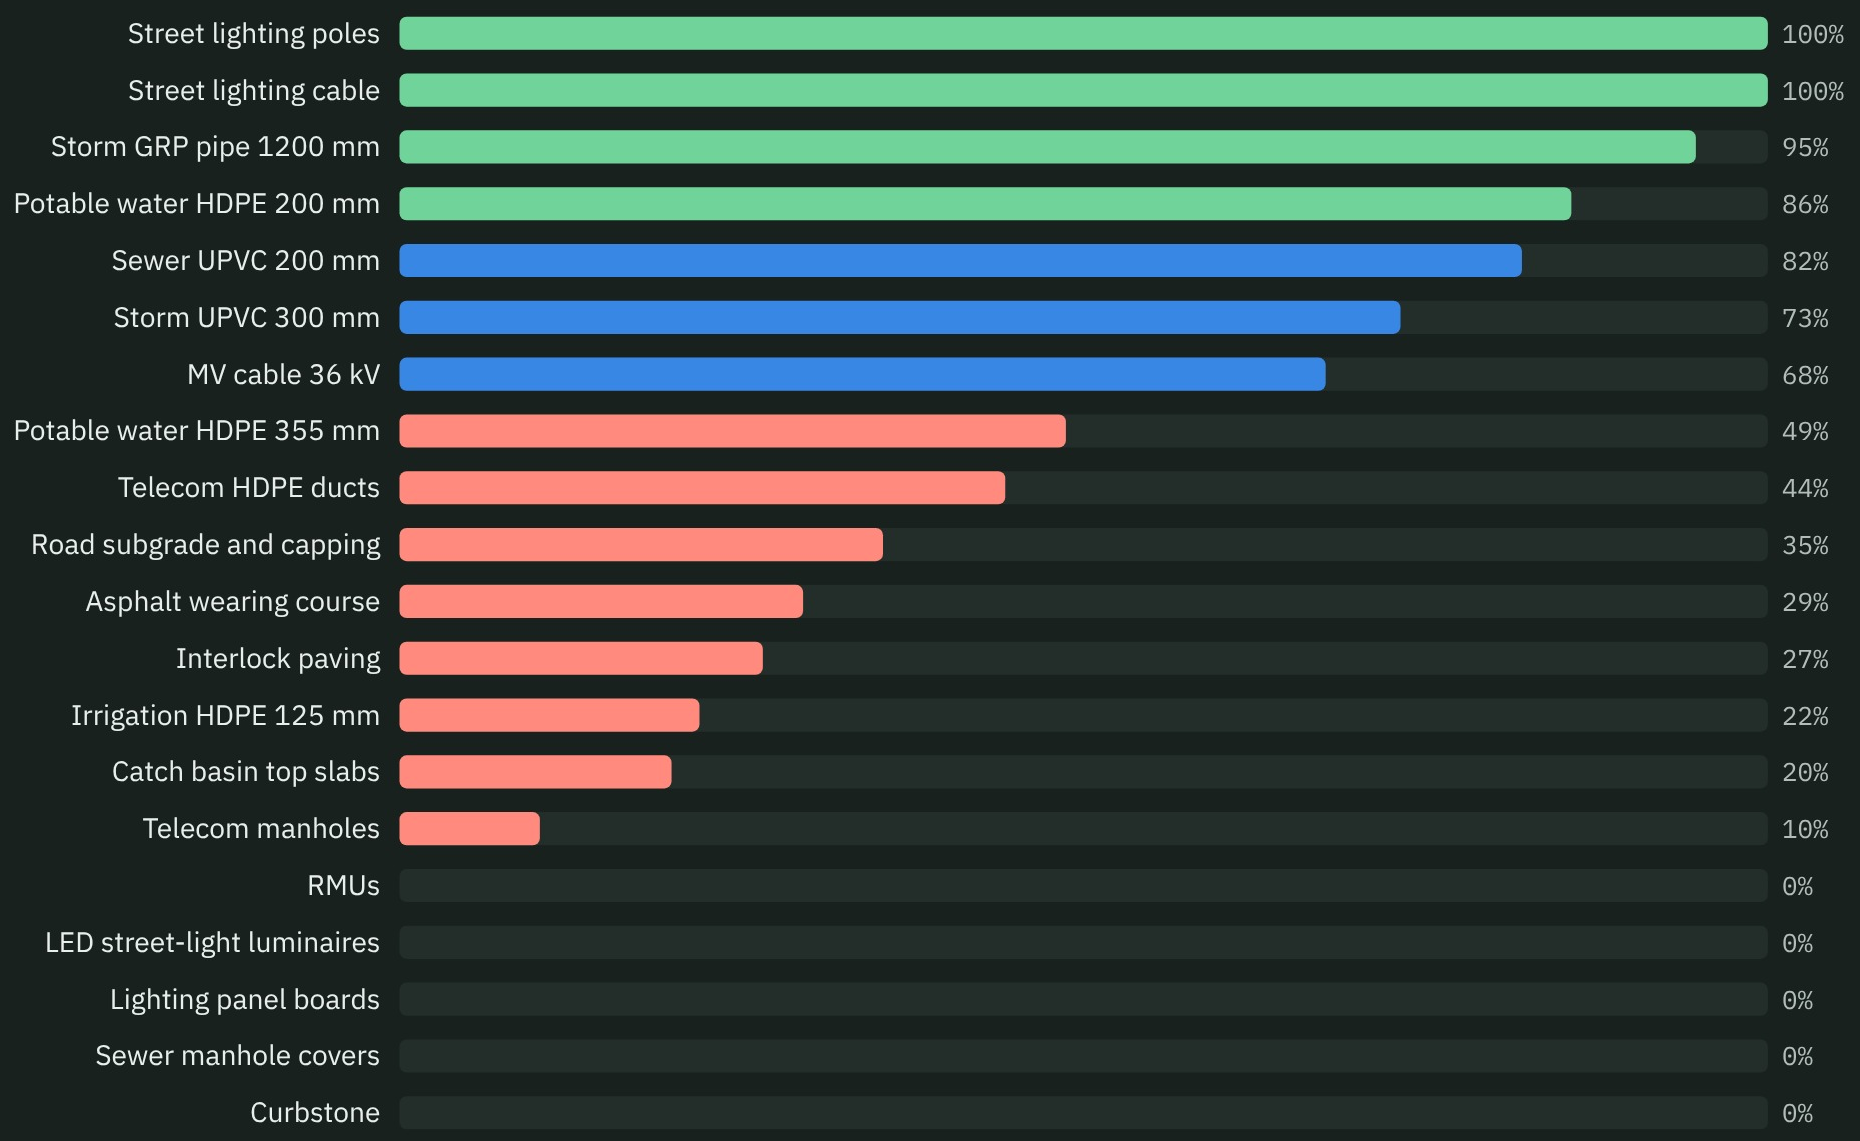

Nothing delivered yet for several items on the critical networks


RMUs (0 of 9), LED street-light luminaires (0 of 363), lighting panel boards (0 of 6), curbstone (0 of 42,552 pieces), sewer manhole covers (0 of 129) and storm covers and gratings. The register rates delay in long-lead materials as a high risk.

Telecom, irrigation and road layers lag

Telecom ducts are 44% delivered and telecom manholes 8 of 78. Irrigation 125 mm pipe is 22% delivered, catch-basin top slabs 20%, and road-layer materials (capping, subgrade, base course, asphalt, interlock) 17–35%. MV cable is at 8,378 of 12,378 m.

Manpower

Head count on site this month by trade, planned vs actual. Source: Manpower sheet. The report has no monthly history.

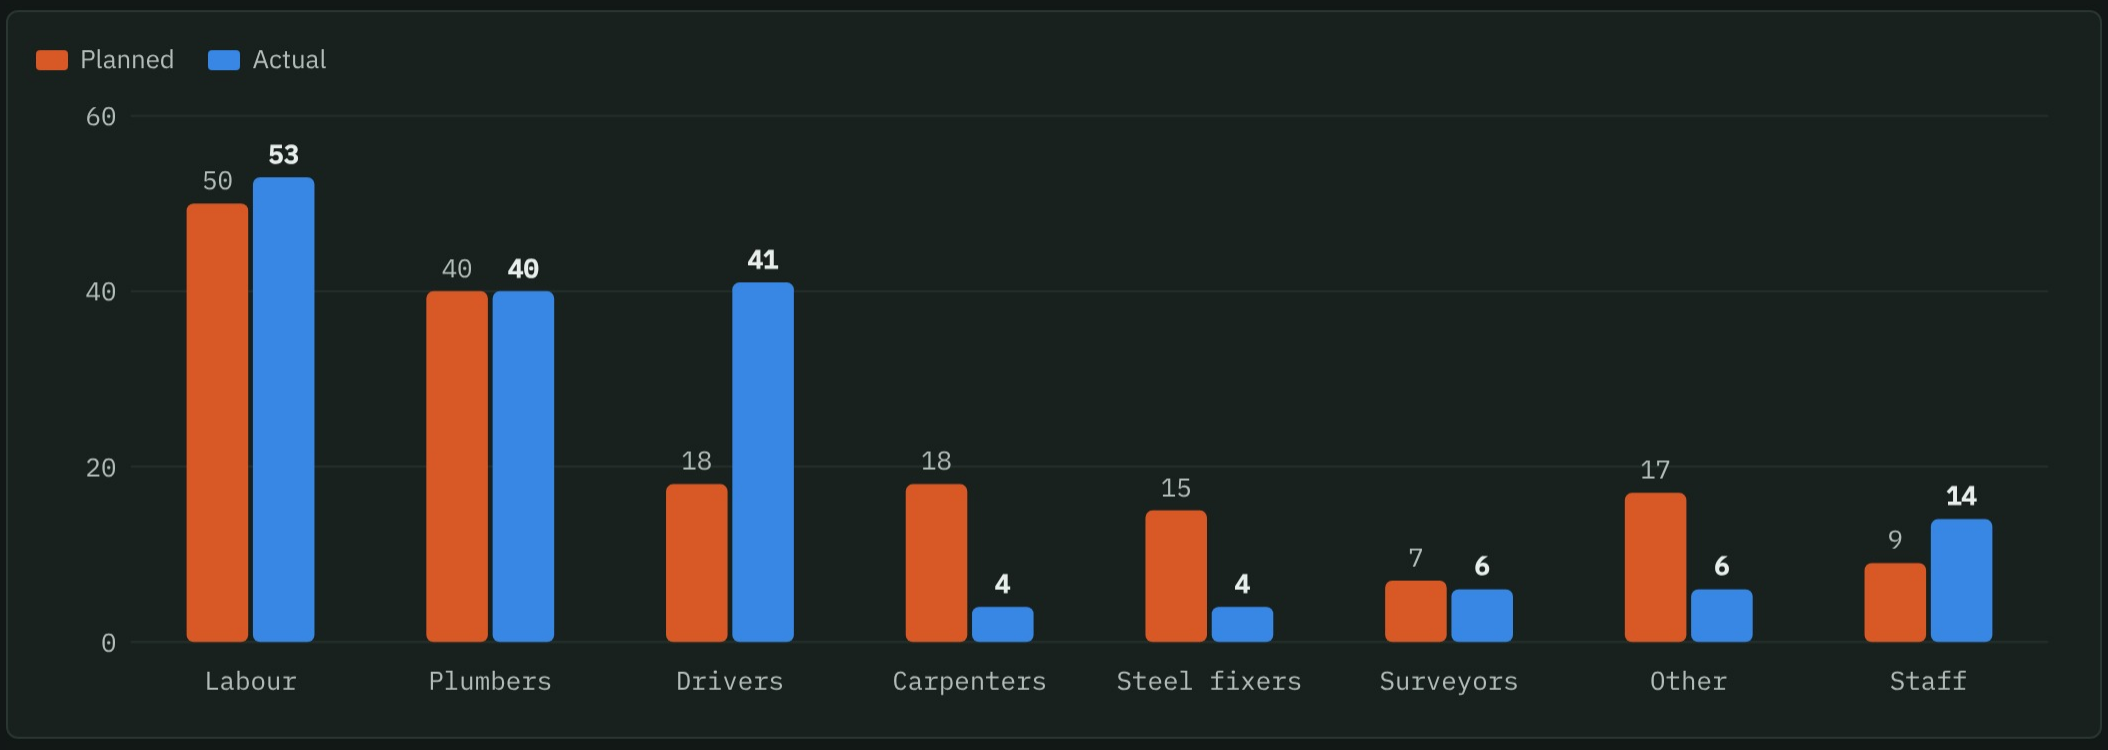

Total head count is 166 against 174 planned: 152 manual workers against 165 and 14 staff against 9. Carpenters and steel fixers are well below plan (4 of 18 and 4 of 15), while drivers and operators are above it (41 of 18). Equipment on site is 74 units against 14 planned.

Cost and invoicing

Contract value

Roads and paving	31,308,119
Storm water drainage	33,717,595
Sewerage and lift stations	24,177,287
Potable water	10,220,942
Irrigation	6,738,491
Street lighting and telecom	6,440,353
Medium voltage	4,788,987
BOQ total (excl. VAT)	**117,391,774**
Contract value incl. 15% VAT	135,000,540
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. The change order log is empty; the report lists one potential change.

Invoices

Advance payment (10%)	11,739,177
Progress invoices submitted	19
Gross value	43,414,468
Advance payment recovered	4,341,447
Retention / penalties	0 / 0
Approved by MODON PM	43,414,468
Paid (18 invoices)	40,094,952
Earned value to date	88,941,456

Invoicing is 37.0% of the contract value against 54.8% physical progress and 75.8% earned value. Invoice 19 (01-Jul to 31-Aug-2026, 3,319,515 SAR gross) is approved and awaiting payment.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	389,098
Man-hours this week	9,120
Lost-time injuries	0
Fatalities	0
First-aid cases	5
Near misses	1
Property damage	0
Inductions / toolbox talks	94 / 314

Cumulative figures. This week: 2 inductions and 6 toolbox talks.

Quality Score 0.90

FIRs issued (cumulative)	1,847
FIRs closed	1,757
FIRs pending (0–10 days)	90
NCRs issued / closed	21 / 21
Site instructions issued / closed	13 / 12
MIRs issued	0
Shop drawings submitted (all code B)	23
Material submittals (A / B / C / D)	1 / 72 / 2 / 1

NCRs close in 7 days on average. 7 material submittals are still to be approved.

Open issues and risks

ISSUE	OWNER	DETAIL
Schedule delay	Contractor	Forecast completion 31-Aug-2027, 232 days late. The report shows 406 failed-start activities (411 last week) and 669 critical-path activities. No recovery schedule approval is recorded.
Long-lead materials	Contractor	Risk 05, rated high and open: delays in long-lead materials could stop work. Mitigation: chase suppliers and get MODON approval for alternative sources. Target 20-Nov-2026.
Tie-in to existing networks	Contractor / MODON	Risk 01, rated low and open: existing infrastructure may not be ready for the tie-ins, delaying commissioning and handover. P6 tie-in milestone 17-Aug-2027, –186.5 days of float.
Testing and commissioning	Contractor	Network testing was planned to start from 12-Oct-2026 (telecom) and 18-Oct-2026 (irrigation). None has started; the forecast starts run from 12-Nov-2026 to 04-Jan-2027.
MV network NOC	Contractor	The Employer's NOC for the medium-voltage network is still outstanding (P6: 14-Dec-2026, –39 days).

Closed in the registers: groundwater and dewatering (high), delayed or failed testing, and the two logged issues (irrigation connection point, pump-station force main). The BOQ re-measurement saving is recorded as a realised opportunity.

Data notes

Only the files in the latest upload (W3) were used.

- Data dates differ: the weekly report (report 92) is dated 13-Oct-2026, while the P6 update, the failed-start list and the PDF exports are dated 20-Oct-2026. This report uses 13-Oct-2026 as its data date and shows P6 figures as of 20-Oct-2026.
- Week 91 is counted from site handover (12-Jan-2025 to 13-Oct-2026 is 639 days), matching "contract week 91 of 104" in the report's milestone sheet. The workbook itself is numbered report 92.
- The four P6 PDF exports (Level 5, look-ahead, WBS summary, remaining works) could not be converted to text, so they were not used.
- On the report cover the physical progress by WBS is shifted by one row (Earthworks shows Irrigation's man-hours, and so on). The figures were taken from the Progress sheet, where they line up with the P6 table.
- The Arabic summary sheet labels 85.79% planned and 75.76% actual as "progress". These are cost-based earned value. Physical progress is 85.32% planned and 54.81% actual.
- The "weekly" physical progress on the cover (603 man-hours planned, 1,493 earned) equals the whole October month-to-date in the Physical-Chart Data sheet. Weekly earned value (2,593,776 SAR) also equals the October figure. The "this week" values may therefore be month-to-date.
- The "Last week vs this week" sheet is still based on the P6 updates of 21-Apr and 28-Apr-2026, so it was not used.

- The physical forecast in the chart data reaches 100% in January 2027, which contradicts the forecast completion of 31-Aug-2027.
- Network totals in the Arabic summary sheet do not match the Major Quantities sheet. For example, potable water is 12,200 LM against 9,720 m of pipe, and medium voltage is 17,328 LM against 19,500 m of cable. The summary also gives 100% supply for MV and street lighting, while the procurement log shows MV cable at 68% and RMUs and luminaires at 0%.
- The summary sheet gives site handover as 12-Feb-2025 (12-Jan-2025 in the weekly report). Its milestone dates also differ from the weekly report baseline: for example, roads 20-Dec-2026 against 21-Oct-2026.
- The procurement log has deliveries above the required quantity: sewer GRP 400 mm SN5000 1,060 of 261 m, irrigation 110 mm couplings 322 of 58, and telecom spacers 5,500 of 4,405. The 250 mm coupling has a required quantity of 0. Two asphalt units read "m132" and "m133".
- Manual head count is 152 on the cover, 154 in the trade table, and 113 in the cover's trade total, which leaves out drivers and operators. The next-month manual forecast of 1,148 looks wrong, and the weekly manpower rows repeat the same values.
- The HSE inspection sheet covers 26-Aug to 01-Sep-2026, not this week.
- Several cover fields show #REF ! (EAC, top issues). The invoice log has stray values of 21,100,000 and 20,900,000 under revised contract value and EAC.
- Storm drainage is 33,717,565 SAR in the Arabic summary sheet and 33,717,595 SAR in invoice 19. The latter matches the BOQ total.
- The earthworks milestone has a baseline of 24-May-2026 but was finished on 31-May-2025. The look-ahead sheet gives an expected finish of 22-Feb-2026, which is already past.
- Photos: one upload is a duplicate, one is too small (384 px), and one is a framed presentation graphic ("MODON 2 — Steel Reinforcement Works"). These were not used.

Compiled 28-Oct-2026 from the latest weekly upload (W3): weekly report 92 (data date 13-Oct-2026) and the P6 update of 20-Oct-2026.
