

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		219	12-Feb-26	16-Feb-27	7,747,393.06	3,271,332.41	3,241,656.30	42.22%	41.84%
PROJECT MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-007	Completion of Site levelling, local roads & parkings	0		12-Feb-26	0.00	0.00	0.00	100%	0%
CONSTRUCTION (67%)		219	20-May-26	16-Feb-27	7,432,092.48	3,046,238.12	2,982,951.55	40.99%	40.14%
RBF 900 SQM FACTORIES		219	20-May-26	16-Feb-27	6,605,490.27	2,297,936.97	2,347,598.61	34.79%	35.54%
BLOCK B6		161	20-May-26	07-Nov-26	479,199.75	182,700.73	52,969.74	38.13%	11.05%
STRUCTURAL		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	06-Jun-26	21-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B6-SS-104	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-106	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DOORS & WINDOWS		7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B6-A-101	Window (CW1)	7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
ELECTRICAL		161	20-May-26	07-Nov-26	357,224.22	60,725.20	52,969.74	17%	14.83%
FIRST STAGE		161	20-May-26	01-Nov-26	69,188.18	60,725.20	27,642.87	87.77%	39.95%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	14-Oct-26	18-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	36,389.98	36,389.98	0.00	100%	0%
SECOND STAGE		12	28-Oct-26	07-Nov-26	288,036.05	0.00	25,326.87	0%	8.79%
DAM3-C-B6-E-730	Installation of Solar power plant	7	31-Oct-26	07-Nov-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	185.40	0.00	0.00	0%	0%
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weather	2	04-Nov-26	05-Nov-26	3,082.69	0.00	0.00	0%	0%
BLOCK B5		118	14-Jun-26	23-Nov-26	662,999.66	409,730.95	90,511.95	61.8%	13.65%
STRUCTURAL		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
DAM3-C-B5-S-127	Concrete pad	7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	14-Jun-26	27-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B5-SS-102	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-104	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		17	28-Jun-26	24-Aug-26	316,333.25	316,333.25	37,542.21	100%	11.87%
WALL FINISHES		7	17-Aug-26	24-Aug-26	44,167.30	44,167.30	37,542.21	100%	85%
DAM3-C-B5-A-150	Paint to Plaster (Primer, Putty & First Coat)	7	17-Aug-26	24-Aug-26	44,167.30	44,167.30	37,542.21	100%	85%
CIELING FINISHES		5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B5-A-151	Installation of Ceiling Gypsum Board	5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DOORS & WINDOWS		12	28-Jun-26	11-Jul-26	225,373.65	225,373.65	0.00	100%	0%
DAM3-C-B5-A-183	Window (CW1)	7	28-Jun-26	05-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B5-A-146	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-147	Supply and install (D5) 1000*2200mm single leaf steel doc	1	07-Jul-26	07-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-153	Supply and install (D4) 800*2200 mm single leaf aluminum	1	08-Jul-26	08-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-154	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	09-Jul-26	09-Jul-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-176	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	11-Jul-26	11-Jul-26	16,016.16	16,016.16	0.00	100%	0%

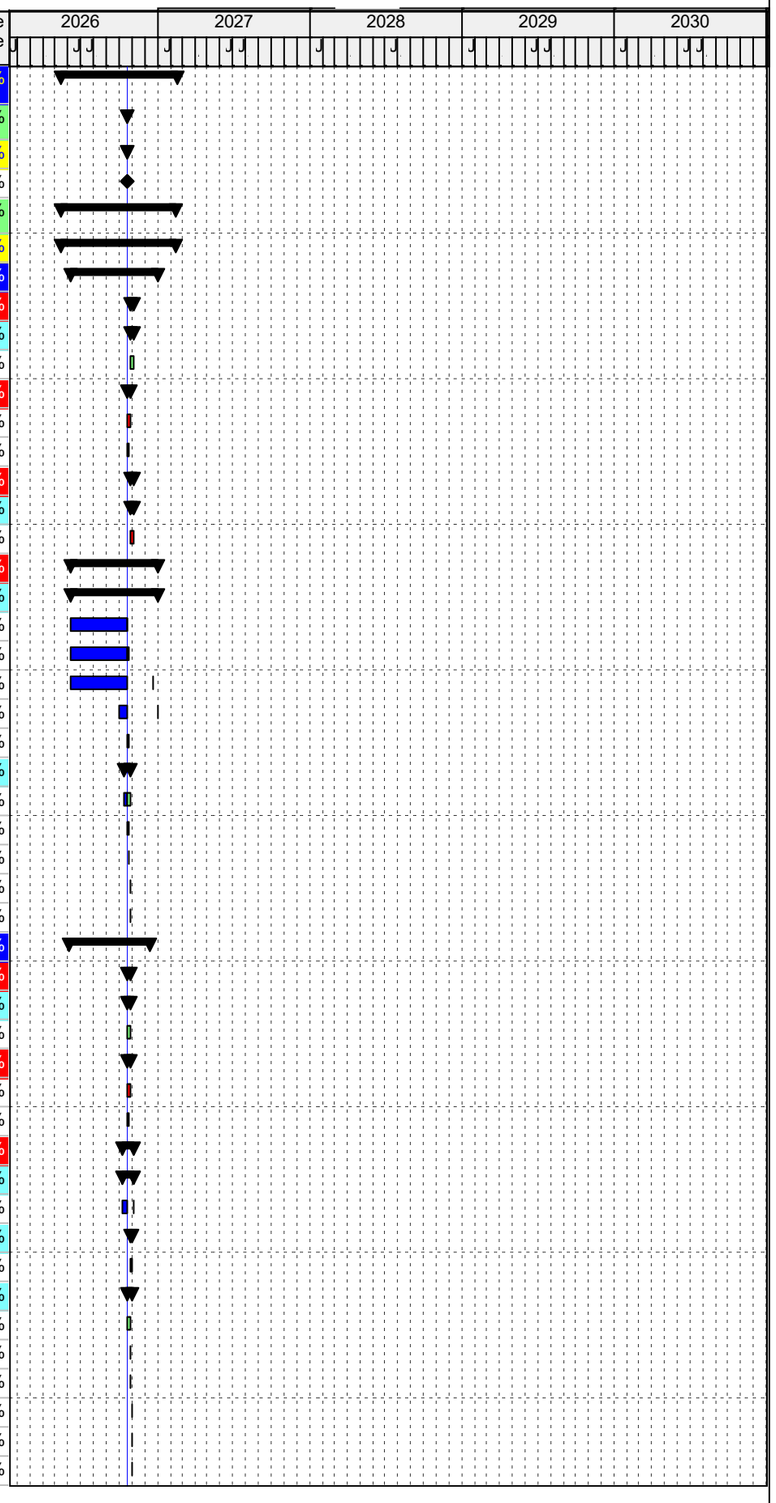

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
MECHANICAL		8	09-Aug-26	23-Aug-26	32,797.19	32,797.19	0.00	100%	0%
SEWER AND DRAINAGE SYSTEM		8	09-Aug-26	23-Aug-26	32,797.19	32,797.19	0.00	100%	0%
FIRST STAGE		2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Floor Drain	2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		6	17-Aug-26	23-Aug-26	21,741.23	21,741.23	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Electric Water Heater	2	17-Aug-26	18-Aug-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Sanitary Fixture and Accessories	4	19-Aug-26	23-Aug-26	19,921.72	19,921.72	0.00	100%	0%
ELECTRICAL		118	30-Jun-26	23-Nov-26	286,066.91	32,798.20	52,969.74	11.47%	18.52%
FIRST STAGE		118	30-Jun-26	13-Oct-26	32,798.20	32,798.20	27,642.87	100%	84.28%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	01-Sep-26	05-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	15-Sep-26	19-Sep-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		14	08-Nov-26	23-Nov-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B5-E-135	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B4		94	28-Jun-26	01-Dec-26	357,129.41	84,214.23	90,511.95	23.58%	25.34%
STRUCTURAL STEEL		14	28-Jun-26	06-Jul-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B4-SS-104	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-102	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	23,161.04	23,161.04	0.00	100%	0%
ARCHITECTURAL		7	08-Sep-26	15-Sep-26	44,167.30	44,167.30	37,542.21	100%	85%
WALL FINISHES		7	08-Sep-26	15-Sep-26	44,167.30	44,167.30	37,542.21	100%	85%
DAM3-C-B4-A-109	Paint to Plaster (Primer, Putty & First Coat)	7	08-Sep-26	15-Sep-26	44,167.30	44,167.30	37,542.21	100%	85%
ELECTRICAL		94	22-Jul-26	01-Dec-26	286,066.91	13,151.73	52,969.74	4.6%	18.52%
FIRST STAGE		94	22-Jul-26	28-Oct-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	24-Sep-26	28-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		7	24-Nov-26	01-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B4-E-104	Installation of Solar power plant	7	24-Nov-26	01-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B3		166	24-Jun-26	24-Dec-26	1,051,389.90	768,243.44	529,934.30	73.07%	50.4%
STRUCTURAL		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B3-S-101	Concrete pad	7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		23	24-Jun-26	15-Jul-26	487,632.50	487,632.50	442,066.52	100%	90.66%
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	11-Jul-26	15-Jul-26	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B3-SS-102	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-103	Steel members for external platform	7	02-Jul-26	09-Jul-26	18,670.78	18,670.78	0.00	100%	0%
DAM3-C-B3-SS-104	Epoxy paint for external platform	5	11-Jul-26	15-Jul-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		27	16-Jul-26	26-Aug-26	276,783.38	276,783.38	34,898.03	100%	12.61%
FLOOR FINISHES		7	19-Aug-26	26-Aug-26	46,530.71	46,530.71	34,898.03	100%	75%
DAM3-C-B3-A-108	Tiles for Toilet	7	19-Aug-26	26-Aug-26	46,530.71	46,530.71	34,898.03	100%	75%
DOORS & WINDOWS		12	16-Jul-26	29-Jul-26	225,373.65	225,373.65	0.00	100%	0%
DAM3-C-B3-A-142	Window (CW1)	7	16-Jul-26	23-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B3-A-105	Roll up Shutter Door	1	25-Jul-26	25-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B3-A-106	Supply and install (D5) 1000*2200mm single leaf steel doc	1	26-Jul-26	26-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-112	Supply and install (D4) 800*2200 mm single leaf aluminum	1	27-Jul-26	27-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B3-A-113	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	28-Jul-26	28-Jul-26	7,811.07	7,811.07	0.00	100%	0%

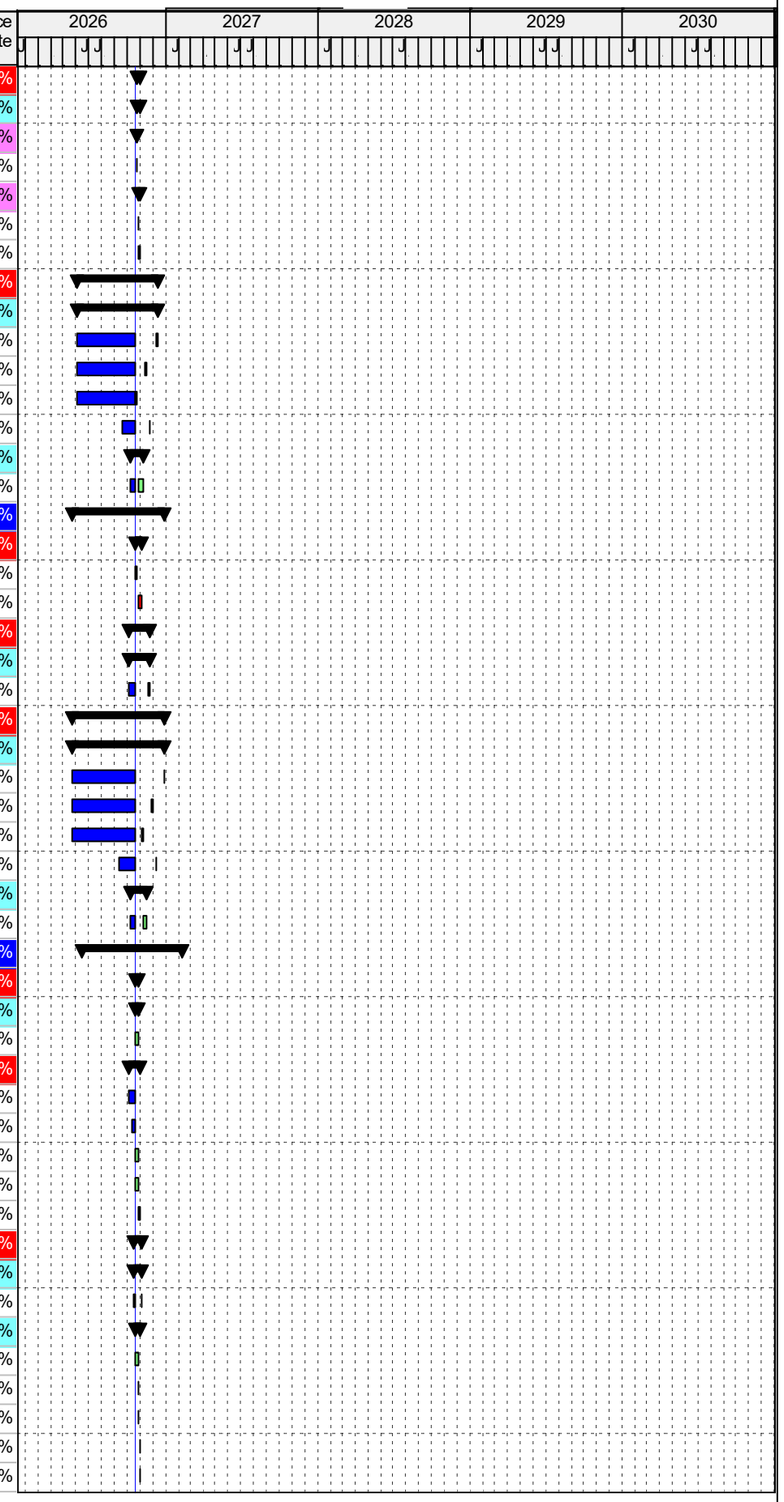

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B3-A-135	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	29-Jul-26	29-Jul-26	16,016.16	16,016.16	0.00	100%	0%
WATER PROOFING WORKS		4	15-Aug-26	18-Aug-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B3-A-122	Waterproofing membrane for toilets	4	15-Aug-26	18-Aug-26	4,879.02	4,879.02	0.00	100%	0%
ELECTRICAL		166	19-Jul-26	24-Dec-26	286,066.91	2,920.45	52,969.74	1.02%	18.52%
FIRST STAGE		166	19-Jul-26	24-Dec-26	32,798.20	2,920.45	27,642.87	8.9%	84.28%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Nov-26	01-Dec-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	12-Dec-26	15-Dec-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		7	02-Dec-26	09-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B3-E-104	Installation of Solar power plant	7	02-Dec-26	09-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B2		54	26-Sep-26	21-Dec-26	612,328.23	339,413.06	150,848.14	55.43%	24.64%
STRUCTURAL STEEL		5	26-Sep-26	01-Oct-26	326,261.32	326,261.32	97,878.40	100%	30%
DAM3-C-B2-SS-013	Installation of wall sandwich panel	5	26-Sep-26	01-Oct-26	326,261.32	326,261.32	97,878.40	100%	30%
ELECTRICAL		47	29-Sep-26	21-Dec-26	286,066.91	13,151.73	52,969.74	4.6%	18.52%
FIRST STAGE		47	29-Sep-26	11-Nov-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	29-Sep-26	04-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	13-Oct-26	18-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		10	10-Dec-26	21-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B2-E-420	Installation of Solar power plant	10	10-Dec-26	21-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B1		63	14-Sep-26	29-Dec-26	660,918.40	337,428.77	162,995.68	51.05%	24.66%
STRUCTURAL STEEL		5	14-Sep-26	19-Sep-26	326,261.32	326,261.32	97,878.40	100%	30%
DAM3-C-B1-SS-013	Installation of wall sandwich panel	5	14-Sep-26	19-Sep-26	326,261.32	326,261.32	97,878.40	100%	30%
ARCHITECTURAL		10	18-Oct-26	03-Nov-26	48,590.16	6,478.69	12,147.54	13.33%	25%
WALL FINISHES		10	18-Oct-26	03-Nov-26	48,590.16	6,478.69	12,147.54	13.33%	25%
DAM3-C-B1-A-180	Internal Wall Plaster	10	18-Oct-26	03-Nov-26	48,590.16	6,478.69	12,147.54	13.33%	25%
ELECTRICAL		63	08-Oct-26	29-Dec-26	286,066.91	4,688.76	52,969.74	1.64%	18.52%
FIRST STAGE		41	08-Oct-26	22-Nov-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	08-Oct-26	12-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	22-Oct-26	26-Oct-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		7	22-Dec-26	29-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B1-E-420	Installation of Solar power plant	7	22-Dec-26	29-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B7		63	24-Sep-26	28-Nov-26	450,061.52	107,324.94	324,858.05	23.85%	72.18%
ARCHITECTURAL		24	24-Sep-26	28-Nov-26	341,096.59	94,173.21	274,365.15	27.61%	80.44%
WALL FINISHES		4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
FLOOR FINISHES		2	11-Nov-26	12-Nov-26	26,867.31	0.00	20,150.48	0%	75%
DAM3-C-B7-A-250	Tiles for Office Area	2	11-Nov-26	12-Nov-26	26,867.31	0.00	20,150.48	0%	75%
DOORS & WINDOWS		7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	84,755.89	100%	90%
DAM3-C-B7-A-552	Window (CW1)	7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	84,755.89	100%	90%
METAL WORKS		5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
ELECTRICAL		63	27-Sep-26	08-Nov-26	108,964.94	13,151.73	50,492.90	12.07%	46.34%
FIRST STAGE		63	27-Sep-26	08-Nov-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	19,646.47	0.00	17,681.82	0%	90%

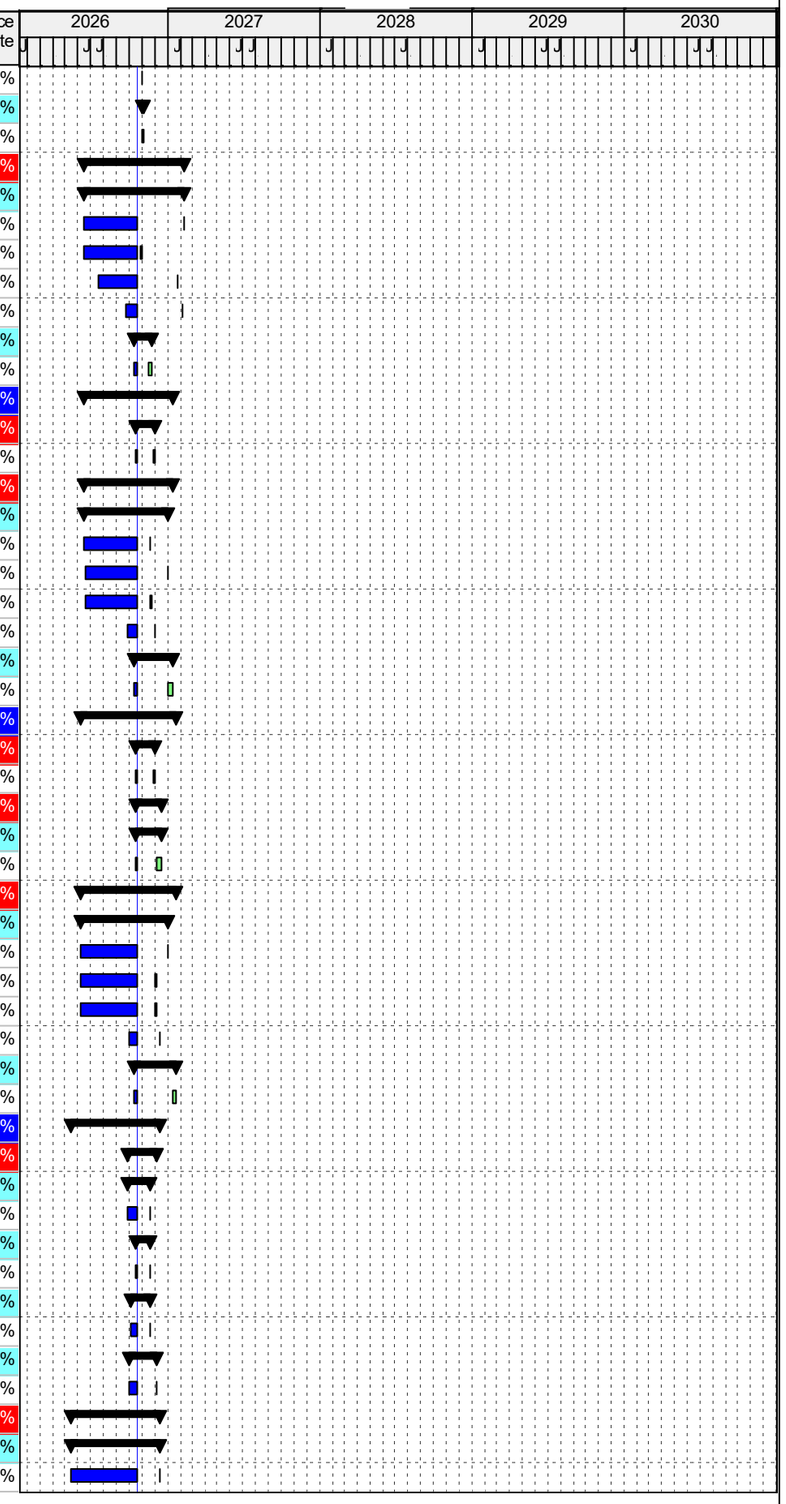

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	27-Sep-26	30-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
BLOCK B8		79	15-Oct-26	14-Jan-27	668,915.38	55,427.53	358,648.81	8.29%	53.62%
ARCHITECTURAL		76	15-Oct-26	19-Dec-26	382,848.47	53,813.26	305,679.07	14.06%	79.84%
WALL FINISHES		4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		8	15-Oct-26	24-Oct-26	162,792.41	53,813.26	136,220.29	33.06%	83.68%
DAM3-C-B8-A-552	Window (CW1)	7	15-Oct-26	22-Oct-26	94,173.21	53,813.26	84,755.89	57.14%	90%
DAM3-C-B8-A-553	Roll up Shutter Door	1	24-Oct-26	24-Oct-26	68,619.20	0.00	51,464.40	0%	75%
METAL WORKS		3	14-Dec-26	19-Dec-26	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B8-A-292	Aluminium composite panel	3	14-Dec-26	19-Dec-26	175,888.76	0.00	131,916.57	0%	75%
ELECTRICAL		61	18-Oct-26	14-Jan-27	286,066.91	1,614.27	52,969.74	0.56%	18.52%
FIRST STAGE		61	18-Oct-26	29-Nov-26	32,798.20	1,614.27	27,642.87	4.92%	84.28%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	18-Oct-26	21-Oct-26	1,768.31	884.15	884.15	50%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	2,920.45	730.11	1,460.23	25%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		7	07-Jan-27	14-Jan-27	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B8-E-420	Installation of Solar power plant	7	07-Jan-27	14-Jan-27	253,268.71	0.00	25,326.87	0%	10%
BLOCK B9		89	19-Oct-26	31-Jan-27	600,296.18	13,453.32	337,030.62	2.24%	56.14%
ARCHITECTURAL		38	19-Oct-26	22-Dec-26	314,229.27	13,453.32	284,060.88	4.28%	90.4%
WALL FINISHES		4	08-Dec-26	15-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	08-Dec-26	15-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		7	19-Oct-26	26-Oct-26	94,173.21	13,453.32	70,629.91	14.29%	75%
DAM3-C-B9-A-552	Window (CW1)	7	19-Oct-26	26-Oct-26	94,173.21	13,453.32	70,629.91	14.29%	75%
METAL WORKS		3	17-Dec-26	22-Dec-26	175,888.76	0.00	175,888.76	0%	100%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	175,888.76	0.00	175,888.76	0%	100%
ELECTRICAL		77	21-Oct-26	31-Jan-27	286,066.91	0.00	52,969.74	0%	18.52%
FIRST STAGE		77	21-Oct-26	02-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	21-Oct-26	25-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		8	16-Jan-27	31-Jan-27	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B9-E-420	Installation of Solar power plant	8	16-Jan-27	31-Jan-27	253,268.71	0.00	25,326.87	0%	10%
BLOCK B10		92	22-Oct-26	08-Feb-27	600,296.18	0.00	178,730.74	0%	29.77%
ARCHITECTURAL		36	22-Oct-26	26-Dec-26	314,229.27	0.00	125,760.99	0%	40.02%
WALL FINISHES		5	12-Dec-26	19-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B10-A-23	Paint to Plaster (Primer, Putty & First Coat)	5	12-Dec-26	19-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		7	22-Oct-26	29-Oct-26	94,173.21	0.00	70,629.91	0%	75%
DAM3-C-B10-A-55	Window (CW1)	7	22-Oct-26	29-Oct-26	94,173.21	0.00	70,629.91	0%	75%
METAL WORKS		3	21-Dec-26	26-Dec-26	175,888.76	0.00	17,588.88	0%	10%
DAM3-C-B10-A-29	Aluminium composite panel	3	21-Dec-26	26-Dec-26	175,888.76	0.00	17,588.88	0%	10%
ELECTRICAL		78	25-Oct-26	08-Feb-27	286,066.91	0.00	52,969.74	0%	18.52%
FIRST STAGE		78	25-Oct-26	06-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B10-E-11	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	19,646.47	0.00	17,681.82	0%	90%

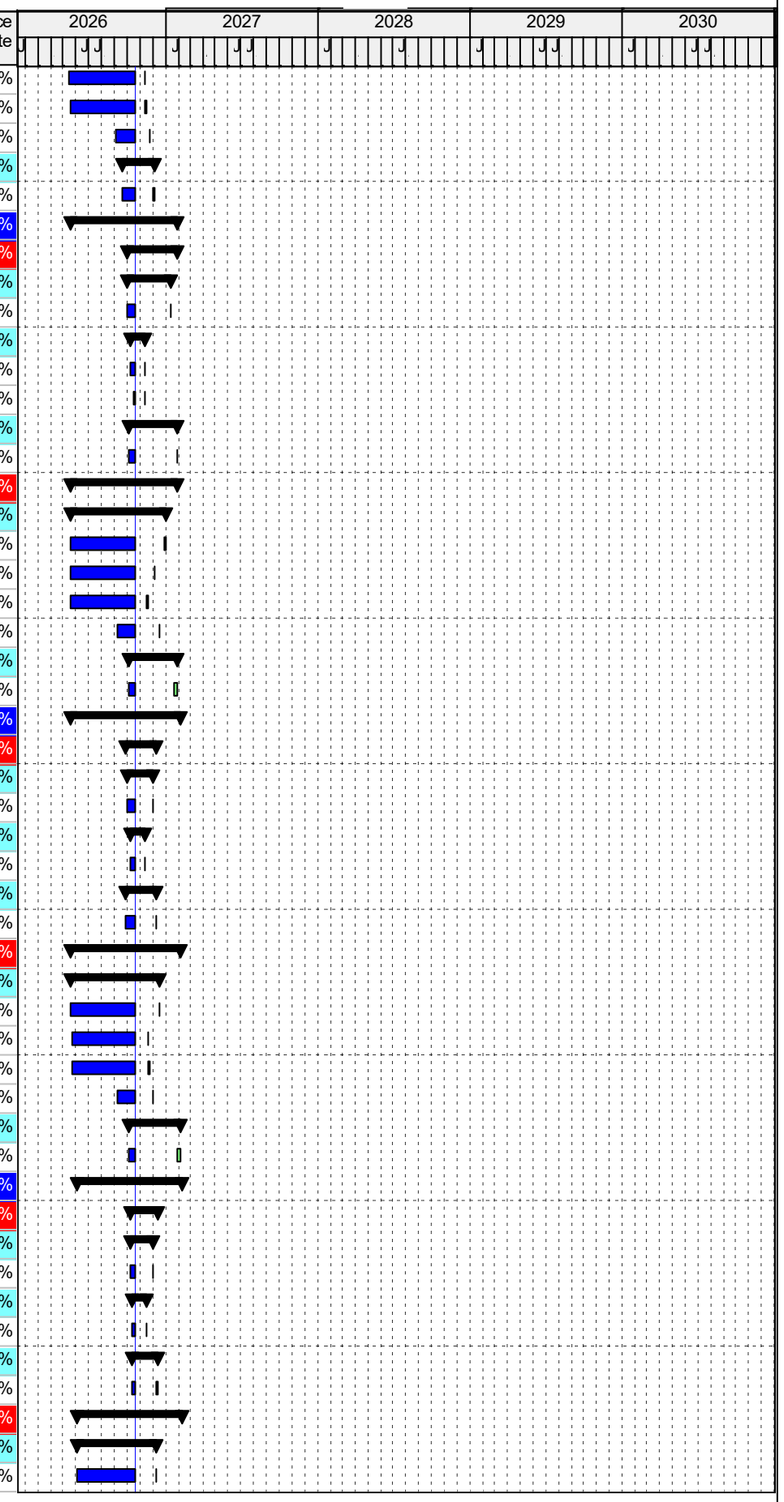

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-25	2 Weeks look ahead		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B10-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	25-Oct-26	28-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B10-E-18	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B10-E-16	Installation of Conduites for Lighting Fixture	4	08-Nov-26	11-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		5	01-Feb-27	08-Feb-27	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B10-E-42	Installation of Solar power plant	5	01-Feb-27	08-Feb-27	253,268.71	0.00	25,326.87	0%	10%
BLOCK B11		125	28-Oct-26	16-Feb-27	461,955.66	0.00	70,558.62	0%	15.27%
ARCHITECTURAL		3	24-Dec-26	29-Dec-26	175,888.76	0.00	17,588.88	0%	10%
METAL WORKS		3	24-Dec-26	29-Dec-26	175,888.76	0.00	17,588.88	0%	10%
DAM3-C-B11-A-29	Aluminium composite panel	3	24-Dec-26	29-Dec-26	175,888.76	0.00	17,588.88	0%	10%
ELECTRICAL		125	28-Oct-26	16-Feb-27	286,066.91	0.00	52,969.74	0%	18.52%
FIRST STAGE		75	28-Oct-26	09-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B11-E-11	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Oct-26	01-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B11-E-18	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B11-E-16	Installation of Conduites for Lighting Fixture	4	11-Nov-26	15-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		4	09-Feb-27	16-Feb-27	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B11-E-42	Installation of Solar power plant	4	09-Feb-27	16-Feb-27	253,268.71	0.00	25,326.87	0%	10%
SITE INFRASTRUCTURE		64	07-Sep-26	07-Dec-26	826,602.22	748,301.15	635,352.94	90.53%	76.86%
NETWORKS		64	07-Sep-26	07-Dec-26	826,602.22	748,301.15	635,352.94	90.53%	76.86%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UI		42	07-Sep-26	21-Oct-26	571,716.96	565,935.31	497,845.16	98.99%	87.08%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	07-Sep-26	14-Sep-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	15-Sep-26	27-Sep-26	364,244.28	364,244.28	327,819.85	100%	90%
DAM3-C-ENV-F-192	Installation of Valves	5	30-Sep-26	05-Oct-26	86,057.93	86,057.93	68,846.34	100%	80%
DAM3-C-ENV-F-202	Warning Tapes	2	28-Sep-26	29-Sep-26	40,471.58	40,471.58	32,377.27	100%	80%
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	06-Oct-26	21-Oct-26	40,471.58	34,689.93	32,377.27	85.71%	80%
WATER SUPPLY SYSTEM		37	15-Sep-26	07-Dec-26	254,885.25	182,365.84	137,507.78	71.55%	53.95%
DAM3-C-ENV-WS-8	Construction of Washout Chamber	7	06-Oct-26	13-Oct-26	17,314.15	17,314.15	13,851.32	100%	80%
DAM3-C-ENV-WS-8	Construction of Air Valve Chamber	7	14-Oct-26	21-Oct-26	16,236.37	11,597.40	12,989.09	71.43%	80%
DAM3-C-ENV-WS-7	Excavation for Water Suppy Works	7	15-Sep-26	22-Sep-26	13,950.39	13,950.39	6,975.20	100%	50%
DAM3-C-ENV-WS-7	Installation of HDPE PN16 Pipes for Cold Water Supply	7	24-Sep-26	05-Oct-26	125,553.50	125,553.50	62,776.75	100%	50%
DAM3-C-ENV-WS-7	Installation of Valves	5	16-Nov-26	21-Nov-26	53,930.05	0.00	26,965.03	0%	50%
DAM3-C-ENV-WS-7	Warning Tape	2	14-Oct-26	15-Oct-26	13,950.39	13,950.39	6,975.20	100%	50%
DAM3-C-ENV-WS-7	Backfilling for Water Supply	14	22-Nov-26	07-Dec-26	13,950.39	0.00	6,975.20	0%	50%
TESTING AND COMMISSIONING (10%)		161	08-Jul-26	19-Jan-27	315,300.58	225,094.29	258,704.75	71.39%	82.05%
TESTING AND COMMISSIONING 900 Sq.m-2		7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
MECHANICAL		7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
P001-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		85	06-Oct-26	19-Jan-27	145,208.18	57,989.14	130,687.36	39.94%	90%
ENVIRONMENTAL		85	06-Oct-26	19-Jan-27	145,208.18	57,989.14	130,687.36	39.94%	90%
S001-C-TC-ENV-F-1(	Testing & Commissioning of External Fire Fighting System :	15	06-Oct-26	22-Oct-26	72,486.43	57,989.14	65,237.78	80%	90%
S001-C-TC-ENV-SW	Testing & Commissioning of Sewer & Drainage System	3	03-Jan-27	19-Jan-27	67,394.23	0.00	60,654.81	0%	90%
S001-C-TC-ENV-WS	Testing & Commissioning of Water Supply System	15	22-Nov-26	08-Dec-26	5,327.52	0.00	4,794.77	0%	90%
SNAGG WORKS		5	08-Jul-26	13-Jul-26	167,105.15	167,105.15	125,328.86	100%	75%
S001-C-TC-E-3606	Electrical Snagg works	5	08-Jul-26	13-Jul-26	167,105.15	167,105.15	125,328.86	100%	75%

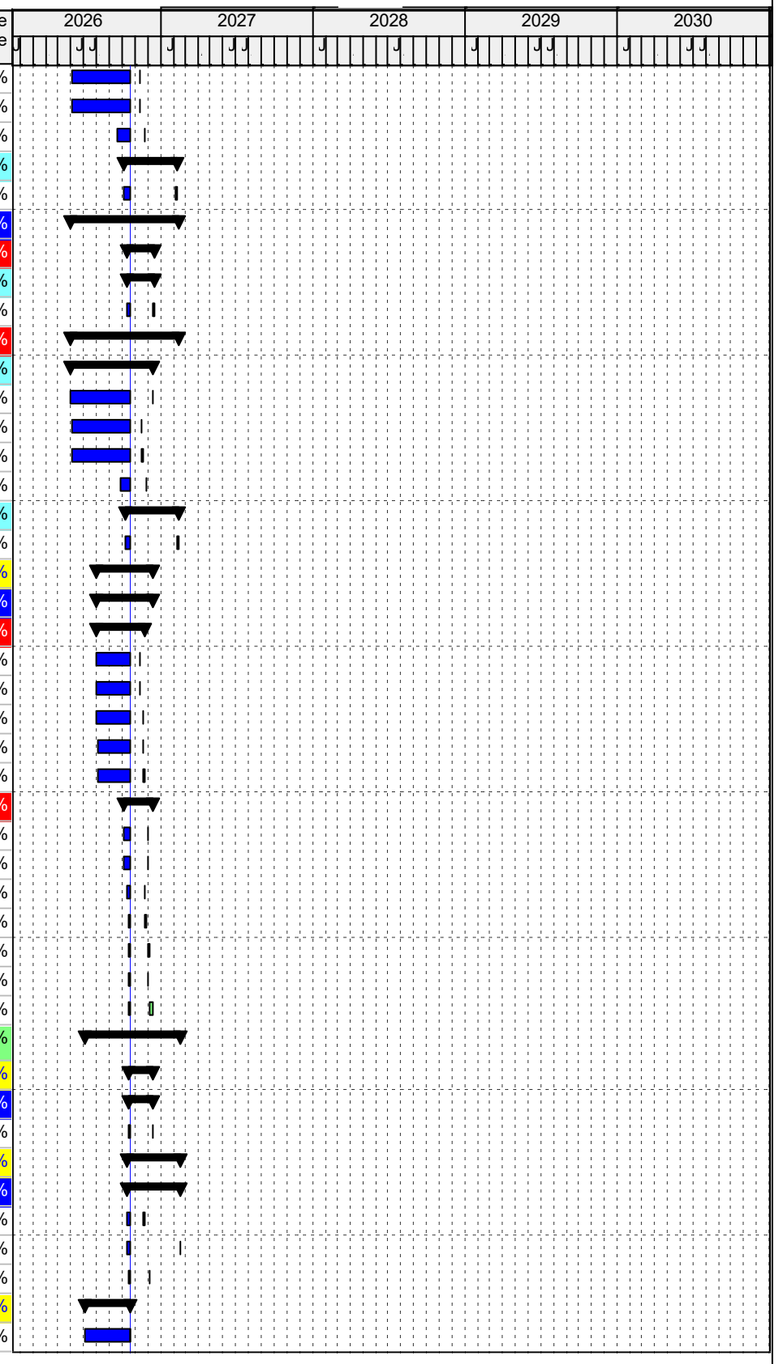

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-25	2 Weeks look ahead		
