
Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		366	07-Jan-26	06-Mar-27	07-Jan-26 A	02-Mar-27	95,996,525.00	69,925,401.98	70,141,305.82	72.84%	73.07%
PROJECT MILESTONES		350	07-Jan-26	06-Mar-27	07-Jan-26 A	02-Mar-27	0.00	0.00	0.00	0%	0%
MOBILIZATION		35	07-Jan-26	16-Feb-26	07-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
ENGINEERING (3%)		159	22-Jan-26	17-May-26	15-Jan-26 A	05-Jul-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
PROCUREMENT (20%)		258	04-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	19,199,305.00	18,821,263.50	19,199,305.00	98.03%	100%
CONSTRUCTION (67%)		321	27-Jan-26	21-Feb-27	14-Jan-26 A	23-Feb-27	64,317,671.75	40,977,321.22	40,781,573.10	63.71%	63.41%
RBF 900 SQM FACTORIES		321	27-Jan-26	16-Feb-27	14-Jan-26 A	23-Feb-27	55,841,646.40	38,968,435.06	38,012,958.67	69.78%	68.07%
SITE WORKS		16	27-Jan-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
BLOCK B6		264	10-Feb-26	23-Nov-26	15-Feb-26 A	17-Jan-27	5,075,523.09	4,056,159.13	3,289,562.29	79.92%	64.81%
BLOCK B5		242	19-Feb-26	23-Nov-26	16-Feb-26 A	23-Dec-26	5,075,523.09	4,820,713.04	3,378,514.23	94.98%	66.56%
BLOCK B4		242	25-Feb-26	01-Dec-26	17-Feb-26 A	03-Jan-27	5,075,523.09	4,583,200.88	3,378,514.23	90.3%	66.56%
BLOCK B3		303	03-Mar-26	28-Dec-26	17-Feb-26 A	15-Feb-27	5,075,523.09	3,476,170.36	3,312,279.43	68.49%	65.26%
BLOCK B2		273	08-Mar-26	02-Jan-27	17-Feb-26 A	15-Feb-27	5,075,523.09	3,426,422.18	2,933,193.28	67.51%	57.79%
BLOCK B1		272	12-Mar-26	03-Jan-27	17-Mar-26 A	15-Feb-27	5,075,523.09	3,354,324.53	2,896,750.65	66.09%	57.07%
BLOCK B7		273	10-Feb-26	06-Jan-27	16-Feb-26 A	26-Dec-26	5,075,523.09	3,446,966.96	4,160,544.65	67.91%	81.97%
BLOCK B8		288	19-Feb-26	14-Jan-27	17-Feb-26 A	23-Feb-27	5,075,523.09	3,108,677.89	3,872,447.51	61.25%	76.3%
BLOCK B9		287	25-Feb-26	31-Jan-27	17-Feb-26 A	06-Feb-27	5,075,523.09	3,064,511.75	3,804,037.02	60.38%	74.95%
BLOCK B10		293	03-Mar-26	08-Feb-27	18-Feb-26 A	10-Feb-27	5,075,523.09	2,912,484.49	3,639,038.61	57.38%	71.7%
BLOCK B11		288	08-Mar-26	16-Feb-27	18-Feb-26 A	15-Feb-27	5,075,523.09	2,707,911.45	3,337,184.36	53.35%	65.75%
SITE INFRASTRUCTURE		282	10-Feb-26	21-Feb-27	19-Jan-26 A	16-Feb-27	8,476,025.35	2,008,886.17	2,768,614.43	23.7%	32.66%
SITE WORKS		23	10-Feb-26	10-Mar-26	19-Jan-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
NETWORKS		84	07-Sep-26	23-Dec-26	01-Aug-26 A	25-Jan-27	1,901,944.63	919,729.18	1,318,470.60	48.36%	69.32%
EXTERNAL WORKS		74	15-Sep-26	25-Jan-27	01-Jul-26 A	16-Feb-27	3,338,525.71	891,466.10	1,252,452.95	26.7%	37.52%
ROAD WORKS		34	23-Nov-26	21-Feb-27	07-Jan-27	15-Feb-27	2,873,764.57	0.00	0.00	0%	0%
LANDSCAPING		12	02-Feb-27	15-Feb-27	01-Feb-27	14-Feb-27	164,099.55	0.00	0.00	0%	0%
TESTING AND COMMISSIONING (10%)		183	24-May-26	18-Feb-27	17-Jun-26 A	24-Feb-27	9,599,652.50	7,246,921.51	7,280,531.96	75.49%	75.84%
PREOJECT CLOSEOUT		25	02-Feb-27	06-Mar-27	01-Feb-27	02-Mar-27	0.00	0.00	0.00	0%	0%

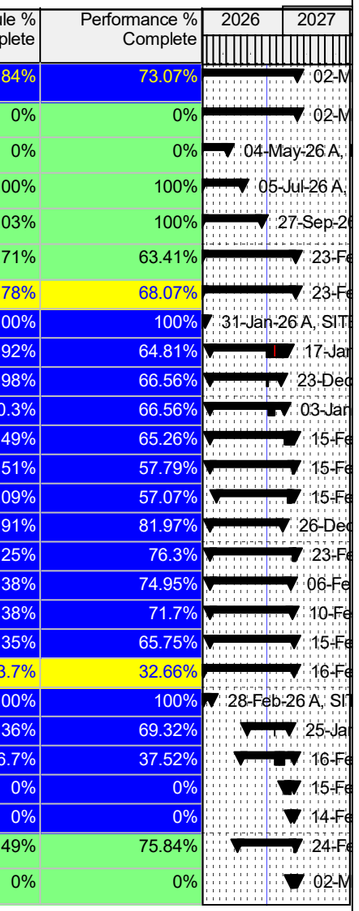

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
20-Oct-26	Weekly Report		
