Developing Infrastructure Networks in Riyadh's Fourth Industrial City

مشروع تطوير شبكات البنية التحتية بالرياض الرابعة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Rawaf Contracting	EGIS Saudi Engineering Consultancy	Shuaib A. Alshuaibi	30-Nov-2025	30-May-2028

Scope: infrastructure over about 6.5 km² of the Fourth Industrial City in Riyadh: roads and tunnels, electrical, telecom, ICT and security networks, potable water and fire-fighting, irrigation, sewage and stormwater networks, and sewage and stormwater pumping stations.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 27.4% against 30.8% planned, the project is behind by 3.5% (SPI 0.89). It gained 2.1% this week against 0.7% planned, so the gap narrowed from 4.9% last week. Most of this week's gain came from procurement. Earthworks remain far ahead of plan, but procurement, the zone network works and the tunnels are still behind.

PHYSICAL % COMPLETE
27.4% / 30.8% plan
▼ SPI 0.89 −3.5%

PROGRESS THIS WEEK
+2.1% / +0.7% plan
▲ 1.4% above the weekly plan

CONTRACT TIME ELAPSED
37.0% · day 337 of 912
▼ P6 finish 25-Jan-2029

INVOICED TO DATE (GROSS)
16.0% · 71.0M SAR
8 invoices, last period ends 30-Sep-2026

The schedule still finishes the project about eight months late.

The P6 update uploaded this week (data date 02-Nov-2026) finishes the project on 25-Jan-2029, 240 days after the contract completion date of 30-May-2028 (last week: 01-Feb-2029, −247 days). The weekly report now gives the same date. In P6 the roads finish on 02-May-2027 and the MV network on 10-Nov-2027, against the contract milestone of 30-Sep-2026 for MV and road works.

Site photos this week

Six photos from the 02-Nov-2026 weekly upload. Five are GPS-stamped 01–02 Nov 2026: asphalt on roads RD-L-7 and RD-A-1, base course compaction on RD-A-1, and ground improvement and backfilling on blocks BL-30 and BL-35. The sixth shows the tunnel slab pour. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt work, RD-L-7, Zone 05

Paver laying the bituminous base course. GPS-stamped 02-Nov-2026, 11:00.



Asphalt work, RD-A-1, Zone 04

Pneumatic roller on the new asphalt layer. GPS-stamped 01-Nov-2026, 08:24.



Aggregate base course, RD-A-1, Zone 08

Rollers compacting the base course. GPS-stamped 02-Nov-2026, 11:17.



Tunnel slab casting

Concrete pumps pouring the tunnel slab (presentation: tunnel part 02). No stamp.



Rapid impact compaction, BL-30, Zone 09

RIC rig compacting the block platform. GPS-stamped 01-Nov-2026, 10:29.



Backfilling, BL-35, Zone 09

Tipper unloading fill for the dozer. GPS-stamped 01-Nov-2026, 10:34.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 02-Nov-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	2.0%	100.0%	84.5%	−15.5%	0.85	▼ Behind
Procurement	8.2%	100.0%	23.4%	−76.6%	0.23	▼ Behind
Construction	78.7%	26.3%	30.3%	+3.9%	1.15	▲ Ahead
↳ Earthworks	21.9%	23.7%	74.0%	+50.3%	3.13	▲ Ahead
↳ Zone works (Z1–Z9)	50.7%	24.8%	10.4%	−14.4%	0.42	▼ Behind
↳ Tunnels	3.0%	99.4%	76.2%	−23.2%	0.77	▼ Behind
↳ Stations, open channels, demolition	3.1%	0.0%	1.4%	+1.4%	–	● Not yet due
Testing & commissioning	11.2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**30.8%**	**27.4%**	**−3.5%**	**0.89**	▼ Behind

Procurement rose from 6.6% to 23.4% this week. Within the zone works, SPI ranges from 0.06 (Zones 1 and 2) to 0.58 (Zone 8). The P6 update has 8,625 activities: 1,506 completed, 445 in progress and 6,674 not started.

Scope of work: quantities

Total scope, quantity executed and quantity remaining for each item, from the executed-quantities sheet of the "Quantities & Procurement" file uploaded on 02-Nov-2026 (the same figures as the weekly report's Conclusion sheet). Quantities are for the whole project, not by zone. "This week" is this week's quantity minus the 26-Oct-2026 report's.

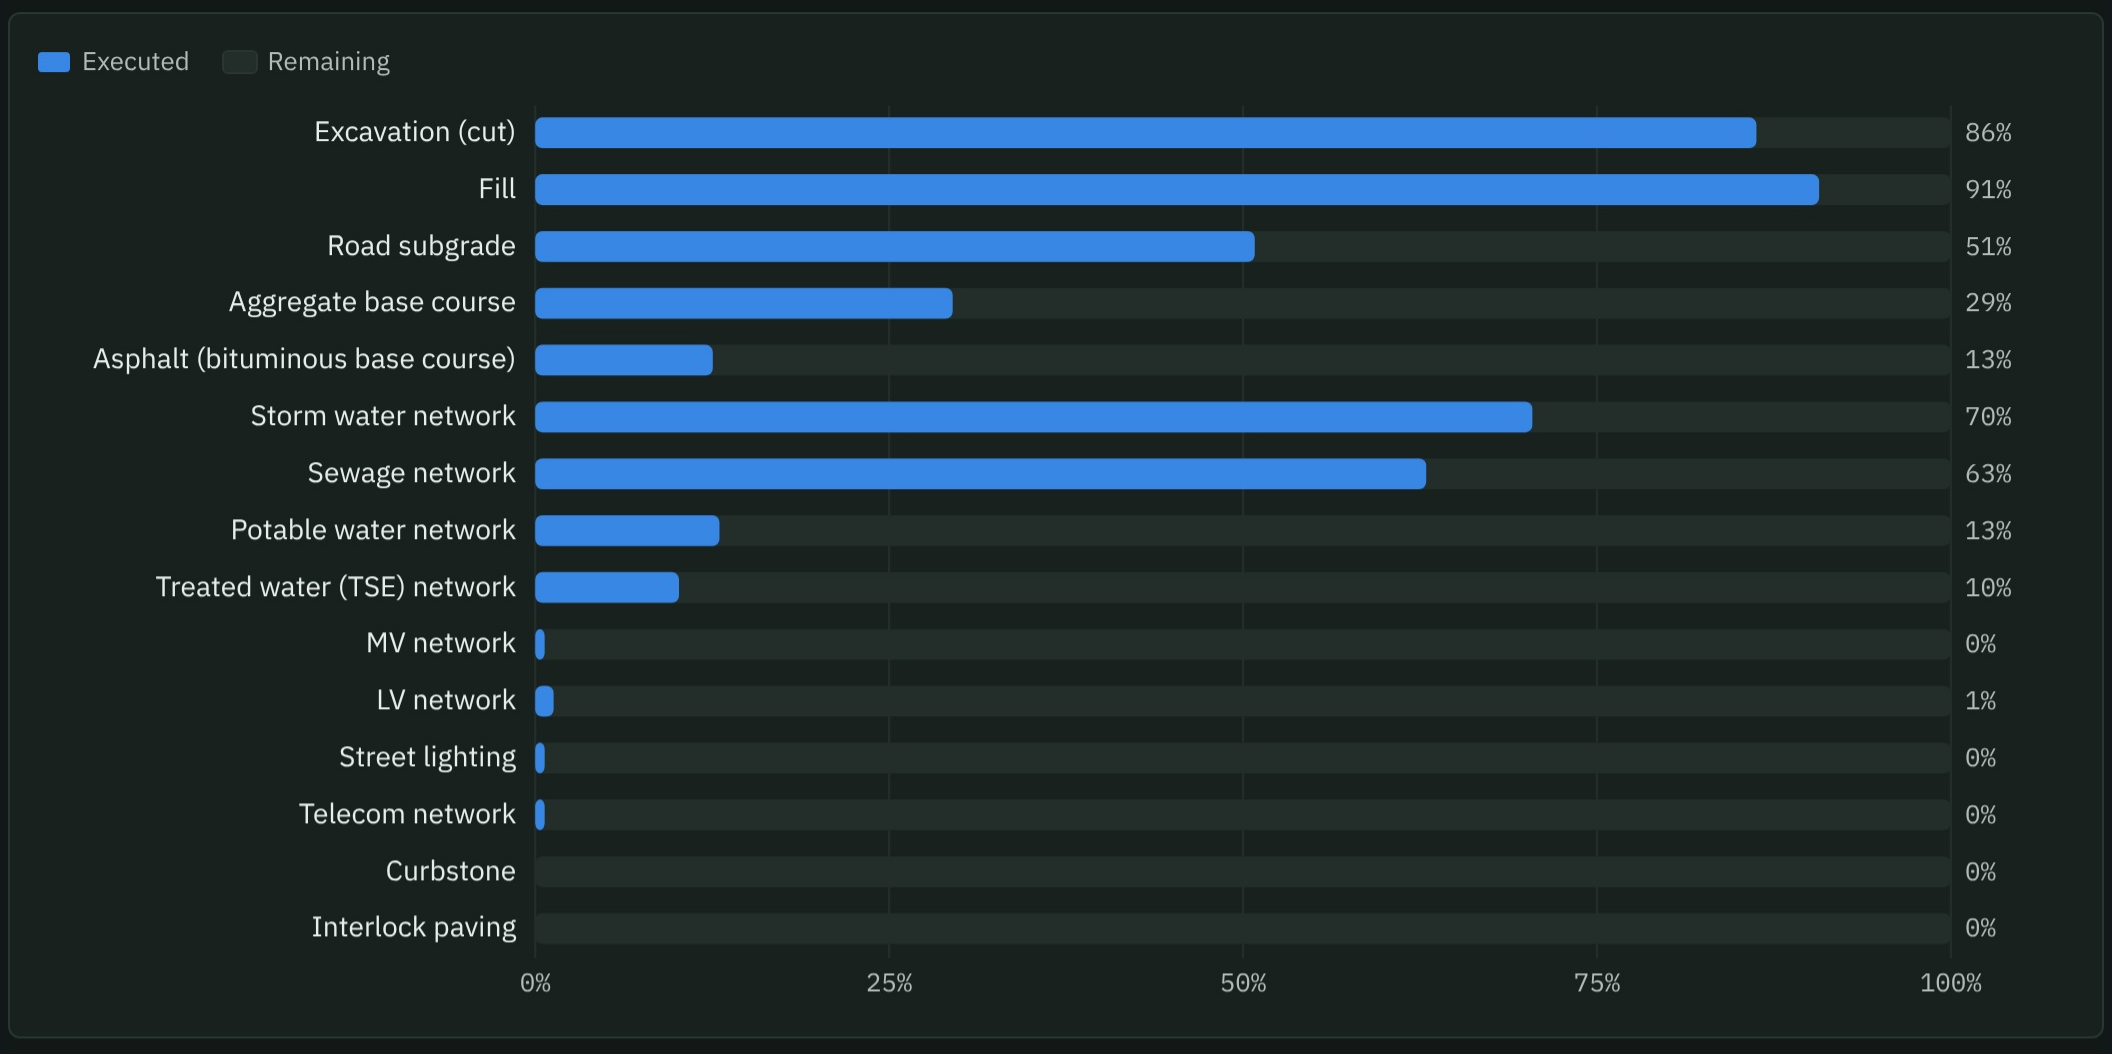

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation (cut)	All	m³	4,319,104	3,726,000	+10,000	593,104	86.3%	–
Fill	All	m³	3,811,986	3,457,315	+2,110	354,671	90.7%	–
Road subgrade	All	m³	232,143	118,000	+2,000	114,143	50.8%	–
Aggregate base course	All	m³	145,809	43,000	+10,000	102,809	29.5%	–
Asphalt (bituminous base course)	All	m³	86,559	10,860	+1,359	75,699	12.5%	–
Storm water network	All	LM	50,642	35,672	+642	14,970	70.4%	–
Sewage network	All	LM	22,579	14,211	+555	8,368	62.9%	–
Potable water network	All	LM	31,687	4,125	+213	27,562	13.0%	–
Treated water (TSE) network	All	LM	35,746	3,632	+182	32,114	10.2%	–
MV network	All	LM	131,104	350	0	130,754	0.3%	–
LV network	All	LM	24,579	320	0	24,259	1.3%	–
Street lighting	All	LM	67,945	180	0	67,765	0.3%	–
Telecom network	All	LM	53,637	201	0	53,436	0.4%	–
Curbstone	All	LM	130,589	0	0	130,589	0.0%	–
Interlock paving	All	m²	42,347	0	0	42,347	0.0%	–

Road layers moving

Aggregate base course rose to 29.5% (+10,000 m³ this week) and asphalt to 12.5% (+1,359 m³). Cut is 86.3%, fill 90.7% and subgrade 50.8%. The storm network is at 70.4% (+642 m) and sewage at 62.9% (+555 m). Tunnel 01 slab concrete rose from 690 to 1,340 m³.

Electrical and telecom networks not moving

The MV network is still at 0.3% (350 of 131,104 m), street lighting 0.3%, telecom 0.4% and LV 1.3%, with no change for three weeks. Potable water is at 13.0% and treated water (TSE) at 10.2%. Curbstone and interlock have not started.

Milestones

Contract milestones from the Milestones sheet of the weekly report, with the forecast dates of the matching milestones in this week's P6 update (data date 02-Nov-2026). The P6 file gives no float values.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	STATUS
Site handover	30-Nov-2025	30-Nov-2025	30-Nov-2025 (actual)	✓ Done
Complete mobilisation	29-Dec-2025	30-Mar-2026	29-Dec-2025 (actual)	? The two sources differ
Drawings and materials submitted and approved	28-Jan-2026	30-Apr-2026	30-Nov-2026	▼ Late
All materials delivered to site	28-Feb-2026	–	16-Dec-2026	▼ Late
Complete MV and road works	30-Sep-2026	30-Sep-2026	Roads 02-May-2027; MV 10-Nov-2027	▼ Late
Complete deep networks	30-May-2027	30-May-2027	16-Nov-2027	▼ Late
Complete all networks	30-Nov-2027	30-Nov-2027	08-Jul-2028	▼ Late
All works complete, ready for initial handover	30-May-2028	30-May-2028	25-Jan-2029	▼ Late

The Milestones sheet still shows no delay.

The weekly report's Milestones sheet keeps every remaining milestone on its contract date, while this week's P6 update forecasts the deep networks about six months late, all networks about seven months late and the project 240 days late. Mobilisation is shown as completed on 29-Dec-2025 in P6 but on 30-Mar-2026 in the weekly report.

Procurement of key materials

Share of total quantity delivered to site. Source: procurement sheet of the "Quantities & Procurement" file and the Major Quantities sheet, 02-Nov-2026.

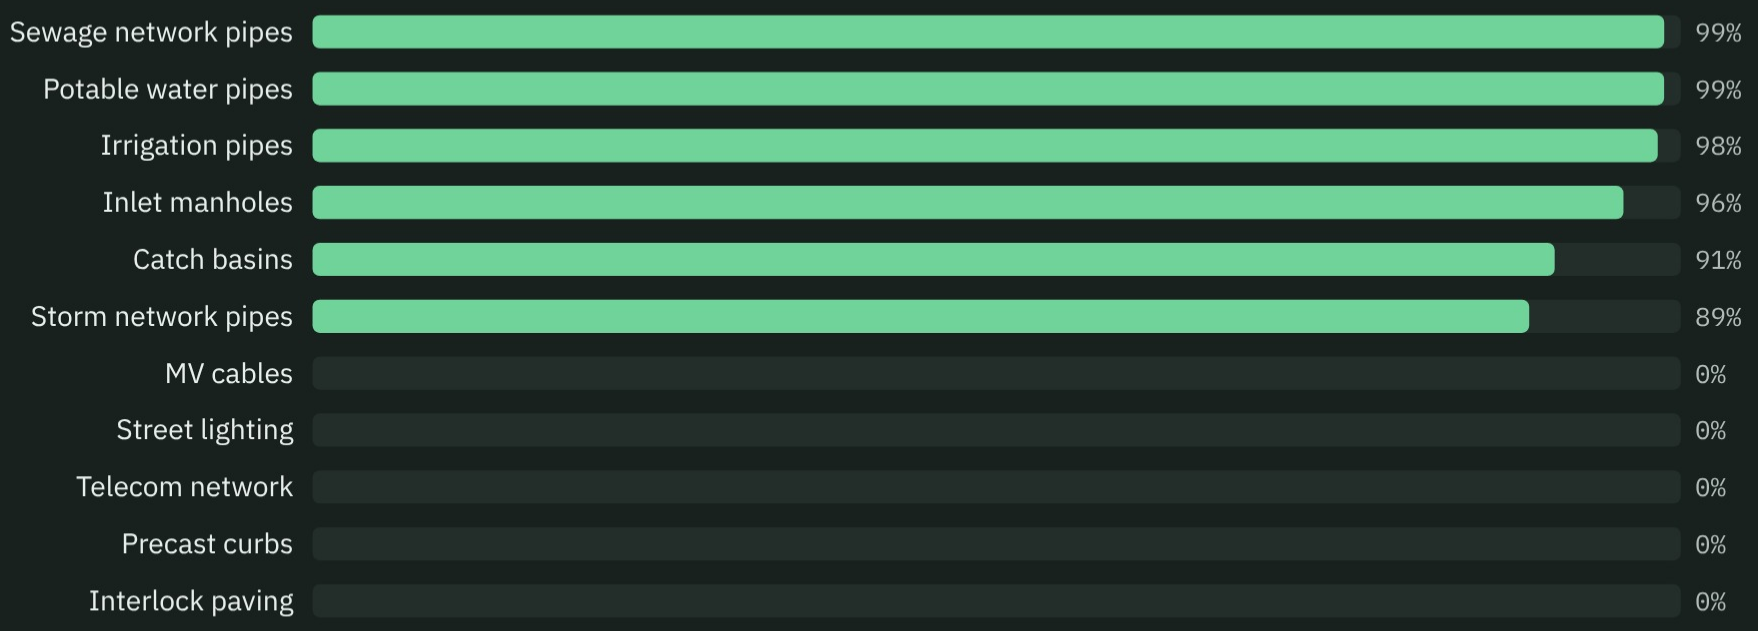

Electrical, telecom, curbs and interlock: nothing delivered


MV (131,104 LM), street lighting (67,945 LM), telecom (53,637 LM), precast curbs (130,589 LM) and interlock (42,347 m²) are all still at 0% delivered.

Wet-network materials mostly on site

Potable water 99%, sewage 99% and irrigation 98% of pipe length is delivered. The storm network is at 89% (45,030 of 50,642 LM), up 1,000 LM on last week. Inlet manholes are at 96% (480 of 501) and catch basins at 91% (906 of 998).

Manpower

Monthly manual head count on site, planned vs actual. Source: Manpower sheet, weekly report 02-Nov-2026.

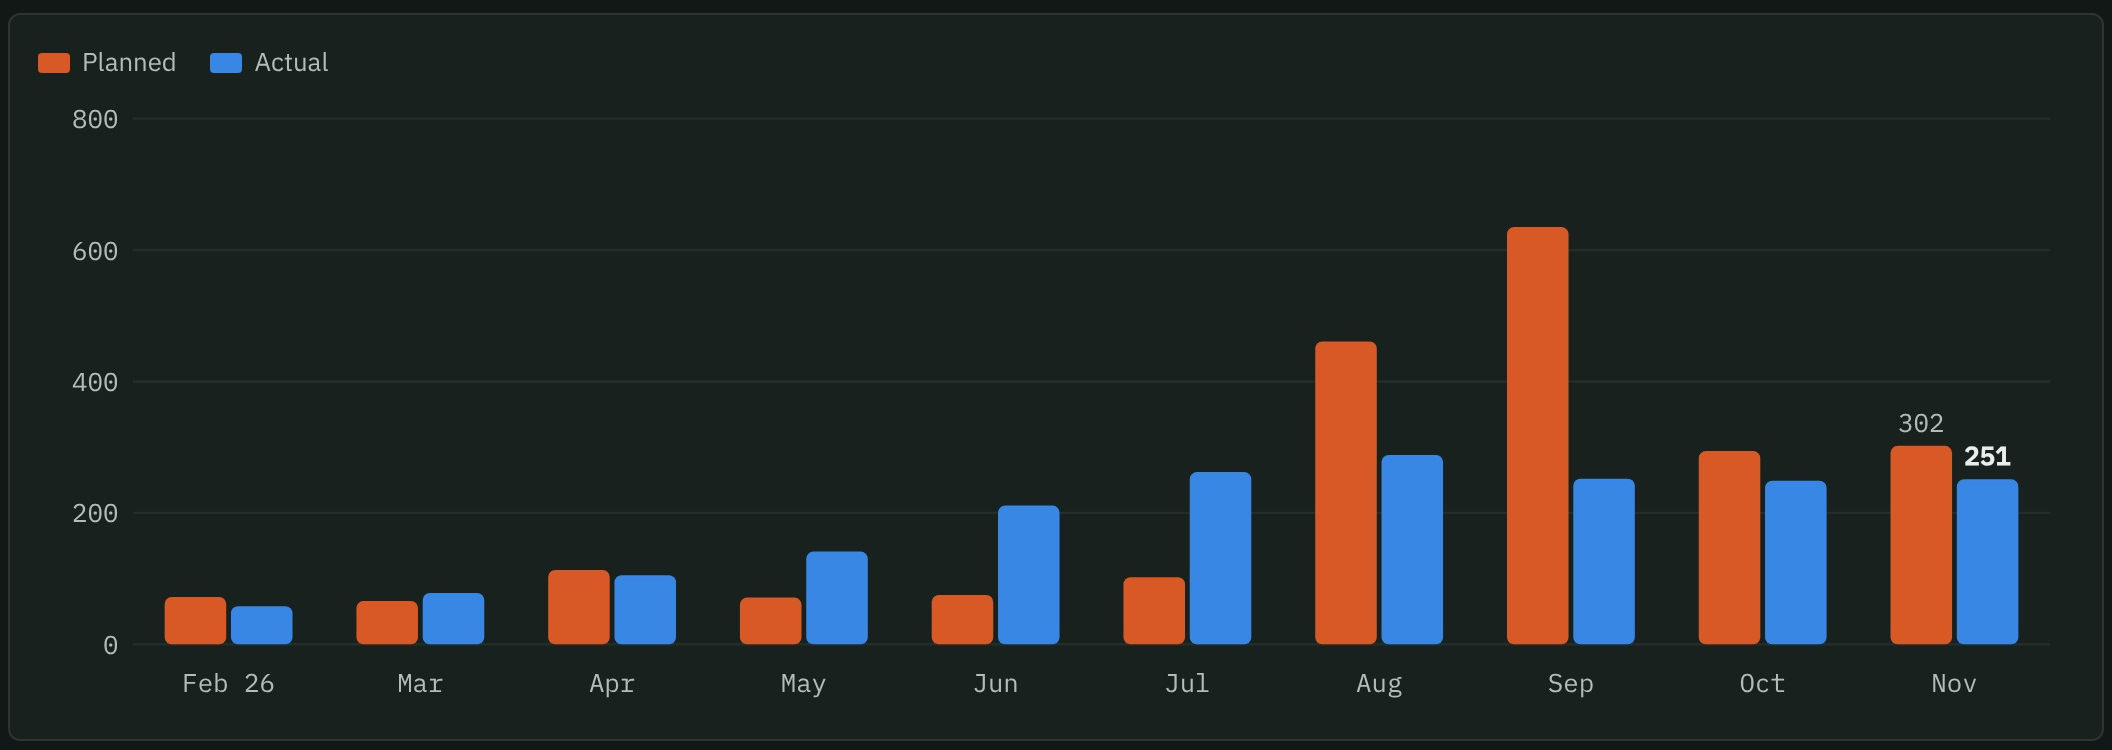

November manual head count so far is 251 against 302 planned (–17%), plus 47 non-manual staff, for 298 in total. The plan rises to 1,033 in March 2027. Major equipment on site fell from 208 to 154 items, including 42 excavators.

Cost and invoicing

Contract value

Bill 1: road and site works	214,146,361
Bill 2: electrical works	56,351,312
Bills 2.1–2.3: telecom, ICT and security	26,333,019
Bills 3–6: water, irrigation, sewage, storm	98,702,595
Bill 7: buildings, utilities and tunnels	49,466,713
Contract value	**445,000,000**
Revised BOQ (excl. VAT)	352,632,896
Change orders	0

All values in SAR. The bills add up to the 445,000,000 contract value. No change orders are registered.

Invoices

Invoices submitted	8
Gross value	71,001,361
Deductions and penalties	380,000
Net incl. VAT	81,271,566
Approved by the consultant	8
Approved by MODON PM / paid	0 / 0

Invoicing is 16.0% of the contract value against 27.4% physical progress. No new invoice was submitted this week. The presentation reports 70,621,360 SAR as paid.

Health, safety and quality

Safety Score 0.68

Safe man-hours (cumulative)	532,860
Man-hours this week	17,880
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	2
Property damage	0
Inductions / toolbox talks	74 / 504

The safety score rose from 0.55 to 0.68. Cumulative figures from the HSE-Stat sheet.

Quality Score 0.84

NCRs issued / closed / open	63 / 50 / 13
Site instructions issued / closed	15 / 10
MIRs issued / closed	113 / 113
Inspection requests closed / pending	1,687 / 236
Shop drawings submitted (code A / B)	1,453 (7 / 1,446)
Material submittals	118

Cumulative counts from the Quality-Stat sheet. NCRs rose from 34 to 63 this week.

Open issues and risks

ISSUE	OWNER	DETAIL
Clash with Green Riyadh services	Contractor / Green Riyadh	An air vent and cathodic protection on Road C8 clash with the works. Coordination with Green Riyadh's contractor is ongoing to get drawings and price the diversion. Rated critical; target moved to 15-Nov-2026.
Clash with ARAMCO gas lines	Contractor / ARAMCO	Wet and dry networks on Roads C8 and RD-L10 clash with two ARAMCO gas lines. Technical solutions were submitted and await ARAMCO's reply; solutions for telecom, sewage, MV, ICT and LV are already approved. Rated high; target moved to 30-Nov-2026.
Procurement delays	Contractor	Purchase orders had to be revised after the design changes, and material prices rose. Orders are issued and supply is under way. Rated high; the presentation targets 15-Nov-2026.
Progress behind plan	Contractor	Progress lags the schedule because of the master plan change (Wadi Al-Sulai) and the equipment shortage at the start. Equipment and network crews were increased; the presentation targets 30-Nov-2026. Rated critical.
SEC cable clashes (closed)	Contractor / SEC	Both clashes are now closed. On Road C2 the contractor appointed by SEC has started and is supporting the high-voltage cables. On Road C8 a start-of-work record was signed with SEC's contractor (Pillar).

Delay reasons stated in the report: the master layout changed after the Wadi Al-Sulai redesign, which changed the design of all networks; and equipment was short at the start of the project.

Data notes

This report uses the files uploaded for 02-Nov-2026 (weekly report, progress presentation, quantities and procurement file, P6 update) and, for this-week values, the 26-Oct-2026 report. Every progress percentage is physical % complete, weighted by budgeted man-hours. There is no S-curve section: the workbook's Physical-Chart Data sheet is empty.

- The week number, 48, is the contract week stated on the Milestones sheet ("Current Contract Weeks: 48 of 130").
- The workbook and the presentation also give a cost-based progress figure, labelled as actual progress in places. This report does not use it.
- The forecast finish now agrees between the P6 update, the P6 extract and the General Information sheet (25-Jan-2029, −240 days). The Milestones sheet still shows no delay on any milestone.

- Mobilisation finished on 29-Dec-2025 according to P6 and the presentation, but on 30-Mar-2026 according to the weekly report.
- Earthworks man-hours did not change this week (74.0%), although the quantities show +10,000 m³ cut and +2,110 m³ fill.
- The presentation's quantity slide repeats the 26-Oct-2026 quantities; this report uses the 02-Nov-2026 figures from the workbook and the quantities file.
- Tunnel 01 concrete is 5,243 m³ on the Major Quantities sheet but 3,903 m³ on the Major sheet.
- Quality: inspection requests show 490 issued but 1,687 closed and 236 pending, which cannot all be right. Cumulative inductions fell from 348 to 74 and the year-to-date man-hours equal the cumulative total, which suggests the HSE counters were reset.
- Invoices: the workbook lists 8 invoices, 71,001,361 SAR gross, none approved by the MODON PM and none paid; the presentation shows 70,621,360 SAR invoiced and the same amount paid. The contract value of 445,000,000 SAR is called "including VAT" on the Conclusion sheet but "excluding VAT" in the bill breakdown.
- The P6 update lists no total float for its activities, so milestone floats are not shown.
- Several summary panels still show `#REF!` or `#DIV/0!` errors.
- Photos: five are stamped 01–02 Nov 2026; the tunnel slab photo has no stamp. A prime-coat photo stamped 03-Nov-2026 (after the data date) was not used.

Compiled 05-Nov-2026 from the files uploaded for 02-Nov-2026, with this-week values from the 26-Oct-2026 report.
