
MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004 - Playground Initiative for Western Region (Asir - Jazan - Je		34300	3913%	3539%	26 Mar 26	25Jan-27	25 Mar26 A	09May-27	$13223,728.59	$11959,734.68	$33793,608.34	-8500
KEY MILESTONES		34300	0%	0%	26 Mar 26	25Jan-27	25 Mar26 A	09May-27	$000	$000	$0.00	-8500
GENERAL MILESTONES		34300	0%	0%	26 Mar 26	25Jan-27	25 Mar26 A	09May-27	$000	$000	$0.00	-8500
MLTX02-004MS-1030	Project Completion	0.00	0%	0%		25Jan-27		09May-27	$000	$000	$0.00	0.00
MLTX02-004MS-1010	Project CommencementDate	0.00	100%	100%	26 Mar 26		25 Mar26 A		$000	$000	$0.00	0.00
CONTRACTUAL MILESTONE		31300	0%	0%	29 Apr 26	25Jan-27	29 Apr26 A	09May-27	$000	$000	$0.00	-8500
MLTX02-004MS-1160	Completionof Asir Works	0.00	0%	0%		19Jan-27		29Mar-27	$000	$000	$0.00	0.00
MLTX02-004MS-1170	Completionof Jazan Works	0.00	0%	0%		25Jan-27		09May-27	$000	$000	$0.00	0.00
MLTX02-004MS-1180	Completionof Jeddah Works	0.00	0%	0%		25Jan-27		25Mar-27	$000	$000	$0.00	0.00
MLTX02-004MS-1100	Completionof Engineering	0.00	100%	0%		22Jul-26		05Nov-26	$000	$000	$0.00	0.00
MLTX02-004MS-1120	Completionof Levelling Works	0.00	100%	0%		09Aug-26		20Oct-26	$000	$000	$0.00	0.00
MLTX02-004MS-1070	Completionof Testing& Commissioning	0.00	0%	0%		19Jan-27		11Apr-27	$000	$000	$0.00	0.00
MLTX02-004MS-1130	Completionof ToiletBuilding	0.00	0%	0%		30Nov-26		04Jan-27	$000	$000	$0.00	0.00
MLTX02-004MS-1140	Completionof Playground Area	0.00	0%	0%		16Jan-27		29Apr-27	$000	$000	$0.00	0.00
MLTX02-004MS-1150	Completionof NaturalLandscape Works	0.00	0%	0%		13Dec-26		08Mar-27	$000	$000	$0.00	0.00
MLTX02-004MS-1050	Completionof Mobilization	0.00	100%	100%		02Jun-26		02Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MS-1060	Baseline ProgrammeApproval	0.00	100%	100%		29Apr-26		29Apr-26A	$000	$000	$0.00	0.00
JEDDAH		30800	4953%	4181%	26 Mar 26	25Jan-27	25 Mar26 A	25Mar-27	$6209,086.52	$5241,231.71	$12535,459.74	-4700
MOBILIZATION		6300	0%	0%	26 Mar 26	10Jun-26	25 Mar26 A	10Jun-26A	$000	$000	$0.00	0.00
TOPOGRAPHICSURVEY		4.00	0%	0%	26 Mar 26	30Mar-26	25 Mar26 A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2100	Site Survey Works	4.00	100%	100%	26 Mar 26	30Mar-26	25 Mar26 A	30Mar-26A	$000	$000	$0.00	0.00
SITEFACILITIES & OFFICES		5575	0%	0%	26 Mar 26	02Jun-26	25 Mar26 A	02Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1980	Manpower Mobalizaton	3150	100%	100%	16 Apr 26	23May-26	16 Apr26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1990	Equipment Mobalization	1.40	100%	100%	14 Apr 26	15Apr-26	14 Apr26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2010	Site Layout Plan	4.00	100%	100%	26 Mar 26	30Mar-26	25 Mar26 A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2020	Clear & GrubforOffices &AccessRoad	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2030	ConstuctSiteAccess Roads	2.00	100%	100%	11 Apr 26	12Apr-26	10 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2040	ConstuctTemporay Fence	3975	100%	100%	14 Apr 26	02Jun-26	14 Apr26 A	02Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2050	ConstuctSiteOffices & Storage	2333	100%	100%	15 Apr 26	12May-26	15 Apr26 A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2060	InstallProject Signs	4.40	100%	100%	26 Apr 26	30Apr-26	25 Apr26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2070	InstallSiteFacilities	2872	100%	100%	08 Apr 26	11May-26	08 Apr26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2080	Electrical Works & Connections	2340	100%	100%	15 Apr 26	12May-26	15 Apr26 A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2090	ConstuctParking Sheds	6.00	100%	100%	12 Apr 26	18Apr-26	12 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
PRELIMINARY SUBMITTALS		5900	0%	0%	31 Mar 26	10Jun-26	31 Mar26 A	10Jun-26A	$000	$000	$0.00	0.00
PREPARATIONS& SUBMITTALBY CONTRACTORS		2700	0%	0%	31 Mar 26	30Apr-26	31 Mar26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2000	Preparation andSubmittal ofDetailedWorkOrderProgramme(Baseline)	2500	100%	100%	31 Mar 26	28Apr-26	31 Mar26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2110	Preparation andSubmittal ofProject Execution Plan	2700	100%	100%	31 Mar 26	30Apr-26	31 Mar26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2120	Submissionof Contactor Project Quality Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2130	Submissionof Construction Safety& EnvironmentalManagement Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2140	Preparation andSubmittal ofOrgarization Chat	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar26 A	08Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2150	Preparation andSubmittal ofCommunication Plan	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar26 A	08Apr-26A	$000	$000	$0.00	0.00
APPROVALS BYEMPLOYERS		5100	0%	0%	09 Apr 26	10Jun-26	09 Apr26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2160	Appoval of DetailedWorkOrderProgramme (Baseline)	1.00	100%	100%	29 Apr 26	29Apr-26	29 Apr26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2170	Appoval of Project Execution Plan	1.00	100%	100%	13May-26	13May-26	13 May 26 A	13May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2180	Appoval of ContactorProject QualityPlan	1900	100%	100%	09 Apr 26	30Apr-26	09 Apr26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2190	Appoval of Constuction Safety &EnvironmentalManagement Plan	1.00	100%	100%	10 Jun 26	10Jun-26	10 Jun 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2200	Appoval of Organization Chat	1000	100%	100%	09 Apr 26	20Apr-26	09 Apr26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-2210	Appoval of Communication Plan	1000	100%	100%	09 Apr 26	20Apr-26	09 Apr26 A	20Apr-26A	$000	$000	$0.00	0.00
ENGINEERING		18500	0%	0%	31 Mar 26	21Jul-26	31 Mar26 A	05Nov-26	$000	$000	$0.00	-9100
SHOP DRAWINGS		14400	0%	0%	31 Mar 26	21Jul-26	31 Mar26 A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWINGS SUBMISSION		13600	0%	0%	31 Mar 26	12Jul-26	31 Mar26 A	25Aug-26A	$000	$000	$0.00	-3800
SHOP DRAWINGSUBMITTALS FOR EARTHINGWORKS		5800	0%	0%	31 Mar 26	09Jun-26	31 Mar26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12100	ShopDWG SubmittalforLayoutPlan	2000	100%	100%	31 Mar 26	22Apr-26	31 Mar26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12110	ShopDWG SubmittalforSetting Out	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar26 A	25Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12120	ShopDWG SubmittalforGrading Layout Plan	2300	100%	100%	31 Mar 26	26Apr-26	31 Mar26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12130	ShopDWG SubmittalforCurb Setting OutPoints	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12140	ShopDWG SubmittalforSigning & MakingLayoutPlan	1.00	100%	100%	09 Jun 26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12150	ShopDWG SubmittalforStandards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGSUBMITTALS FOR SERVICE/TOILETWORKS		13600	0%	0%	31 Mar 26	12Jul-26	31 Mar26 A	25Aug-26A	$000	$000	$0.00	-3800
ARCHITECTURE WORKS		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-124	ShopDWG SubmittalforFloorPlan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-124	ShopDWG SubmittalforElevations	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforSections	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforCeiling Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforFinishes Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00

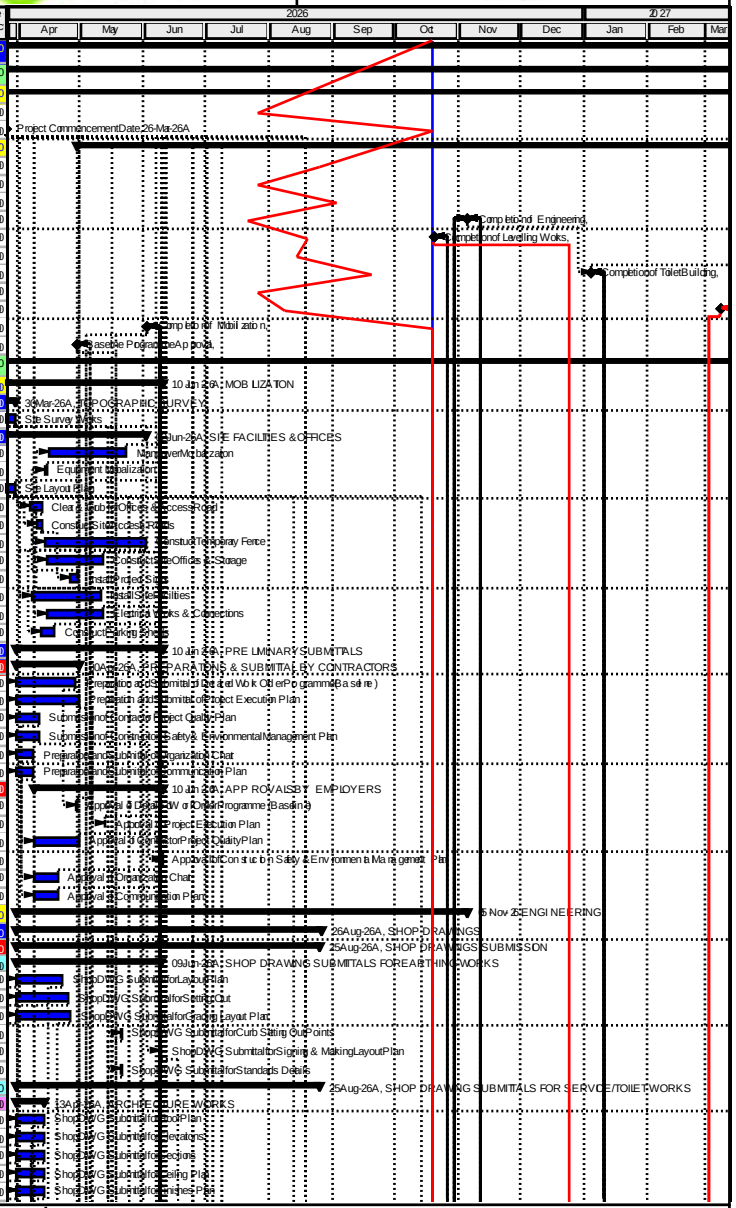

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-125	ShopDWG SubmittalforToilet Details	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforDoorsWindows Schedule	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		9.00	0%	0%	08 Apr 26	18Apr-26	08 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforFoundationPlan	9.00	100%	100%	08 Apr 26	18Apr-26	08 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforGroundFloorFraming Plan	9.00	100%	100%	08 Apr 26	18Apr-26	08 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforSections/Details	9.00	100%	100%	08 Apr 26	18Apr-26	08 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		3800	0%	0%	08 Apr 26	21May-26	08 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforHVAC Plan	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforExhaustAirPlan	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforHVAC Equipment Schedule	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforFireFighting Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforWaterSupply Layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforWaterSupply Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforDrainage Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforDrainage Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforDut RoutingLayout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	ShopDWG SubmittalforDiffusersLayout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		12900	0%	0%	08 Apr 26	12Jul-26	08 Apr 26 A	25Aug-26A	$000	$000	$0.00	-3800
MLTX-02-004EN-126	ShopDWG SubmittalforLighting layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-126	ShopDWG SubmittalforPower layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-126	ShopDWG SubmittalforPower SingleLineDiagram	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-126	ShopDWG SubmittalforPanelBoardSchedules	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforLighting Installation Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforPower Installation Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforCableTrayInstallation Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforManhole& Ductbank Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforGrounding Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforLightningProtecton Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforFireAlarmInstallation Details	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforCCTV Details	3.00	100%	100%	09 Jul-26	12Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	2.00
MLTX-02-004EN-127	ShopDWG SubmittalforGrounding Layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-127	ShopDWG SubmittalforLightningProtecton System Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-128	ShopDWG SubmittalforFireAlarmLayout	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-128	ShopDWG SubmittalforFireAlarmRiserDiagram	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-128	ShopDWG SubmittalforCCTV Layout	5.00	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-128	ShopDWG SubmittalforCCTV Riser Diagram	5.00	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-128	ShopDWG SubmittalforTelephone & Data Layout	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-128	ShopDWG SubmittalforTelephone & Data Riser Diagram	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GSSUBMITTALS FOR PLAYGROUND WORKS		13400	0%	0%	31 Mar 26	09Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-4000
ARCHITECTURE WORKS		3900	0%	0%	31 Mar 26	14May-26	31 Mar 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforPlayground Plan/Layout	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforFurniture& Marking	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforSections	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforInterlockPatten Plan	7.00	100%	100%	31 Mar 26	07Apr-26	31 Mar 26 A	07Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforDoorsWindows Schedule	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforDome Internal Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforAir Dome System	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforFoundationof AirDome	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforAir Dome Structural Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforMembrane PanelLayout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforCableTension Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforAirlock DoorDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-131	ShopDWG SubmittalforEmergency ExitDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	ShopDWG SubmittalforFootball Turf Instalation	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	ShopDWG SubmittalforBasketballCourtMarking	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	ShopDWG SubmittalforPadelCourtStructure	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		2000	0%	0%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforHVAC Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-130	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		9100	0%	0%	20 May-26	09Jul-26	20 May 26 A	25Aug-26A	$000	$000	$0.00	-4000
MLTX-02-004EN-125	ShopDWG SubmittalforLighting layout	1.00	100%	100%	20 May-26	20May-26	20 May 26 A	20May-26A	$000	$000	$0.00	0.00

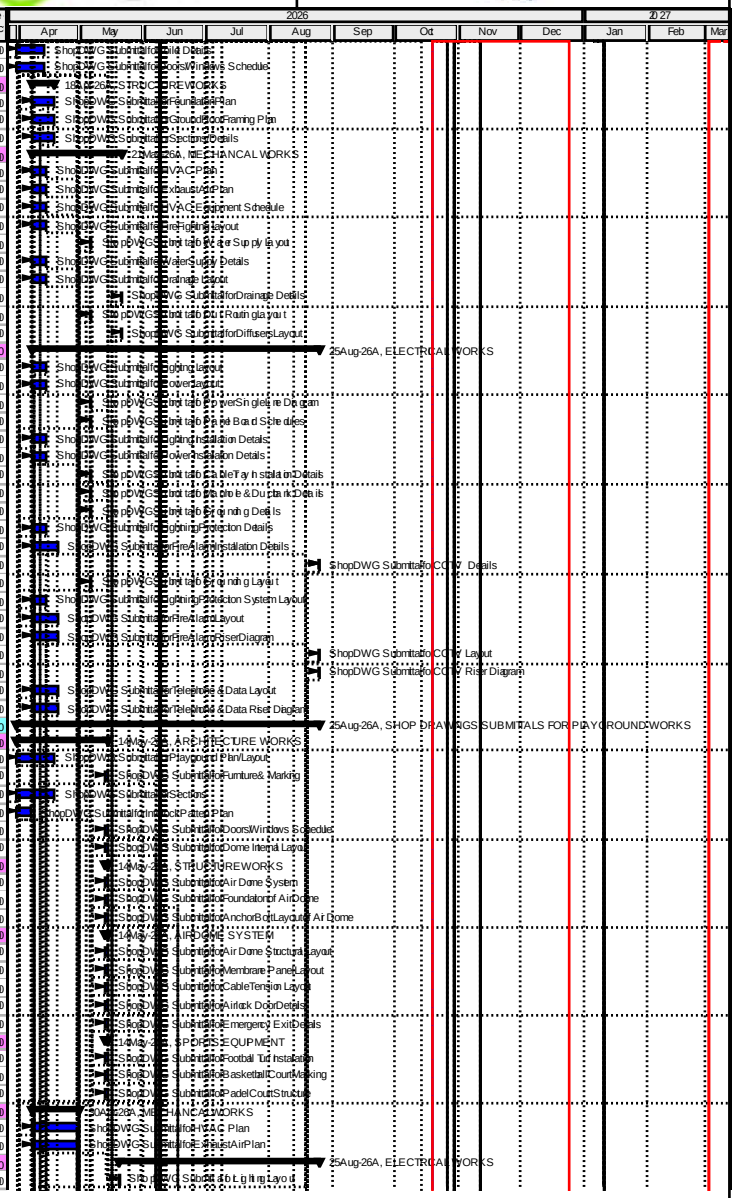

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004EN-125	ShopDWG SubmittalforPower Layout	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforPower SingleLineDiagram	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforPanelBoardSchedules	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforPower Installation Details	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforFireAlarmInstallation Details	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforCCTV Details	4.00	100%	100%	05 Jul-25	08Jul-26	25 Aug-25A	25Aug-26A	$000	$000	$0.00	3.00
MLTX02-004EN-125	ShopDWG SubmittalforFireAlarmLayout	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-130	ShopDWG SubmittalforFireAlarmRiserDiagram	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-130	ShopDWG SubmittalforCCTV Layout	5.00	100%	100%	05 Jul-25	09Jul-26	25 Aug-25A	25Aug-26A	$000	$000	$0.00	4.00
MLTX02-004EN-130	ShopDWG SubmittalforCCTV Riser Diagram	5.00	100%	100%	05 Jul-25	09Jul-26	25 Aug-25A	25Aug-26A	$000	$000	$0.00	4.00
SHOP DRAWIN GSSUBMITTALS FOR LANDSCAPE WORKS		6500	0%	0%	31 Mar26	17Jun-26	31 Mar26A	17Jun-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		4200	0%	0%	31 Mar26	18May-26	31 Mar26A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforLandscape Layout	2000	100%	100%	31 Mar26	22Apr-26	31 Mar26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforHardscape Plan	5.00	100%	100%	13 May-26	18May-26	13 May-26A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforPlanting Plan	5.00	100%	100%	13 May-26	18May-26	13 May-26A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforLandscape Details	5.00	100%	100%	13 May-26	18May-26	13 May-26A	18May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	17 Jun26	17Jun-26	17 Jun26A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforIrrigation Details	1.00	100%	100%	17 Jun26	17Jun-26	17 Jun26A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforIrrigation Layout	1.00	100%	100%	17 Jun26	17Jun-26	17 Jun26A	17Jun-26A	$000	$000	$0.00	0.00
EIECTRCAL WORKS		1.00	0%	0%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALS		13800	0%	0%	07 Apr26	21Jul-26	07 Apr26A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWIN GAPPROVALFOR EARTHINGW ORKS		6500	0%	0%	07 Apr26	24Jun-26	07 Apr26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15530	ShopDWG Appovalfor layoutPlan	4.00	100%	100%	22 Apr26	26Apr-26	22 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15540	ShopDWG Appovalfor SettingOut	1700	100%	100%	07 Apr26	26Apr-26	07 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15550	ShopDWG Appovalfor GradingLayoutPlan	1.00	100%	100%	26 Apr26	26Apr-26	26 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15560	ShopDWG Appovalfor Curb SetingOut Points	1.00	100%	100%	21 May-26	21May-26	21 May-26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15570	ShopDWG Appovalfor Signing& Marking Layout Plan	1.00	100%	100%	24 Jun26	24Jun-26	24 Jun26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15580	ShopDWG Appovalfor Standards Details	1.00	100%	100%	21 May-26	21May-26	21 May-26A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GAPPROVALFOR SERVIC EBDILIETWORKS		13200	0%	0%	14 Apr26	21Jul-26	14 Apr26A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		9.00	0%	0%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor floorPlan	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Elevations	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Sections	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor CeilingPlan	5.00	100%	100%	14 Apr26	19Apr-26	14 Apr26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor finishes Plan	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor ToiletDetails	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Doors/WindowsSchedule	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26A	24Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		6.00	0%	0%	18 Apr26	23Apr-26	18 Apr26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor Foundation Plan	6.00	100%	100%	18 Apr26	23Apr-26	18 Apr26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor Gound floorFraming Plan	6.00	100%	100%	18 Apr26	23Apr-26	18 Apr26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor SectionsDetails	6.00	100%	100%	18 Apr26	23Apr-26	18 Apr26A	23Apr-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1400	0%	0%	06 May-26	21May-26	06 May-26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	06 May-26	06May-26	06 May-26A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor HVACEquipment Schedule	1.00	100%	100%	06 May-26	06May-26	06 May-26A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor fire fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor WaterSupplyLayout	0.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor WaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor DrainageLayout	1.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor DrainageDetails	1.00	100%	100%	21 May-26	21May-26	21 May-26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-163	ShopDWG Appovalfor Duct RoutingLayout	1.00	100%	100%	07 May-26	07May-26	07 May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-163	ShopDWG Appovalfor Diffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May-26A	21May-26A	$000	$000	$0.00	0.00
EIECTRCAL WORKS		13100	0%	0%	15 Apr26	21Jul-26	15 Apr26A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-15(	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Power Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor lighting InstallationDetails	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Power InstallationDetails	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Cable Tray InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Manhole& Ducttank Details	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Grounding Details	1.00	100%	100%	23 May-26	23May-26	23 May-26A	23May-26A	$000	$000	$0.00	0.00

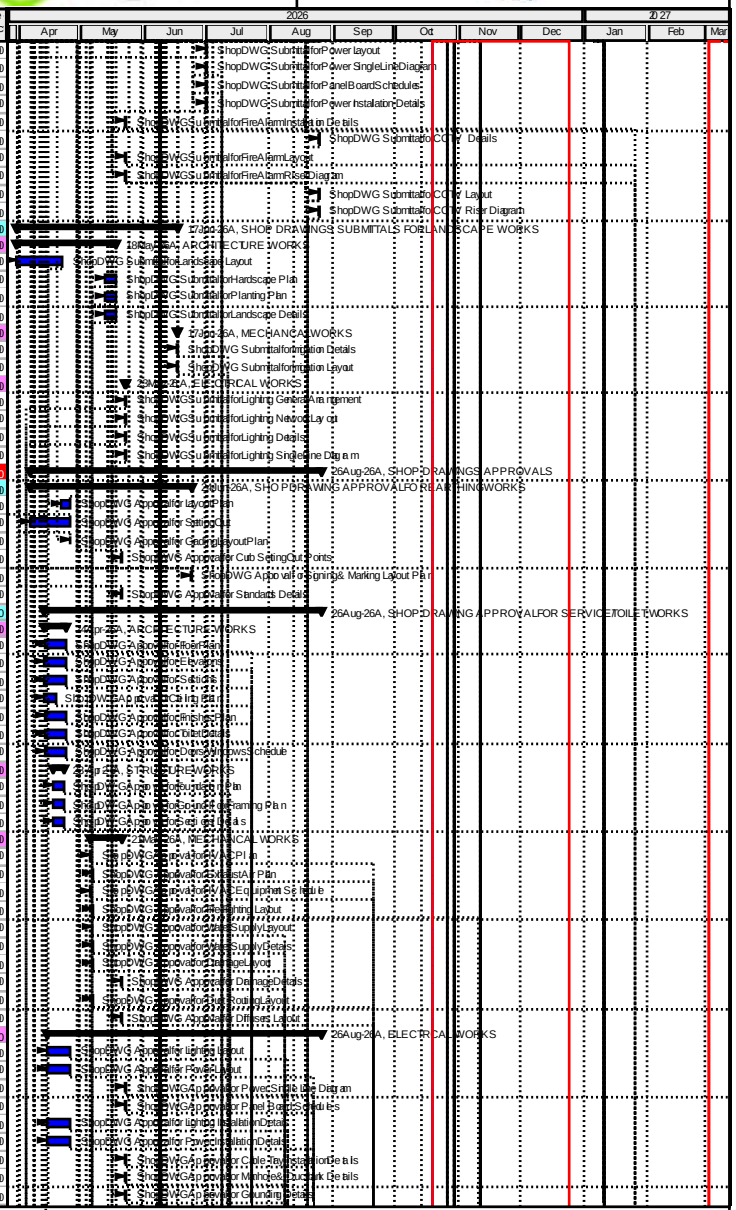


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004EN-159	ShopDWG Approval for lightning Protection Details	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for fire Alarm Installation Details	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for CCTV Details	8.00	100%	100%	13 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	7.00
MLTX02-004EN-159	ShopDWG Approval for Grounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for lightning Protection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for CCTV Layout	8.00	100%	100%	13 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	7.00
MLTX02-004EN-159	ShopDWG Approval for CCTV RiserDiagram	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-159	ShopDWG Approval for Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for Telephone & Data Riser Diagram	7.00	100%	100%	20 Apr 26	27Apr-26	20 Apr 26A	27Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		13700	0%	0%	08 Apr 26	21Jul-26	08 Apr 26A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		5400	0%	0%	08 Apr 26	13Jun-26	08 Apr 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Approval for Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Approval for Furniture & Marking	1.00	100%	100%	13Jun-26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Approval for Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Interlock Pattern Plan	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Doors/Windows Schedule	1.00	100%	100%	13Jun-26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Dome Internal Layout	1.00	100%	100%	13Jun-26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTURE WORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Air Dome System	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Foundation of Air Dome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Foundation of Air Dome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Anchor Bolt layout of Air Dome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
AIR DOMES YSTEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Air Dome Structural Layout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Membrane Panel Layout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Cable Tension Layout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Airlock Door Details	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Emergency Exit Details	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Football Tuf Installation	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Basketball Court Marking	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Approval for Padel Court Stucture	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Approval for HVAC Plan	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Approval for Exhaust Air Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-160	ShopDWG Approval for lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for Power Single line Diagram	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Approval for Panel Board Schedules	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Approval for Power Installation Details	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Approval for CCTV Details	1000	100%	100%	09 Jul-26	20Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-161	ShopDWG Approval for CCTV Layout	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-161	ShopDWG Approval for CCTV RiserDiagram	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		8700	0%	0%	11 Apr 26	11Jul-26	11 Apr 26A	18Jul-26A	$000	$000	$0.00	-600
ARCHITECTURE WORKS		2000	0%	0%	22 Apr 26	14May-26	22 Apr 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for landscape Layout	4.00	100%	100%	22 Apr 26	26Apr-26	22 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for Hardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for Planting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Approval for landscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		6.00	0%	0%	05 Jul-26	11Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-160	ShopDWG Approval for Irrigation Details	6.00	100%	100%	05 Jul-26	11Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-160	ShopDWG Approval for Irrigation Layout	6.00	100%	100%	05 Jul-26	11Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	5.00
ELECTRCAL WORKS		3700	0%	0%	11 Apr 26	23May-26	11 Apr 26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for lighting General Arrangement	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for lighting Network Layout	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for lighting Details	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Approval for lighting Single Line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		18500	0%	0%	31 Mar 26	21Jul-26	31 Mar 26A	05Nov-26	$000	$000	$0.00	-9100
METHOD STATEMENT SUBMITTAL		17500	0%	0%	31 Mar 26	21Jul-26	31 Mar 26A	25Oct-26	$000	$000	$0.00	-8100
CIVL WORKS		4500	0%	0%	31 Mar 26	21May-26	31 Mar 26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12200	Preparation & Submission of Method Statement for Earthwork	1700	100%	100%	31 Mar 26	19Apr-26	31 Mar 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12210	Preparation & Submission of Method Statement for Concete Works	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12220	Preparation & Submission of Method Statement for Waterproding	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar 26A	25Apr-26A	$000	$000	$0.00	0.00

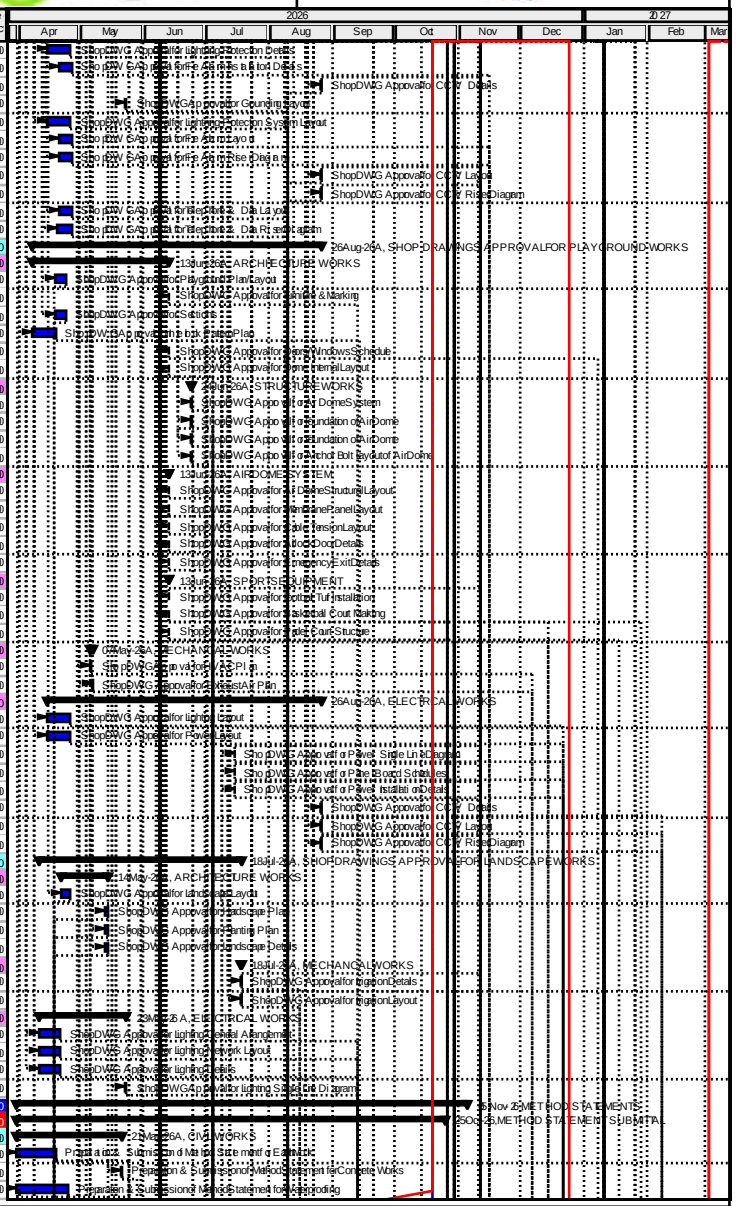

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation


MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

PROFAST

egis

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
	ARCHITECTURE WORKS	12600	0%	0%	31-May-26	11Jul-26	31 May 26 A	25Oct-26	$000	$000	$0.00	-9000
MLTX02.00.4EN-12330	Preparation & Submissionof MethodStatement forFenceWorks	5.00	100%	0%	05 Jul- 26	09Jul-26	20 Oct 26	25Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4EN-12250	Preparation & Submissionof MethodStatement forPlasteringWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12260	Preparation & Submissionof MethodStatement forMasonary Works	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12270	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12280	Preparation & Submissionof MethodStatement forSeatsBenchesWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12290	Preparation & Submissionof MethodStatement forDoorsWindows Works	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12300	Preparation & Submissionof MethodStatement forInterlock/Curbstone Works	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12310	Preparation & Submissionof MethodStatement forParking Works	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12320	Preparation & Submissionof MethodStatement forSoftScapeWorks	5.00	100%	100%	05 Jul- 26	09Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4EN-12340	Preparation & Submissionof MethodStatement forAirDome Works	5.00	100%	100%	05 Jul- 26	09Jul-26	19 Aug 26 A	19Aug-26A	$000	$000	$0.00	4.00
MLTX02.00.4EN-12350	Preparation & Submissionof MethodStatement forMetalWorks	6.00	100%	100%	05 Jul- 26	11Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02.00.4EN-12360	Preparation & Submissionof MethodStatement forPartitions Works	5.00	100%	100%	05 Jul- 26	09Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4EN-12370	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	14 Jun 26	14Jun-26	14 Jun 26 A	14Jun-26A	$000	$000	$0.00	0.00
	MECHANICALWORKS	4800	0%	0%	07 Apr 26	04Jun-26	07 Apr 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12380	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12390	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12400	Preparation & Submissionof MethodStatement forFire FightingSystem	7.00	100%	100%	07 Apr 26	14Apr-26	07 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12410	Preparation & Submissionof MethodStatement forIrrigation System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12420	Preparation & Submissionof MethodStatement forHVAC System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
	ELECTRICAL WORKS	4900	0%	0%	13 Jun 26	21Jul-26	13 Jun 26 A	22Jul-26A	$000	$000	$0.00	-100
MLTX02.00.4EN-12230	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12240	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12430	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	1000	100%	100%	11 Jul- 26	21Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-12440	Preparation & Submissionof MethodStatement forCCTV System	1000	100%	100%	11 Jul- 26	21Jul-26	22 Jul -26A	22Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-12450	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12460	Preparation & Submissionof MethodStatement forEarthing/Lightning Works	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-12470	Preparation & Submissionof MethodStatement forPanelBoardsWorks	9.00	100%	100%	05 Jul- 26	14Jul-26	18 Jul -26A	18Jul-26A	$000	$000	$0.00	8.00
	METHOD STATEMENT APPROVAL	17200	0%	0%	15 Apr 26	21Jul-26	15 Apr 26 A	05Nov-26	$000	$000	$0.00	-9100
	CIVL WORKS	6.00	0%	0%	21 May-26	31May-26	21 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15260	Appoval of Method Statementfor Earthwork	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15270	Appoval of Method Statementfor Concrete Woks	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15280	Appoval of Method Statementfor Waterproofing	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
	ARCHITECTURE WORKS	13600	0%	0%	31 May-26	21Jul-26	31 May 26 A	05Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4EN-15390	Appoval of Method Statementfor fence Works	1000	100%	0%	11 Jul- 26	21Jul-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4EN-15310	Appoval of Method Statementfor Plasteing Works	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15320	Appoval of Method Statementfor MasonaryWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15330	Appoval of Method Statementfor Tiling Woks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15340	Appoval of Method Statementfor Seats/Benches Works	6.00	100%	100%	05 Jul- 26	11Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02.00.4EN-15350	Appoval of Method Statementfor Doors/WindowsWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15360	Appoval of Method Statementfor Intelock/Curbstone Woks	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15370	Appoval of Method Statementfor ParkingWorks	1.00	100%	100%	31-May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15380	Appoval of Method Statementfor Soft Scape Woks	1000	100%	100%	11 Jul- 26	21Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15400	Appoval of Method Statementfor Air DomeWorks	1000	100%	100%	11 Jul- 26	21Jul-26	27 Aug 26 A	27Aug-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15410	Appoval of Method Statementfor PartitionsWorks	1000	100%	100%	11 Jul- 26	21Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15420	Appoval of Method Statementfor Gypsum Board Woks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
	MECHANICALWORKS	4700	0%	0%	15 Apr 26	11Jun-26	15 Apr 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15430	Appoval of Method Statementfor Sewage/DainageSystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15440	Appoval of Method Statementfor WaterSupplySystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15450	Appoval of Method Statementfor fireFighting System	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15460	Appoval of Method Statementfor IrrigationSystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4EN-15470	Appoval of Method Statementfor HVAC System	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
	ELECTRICAL WORKS	2100	0%	0%	05 Jul- 26	21Jul-26	11 Jul -26A	22Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4EN-15290	Appoval of Method Statementfor ElectricalConduits/Pulling Works	6.00	100%	100%	05 Jul- 26	11Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02.00.4EN-15300	Appoval of Method Statementfor Lighting Poles Installation	1000	100%	100%	05 Jul- 26	15Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15480	Appoval of Method Statementfor Telecommunication & Data System	1000	100%	100%	05 Jul- 26	15Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15490	Appoval of Method Statementfor CCTV System	1000	100%	100%	11 Jul- 26	21Jul-26	22 Jul -26A	22Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15500	Appoval of Method Statementfor Lighting Works	1000	100%	100%	05 Jul- 26	15Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02.00.4EN-15510	Appoval of Method Statementfor Earthing/LightningWorks	5.00	100%	100%	05 Jul- 26	09Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4EN-15520	Appoval of Method Statementfor Panel Boards Works	5.00	100%	100%	16 Jul- 26	21Jul-26	18 Jul -26A	18Jul-26A	$000	$000	$0.00	4.00
	PRE-QUALFICATION& MATERIAL	18000	0%	0%	31 Mar 26	15Jul-26	31 Mar 26 A	31Oct-26	$000	$000	$0.00	-9100
	PRE-QUALFICATION	4500	0%	0%	31 Mar 26	21May-26	31 Mar 26 A	21May-26A	$000	$000	$0.00	0.00
	TOILETSERVICEWORKS	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
	STEELREINFORCEMENT	1200	0%	0%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualification Approvalfor SteelReinfocement	2.00	100%	100%	12 Apr 26	13Apr-26	12 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-142	PreQualification SubmittalforSteelReinforcement	1100	100%	100%	31 Mar 26	12Apr-26	31 Mar 26 A	12Apr-26A	$000	$000	$0.00	0.00

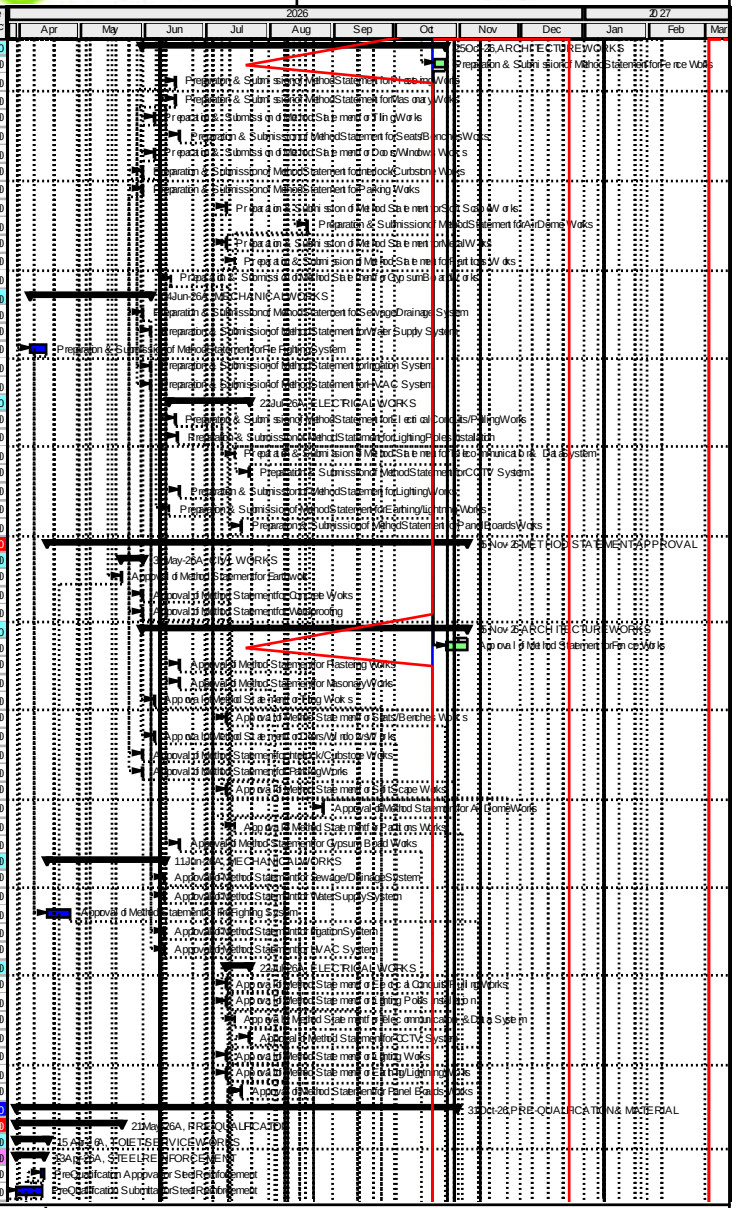

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule D.D 19-10-2026







ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	READY MIX CONCRETE	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-142	PreQualification Submittal for Ready Mixed Concrete	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-142	PreQualification Approval of Ready Mixed Concrete	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	CONCRETE BLOCKS	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Submittal for Concrete Blocks	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Approval for Concrete Blocks	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	WATERPROOFING	1200	0%	0%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualification Approval for WaterProofing	3.00	100%	100%	11 Apr 26	13 Apr-26	11 Apr 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualification Submittal for WaterProofing	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
	FLOORING ALL TILES	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Submittal for Tilling Materials	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Approval for Tailing Material	5.00	100%	100%	07 Apr 26	12 Apr-26	07 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	SUSPENDED CEILING	1200	0%	0%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Submittal for Suspend Ceiling	1100	100%	100%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Approval for Suspend Ceiling	2.00	100%	100%	12 Apr 26	13 Apr-26	12 Apr 26	13 Apr-26	$000	$000	$0.00	0.00
	DOORS/WINDOWS	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Submittal for Doors/Windows	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Approval for Doors/Windows	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	FURNITURES	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Submittal for Furnitures	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Approval for Furnitures	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	SANITARY FIXTURES	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Submittal for Sanitary Fixtures	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Approval for Sanitay Fixtures	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	WATER SUPPLY PIPES	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Submittal for Water Supply Pipes	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-145	PreQualification Approval for WaterSupply Pipes	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	SEWAGE DRAINAGE PIPES	1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Submittal for Sewage Drainage Pipes	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26	11 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Approval for Sewage/DrainagePipes	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
	PACKAGE ACUNITS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Submittal for PackageAC Units	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Approval for PackageAC Units	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	AIRDFUSSERS/GRILLS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Submittal for Air Diffusers/Grills	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Approval for Air Diffusers/Grills	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	GALVANIZED DUCTS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Submittal for Galvarized Ducts	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Approval for Galvanized Ducts	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	EXHAUST FANS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Submittal for ExhaustFans	5.00	100%	100%	07 Apr 26	12 Apr-26	07 Apr 26	12 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualification Approval for ExhaustFans	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	LIGHTING FIXTURES	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Submittal for Lighting Fixtures	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26	09 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Approval for Lighting Fixtures	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	SWITCHES/SOCKETS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Submittal for Switches/Sockets	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26	09 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualification Approval for Switches/Sockets	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	EARTHINGSYSTEM	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Submittal for Earthing System	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26	09 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Approval for Eathing System	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	DISTRIBUTION PANNELS	8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Submittal for Distribution Panels	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26	09 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification Approval for Distribution Panels	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	PLAYGROUND WORKS	1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26	15 Apr-26	$000	$000	$0.00	0.00
	PVC MEMBRANE	1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualification Submittal for PVC Membane	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualification Approval for PVC Membrane	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	STEEL TENSION CABLES	1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualification Submittal for Steel Tension Cables	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification Approval for Steel Tension Cables	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	EMERGENCY DOORS	1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualification Submittal for Emergency Doos	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification Approval for EmergencyDoors	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26	15 Apr-26	$000	$000	$0.00	0.00
	PRESSURE UNITS	1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26	15 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualification Submittal for Pressue Units	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26	13 Apr-26	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification Approval for Pressue Units	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26	15 Apr-26	$000	$000	$0.00	0.00

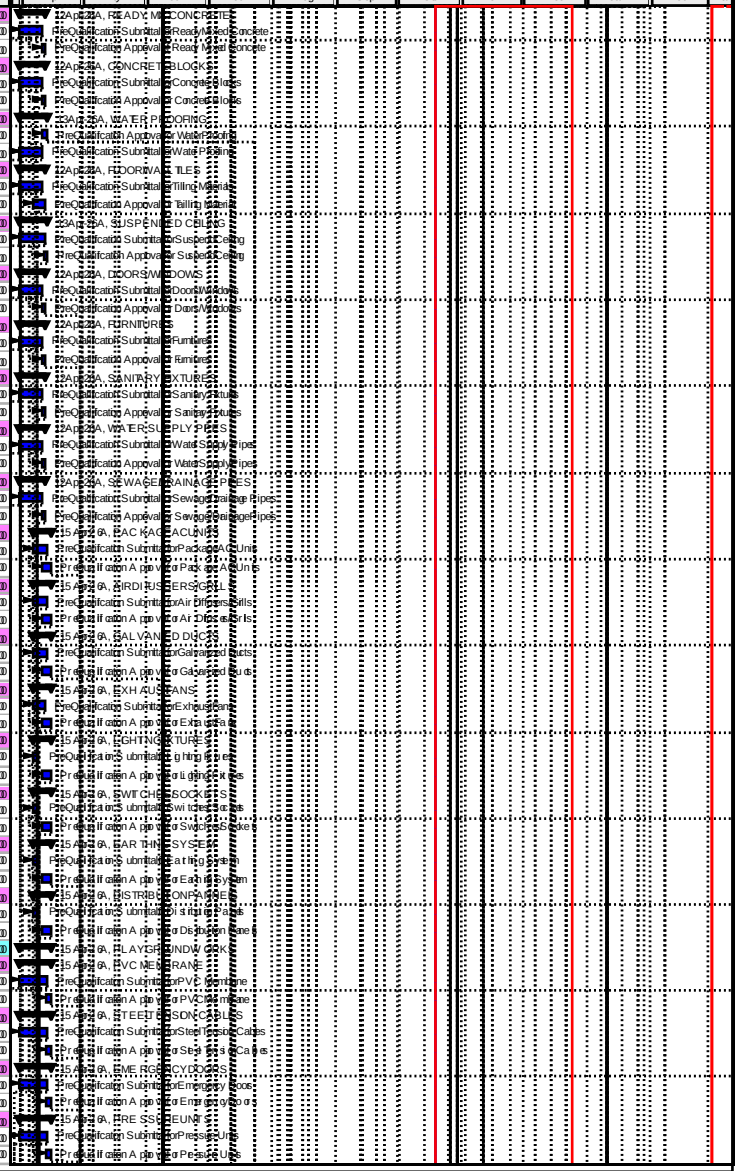

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	AIRLOCK DOORS	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation SubmittalforLockDoors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor lock Doors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	ARTIFICIAL TURF	1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation SubmittalforArtificial TURF	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor ArtificialTURF	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
	RUBBER GRANULES	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation SubmittalforRubberGranules	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor RubberGranules	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	PADELGLASS	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation SubmittalforPadelGlass	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor Padel Glass	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	PADEL WIREMESH/STEEL SETS	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation SubmittalforWireMesh/SteelSets	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor WireMesh/Steel Sets	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	AGGREGATE BASECOURSE	1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation SubmittalforAggregate Base Course	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation Appovalfor Aggregate BaseCourse	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	BITUMNOUS BASE &WEARING COURSE	7.00	0%	0%	07 Apr 26	14Apr-26	07 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation Appovalfor he Site	3.00	100%	100%	12 Apr 26	14Apr-26	12 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
	INTERLOCKING PAVING	2.00	0%	0%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualifcation Appovalfor hterbocking BlockPavers	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation SubmittalforIntelocking Block Paves	1.00	100%	100%	11 Apr 26	11Apr-26	11 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.00
	MARKINGPAINT	8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-146	PreQualifcation SubmittalforMarking Paint	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-152	PreQualifcation Appovalfor MakingPaint	1.00	100%	100%	12 Apr 26	12Apr-26	12 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
	PACKAGE ACUNITS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualifcation SubmittalforPackageAC Units	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualifcation Appovalfor PackageAC Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	AIRDFUSSERS/GRILLS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-147	PreQualifcation SubmittalforAir Dfussers/Grills	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation Appovalfor Air Dfusses/Grills	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	GALVANIZEDDUCTS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation SubmittalforGalvanized Duct	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation Appovalfor Galvanized Duct	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	EXHAUSTFANS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation SubmittalforExhaustFans	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-148	PreQualifcation Appovalfor ExhaustFans	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	DISTRBUTON BOARDS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation SubmittalforDistribution Boards	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation Appovalfor Distribution Boards	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	POWERCABLES	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation SubmittalforPowerCables	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation Appovalfor Power Cables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	LIGHTFXTURES	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation SubmittalforLightFixtures	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation Appovalfor lightFixtures	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	CCTV MATERALS	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation SubmittalforCCTV	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation Appovalfor CCTV	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	POWEROUTIETS/SWITCHES	1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-149	PreQualifcation SubmittalforPowerOutlets/Switches	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation Appovalfor Power OutetsSwitches	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
	LANDSCAPE WORKS	4200	0%	0%	04 Apr 26	21May-26	04 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
	INTERLOCKING PAVING	8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation SubmittalforIntelocking Block Paves	7.00	100%	100%	04 Apr 26	11Apr-26	04 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualifcation Appovalfor hterbocking BlockPavers	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
	CURBSTONE	8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualifcation SubmittalforCurbstone	7.00	100%	100%	04 Apr 26	11Apr-26	04 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualifcation Appovalfor Cubstone	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
	PAVEMENTMARKNG	8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualifcation Appovalfor PavementMarkings	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation SubmittalforPavementMarkings	3.00	100%	100%	04 Apr 26	06Apr-26	04 Apr 26 A	06Apr-26A	$000	$000	$0.00	0.00
	TRAFFC SGNS	1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-142	PreQualifcation SubmittalforTraffic Signs	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-143	PreQualifcation Appovalfor Traffic Signs	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00

2026: Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec

2027: Jan | Feb | Mar

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
	IRRIGATIONPIPES&SPRINKLERS	4200	0%	0%	04 Apr 26	21-May-26	01 Apr 26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification SubmittalforIrrigation Pipes/Sprinkles	2000	100%	100%	04 Apr 26	26Apr-26	01 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-144	PreQualification AppovalforIrrigationPipes&Sprinkles	1.00	100%	100%	21 May-26	21-May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
	AGRICULTURE SOIL	4200	0%	0%	04 Apr 26	21-May-26	01 Apr 26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualification SubmittalforAgricultue Soil	2000	100%	100%	04 Apr 26	26Apr-26	01 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification AppovalforAgricutureSoil	1.00	100%	100%	21 May-26	21-May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
	TRACK SURFACE	8.00	0%	0%	04 Apr 26	12Apr-26	01 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification SubmittalforTrackSurface	3.00	100%	100%	04 Apr 26	06Apr-26	01 Apr 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification AppovalforTackSurface	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
	GRASS/TREES	1400	0%	0%	04 Apr 26	19Apr-26	01 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification SubmittalforGrass/Trees	1000	100%	100%	04 Apr 26	14Apr-26	01 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-151	PreQualification AppovalforGass/Trees	5.00	100%	100%	14 Apr 26	19Apr-26	14 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
	CABLES	2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualification SubmittalforCables	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-150	PreQualification AppovalforCables	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
	LIGHTPOLES	2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-142	PreQualification SubmittalforLighting poles	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-142	PreQualification AppovalforLighting poles	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
	MATERIALSUBMITTAL	17100	0%	0%	11 Apr 26	15Jul-26	11 Apr 26A	31Oct-26	$000	$000	$0.00	-9100
	TOILETSERVICEWORKS	9100	0%	0%	11 Apr 26	11Jul-26	11 Apr 26A	22Jul-26A	$000	$000	$0.00	-1000
	STEELREINFORCEMENT	2.00	0%	0%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Steel Reinforement	1.00	100%	100%	11 Apr 26	11Apr-26	11 Apr 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforSteelReinbrcement	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
	READY MIXCONCRETE	2.00	0%	0%	14 Apr 26	15Apr-26	14 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Ready MixedConcete	1.00	100%	100%	14 Apr 26	14Apr-26	14 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalofReady Mixed Concrete	2.00	100%	100%	14 Apr 26	15Apr-26	14 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
	CONCRETE BLOCKS	3.00	0%	0%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-134	MaterialSubmittal for ConcreteBlocks	2.00	100%	100%	13 Apr 26	14Apr-26	13 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-134	MaterialApprovalforConcete Blocks	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
	FLOORWALLTILES	8700	0%	0%	15 Apr 26	11Jul-26	15 Apr 26A	22Jul-26A	$000	$000	$0.00	-1000
MLTX-02-004EN-134	MaterialSubmittal for TilingMaterials	3.00	100%	100%	15 Apr 26	18Apr-26	15 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-134	MaterialApprovalforTilingMaterial	6.00	100%	100%	05 Jul-26	11Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.00
	SUSPENDED CEILING	5.00	0%	0%	15 Apr 26	20Apr-26	15 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Suspend Ceiling	3.00	100%	100%	15 Apr 26	18Apr-26	15 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforSuspend Ceiling	2.00	100%	100%	19 Apr 26	20Apr-26	19 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
	DOORS/WINDOWS	1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Doors/Windows	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforDoors/Windows	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
	FURNITURES	2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Furnitures	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforFurnitures	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
	SANITARYFIXTURES	1400	0%	0%	15 Apr 26	30Apr-26	15 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for SanitaryFixtures	6.00	100%	100%	15 Apr 26	21Apr-26	15 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforSanitary fixtures	1100	100%	100%	19 Apr 26	30Apr-26	19 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
	WATERSUPPLY PIPES	2.00	0%	0%	15 Apr 26	16Apr-26	15 Apr 26A	16Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Water SupplyPipes	1.00	100%	100%	15 Apr 26	15Apr-26	15 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforWater Supply Pipes	2.00	100%	100%	15 Apr 26	16Apr-26	15 Apr 26A	16Apr-26A	$000	$000	$0.00	0.00
	SEWAGEDRAINAGEPIPES	2.00	0%	0%	15 Apr 26	16Apr-26	15 Apr 26A	16Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Sewage/Drainage Pipes	1.00	100%	100%	15 Apr 26	15Apr-26	15 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforSewageDrainage Pipes	2.00	100%	100%	15 Apr 26	16Apr-26	15 Apr 26A	16Apr-26A	$000	$000	$0.00	0.00
	PACKAGE ACUNITS	2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Package ACUnits	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforPackage AC Units	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
	AIRDIFUSSERS/GRILLS	1900	0%	0%	16 Apr 26	07May-26	16 Apr 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for AirDiffusers/Grills	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-137	MaterialApprovalforAirDiffusers/Grills	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
	GALVANIZEDDUCTS	6.00	0%	0%	13 Jun 26	18Jun-26	13 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-137	MaterialSubmittal for GalvanizedDucts	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-137	MaterialApprovalforGalvanizedDucts	1.00	100%	100%	18 Jun 26	18Jun-26	13 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
	EXHAUSTFANS	1800	0%	0%	16 Apr 26	06May-26	16 Apr 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-137	MaterialSubmittal for Exhaust Fans	2.00	100%	100%	16 Apr 26	18Apr-26	16 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-137	MaterialApprovalforExhaust Fans	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
	LIGHTING FIXTURES	8.00	0%	0%	16 Apr 26	25Apr-26	16 Apr 26A	25Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for LightingFixtures	3.00	100%	100%	16 Apr 26	19Apr-26	16 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialApprovalforLightingFixtures	5.00	100%	100%	20 Apr 26	25Apr-26	20 Apr 26A	25Apr-26A	$000	$000	$0.00	0.00
	SWITCHES/SOCKETS	8.00	0%	0%	16 Apr 26	25Apr-26	16 Apr 26A	25Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	MaterialSubmittal for Switches/Sockets	3.00	100%	100%	16 Apr 26	19Apr-26	16 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00

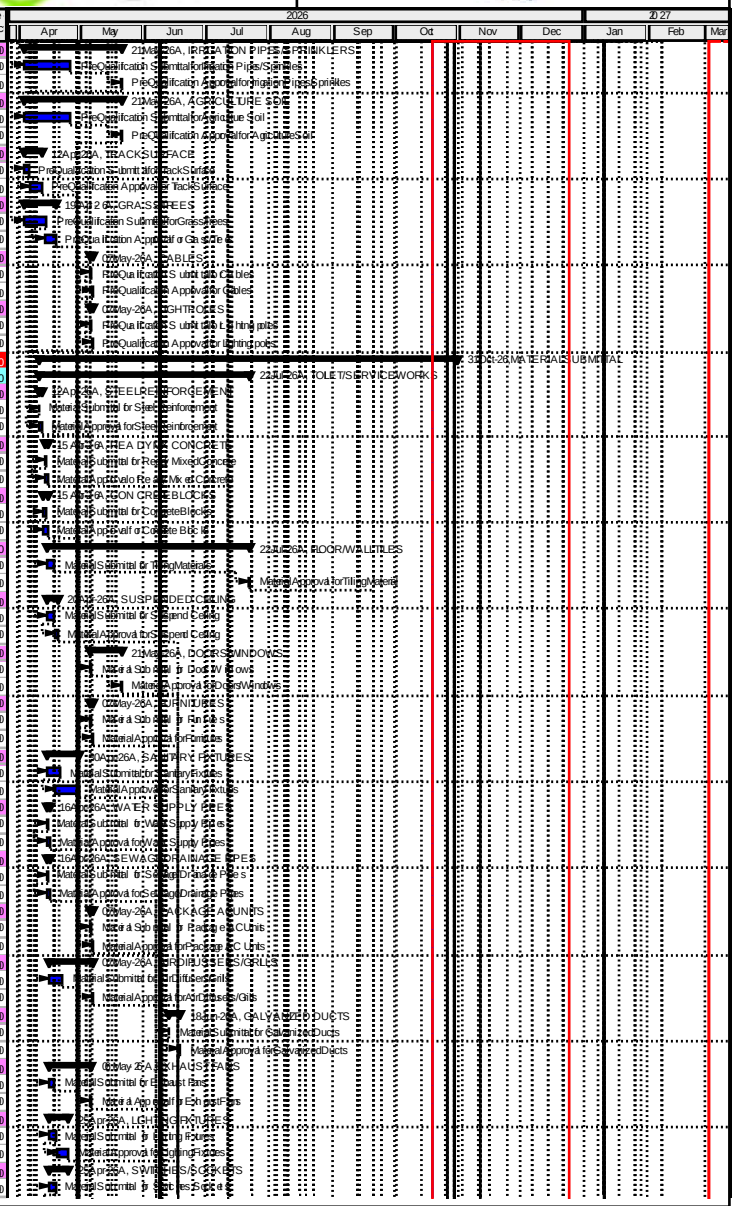


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-1360	Material Approval for Switches/Sockets	5.00	100%	100%	20 Apr 26	25Apr-26	20 Apr26 A	25Apr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1340	Material Submittal for EarthingSystem	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1340	Material Approval for Earthing System	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		8.00	0%	0%	16 Apr26	25Apr-26	16 Apr26 A	25Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1340	Material Submittal for DistributionPanels	3.00	100%	100%	16 Apr26	19Apr-26	16 Apr26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1340	Material Approval for Distributon Panels	5.00	100%	100%	20 Apr26	25Apr-26	20 Apr26 A	25Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		17000	0%	0%	12 Apr26	15Jul-26	12 Apr26 A	31Oct-26	$000	$000	$0.00	-9100
PVC MEMBRANE		7700	0%	0%	06 May-26	15Jul-26	06 May 26 A	27Jul-26A	$000	$000	$0.00	-1000
MLTX-02-004EN-1380	Material Submittal for PVC Membrane	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Approval for PVC Membane	1000	100%	100%	05 Jul-26	15Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	9.00
STEELTENSION CABLES		14900	0%	0%	06 May-26	15Jul-26	06 May 26 A	31Oct-26	$000	$000	$0.00	-9100
MLTX-02-004EN-1410	Material Approval for Steel Tension Cables	1000	100%	0%	05 Jul-26	15Jul-26	20 Oct26	31Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for Steel TensionCables	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		14700	0%	0%	06 May-26	15Jul-26	06 May 26 A	19Aug-26A	$000	$000	$0.00	-3000
MLTX-02-004EN-1380	Material Submittal for Emegency Doors	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1410	Material Approval for Emergency Doors	1000	100%	100%	05 Jul-26	15Jul-26	19 Aug 26 A	19Aug-26A	$000	$000	$0.00	9.00
PRESSURE UNITS		14900	0%	0%	06 May-26	15Jul-26	06 May 26 A	31Oct-26	$000	$000	$0.00	-9100
MLTX-02-004EN-1410	Material Approval for Pressure Units	1000	100%	0%	05 Jul-26	15Jul-26	20 Oct26	31Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for PressureUnits	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for Lock Doors	5.00	100%	100%	06 May-26	11May-26	06 May 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1410	Material Approval for LockDoors	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1700	0%	0%	12 Apr26	30Apr-26	12 Apr26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1400	Material Submittal for Artificial TURF	1500	100%	100%	12 Apr26	28Apr-26	12 Apr26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1410	Material Approval for Artificial TURF	3.00	100%	100%	28 Apr26	30Apr-26	28 Apr26 A	30Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		7300	0%	0%	06 May-26	15Jul-26	06 May 26 A	22Jul-26A	$000	$000	$0.00	-600
MLTX-02-004EN-1400	Material Submittal for Rubber Granules	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1420	Material Approval for RubberGranules	1000	100%	100%	05 Jul-26	15Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
PADEL GIASS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1400	Material Submittal for Padel Glass	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1420	Material Approval for PadelGlass	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
PADEL WIREMESH/STEEL SETS		5700	0%	0%	25 May-26	15Jul-26	25 May 26 A	22Jul-26A	$000	$000	$0.00	-600
MLTX-02-004EN-1400	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25 May-26	25May-26	25 May 26 A	25May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1420	Material Approval for Wire Mesh/Steel Sets	1000	100%	100%	05 Jul-26	15Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
AGGREGATE BASECOURSE		1100	0%	0%	21 May-26	06Jun-26	21 May 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1320	Material Submittal for AggregateBase Cairse	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1330	Material Approval for Aggregate Base Couse	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		2.00	0%	0%	16 Apr26	18Apr-26	16 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1330	Material Submittal for BitiminousBase& Wearing Couce	2.00	100%	100%	16 Apr26	18Apr-26	16 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1330	Material Approval forthe Site	1.00	100%	100%	18 Apr26	18Apr-26	18 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1.00	0%	0%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1330	Material Submittal for InterlockingBlockPavers	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1330	Material Approval forInterlocking Bbck Pavers	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MARKINGPAINT		6.00	0%	0%	13 Apr26	19Apr-26	13 Apr26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1360	Material Submittal for Making Paint	5.00	100%	100%	13 Apr26	18Apr-26	13 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1420	Material Approval for Marking Paint	2.00	100%	100%	18 Apr26	19Apr-26	18 Apr26 A	19Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1370	Material Submittal for Package ACUnits	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1370	Material Approval for Package AC Units	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		2100	0%	0%	13 Apr26	06May-26	13 Apr26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1370	Material Submittal for AirDifussersGrills	9.00	100%	100%	13 Apr26	22Apr-26	13 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1370	Material Approval for AirDifussers/Grills	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
GALVANIZEDUCTS		6.00	0%	0%	13 Jun 26	18Jun-26	13 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1370	Material Submittal for GalvanizedDuct	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Approval for GalvanizedDuct	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		2100	0%	0%	13 Apr26	06May-26	13 Apr26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for Exhaust Fans	5.00	100%	100%	13 Apr26	18Apr-26	13 Apr26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Approval for Exhaust Fans	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
DISTRBUTON BOARDS		9.00	0%	0%	13 Apr26	22Apr-26	13 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for DistributionBoards	3.00	100%	100%	13 Apr26	15Apr-26	13 Apr26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Approval for Distributon Boards	6.00	100%	100%	16 Apr26	22Apr-26	16 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		9.00	0%	0%	13 Apr26	22Apr-26	13 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for PowerCables	3.00	100%	100%	13 Apr26	15Apr-26	13 Apr26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1390	Material Approval for PowerCables	6.00	100%	100%	16 Apr26	22Apr-26	16 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
LIGHTFIXTURES		9.00	0%	0%	13 Apr26	22Apr-26	13 Apr26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1380	Material Submittal for Light Fixtures	3.00	100%	100%	13 Apr26	15Apr-26	13 Apr26 A	15Apr-26A	$000	$000	$0.00	0.00

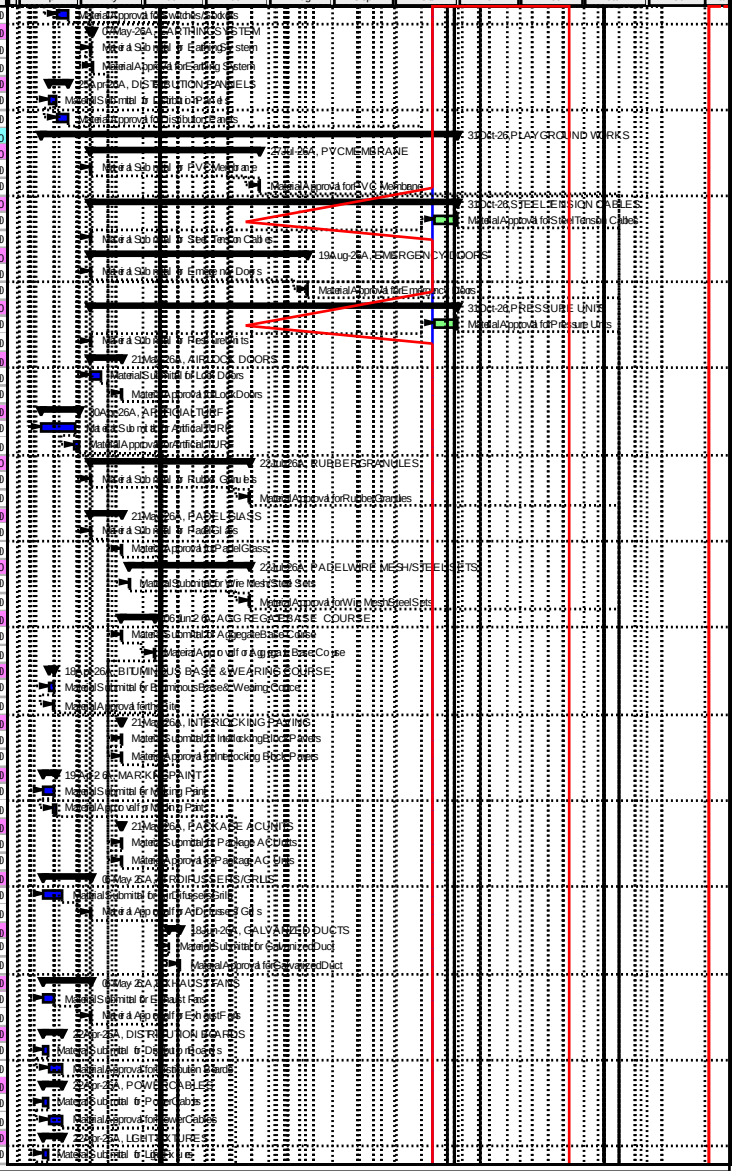


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-135	Material Approval for Light Fixtures	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-136	Material Submittal for CCTV	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-136	Material Approval for CCTV	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
POWER OUTLETS/SWITCHES		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-139	Material Submittal for PowerOutlets/Switches	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-139	Material Approval for PowerOutlets/Switches	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		44.00	0%	0%	13 Apr 26	06Jun-26	13 Apr 26A	06Jun-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Submittal for Interlocking Block Pavers	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Approval for Interlocking Block Pavers	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
CURB STONE		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-141	Material Submittal for Curbstone	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-141	Material Approval for Curbstone	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
PAVEMENT MARKING		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	Material Submittal for Pavement Markings	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	Material Approval for Pavement Markings	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
TRAFFIC SIGNS		24.00	0%	0%	06 May-26	06Jun-26	06 May 26A	06Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	Material Submittal for Traffic Signs	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-133	Material Approval for Traffic Signs	1.00	100%	100%	06 Jun-26	06Jun-26	06 Jun-26A	06Jun-26A	$000	$000	$0.00	0.00
IRRGATION PIPES & PRINKLERS		34.00	0%	0%	13 Apr 26	21May-26	13 Apr 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-134	Material Submittal for Irrigation Pipes/Sprinkles	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-134	Material Approval for Irrigation Pipes/Sprinkles	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
AGRICULTURE SOIL		14.00	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Submittal for Agriculture Soil	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Approval for Agriculture Soil	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		14.00	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Submittal for Track Suface	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-141	Material Approval for Track Surface	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
GRASS/TREES		14.00	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-141	Material Submittal for Grass/Trees	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-141	Material Approval for Grass/Trees	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
CABIES		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-135	Material Submittal for Cables	2.00	100%	100%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-140	Material Approval for Cables	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
LIGHT POLES		22.00	0%	0%	13 Apr 26	07May-26	13 Apr 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	Material Submittal for Lighting poles	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-132	Material Approval for Lighting poles	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
PROCUREMENT		183.00	0%	0%	07 May-26	14Sep-26	20 Apr 26A	10Dec-26	$000	$000	$0.00	-89.00
SHORT LEAD ITEM		176.00	0%	0%	07 May-26	17Aug-26	20 Apr 26A	02Dec-26	$000	$000	$0.00	-16.00
TOILETS/SERVICE WORKS		158.00	0%	0%	07 May-26	15Aug-26	07 May 26A	11Nov-26	$000	$000	$0.00	-75.00
STEEL REINFORCEMENT		58.00	0%	0%	13 May-26	09Jul-26	13 May 26A	18Jul-26A	$000	$000	$0.00	-7.00
MLTX02004PR-11050	PO for Steel Reinforcement	2.00	100%	100%	13 May-26	14May-26	13 May 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02004PR-11150	Material Delivery of Steel Reinforcement	5.00	100%	100%	05 Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
CONCRETE BLOCKS		74.00	0%	0%	07 May-26	13Jul-26	07 May 26A	27Jul-26A	$000	$000	$0.00	-12.00
MLTX02004PR-11230	PO for Concrete Blocks	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX02004PR-11240	Material Delivery of Concrete Blocks	8.00	100%	100%	05 Jul-26	13Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	7.00
FLOOR/WALL TILES		91.00	0%	0%	05 Jul-26	15Aug-26	22 Jul-26A	27Sep-26A	$000	$000	$0.00	-21.00
MLTX02004PR-11250	PO for Tilling Materials	5.00	100%	100%	05 Jul-26	09Jul-26	22 Jul-26A	23Jul-26A	$000	$000	$0.00	4.00
MLTX02004PR-11260	Material Delivery of Tailling Material	13.00	100%	100%	01 Aug-26	15Aug-26	27 Sep 26A	27Sep-26A	$000	$000	$0.00	12.00
SUSPENDED CEILING		37.00	0%	0%	24 Jun 26	19Jul-26	24 Jun 26A	22Jul-26A	$000	$000	$0.00	-2.00
MLTX02004PR-11270	PO for Suspend Celing	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11280	Material Delivery of Suspend Ceiling	13.00	100%	100%	05 Jul-26	19Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	13.00
DOORS/WINDOWS		99.00	0%	0%	24 Jun 26	21Jul-26	24 Jun 26A	05Oct-26A	$000	$000	$0.00	-64.00
MLTX02004PR-11290	PO for Doos/Windows	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11300	Material Delivery for Doos/Windows	15.00	100%	100%	05 Jul-26	21Jul-26	01 Oct 26A	05Oct-26A	$000	$000	$0.00	11.00
WATER SUPPLY PIPES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11330	PO for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11340	Material Delivery for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11350	PO for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11360	Material Delivery for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		117.00	0%	0%	16 Jun 26	19Jul-26	16 Jun 26A	05Aug-26A	$000	$000	$0.00	-15.00
MLTX02004PR-11310	PO for Sanitary Fixtures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02004PR-11320	Material Delivery for Sanitary Fixtures	13.00	100%	100%	05 Jul-26	19Jul-26	03 Aug 26A	05Aug-26A	$000	$000	$0.00	10.00
PACKAGE ACUNITS		122.00	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	05Nov-26	$000	$000	$0.00	-91.00
MLTX02004PR-11460	Material Delivery for Package AC Units	15.00	100%	0%	05 Jul-26	21Jul-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00

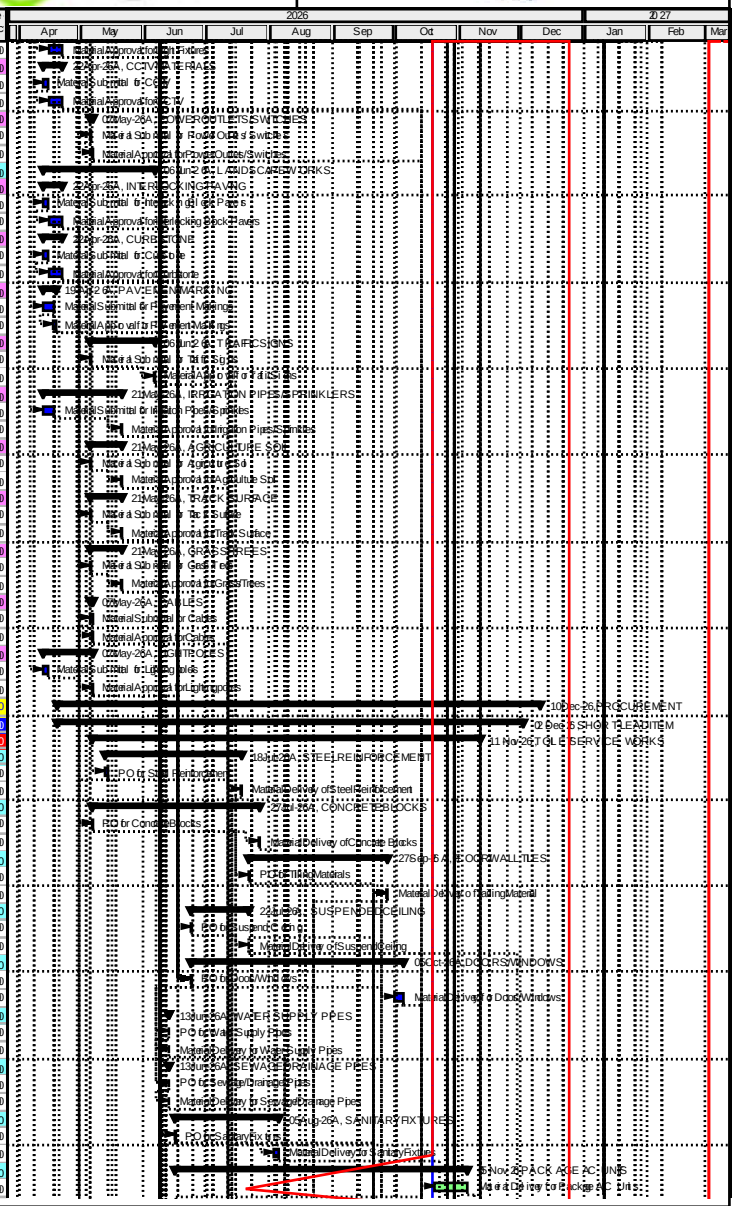

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02.00.4PR-11450	PO for Package AC Units	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/GRILS		2300	0%	0%	05 Jul-26	30Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	22.00
MLTX02.00.4PR-11470	PO for AirDiffusersGrills	8.00	100%	100%	05 Jul-26	13Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	8.00
MLTX02.00.4PR-11480	MaterialDelivery for AirDiffusersGrills	1500	100%	100%	14 Jul-26	30Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	14.00
GALVANIZED DUCTS		2300	0%	0%	05 Jul-26	30Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	22.00
MLTX02.00.4PR-11490	PO for GalvanizedDucts	8.00	100%	100%	05 Jul-26	13Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	7.00
MLTX02.00.4PR-11500	MaterialDelivery for GalvanizedDucts	1500	100%	100%	14 Jul-26	30Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	14.00
EXHAUST FANS		9700	0%	0%	18 Jun 26	15Jul-26	18 Jun 26A	27Sep-26A	$000	$000	$0.00	-62.00
MLTX02.00.4PR-11510	PO for Exhaust Fans	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11520	MaterialDelivery for Exhaust Fans	1000	100%	100%	05 Jul-26	15Jul-26	27 Sep 25 A	27Sep-26A	$000	$000	$0.00	9.00
LIGHTING FIXTURES		10400	0%	0%	01 Jul-26	15Jul-26	01 Jul-26A	31Oct-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11380	MaterialDelivery for LightingFixtures	1000	100%	0%	05 Jul-26	15Jul-26	20 Oct 26	31Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11370	PO for LightingFixtures	2.00	100%	100%	01 Jul-26	02Jul-26	01 Jul-26A	02Jul-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		10000	0%	0%	24 Jun 26	12Jul-26	24 Jun 26A	10Oct-26A	$000	$000	$0.00	-76.00
MLTX02.00.4PR-11390	PO for Switches/Sockets	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11400	MaterialDelivery for Switches/Sockets	7.00	100%	100%	05 Jul-26	12Jul-26	05 Oct 26A	10Oct-26A	$000	$000	$0.00	2.00
EARTHINGSYSTEM		1.00	0%	0%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11190	PO for EathingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11200	MaterialDelivery for EarthingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		2000	0%	0%	05 Jul-26	27Jul-26	20 Oct 26	11Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11210	PO for DistributionPanels	5.00	100%	0%	05 Jul-26	09Jul-26	20 Oct 26	25Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11220	MaterialDelivery for Distibuton Panels	1500	100%	0%	11 Jul-26	27Jul-26	26 Oct 26	11Nov-26	$000	$000	$0.00	0.00
FURNITURES		12700	0%	0%	16 Jun 26	27Jul-26	16 Jun 26A	11Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11420	MaterialDelivery for Furnitures	2000	100%	0%	05 Jul-26	27Jul-26	20 Oct 26	11Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11410	PO for Furnitures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		17600	0%	0%	07 May-26	17Aug-26	20 Apr 26A	02Dec-26	$000	$000	$0.00	-106.00
PVC MEMBRANE		12700	0%	0%	16 Jun 26	27Jul-26	16 Jun 26A	11Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11620	MaterialDelivery for PVC Membrane	2000	100%	0%	05 Jul-26	27Jul-26	20 Oct 26	11Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11610	PO for PVC Membrane	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		11900	0%	0%	16 Jun 26	18Jul-26	16 Jun 26A	02Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11860	MaterialDelivery for Artificial TURF	1200	100%	0%	05 Jul-26	18Jul-26	20 Oct 26	02Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11850	PO for Artificial TURF	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		11900	0%	0%	16 Jun 26	18Jul-26	16 Jun 26A	02Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11880	MaterialDelivery for Rubber Granules	1200	100%	0%	05 Jul-26	18Jul-26	20 Oct 26	02Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11870	PO for Rubber Granules	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
PADEL GLASS		12500	0%	0%	16 Jun 26	25Jul-26	16 Jun 26A	09Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11900	MaterialDelivery for PadelGlass	1800	100%	0%	05 Jul-26	25Jul-26	20 Oct 26	09Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11890	PO for Padel Glass	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		12200	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	05Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11920	MaterialDelivery for Wire MeshSteelSets	1500	100%	0%	05 Jul-26	21Jul-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11910	PO for Wire MeshSteelSets	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1.00	0%	0%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11060	PO for AggregateBase Couse	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11070	MaterialDelivery for AggregateBase Couse	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		1500	0%	0%	16 Jun 26	02Jul-26	16 Jun 26A	02Jul-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11080	PO for Bituminous Base & Wearing Course	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11090	MaterialDelivery for theSite	1.00	100%	100%	02 Jul-26	02Jul-26	02 Jul-26A	02Jul-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		14300	0%	0%	07 May-26	13Jul-26	20 Apr 26A	07May-26A	$000	$000	$0.00	39.00
MLTX02.00.4PR-11100	PO for InterlockingBlock Pavers	1.00	100%	100%	07 May-26	07May-26	07 May 25 A	07May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11110	MaterialDelivery for Interlocking Block Pavers	8.00	100%	100%	05 Jul-26	13Jul-26	20 Apr 26A	20Apr-26A	$000	$000	$0.00	7.00
MARKING PAINT		11400	0%	0%	05 Jul-26	17Aug-26	22 Jul-26A	02Dec-26	$000	$000	$0.00	-76.00
MLTX02.00.4PR-11440	MaterialDelivery for Marking Paint	1700	100%	0%	29 Jul-26	17Aug-26	14 Nov 26	02Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11430	PO for Making Paint	1500	100%	100%	05 Jul-26	21Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	14.00
PACKAGE ACUNITS		12200	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	05Nov-26	$000	$000	$0.00	-91.00
MLTX02.00.4PR-11540	MaterialDelivery for Package AC Units	1500	100%	0%	05 Jul-26	21Jul-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11530	PO for Package AC Units	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/GRILS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	10Aug-26A	$000	$000	$0.00	-17.00
MLTX02.00.4PR-11550	PO for AirDiffussersGrills	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11560	MaterialDelivery for AirDifusers/Grills	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 25 A	10Aug-26A	$000	$000	$0.00	12.00
GALVANIZED DUCTS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	12Aug-26A	$000	$000	$0.00	-19.00
MLTX02.00.4PR-11570	PO for GalvanizedDuct	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11580	MaterialDelivery for GalvanizedDuct	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 25 A	12Aug-26A	$000	$000	$0.00	10.00
EXHAUST FANS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	18Aug-26A	$000	$000	$0.00	-24.00
MLTX02.00.4PR-11590	PO for Exhaust Fans	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11600	MaterialDelivery for Exhaust Fans	1500	100%	100%	05 Jul-26	21Jul-26	17 Aug 26 A	18Aug-26A	$000	$000	$0.00	13.00
DISTRBUTION BOARDS		7600	0%	0%	22 Jul-26	13Aug-26	22 Jul-26A	05Nov-26	$000	$000	$0.00	-71.00
MLTX02.00.4PR-11720	MaterialDelivery for Distibuton Boards	1500	100%	0%	28 Jul-26	13Aug-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00

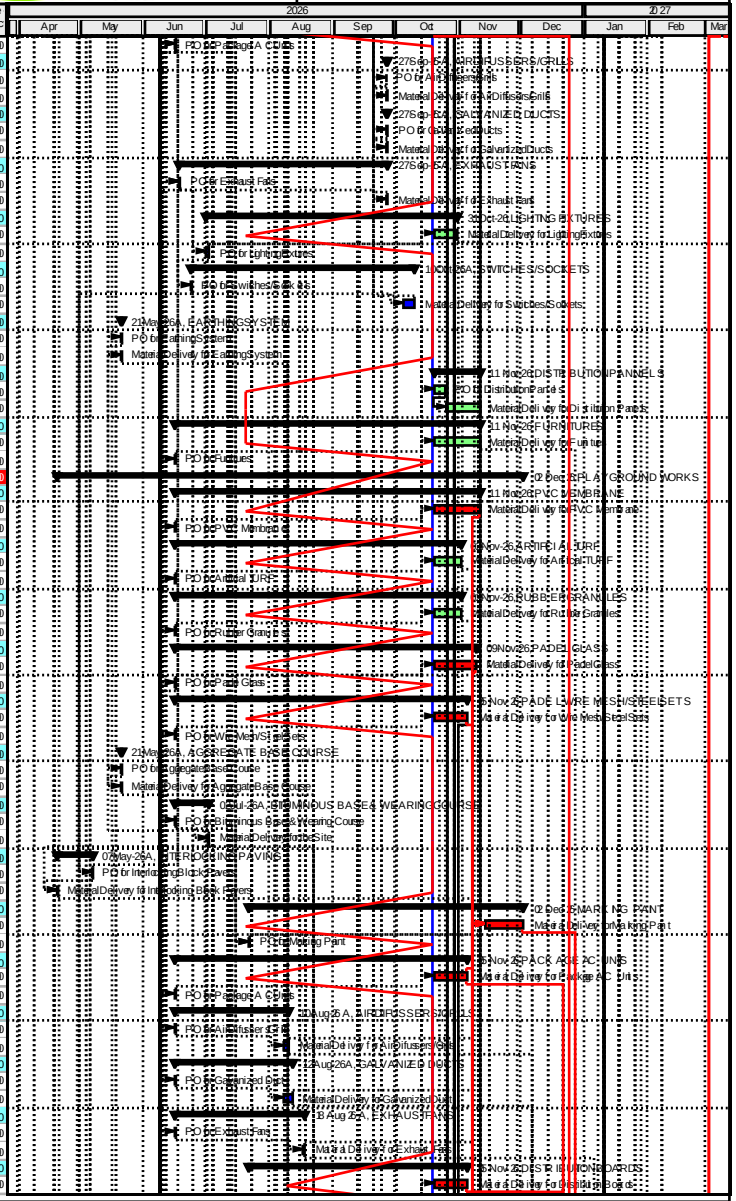

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02.0.4PR-11710	PO for DistributionBoards	5.0	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.0
POWERCABLES		11500	0%	0%	16-Jun-26	15-Jul-26	16-Jun-26A	16-Sep-26A	$000	$000	$0.00	-5400
MLTX02.0.4PR-11730	PO for PowerCables	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
MLTX02.0.4PR-11740	MaterialDelivery for PowerCables	1000	100%	100%	05-Jul-26	15-Jul-26	16-Sep-26A	16-Sep-26A	$000	$000	$0.00	9.0
LIGHTFIXTURES		12300	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26A	07-Nov-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-11760	MaterialDelivery for Light Fixtures	1600	100%	0%	05-Jul-26	22-Jul-26	20-Oct-26	07-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11750	PO for Light Fixtures	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
CCTV MATERIALS		2100	0%	0%	05-Jul-26	28-Jul-26	20-Oct-26	12-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11770	PO for CCTV	6.0	100%	0%	05-Jul-26	11-Jul-26	20-Oct-26	26-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11780	MaterialDelivery for CCTV	1500	100%	0%	12-Jul-26	28-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.0
POWEROUTLETS/SWITCHES		1600	0%	0%	05-Jul-26	28-Jul-26	20-Oct-26	07-Nov-26	$000	$000	$0.00	5.0
MLTX02.0.4PR-11790	PO for PowerOutlets/Switches	6.0	100%	0%	05-Jul-26	11-Jul-26	20-Oct-26	26-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11800	MaterialDelivery for PowerOutlets/Switches	6.0	100%	0%	22-Jul-26	28-Jul-26	01-Nov-26	07-Nov-26	$000	$000	$0.00	0.0
LANDSCAPE WORKS		16500	0%	0%	07-May-26	10-Aug-26	20-Apr-26A	19-Nov-26	$000	$000	$0.00	-101.0
INTERLOCKING PAVING		14700	0%	0%	07-May-26	18-Jul-26	20-Apr-26A	20-Oct-26	$000	$000	$0.00	-9400
MLTX02.0.4PR-11830	PO for InterlockingBlock Pavers	1.0	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.0
MLTX02.0.4PR-11840	MaterialDelivery for Interlocking Block Pavers	1200	100%	100%	05-Jul-26	18-Jul-26	20-Apr-26A	20-Oct-26	$000	$000	$0.00	-141.0
CURBSTONE		12700	0%	0%	07-May-26	18-Jul-26	07-May-26A	14-Sep-26A	$000	$000	$0.00	-5000
MLTX02.0.4PR-11970	PO for Cubstone	1.0	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.0
MLTX02.0.4PR-11980	MaterialDelivery for Curbstone	1200	100%	100%	05-Jul-26	18-Jul-26	14-Sep-26A	14-Sep-26A	$000	$000	$0.00	11.0
PAVEMENTMARKING		9000	0%	0%	05-Jul-26	21-Jul-26	18-Jul-26A	31-Oct-26	$000	$000	$0.00	-7500
MLTX02.0.4PR-11130	MaterialDelivery for Pavement Makings	1000	100%	0%	11-Jul-26	21-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11120	PO for Pavement Makings	5.0	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0
TRAFFC SIGNS		8600	0%	0%	05-Jul-26	21-Jul-26	22-Jul-26A	31-Oct-26	$000	$000	$0.00	-7100
MLTX02.0.4PR-11160	MaterialDelivery for TrafficSigns	1000	100%	0%	11-Jul-26	21-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11140	PO for TrafficSigns	5.0	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26A	27-Jul-26A	$000	$000	$0.00	0.0
IRRGATION PIPES&SPRINKLERS		8500	0%	0%	05-Jul-26	19-Jul-26	18-Jul-26A	15-Aug-26A	$000	$000	$0.00	-1200
MLTX02.0.4PR-11170	PO for Irrigation Pipes/Spimkles	5.0	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0
MLTX02.0.4PR-11180	MaterialDelivery for Irrigation Pipes/Spimkles	8.0	100%	100%	11-Jul-26	19-Jul-26	13-Aug-26A	15-Aug-26A	$000	$000	$0.00	6.0
AGRICULTURE SOL		9200	0%	0%	05-Jul-26	23-Jul-26	18-Jul-26A	02-Nov-26	$000	$000	$0.00	-7500
MLTX02.0.4PR-11940	MaterialDelivery for Agriculture Sol	1200	100%	0%	11-Jul-26	23-Jul-26	20-Oct-26	02-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11930	PO for Agriculture Sol	5.0	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0
TRACK SURFACE		11000	0%	0%	24-Jun-26	15-Jul-26	24-Jun-26A	31-Oct-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-11960	MaterialDelivery for Track Surface	1000	100%	0%	05-Jul-26	15-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11950	PO for Track Suface	1.0	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26A	24-Jun-26A	$000	$000	$0.00	0.0
GRASS/TREES		10700	0%	0%	11-Jul-26	10-Aug-26	18-Jul-26A	19-Nov-26	$000	$000	$0.00	-8000
MLTX02.0.4PR-12000	MaterialDelivery for Grass/Trees	1500	100%	0%	25-Jul-26	10-Aug-26	03-Nov-26	19-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11990	PO for Grass/Trees	5.0	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0
CABLES		7000	0%	0%	11-Jul-26	02-Aug-26	18-Jul-26A	17-Sep-26A	$000	$000	$0.00	-3400
MLTX02.0.4PR-11810	PO for Cables	5.0	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0
MLTX02.0.4PR-11820	MaterialDelivery for Cables	1500	100%	100%	16-Jul-26	02-Aug-26	17-Sep-26A	17-Sep-26A	$000	$000	$0.00	14.0
LONG LEAD ITEM		15200	0%	0%	16-Jun-26	14-Sep-26	16-Jun-26A	10-Dec-26	$000	$000	$0.00	-7400
PLAYGROUND WORKS		15200	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26A	10-Dec-26	$000	$000	$0.00	-9100
STEELTENSION CABLES		14100	0%	0%	16-Jun-26	18-Aug-26	16-Jun-26A	28-Nov-26	$000	$000	$0.00	-8600
MLTX02.0.4PR-12050	Staging time	7.0	100%	0%	11-Aug-26	18-Aug-26	21-Nov-26	28-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11640	MaterialDelivery for Steel Tension Cables	1500	100%	0%	16-Jul-26	02-Aug-26	01-Nov-26	17-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-12010	MaterialFabricationforSteelTension Cables	1000	100%	0%	05-Jul-26	15-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11630	PO for Steel Tension Cables	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
EMERGENCY DOORS		14700	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26A	05-Dec-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-12060	Staging time	5.0	100%	0%	15-Aug-26	19-Aug-26	30-Nov-26	05-Dec-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11660	MaterialDelivery for Emergency Doors	2000	100%	0%	22-Jul-26	13-Aug-26	07-Nov-26	29-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-12020	MaterialFabricationforEmergency Doos	1500	100%	0%	05-Jul-26	21-Jul-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11650	PO for Emegency Doors	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
PRESSURE UNITS		15200	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26A	10-Dec-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-12070	Staging time	5.0	100%	0%	20-Aug-26	25-Aug-26	05-Dec-26	10-Dec-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11680	MaterialDelivery for Pressure Units	2000	100%	0%	22-Jul-26	13-Aug-26	07-Nov-26	29-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-12030	MaterialFabricationforPressue Units	1500	100%	0%	05-Jul-26	21-Jul-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11670	PO for PressureUnits	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
AIRLOCK DOORS		14700	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26A	05-Dec-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-12080	Staging time	5.0	100%	0%	15-Aug-26	19-Aug-26	30-Nov-26	05-Dec-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11700	MaterialDelivery for LockDoors	2000	100%	0%	22-Jul-26	13-Aug-26	07-Nov-26	29-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-12040	MaterialFabricationforLock Doors	1500	100%	0%	05-Jul-26	21-Jul-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.0
MLTX02.0.4PR-11690	PO for Lock Doors	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
LANDSCAPE WORKS		14900	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26A	28-Sep-26A	$000	$000	$0.00	-1100
LIGHTPOLES		14900	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26A	28-Sep-26A	$000	$000	$0.00	-1100
MLTX02.0.4PR-12090	Staging time	5.0	100%	100%	09-Sep-26	14-Sep-26	28-Sep-26A	28-Sep-26A	$000	$000	$0.00	4.0
MLTX02.0.4PR-11020	PO for Lightingpoles	1.0	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.0

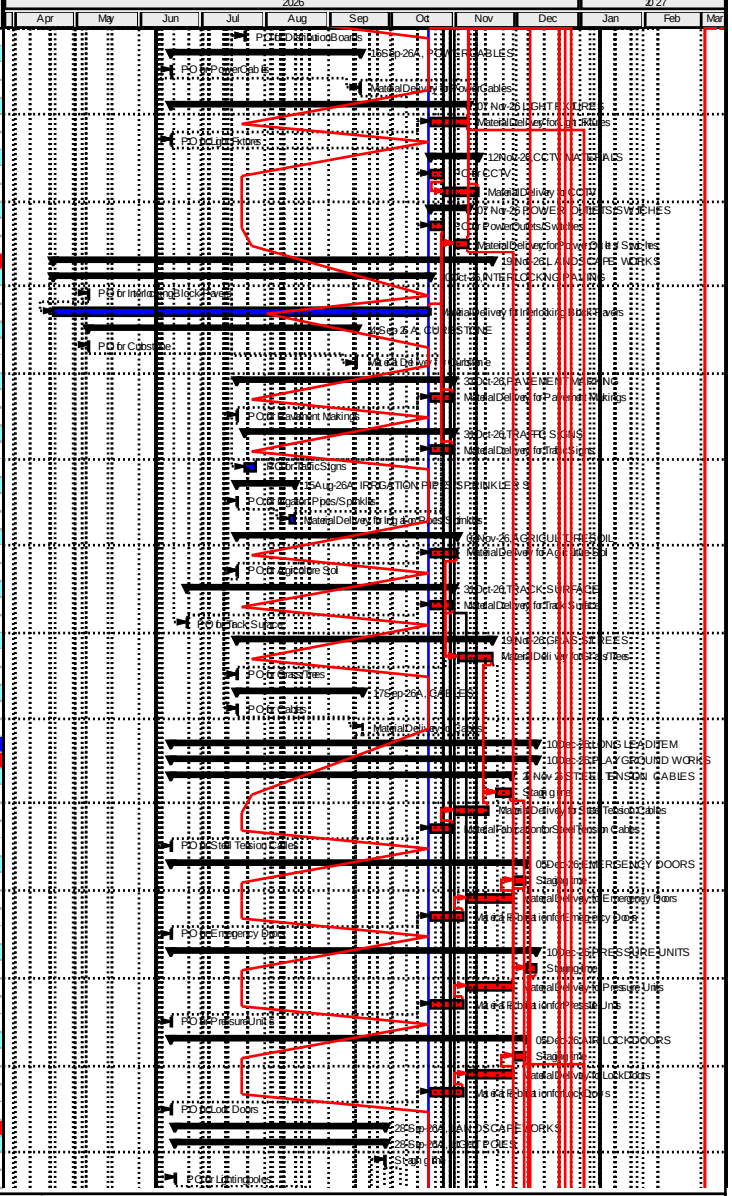


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004-4PR-11030	MaterialFabricationforLighting poles	2500	100%	100%	19-Jul-26	16-Aug-26	27-Aug-26 A	27-Aug-26A	$000	$000	$0.00	24.00
MLTX02-004-4PR-11040	MaterialDelivery for Lightingpoles	2000	100%	100%	17-Aug-26	08-Sep-26	28-Sep-26 A	28-Sep-26A	$000	$000	$0.00	19.00
CONSTRUCTION PHASE		28300	4953%	4181%	25-Apr-26	25-Jan-27	25-Apr-26 A	25-Mar-27	$6209,08752	$5241,23171	$12535,45974	-4700
SITEWORKS		28300	4746%	4099%	25-Apr-26	25-Jan-27	25-Apr-26 A	25-Mar-27	$5415,23620	$4676,44132	$11408,91700	-4700
EARTH WORKS		8080	100%	100%	25-Apr-26	30-Jul-26	25-Apr-26 A	08-Aug-26A	$1195,73661	$1195,73661	$1 195 7 366 1	-700
MLTX-02-004-CN-13 310	Excavation(inall types of soil) including Compaction(PlaygoundArea)	1450	100%	100%	25-Apr-26	11-May-26	25-Apr-26 A	11-May-26A	$2 119 26 00	$211926 00	$2 119 26.00	0.00
MLTX-02-004-CN-13 320	Excavation(inall types of soil) including Compaction(Service/ToiletBuilding)	1514	100%	100%	27-Apr-26	14-May-26	27-Apr-26 A	14-May-26A	$1 077 3 75	$1 077 3.75	$10773.75	0.00
MLTX-02-004-CN-13 330	Excavation(inall types of soil) including Compaction(Landscape Area)	1320	100%	100%	25-Apr-26	10-May-26	25-Apr-26 A	10-May-26A	$1 305 41 73	$130541 73	$1 305 41.73	0.00
MLTX-02-004-CN-13 340	Backfilling onLayers(Rockfill) including Compaction(Playgound Area)	4350	100%	100%	10-May-26	02-Jul-26	10-May-26 A	02-Jul-26A	$2 909 41 90	$290941 90	$2 909 41.90	0.00
MLTX-02-004-CN-13 350	Backfilling onLayers(Rockfill)includingCompaction (Service/Toilet Building)	3900	100%	100%	16-May-26	02-Jul-26	16-May-26 A	02-Jul-26A	$5 118 7 50	$5 118 7.50	$51187.50	0.00
MLTX-02-004-CN-13 360	Backfilling onLayers(Rockfill)includingCompacton (Landscape Area)	4380	100%	100%	10-May-26	02-Jul-26	10-May-26 A	02-Jul-26A	$2 388 75 00	$238875 00	$2 388 75.00	0.00
MLTX-02-004-CN-13 460	Backfilling onLayers(Selected Soil)including Compaction (Service/Toilet Building)	800	100%	100%	05-Jul-26	13-Jul-26	05-Jul-26 A	19-Jul-26A	$2 730 00 00	$2 730 0.00	$27300.00	-460
MLTX-02-004-CN-14 740	Backfilling onLayers(Selected Soil)including Compaction (landscape Area)	1500	100%	100%	14-Jul-26	30-Jul-26	09-Jul-26 A	05-Aug-26A	$1 318 24 88	$131824 88	$1 318 24.88	-770
MLTX-02-004-CN-14 750	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	1000	100%	100%	14-Jul-26	25-Jul-26	18-Jul-26 A	08-Aug-26A	$1 023 68 65	$102368 65	$1 023 68.65	-820
LANDSCAPE WORKS		19000	4171%	3412%	05-Jul-26	25-Jan-27	11-Jul-26 A	25-Mar-27	$4219,49459	$3451,45171	$10115,67340	-4200
PLAYGROUND AREA		15400	7161%	5725%	05-Jul-26	05-Jan-27	22-Aug-26 A	17-Feb-27	$1318,62559	$1054,15245	$1 841 3 807 0	400
FOOTBALLPLAYGROUND		14200	75%	4167%	05-Jul-26	21-Nov-26	22-Aug-26 A	03-Feb-27	$2 568 62 50	$143812 50	$3 451 50.00	-2300
MLTX-02-004-CN-13	InstallSportEquipments -Goal /Nets- Football Playground)	1000	0%	0%	10-Nov-26	21-Nov-26	21-Jan-27	03-Feb-27	$000	$000	$71906.25	0.00
MLTX-02-004-CN-13	Surface Makingand Painting(FootballPlayground)	1000	0%	0%	27-Oct-26	07-Nov-26	03-Jan-27	13-Jan-27	$000	$000	$14381.25	0.00
MLTX-02-004-CN-13	Finishingand SufaceFinish Works (football Playground)	1500	100%	20%	21-Sep-26	08-Oct-26	12-Oct-26 A	05-Nov-26	$1 438 12 50	$2 87.5 2.50	$1 438 12.50	-700
MLTX-02-004-CN-13	Preparation andProofing for Subgade (Football Playground)	1800	100%	100%	05-Jul-26	25-Jul-26	22-Aug-26 A	24-Aug-26A	$5 752 5 00	$5 752 5.00	$57525.00	15.00
MLTX-02-004-CN-13	Backfilling andCompacton ofBaseLayers(FootballPlayground)	1100	100%	100%	26-Jul-26	06-Aug-26	29-Aug-26 A	15-Sep-26A	$5 752 5 00	$5 752 5.00	$57525.00	-500
PADEL PLAYGROUND		12400	80%	55%	26-Jul-26	21-Nov-26	22-Aug-26 A	03-Feb-27	$1 716 00 00	$117975 00	$2 165 00.00	-4100
MLTX-02-004-CN-13	Finishingand SufaceFinish Works (Padel Playgrount)	1500	100%	0%	21-Sep-26	08-Oct-26	29-Nov-26	15-Dec-26	$5 362 5 00	$000	$53625.00	0.00
MLTX-02-004-CN-13	InstallSportEquipments -Goal /Nets- Padel Playground)	1000	0%	0%	10-Nov-26	21-Nov-26	21-Jan-27	03-Feb-27	$000	$000	$32175.00	0.00
MLTX-02-004-CN-13	Surface Makingand Painting(PadelPlayground)	1000	0%	0%	10-Nov-26	21-Nov-26	21-Jan-27	03-Feb-27	$000	$000	$10725.00	0.00
MLTX-02-004-CN-13	Preparation andProofing for Subgade PadelPlayground)	1100	100%	100%	26-Jul-26	06-Aug-26	22-Aug-26 A	24-Aug-26A	$7 507 5 00	$7 507 5.00	$75075.00	8.00
MLTX-02-004-CN-13	Backfilling andCompacton ofBaseLayers(PadelPlayground)	1000	100%	100%	08-Aug-26	18-Aug-26	29-Aug-26 A	15-Sep-26A	$4 290 0 00	$4 29.0 0.00	$42900.00	-600
BASKETBALLPLAYGROUND		12500	60%	20%	08-Aug-26	05-Dec-26	22-Aug-26 A	17-Feb-27	$1 872 00 39	$5 240 0.00	$3 120 00.00	-5200
MLTX-02-004-CN-13	Finishingand SufaceFinish Works (Basketbal Playground)	1500	60%	0%	10-Oct-26	26-Oct-26	16-Dec-26	02-Jan-27	$1 248 00 39	$000	$1 560 00.00	0.00
MLTX-02-004-CN-13	InstallSportEquipments -Goal /Nets- Basketball Playgrount)	1000	0%	0%	22-Nov-26	02-Dec-26	04-Feb-27	15-Feb-27	$000	$000	$78000.00	0.00
MLTX-02-004-CN-13	Surface Makingand Painting(BasketballPlaygound)	1200	0%	0%	22-Nov-26	05-Dec-26	04-Feb-27	17-Feb-27	$000	$000	$15600.00	0.00
MLTX-02-004-CN-13	Preparation andProofing for Subgade (Basketball Playground)	1000	100%	100%	08-Aug-26	18-Aug-26	22-Aug-26 A	24-Aug-26A	$3 120 0 00	$3 120 0.00	$31200.00	7.00
MLTX-02-004-CN-13	Backfilling andCompacton ofBaseLayers(BasketballPlaygound)	1000	100%	100%	19-Aug-26	30-Aug-26	29-Aug-26 A	15-Sep-26A	$3 120 0 00	$3 120 0.00	$31200.00	-600
PADELFENCE		10800	0%	35%	06-Dec-26	05-Jan-27	15-Sep-26 A	18-Nov-26	$000	$2 900 6.25	$82875.00	-2800
MLTX-02-004-CN-13	Tempered Glass Fenc Installaion and Fixation	1000	0%	0%	13-Dec-26	23-Dec-26	20-Oct-26	31-Oct-26	$000	$000	$33150.00	0.00
MLTX-02-004-CN-13	Chain LinkFenceInstallation andFixation	1000	0%	0%	13-Dec-26	23-Dec-26	07-Nov-26	17-Nov-26	$000	$000	$16575.00	0.00
MLTX-02-004-CN-13	Installof Fence Gates	1100	0%	0%	24-Dec-26	05-Jan-27	07-Nov-26	18-Nov-26	$000	$000	$4 143 7 50	0.00
MLTX-02-004-CN-13	ExcavationforFence	500	0%	100%	06-Dec-26	10-Dec-26	15-Sep-26 A	15-Sep-26A	$000	$8287.50	$8 287 5 00	4.00
MLTX-02-004-CN-13	Concrete Roundation for Fence includingPostsFixaton	400	0%	100%	06-Dec-26	09-Dec-26	29-Sep-26 A	29-Sep-26A	$000	$1 657 5.00	$16575.00	3.00
MLTX-02-004-CN-13	Backfilling andReinstatementforConcete Foundation	200	0%	100%	10-Dec-26	12-Dec-26	04-Oct-26 A	06-Oct-26A	$000	$4143.75	$4 143 7 50	-100
CURBSTONE/INTERLOCK		4300	7904%	7904%	29-Sep-26	05-Nov-26	20-Sep-26 A	05-Nov-26	$7 009 58 70	$700958 70	$8 868 58.70	-700
MLTX-02-004-CN-13	Interlock Installaion (Grey Scale)forLandScape(IncludingFinishingWorks)	1500	0%	0%	20-Oct-26	05-Nov-26	20-Oct-26	05-Nov-26	$000	$000	$1 859 0.00	0.00
MLTX-02-004-CN-13	Concrete WorksUnder Curbstone	800	100%	100%	29-Sep-26	07-Oct-26	20-Sep-26 A	22-Sep-26A	$2 581 58 55	$258158 55	$2 581 58.55	6.00
MLTX-02-004-CN-13	CurbstoneInstalation	1000	100%	100%	08-Oct-26	19-Oct-26	20-Sep-26 A	29-Sep-26A	$4 428 00 15	$442800 15	$4 428 00.15	3.00
AIRDOME		17300	5174%	225%	31-Aug-26	04-Jan-27	11-Jul-26 A	06-Mar-27	$2900,87500	$1261,40625	$5 696 2 500 0	-9500
CIVL WORKS		10200	100%	50%	31-Aug-26	05-Oct-26	11-Jul-26 A	12-Dec-26	$2354,62500	$1177,31250	$2 354 6 250 0	-102.00
MLTX-02-004-CN-13	Installof Membane CoveringSystem (AirDome)	1200	100%	0%	21-Sep-26	05-Oct-26	29-Nov-26	12-Dec-26	$5 606 25 00	$000	$5 606 25.00	0.00
MLTX-02-004-CN-13	Thermal Insulaton Works (Air Dome)	600	100%	0%	21-Sep-26	28-Sep-26	06-Dec-26	12-Dec-26	$5 606 25 00	$000	$5 606 25.00	0.00
MLTX-02-004-CN-13	Cable System Installaton (Air Dome)	800	100%	90%	12-Sep-26	20-Sep-26	21-Sep-26 A	28-Nov-26	$5 606 25 00	$5045625	$5 606 25.00	-4800
MLTX-02-004-CN-13	ExcavationforFoundaton & Playgound Area (Air Dome)	500	100%	100%	31-Aug-26	05-Sep-26	11-Jul-26 A	12-Aug-26A	$2 803 12 50	$2803125	$2 803 12.50	-2400
MLTX-02-004-CN-13	Concrete Worksfor Roundations including Anchor Bolts (Air Dome)	500	100%	100%	06-Sep-26	10-Sep-26	29-Jul-26 A	22-Sep-26A	$3 924 37 50	$3924375	$3 924 37.50	-4300
MECHANICALWORKS		3600	4038%	0%	29-Sep-26	09-Nov-26	13-Dec-26	23-Jan-27	$1 528 12 50	$000	$1 121 2 500 0	0.00
MLTX-02-004-CN-13	AirDuctsand GrillsInstallation (Air Dome)	1300	100%	0%	29-Sep-26	13-Oct-26	13-Dec-26	27-Dec-26	$2 803 12 50	$000	$2 803 12.50	0.00
MLTX-02-004-CN-13	AirUnitsInstallaton (Air Dome)	1300	3846%	0%	14-Oct-26	28-Oct-26	28-Dec-26	11-Jan-27	$1 725 00 00	$000	$4 485 0.00	0.00
MLTX-02-004-CN-13	Exhaust Fans andDucts Instalation (Air Dome)	1000	0%	0%	29-Oct-26	09-Nov-26	12-Jan-27	23-Jan-27	$000	$000	$3 924 37.50	0.00
ELECTRCALWORKS		5300	515%	5%	14-Oct-26	04-Jan-27	15-Oct-26 A	25-Feb-27	$9 343 7 50	$3 40 3.75	$1 681 8 750 0	-4300
MLTX-02-004-CN-13	Distibuton Board and ElecticalWorks (Air Dome)	1500	0%	0%	07-Nov-26	23-Nov-26	28-Dec-26	13-Jan-27	$000	$000	$2 803 12.50	0.00
MLTX-02-004-CN-13	External ElectricalConnection Works (Air Dome)	1500	0%	0%	24-Nov-26	10-Dec-26	14-Jan-27	31-Jan-27	$000	$000	$2 803 12.50	0.00
MLTX-02-004-CN-13	Emergency GeneratorInstallaton (AirDome)	1100	0%	0%	12-Dec-26	23-Dec-26	01-Feb-27	13-Feb-27	$000	$000	$5 606 25.00	0.00
MLTX-02-004-CN-13	Contol System Installation(AirDome)	1000	0%	0%	24-Dec-26	04-Jan-27	14-Feb-27	25-Feb-27	$000	$000	$2 803 12.50	0.00
MLTX-02-004-CN-13	Light FktureWorks(AirDome)	1500	3333%	30%	14-Oct-26	31-Oct-26	15-Oct-26 A	27-Dec-26	$9 343 7 50	$3 40 3.75	$2 803 12.50	-4800
FINISHES WORKS		4300	0%	0%	24-Nov-26	26-Dec-26	14-Jan-27	06-Mar-27	$000	$000	$4 485 0.00	-1500
MLTX-02-004-CN-13	Doos Installaton Including Emegency,Entrance doos (Air Dome)	1500	0%	0%	24-Nov-26	10-Dec-26	14-Jan-27	31-Jan-27	$000	$000	$2 242 5.00	0.00
MLTX-02-004-CN-13	Logoand Signs Installation(AirDome)	1300	0%	0%	12-Dec-26	26-Dec-26	18-Feb-27	06-Mar-27	$000	$000	$2 242 5.00	0.00
IRRIGATION NETWORK		2900	0%	7929%	20-Oct-26	21-Nov-26	22-Aug-26 A	30-Nov-26	$000	$212225 00	$2 676 7.00	-5800

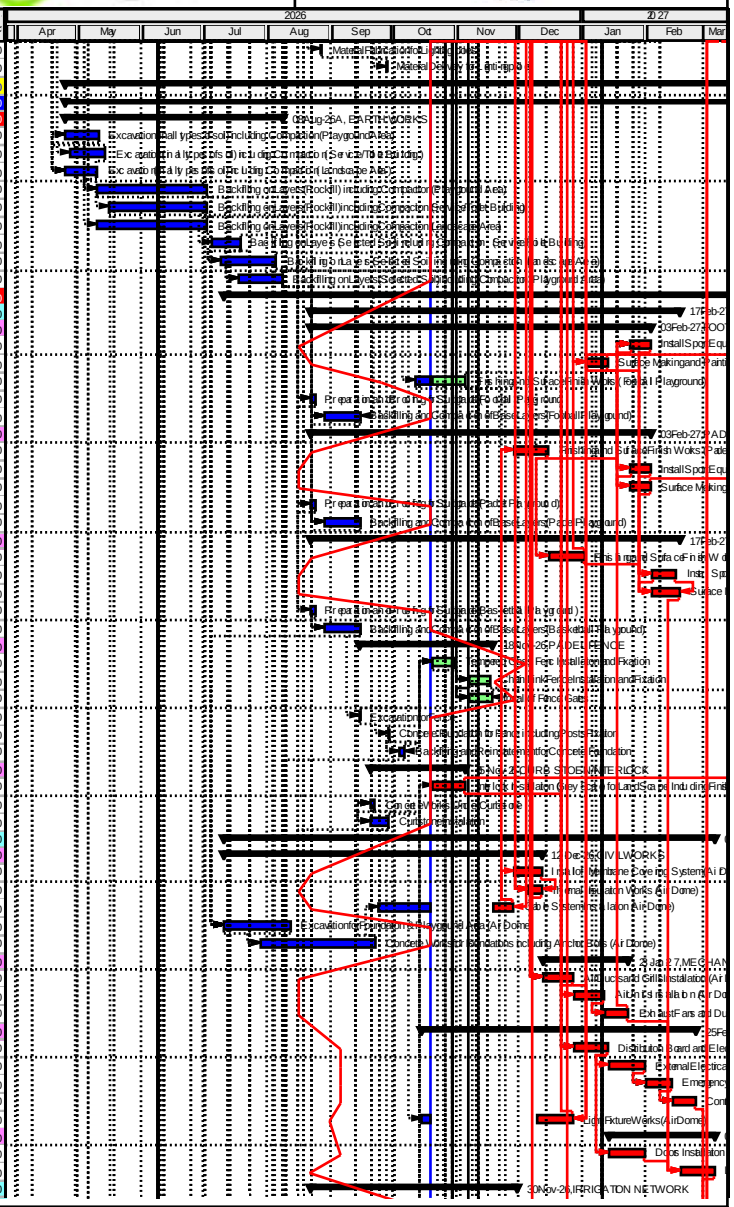

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02 00 4CN-14650	Installing of Bubblers and Sprayers	3.00	0%	0%	18-Nov-26	21-Nov-26	28-Nov-25	30-Nov-26	$000	$000	$46150.00	0.00
MLTX02 00 4CN-14640	Installing of Valves and fittings for Irrigation Network	3.00	0%	80%	09-Nov-26	11-Nov-26	15-Sep-25 A	21-Nov-26	$000	$37380.00	$46475.00	-5400
MLTX02 00 4CN-14620	Installing of HDPE Pipes for Irrigation Network (Main Line)	12.00	0%	100%	20-Oct-26	02-Nov-26	22-Aug-25 A	31-Aug-26A	$000	$80075.00	$80795.00	3.00
MLTX02 00 4CN-14630	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	5.00	0%	100%	03-Nov-26	08-Nov-26	31-Aug-25 A	31-Aug-26A	$000	$94250.00	$94250.00	4.00
NATURAL GROUND		5.00	0%	0%	12-Nov-26	17-Nov-26	22-Nov-25	26-Nov-26	$000	$000	$1170000.00	0.00
MLTX02 00 4CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	5.00	0%	0%	12-Nov-26	17-Nov-26	22-Nov-25	26-Nov-26	$000	$000	$1170000.00	0.00
PLANTING		1800	0%	5.9%	22-Nov-26	12-Dec-26	12-Oct-26A	13-Dec-26	$000	$52552.50	$88863.75	-3600
MLTX02 00 4CN-13480	Placement of Sweet Agricultural Soil (Including Levelling and Grading)	5.00	0%	0%	22-Nov-26	26-Nov-26	01-Dec-25	06-Dec-26	$000	$000	$32194.00	0.00
MLTX02 00 4CN-13500	Placement and Fixation of Trees	6.00	0%	0%	28-Nov-26	03-Dec-26	07-Dec-25	13-Dec-26	$000	$000	$38751.75	0.00
MLTX02 00 4CN-13490	Placement of Lawn Ground Cover (Rolling and Compacton)	7.00	0%	30%	05-Dec-26	12-Dec-26	12-Oct-26A	27-Oct-26	$000	$52552.50	$51751.50	-700
WALKING/BIKE PATHS		8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-25 A	31-Oct-26	$000	$276412.50	$552825.00	-5700
MLTX02 00 4CN-13430	Bike Path Preparation and Installation Works	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-25 A	31-Oct-26	$000	$142045.32	$284090.63	-5700
MLTX02 00 4CN-13440	Walking Path Preparaton and Installation Works	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-25 A	28-Oct-26	$000	$134367.19	$268734.38	-5500
GENERAL/FURNITURE		12400	0%	703%	20-Oct-26	25-Jan-27	19-Sep-25 A	25-Mar-27	$000	$594703.00	$884595.98	-7300
MLTX02 00 4CN-13400	Stamped Concete Works for landScape (Including Finishing Works)	7.00	0%	0%	22-Dec-26	29-Dec-26	09-Mar-27	20-Mar-27	$000	$000	$28080.00	0.00
MLTX02 00 4CN-13470	Traffic Signs Posts and Poles Installation	5.00	0%	0%	13-Jan-27	18-Jan-27	21-Mar-27	25-Mar-27	$000	$000	$9750.00	0.00
MLTX02 00 4CN-13870	Fixation and Installation of Steel Frame for Benches	1000	0%	0%	22-Dec-26	02-Jan-27	01-Nov-25	11-Nov-26	$000	$000	$17276.03	0.00
MLTX02 00 4CN-13880	Fixation and Installation of Benches	9.00	0%	0%	03-Jan-27	12-Jan-27	12-Nov-25	22-Nov-26	$000	$000	$40310.73	0.00
MLTX02 00 4CN-13890	Fixation and Installation of Precast Concrete Seats (Rectangular)	9.00	0%	0%	03-Jan-27	12-Jan-27	12-Nov-25	22-Nov-26	$000	$000	$43680.00	0.00
MLTX02 00 4CN-13900	Fixation and Installation of Precast Concrete Seats (Circular)	9.00	0%	0%	03-Jan-27	12-Jan-27	12-Nov-25	22-Nov-26	$000	$000	$17160.00	0.00
MLTX02 00 4CN-13910	Fixation and Installation of Precast Concrete Trash Bins	1100	0%	0%	13-Jan-27	25-Jan-27	14-Dec-25	26-Dec-26	$000	$000	$14625.00	0.00
MLTX02 00 4CN-14360	Installing of Site Light Poles	12.00	0%	83%	30-Dec-26	12-Jan-27	04-Oct-26A	20-Mar-27	$000	$392205.25	$447253.64	-128.00
MLTX02 00 4CN-14350	Preliminay Woks for Site Light Poles Including Cable and Bases Works	12.00	0%	100%	20-Oct-26	02-Nov-26	19-Sep-25 A	01-Oct-26A	$000	$202497.75	$202497.75	1.00
PARKING		8100	0%	30%	30-Dec-26	12-Jan-27	11-Aug-25 A	28-Oct-26	$000	$29250.00	$97499.02	-5500
MLTX02-004-CN-13370	Interlock Installaton (8 Cm) for Parking Area (Including Finishing Works)	8.00	0%	0%	04-Jan-27	12-Jan-27	20-Oct-26	28-Oct-26	$000	$000	$68249.02	0.00
MLTX02-004-CN-13380	Site Prepaation & Compaction Under Interlock for Parking Area	4.00	0%	100%	30-Dec-26	03-Jan-27	11-Aug-25 A	18-Oct-26A	$000	$29250.00	$29250.00	-5400
TOILETS/ERVICE BULDING		12600	7047%	5013%	14-Jul-26	30-Nov-26	19-Jul-26A	29-Nov-26	$7938514.29	$564790.39	$1126547.71	5.00
STRUCTURE WORKS		3700	100%	100%	14-Jul-26	14-Sep-26	19-Jul-26A	11-Aug-26A	$1579500.00	$157950.00	$1579500.00	33.00
CONCRETE WORKS		3700	100%	100%	15-Jul-26	14-Sep-26	19-Jul-26A	03-Aug-26A	$1137825.00	$113782.50	$1137825.00	39.00
SUB-STRUCTURE		5.00	100%	100%	15-Jul-26	23-Jul-26	19-Jul-26A	25-Jul-26A	$33345.00	$3334.50	$33345.00	2.00
MLTX02-004-CN-13	Plain Concete Under Footing	3.00	100%	100%	15-Jul-26	18-Jul-26	19-Jul-26A	19-Jul-26A	$1170.00	$117.00	$1170.00	2.00
MLTX02-004-CN-13	Reinforced Concrete Works for Slab on Grade including Steel Fixing	5.00	100%	100%	19-Jul-26	23-Jul-26	20-Jul-26A	25-Jul-26A	$32175.00	$3217.50	$32175.00	0.00
SUPER-STRUCTURE		2400	100%	100%	29-Jul-26	14-Sep-26	30-Jul-26A	03-Aug-26A	$80437.50	$8043.75	$80437.50	37.00
MLTX02-004-CN-13	AAC Panels Works for Walls	1800	100%	100%	29-Jul-26	18-Aug-26	30-Jul-26A	01-Aug-26A	$48262.50	$4826.25	$48262.50	16.00
MLTX02-004-CN-13	Parpet Works and Lintels	8.00	100%	100%	06-Sep-26	14-Sep-26	01-Aug-25 A	02-Aug-26A	$16087.50	$1608.75	$16087.50	6.00
MLTX02-004-CN-13	AAC Panels Works for Slabs	1500	100%	100%	19-Aug-26	05-Sep-26	02-Aug-25 A	03-Aug-26A	$16087.50	$1608.75	$16087.50	13.00
UNDER GROUND SEPTIC TANK		1100	100%	100%	15-Jul-26	12-Aug-26	23-Jul-26A	27-Jul-26A	$33930.00	$3393.00	$33930.00	21.00
MLTX02 00 4CN-14510	Plain Concete Under Footing	3.00	100%	100%	15-Jul-26	18-Jul-26	23-Jul-26A	23-Jul-26A	$1170.00	$1170.00	$1170.00	2.00
MLTX02 00 4CN-14520	Reinforced Concrete Works for Tank Slab Including Shutteing and Steel Fixing	8.00	100%	100%	04-Aug-26	12-Aug-26	27-Jul-26A	27-Jul-26A	$8775.00	$877.50	$8775.00	7.00
MLTX02 00 4CN-14530	Reinforced Concrete Works for Tank Foundation Including Shutteing and Steel Fixing	8.00	100%	100%	19-Jul-26	27-Jul-26	23-Jul-26A	23-Jul-26A	$7605.00	$760.50	$7605.00	7.00
MLTX02 00 4CN-14540	Reinforced Concrete Works for Tank Walls Including Steel Fixing	6.00	100%	100%	28-Jul-26	03-Aug-26	27-Jul-26A	27-Jul-26A	$16380.00	$1638.00	$16380.00	5.00
THERMAL& MOISTER PROTECTION		2800	100%	100%	14-Jul-26	27-Aug-26	20-Jul-26A	11-Aug-26A	$102375.00	$10237.50	$102375.00	19.00
ANTTERMITCONTROL		1000	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	30-Jul-26A	$4387.50	$438.75	$4387.50	-900
MLTX02-004-CN-13	Anti Termite Works Under Faundation	1.00	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	20-Jul-26A	$1755.00	$175.50	$1755.00	0.00
MLTX02-004-CN-14	Anti Termite Works Under Slab on Grade and Grade Beams	1.00	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26A	30-Jul-26A	$2632.50	$263.25	$2632.50	0.00
POLYETHYLENESHEET		1000	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	30-Jul-26A	$2193.75	$219.38	$2193.75	-900
MLTX02-004-CN-13	Water Proofing Under Blinding Concrete (Polyhelen Sheet)	1.00	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	20-Jul-26A	$877.50	$87.75	$877.50	0.00
MLTX02-004-CN-13	Water Proofing Under Slab on Grade (Polythelen Sheet)	1.00	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26A	30-Jul-26A	$1316.25	$131.63	$1316.25	0.00
EPOXY		1000	100%	100%	13-Aug-26	27-Aug-26	09-Aug-26 A	11-Aug-26A	$3656.25	$365.63	$3656.25	10.00
MLTX02-004-CN-14	Surface Preparaton for Epoxy Coating	5.00	100%	100%	13-Aug-26	18-Aug-26	09-Aug-26 A	09-Aug-26A	$1096.88	$109.69	$1096.88	4.00
MLTX02-004-CN-14	Epoxy Coating for Walls and Slabof Tank	8.00	100%	100%	19-Aug-26	27-Aug-26	11-Aug-26 A	11-Aug-26A	$2559.38	$255.94	$2559.38	7.00
MASONARY WORK		4.00	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26 A	12-Aug-26A	$12285.00	$1228.50	$12285.00	1.00
MLTX02-004-CN-14	CMU Masonary Works Including all Accessories	4.00	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26 A	12-Aug-26A	$12285.00	$1228.50	$12285.00	1.00
THERMAL& MOISTER PROTECTION		2600	100%	100%	15-Sep-26	08-Oct-26	15-Sep-26 A	11-Oct-26A	$34700.25	$3470.03	$34700.25	-200
MLTX02-004-CN-14	Preparing Surface and Preliminary Works for Toilets Waterpoofing	4.00	100%	100%	15-Sep-26	19-Sep-26	15-Sep-26 A	15-Sep-26A	$2106.00	$210.60	$2106.00	3.00
MLTX02-004-CN-14	Finalize Water Proofing Works for Toilets	5.00	100%	100%	20-Sep-26	26-Sep-26	15-Sep-26 A	28-Sep-26A	$4914.00	$491.40	$4914.00	-600
MLTX02-004-CN-14	Preparing Surface and Preliminary Works for Roofing and Wet Areas Insulaton	5.00	100%	100%	27-Sep-26	01-Oct-26	27-Sep-26 A	27-Sep-26A	$11072.10	$1107.21	$11072.10	4.00
MLTX02-004-CN-14	Finalize Water Proofing Works for Roofing and Wet Areas	6.00	100%	100%	03-Oct-26	08-Oct-26	28-Sep-26 A	11-Oct-26A	$16608.15	$1660.82	$16608.15	-600
MECHANICAL WORK		9300	8854%	3647%	15-Sep-26	08-Nov-26	15-Aug-25 A	21-Nov-26	$8836437.21	$158018.25	$4332655.13	-3800
HVAC SYSTEM		1600	4156%	4755%	12-Oct-26	08-Nov-26	27-Sep-25 A	21-Nov-26	$1588857	$132500	$27885.00	-2400
MLTX02 00 4CN-14160	Install and Finish HVAC and Ventilation Works Including Split Air Units	6.00	0%	0%	02-Nov-26	08-Nov-26	15-Nov-25	21-Nov-26	$000	$000	$14625.00	0.00
MLTX02 00 4CN-14150	Preliminay HVAC and Ventilation Woks	3.00	100%	100%	12-Oct-26	14-Oct-26	27-Sep-25 A	27-Sep-26A	$9360.00	$936.00	$9360.00	2.00
MLTX02 00 4CN-14170	Exhaust, Air Ducts Installaion with all Accessories	7.00	5714%	100%	15-Oct-26	22-Oct-26	27-Sep-25 A	27-Sep-26A	$22285.57	$3900.00	$3900.00	6.00
WATER SUPPLY SYSTEM		6300	100%	1889%	17-Sep-26	18-Oct-26	15-Aug-25 A	31-Oct-26	$2521275.0	$81767.50	$2521275.0	-4000
MLTX02 00 4CN-14200	Installing of Booster Pump Units Including fittings and accessories	5.00	100%	0%	08-Oct-26	13-Oct-26	25-Oct-26	31-Oct-26	$91000.00	$000	$91000.00	0.00
MLTX02 00 4CN-14210	Installing of GRP Tanks	5.00	100%	0%	03-Oct-26	07-Oct-26	20-Oct-26	25-Oct-26	$1040000.00	$000	$1040000.00	0.00
MLTX02 00 4CN-14600	Installing of Valves and Rttings	4.00	100%	0%	21-Sep-26	26-Sep-26	20-Oct-26	24-Oct-26	$9750.00	$000	$9750.00	0.00

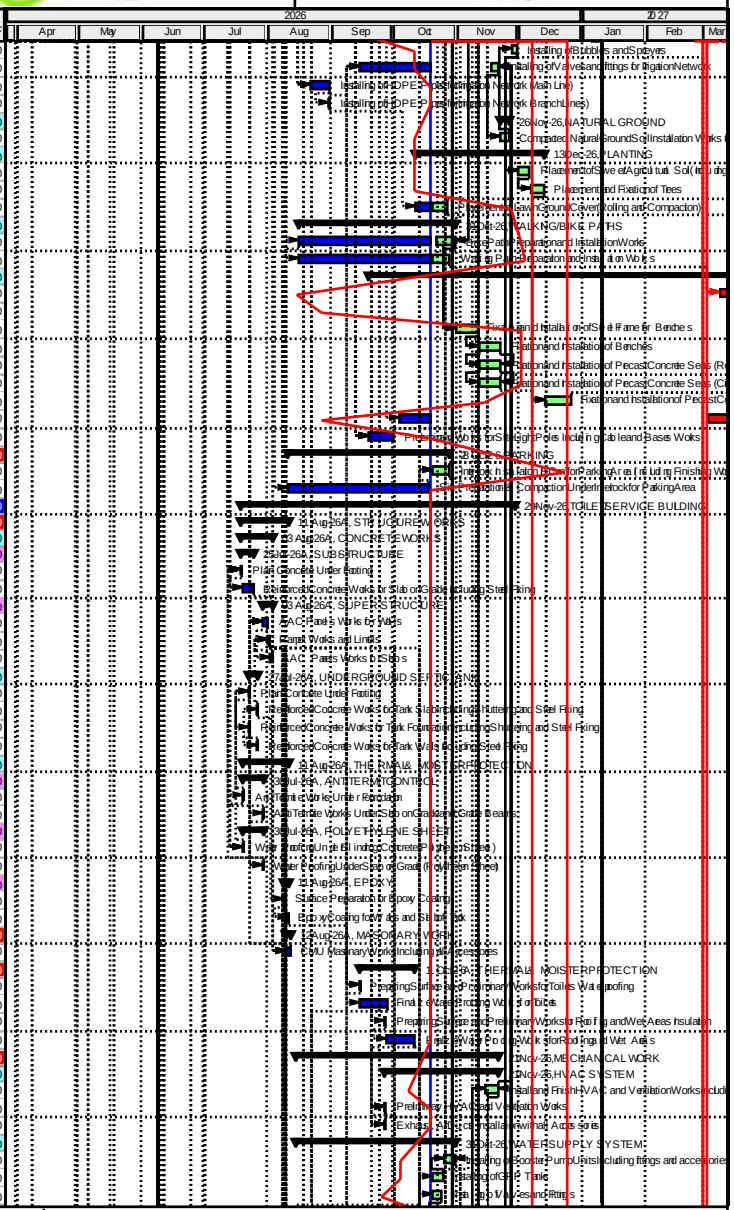


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004CN-14180	Installing of PPR Pipes and Fittings for Water Network	3.00	100%	100%	17-Sep-26	20-Sep-26	15-Aug-26 A	15-Aug-26 A	$6,922.50	$6,922.50	$6,922.50	2.00
MLTX-02-004CN-14190	Installing of HDPE Pipes and Valves for Water Supply Network	5.00	100%	100%	27-Sep-26	01-Oct-26	05-Oct-26 A	10-Oct-26 A	$3,900.00	$3,900.00	$39,000.00	0.00
MLTX-02-004CN-14690	Installing of Water Heater	4.00	100%	100%	14-Oct-26	18-Oct-26	08-Oct-26 A	11-Oct-26 A	$1,755.00	$1,755.00	$1,755.00	1.00
SEWERDRAIN AGES YSTEM		7500	7921%	6428%	15-Sep-26	29-Oct-26	15-Aug-26 A	11-Nov-26	$1,196,276.63	$97,080.75	$1,510,212.63	-3800
MLTX-02-004CN-14230	Installing of Plumping Fixtures and Accessories	4.00	100%	0%	29-Sep-26	03-Oct-26	25-Oct-26	28-Oct-26	$1,035,938	$000	$10359.38	0.00
MLTX-02-004CN-14680	Installing Inspection Chamber for Sewage Network	5.00	100%	0%	17-Sep-26	22-Sep-26	20-Oct-26	25-Oct-26	$1,218,750	$000	$12187.50	0.00
MLTX-02-004CN-14700	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	3.00	0%	0%	27-Oct-26	29-Oct-26	09-Nov-26	11-Nov-26	$000	$000	$31395.00	0.00
MLTX-02-004CN-14220	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	15-Sep-26	16-Sep-26	15-Aug-26 A	15-Aug-26 A	$1,176,825	$1,176,825	$11768.25	1.00
MLTX-02-004CN-14610	Installing UPVC Pipes for External Connection for Sewage Network	4.00	100%	100%	24-Sep-26	28-Sep-26	05-Oct-26 A	11-Oct-26 A	$8,521,250	$8,521,250	$85312.50	-200
FIREPROTECTION		4.00	0%	0%	04-Nov-26	08-Nov-26	17-Nov-26	21-Nov-26	$000	$000	$1,950.00	0.00
MLTX-02-004CN-14240	Installing of Fire Fighting Extinguisher and accessories (PIE-1, PIE-2)	4.00	0%	0%	04-Nov-26	08-Nov-26	17-Nov-26	21-Nov-26	$000	$000	$1,950.00	0.00
ELECTRICAL WORKS		9000	3366%	5087%	15-Sep-26	16-Nov-26	16-Aug-26 A	29-Nov-26	$7,283,250	$110078.98	$2,164,013.38	-3700
ROUGH-IN WORKS		2400	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$7,283,250	$7,283,250	$72832.50	-300
MLTX-02-004CN-14280	Preliminary Woks for Cable Works	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$1,070,004	$1,070,004	$10700.04	-300
MLTX-02-004CN-14290	Preliminary Woks for Sockets and Power Points	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$9,230.91	$9230.91	$9,230.91	-300
MLTX-02-004CN-14310	Preliminary Woks for Lightning Works	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$9,750.00	$9750.00	$9,750.00	-300
MLTX-02-004CN-14330	Preliminary Woks for Data & Telecommunication System	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$1,228,500	$1,228,500	$12285.00	-300
MLTX-02-004CN-14370	Preliminary Woks for Security and Access Control System	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$1,526,655	$1,526,655	$15266.55	-300
MLTX-02-004CN-14660	Preliminary Woks for Earthing Works	9.00	100%	100%	15-Sep-26	26-Sep-26	16-Aug-26 A	29-Aug-26 A	$1,560,000	$1,560,000	$15600.00	-300
FIXTURE WORKS		1500	0%	2594%	02-Nov-26	16-Nov-26	05-Oct-26 A	29-Nov-26	$000	$2,721,649	$1,485,618.88	-3500
MLTX-02-004CN-14250	Installing of Fireautomation and Fire Alarm System	7.00	0%	0%	09-Nov-26	16-Nov-26	22-Nov-26	29-Nov-26	$000	$000	$34320.00	0.00
MLTX-02-004CN-14320	Installing and Finalize Works of Lighting Works including Light Fixtures	4.00	0%	0%	04-Nov-26	08-Nov-26	17-Nov-26	21-Nov-26	$000	$000	$16050.00	0.00
MLTX-02-004CN-14340	Installing Data and Telecommunication System with all Accessories	4.00	0%	0%	04-Nov-26	08-Nov-26	17-Nov-26	21-Nov-26	$000	$000	$18427.50	0.00
MLTX-02-004CN-14380	Installing and Finalize Works of Security and Access Control System	6.00	0%	0%	02-Nov-26	08-Nov-26	15-Nov-26	21-Nov-26	$000	$000	$22899.83	0.00
MLTX-02-004CN-14400	Installing and Finalize Works of Lightning Protection System	6.00	0%	0%	02-Nov-26	08-Nov-26	15-Nov-26	21-Nov-26	$000	$000	$14625.00	0.00
MLTX-02-004CN-14300	Installing and Finalize Works of Sockets and Power Points	4.00	0%	100%	04-Nov-26	08-Nov-26	05-Oct-26 A	10-Oct-26 A	$000	$1,388,649	$13846.49	-100
MLTX-02-004CN-14390	Installing and Finalize Works of Earthing Works	6.00	0%	100%	02-Nov-26	08-Nov-26	05-Oct-26 A	11-Oct-26 A	$000	$2,340,000	$23400.00	0.00
DOORS/WINDOWS		4800	40%	1429%	15-Sep-26	30-Nov-26	07-Oct-26 A	18-Nov-26	$2,730,000	$9750.00	$68250.00	28 00
MLTX-02-004CN-14470	Finalize Glazzed Curtain Wall Works	4.00	0%	0%	02-Nov-26	05-Nov-26	15-Nov-26	18-Nov-26	$000	$000	$35100.00	0.00
MLTX-02-004CN-14550	Preliminay Woks For Windows/Curtain Wall	2.00	100%	0%	15-Sep-26	16-Sep-26	20-Oct-26	21-Oct-26	$2,340,000	$000	$23400.00	0.00
MLTX-02-004CN-14090	Preliminay Woks For Doors	3.00	100%	100%	15-Sep-26	17-Sep-26	08-Oct-26 A	10-Oct-26 A	$3,900.00	$3,900.00	$3,900.00	1.00
MLTX-02-004CN-14100	Finalize Metal Doors for Toilets Building	1200	0%	100%	17-Nov-26	30-Nov-26	07-Oct-26 A	12-Oct-26 A	$000	$5850.00	$5,850.00	7.00
METALWORKS		900	525%	100%	12-Oct-26	29-Oct-26	16-Sep-26 A	27-Sep-26 A	$5,118,750	$9750.00	$9,750.00	7.00
MLTX-02-004CN-14040	Installation of Galvanized Steel Ladder	8.00	875%	100%	12-Oct-26	20-Oct-26	27-Sep-26 A	27-Sep-26 A	$5,118,750	$5850.00	$5,850.00	7.00
MLTX-02-004CN-14420	Installation of Galvanized Steel Roof Scupper	8.00	0%	100%	21-Oct-26	29-Oct-26	16-Sep-26 A	16-Sep-26 A	$000	$3900.00	$3,900.00	7.00
FINISHING WORKS		5900	6306%	5336%	27-Sep-26	17-Nov-26	29-Aug-26 A	16-Nov-26	$8,599,622	$7,225,749	$1,354,141.50	-2300
FLOOR FINISHES		4100	9318%	8295%	30-Sep-26	17-Nov-26	01-Oct-26 A	24-Oct-26	$1,599,000	$1,425,000	$17160.00	22 00
MLTX-02-004CN-14480	Granite Tiles Floor Finish Works	4.00	100%	0%	05-Oct-26	08-Oct-26	20-Oct-26	24-Oct-26	$2,925.00	$000	$2,925.00	0.00
MLTX-02-004CN-14110	Ceramic Tiles Floor finish Works	4.00	100%	100%	30-Sep-26	04-Oct-26	01-Oct-26 A	04-Oct-26 A	$1,189,500	$1,189,500	$11895.00	2.00
MLTX-02-004CN-14490	Epoxy Coaton Concrete floor	1000	0%	100%	07-Nov-26	17-Nov-26	07-Oct-26 A	10-Oct-26 A	$000	$1170.00	$1,170.00	7.00
MLTX-02-004CN-14500	Ceramic Skirting Tiles Finish Works	2.00	100%	100%	10-Oct-26	11-Oct-26	05-Oct-26 A	07-Oct-26 A	$1,170.00	$1170.00	$1,170.00	-100
WALL FINISHES		5100	5639%	4863%	27-Sep-26	03-Nov-26	29-Aug-26 A	16-Nov-26	$5,924,750	$5,109,650	$1,050,252.50	-3500
MLTX-02-004CN-14460	Phendic Patitons for Toilets	5.00	0%	0%	21-Oct-26	26-Oct-26	08-Nov-26	08-Nov-26	$000	$000	$31200.00	0.00
MLTX-02-004CN-14570	Glass Partitions including all accessories and doors	5.00	0%	0%	27-Oct-26	01-Nov-26	09-Nov-26	14-Nov-26	$000	$000	$12285.00	0.00
MLTX-02-004CN-14580	Granite Capping for Papet	2.00	100%	0%	10-Oct-26	11-Oct-26	20-Oct-26	21-Oct-26	$8,151.00	$000	$8,151.00	0.00
MLTX-02-004CN-14670	Painting Finish Works for Intenal Walls	2.00	0%	0%	02-Nov-26	03-Nov-26	15-Nov-26	16-Nov-26	$000	$000	$2,340.00	0.00
MLTX-02-004CN-14120	Preliminay Woks for Wall Finish Works including Plastering (Intenal)	3.00	100%	100%	27-Sep-26	29-Sep-26	29-Aug-26 A	09-Sep-26 A	$1,836,900	$1,836,900	$18369.00	-800
MLTX-02-004CN-14430	Preliminay Woks for Wall Finish Works (External)	8.00	100%	100%	27-Sep-26	05-Oct-26	09-Sep-26 A	10-Sep-26 A	$6,552.00	$6552.00	$6,552.00	6.00
MLTX-02-004CN-14440	Painting Finish Works for External Walls	3.00	100%	100%	06-Oct-26	08-Oct-26	11-Oct-26 A	13-Oct-26 A	$1,047,800	$1,047,800	$10478.00	0.00
MLTX-02-004CN-14450	Ceramic Finish Works for Walls	6.00	100%	100%	05-Oct-26	11-Oct-26	28-Sep-26 A	29-Sep-26 A	$1,569,750	$1,569,750	$15697.50	5.00
CEILING FINISHES		1700	7707%	5254%	30-Sep-26	24-Oct-26	07-Oct-26 A	03-Nov-26	$1,015,872	$692640	$131,182.00	-300
MLTX-02-004CN-14710	Painting Finish Works for Ceiling	3.00	0%	0%	21-Oct-26	24-Oct-26	01-Nov-26	03-Nov-26	$000	$000	$1,638.00	0.00
MLTX-02-004CN-14730	Preliminay Woks for Ceiling Painting Woks	1000	100%	0%	30-Sep-26	11-Oct-26	20-Oct-26	31-Oct-26	$4,617.60	$000	$4,617.60	0.00
MLTX-02-004CN-14720	Gypsum Board Suspended Ceiling finish Works For Ceiling	5.00	80%	100%	15-Oct-26	20-Oct-26	07-Oct-26 A	12-Oct-26 A	$5,541.12	$6926.40	$6,926.40	0.00
SPECIALTIES WORK		2600	25%	0%	04-Oct-26	15-Nov-26	29-Oct-26	28-Nov-26	$1,462,500	$000	$58506.46	11 00
MLTX-02-004CN-14130	Sanitary Fixtures and Accessories Works	4.00	100%	0%	04-Oct-26	07-Oct-26	29-Oct-26	02-Nov-26	$1,462,500	$000	$14625.00	0.00
MLTX-02-004CN-14140	Installation of MODON logo on the entrance	1000	0%	0%	04-Nov-26	15-Nov-26	17-Nov-26	28-Nov-26	$000	$000	$19506.46	0.00
MLTX-02-004CN-14590	Installation of Phenolic Locker	2.00	0%	0%	27-Oct-26	28-Oct-26	09-Nov-26	10-Nov-26	$000	$000	$24375.00	0.00
TESTING & COMMISSIONING		9500	0%	0%	01-Dec-26	18-Jan-27	01-Dec-26	25-Mar-27	$000	$000	$0.00	-5300
MLTX-02-004TC-11920	Testing and Commissioning for MEP Works for Playground Area	8.00	0%	0%	05-Jan-27	13-Jan-27	07-Mar-27	18-Mar-27	$000	$000	$0.00	0.00
MLTX-02-004TC-11930	Testing and Commissioning for MEP Works for Toilet Service Building	1500	0%	0%	01-Dec-26	17-Dec-26	01-Dec-26	17-Dec-26	$000	$000	$0.00	0.00
MLTX-02-004TC-11940	Testing and Commissioning for MEP Works for Landscape Works	4.00	0%	0%	14-Jan-27	18-Jan-27	22-Mar-27	25-Mar-27	$000	$000	$0.00	0.00
ASIR		31900	2896%	3828%	26-Mar-26	24-Jan-27	26-Mar-26 A	11-Apr-27	$3,063,276.66	$4049,399.23	$10578,073.08	-6200
MOBILIZATION		6300	0%	0%	26-Mar-26	10-Jun-26	26-Mar-26 A	10-Jun-26 A	$000	$000	$0.00	0.00
TOPOGRAPHIC SURVEY		400	0%	0%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	$000	$000	$0.00	0.00
MLTX-02-004MB-1320	Site Survey Works	4.00	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26 A	$000	$000	$0.00	0.00

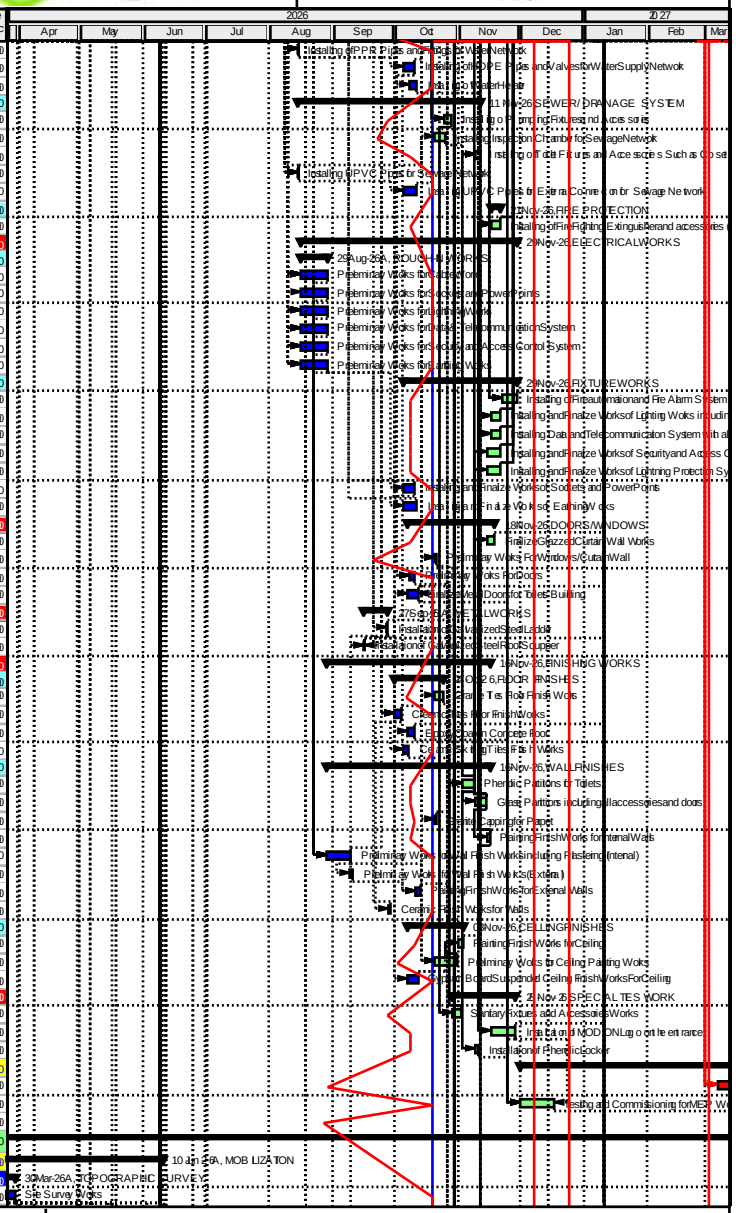

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SITEFACILITIES & OFFICES		4970	0%	0%	26 Mar 26	23May-26	26 Mar 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1440	Manpower Mobalizaton	3170	100%	100%	16 Apr 26	23May-26	16 Apr 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1430	Equipment Mobalization	2440	100%	100%	14 Apr 26	12May-26	14 Apr 26 A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1340	Site Layout Plan	4.00	100%	100%	26 Mar 26	30Mar-26	26 Mar 26 A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1350	Clear & Grub for Offices & Access Road	3.00	100%	100%	31 Mar 26	02Apr-26	31 Mar 26 A	02Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1360	Construct Site Access Roads	4.00	100%	100%	31 Mar 26	04Apr-26	31 Mar 26 A	04Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1370	Construct Temporary Fence	3175	100%	100%	15 Apr 26	21May-26	15 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1380	Construct Site Offices & Storage	1880	100%	100%	20 Apr 26	11May-26	20 Apr 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1390	Install Project Signs	3.00	100%	100%	21 Apr 26	23Apr-26	21 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1400	Install Site Facilities	2355	100%	100%	12 Apr 26	09May-26	12 Apr 26 A	09May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1410	Electrical Works & Connections	2695	100%	100%	12 Apr 26	12May-26	12 Apr 26 A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1420	Construct Parking Sheds	2675	100%	100%	12 Apr 26	12May-26	12 Apr 26 A	12May-26A	$000	$000	$0.00	0.00
PRELIMNARY SUBMITTAIS		5900	0%	0%	31 Mar 26	10Jun-26	31 Mar 26 A	10Jun-26A	$000	$000	$0.00	0.00
PREPARATIONS& SUBMITTAL BY CONTRACTORS		2700	0%	0%	31 Mar 26	30Apr-26	31 Mar 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1540	Preparation and Submittal of Detailed Work Order Programme (Baseline)	2500	100%	100%	31 Mar 26	28Apr-26	31 Mar 26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1550	Preparation and Submittal of Project Execution Plan	2700	100%	100%	31 Mar 26	30Apr-26	31 Mar 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1560	Submission of Contactor Project Quality Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1570	Submission of Construction Safety & Environmental Management Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1580	Preparation and Submittal of Organization Chat	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar 26 A	08Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1590	Preparation and Submittal of Communication Plan	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar 26 A	08Apr-26A	$000	$000	$0.00	0.00
APPROVALS BY EMPLOYERS		5100	0%	0%	09 Apr 26	10Jun-26	09 Apr 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1630	Approval of Detailed Work Order Programme (Baseline)	1.00	100%	100%	29 Apr 26	29Apr-26	29 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1690	Approval of Project Execution Plan	1.00	100%	100%	13May-26	13May-26	13 May 26 A	13May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1700	Approval of Contactor Project Quality Plan	1900	100%	100%	09 Apr 26	30Apr-26	09 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1710	Approval of Constuction Safety & Environmental Management Plan	1.00	100%	100%	10 Jun 26	10Jun-26	10 Jun 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1720	Approval of Organization Chat	1800	100%	100%	09 Apr 26	29Apr-26	09 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1730	Approval of Communication Plan	1000	100%	100%	09 Apr 26	20Apr-26	09 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
ENGINEERING		20600	0%	0%	31 Mar 26	02Sep-26	31 Mar 26 A	30Nov-26	$000	$000	$0.00	-7500
SHOP DRAWINGS		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-3400
SHOP DRAWINGS SUBMISSION		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-3300
SHOP DRAWINGSUBMITTALS FOR EARTHINGWORKS		5800	0%	0%	31 Mar 26	09Jun-26	31 Mar 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1790	ShopDWG Submittal for Layout Plan	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1800	ShopDWG Submittal for Setting Out	4420	100%	100%	31 Mar 26	21May-26	31 Mar 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1810	ShopDWG Submittal for Grading Layout Plan	2500	100%	100%	31 Mar 26	28Apr-26	31 Mar 26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1820	ShopDWG Submittal for Curb Setting Out Points	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1830	ShopDWG Submittal for Signing & Making Layout Plan	1.00	100%	100%	09 Jun 26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1840	ShopDWG Submittal for Standards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGSUBMITTALS FOR SERVCE/TOILETWORKS		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-3300
ARCHITECTURE WORKS		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-187	ShopDWG Submittal for Floor Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-188	ShopDWG Submittal for Elevations	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-189	ShopDWG Submittal for Sections	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-190	ShopDWG Submittal for Ceiling Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-191	ShopDWG Submittal for Finishes Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-192	ShopDWG Submittal for Toilet Details	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-193	ShopDWG Submittal for Doors\Windows Schedule	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2000	0%	0%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-195	ShopDWG Submittal for Foundaton Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-196	ShopDWG Submittal for Ground Floor Framing Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-197	ShopDWG Submittal for Sections/Details	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		3800	0%	0%	08 Apr 26	21May-26	08 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-199	ShopDWG Submittal for HVAC Plan	7.00	100%	100%	08 Apr 26	15Apr-26	08 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-200	ShopDWG Submittal for Exhaust Air Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-201	ShopDWG Submittal for HVAC Equipment Schedule	7.00	100%	100%	08 Apr 26	15Apr-26	08 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-206	ShopDWG Submittal for Fire Fighting Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-207	ShopDWG Submittal for Water Supply Layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-208	ShopDWG Submittal for Water Supply Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-202	ShopDWG Submittal for Drainage Layout	3800	100%	100%	08 Apr 26	21May-26	08 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-203	ShopDWG Submittal for Drainage Details	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-204	ShopDWG Submittal for Dut Routing Layout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-205	ShopDWG Submittal for Diffusers Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13400	0%	0%	08 Apr 26	18Jul-26	08 Apr 26 A	25Aug-26A	$000	$000	$0.00	-3300
MLTX02-004EN-210	ShopDWG Submittal for Lighting layout	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-211	ShopDWG Submittal for Power layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-212	ShopDWG Submittal for Power Single Line Diagram	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-213	ShopDWG Submittal for Panel Board Schedules	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00

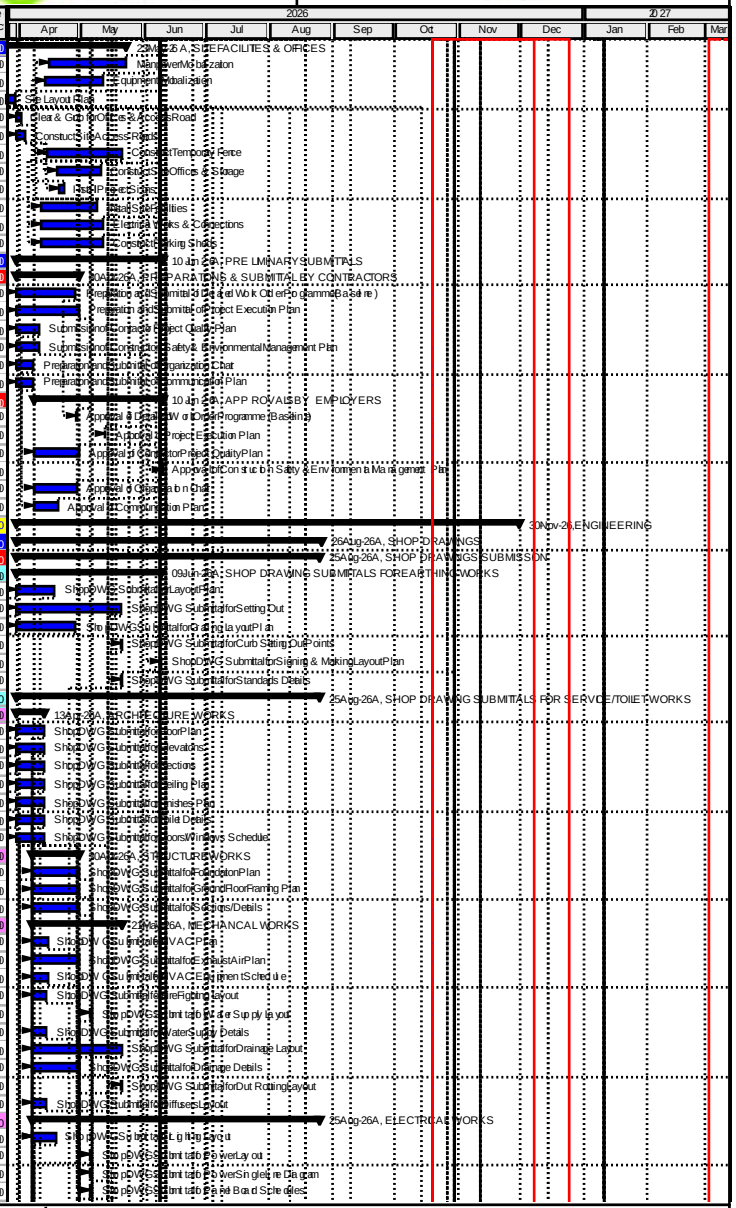

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation


MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

PROFAST

egis

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004EN-214	ShopDWG SubmittalforLighting Installation Details	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-215	ShopDWG SubmittalforPower Installation Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-216	ShopDWG SubmittalforCableTrayInstalation Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-217	ShopDWG SubmittalforManhole& Ductbank Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-218	ShopDWG SubmittalforGrounding Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-221	ShopDWG SubmittalforLightningProtecton Details	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-215	ShopDWG SubmittalforFireAlarmInstallation Details	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-224	ShopDWG SubmittalforCCTV Details	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-227	ShopDWG SubmittalforGrounding Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-222	ShopDWG SubmittalforLightningProtecton System Layout	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-220	ShopDWG SubmittalforFireAlarmLayout	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-222	ShopDWG SubmittalforFireAlarmRiserDiagram	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-225	ShopDWG SubmittalforCCTV Layout	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-226	ShopDWG SubmittalforCCTV Riser Diagram	6.00	100%	100%	12 Jul-25	18Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-226	ShopDWG SubmittalforTelephone & Data Layout	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-225	ShopDWG SubmittalforTelephone & Data Riser Diagram	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWINGSSUBMITTALS FOR PLAYGROUND WORKS		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26A	25Aug-26A	$000	$000	$0.00	-3300
ARCHITECTURE WORKS		3900	0%	0%	31 Mar 26	14May-26	31 Mar 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-232	ShopDWG SubmittalforPlaygound Plan/Layout	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-233	ShopDWG SubmittalforFurniture& Marking	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-234	ShopDWG SubmittalforSections	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-238	ShopDWG SubmittalforInterlockPatten Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-236	ShopDWG SubmittalforDoors&Windows Schedule	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-237	ShopDWG SubmittalforDome Internal Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-238	ShopDWG SubmittalforAir Dome System	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-240	ShopDWG SubmittalforFoundationof AirDome	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-242	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-244	ShopDWG SubmittalforAir Dome Structural Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-245	ShopDWG SubmittalforMembrane PanelLayout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-246	ShopDWG SubmittalforCableTension Layout	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-247	ShopDWG SubmittalforAirlock DoorDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-248	ShopDWG SubmittalforEmergency ExitDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
SPORTS EQUPMENT		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-250	ShopDWG SubmittalforFootball Turf Installation	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-251	ShopDWG SubmittalforBasketballCourtMarking	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-252	ShopDWG SubmittalforPadelCourtStructure	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		2000	0%	0%	08 Apr 26	30Apr-26	08 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-254	ShopDWG SubmittalforHVAC Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-255	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		9600	0%	0%	23 May-26	18Jul-26	23 May 26 A	25Aug-26A	$000	$000	$0.00	-3300
MLTX02-004EN-257	ShopDWG SubmittalforLighting Layout	1.00	100%	100%	25 May-26	25May-26	25 May 26 A	25May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-258	ShopDWG SubmittalforPower Layout	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-262	ShopDWG SubmittalforPower SingleLineDiagram	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-263	ShopDWG SubmittalforPanelBoardSchedules	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-259	ShopDWG SubmittalforPower Instalation Details	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-266	ShopDWG SubmittalforFireAlarmInstallation Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-265	ShopDWG SubmittalforCCTV Details	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-261	ShopDWG SubmittalforFireAlarmLayout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-264	ShopDWG SubmittalforFireAlarmRiserDiagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-266	ShopDWG SubmittalforCCTV Layout	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-267	ShopDWG SubmittalforCCTV Riser Diagram	6.00	100%	100%	12 Jul-25	18Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
SHOP DRAWINGSSUBMITTALS FOR LANDSCAPE WORKS		6500	0%	0%	31 Mar 26	17Jun-26	31 Mar 26A	17Jun-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		3900	0%	0%	31 Mar 26	14May-26	31 Mar 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-270	ShopDWG SubmittalforLandscape Layout	6.00	100%	100%	31 Mar 26	06Apr-26	31 Mar 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-271	ShopDWG SubmittalforHardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-272	ShopDWG SubmittalforPlanting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-273	ShopDWG SubmittalforLandscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		1.00	0%	0%	17 Jun 26	17Jun-26	17 Jun 26A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-277	ShopDWG SubmittalforIrrigation Details	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-281	ShopDWG SubmittalforIrrigation Layout	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26A	17Jun-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		1.00	0%	0%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-286	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-287	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-284	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00

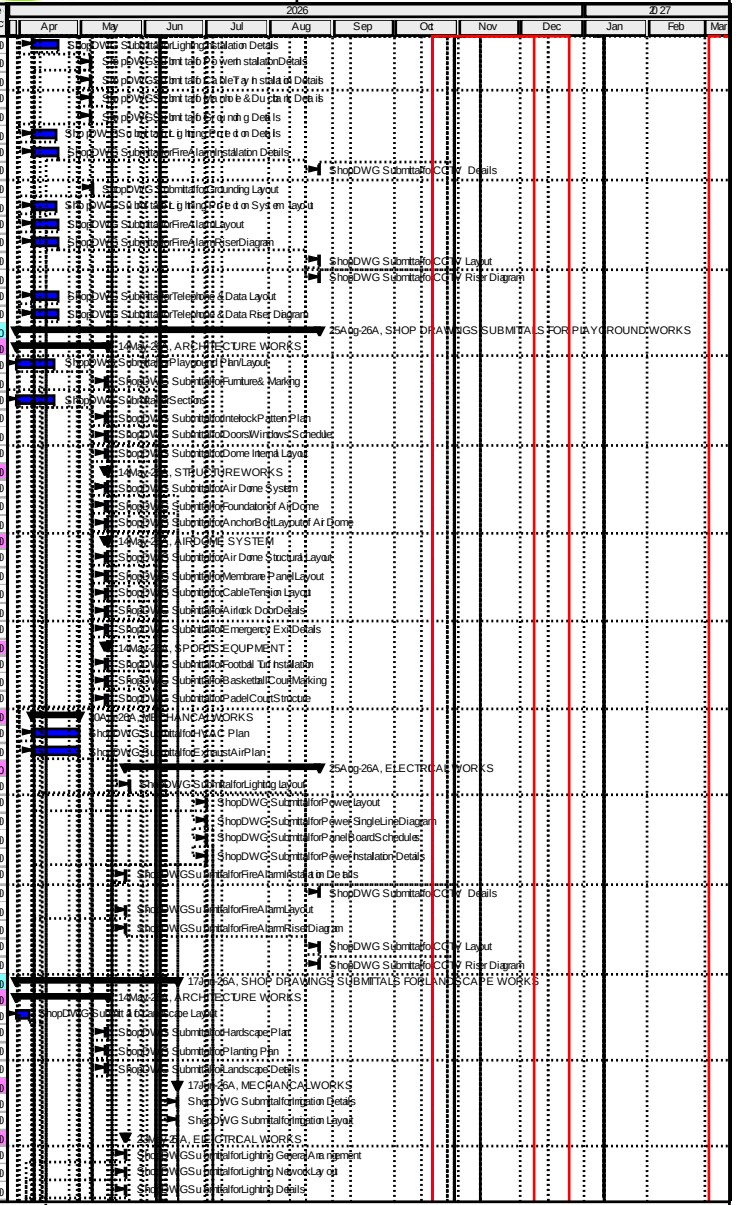

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-28	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23-May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALS		12900	0%	0%	07 Apr 26	11Jul-26	07 Apr 26 A	26Aug-26A	$000	$000	$0.00	-4000
SHOP DRAWIN GAPPROVALFOR EARTHINGW ORKS		5200	0%	0%	07 Apr 26	09Jun-26	07 Apr 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2900	ShopDWG Appovalfor layoutPlan	6.00	100%	100%	18 Apr 26	23Apr-26	18 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2910	ShopDWG Appovalfor SettingOut	0.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2920	ShopDWG Appovalfor GadingLayoutPlan	2000	100%	100%	07 Apr 26	29Apr-26	07 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2930	ShopDWG Appovalfor Cub SettingOut Points	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2940	ShopDWG Appovalfor Signing& Marking Layout Plan	1.00	100%	100%	09 Jun 26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-2950	ShopDWG Appovalfor Standards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GAPPROVALFOR SERVICE ETOILETWORKS		11100	0%	0%	14 Apr 26	11Jul-26	14 Apr 26 A	12Aug-26A	$000	$000	$0.00	-2800
ARCHITECTURE WORKS		9.00	0%	0%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor floorPlan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor Elevations	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-30	ShopDWG Appovalfor Sections	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-301	ShopDWG Appovalfor CeilingPlan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-302	ShopDWG Appovalfor finishes Plan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-303	ShopDWG Appovalfor ToiletDetails	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-304	ShopDWG Appovalfor Doors/WindowsSchedule	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-306	ShopDWG Appovalfor foundation Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-307	ShopDWG Appovalfor Gound floorFraming Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-308	ShopDWG Appovalfor SectionsDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1300	0%	0%	07 May-26	21May-26	07 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-310	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-311	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-312	ShopDWG Appovalfor HVACEquipment Schedule	4.00	100%	100%	07 May-26	11May-26	07 May 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-317	ShopDWG Appovalfor fire fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-318	ShopDWG Appovalfor WaterSupplyLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-319	ShopDWG Appovalfor WaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-313	ShopDWG Appovalfor DrainageLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-314	ShopDWG Appovalfor DrainageDetails	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-315	ShopDWG Appovalfor Duct RoutingLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-316	ShopDWG Appovalfor Diffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		11000	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	12Aug-26A	$000	$000	$0.00	-2800
MLTX02-004EN-321	ShopDWG Appovalfor Lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-322	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-323	ShopDWG Appovalfor Power Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-324	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-325	ShopDWG Appovalfor Lighting InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-326	ShopDWG Appovalfor Power InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-327	ShopDWG Appovalfor Cable Tray InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-328	ShopDWG Appovalfor Manhole& DuctbankDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-329	ShopDWG Appovalfor Grounding Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-332	ShopDWG Appovalfor lightning Potection Details	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-336	ShopDWG Appovalfor fire Alarm Installation Details	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-335	ShopDWG Appovalfor CCTV Details	6.00	100%	100%	05 Jul-25	11Jul-26	12 Aug 25 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-330	ShopDWG Appovalfor Grounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-333	ShopDWG Appovalfor lightning Potection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-331	ShopDWG Appovalfor fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-334	ShopDWG Appovalfor fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-338	ShopDWG Appovalfor CCTV Layout	6.00	100%	100%	05 Jul-25	11Jul-26	12 Aug 25 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-339	ShopDWG Appovalfor CCTV RiserDiagram	6.00	100%	100%	05 Jul-25	11Jul-26	12 Aug 25 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-337	ShopDWG Appovalfor Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-340	ShopDWG Appovalfor Telephone & Data Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GSAPPROVALFOR PLAYGROUND WORKS		12200	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-4000
ARCHITECTURE WORKS		4500	0%	0%	19 Apr 26	13Jun-26	19 Apr 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-343	ShopDWG Appovalfor Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-344	ShopDWG Appovalfor Furniture & Marking	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-345	ShopDWG Appovalfor Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-346	ShopDWG Appovalfor Interlock PatternPlan	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-347	ShopDWG Appovalfor Doors/WindowsSchedule	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-348	ShopDWG Appovalfor Dome InternalLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-350	ShopDWG Appovalfor Air DomeSystem	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-351	ShopDWG Appovalfor foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00

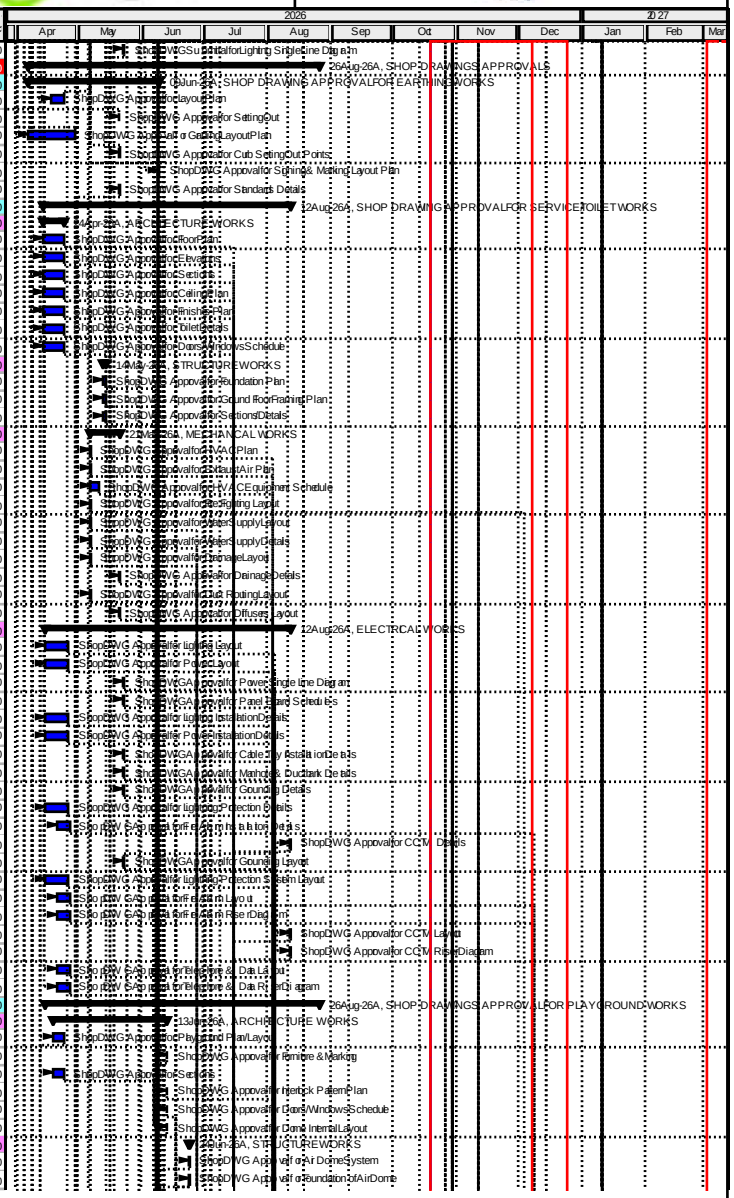


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-3521	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3531	ShopDWG Appovalfor Anchor Bolt layoutof AirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3551	ShopDWG Appovalfor Air DomeStructuralLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3561	ShopDWG Appovalfor MembranePanelLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3571	ShopDWG Appovalfor Cable TensionLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3581	ShopDWG Appovalfor AirlockDoorDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3591	ShopDWG Appovalfor EmergencyExitDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUPMENT		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3611	ShopDWG Appovalfor Footbal Tuf Installation	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3621	ShopDWG Appovalfor Basketball Court Making	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3631	ShopDWG Appovalfor Padel Court Stucture	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3651	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3661	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		12200	0%	0%	15 Apr 26	11Jul-26	15 Apr 26A	26Aug-26A	$000	$000	$0.00	-4000
MLTX02-004EN-3681	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3691	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3731	ShopDWG Appovalfor Power Single line Diagram	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-3741	ShopDWG Appovalfor Panel Board Schedules	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-3701	ShopDWG Appovalfor Power InstallitionDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3761	ShopDWG Appovalfor CCTV Details	6.00	100%	100%	05 Jul-26	11Jul-26	26 Aug 26A	26Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-3771	ShopDWG Appovalfor CCTV Layout	6.00	100%	100%	05 Jul-26	11Jul-26	26 Aug 26A	26Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-3781	ShopDWG Appovalfor CCTV RiserDiagram	6.00	100%	100%	05 Jul-26	11Jul-26	26 Aug 26A	26Aug-26A	$000	$000	$0.00	5.00
SHOP DRAWIN GSAPPROVALFOR LANDSCAPE WORKS		6200	0%	0%	11 Apr 26	24Jun-26	11 Apr 26A	24Jun-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		2300	0%	0%	19 Apr 26	14May-26	19 Apr 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3811	ShopDWG Appovalfor landscape Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3821	ShopDWG Appovalfor Hardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3831	ShopDWG Appovalfor Planting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3841	ShopDWG Appovalfor landscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26A	14May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3881	ShopDWG Appovalfor IrrigationDetails	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3921	ShopDWG Appovalfor IrrigationLayout	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		3700	0%	0%	11 Apr 26	23May-26	11 Apr 26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3971	ShopDWG Appovalfor lighting General Arrangement	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3981	ShopDWG Appovalfor lighting Network Layout	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3991	ShopDWG Appovalfor lighting Details	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-3961	ShopDWG Appovalfor lighting Single Line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26A	23May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		18600	0%	0%	31 Mar 26	03Aug-26	31 Mar 26A	07Nov-26	$000	$000	$0.00	-8100
METHOD STATEMENT SUBMITTAL		17600	0%	0%	31 Mar 26	19Jul-26	31 Mar 26A	26Oct-26	$000	$000	$0.00	-8400
CIVL WORKS		4500	0%	0%	31 Mar 26	21May-26	31 Mar 26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4020	Preparation & Submissionof MethodStatement forEarthwork	1700	100%	100%	31 Mar 26	19Apr-26	31 Mar 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4030	Preparation & Submissionof MethodStatement forConcete Works	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4040	Preparation & Submissionof MethodStatement forWaterproding	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar 26A	25Apr-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		12700	0%	0%	31 May-26	11Jul-26	31 May 26A	26Oct-26	$000	$000	$0.00	-9100
MLTX02-004EN-4140	Preparation & Submissionof MethodStatement forFenceWorks	6.00	100%	0%	05 Jul-26	11Jul-26	20 Oct 26	26Oct-26	$000	$000	$0.00	0.00
MLTX02-004EN-4060	Preparation & Submissionof MethodStatement forPlastringWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4070	Preparation & Submissionof MethodStatement forMasonary Waks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4080	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4090	Preparation & Submissionof MethodStatement forSeatsBenchesWoks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4100	Preparation & Submissionof MethodStatement forDoorsWindows Waks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4110	Preparation & Submissionof MethodStatement forInterlockCurbstone Works	1.00	100%	100%	31 May-26	31May-26	31 May 26A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4120	Preparation & Submissionof MethodStatement forParking Waks	1.00	100%	100%	31 May-26	31May-26	31 May 26A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4130	Preparation & Submissionof MethodStatement forSoftScapeWorks	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4150	Preparation & Submissionof MethodStatement forAirDome Waks	6.00	100%	100%	05 Jul-26	11Jul-26	17 Aug 26A	17Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4160	Preparation & Submissionof MethodStatement forMetalWoks	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4170	Preparation & Submissionof MethodStatement forPartitions Woks	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4180	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4800	0%	0%	07 Apr 26	04Jun-26	07 Apr 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4200	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31 May-26	31May-26	31 May 26A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4210	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4220	Preparation & Submissionof MethodStatement forFire FightingSystem	7.00	100%	100%	07 Apr 26	14Apr-26	07 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4230	Preparation & Submissionof MethodStatement forIrrigation System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4240	Preparation & Submissionof MethodStatement forHVAC System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		5800	0%	0%	18 Jun 26	19Jul-26	18 Jun 26A	11Aug-26A	$000	$000	$0.00	-2000
MLTX02-004EN-4310	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00

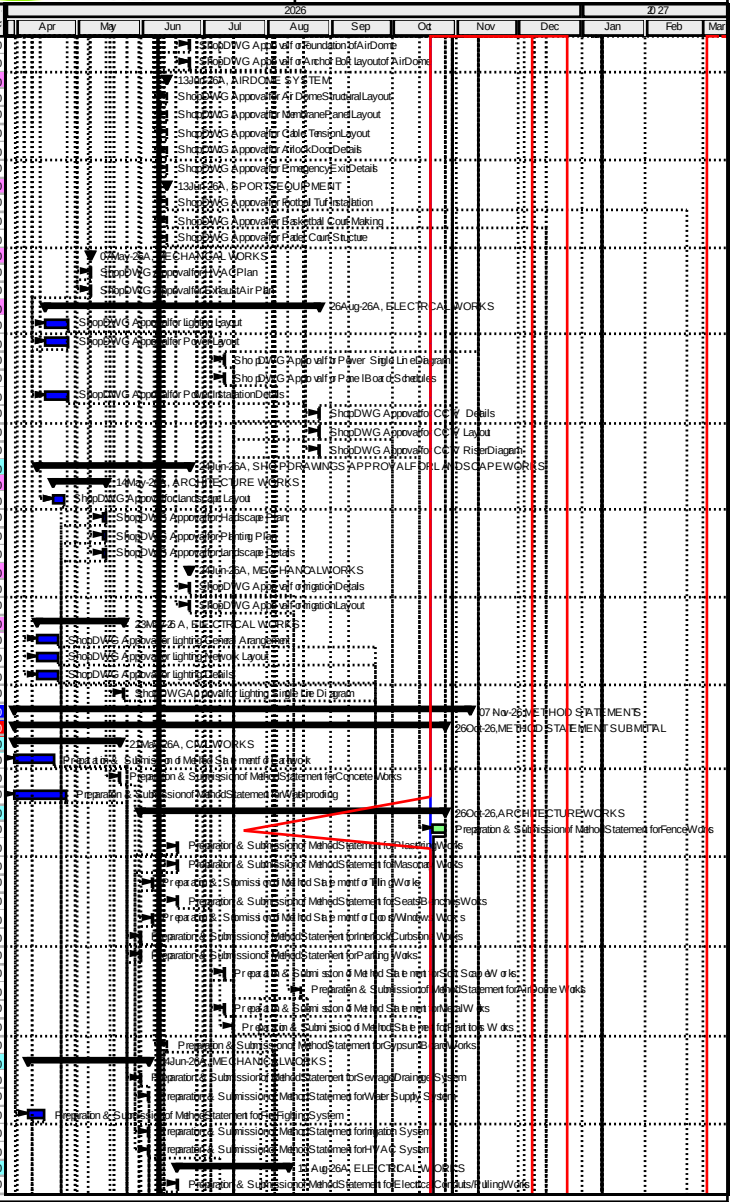


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02004EN-4330	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4260	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	7.00	100%	100%	12-Jul-26	19-Jul-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	6.00
MLTX02004EN-4270	Preparation & Submissionof MethodStatement forCCTV System	7.00	100%	100%	12-Jul-26	19-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	6.00
MLTX02004EN-4280	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4290	Preparation & Submissionof MethodStatement forEarthing/Lightning Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4300	Preparation & Submissionof MethodStatement forPanelBoardsWorks	6.00	100%	100%	05-Jul-26	11-Jul-26	11-Aug-26A	11-Aug-26A	$000	$000	$0.00	5.00
METHOD STATEMENT APPROVAL		17300	0%	0%	15-Apr-26	03-Aug-26	15-Apr-26A	07-Nov-26	$000	$000	$0.00	-8100
CIVL WORKS		1.00	0%	0%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX02004EN-4360	Appoval of Method Statementfor Earthwok	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX02004EN-4370	Appoval of Method Statementfor Concrete Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX02004EN-4380	Appoval of Method Statementfor Waterproofing	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		13700	0%	0%	31-May-26	22-Jul-26	31-May-26A	07-Nov-26	$000	$000	$0.00	-9100
MLTX02004EN-4480	Appoval of Method Statementfor Fence Works	1000	100%	0%	12-Jul-26	22-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02004EN-4400	Appoval of Method Statementfor Plasteing Works	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4410	Appoval of Method Statementfor MasonaryWorks	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4420	Appoval of Method Statementfor Tiling Works	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4430	Appoval of Method Statementfor Seats/Benches Works	6.00	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	5.00
MLTX02004EN-4440	Appoval of Method Statementfor Doors/WindowsWorks	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4450	Appoval of Method Statementfor Interlock/Curbstone Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX02004EN-4460	Appoval of Method Statementfor ParkingWorks	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX02004EN-4470	Appoval of Method Statementfor Soft Scape Works	1000	100%	100%	12-Jul-26	22-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4490	Appoval of Method Statementfor Air DomeWorks	1000	100%	100%	12-Jul-26	22-Jul-26	27-Aug-26A	27-Aug-26A	$000	$000	$0.00	9.00
MLTX02004EN-4510	Appoval of Method Statementfor PartitionsWorks	1000	100%	100%	12-Jul-26	22-Jul-26	27-Aug-26A	27-Aug-26A	$000	$000	$0.00	9.00
MLTX02004EN-4520	Appoval of Method Statementfor Gypsum Board Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4700	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4540	Appoval of Method Statementfor Sewage/DrainageSystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4550	Appoval of Method Statementfor WaterSupplySystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4560	Appoval of Method Statementfor FireFighting System	1000	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-4570	Appoval of Method Statementfor IrrigationSystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4580	Appoval of Method Statementfor HVAC System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
ELECTRICAL WORKS		7000	0%	0%	16-Jun-26	03-Aug-26	16-Jun-26A	12-Aug-26A	$000	$000	$0.00	-800
MLTX02004EN-4600	Appoval of Method Statementfor ElectricalConduits/Pulling Works	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4620	Appoval of Method Statementfor Lighting Poles Installation	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4630	Appoval of Method Statementfor Telecommunication & Data System	1000	100%	100%	23-Jul-26	03-Aug-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4640	Appoval of Method Statementfor CCTV System	1000	100%	100%	23-Jul-26	03-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4650	Appoval of Method Statementfor Lighting Works	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4660	Appoval of Method Statementfor Earthing/LightningWorks	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4670	Appoval of Method Statementfor Panel Boards Works	1000	100%	100%	12-Jul-26	22-Jul-26	12-Aug-26A	12-Aug-26A	$000	$000	$0.00	9.00
PRE-QUALIFICATION& MATERIAL		20600	0%	0%	31-Mar-26	02-Sep-26	31-Mar-26A	30-Nov-26	$000	$000	$0.00	-7500
PRE-QUALIFICATION		4500	0%	0%	31-Mar-26	21-May-26	31-Mar-26A	21-May-26A	$000	$000	$0.00	0.00
TOILETSERVICE EWORKS		2100	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
STEEL RENFORCEMENT		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-472	PreQualifcation SubmittalforSteelReinforcement	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-473	PreQualifcation Appovalfor SteelReinfocement	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
READY MKCONCRETE		2100	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-475	PreQualifcation SubmittalforReadyMixed Concrete	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-476	PreQualifcation Appovalof Ready Mixed Concete	1100	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26A	23-Apr-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		2100	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-478	PreQualifcation SubmittalforConcrete Blocks	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-479	PreQualifcation Appovalfor Concrete Blocks	1500	100%	100%	07-Apr-26	23-Apr-26	07-Apr-26A	23-Apr-26A	$000	$000	$0.00	0.00
WATERPROOFING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-481	PreQualifcation SubmittalforWater Proofing	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-482	PreQualifcation Appovalfor WaterProofing	3.00	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
FLOORWALL TILES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-484	PreQualifcation SubmittalforTiling Materials	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-485	PreQualifcation Appovalfor Tailing Material	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SUSPENDED CEILING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-487	PreQualifcation SubmittalforSuspendCeiling	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-488	PreQualifcation Appovalfor SuspendCeiling	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
DOORS/WINDOWS		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-490	PreQualifcation SubmittalforDoors/Windows	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-491	PreQualifcation Appovalfor Doors/Windows	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
FURNITURES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-493	PreQualifcation SubmittalforFurnitures	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-494	PreQualifcation Appovalfor Furnitures	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00

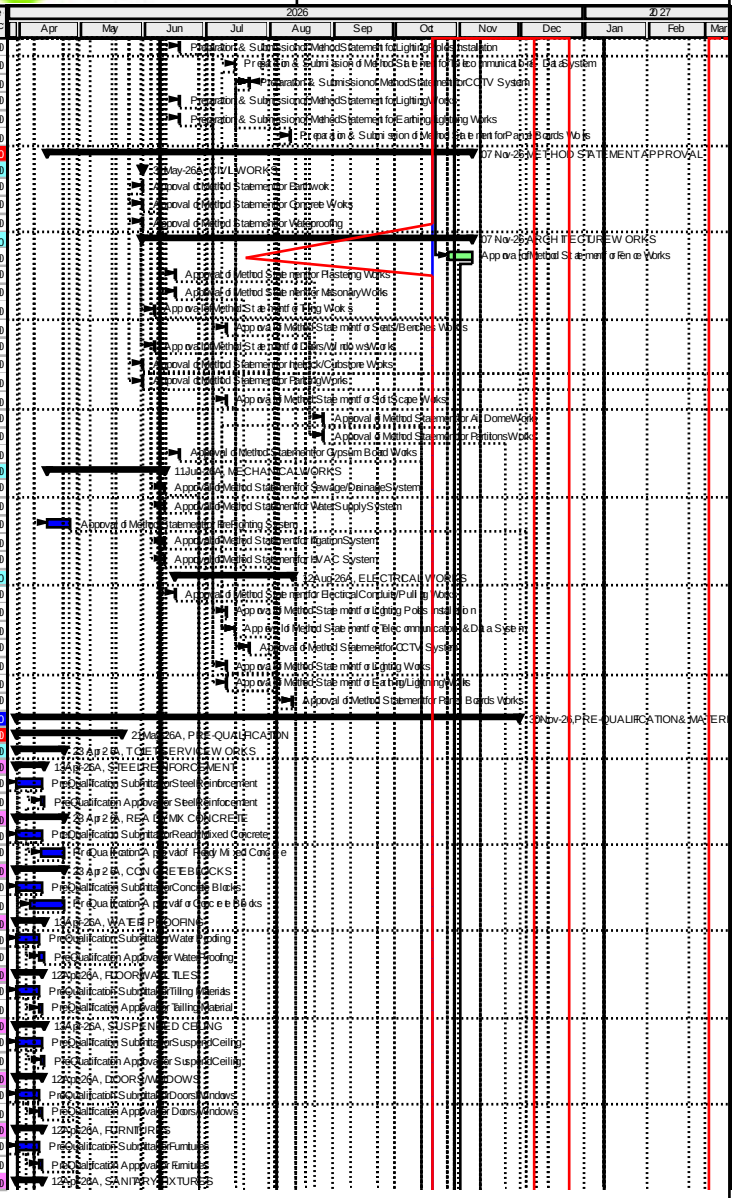

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-496	PreQualifcation SubmittalforSanitary Fixtures	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-497	PreQualifcation Appovalfor Sanitay Fixtures	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
WATERSUPPLY PIPES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-498	PreQualifcation SubmittalforWater Supply Pipes	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-500	PreQualifcation Appovalfor WaterSupplyPipes	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
SEWAGEDRAINAGEPIPES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-502	PreQualifcation SubmittalforSewageDrainage Pipes	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-503	PreQualifcation Appovalfor Sewage/DrainagePipes	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-505	PreQualifcation SubmittalforPackageAC Units	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-506	PreQualifcation Appovalfor PackageAC Units	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-508	PreQualifcation SubmittalforAir Diffusers/Grills	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-509	PreQualifcation Appovalfor Air Diffusers/Grills	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-511	PreQualifcation SubmittalforGalvanized Ducts	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-512	PreQualifcation Appovalfor Galvanized Ducts	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-514	PreQualifcation SubmittalforExhaustFans	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-515	PreQualifcation Appovalfor ExhaustFans	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-517	PreQualifcation SubmittalforLighting Fixtures	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-518	PreQualifcation Appovalfor Lighting Fixtures	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-520	PreQualifcation SubmittalforSwitches/Sockets	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-521	PreQualifcation Appovalfor Switches/Sockets	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-523	PreQualifcation SubmittalforEarthing System	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-524	PreQualifcation Appovalfor Earthing System	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
DISTRIBUTON PANNELS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-526	PreQualifcation SubmittalforDistribution Panels	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-527	PreQualifcation Appovalfor Distribution Panels	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		2100	0%	0%	31 Mar 26	23Apr-26	31 Mar 26A	23Apr-26A	$000	$000	$0.00	0.00
PVC MEMBRANE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-530	PreQualifcation SubmittalforPVC Membane	1100	100%	100%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-531	PreQualifcation Appovalfor PVCMembrane	4.00	100%	100%	12 Apr 26	15Apr-26	12 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
STEELTENSION CABLES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-533	PreQualifcation SubmittalforSteelTension Cables	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-534	PreQualifcation Appovalfor SteelTensionCables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-536	PreQualifcation SubmittalforEmergency Doors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-537	PreQualifcation Appovalfor EmergencyDoors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-539	PreQualifcation SubmittalforPressue Units	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-540	PreQualifcation Appovalfor Pessue Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-542	PreQualifcation SubmittalforLockDoors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-543	PreQualifcation Appovalfor Lock Doos	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-545	PreQualifcation SubmittalforArtificial TURF	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-546	PreQualifcation Appovalfor ArtificialTURF	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-548	PreQualifcation SubmittalforRubberGranules	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-549	PreQualifcation Appovalfor RubberGranules	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADELGLASS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-551	PreQualifcation SubmittalforPadelGlass	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-552	PreQualifcation Appovalfor Padel Glass	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADELWIREMESH/STEELSETS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-554	PreQualifcation SubmittalforWireMesh/SteelSets	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-555	PreQualifcation Appovalfor WireMesh/Steel Sets	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-557	PreQualifcation SubmittalforAggregate Base Course	1400	100%	100%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-558	PreQualifcation Appovalfor Aggregate BaseCourse	1.00	100%	100%	15 Apr 26	15Apr-26	15 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		7.00	0%	0%	07 Apr 26	14Apr-26	07 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-560	PreQualifcation SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-561	PreQualifcation Appovalfor the Site	3.00	100%	100%	12 Apr 26	14Apr-26	12 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1500	0%	0%	07 Apr 26	23Apr-26	07 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00

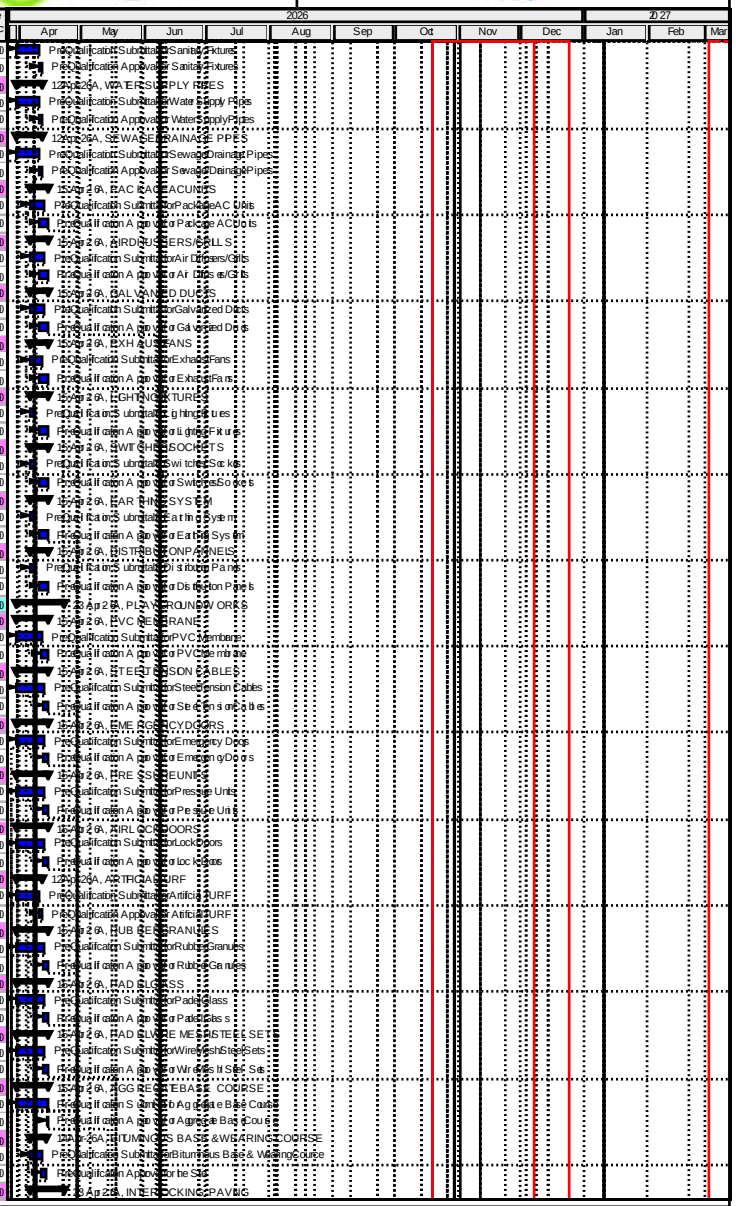

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule D.D 19-10-2026







ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-563	PreQualification SubmittalforInterlocking Block Pavers	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-564	PreQualification Approvalfor Interlocking BlockPavers	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MARKINGPAINT		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-566	PreQualification SubmittalforMarking Paint	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-567	PreQualification Approvalfor MakingPaint	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-569	PreQualification SubmittalforPackageAC Units	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-570	PreQualification Approvalfor PackageAC Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-572	PreQualification SubmittalforAir Difussers/Grills	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-573	PreQualification Approvalfor Air Difussers/Grills	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-575	PreQualification SubmittalforGalvanized Duct	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-576	PreQualification Approvalfor Galvanized Duct	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-578	PreQualification SubmittalforExhaustFans	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-579	PreQualification Approvalfor ExhaustFans	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
DISTRBUTON BOARDS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-581	PreQualification SubmittalforDistribution Boards	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-582	PreQualification Approvalfor Distribution Boards	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-584	PreQualification SubmittalforPowerCables	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-585	PreQualification Approvalfor Power Cables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
LIGHTFXTURES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-587	PreQualification SubmittalforLightFixtures	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-588	PreQualification Approvalfor LightFixtures	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
CCTV MATERALS		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-590	PreQualification SubmittalforCCTV	3.00	100%	100%	04 Apr 26	06Apr-26	04 Apr 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-591	PreQualification Approvalfor CCTV	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
POWEROUTIETS/SWITCHES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-593	PreQualification SubmittalforPowerOutlets/Switches	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-594	PreQualification Approvalfor Power OutletsSwitches	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.00
INTERLOCKNG PAVING		1800	0%	0%	04 Apr 26	23Apr-26	04 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-597	PreQualification SubmittalforInterlocking Block Pavers	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-598	PreQualification Approvalfor Interlocking BlockPavers	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		1800	0%	0%	04 Apr 26	23Apr-26	04 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-600	PreQualification SubmittalforCurbstone	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-601	PreQualification Approvalfor Curbstone	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
PAVEMENTMARKNG		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-603	PreQualification SubmittalforPavementMarkings	3.00	100%	100%	04 Apr 26	06Apr-26	04 Apr 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-604	PreQualification Approvalfor PavementMarkings	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
TRAFFC SGNS		1400	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-606	PreQualification SubmittalforTraffic Signs	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-607	PreQualification Approvalfor Traffic Signs	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
IRRGATIONPIPESSPRINKLERS		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-609	PreQualification SubmittalforIrrigation Pipes/Sprinkles	2000	100%	100%	04 Apr 26	26Apr-26	04 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-610	PreQualification Approvalfor IrrigationPipesSprinkles	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
AGRICULTURE SOIL		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-612	PreQualification SubmittalforAgricultue Soil	2000	100%	100%	04 Apr 26	26Apr-26	04 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-613	PreQualification Approvalfor AgricutureSoil	1.00	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-615	PreQualification SubmittalforTrackSurface	3.00	100%	100%	04 Apr 26	06Apr-26	04 Apr 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-616	PreQualification Approvalfor TrackSurface	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
GRASS/TREES		1400	0%	0%	04 Apr 26	19Apr-26	04 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-618	PreQualification SubmittalforGrass/Trees	1000	100%	100%	04 Apr 26	14Apr-26	04 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-619	PreQualification Approvalfor Gass/Tees	5.00	100%	100%	14 Apr 26	19Apr-26	14 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
CABIES		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-621	PreQualification SubmittalforCables	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-622	PreQualification Approvalfor Cables	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
LIGHTPOLES		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-624	PreQualification SubmittalforLighting poles	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-625	PreQualification Approvalfor lighting poles	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
MATERIALSUBMITTAL& APPROVAL		19700	0%	0%	11 Apr 26	02Sep-26	11 Apr 26A	30Nov-26	$000	$000	$0.00	-7500
TOILETSERVICE WORKS		9200	0%	0%	11 Apr 26	12Jul-26	11 Apr 26A	22Jul-26A	$000	$000	$0.00	-900
STEEL RENFORCEMENT		4.00	0%	0%	11 Apr 26	14Apr-26	11 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-628	MaterialSubmittal for Steel Reinforement	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00

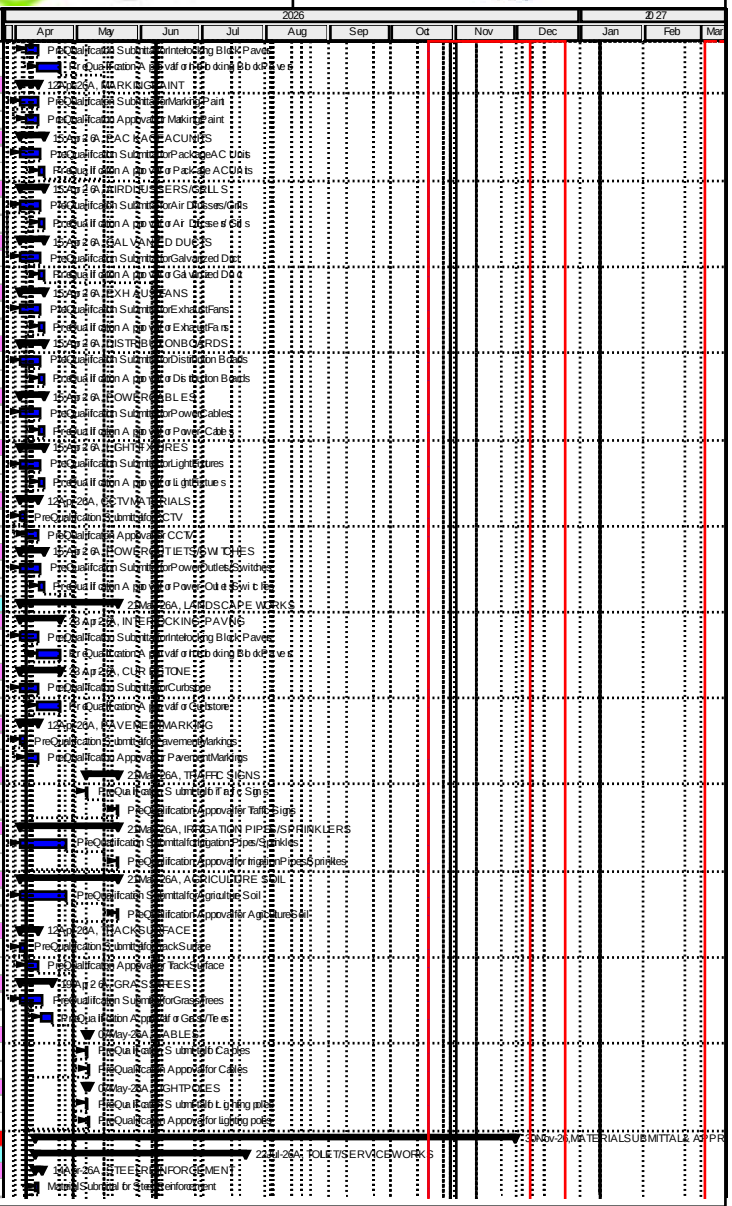


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-630	Material Approval for Steel Reinforcement	3.00	100%	100%	12 Apr 26	14 Apr-26	12 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.00
READY MIX CONCRETE		1000	0%	0%	15 Apr 26	26 Apr-26	15 Apr 26 A	26 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-632	Material Submittal for Ready Mixed Concrete	3.00	100%	100%	15 Apr 26	18 Apr-26	15 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-633	Material Approval of Ready Mixed Concrete	7.00	100%	100%	19 Apr 26	26 Apr-26	19 Apr 26 A	26 Apr-26 A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		1000	0%	0%	15 Apr 26	26 Apr-26	15 Apr 26 A	26 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-635	Material Submittal for Concrete Blocks	3.00	100%	100%	15 Apr 26	18 Apr-26	15 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-636	Material Approval for Concrete Blocks	7.00	100%	100%	19 Apr 26	26 Apr-26	19 Apr 26 A	26 Apr-26 A	$000	$000	$0.00	0.00
FLOOR/WALL TILES		8800	0%	0%	15 Apr 26	12 Jul-26	15 Apr 26 A	22 Jul-26 A	$000	$000	$0.00	-900
MLTX-02-004EN-641	Material Submittal for Tiling Materials	3.00	100%	100%	15 Apr 26	18 Apr-26	15 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-642	Material Approval for Tiling Material	7.00	100%	100%	05 Jul-26	12 Jul-26	22 Jul-26 A	22 Jul-26 A	$000	$000	$0.00	6.00
SUSPENDED CEILING		5.00	0%	0%	15 Apr 26	20 Apr-26	15 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-644	Material Submittal for Suspend Ceiling	3.00	100%	100%	15 Apr 26	18 Apr-26	15 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-645	Material Approval for Suspend Ceiling	2.00	100%	100%	19 Apr 26	20 Apr-26	19 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
DOORS/WINDOWS		1400	0%	0%	06 May-26	21 May-26	06 May 26 A	21 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-647	Material Submittal for Doors/Windows	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-648	Material Approval for Doors/Windows	1.00	100%	100%	21 May-26	21 May-26	21 May 26 A	21 May-26 A	$000	$000	$0.00	0.00
FURNITURES		2.00	0%	0%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-650	Material Submittal for Furnitures	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-651	Material Approval for Furnitures	1.00	100%	100%	07 May-26	07 May-26	07 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
SANITARY FIXTURES		1400	0%	0%	15 Apr 26	30 Apr-26	15 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-653	Material Submittal for Sanitary Fixtures	6.00	100%	100%	15 Apr 26	21 Apr-26	15 Apr 26 A	21 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-654	Material Approval for Sanitary fixtures	1100	100%	100%	19 Apr 26	30 Apr-26	19 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		2.00	0%	0%	15 Apr 26	16 Apr-26	15 Apr 26 A	16 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-656	Material Submittal for Water Supply Pipes	1.00	100%	100%	15 Apr 26	15 Apr-26	15 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-657	Material Approval for Water Supply Pipes	2.00	100%	100%	15 Apr 26	16 Apr-26	15 Apr 26 A	16 Apr-26 A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		2.00	0%	0%	15 Apr 26	16 Apr-26	15 Apr 26 A	16 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-659	Material Submittal for Sewage/Drainage Pipes	1.00	100%	100%	15 Apr 26	15 Apr-26	15 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-660	Material Approval for Sewage Drainage Pipes	2.00	100%	100%	15 Apr 26	16 Apr-26	15 Apr 26 A	16 Apr-26 A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		2.00	0%	0%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-662	Material Submittal for Package AC Units	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-663	Material Approval for Package AC Units	1.00	100%	100%	07 May-26	07 May-26	07 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1800	0%	0%	16 Apr 26	06 May-26	16 Apr 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-665	Material Submittal for AirDiffusers/Grills	6.00	100%	100%	16 Apr 26	22 Apr-26	16 Apr 26 A	22 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-666	Material Approval for AirDiffusers/Grills	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		6.00	0%	0%	13 Jun 26	18 Jun-26	13 Jun 26 A	18 Jun-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-668	Material Submittal for Galvanized Ducts	1.00	100%	100%	13 Jun 26	13 Jun-26	13 Jun 26 A	13 Jun-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-669	Material Approval for Galvanized Ducts	1.00	100%	100%	18 Jun 26	18 Jun-26	18 Jun 26 A	18 Jun-26 A	$000	$000	$0.00	0.00
EXHAUST FANS		1800	0%	0%	16 Apr 26	06 May-26	16 Apr 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-671	Material Submittal for Exhaust Fans	2.00	100%	100%	16 Apr 26	18 Apr-26	16 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-672	Material Approval for Exhaust Fans	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	16 Apr 26	25 Apr-26	16 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-674	Material Submittal for Lighting Fixtures	3.00	100%	100%	16 Apr 26	19 Apr-26	16 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-675	Material Approval for Lighting Fixtures	5.00	100%	100%	20 Apr 26	25 Apr-26	20 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	16 Apr 26	25 Apr-26	16 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-677	Material Submittal for Switches/Sockets	3.00	100%	100%	16 Apr 26	19 Apr-26	16 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-678	Material Approval for Switches/Sockets	5.00	100%	100%	20 Apr 26	25 Apr-26	20 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		2.00	0%	0%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-680	Material Submittal for EathingSystem	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-681	Material Approval for Earthing System	1.00	100%	100%	07 May-26	07 May-26	07 May 26 A	07 May-26 A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		8.00	0%	0%	16 Apr 26	25 Apr-26	16 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-683	Material Submittal for Distribution Panels	3.00	100%	100%	16 Apr 26	19 Apr-26	16 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-684	Material Approval for Distibuton Panels	5.00	100%	100%	20 Apr 26	25 Apr-26	20 Apr 26 A	25 Apr-26 A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		19600	0%	0%	12 Apr 26	02 Sep-26	12 Apr 26 A	30 Nov-26	$000	$000	$0.00	-7500
PVC MEMBRANE		16500	0%	0%	15 Apr 26	13 Jul-26	15 Apr 26 A	28 Oct-26	$000	$000	$0.00	-9100
MLTX-02-004EN-688	Material Approval for PVC Membane	8.00	100%	0%	05 Jul-26	13 Jul-26	20 Oct 26	28 Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-687	Material Submittal for PVC Membrane	3.00	100%	100%	15 Apr 26	18 Apr-26	15 Apr 26 A	18 Apr-26 A	$000	$000	$0.00	0.00
STEEL TENSION CABLES		15600	0%	0%	06 May-26	23 Jul-26	06 May 26 A	08 Nov-26	$000	$000	$0.00	-9100
MLTX-02-004EN-691	Material Approval for Steel Tension Cables	9.00	100%	0%	14 Jul-26	23 Jul-26	29 Oct 26	08 Nov-26	$000	$000	$0.00	0.00
MLTX-02-004EN-690	Material Submittal for Steel Tension Cables	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
EMERGENCY DOORS		16500	0%	0%	06 May-26	03 Aug-26	06 May 26 A	18 Nov-26	$000	$000	$0.00	-9100
MLTX-02-004EN-694	Material Approval for Emergency Doors	9.00	100%	0%	25 Jul-26	03 Aug-26	09 Nov 26	18 Nov-26	$000	$000	$0.00	0.00
MLTX-02-004EN-693	Material Submittal for Emegency Doors	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
PRESSURE UNITS		17100	0%	0%	06 May-26	13 Aug-26	06 May 26 A	24 Aug-26 A	$000	$000	$0.00	-900
MLTX-02-004EN-696	Material Submittal for PressureUnits	1.00	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-697	Material Approval for Pressure Units	9.00	100%	100%	04 Aug-26	13 Aug-26	21 Aug 26 A	24 Aug-26 A	$000	$000	$0.00	8.00
AIRLOCK DOORS		16700	0%	0%	06 May-26	24 Aug-26	06 May 26 A	21 Nov-26	$000	$000	$0.00	-7500
MLTX-02-004EN-700	Material Approval for LockDoors	8.00	100%	0%	16 Aug-26	24 Aug-26	12 Nov 26	21 Nov-26	$000	$000	$0.00	0.00

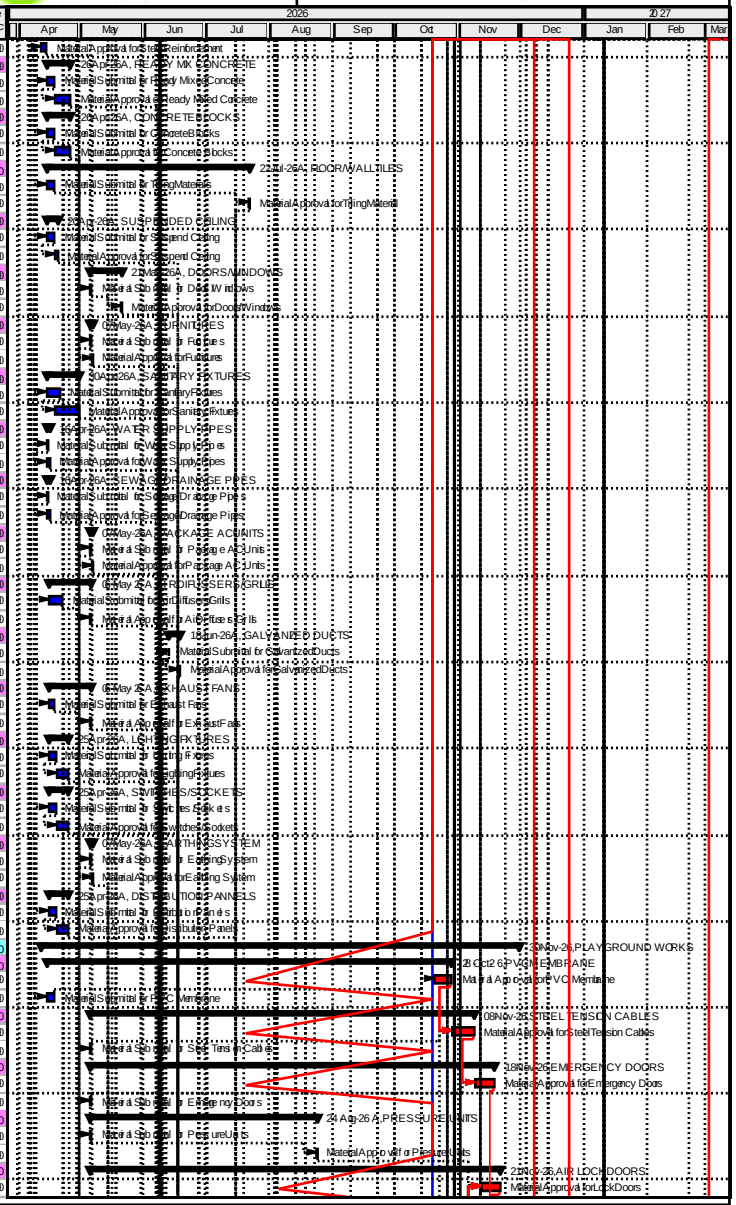

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-695	Material Submittal for Lock Doors	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1700	0%	0%	12 Apr 26	30Apr-26	12 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-702	Material Submittal for Artificial TURF	1500	100%	100%	12 Apr 26	28Apr-26	12 Apr 26A	28Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-703	Material Approval for Artificial TURF	3.00	100%	100%	28 Apr 26	30Apr-26	28 Apr 26A	30Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	06 May-26	21May-26	06 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-705	Material Submittal for Rubber Granules	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-706	Material Approval for Rubber Granules	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
PADEL GLASS		1400	0%	0%	06 May-26	21May-26	06 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-708	Material Submittal for Padel Glass	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-709	Material Approval for Padel Glass	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		15900	0%	0%	25 May-26	02Sep-26	25 May-26 A	30Nov-26	$000	$000	$0.00	-7500
MLTX-02-004EN-712	Material Approval for Wie Mesh/Steel Sets	8.00	100%	0%	25 Aug-26	02Sep-26	22 Nov-26	30Nov-26	$000	$000	$0.00	0.00
MLTX-02-004EN-711	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25 May-26	25May-26	25 May-26 A	25May-26A	$000	$000	$0.00	0.00
AGGREGATE BASE COURSE		2200	0%	0%	21 May-26	18Jun-26	21 May-26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-714	Material Submittal for Aggregate Base Cairse	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-715	Material Approval for Aggregate Base Couse	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		2.00	0%	0%	16 Apr 26	18Apr-26	16 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-717	Material Submittal for Bituminous Base& Wearing Couce	2.00	100%	100%	16 Apr 26	18Apr-26	16 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-718	Material Approval for the Site	1.00	100%	100%	18 Apr 26	18Apr-26	18 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1.00	0%	0%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-720	Material Submittal for Interlocking Block Pavers	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-721	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MARKING PAINT		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-722	Material Submittal for Making Paint	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-724	Material Approval for Marking Paint	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-726	Material Submittal for Packege ACUnits	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-727	Material Approval for Package AC Units	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		2100	0%	0%	13 Apr 26	06May-26	13 Apr 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-729	Material Submittal for AirDifussersGrills	9.00	100%	100%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-730	Material Approval for AirDifussers/Grills	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		6.00	0%	0%	13 Jun 26	18Jun-26	13 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-732	Material Submittal for GalvanizedDuct	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-733	Material Approval for GalvanizedDuct	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
EXHAUST FANS		2100	0%	0%	13 Apr 26	06May-26	13 Apr 26A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-735	Material Submittal for Exhaust Fans	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-736	Material Approval for Exhaust Fans	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
DISTRBUTION BOARDS		1100	0%	0%	13 Apr 26	25Apr-26	13 Apr 26A	25Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-738	Material Submittal for Distribution Boards	6.00	100%	100%	13 Apr 26	19Apr-26	13 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-739	Material Approval for Distibuton Boards	6.00	100%	100%	19 Apr 26	25Apr-26	19 Apr 26A	25Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		7.00	0%	0%	13 Apr 26	20Apr-26	13 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-741	Material Submittal for PowerCables	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-742	Material Approval for PowerCables	4.00	100%	100%	16 Apr 26	20Apr-26	16 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
LIGHT FIXTURES		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-744	Material Submittal for Light Fixtures	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-745	Material Approval for Light Fixtures	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-747	Material Submittal for CCTV	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-748	Material Approval for CCTV	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
POWEROUTLETS/SWITCHES		2.00	0%	0%	06 May-26	07May-26	06 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-750	Material Submittal for PowerOutlets/Switches	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-751	Material Approval for PowerOutlets/Switches	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		9300	0%	0%	13 Apr 26	11Jul-26	13 Apr 26A	27Jul-26A	$000	$000	$0.00	-1400
INTERLOCKING PAVING		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-754	Material Submittal for Interlocking Block Pavers	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-755	Material Approval for Interlocking Bbck Pavers	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-757	Material Submittal for Cubstone	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-758	Material Approval for Curbstone	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
PAVEMENT MARKNG		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-760	Material Submittal for Pavement Makings	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-761	Material Approval for Pavement Makings	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
TRAFFIC SIGNS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-763	Material Submittal for Tafficc Signs	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-764	Material Approval for Traficc Signs	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26A	22Apr-26A	$000	$000	$0.00	0.00
IRRGATIONPIPES/PRINKLERS		9300	0%	0%	13 Apr 26	11Jul-26	13 Apr 26A	27Jul-26A	$000	$000	$0.00	-1400
MLTX-02-004EN-766	Material Submittal for Irrigaton Pipes/Sprinkles	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00

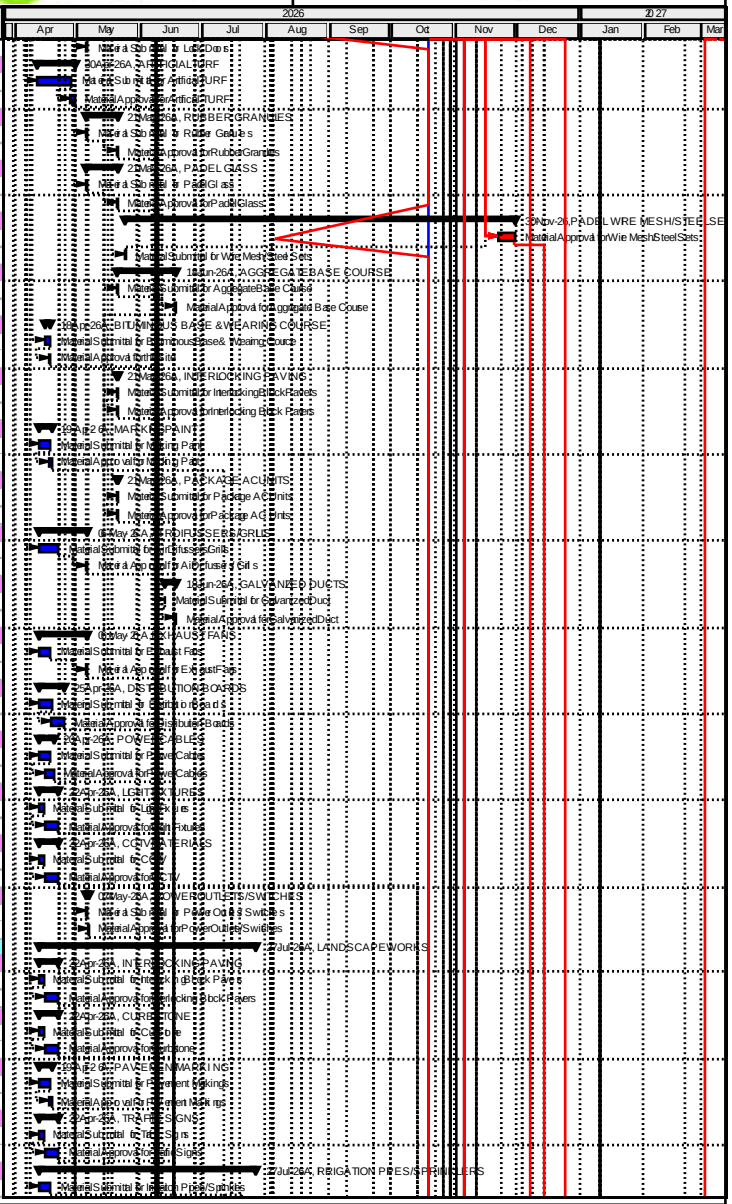

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation


MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

PROFAST

egis

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004EN-767	Material Approval for Irrigation Pipes/Sprinkles	6.00	100%	100%	05 Jul-25	11Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	5.00
AGRICULTURE SOIL		1400	0%	0%	06 May-26	21May-26	06 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-765	Material Submittal for Agriculture Soil	1.00	100%	100%	06 May-26	06May-26	06 May 25 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-770	Material Approval for Agriculture Soil	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		1400	0%	0%	06 May-26	21May-26	06 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-772	Material Submittal for Track Suface	1.00	100%	100%	06 May-26	06May-26	06 May 25 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-773	Material Approval for Track Surface	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
GRASS/TREES		1400	0%	0%	06 May-26	21May-26	06 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-775	Material Submittal for Grass/Trees	1.00	100%	100%	06 May-26	06May-26	06 May 25 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-776	Material Approval for Grass/Trees	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
CABLES		7.00	0%	0%	13 Apr 26	20Apr-26	13 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-778	Material Submittal for Cables	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-779	Material Approval for Cables	4.00	100%	100%	16 Apr 26	20Apr-26	16 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
LIGHTPOLES		2100	0%	0%	13 Apr 26	06May-26	13 Apr 26A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-781	Material Submittal for Lightingpoles	7.00	100%	100%	13 Apr 26	20Apr-26	13 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-782	Material Approval for Lightingpoles	1800	100%	100%	16 Apr 26	06May-26	16 Apr 26A	06May-26A	$000	$000	$0.00	0.00
PROCU REMENT		25100	0%	0%	07 May-26	07Dec-26	07 May 25 A	31Jan-27	$000	$000	$0.00	-4700
SHORTHEAD ITEM		21600	0%	0%	07 May-26	12Oct-26	07 May 25 A	18Jan-27	$000	$000	$0.00	-8400
TOILETSERVICE WORKS		15800	0%	0%	07 May-26	08Aug-26	07 May 25 A	11Nov-26	$000	$000	$0.00	-8100
STEELREINFORCEMENT		2400	0%	0%	13 May-26	13Jun-26	13 May 25 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7880	PO for Steel Reinforcement	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7900	Material Delivery of Steel Reinforcement	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		7000	0%	0%	07 May-26	08Jul-26	07 May 25 A	27Jul-26A	$000	$000	$0.00	-1600
MLTX02-004PR-7950	PO for Concrete Blocks	1.00	100%	100%	07 May-26	07May-26	07 May 25 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7970	Material Delivery of Concrete Blocks	4.00	100%	100%	05 Jul-25	08Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	3.00
FLOORWALL TILES		7100	0%	0%	13 Jul-25	02Aug-26	22 Jul-26A	12Sep-26A	$000	$000	$0.00	-2700
MLTX02-004PR-8030	PO for TilingMaterials	5.00	100%	100%	13 Jul-25	18Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
MLTX02-004PR-8050	Material Delivery of TailingMaterial	1300	100%	100%	19 Jul-25	02Aug-26	12 Sep 25 A	12Sep-26A	$000	$000	$0.00	12.00
SUSPENDED CEILING		8600	0%	0%	19 Jul-25	08Aug-26	22 Jul-26A	10Oct-26A	$000	$000	$0.00	-4900
MLTX02-004PR-8070	PO for Suspend Ceiling	5.00	100%	100%	19 Jul-25	23Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
MLTX02-004PR-8090	Material Delivery of SuspendCeiling	1300	100%	100%	25 Jul-25	08Aug-26	10 Oct26A	10Oct-26A	$000	$000	$0.00	13.00
DOORS/WINDOWS		11200	0%	0%	24 Jun 26	21Jul-26	24 Jun 26A	03Oct-26A	$000	$000	$0.00	-6200
MLTX02-004PR-8110	PO for Doors/Windows	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8130	Material Delivery for Doors/Windows	1500	100%	100%	05 Jul-25	21Jul-26	01 Oct26A	03Oct-26A	$000	$000	$0.00	13.00
WATERSUPPLYPIPES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8230	PO for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8250	Material Delivery for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SEWAGEDRAINAGEPIPES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8270	PO for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8290	Material Delivery for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SANITARYFIXTURES		11700	0%	0%	16 Jun 26	19Jul-26	16 Jun 26A	03Aug-26A	$000	$000	$0.00	-1300
MLTX02-004PR-8190	PO for SanitaryFixtures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8210	Material Delivery for SanitaryFixtues	1300	100%	100%	05 Jul-25	19Jul-26	08 Aug 25 A	03Aug-26A	$000	$000	$0.00	12.00
PACKAGE ACUNITS		12200	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	05Nov-26	$000	$000	$0.00	-9100
MLTX02-004PR-8330	Material Delivery for Package AC Units	1500	100%	0%	05 Jul-25	21Jul-26	20 Oct26	05Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-8310	PO for Package AC Units	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/GRILLS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02-004PR-8350	PO for AirDiffusersGrills	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8370	Material Delivery for AirDiffusersGrills	1500	100%	100%	05 Jul-25	21Jul-26	08 Aug 25 A	08Aug-26A	$000	$000	$0.00	14.00
GALVANIZED D UCTS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02-004PR-8390	PO for GalvanizedDucts	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8410	Material Delivery for GalvanizedDucts	1500	100%	100%	05 Jul-25	21Jul-26	08 Aug 25 A	08Aug-26A	$000	$000	$0.00	14.00
EXHAUSTFANS		11400	0%	0%	16 Jun 26	15Jul-26	16 Jun 26A	17Aug-26A	$000	$000	$0.00	-2800
MLTX02-004PR-8430	PO for Exhaust Fans	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8450	Material Delivery for Exhaust Fans	1000	100%	100%	05 Jul-25	15Jul-26	17 Aug 25 A	17Aug-26A	$000	$000	$0.00	9.00
LIGHTING FIXTURES		11700	0%	0%	16 Jun 26	15Jul-26	16 Jun 26A	31Oct-26	$000	$000	$0.00	-9100
MLTX02-004PR-8490	Material Delivery for LightingFixtures	1000	100%	0%	05 Jul-25	15Jul-26	20 Oct26	31Oct-26	$000	$000	$0.00	0.00
MLTX02-004PR-8470	PO for LightingFixtures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		10700	0%	0%	24 Jun 26	12Jul-26	24 Jun 26A	27Oct-26	$000	$000	$0.00	-9100
MLTX02-004PR-8530	Material Delivery for Switches/Sockets	7.00	100%	0%	05 Jul-25	12Jul-26	20 Oct26	27Oct-26	$000	$000	$0.00	0.00
MLTX02-004PR-8510	PO for Switches/Sockets	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		1.00	0%	0%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8550	PO for EathingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8570	Material Delivery for EarthingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		9100	0%	0%	05 Jul-25	27Jul-26	22 Jul-26A	05Nov-26	$000	$000	$0.00	-7100
MLTX02-004PR-8610	Material Delivery for Distibuton Panels	1500	100%	0%	11 Jul-25	27Jul-26	20 Oct26	05Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-8590	PO for DistributionPanels	5.00	100%	100%	05 Jul-25	09Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00

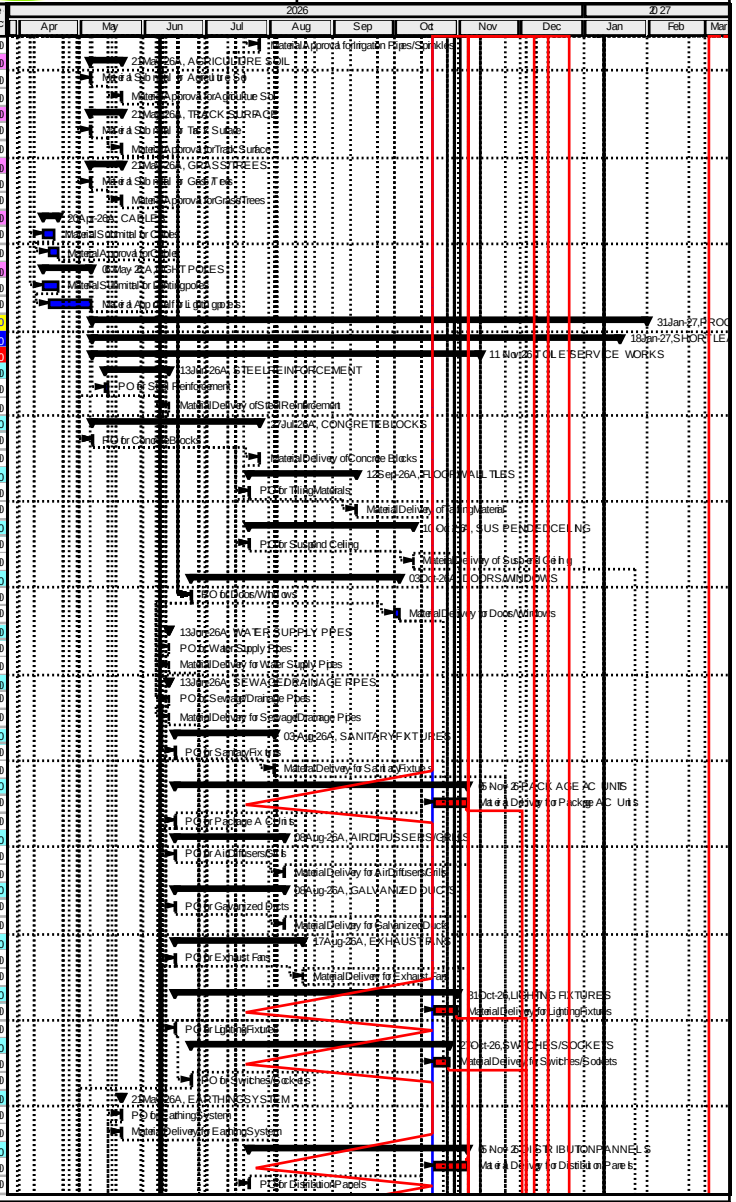


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
	FURNITURES	12700	0%	0%	16 Jun 26	27Jul-26	16 Jun 26A	11Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-8170	Material Delivery for Furnitures	2000	100%	0%	05 Jul-26	27Jul-26	20 Oct 26	11Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8150	PO for Furnitures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	PLAYGROUND WORKS	16800	0%	0%	07 May-26	01Sep-26	07 May 25A	23Nov-26	$000	$000	$0.00	-7000
	PVC MEMBRANE	11100	0%	0%	16 Jun 26	08Jul-26	16 Jun 26A	24Oct-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-8650	Material Delivery for PVC Membrane	4.00	100%	0%	05 Jul-26	08Jul-26	20 Oct 26	24Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8640	PO for PVC Membrane	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	ARTIFICIAL TURF	12300	0%	0%	16 Jun 26	22Jul-26	16 Jun 26A	07Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-8850	Material Delivery for Artificial TURF	1200	100%	0%	09 Jul-26	22Jul-26	25 Oct 26	07Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8830	PO for Artificial TURF	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	RUBBER GRANULES	4300	0%	0%	16 Jun 26	18Jul-26	16 Jun 26A	22Jul-26A	$000	$000	$0.00	-400
MLTX02.00.4PR-8870	PO for Rubber Granules	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8890	Material Delivery for Rubber Granules	1200	100%	100%	05 Jul-26	18Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	11.00
	PADEL GLASS	12500	0%	0%	16 Jun 26	25Jul-26	16 Jun 26A	09Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-8930	Material Delivery for Padel Glass	1800	100%	0%	05 Jul-26	25Jul-26	20 Oct 26	09Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8910	PO for Padel Glass	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	PADEL WIRE MESH/STEEL SETS	12300	0%	0%	16 Jun 26	22Jul-26	16 Jun 26A	07Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-8970	Material Delivery for Wire Mesh/Steel Sets	1600	100%	0%	05 Jul-26	22Jul-26	20 Oct 26	07Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8950	PO for Wire Mesh/Steel Sets	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	AGGREGATE BASE COURSE	1.00	0%	0%	21 May-26	21May-26	21 May 25A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8990	PO for Aggregate Base Course	1.00	100%	100%	21 May-26	21May-26	21 May 25A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9000	Material Delivery for Aggregate Base Course	1.00	100%	100%	21 May-26	21May-26	21 May 25A	21May-26A	$000	$000	$0.00	0.00
	BITUMINOUS BASE &WEARING COURSE	1.00	0%	0%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9020	PO for Bituminous Base & Wearing Course	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9030	Material Delivery for the Site	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	INTERLOCKING PAVING	14500	0%	0%	07 May-26	12Jul-26	07 May 25A	27Oct-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-9070	Material Delivery for Interlocking Block Pavers	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9050	PO for Interlocking Block Pavers	1.00	100%	100%	07 May-26	07May-26	07 May 25A	07May-26A	$000	$000	$0.00	0.00
	MARKING PAINT	8700	0%	0%	05 Jul-26	18Jul-26	18 Jul-26A	27Oct-26	$000	$000	$0.00	-7500
MLTX02.00.4PR-9110	Material Delivery for Marking Paint	7.00	100%	0%	11 Jul-26	18Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9090	PO for Making Paint	5.00	100%	100%	05 Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
	PACKAGE ACUNITS	12200	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	05Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-9150	Material Delivery for Package AC Units	1500	100%	0%	05 Jul-26	21Jul-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9130	PO for Package AC Units	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	AIRDIFUSSERS/ GRILLS	11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02.00.4PR-9170	PO for AirDiffussers/Grills	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9190	Material Delivery for AirDifussers/Grills	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 25A	08Aug-26A	$000	$000	$0.00	14.00
	GALVANIZED D UCTS	11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02.00.4PR-9210	PO for Galvanized Duct	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9230	Material Delivery for Galvanized Duct	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 25A	08Aug-26A	$000	$000	$0.00	14.00
	EXHAUST FANS	11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26A	17Aug-26A	$000	$000	$0.00	-2300
MLTX02.00.4PR-9250	PO for Exhaust Fans	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9270	Material Delivery for Exhaust Fans	1500	100%	100%	05 Jul-26	21Jul-26	17 Aug 25A	17Aug-26A	$000	$000	$0.00	14.00
	DISTRBUTION BOARDS	7500	0%	0%	23 Jul-26	15Aug-26	22 Jul-26A	05Nov-26	$000	$000	$0.00	-7100
MLTX02.00.4PR-9310	Material Delivery for Distibuton Boards	1500	100%	0%	29 Jul-26	15Aug-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9290	PO for DistributionBoards	5.00	100%	100%	23 Jul-26	28Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.00
	POWERCABLES	8600	0%	0%	29 Jul-26	15Aug-26	22 Jul-26A	31Oct-26	$000	$000	$0.00	-7100
MLTX02.00.4PR-9350	Material Delivery for PowerCables	1000	100%	0%	04 Aug-26	15Aug-26	20 Oct 26	31Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9330	PO for PowerCables	5.00	100%	100%	29 Jul-26	03Aug-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
	LIGHTFIXTURES	12300	0%	0%	16 Jun 26	22Jul-26	16 Jun 26A	07Nov-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-9390	Material Delivery for Light Fixtures	1600	100%	0%	05 Jul-26	22Jul-26	20 Oct 26	07Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9370	PO for Light Fixtures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
	CCTV MATERIA IS	3000	0%	0%	12 Jul-26	01Sep-26	20 Oct 26	23Nov-26	$000	$000	$0.00	15.00
MLTX02.00.4PR-9410	PO for CCTV	5.00	100%	0%	12 Jul-26	16Jul-26	20 Oct 26	25Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9430	Material Delivery for CCTV	1500	100%	0%	16 Aug-26	01Sep-26	07 Nov 25	23Nov-26	$000	$000	$0.00	0.00
	POWEROUTLE TS/ SWITCHES	7600	0%	0%	22 Jul-26	15Aug-26	22 Jul-26A	05Nov-26	$000	$000	$0.00	-7000
MLTX02.00.4PR-9470	Material Delivery for PowerOutlets/Switches	1500	100%	0%	29 Jul-26	15Aug-26	20 Oct 26	05Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9450	PO for PowerOutlets/Switches	6.00	100%	100%	22 Jul-26	28Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.00
	LANDSCAPE WORKS	21600	0%	0%	07 May-26	12Oct-26	07 May 25A	18Jan-27	$000	$000	$0.00	-8400
	INTERLOCKING PAVING	18000	0%	0%	07 May-26	15Sep-26	07 May 25A	07Dec-26	$000	$000	$0.00	-7000
MLTX02.00.4PR-9520	Material Delivery for Interlocking Block Pavers	1200	100%	0%	02 Sep-26	15Sep-26	24 Nov 25	07Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9500	PO for Interlocking Block Pavers	1.00	100%	100%	07 May-26	07May-26	07 May 25A	07May-26A	$000	$000	$0.00	0.00
	CURBSTONE	11300	0%	0%	07 May-26	05Aug-26	07 May 25A	12Aug-26A	$000	$000	$0.00	-600
MLTX02.00.4PR-9540	PO for Cubstone	1.00	100%	100%	07 May-26	07May-26	07 May 25A	07May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9560	Material Delivery for Curbstone	1200	100%	100%	23 Jul-26	05Aug-26	12 Aug 25A	12Aug-26A	$000	$000	$0.00	11.00
	PAVEMENT MARKNG	5800	0%	0%	06 Aug-26	23Aug-26	22 Jul-26A	31Oct-26	$000	$000	$0.00	-7100
MLTX02.00.4PR-9600	Material Delivery for Pavement Makings	1000	100%	0%	12 Aug-26	23Aug-26	20 Oct 26	31Oct-26	$000	$000	$0.00	0.00

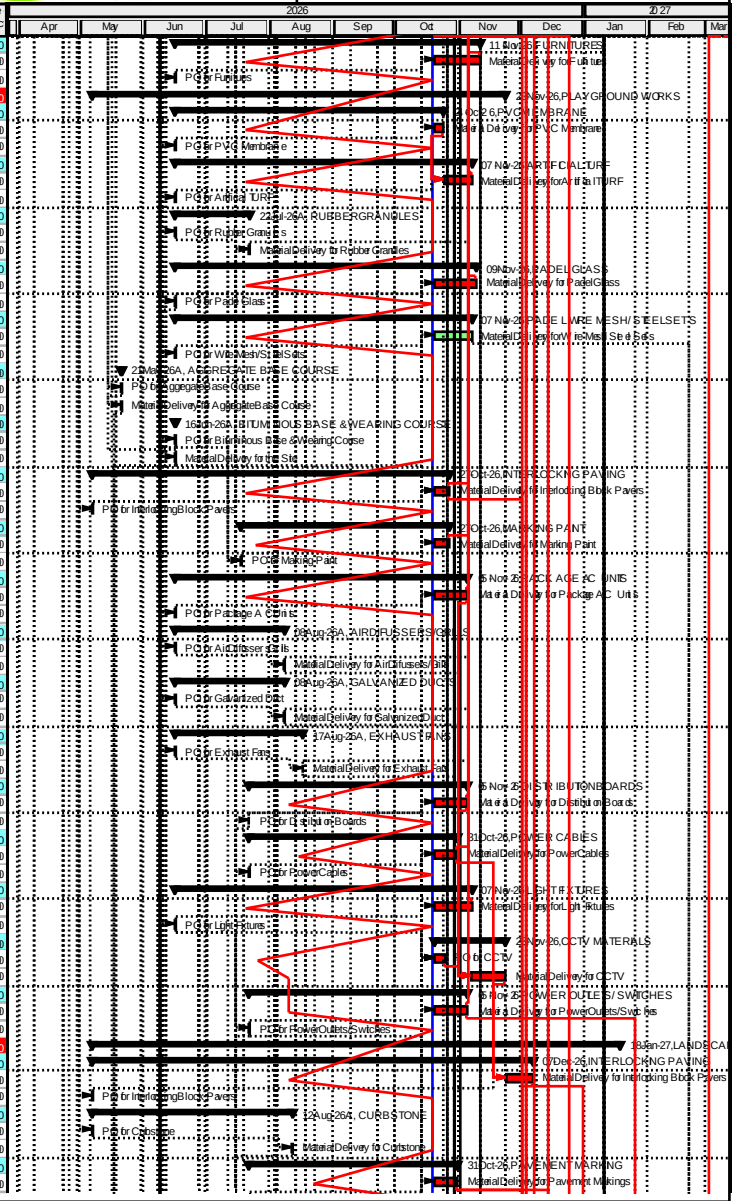


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004PR-9580	PO for Pavement Markings	5.00	100%	100%	06-Aug-26	11-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.00
TRAFFIC SIGNS		1400	0%	0%	16-Sep-26	03-Oct-26	02-Jan-27	17-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-9620	PO for Traffic Signs	5.00	100%	0%	16-Sep-26	21-Sep-26	02-Jan-27	06-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-9640	Material Delivery for Traffic Signs	9.00	100%	0%	22-Sep-26	03-Oct-26	07-Jan-27	17-Jan-27	$000	$000	$0.00	0.00
IRRGATION PIPES&SPRINKLERS		7200	0%	0%	12-Aug-26	26-Aug-26	18-Jul-26A	13-Aug-26A	$000	$000	$0.00	-1100
MLTX02-004PR-9660	PO for Irrigation Pipes/Sprinkles	5.00	100%	100%	12-Aug-26	17-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
MLTX02-004PR-9680	Material Delivery for Irrigation Pipes/Sprinkles	8.00	100%	100%	18-Aug-26	26-Aug-26	13-Aug-26A	13-Aug-26A	$000	$000	$0.00	7.00
AGRICULTURE SOIL		7400	0%	0%	22-Sep-26	12-Oct-26	08-Aug-26A	02-Nov-26	$000	$000	$0.00	-5700
MLTX02-004PR-9720	Material Delivery for Agriculture Soil	1200	100%	0%	29-Sep-26	12-Oct-26	20-Oct-26	02-Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-9700	PO for Agriculture Soil	5.00	100%	100%	22-Sep-26	28-Sep-26	08-Aug-26A	08-Aug-26A	$000	$000	$0.00	4.00
TRACK SURFACE		1500	0%	0%	05-Sep-26	21-Sep-26	21-Dec-26	06-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-9740	PO for Track Suface	5.00	100%	0%	05-Sep-26	09-Sep-26	21-Dec-26	26-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-9760	Material Delivery for Track Surface	1000	100%	0%	10-Sep-26	21-Sep-26	27-Dec-26	06-Jan-27	$000	$000	$0.00	0.00
GRASS/TREES		2000	0%	0%	10-Sep-26	04-Oct-26	27-Dec-26	18-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-9780	PO for Grass/Trees	5.00	100%	0%	10-Sep-26	15-Sep-26	27-Dec-26	31-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-9800	Material Delivery for Grass/Trees	1500	100%	0%	16-Sep-26	04-Oct-26	02-Jan-27	18-Jan-27	$000	$000	$0.00	0.00
CABLES		2000	0%	0%	12-Aug-26	03-Sep-26	28-Sep-26A	28-Sep-26A	$000	$000	$0.00	19.00
MLTX02-004PR-9820	PO for Cables	5.00	100%	100%	12-Aug-26	17-Aug-26	28-Sep-26A	28-Sep-26A	$000	$000	$0.00	4.00
MLTX02-004PR-9840	Material Delivery for Cables	1500	100%	100%	18-Aug-26	03-Sep-26	28-Sep-26A	28-Sep-26A	$000	$000	$0.00	14.00
LONG LEAD ITEM		22000	0%	0%	16-Jun-26	07-Dec-26	16-Jun-26A	31-Jan-27	$000	$000	$0.00	-4700
PLAYGROUND WORKS		19600	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26A	31-Jan-27	$000	$000	$0.00	-9100
STEELTENSION CABLES		19600	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26A	31-Jan-27	$000	$000	$0.00	-9100
MLTX02-004PR-8690	Material Delivery for Steel Tension Cables	2900	100%	0%	05-Sep-26	08-Oct-26	21-Dec-26	23-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-8680	Material Fabrication for Steel Tension Cables	2000	100%	0%	29-Jul-26	20-Aug-26	20-Oct-26	11-Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-9890	Staging time	7.00	100%	0%	10-Oct-26	17-Oct-26	24-Jan-27	31-Jan-27	$000	$000	$0.00	0.00
MLTX02-004PR-8670	PO for Steel Tension Cables	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		16000	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	20-Dec-26	$000	$000	$0.00	-9100
MLTX02-004PR-8730	Material Delivery for Emergency Doors	2500	100%	0%	28-Jul-26	25-Aug-26	12-Nov-26	10-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8720	Material Fabrication for Emergency Doors	2000	100%	0%	05-Jul-26	27-Jul-26	20-Oct-26	11-Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-9900	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	12-Dec-26	20-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8710	PO for Emegency Doors	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		16000	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	20-Dec-26	$000	$000	$0.00	-9100
MLTX02-004PR-8770	Material Delivery for Pressure Units	2500	100%	0%	28-Jul-26	25-Aug-26	12-Nov-26	10-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8760	Material Fabrication for Pressue Units	2000	100%	0%	05-Jul-26	27-Jul-26	20-Oct-26	11-Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-9910	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	12-Dec-26	20-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8750	PO for PressureUnits	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		16000	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	20-Dec-26	$000	$000	$0.00	-9100
MLTX02-004PR-8810	Material Delivery for LockDoors	2500	100%	0%	28-Jul-26	25-Aug-26	12-Nov-26	10-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8800	Material Fabrication for Lock Doors	2000	100%	0%	05-Jul-26	27-Jul-26	20-Oct-26	11-Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-9920	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	12-Dec-26	20-Dec-26	$000	$000	$0.00	0.00
MLTX02-004PR-8790	PO for Lock Doors	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		21800	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26A	29-Sep-26A	$000	$000	$0.00	59.00
LIGHTPOLES		21800	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26A	29-Sep-26A	$000	$000	$0.00	59.00
MLTX02-004PR-9860	PO for Lightingpoles	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-9870	Material Fabrication for Lighting poles	3000	9333%	100%	16-Sep-26	21-Oct-26	29-Sep-26A	29-Sep-26A	$000	$000	$0.00	29.00
MLTX02-004PR-9880	Material Delivery for Lightingpoles	2500	0%	100%	22-Oct-26	19-Nov-26	29-Sep-26A	29-Sep-26A	$000	$000	$0.00	24.00
MLTX02-004PR-9930	Staging time	1500	0%	100%	21-Nov-26	07-Dec-26	29-Sep-26A	29-Sep-26A	$000	$000	$0.00	14.00
CONSTR UCTION PHASE		29000	2896%	3828%	27-Apr-26	24-Jan-27	27-Apr-26A	08-Apr-27	$3063.2766	$4049.39923	$10578.073.00	-6000
SITEWORKS		29000	21.1%	378%	27-Apr-26	24-Jan-27	27-Apr-26A	08-Apr-27	$1972.3713.2	$3533.31532	$9.346.3.715.4	-6000
EARTH WORKS		8907	100%	100%	27-Apr-26	09-Aug-26	27-Apr-26A	12-Aug-26A	$1.855.455.71	$487.645.71	$4.876.45.71	-296
MLTX-02-004CN-9930	Excavation(inall types of soil) including Compaction(PlaygroundArea)	1275	100%	100%	27-Apr-26	11-May-26	27-Apr-26A	11-May-26A	$1.014.00.00	$101.400.00	$1.014.00.00	0.00
MLTX-02-004CN-9940	Excavation(inall types of soil) including Compaction(Service/ToiletBuilding)	805	100%	100%	06-May-26	16-May-26	06-May-26A	16-May-26A	$323.21.25	$323.21.25	$323.21.25	0.00
MLTX-02-004CN-9950	Excavation(inall types of soil) including Compaction(Landscape Area)	1735	100%	100%	29-Apr-26	19-May-26	29-Apr-26A	19-May-26A	$2.093.27.63	$209.327.63	$2.093.27.63	0.00
MLTX-02-004CN-9960	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	2040	100%	100%	17-May-26	13-Jun-26	17-May-26A	13-Jun-26A	$6.142.5.00	$6.142.5.00	$61.425.00	0.00
MLTX-02-004CN-9970	Backfilling onLayers(Selected Soil)including Compaction (Service/ToiletBuilding)	1780	100%	100%	17-May-26	09-Jun-26	17-May-26A	09-Jun-26A	$1.706.2.50	$1.706.2.50	$17.062.50	0.00
MLTX-02-004CN-9980	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)	2300	100%	100%	08-Jun-26	04-Jul-26	08-Jun-26A	04-Jul-26A	$2.985.9.38	$2.985.9.38	$29.859.38	0.00
MLTX-02-004CN-9980R	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)Remain	3007	100%	100%	05-Jul-26	09-Aug-26	04-Jul-26A	12-Aug-26A	$3.624.9.95	$3.628.9.95	$36249.96	-396
LANDSCAPE WORKS		26800	1676%	3438%	23-May-26	24-Jan-27	23-May-26A	08-Apr-27	$1484.7256.0	$3045.66961	$8.858.7.258.3	-6000
PLAYGROUND AREA		25400	3725%	4677%	23-May-26	04-Jan-27	23-May-26A	23-Mar-27	$1.248.85.00	$532886.25	$1.139.2.550.0	-6300
FOOTBALLPLAYGROUND		24400	20%	20%	23-May-26	13-Dec-26	23-May-26A	08-Mar-27	$5.752.5.00	$5.752.5.00	$52.876.25.00	-7200
MLTX-02-004CN-1000	Finishingand SufaceFinish Works (Football Playground)	3000	0%	0%	29-Oct-26	02-Dec-26	20-Oct-26	23-Nov-26	$000	$000	$1.488.12.50	0.00
MLTX-02-004CN-1010	InstallSportEquipments -Goal /Nets- Football Playground	9.00	0%	0%	03-Dec-26	13-Dec-26	27-Feb-27	08-Mar-27	$000	$000	$71906.25	0.00
MLTX-02-004CN-1020	Surface Makingand Painting(FootballPlayground)	8.00	0%	0%	03-Dec-26	12-Dec-26	27-Feb-27	07-Mar-27	$000	$000	$143811.25	0.00
MLTX-02-004CN-1030	Preparation andProofing for Subgrade (Football Playground)	1.20	100%	100%	23-May-26	24-May-26	23-May-26A	24-May-26A	$2.876.2.50	$2.876.2.50	$28762.50	0.00
MLTX-02-004CN-1040	Backfilling andCompacton ofBaseLayers(FootballPlayground)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26A	04-Jul-26A	$2.444.8.13	$2.444.8.13	$24448.13	0.00
MLTX-02-004CN-1050	Backfilling andCompacton ofBaseLayers(FootballPlayground)Remaining	3000	100%	100%	05-Jul-26	08-Aug-26	20-Jul-26A	31-Aug-26A	$4.314.38	$4314.38	$4.314.38	-670
PADEL PLAYGROUND		24500	5%	80%	23-May-26	14-Dec-26	23-May-26A	09-Mar-27	$1.179.75.00	$171600.00	$2.165.0.00.00	-7200

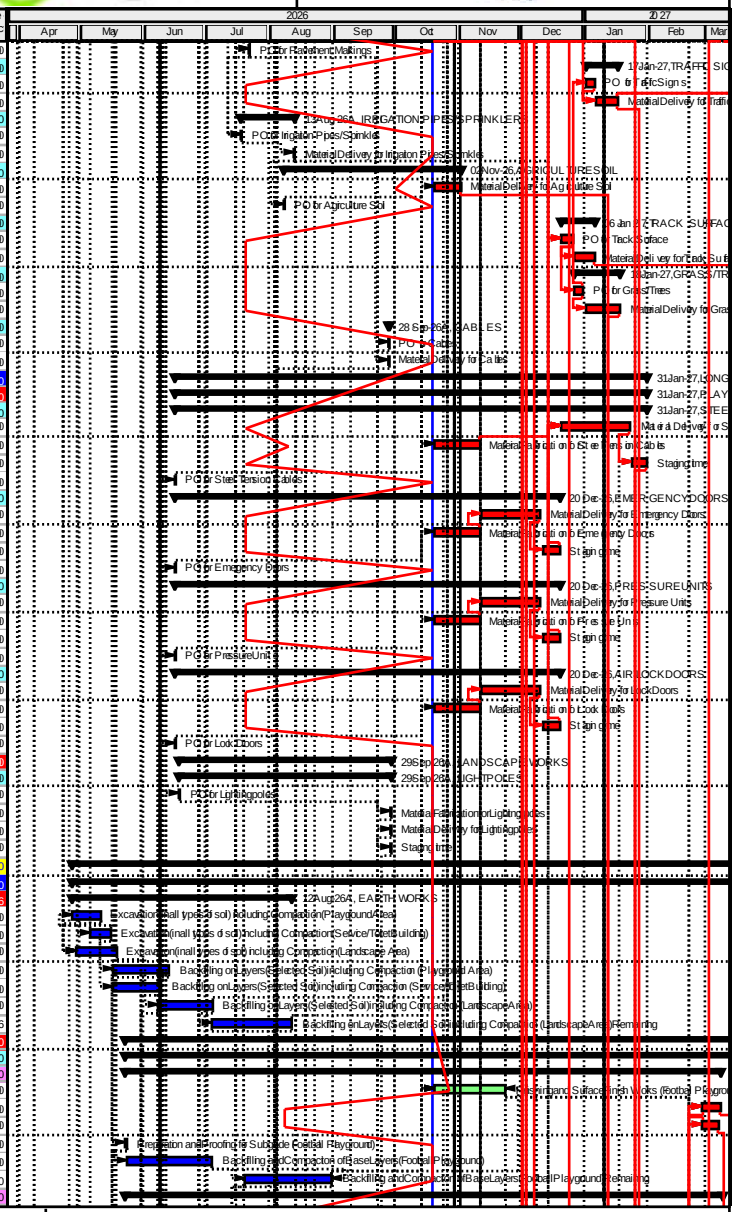

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004CN-101	Install Sport Equipments -Goal /Nets- Padel Playground)	1000	0%	0%	03-Dec-26	14-Dec-26	27-Feb-27	09-Mar-27	$000	$000	$32175.00	0.00
MLTX-02-004CN-101	Surface Makingand Painting(Padel Playground)	8.00	0%	0%	03-Dec-26	12-Dec-26	01-Mar-27	09-Mar-27	$000	$000	$10725.00	0.00
MLTX-02-004CN-100	Preparation and Proofing for Subgrade Padel Playground)	1.00	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$7507.50	$7507.50	$75075.00	0.00
MLTX-02-004CN-101	Backfilling and Compacton of Base Layers (Padel Playground)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26A	04-Jul-26A	$37537.50	$37537.50	$37537.50	0.00
MLTX-02-004CN-101	Finishing and Suface Finish Works (Padel Playground)	3000	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26A	16-Sep-26A	$000	$53625.00	$53625.00	29.00
MLTX-02-004CN-100	Backfilling and Compacton of Base Layers (Padel Playground) Remaining	3000	100%	100%	09-Aug-26	12-Sep-26	20-Jul-26A	09-Aug-26A	$5362.50	$5362.50	$5362.50	12.00
BASKETBALL PLAYGROUND		25400	1995%	6998%	23-May-26	20-Dec-26	23-May-26A	23-Mar-27	$62205.00	$218205.00	$31185.00	-7600
MLTX-02-004CN-102	Install Sport Equipments -Goal /Nets- (Basketball Playground)	1500	0%	0%	03-Dec-26	20-Dec-26	27-Feb-27	18-Mar-27	$000	$000	$78000.00	0.00
MLTX-02-004CN-102	Surface Makingand Painting(Basketball Playground)	7.00	0%	0%	13-Dec-26	20-Dec-26	16-Mar-27	23-Mar-27	$000	$000	$15600.00	0.00
MLTX-02-004CN-101	Backfilling and Compacton Subgrade(Basketball Playground)	0.60	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$31200.00	$31200.00	$31200.00	0.00
MLTX-02-004CN-101	Backfilling and Compacton of Base Layers (Basketball Playground)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26A	04-Jul-26A	$27495.00	$27495.00	$27495.00	0.00
MLTX-02-004CN-102	Finishing and Suface Finish Works (Basketball Playground)	3000	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26A	16-Sep-26A	$000	$156000.00	$156000.00	28.00
MLTX-02-004CN-101	Backfilling and Compacton of Base Layers (Basketball Playground) Remaining	3000	100%	100%	13-Sep-26	18-Oct-26	20-Jul-26A	09-Aug-26A	$3510.00	$3510.00	$3510.00	12.00
PADEL FENCE		16900	0%	35%	21-Dec-26	04-Jan-27	16-Aug-26A	11-Nov-26	$000	$29006.25	$82875.00	-6200
MLTX-02-004CN-102	Tempered Glass Fenc Installaton and Fixation	2.00	0%	0%	31-Dec-26	02-Jan-27	08-Nov-26	09-Nov-26	$000	$000	$33150.00	0.00
MLTX-02-004CN-102	Chain Link Fence Installation and Fixation	2.00	0%	0%	03-Jan-27	04-Jan-27	10-Nov-26	11-Nov-26	$000	$000	$16575.00	0.00
MLTX-02-004CN-102	Install of Fence Gates	2.00	0%	0%	03-Jan-27	04-Jan-27	10-Nov-26	11-Nov-26	$000	$000	$4143.75	0.00
MLTX-02-004CN-102	Excavation for Fence	5.00	0%	100%	21-Dec-26	26-Dec-26	16-Aug-26A	16-Aug-26A	$000	$8287.50	$8287.50	4.00
MLTX-02-004CN-102	Concrete Foundation for Fence including Posts Fixation	5.00	0%	100%	21-Dec-26	26-Dec-26	25-Aug-26A	01-Sep-26A	$000	$16575.00	$16575.00	-2.00
MLTX-02-004CN-102	Backfilling and Reinstatement for Concrete Foundation	4.00	0%	100%	27-Dec-26	30-Dec-26	08-Oct-26A	08-Oct-26A	$000	$4143.75	$4143.75	3.00
CURBSTONE/INTERLOCK		9596	77%	2332%	23-Aug-26	22-Oct-26	10-Aug-26A	19-Dec-26	$1866.80	$6655.00	$2424.50	-5996
MLTX-02-004CN-101	Interlock Installaton (Grey Scale) for Land Scape (Including Finishing Works)	1000	70%	0%	12-Oct-26	22-Oct-26	08-Dec-26	19-Dec-26	$1301.30	$000	$1859.00	0.00
MLTX-02-004CN-101	Concrete Works Under Cubstone	1500	100%	100%	23-Aug-26	08-Sep-26	10-Aug-26A	10-Aug-26A	$19987.50	$19987.50	$19987.50	15.00
MLTX-02-004CN-101	Curbstone Instalation	4.00	100%	100%	07-Oct-26	11-Oct-26	11-Aug-26A	16-Aug-26A	$3656.25	$3656.25	$36562.50	-100
AIRDOME		24200	1344%	264%	16-Jun-26	31-Dec-26	16-Jun-26A	30-Mar-27	$7534.32.94	$1480,05000	$5696.25.00	-7200
CIVL WORKS		21000	32%	5238%	16-Jun-26	24-Nov-26	16-Jun-26A	16-Feb-27	$7534.32.94	$1233,37500	$2354.62.50	-7200
MLTX-02-004CN-103	Install of Membane Covering System (Air Dome)	1400	0%	0%	09-Nov-26	24-Nov-26	01-Feb-27	16-Feb-27	$000	$000	$5606.25.00	0.00
MLTX-02-004CN-103	Themal Insulaton Works (Air Dome)	1400	0%	0%	09-Nov-26	24-Nov-26	01-Feb-27	16-Feb-27	$000	$000	$5606.25.00	0.00
MLTX-02-004CN-103	Excavation for Foundaton & Playgound Aea (Air Dome)	1150	100%	100%	16-Jun-26	29-Jun-26	16-Jun-26A	29-Jun-26A	$2803.12.50	$2803.12.50	$2803.12.50	0.00
MLTX-02-004CN-103	Concrete Works for Roundations including Anchor Bolts (Air Dome)	2600	100%	100%	23-Jul-26	22-Aug-26	11-Jul-26A	22-Sep-26A	$3924.37.50	$3924.37.50	$3924.37.50	-3744
MLTX-02-004CN-103	Cable System Installaton (Air Dome)	1000	20%	100%	18-Oct-26	28-Oct-26	24-Sep-26A	12-Oct-26A	$3682.29	$560625.00	$5606.25.00	-600
MECHANICAL WORKS		1300	0%	0%	25-Nov-26	09-Dec-26	17-Feb-27	04-Mar-27	$000	$000	$1121.25.00	0.00
MLTX-02-004CN-104	Air Ducts and Grills Installaton (Air Dome)	1000	0%	0%	25-Nov-26	06-Dec-26	17-Feb-27	01-Mar-27	$000	$000	$2803.12.50	0.00
MLTX-02-004CN-104	Air Units Installaton (Air Dome)	1300	0%	0%	25-Nov-26	09-Dec-26	17-Feb-27	04-Mar-27	$000	$000	$4485.00.00	0.00
MLTX-02-004CN-104	Exhaust Fans and Ducts Instalation (Air Dome)	7.00	0%	0%	25-Nov-26	02-Dec-26	17-Feb-27	25-Feb-27	$000	$000	$3924.37.50	0.00
EIECTRICAL WORKS		2600	0%	1467%	10-Dec-26	31-Dec-26	07-Oct-26A	30-Mar-27	$000	$246675.00	$1681.81.8.750	-127.00
MLTX-02-004CN-104	Distibution Board and Elecitical Works (Air Dome)	3.00	0%	0%	15-Dec-26	17-Dec-26	06-Mar-27	08-Mar-27	$000	$000	$2803.12.50	0.00
MLTX-02-004CN-104	External Elecitical Connection Works (Air Dome)	4.00	0%	0%	19-Dec-26	22-Dec-26	09-Mar-27	16-Mar-27	$000	$000	$2803.12.50	0.00
MLTX-02-004CN-104	Emergency Generator Installaton (Air Dome)	4.00	0%	0%	23-Dec-26	27-Dec-26	17-Mar-27	21-Mar-27	$000	$000	$5606.25.00	0.00
MLTX-02-004CN-104	Contol System Installaition (Air Dome)	4.00	0%	0%	28-Dec-26	31-Dec-26	27-Mar-27	30-Mar-27	$000	$000	$2803.12.50	0.00
MLTX-02-004CN-104	Light Fixture Works (Air Dome)	4.00	0%	88%	10-Dec-26	14-Dec-26	07-Oct-26A	04-Mar-27	$000	$246675.00	$2803.12.50	-123.00
FINISHES WORKS		1500	0%	0%	10-Dec-26	27-Dec-26	06-Mar-27	25-Mar-27	$000	$000	$4485.00.00	0.00
MLTX-02-004CN-103	Doos Installaton Including Emegency, Entrance doors (Air Dome)	6.00	0%	0%	10-Dec-26	16-Dec-26	06-Mar-27	15-Mar-27	$000	$000	$2242.50.00	0.00
MLTX-02-004CN-103	Logoand Signs Installaition (Air Dome)	9.00	0%	0%	17-Dec-26	27-Dec-26	16-Mar-27	25-Mar-27	$000	$000	$2242.50.00	0.00
IRRGATION NETWORK		10300	6118%	8203%	12-Oct-26	04-Nov-26	20-Aug-26A	21-Jan-27	$1887.84.38	$253142.50	$3085.87.50	-111.00
MLTX-02-004CN-11460	Installing of Bubblers and Sprayers	3.00	0%	0%	02-Nov-26	04-Nov-26	19-Jan-27	21-Jan-27	$000	$000	$46150.00	0.00
MLTX-02-004CN-11450	Installing of Valves and fittings for Irigation Network	4.00	0%	80%	21-Oct-26	25-Oct-26	24-Sep-26A	14-Dec-26	$000	$9738.00	$46475.00	-6600
MLTX-02-004CN-11430	Installing of HDPE Pipes for Irrigation Network (Main Line)	4.00	100%	100%	12-Oct-26	15-Oct-26	20-Aug-26A	29-Aug-26A	$107250.00	$107250.00	$107250.00	-400
MLTX-02-004CN-11440	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	4.00	75%	100%	17-Oct-26	20-Oct-26	29-Aug-26A	31-Aug-26A	$8153.43.8	$108712.50	$10807.12.50	2.00
NATURAL GROUND		6.00	0%	0%	26-Oct-26	01-Nov-26	20-Dec-26	26-Dec-26	$000	$000	$80291.25	0.00
MLTX-02-004CN-10550	Compacted Natural Ground Soil Installaton Works for Landscape	6.00	0%	0%	26-Oct-26	01-Nov-26	20-Dec-26	26-Dec-26	$000	$000	$80291.25	0.00
PLANTING		4000	0%	6.28%	05-Nov-26	13-Dec-26	13-Oct-26A	08-Mar-27	$000	$9728.40.00	$5978.37.50	-9200
MLTX-02-004CN-10580	Placement of Lawn Ground Cover (Rolling and Compacton)	3.00	0%	0%	10-Dec-26	13-Dec-26	06-Mar-27	08-Mar-27	$000	$000	$1751.75.00	0.00
MLTX-02-004CN-10590	Placement and Fixation of Trees	3.00	0%	0%	07-Dec-26	09-Dec-26	02-Mar-27	04-Mar-27	$000	$000	$2362.42.50	0.00
MLTX-02-004CN-10570	Placement of Sweet Agricultural Soil (Including Levelling and Grading)	3.00	20%	0%	05-Nov-26	08-Nov-26	13-Oct-26A	21-Jan-27	$000	$9728.40.00	$1864.20.00	-8400
WALKNG/BIKE PATHS		1200	50%	50%	14-Dec-26	27-Dec-26	11-Aug-26A	08-Mar-27	$000	$138206.39	$2764.12.77	-166.00
MLTX-02-004CN-10510	Bike Path Preparation and Installation Works	1200	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26A	08-Mar-27	$000	$71022.68	$1420.45.36	-166.00
MLTX-02-004CN-10520	Walking Path Preparaton and Installaion Works	1200	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26A	08-Mar-27	$000	$67183.70	$1343.67.41	-166.00
GENERAL/FURNITURE		14000	139%	7106%	12-Oct-26	24-Jan-27	29-Sep-26A	08-Apr-27	$1181.23.69	$604100.47	$8501.91.81	-7100
MLTX-02-004CN-10610	Stamped Concete Works for land Scape (Including Finishing Works)	9.00	0%	0%	28-Dec-26	06-Jan-27	09-Mar-27	22-Mar-27	$000	$000	$42068.52	0.00
MLTX-02-004CN-10630	Fixation and Installtion of Steel Rame for Benches	7.00	0%	0%	28-Dec-26	04-Jan-27	09-Mar-27	20-Mar-27	$000	$000	$17276.02	0.00
MLTX-02-004CN-10640	Fixation and Installtion of Benches	7.00	0%	0%	05-Jan-27	12-Jan-27	21-Mar-27	28-Mar-27	$000	$000	$40310.73	0.00
MLTX-02-004CN-10650	Fixation and Installtion of Precast Concrete Seats (Rectangular)	7.00	0%	0%	05-Jan-27	12-Jan-27	21-Mar-27	28-Mar-27	$000	$000	$43680.00	0.00
MLTX-02-004CN-10660	Fixation and Installtion of Precast Concrete Seats (Circular)	8.00	0%	0%	05-Jan-27	13-Jan-27	21-Mar-27	29-Mar-27	$000	$000	$17160.00	0.00
MLTX-02-004CN-10670	Fixation and Installtion of Precast Concrete Trash Bins	9.00	0%	0%	14-Jan-27	24-Jan-27	30-Mar-27	08-Apr-27	$000	$000	$14625.00	0.00
MLTX-02-004CN-11800	Installing of Site Light Poles	1100	0%	85%	07-Jan-27	19-Jan-27	01-Oct-26A	22-Mar-27	$000	$401602.72	$4724.73.79	-133.00

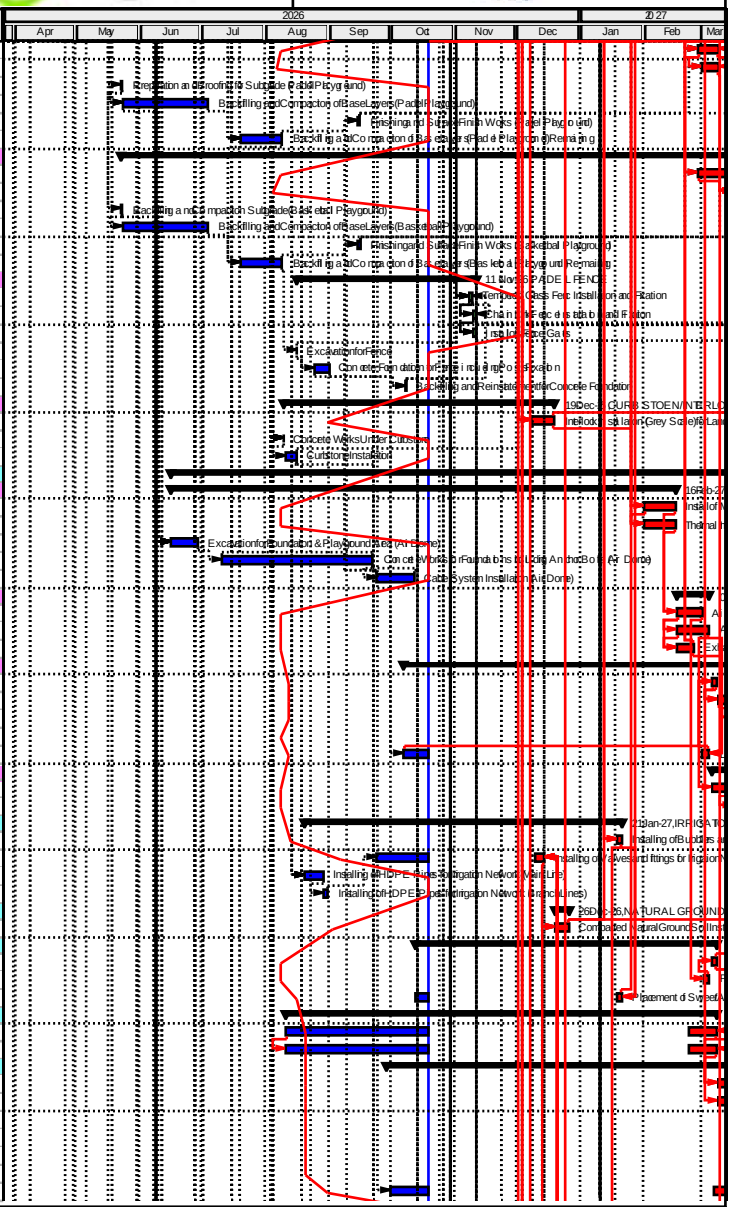

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02004CN-11710	Preliminary Works forSiteLightPoles IncludingCableand Bases Works	1200	5833%	100%	12 Oct 26	25Oct-26	29 Sep 25 A	01Oct-26A	$1,181,236.65	$202497.75	$2,024,97.75	9.00
TOILETSERVICE BULDING		17484	8857%	419%	06 Jun 26	02Nov-26	06 Jun 26 A	27Dec-26	$1090,905.15	$516083.91	$1,231,7,015.4	-4700
STRUCTUREWORKS		6084	100%	100%	06 Jun 26	18Aug-26	06 Jun 26 A	26Jul-26A	$1,580,21.65	$158021.65	$1,580,2.65	20.00
CONCRETE WORKS		5360	100%	100%	14 Jun 26	18Aug-26	14 Jun 26 A	26Jul-26A	$1,137,82.50	$113782.50	$1,137,82.50	20.00
SUB-STRUCTURE		840	100%	100%	14 Jun 26	23Jun-26	14 Jun 26 A	23Jun-26A	$33,345.00	$33,345.00	$33345.00	0.00
MLTX02004CN-107	Plain Concrete Under Footing	220	100%	100%	14 Jun 26	16Jun-26	14 Jun 26 A	16Jun-26A	$1,170.00	$1,170.00	$1,170.00	0.00
MLTX02004CN-108	ReinforcedConcrete Works for Slab onGrade Including Steel Fixing	720	100%	100%	15 Jun 26	23Jun-26	15 Jun 26 A	23Jun-26A	$32,175.00	$32,175.00	$32175.00	0.00
SUPER-STRUCTURE		1900	100%	100%	15 Jul-26	18Aug-26	22 Jul-26A	26Jul-26A	$8,043.75	$8,043.75	$80437.50	26.00
MLTX02004CN-109	AAC Panels Works for Walls	1200	100%	100%	15 Jul-26	28Jul-26	22 Jul-26A	23Jul-26A	$4,826.25	$4,826.25	$48262.50	10.00
MLTX02004CN-109	Parpet Works and Lintels	800	100%	100%	10 Aug-26	18Aug-26	26 Jul-26A	26Jul-26A	$1,608.75	$1,608.75	$16087.50	7.00
MLTX02004CN-109	AAC Panels Works for Slabs	1000	100%	100%	29 Jul-26	09Aug-26	23 Jul-26A	26Jul-26A	$1,608.75	$1,608.75	$16087.50	7.00
UNDER GROUNDSEPTIC TANK		1810	100%	100%	06 Jun 26	27Jun-26	06 Jun 26 A	27Jun-26A	$33,393.00	$33,393.00	$33930.00	0.00
MLTX02004CN-10860	Plain Concrete Under Footing	400	100%	100%	06 Jun 26	10Jun-26	06 Jun 26 A	10Jun-26A	$1,170.00	$1,170.00	$1,170.00	0.00
MLTX02004CN-10890	ReinforcedConcrete Works for Tank SlabIncludingShutteing and Steel Fixing	460	100%	100%	22 Jun 26	27Jun-26	22 Jun 26 A	27Jun-26A	$8,775.00	$8,775.00	$8,775.00	0.00
MLTX02004CN-10870	ReinforcedConcrete Works for Tank FountationIncludingShutteing and Steel Fixing	860	100%	100%	10 Jun 26	20Jun-26	10 Jun 26 A	20Jun-26A	$7,605.00	$7,605.00	$7,605.00	0.00
MLTX02004CN-10880	ReinforcedConcrete Works for Tank Walls including Steel Fixing	380	100%	100%	17 Jun 26	21Jun-26	17 Jun 26 A	21Jun-26A	$1,638.00	$1,638.00	$16380.00	0.00
THERMAL& MOISTERPROTECTION		4684	100%	100%	06 Jun 26	18Jul-26	06 Jun 26 A	22Jul-26A	$1,080,916	$1,080,916	$10309.16	-330
ANTITERMITCONTROL		2024	100%	100%	06 Jun 26	29Jun-26	06 Jun 26 A	29Jun-26A	$4,387.50	$4,387.50	$4,387.50	0.00
MLTX02004CN-109	AntiTermite Works Under Faundation	7.31	100%	100%	06 Jun 26	14Jun-26	06 Jun 26 A	14Jun-26A	$1,755.00	$1,755.00	$1,755.00	0.00
MLTX02004CN-109	AntiTermite Works Under Slab onGradeand Grade Beams	5.40	100%	100%	23 Jun 26	29Jun-26	23 Jun 26 A	29Jun-26A	$2,632.50	$2,632.50	$2,632.50	0.00
POLYETHYLENESHEET		2064	100%	100%	06 Jun 26	29Jun-26	06 Jun 26 A	29Jun-26A	$2,193.75	$2,193.75	$2,193.75	0.00
MLTX02004CN-109	Water Proofing Under Blinding Concrete(PolyhelenSheet)	7.31	100%	100%	06 Jun 26	14Jun-26	06 Jun 26 A	14Jun-26A	$877.50	$877.50	$8,775.00	0.00
MLTX02004CN-109	Water Proofing Under Slab on Grade (Polythelen Sheet)	5.80	100%	100%	23 Jun 26	29Jun-26	23 Jun 26 A	29Jun-26A	$1,316.25	$1,316.25	$1,316.25	0.00
EPOXY		1300	100%	100%	05 Jul-26	18Jul-26	14 Jul-26A	22Jul-26A	$3,727.91	$3,727.91	$3,727.91	4.70
MLTX02004CN-111	Surface Preparation for Epoxy Coating	5.00	100%	100%	05 Jul-26	09Jul-26	14 Jul-26A	21Jul-26A	$1,168.54	$1,168.54	$1,168.54	-150
MLTX02004CN-111	EpoxyCoating forWalls andSlabof Tank	7.00	100%	100%	11 Jul-26	18Jul-26	21 Jul-26A	22Jul-26A	$2,559.38	$2,559.38	$2,559.38	5.70
MASONARY WORK		5.00	100%	100%	09 Jul-26	14Jul-26	26 Jul-26A	28Jul-26A	$1,228.50	$1,228.50	$12285.00	2.00
MLTX02004CN-11030	CMU MasonaryWorksIncluding all Accessories	5.00	100%	100%	09 Jul-26	14Jul-26	26 Jul-26A	28Jul-26A	$1,238.50	$1,228.50	$12285.00	2.00
THERMAL& MOISTER PROTECTION		2100	100%	9393%	23 Aug-26	15Sep-26	26 Sep 25 A	21Oct-26	$34,700.25	$9,259.425	$34700.25	-200
MLTX02004CN-11150	PreparingSurface andPreliminaryWorksforToilets Waterpoofing	2.00	100%	0%	23 Aug-26	24Aug-26	20 Oct 26	21Oct-26	$2,106.00	$000	$2,106.00	0.00
MLTX02004CN-11170	FinalizeWaterProofing Worksfor Toilets	6.00	100%	100%	25 Aug-26	31Aug-26	06 Oct 26 A	10Oct-26A	$4,914.00	$4914.00	$4,914.00	2.00
MLTX02004CN-11160	PreparingSurface andPreliminaryWorksforRoofing andWet Areas Insulaton	5.00	100%	100%	01 Sep-26	06Sep-26	26 Sep 25 A	26Sep-26A	$11,072.10	$1,107.210	$11,072.10	4.00
MLTX02004CN-11180	FinalizeWaterProofing Worksfor Roofingand Wet Areas	8.00	100%	100%	07 Sep-26	15Sep-26	27 Sep 25 A	17Oct-26A	$1,660.815	$1,660.815	$16608.15	-1000
MECHANICALWORK		8600	9924%	2725%	01 Sep-26	20Oct-26	04 Jul-26A	14Dec-26	$8,818,288.88	$104832.00	$3,867,51.88	-9800
HVAC SYSTEM		6900	9126%	3357%	15 Sep-26	20Oct-26	10 Aug 25 A	14Dec-26	$2,594,750	$9360.00	$27885.00	-7800
MLTX02004CN-11500	Installand FinishHVAC and VentilationWorksIncludingSplitAir Units	6.00	8333%	0%	14 Oct 26	20Oct-26	08 Dec 25	14Dec-26	$1,218,750	$000	$14625.00	0.00
MLTX02004CN-11490	Exhaust, Air Ducts Installationwithall Accessories	8.00	100%	0%	19 Sep-26	28Sep-26	20 Oct 26	28Oct-26	$3,900.00	$000	$3,900.00	0.00
MLTX02004CN-11480	Preliminay HVAC and Ventilation Works	3.00	100%	100%	15 Sep-26	17Sep-26	10 Aug 25 A	10Aug-26A	$9,360.00	$9360.00	$9,360.00	2.00
WATERSUPPLYSYSTEM		7500	100%	3.25%	03 Sep-26	10Oct-26	04 Jul-26A	03Dec-26	$2,124,27.50	$6922.50	$2,124,27.50	-100.0
MLTX02004CN-11530	Installing ofHDPE Pipes andValvesforWaterSupplyNetwok	3.00	100%	0%	09 Sep-26	12Sep-26	25 Oct 26	27Oct-26	$3,900.00	$000	$39000.00	0.00
MLTX02004CN-11550	Installing ofBooster PumpUnitsIncluding fittings and accessories	7.00	100%	0%	29 Sep-26	06Oct-26	01 Nov 26	08Nov-26	$51,000.00	$000	$51000.00	0.00
MLTX02004CN-11560	Installing ofGRP Tanks	8.00	100%	0%	19 Sep-26	28Sep-26	22 Oct 26	31Oct-26	$1,040,00.00	$000	$1,040,00.00	0.00
MLTX02004CN-11520	Installing ofValvesand fittings	2.00	100%	0%	07 Sep-26	08Sep-26	22 Oct 26	24Oct-26	$9,750.00	$000	$9,750.00	0.00
MLTX02004CN-11860	Installing ofWater Heater	4.00	100%	0%	06 Oct 26	10Oct-26	30 Nov 26	03Dec-26	$1,755.00	$000	$1,755.00	0.00
MLTX02004CN-11540	Installing ofPPR Pipes andFittings for WaterNetwork	3.00	100%	100%	03 Sep-26	06Sep-26	04 Jul-26A	09Aug-26A	$6,922.50	$6922.50	$6,922.50	-2855
SEWERDRAIN AGESYSTEM		8200	100%	6214%	01 Sep-26	15Oct-26	04 Jul-26A	09Dec-26	$1,424,91.38	$8,858.955	$1,424,91.38	-9800
MLTX02004CN-11600	Installing ofPlumping Fixturesand Accessories	2.00	100%	0%	19 Sep-26	20Sep-26	14 Nov 25	15Nov-26	$1,085,938	$000	$10359.38	0.00
MLTX02004CN-11850	Installing Inspection Chamber forSewageNetwok	9.00	100%	0%	03 Sep-26	13Sep-26	20 Oct 26	29Oct-26	$1,218,750	$000	$12187.50	0.00
MLTX02004CN-11870	Installing ofToilet fixturesand Accessories Such as Cbsetsand Basins	9.00	100%	0%	06 Oct 26	15Oct-26	30 Nov 26	09Dec-26	$3,139,500	$000	$31395.00	0.00
MLTX02004CN-11590	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	01 Sep-26	02Sep-26	04 Jul-26A	09Aug-26A	$1,176,825	$1,176,825	$11768.25	-2960
MLTX02004CN-11580	Installing UPVC Pipes for ExternalConnecton for Sewage Network	4.00	100%	100%	14 Sep-26	17Sep-26	08 Oct 26 A	10Oct-26A	$7,678,125	$7,678,125	$76781.25	2.00
FIREPROTECTION		4.00	75%	0%	17 Oct 26	20Oct-26	10 Dec 25	14Dec-26	$1,462,500	$000	$1,950.00	0.00
MLTX02004CN-11620	Installing ofFireFighting Extingusherand accessories (PIE-1, PIE-2)	4.00	75%	0%	17 Oct 26	20Oct-26	10 Dec 25	14Dec-26	$1,462,500	$000	$1,950.00	0.00
ELECTRICAL WORKS		12000	7382%	3954%	19 Aug-26	25Oct-26	30 Jul-26A	19Dec-26	$2,779,336	$148882.50	$3,765,25.25	-6400
ROUGH-N WORKS		3600	100%	100%	19 Aug-26	30Aug-26	30 Jul-26A	26Aug-26A	$1,488,82.50	$148882.50	$1,488,82.50	-1400
MLTX02004CN-11660	Preliminay Works forPanelBoards	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$7,605,000	$7,605,000	$76050.00	-400
MLTX02004CN-11670	Preliminay Works forCableWorks	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$1,070,004	$1,070,004	$10700.04	-400
MLTX02004CN-11680	Preliminay Works forSockets andPowerPoints	1000	100%	100%	19 Aug-26	30Aug-26	30 Jul-26A	30Jul-26A	$9,230,91	$9230.91	$9,230,91	9.00
MLTX02004CN-11690	Preliminay Works forLightningWorks	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$9,750,00	$9750.00	$9,750.00	-400
MLTX02004CN-11700	Preliminay Works forData& TelecommunicationSystem	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$1,228,500	$1,228,500	$12285.00	-400
MLTX02004CN-11720	Preliminay Works forSecurity and Access Contol System	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$1,526,655	$1,526,655	$15266.55	-400
MLTX02004CN-11650	Preliminay Works forEarbing Works	1000	100%	100%	19 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$1,560,000	$1,560,000	$15600.00	-400
FIXTURE WORKS		1000	5669%	0%	14 Oct 26	25Oct-26	08 Dec 25	19Dec-26	$1,291,513	$000	$2,276,48.75	0.00
MLTX02004CN-11780	Installing ofFireautomationand Fire Alarm System	4.00	0%	0%	21 Oct 26	25Oct-26	15 Dec 25	19Dec-26	$000	$000	$34320.00	0.00
MLTX02004CN-11740	Installing andFinish Works ofPanelBoards	1000	50%	0%	14 Oct 26	25Oct-26	08 Dec 25	19Dec-26	$4,203,750	$000	$84075.00	0.00
MLTX02004CN-11760	Installing andFinalize Worksof Sockets and PowerPoints	4.00	75%	0%	17 Oct 26	20Oct-26	10 Dec 25	14Dec-26	$1,088,477	$000	$13846.37	0.00
MLTX02004CN-11790	Installing andFinalize Worksof Lighting Works includingLightFixtures	4.00	75%	0%	17 Oct 26	20Oct-26	10 Dec 25	14Dec-26	$1,203,755	$000	$16050.00	0.00

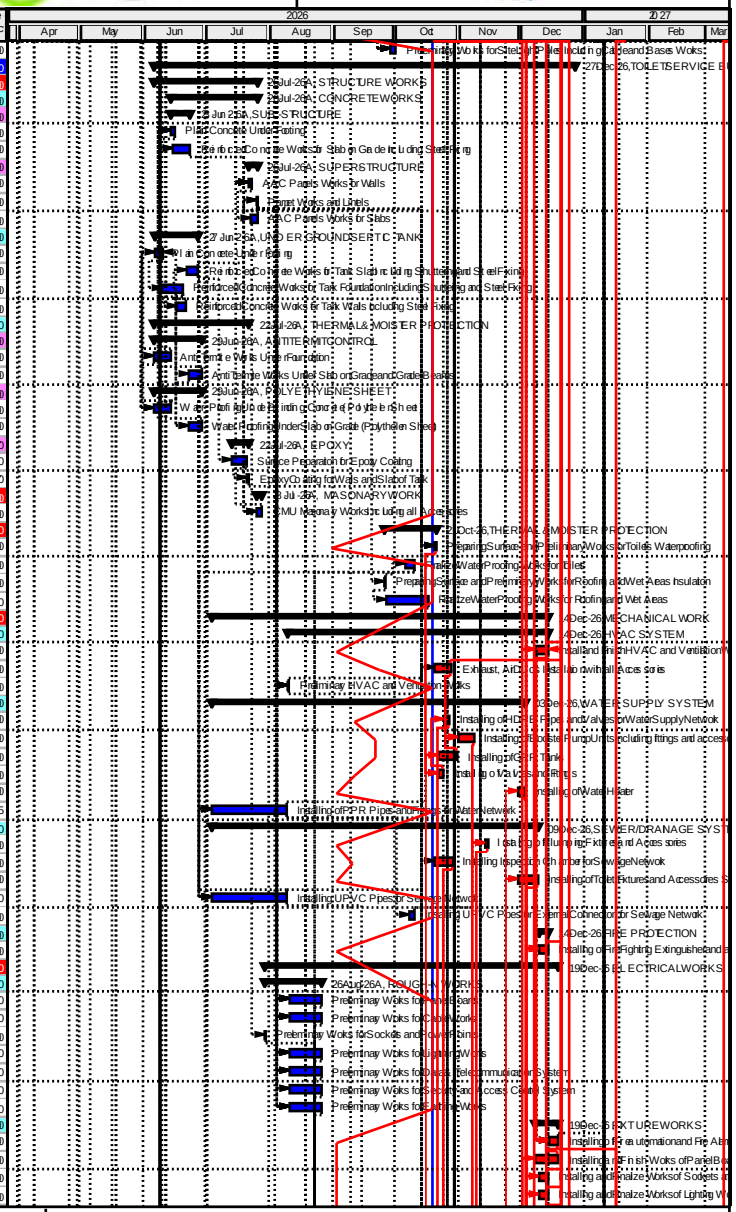

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-11750	Installing Data and Telecommunication System with all Accessories	4.00	75%	0%	17-Oct-26	20-Oct-26	10-Dec-26	14-Dec-26	$1,312.06	$0.00	$18,427.50	0.00
MLTX02-004CN-11830	Installing and Finalize Works of Security and Access Control System	6.00	8333%	0%	14-Oct-26	20-Oct-26	08-Dec-26	14-Dec-26	$1,198.31	$0.00	$22,899.83	0.00
MLTX02-004CN-11770	Installing and Finalize Works of Earthing Works	6.00	8333%	0%	14-Oct-26	20-Oct-26	08-Dec-26	14-Dec-26	$1,950.00	$0.00	$23,400.00	0.00
MLTX02-004CN-11820	Installing and Finalize Works of Lightning Protection System	6.00	8333%	0%	14-Oct-26	20-Oct-26	08-Dec-26	14-Dec-26	$1,218.75	$0.00	$14,625.00	0.00
DOORS/WINDOWS		5900	4245%	0%	19-Aug-26	02-Nov-26	20-Oct-26	27-Dec-26	$2,897.14	$0.00	$68,250.00	5.00
MLTX02-004CN-11110	Preliminary Works For Doors	3.00	100%	0%	19-Aug-26	22-Aug-26	20-Oct-26	22-Oct-26	$3,900.00	$0.00	$3,900.00	0.00
MLTX02-004CN-11120	Finalize Metal Doors for Toilets Building	7.00	2857%	0%	18-Oct-26	25-Oct-26	08-Dec-26	15-Dec-26	$1,671.43	$0.00	$5,850.00	0.00
MLTX02-004CN-11130	Finalize Glazzed Curtain Wall Works	7.00	0%	0%	26-Oct-26	02-Nov-26	20-Dec-26	27-Dec-26	$0.00	$0.00	$35,100.00	0.00
MLTX02-004CN-11100	Preliminary Works For Windows/Curtain Wall	2.00	100%	0%	19-Aug-26	20-Aug-26	31-Oct-26	01-Nov-26	$2,340.00	$0.00	$23,400.00	0.00
METAL WORKS		3544	100%	7143%	19-Jul-26	17-Oct-26	20-Sep-26 A	31-Oct-26	$1,365.00	$9750.00	$13650.00	42.44
MLTX02-004CN-11150	Installation of DI Cover for Tank	1000	100%	0%	19-Jul-26	29-Jul-26	20-Oct-26	31-Oct-26	$3,900.00	$0.00	$3,900.00	0.00
MLTX02-004CN-11160	Installation of Galvanized Steel Ladder	1200	100%	100%	19-Sep-26	03-Oct-26	21-Sep-26 A	03-Oct-26A	$5,850.00	$5850.00	$5,850.00	2.44
MLTX02-004CN-11170	Installation of Galvanized Steel Roof Scupper	1200	100%	100%	04-Oct-26	17-Oct-26	20-Sep-26 A	20-Sep-26A	$3,900.00	$3900.00	$3,900.00	12.00
FINISHING WORKS		6856	100%	344%	01-Sep-26	17-Oct-26	29-Aug-26 A	10-Dec-26	$1,445,145.15	$14,971.85	$1,445,116.50	-49.56
FLOOR FINISHES		3400	100%	0%	07-Sep-26	17-Oct-26	02-Nov-26	10-Dec-26	$1,716.00	$0.00	$17160.00	0.00
MLTX02-004CN-11200	Ceramic Tiles Floor Finish Works	2.00	100%	0%	07-Sep-26	08-Sep-26	02-Nov-26	03-Nov-26	$1,189.50	$0.00	$11895.00	0.00
MLTX02-004CN-11210	Granite Tiles Floor Finish Works	4.00	100%	0%	09-Sep-26	13-Sep-26	04-Nov-26	08-Nov-26	$2,925.00	$0.00	$2,925.00	0.00
MLTX02-004CN-11220	Epoxy Coaton Concete floor	3.00	100%	0%	14-Oct-26	17-Oct-26	08-Dec-26	10-Dec-26	$1,170.00	$0.00	$1,170.00	0.00
MLTX02-004CN-11230	Ceramic Skirting Tiles Finish Works	4.00	100%	0%	14-Sep-26	17-Sep-26	09-Nov-26	12-Nov-26	$1,170.00	$0.00	$1,170.00	0.00
WALL FINISHES		6756	100%	4355%	01-Sep-26	15-Oct-26	29-Aug-26 A	09-Dec-26	$1,141,725.00	$14,971.85	$1,141,725.00	-49.56
MLTX02-004CN-11300	Painting Finish Works for External Walls	7.00	100%	0%	13-Sep-26	20-Sep-26	28-Oct-26	04-Nov-26	$1,947.80	$0.00	$10,478.00	0.00
MLTX02-004CN-11320	Phendic Partitons for Toilets	7.00	100%	0%	28-Sep-26	05-Oct-26	22-Nov-26	29-Nov-26	$3,120.00	$0.00	$31200.00	0.00
MLTX02-004CN-11260	Glass Partitions including all accessories and doors	7.00	100%	0%	06-Oct-26	13-Oct-26	30-Nov-26	07-Dec-26	$1,228.50	$0.00	$12285.00	0.00
MLTX02-004CN-11270	Granite Capping for Papet	2.00	100%	0%	16-Sep-26	17-Sep-26	20-Oct-26	21-Oct-26	$815.00	$0.00	$8,151.00	0.00
MLTX02-004CN-11840	Painting Finish Works for Internal Walls	2.00	100%	0%	14-Oct-26	15-Oct-26	08-Dec-26	09-Dec-26	$2,340.00	$0.00	$2,340.00	0.00
MLTX02-004CN-11280	Preliminary Works for Wall Finish Works including Plastering (Internal)	5.00	100%	100%	01-Sep-26	06-Sep-26	29-Aug-26 A	09-Sep-26A	$1,686.90	$1,836.90	$18369.00	-5.56
MLTX02-004CN-11290	Preliminary Works for Wall Finish Works (External)	1000	100%	100%	01-Sep-26	12-Sep-26	10-Sep-26 A	12-Sep-26A	$655.20	$655.20	$655.20	8.44
MLTX02-004CN-11310	Ceramic Finish Works for Walls	5.00	100%	100%	09-Sep-26	14-Sep-26	12-Sep-26 A	14-Sep-26A	$1,559.75	$1,559.75	$15697.50	2.00
MLTX02-004CN-11250	Stone Cladding Finish Works for External Walls	5.00	100%	100%	21-Sep-26	27-Sep-26	19-Sep-26 A	26-Sep-26A	$910.00	$9100.00	$910.00	-100
CELING FINISHES		1000	100%	0%	07-Sep-26	30-Sep-26	20-Oct-26	31-Oct-26	$1,318.20	$0.00	$13182.00	10.00
MLTX02-004CN-11350	Painting Finish Works for Ceiling	3.00	100%	0%	28-Sep-26	30-Sep-26	28-Oct-26	31-Oct-26	$1,638.00	$0.00	$1,638.00	0.00
MLTX02-004CN-11360	Gypsum Board Suspended Ceiling finish Works For Ceiling	7.00	100%	0%	19-Sep-26	27-Sep-26	20-Oct-26	27-Oct-26	$6,925.40	$0.00	$6,926.40	0.00
MLTX02-004CN-11340	Preliminary Works for Ceiling Painting Works	3.00	100%	0%	07-Sep-26	09-Sep-26	20-Oct-26	22-Oct-26	$1,617.60	$0.00	$4,617.60	0.00
SPECIALTIES WORK		1500	100%	0%	21-Sep-26	08-Oct-26	16-Nov-26	02-Dec-26	$3,900.00	$0.00	$39000.00	0.00
MLTX02-004CN-11190	Sanitary Fixtures and Accessories Works	5.00	100%	0%	21-Sep-26	27-Sep-26	16-Nov-26	21-Nov-26	$1,462.50	$0.00	$14625.00	0.00
MLTX02-004CN-11180	Installation of Phenolic Locker	3.00	100%	0%	06-Oct-26	08-Oct-26	30-Nov-26	02-Dec-26	$2,437.50	$0.00	$24375.00	0.00
TESTING & COMMISSIONING		6400	0%	0%	05-Nov-26	12-Jan-27	28-Jan-27	11-Apr-27	$0.00	$0.00	$0.00	-5.00
MLTX02-004TC-11860	Testing and Commissioning for MEP Works for Playground Area	1000	0%	0%	02-Jan-27	12-Jan-27	31-Mar-27	11-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX02-004TC-11870	Testing and Commissioning for MEP Works for Toilet Service Building	2200	0%	0%	05-Nov-26	30-Nov-26	28-Jan-27	16-Feb-27	$0.00	$0.00	$0.00	0.00
MLTX02-004TC-11880	Testing and Commissioning for MEP Works for Landscape Works	2200	0%	0%	01-Dec-26	26-Dec-26	17-Feb-27	18-Mar-27	$0.00	$0.00	$0.00	0.00
JAZAN		34300	3%	2499%	26-Mar-26	25-Jan-27	26-Mar-26 A	09-May-27	$3,951,358.81	$2,669,083.74	$10,680,072.52	-8.50
MOBILIZATION		6300	0%	0%	26-Mar-26	10-Jun-26	26-Mar-26 A	10-Jun-26A	$0.00	$0.00	$0.00	0.00
TOPOGRAPHIC SURVEY		4.00	0%	0%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1860	Site Survey Works	4.00	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26A	$0.00	$0.00	$0.00	0.00
SITE FACILITIES & OFFICES		5575	0%	0%	26-Mar-26	02-Jun-26	26-Mar-26 A	02-Jun-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1740	Manpower Mobalizaton	3150	100%	100%	16-Apr-26	23-May-26	16-Apr-26 A	23-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1750	Equipment Mobalization	2.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1770	Site Layout Plan	4.00	100%	100%	26-Mar-26	30-Mar-26	26-Mar-26 A	30-Mar-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1780	Clear & Grib for Offices & Access Road	3.00	100%	100%	31-Mar-26	02-Apr-26	31-Mar-26 A	02-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1790	Constuct Site Access Roads	4.00	100%	100%	31-Mar-26	04-Apr-26	31-Mar-26 A	04-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1800	Constuct Temporay Fence	3875	100%	100%	15-Apr-26	02-Jun-26	15-Apr-26 A	02-Jun-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1810	Constuct Site Offices & Storage	2.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1820	Install Project Signs	1800	100%	100%	20-Apr-26	10-May-26	20-Apr-26 A	10-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1830	Install Site Facilities	1.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1840	Electrical Works & Connections	1.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1850	Constuct Parking Sheds	1.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$0.00	$0.00	$0.00	0.00
PRELIMINARY SUBMITTALS		5900	0%	0%	31-Mar-26	10-Jun-26	31-Mar-26 A	10-Jun-26A	$0.00	$0.00	$0.00	0.00
PREPARATIONS & SUBMITTALS BY CONTRACTORS		2700	0%	0%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1760	Preparation and Submittal of Detailed Work Order Programme (Baseline)	2500	100%	100%	31-Mar-26	28-Apr-26	31-Mar-26 A	28-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1870	Preparation and Submittal of Project Execution Plan	2700	100%	100%	31-Mar-26	30-Apr-26	31-Mar-26 A	30-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1880	Submission of Contactor Project Quality Plan	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1890	Submission of Construction Safety & Environmental Management Plan	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26 A	11-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1900	Preparation and Submittal of Organization Chart	8.00	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26A	$0.00	$0.00	$0.00	0.00
MLTX02-004MB-1910	Preparation and Submittal of Communication Plan	8.00	100%	100%	31-Mar-26	08-Apr-26	31-Mar-26 A	08-Apr-26A	$0.00	$0.00	$0.00	0.00
APPROVALS BY EMPLOYERS		5100	0%	0%	09-Apr-26	10-Jun-26	09-Apr-26 A	10-Jun-26A	$0.00	$0.00	$0.00	0.00



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004MB-1920	Approval of Detailed Work Order Programme (Baseline)	1.0d	100%	100%	29 Apr 26	29 Apr-26	29 Apr 26 A	29 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004MB-1930	Approval of Project Execution Plan	1.0d	100%	100%	13 May-26	13 May-26	13 May 26 A	13 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004MB-1940	Approval of Contactor Project Quality Plan	19.0d	100%	100%	09 Apr 26	30 Apr-26	09 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004MB-1950	Approval of Constuction Safety & Environmental Management Plan	1.0d	100%	100%	10 Jun 26	10 Jun-26	10 Jun 26 A	10 Jun-26 A	$000	$000	$0.00	0.0d
MLTX-02-004MB-1960	Approval of Organization Chat	10.0d	100%	100%	09 Apr 26	20 Apr-26	09 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004MB-1970	Approval of Communication Plan	10.0d	100%	100%	09 Apr 26	20 Apr-26	09 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
ENGINEERING		185.0d	0%	0%	31 Mar 26	02 Aug-26	31 Mar 26 A	05 Nov-26	$000	$000	$0.00	-81.0d
SHOP DRAWINGS		144.0d	0%	0%	31 Mar 26	21 Jul-26	31 Mar 26 A	26 Aug-26 A	$000	$000	$0.00	-31.0d
SHOP DRAWINGS SUBMISSION		134.0d	0%	0%	31 Mar 26	09 Jul-26	31 Mar 26 A	25 Aug-26 A	$000	$000	$0.00	-40.0d
SHOP DRAWINGS SUBMITTALS FOR EARTHWORKS		68.0d	0%	0%	31 Mar 26	21 Jun-26	31 Mar 26 A	21 Jun-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7830	Shop DWG Submittal for Layout Plan	15.0d	100%	100%	31 Mar 26	16 Apr-26	31 Mar 26 A	16 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7840	Shop DWG Submittal for Setting Out	21.0d	100%	100%	31 Mar 26	23 Apr-26	31 Mar 26 A	25 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7850	Shop DWG Submittal for Grading Layout Plan	6.0d	100%	100%	31 Mar 26	06 Apr-26	31 Mar 26 A	06 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7860	Shop DWG Submittal for Curb Setting Out Points	1.0d	100%	100%	23 May-26	23 May-26	23 May 26 A	23 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7870	Shop DWG Submittal for Signing & Making Layout Plan	1.0d	100%	100%	21 Jun 26	21 Jun-26	21 Jun 26 A	21 Jun-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-7880	Shop DWG Submittal for Standards Details	1.0d	100%	100%	21 May-26	21 May-26	21 May 26 A	21 May-26 A	$000	$000	$0.00	0.0d
SHOP DRAWINGS SUBMITTALS FOR SERVICE/TOILET WORKS		134.0d	0%	0%	31 Mar 26	09 Jul-26	31 Mar 26 A	25 Aug-26 A	$000	$000	$0.00	-40.0d
ARCHITECTURE WORKS		12.0d	0%	0%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8210	Shop DWG Submittal for Floor Plan	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8220	Shop DWG Submittal for Elevations	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8230	Shop DWG Submittal for Sections	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8240	Shop DWG Submittal for Ceiling Plan	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8250	Shop DWG Submittal for Finishes Plan	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8260	Shop DWG Submittal for Toilet Details	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8270	Shop DWG Submittal for Doors&Windows Schedule	12.0d	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.0d
STRUCTURE WORKS		20.0d	0%	0%	08 Apr 26	30 Apr-26	08 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8280	Shop DWG Submittal for Foundation Plan	20.0d	100%	100%	08 Apr 26	30 Apr-26	08 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8290	Shop DWG Submittal for Ground Floor Framing Plan	20.0d	100%	100%	08 Apr 26	30 Apr-26	08 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8300	Shop DWG Submittal for Sections/Details	20.0d	100%	100%	08 Apr 26	30 Apr-26	08 Apr 26 A	30 Apr-26 A	$000	$000	$0.00	0.0d
MECHANCAL WORKS		38.0d	0%	0%	08 Apr 26	21 May-26	08 Apr 26 A	21 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8310	Shop DWG Submittal for HVAC Plan	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8320	Shop DWG Submittal for Exhaust Air Plan	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8330	Shop DWG Submittal for HVAC Equipment Schedule	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8340	Shop DWG Submittal for Fire Fighting Layout	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8350	Shop DWG Submittal for Water Supply Layout	1.0d	100%	100%	06 May-26	06 May-26	06 May 26 A	06 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8360	Shop DWG Submittal for Water Supply Details	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8370	Shop DWG Submittal for Drainage Layout	1.0d	100%	100%	21 May-26	21 May-26	21 May 26 A	21 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8380	Shop DWG Submittal for Drainage Details	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8920	Shop DWG Submittal for Dut Routing Layout	6.0d	100%	100%	08 Apr 26	14 Apr-26	08 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8930	Shop DWG Submittal for Diffusers Layout	1.0d	100%	100%	21 May-26	21 May-26	21 May 26 A	21 May-26 A	$000	$000	$0.00	0.0d
ELECTRCAL WORKS		127.0d	0%	0%	08 Apr 26	09 Jul-26	08 Apr 26 A	25 Aug-26 A	$000	$000	$0.00	-40.0d
MLTX-02-004EN-8360	Shop DWG Submittal for Lighting layout	10.0d	100%	100%	08 Apr 26	19 Apr-26	08 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8400	Shop DWG Submittal for Power layout	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8410	Shop DWG Submittal for Power Single Line Diagram	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8420	Shop DWG Submittal for Panel Board Schedules	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8430	Shop DWG Submittal for Lighting Installation Details	10.0d	100%	100%	08 Apr 26	19 Apr-26	08 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8440	Shop DWG Submittal for Power Installation Details	10.0d	100%	100%	08 Apr 26	19 Apr-26	08 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8450	Shop DWG Submittal for Cable Tray Installation Details	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8460	Shop DWG Submittal for Manhole& Ducbank Details	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8470	Shop DWG Submittal for Grounding Details	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8480	Shop DWG Submittal for Lightning Protecton Details	10.0d	100%	100%	08 Apr 26	19 Apr-26	08 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8490	Shop DWG Submittal for Fire Alarm Installation Details	11.0d	100%	100%	08 Apr 26	20 Apr-26	08 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8500	Shop DWG Submittal for CCTV Details	5.0d	100%	100%	05 Jul-26	09 Jul-26	25 Aug 26 A	25 Aug-26 A	$000	$000	$0.00	4.0d
MLTX-02-004EN-8510	Shop DWG Submittal for Grounding Layout	20.0d	100%	100%	06 May-26	07 May-26	06 May 26 A	07 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8520	Shop DWG Submittal for Lightning Protecton System Layout	10.0d	100%	100%	08 Apr 26	19 Apr-26	08 Apr 26 A	19 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8530	Shop DWG Submittal for Fire Alarm Layout	11.0d	100%	100%	08 Apr 26	20 Apr-26	08 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8540	Shop DWG Submittal for Fire Alarm Riser Diagram	11.0d	100%	100%	08 Apr 26	20 Apr-26	08 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8550	Shop DWG Submittal for CCTV Layout	5.0d	100%	100%	05 Jul-26	09 Jul-26	25 Aug 26 A	25 Aug-26 A	$000	$000	$0.00	4.0d
MLTX-02-004EN-8560	Shop DWG Submittal for CCTV Riser Diagram	5.0d	100%	100%	05 Jul-26	09 Jul-26	25 Aug 26 A	25 Aug-26 A	$000	$000	$0.00	4.0d
MLTX-02-004EN-8570	Shop DWG Submittal for Telephone & Data Layout	11.0d	100%	100%	08 Apr 26	20 Apr-26	08 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8580	Shop DWG Submittal for Telephone & Data Riser Diagram	11.0d	100%	100%	08 Apr 26	20 Apr-26	08 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.0d
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		134.0d	0%	0%	31 Mar 26	09 Jul-26	31 Mar 26 A	25 Aug-26 A	$000	$000	$0.00	-40.0d
ARCHITECTURE WORKS		39.0d	0%	0%	31 Mar 26	14 May-26	31 Mar 26 A	14 May-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8780	Shop DWG Submittal for Playground Plan/Layout	16.0d	100%	100%	31 Mar 26	18 Apr-26	31 Mar 26 A	18 Apr-26 A	$000	$000	$0.00	0.0d
MLTX-02-004EN-8790	Shop DWG Submittal for Furniture& Marking	20.0d	100%	100%	13 May-26	14 May-26	13 May 26 A	14 May-26 A	$000	$000	$0.00	0.0d

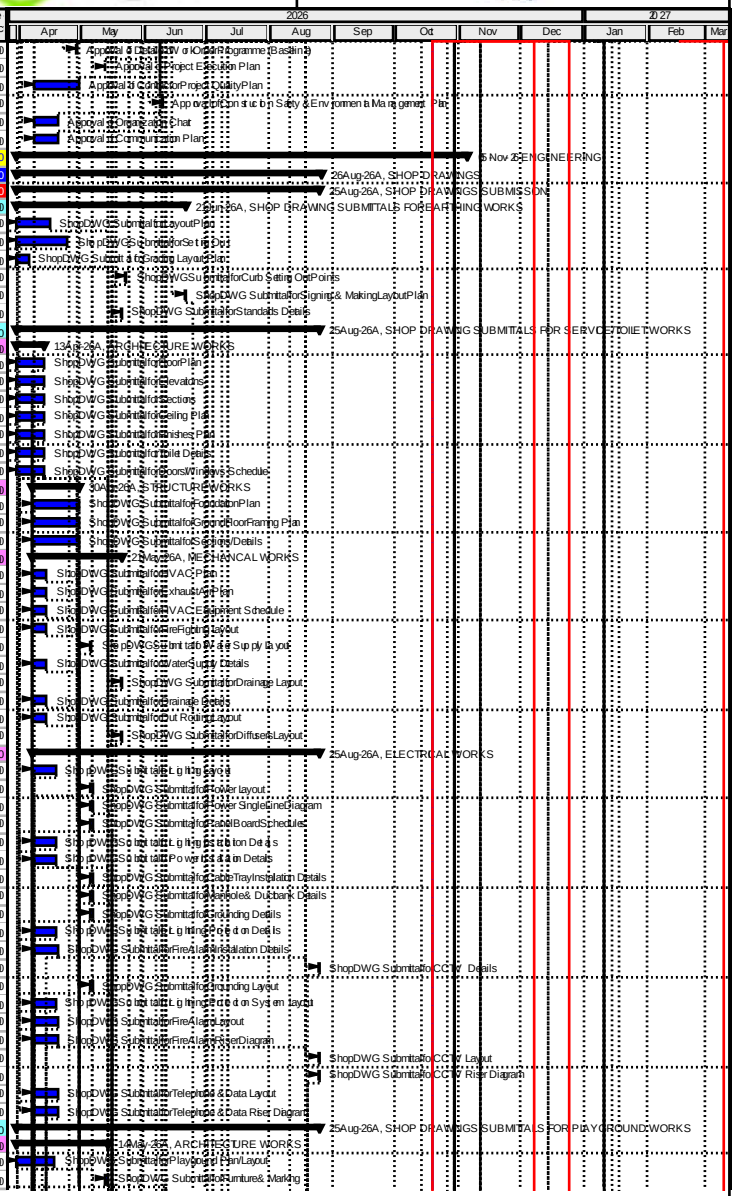


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-880	ShopDWG SubmittalforSections	1600	100%	100%	31-Mar-26	18A pr-26	31-Mar-26A	18A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-881	ShopDWG SubmittalforInterlockPatten Plan	7.00	100%	100%	31-Mar-26	07A pr-26	31-Mar-26A	07A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-882	ShopDWG SubmittalforDoors\Windows Schedule	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-885	ShopDWG SubmittalforDome Internal Layout	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-883	ShopDWG SubmittalforAir Dome System	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-884	ShopDWG SubmittalforFoundationof AirDome	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-886	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
AIRDOMESYSTEM		2.00	0%	0%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-887	ShopDWG SubmittalforAir Dome Structural Layout	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-888	ShopDWG SubmittalforMembrane PanelLayout	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-888	ShopDWG SubmittalforCableTension Layout	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-890	ShopDWG SubmittalforAirlock DoorDetails	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-891	ShopDWG SubmittalforEmergency ExitDetails	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		2.00	0%	0%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-894	ShopDWG SubmittalforFootball Turf Installation	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-895	ShopDWG SubmittalforBasketballCourtMarking	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-896	ShopDWG SubmittalforPadelCourtStructure	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		2000	0%	0%	08 Apr-26	30A pr-26	08 Apr-26A	30A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-876	ShopDWG SubmittalforHVAC Plan	2000	100%	100%	08 Apr-26	30A pr-26	08 Apr-26A	30A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-877	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr-26	30A pr-26	08 Apr-26A	30A pr-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		8900	0%	0%	23-May-26	09Jul-26	23-May-26A	25Aug-26A	$000	$000	$0.00	-4000
MLTX-02-004EN-865	ShopDWG SubmittalforLighting Layout	1.00	100%	100%	25-May-26	25-May-26	25-May-26A	25-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-866	ShopDWG SubmittalforPower layout	5.00	100%	100%	05-Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-867	ShopDWG SubmittalforPower SingleLineDiagram	5.00	100%	100%	05-Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-868	ShopDWG SubmittalforPanelBoardSchedules	5.00	100%	100%	05-Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-869	ShopDWG SubmittalforPowerInstalation Details	5.00	100%	100%	05-Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-870	ShopDWG SubmittalforFireAlarmInstalation Details	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-871	ShopDWG SubmittalforCCTV Details	5.00	100%	100%	05-Jul-26	09Jul-26	25 Aug-26A	25Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-872	ShopDWG SubmittalforFireAlarmLayout	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-873	ShopDWG SubmittalforFireAlarmRiserDiagram	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-874	ShopDWG SubmittalforCCTV Layout	5.00	100%	100%	05-Jul-26	09Jul-26	25 Aug-26A	25Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-875	ShopDWG SubmittalforCCTV Riser Diagram	5.00	100%	100%	05-Jul-26	09Jul-26	25 Aug-26A	25Aug-26A	$000	$000	$0.00	4.00
SHOP DRAWINGSSUBMITTALS FOR LANDSCAPE WORKS		9500	0%	0%	31-Mar-26	09Jul-26	31-Mar-26A	18Jul-26A	$000	$000	$0.00	-700
ARCHITECTURE WORKS		3900	0%	0%	31-Mar-26	14May-26	31-Mar-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-859	ShopDWG SubmittalforLandscape Layout	1500	100%	100%	31-Mar-26	16A pr-26	31-Mar-26A	16A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-860	ShopDWG SubmittalforHardscape Plan	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-861	ShopDWG SubmittalforPlanting Plan	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-862	ShopDWG SubmittalforLandscape Details	2.00	100%	100%	13-May-26	14May-26	13-May-26A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		5.00	0%	0%	05-Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-863	ShopDWG SubmittalforIrrigation Details	5.00	100%	100%	05-Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-864	ShopDWG SubmittalforIrrigation Layout	5.00	100%	100%	05-Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
ELECTRCALWORKS		1.00	0%	0%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-788	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-790	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-791	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-792	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALS		13800	0%	0%	07 Apr-26	21Jul-26	07 Apr-26A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWIN GAPPROVALFOR EARTHINGW ORKS		7100	0%	0%	07 Apr-26	01Jul-26	07 Apr-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11260	ShopDWG Appovalfor layoutPlan	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11270	ShopDWG Appovalfor SettingOut	1700	100%	100%	07 Apr-26	26A pr-26	07 Apr-26A	26A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11280	ShopDWG Appovalfor GradingLayoutPlan	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11290	ShopDWG Appovalfor Cub SetingOut Points	1.00	100%	100%	23-May-26	23May-26	23-May-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11300	ShopDWG Appovalfor Signing& Marking Layout Plan	1.00	100%	100%	01-Jul-26	01Jul-26	01-Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11310	ShopDWG Appovalfor Standards Details	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GAPPROVALFOR SERVICEDILETWORKS		13200	0%	0%	14 Apr-26	21Jul-26	14 Apr-26A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		9.00	0%	0%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-113	ShopDWG Appovalfor RoofPlan	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-113	ShopDWG Appovalfor Elevations	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-113	ShopDWG Appovalfor Sections	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-113	ShopDWG Appovalfor CeilingPlan	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor finishes Plan	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor ToiletDetails	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor Doors/WindowsSchedule	9.00	100%	100%	14 Apr-26	23A pr-26	14 Apr-26A	24A pr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	07-May-26	07May-26	07-May-26A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor Foundation Plan	1.00	100%	100%	07-May-26	07May-26	07-May-26A	07May-26A	$000	$000	$0.00	0.00

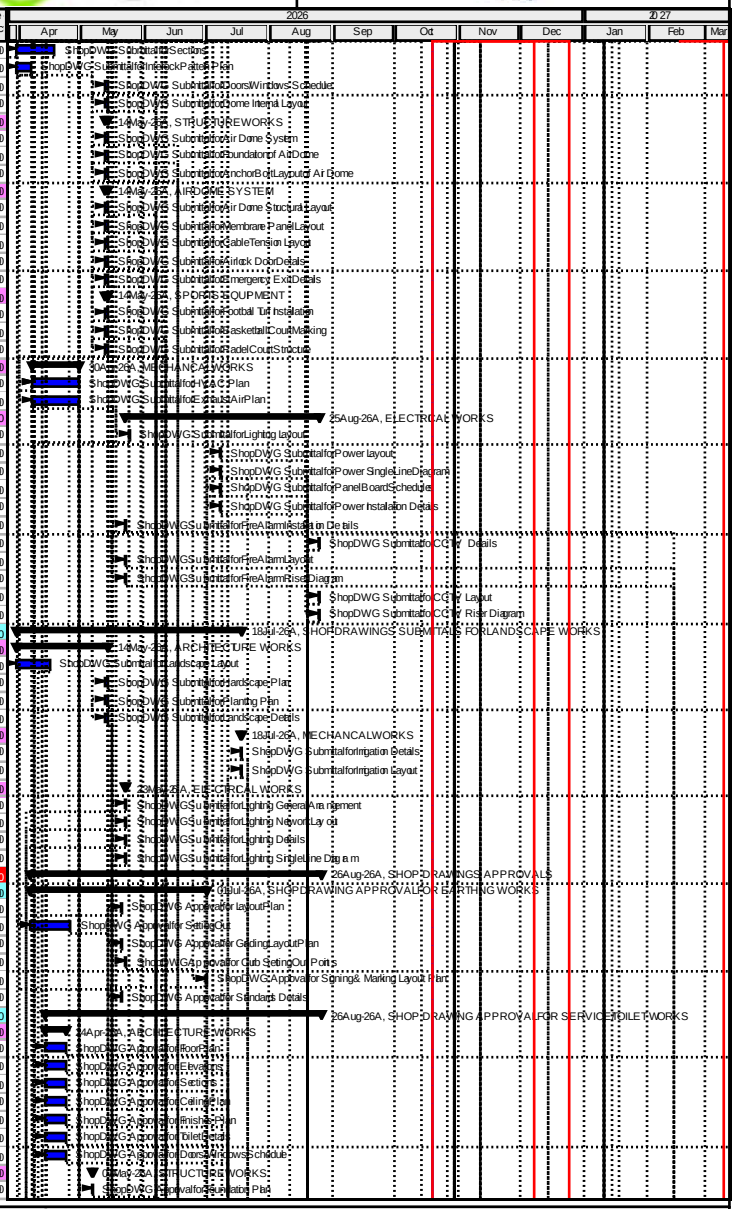

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-114	ShopDWG Appovalfor Gound FloorFraming Plan	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor SectionsDetails	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1300	0%	0%	07 May-26	21May-26	07 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor HVACEquipment Schedule	4.00	100%	100%	07 May-26	11May-26	07 May-26 A	11May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-114	ShopDWG Appovalfor fire fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor WaterSupplyLayout	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor WaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor DrainageLayout	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor DrainageDetails	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Duct RoutingLayout	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Diffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
MLTX-02-004EN-115	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Power Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor lighting InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Power InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor Cable Tray InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor Manhole& Ducttank Details	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor Grounding Details	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor lightning Potection Details	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor fire Alarm Instalation Details	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor CCTV Details	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug-26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-116	ShopDWG Appovalfor Grounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May-26 A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor lightning Potection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-116	ShopDWG Appovalfor fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-117	ShopDWG Appovalfor CCTV Layout	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug-26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-117	ShopDWG Appovalfor CCTV RiserDiagam	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug-26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-117	ShopDWG Appovalfor Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-117	ShopDWG Appovalfor Telephone & Data Riser Diagam	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GSAPPROVALFOR PLAYGROUND WORKS		13700	0%	0%	08 Apr 26	21Jul-26	08 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		5900	0%	0%	08 Apr 26	18Jun-26	08 Apr 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Furniture & Marking	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Interbock PatternPlan	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Doors/WindowsSchedule	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Dome InternalLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Air DomeSystem	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Anchor Bolt layoutof AirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Air DomeStructuralLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor MembranePanelLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Cable TensionLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor AirlockDoorDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor EmergencyExitDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		1.00	0%	0%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Footbal Tuf Installation	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Basketball Court Making	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-120	ShopDWG Appovalfor Padel Court Stuctue	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
MLTX-02-004EN-115	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-115	ShopDWG Appovalfor Power Single line Diagram	1000	100%	100%	11 Jul-26	21Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-115	ShopDWG Appovalfor Panel Board Schedules	1000	100%	100%	11 Jul-26	21Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	9.00

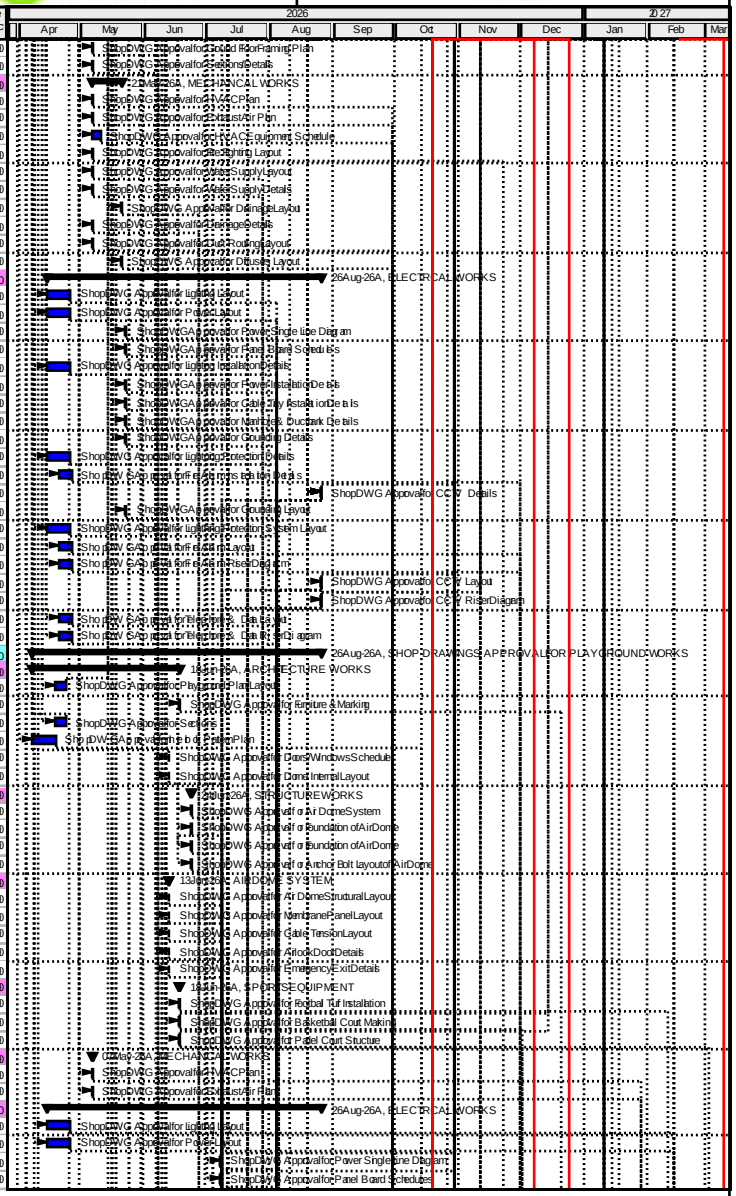

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-1150	ShopDWG Appovalfor Power InstallationDetails	10.00	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1180	ShopDWG Appovalfor CCTV Details	10.00	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26A	26-Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-1181	ShopDWG Appovalfor CCTV Layout	10.00	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26A	26-Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-1182	ShopDWG Appovalfor CCTV RiserDiagram	10.00	100%	100%	11-Jul-26	21-Jul-26	26-Aug-26A	26-Aug-26A	$000	$000	$0.00	9.00
SHOP DRAWIN GSAPPROVALFOR LANDSCAPE WORKS		91.00	0%	0%	11-Apr-26	21-Jul-26	11-Apr-26A	18-Jul-26A	$000	$000	$0.00	3.00
ARCHITECTURE WORKS		31.00	0%	0%	18-Apr-26	23-May-26	17-Apr-26A	23-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1170	ShopDWG Appovalfor landscape Layout	6.00	100%	100%	18-Apr-26	23-Apr-26	17-Apr-26A	24-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1171	ShopDWG Appovalfor Hadscape Plan	1.00	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1172	ShopDWG Appovalfor Planting Plan	1.00	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1173	ShopDWG Appovalfor landscape Details	1.00	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		10.00	0%	0%	11-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-1174	ShopDWG Appovalfor IrigationDetails	10.00	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-1175	ShopDWG Appovalfor IrigationLayout	10.00	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	9.00
ELECTRCAL WORKS		37.00	0%	0%	11-Apr-26	23-May-26	11-Apr-26A	23-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1130	ShopDWG Appovalfor lighting General Arrangement	10.00	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26A	21-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1131	ShopDWG Appovalfor lighting Network Layout	10.00	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26A	21-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1132	ShopDWG Appovalfor lighting Details	10.00	100%	100%	11-Apr-26	21-Apr-26	11-Apr-26A	21-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-1133	ShopDWG Appovalfor lighting Sirigle Line Diagram	1.00	100%	100%	23-May-26	23-May-26	23-May-26A	23-May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		185.00	0%	0%	31-Mar-26	02-Aug-26	31-Mar-26A	05-Nov-26	$000	$000	$0.00	-81.00
METHOD STATEMENT SUBMITTAL		175.00	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26A	25-Oct-26	$000	$000	$0.00	-84.00
CIVL WORKS		45.00	0%	0%	31-Mar-26	21-May-26	31-Mar-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7930	Preparation & Submissionof MethodStatement forEarthwork	17.00	100%	100%	31-Mar-26	19-Apr-26	31-Mar-26A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7940	Preparation & Submissionof MethodStatement forConcrete Works	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7950	Preparation & Submissionof MethodStatement forWaterproding	22.00	100%	100%	31-Mar-26	25-Apr-26	31-Mar-26A	25-Apr-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		126.00	0%	0%	31-May-26	11-Jul-26	31-May-26A	25-Oct-26	$000	$000	$0.00	-90.00
MLTX-02-004EN-8060	Preparation & Submissionof MethodStatement forFenceWorks	5.00	0%	0%	05-Jul-26	09-Jul-26	20-Oct-26	25-Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-7980	Preparation & Submissionof MethodStatement forPlasteringWorks	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7990	Preparation & Submissionof MethodStatement forMasonary Works	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8000	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8010	Preparation & Submissionof MethodStatement forSeatsBenchesWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8020	Preparation & Submissionof MethodStatement forDoorsWindows Works	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8030	Preparation & Submissionof MethodStatement forInterlockCurbstone Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8040	Preparation & Submissionof MethodStatement forParking Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8050	Preparation & Submissionof MethodStatement forSoftScapeWorks	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8070	Preparation & Submissionof MethodStatement forAirDome Works	5.00	100%	100%	05-Jul-26	09-Jul-26	17-Aug-26A	17-Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8080	Preparation & Submissionof MethodStatement forMetalWoks	6.00	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	5.00
MLTX-02-004EN-8090	Preparation & Submissionof MethodStatement forPartitions Works	5.00	100%	100%	05-Jul-26	09-Jul-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8100	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		48.00	0%	0%	07-Apr-26	04-Jun-26	07-Apr-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8110	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8120	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8130	Preparation & Submissionof MethodStatement forFire FightingSystem	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	14-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8140	Preparation & Submissionof MethodStatement forIrrigation System	0.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8150	Preparation & Submissionof MethodStatement forHVAC System	0.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		58.00	0%	0%	18-Jun-26	18-Jul-26	18-Jun-26A	12-Aug-26A	$000	$000	$0.00	-22.00
MLTX-02-004EN-7960	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7970	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8160	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	7.00	100%	100%	11-Jul-26	18-Jul-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	6.00
MLTX-02-004EN-8170	Preparation & Submissionof MethodStatement forCCTV System	7.00	100%	100%	11-Jul-26	18-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	6.00
MLTX-02-004EN-8180	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8190	Preparation & Submissionof MethodStatement forEarthing/lightning Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8200	Preparation & Submissionof MethodStatement forPanelBoardsWoks	6.00	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26A	12-Aug-26A	$000	$000	$0.00	5.00
METHOD STATEMENT APPROVAL		172.00	0%	0%	15-Apr-26	02-Aug-26	15-Apr-26A	05-Nov-26	$000	$000	$0.00	-81.00
CIVL WORKS		10.00	0%	0%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-10990	Appoval of Method Statementfor Earthwork	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11000	Appoval of Method Statementfor Concrete Woks	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11010	Appoval of Method Statementfor Wateproofing	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		136.00	0%	0%	31-May-26	21-Jul-26	31-May-26A	05-Nov-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-11120	Appoval of Method Statementfor fence Works	10.00	0%	0%	11-Jul-26	21-Jul-26	25-Oct-26	05-Nov-26	$000	$000	$0.00	0.00
MLTX-02-004EN-11040	Appoval of Method Statementfor Plasteing Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11050	Appoval of Method Statementfor MasonaryWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11060	Appoval of Method Statementfor Tiling Works	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11070	Appoval of Method Statementfor Seats/Benches Works	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-11080	Appoval of Method Statementfor Doors/Windows Works	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11090	Appoval of Method Statementfor Intelock/Curbstore Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11100	Appoval of Method Statementfor ParkingWorks	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)


Updateded schedule D.D 19-10-2026








ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02004EN-11110	Approval of Method Statement for Soft Scape Works	1000	100%	100%	11-Jul-26	21-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11130	Approval of Method Statement for Air Dome Works	1000	100%	100%	11-Jul-26	21-Jul-26	27-Aug-25 A	27-Aug-26A	$000	$000	$0.00	9.00
MLTX02004EN-11140	Approval of Method Statement for Partitions Works	1000	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11150	Approval of Method Statement for Gypsum Board Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MECHANICAL WORKS		4700	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-11160	Approval of Method Statement for Sewage/Dainage System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-11170	Approval of Method Statement for Water Supply System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-11180	Approval of Method Statement for Fire Fighting System	1000	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-11190	Approval of Method Statement for Irigation System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-11200	Approval of Method Statement for HVAC System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
ELECTRICAL WORKS		4900	0%	0%	05-Jul-26	02-Aug-26	11-Jul-26A	15-Aug-26A	$000	$000	$0.00	-600
MLTX02004EN-11020	Approval of Method Statement for Electrical Conduits/Pulling Works	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX02004EN-11030	Approval of Method Statement for Lighting Poles Installation	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11210	Approval of Method Statement for Telecommunication & Data System	1000	100%	100%	22-Jul-26	02-Aug-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11220	Approval of Method Statement for CCTV System	1000	100%	100%	19-Jul-26	29-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11230	Approval of Method Statement for Lighting Works	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11240	Approval of Method Statement for Earthing/Lightning Works	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-11250	Approval of Method Statement for Panel Boards Works	1000	100%	100%	12-Jul-26	22-Jul-26	15-Aug-25 A	15-Aug-26A	$000	$000	$0.00	9.00
PRE-QUALIFICATION & MATERIAL		17700	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26A	27-Oct-26	$000	$000	$0.00	-9600
PRE-QUALIFICATION		4500	0%	0%	31-Mar-26	21-May-26	31-Mar-26A	21-May-26A	$000	$000	$0.00	0.00
TOILETS SERVICE WORKS		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
STEEL REINFORCEMENT		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-999	PreQualifcation Submittal for Steel Reinforcement	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-101	PreQualifcation Appoval for Steel Reinfocement	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
READY MIX CONCRETE		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-100	PreQualifcation Submittal for Ready Mixed Concrete	1400	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-100	PreQualifcation Appoval of Ready Mixed Concete	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Submittal for Concrete Blocks	1400	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Appoval for Concrete Blocle	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
WATERPROOFING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-100	PreQualifcation Submittal for Water Proding	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-101	PreQualifcation Appoval for Water Proofing	3.00	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
FLOORING & TILES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Submittal for Tilling Materials	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Appoval for Tailing Material	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SUSPENDED CEILING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Submittal for Suspend Ceiling	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Appoval for Suspend Ceiling	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
DOORS/WINDOWS		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Submittal for Doors/Windows	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Appoval for Doors/Windows	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
FURNITURES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Submittal for Furnitures	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Appoval for Furnitures	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-102	PreQualifcation Submittal for Sanitary Fixtures	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Appoval for Sanitay Fixtures	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Submittal for Water Supply Pipes	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Appoval for Water Supply Pipes	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Submittal for Sewage Drainage Pipes	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-103	PreQualifcation Appoval for Sewage/Dainage Pipes	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Submittal for Package AC Units	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Appoval for Package AC Units	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Submittal for Air Diffusers/Grills	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Appoval for Air Diffuses/Grills	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Submittal for Galvarized Ducts	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Appoval for Galvanized Ducts	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
EXHAUST FANS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Submittal for Exhaust Fans	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-104	PreQualifcation Appoval for Exhaust Fans	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00

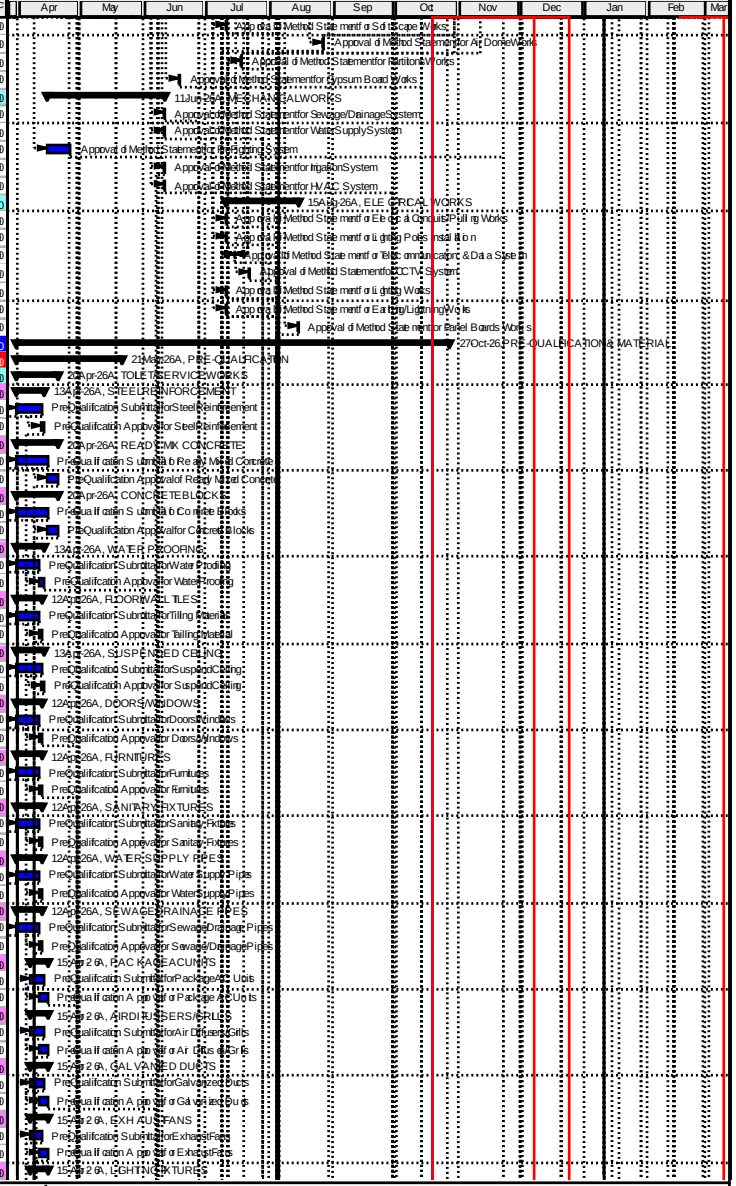


© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-102	PreQualifcation SubmittalforLighting Fixtures	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-103	PreQualifcation Appovalfor Lighting Fixtures	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforSwitches/Sockets	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-103	PreQualifcation Appovalfor Switches/Sockets	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation SubmittalforEarthing System	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation Appovalfor Eathing System	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
DISTRIBUTION PANNELS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation SubmittalforDistibution Panels	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26A	09Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation Appovalfor Distribution Panels	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		1800	0%	0%	31 Mar 26	20Apr-26	31 Mar 26A	20Apr-26A	$000	$000	$0.00	0.00
PVC MEMBRANE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation SubmittalforPVC Membane	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor PVC Membrane	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
STEEL TENSION CABLES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforSteel Tension Cables	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation Appovalfor Steel TensionCables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforEmergency Doos	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation Appovalfor EmergencyDoors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforPressue Units	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation Appovalfor Pressue Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforLockDoors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation Appovalfor lock Doors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
ARTICIAL TURF		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-107	PreQualifcation SubmittalforArtificial TURF	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor ArtificialTURF	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-107	PreQualifcation SubmittalforRubberGranules	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor RubberGranules	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADEL GLASS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforPadelGlass	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor Padel Glass	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADEL WIREMESH/STEEL SETS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforWireMesh/Steel Sets	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor WireMesh/Steel Sets	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1800	0%	0%	31 Mar 26	20Apr-26	31 Mar 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforAggregate Base Course	1800	100%	100%	31 Mar 26	20Apr-26	31 Mar 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-103	PreQualifcation Appovalfor Aggregate BaseCourse	3.00	100%	100%	18 Apr 26	20Apr-26	18 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		7.00	0%	0%	07 Apr 26	14Apr-26	07 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation Appovalfor the Site	3.00	100%	100%	12 Apr 26	14Apr-26	12 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1200	0%	0%	07 Apr 26	20Apr-26	07 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforInterlocking Block Paves	8.00	100%	100%	07 Apr 26	15Apr-26	07 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation Appovalfor Interbcking BlockPavers	5.00	100%	100%	15 Apr 26	20Apr-26	15 Apr 26A	20Apr-26A	$000	$000	$0.00	0.00
MARKINGPAINT		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-104	PreQualifcation SubmittalforMarking Paint	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor MakingPaint	1.00	100%	100%	12 Apr 26	12Apr-26	12 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation SubmittalforPackageAC Units	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor PackageAC Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation SubmittalforAir Dfusses/Grills	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor Air Dfusses/Grills	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation SubmittalforGalvarized Duct	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor Galvanized Duct	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation SubmittalforExhaustFans	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-105	PreQualifcation Appovalfor ExhaustFans	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
DISTRBUTION BOARDS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation SubmittalforDistibution Boards	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-106	PreQualifcation Appovalfor Distribution Boards	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00

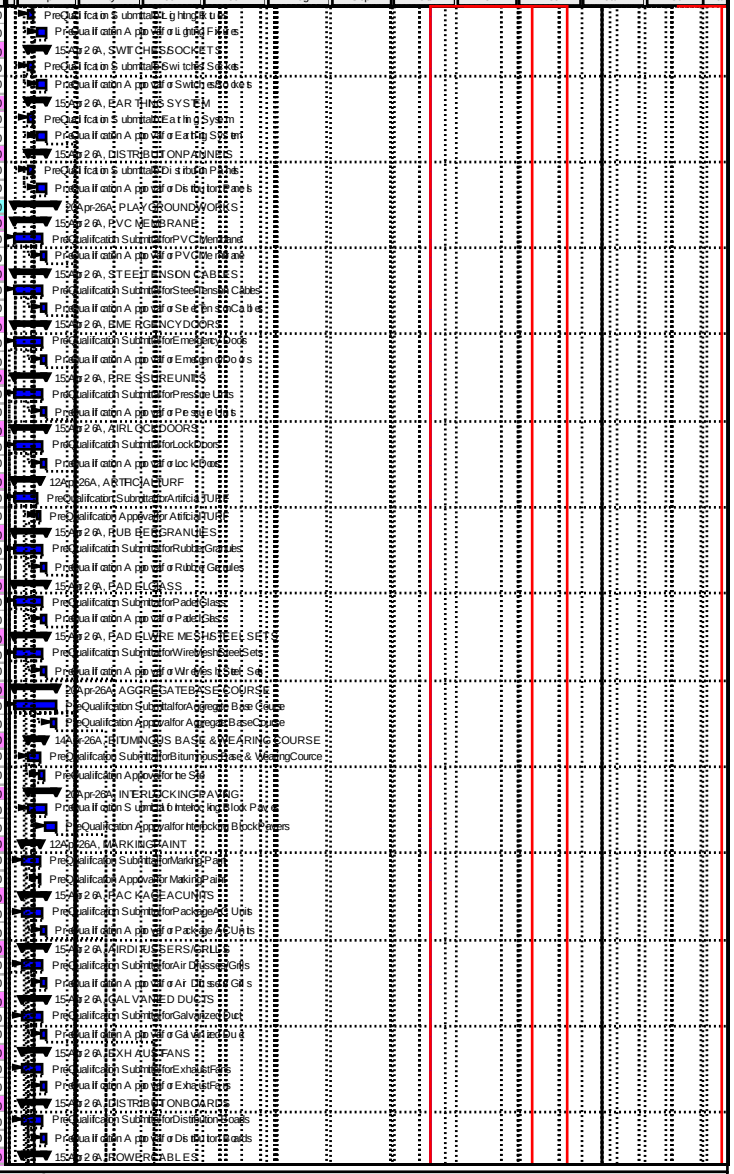

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-108	PreQualification Submittal for Power Cables	9.0d	100%	100%	04 Apr 26	13A pr-26	04 Apr 26A	13A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for Power Cables	3.0d	100%	100%	13 Apr 26	15A pr-26	13 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
LIGHT FIXTURES		11.0d	0%	0%	04 Apr 26	15A pr-26	04 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Light Fixtures	9.0d	100%	100%	04 Apr 26	13A pr-26	04 Apr 26A	13A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for light fixtures	3.0d	100%	100%	13 Apr 26	15A pr-26	13 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
CCTV MATERIALS		11.0d	0%	0%	04 Apr 26	15A pr-26	04 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Submittal for CCTV	9.0d	100%	100%	04 Apr 26	13A pr-26	04 Apr 26A	13A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Approval for CCTV	3.0d	100%	100%	13 Apr 26	15A pr-26	13 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
POWER OUTLETS/SWITCHES		11.0d	0%	0%	04 Apr 26	15A pr-26	04 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Submittal for Power Outlets/Switches	9.0d	100%	100%	04 Apr 26	13A pr-26	04 Apr 26A	13A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Approval for Power Outlets Switches	3.0d	100%	100%	13 Apr 26	15A pr-26	13 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
LANDSCAPE WORKS		42.0d	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.0d
INTERLOCKING PAVING		15.0d	0%	0%	04 Apr 26	20A pr-26	04 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Submittal for Interlocking Block Pavers	11.0d	100%	100%	04 Apr 26	15A pr-26	04 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Approval for Interlocking Block Pavers	5.0d	100%	100%	15 Apr 26	20A pr-26	15 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
CURB STONE		15.0d	0%	0%	04 Apr 26	20A pr-26	04 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Curb stone	11.0d	100%	100%	04 Apr 26	15A pr-26	04 Apr 26A	15A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for Curb stone	5.0d	100%	100%	15 Apr 26	20A pr-26	15 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
PAVEMENT MARKING		8.0d	0%	0%	04 Apr 26	12A pr-26	04 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Pavement Markings	3.0d	100%	100%	04 Apr 26	06A pr-26	04 Apr 26A	06A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-101	PreQualification Approval for Pavement Markings	5.0d	100%	100%	07 Apr 26	12A pr-26	07 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
TRAFFIC SIGNS		14.0d	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-100	PreQualification Submittal for Traffic Signs	1.0d	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-101	PreQualification Approval for Traffic Signs	1.0d	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.0d
IRRIGATION PIPES/SPRINKLERS		42.0d	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-101	PreQualification Submittal for Irrigation Pipes/Sprinkles	20.0d	100%	100%	04 Apr 26	26A pr-26	04 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-101	PreQualification Approval for Irrigation Pipes Sprinkles	1.0d	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.0d
AGRICULTURE SOIL		42.0d	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Agriculture Soil	20.0d	100%	100%	04 Apr 26	26A pr-26	04 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for Agicuture Soil	1.0d	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.0d
TRACK SURFACE		8.0d	0%	0%	04 Apr 26	12A pr-26	04 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Track Surface	3.0d	100%	100%	04 Apr 26	06A pr-26	04 Apr 26A	06A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for Track Surface	5.0d	100%	100%	07 Apr 26	12A pr-26	07 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
GRASS/TREES		14.0d	0%	0%	04 Apr 26	19A pr-26	04 Apr 26A	19A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Submittal for Grass/Trees	10.0d	100%	100%	04 Apr 26	14A pr-26	04 Apr 26A	14A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-108	PreQualification Approval for Gass/Trees	5.0d	100%	100%	14 Apr 26	19A pr-26	14 Apr 26A	19A pr-26A	$000	$000	$0.00	0.0d
CABLES		2.0d	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Submittal for Cables	1.0d	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-107	PreQualification Approval for Cables	1.0d	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.0d
LIGHT POLES		2.0d	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-997	PreQualification Submittal for Lighting poles	1.0d	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-998	PreQualification Approval for Lighting poles	1.0d	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.0d
MATERIALS SUBMITTAL		171.0d	0%	0%	07 Apr 26	18Jul-26	07 Apr 26A	27Oct-26	$000	$000	$0.00	-86.0d
TOILET SERVICE WORKS		164.0d	0%	0%	11 Apr 26	12Jul-26	11 Apr 26A	22Jul-26A	$000	$000	$0.00	-90.0d
STEEL REINFORCEMENT		2.0d	0%	0%	11 Apr 26	12A pr-26	11 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-899	Material Submittal for Steel Reinforement	1.0d	100%	100%	11 Apr 26	11A pr-26	11 Apr 26A	11A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-910	Material Approval for Steel Reinbrcement	2.0d	100%	100%	11 Apr 26	12A pr-26	11 Apr 26A	12A pr-26A	$000	$000	$0.00	0.0d
READY MIX CONCRETE		10.0d	0%	0%	15 Apr 26	26A pr-26	15 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-900	Material Submittal for Ready Mixed Concrete	3.0d	100%	100%	15 Apr 26	18A pr-26	15 Apr 26A	18A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-901	Material Approval of Ready Mixed Concrete	7.0d	100%	100%	19 Apr 26	26A pr-26	19 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
CONCRETE BLOCKS		10.0d	0%	0%	15 Apr 26	26A pr-26	15 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-915	Material Submittal for Concrete Blocks	3.0d	100%	100%	15 Apr 26	18A pr-26	15 Apr 26A	18A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-920	Material Approval for Concete Bbcks	7.0d	100%	100%	19 Apr 26	26A pr-26	19 Apr 26A	26A pr-26A	$000	$000	$0.00	0.0d
FLOOR/WALL TILES		88.0d	0%	0%	15 Apr 26	12Jul-26	15 Apr 26A	22Jul-26A	$000	$000	$0.00	-90.0d
MLTX-02-004EN-921	Material Submittal for Tiling Materials	3.0d	100%	100%	15 Apr 26	18A pr-26	15 Apr 26A	18A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-922	Material Approval for Tiling Material	7.0d	100%	100%	05 Jul-26	12Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	6.0d
SUSPENDED CEILING		5.0d	0%	0%	15 Apr 26	20A pr-26	15 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-923	Material Submittal for Suspend Ceiling	3.0d	100%	100%	15 Apr 26	18A pr-26	15 Apr 26A	18A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-924	Material Approval for Suspend Ceiling	2.0d	100%	100%	19 Apr 26	20A pr-26	19 Apr 26A	20A pr-26A	$000	$000	$0.00	0.0d
DOORS/WINDOWS		14.0d	0%	0%	06 May-26	21May-26	06 May 26A	21May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-925	Material Submittal for Doors/Windows	1.0d	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-926	Material Approval for Doors/Windows	1.0d	100%	100%	21 May-26	21May-26	21 May 26A	21May-26A	$000	$000	$0.00	0.0d
FURNITURES		2.0d	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-937	Material Submittal for Furnitures	1.0d	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-938	Material Approval for Furnitures	1.0d	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.0d
SANITARY FIXTURES		14.0d	0%	0%	15 Apr 26	30A pr-26	15 Apr 26A	30A pr-26A	$000	$000	$0.00	0.0d
MLTX-02-004EN-927	Material Submittal for Sanitary Fixtures	6.0d	100%	100%	15 Apr 26	21A pr-26	15 Apr 26A	21A pr-26A	$000	$000	$0.00	0.0d

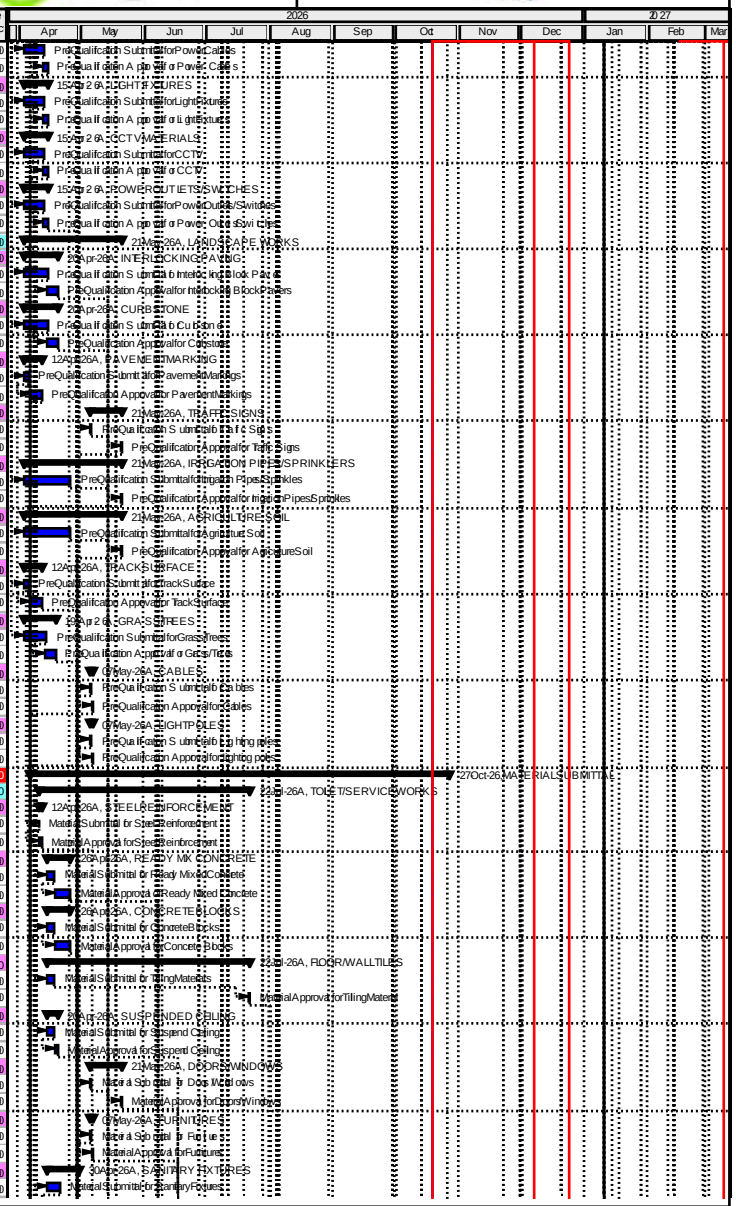

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004EN-928	Material Approval for Sanitary fixtures	1100	100%	100%	19 Apr 26	30A pr-26	19 Apr 26 A	30A pr-26A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		2.00	0%	0%	15 Apr 26	16A pr-26	15 Apr 26 A	16A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-929	Material Submittal for Water Supply Pipes	1.00	100%	100%	15 Apr 26	15A pr-26	15 Apr 26 A	15A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-930	Material Approval for Water Supply Pipes	2.00	100%	100%	15 Apr 26	16A pr-26	15 Apr 26 A	16A pr-26A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		2.00	0%	0%	15 Apr 26	16A pr-26	15 Apr 26 A	16A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-931	Material Submittal for Sewage/Drainage Pipes	1.00	100%	100%	15 Apr 26	15A pr-26	15 Apr 26 A	15A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-932	Material Approval for Sewage Drainage Pipes	2.00	100%	100%	15 Apr 26	16A pr-26	15 Apr 26 A	16A pr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-940	Material Submittal for Package AC Units	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-941	Material Approval for Package AC Units	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1800	0%	0%	16 Apr 26	06May-26	16 Apr 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-942	Material Submittal for AirDiffusers/Grills	6.00	100%	100%	16 Apr 26	22A pr-26	16 Apr 26 A	22A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-943	Material Approval for AirDiffusers/Grills	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		11300	0%	0%	13 Jun 26	11Jul-26	13 Jun 26 A	17Jun-26A	$000	$000	$0.00	20.00
MLTX-02-004EN-944	Material Submittal for GalvanizedDucts	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-945	Material Approval for GalvanizedDucts	6.00	100%	100%	05 Jul-26	11Jul-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	5.00
EXHAUST FANS		1800	0%	0%	16 Apr 26	06May-26	16 Apr 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-946	Material Submittal for Exhaust Fans	2.00	100%	100%	16 Apr 26	18A pr-26	16 Apr 26 A	18A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-947	Material Approval for Exhaust Fans	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	16 Apr 26	25A pr-26	16 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-933	Material Submittal for Lighting Fixtures	3.00	100%	100%	16 Apr 26	19A pr-26	16 Apr 26 A	19A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-934	Material Approval for Lighting Fixtures	5.00	100%	100%	20 Apr 26	25A pr-26	20 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	16 Apr 26	25A pr-26	16 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-935	Material Submittal for Switches/Sockets	3.00	100%	100%	16 Apr 26	19A pr-26	16 Apr 26 A	19A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-936	Material Approval for Switches/Sockets	5.00	100%	100%	20 Apr 26	25A pr-26	20 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		2.00	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-915	Material Submittal for EathingSystem	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-916	Material Approval for Earthing System	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		8.00	0%	0%	16 Apr 26	25A pr-26	16 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-917	Material Submittal for DistributionPanels	3.00	100%	100%	16 Apr 26	19A pr-26	16 Apr 26 A	19A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-918	Material Approval for Distibuton Panels	5.00	100%	100%	20 Apr 26	25A pr-26	20 Apr 26 A	25A pr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		16700	0%	0%	12 Apr 26	12Jul-26	12 Apr 26 A	27Oct-26	$000	$000	$0.00	-91.00
PVC MEMBRANE		14600	0%	0%	06 May-26	12Jul-26	06 May 26 A	27Oct-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-957	Material Approval for PVC Membane	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-956	Material Submittal for PVC Membrane	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
STEEL TENSION CABLES		14600	0%	0%	06 May-26	12Jul-26	06 May 26 A	27Oct-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-988	Material Approval for Steel Tension Cables	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-958	Material Submittal for Steel TensionCables	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		14600	0%	0%	06 May-26	12Jul-26	06 May 26 A	27Oct-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-988	Material Approval for Emergency Doors	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-955	Material Submittal for Emegency Doors	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		14300	0%	0%	06 May-26	12Jul-26	06 May 26 A	24Aug-26A	$000	$000	$0.00	-37.00
MLTX-02-004EN-960	Material Submittal for PressureUnits	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-990	Material Approval for Pressure Units	7.00	100%	100%	05 Jul-26	12Jul-26	21 Aug 26 A	24Aug-26A	$000	$000	$0.00	6.00
AIRLOCK DOORS		14600	0%	0%	06 May-26	12Jul-26	06 May 26 A	27Oct-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-991	Material Approval for LockDoors	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-961	Material Submittal for Lock Doors	5.00	100%	100%	06 May-26	11May-26	06 May 26 A	11May-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1700	0%	0%	12 Apr 26	30A pr-26	12 Apr 26 A	30A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-976	Material Submittal for Artificial TURF	1500	100%	100%	12 Apr 26	28A pr-26	12 Apr 26 A	28A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-992	Material Approval for Artificial TURF	3.00	100%	100%	28 Apr 26	30A pr-26	28 Apr 26 A	30A pr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-977	Material Submittal for Rubber Granules	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-993	Material Approval for RubberGranules	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
PADEL GLASS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-978	Material Submittal for Padel Glass	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-994	Material Approval for PadelGlass	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		13000	0%	0%	25 May-26	12Jul-26	25 May 26 A	27Oct-26	$000	$000	$0.00	-91.00
MLTX-02-004EN-995	Material Approval for Wie Mesh/Steel Sets	7.00	100%	0%	05 Jul-26	12Jul-26	20 Oct 26	27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004EN-975	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25 May-26	25May-26	25 May 26 A	25May-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-948	Material Submittal for Package ACUnits	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-949	Material Approval for Package AC Units	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		2100	0%	0%	13 Apr 26	06May-26	13 Apr 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-950	Material Submittal for AirDiffusersGrills	9.00	100%	100%	13 Apr 26	22A pr-26	13 Apr 26 A	22A pr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-951	Material Approval for AirDiffusers/Grills	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
AGGREGATE BASE COURSE		3300	0%	0%	21 May-26	01Jul-26	21 May 26 A	01Jul-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-902	Material Submittal for AggregateBase Cairse	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00

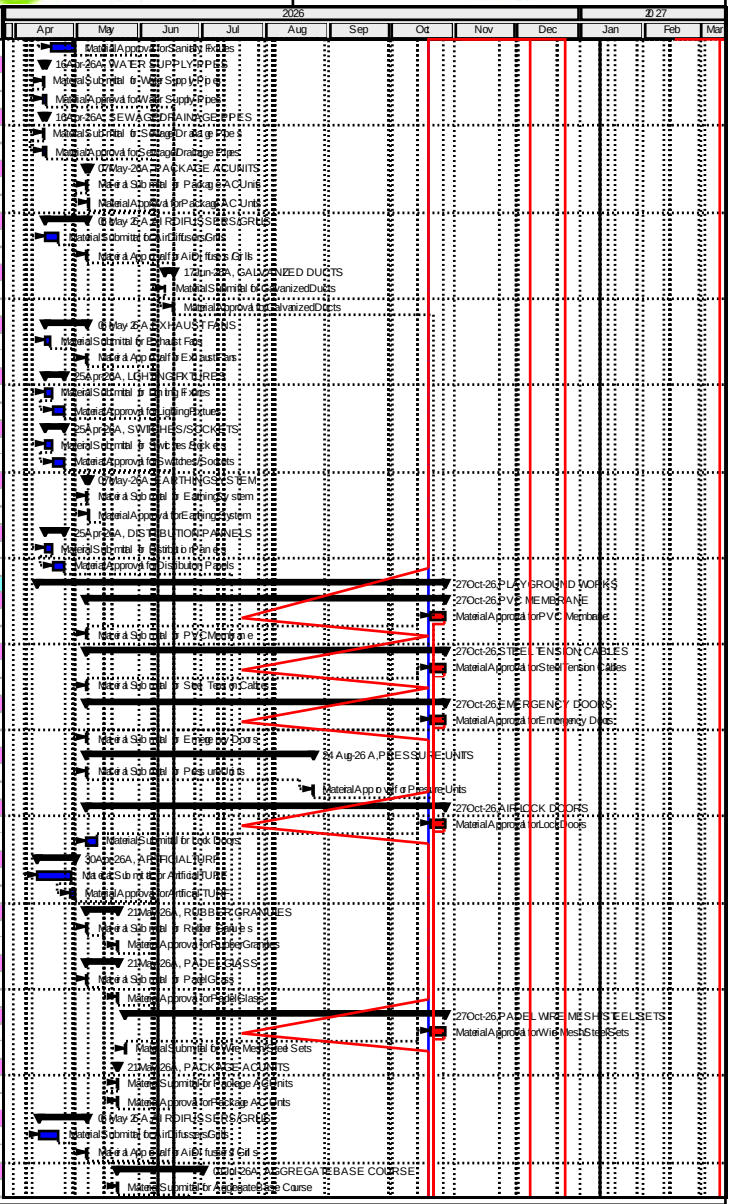


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02-004EN-903	Material Approval for Aggregate Base Course	1.00	100%	100%	01-Jul-26	01-Jul-26	01-Jul-26A	01-Jul-26A	$000	$000	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		2.00	0%	0%	16-Apr-26	18-Apr-26	16-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-904	Material Submittal for Bituminous Base& Wearing Couce	2.00	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-905	Material Approval for the Site	1.00	100%	100%	18-Apr-26	18-Apr-26	18-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-906	Material Submittal for Interlocking Block Pavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-911	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MARKING PAINT		6.00	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-938	Material Submittal for Making Paint	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-996	Material Approval for Marking Paint	2.00	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		113.00	0%	0%	13-Jun-26	11-Jul-26	13-Jun-26A	08-Aug-26A	$000	$000	$0.00	-24.00
MLTX02-004EN-952	Material Submittal for Galvanized Duct	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-953	Material Approval for Galvanized Duct	6.00	100%	100%	05-Jul-26	11-Jul-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.00	5.00
EXHAUST FANS		21.00	0%	0%	13-Apr-26	06-May-26	13-Apr-26A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-954	Material Submittal for Exhaust Fans	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-955	Material Approval for Exhaust Fans	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
DISTRIBUTION BOARDS		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-962	Material Submittal for Distribution Boards	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-963	Material Approval for Distibuton Boards	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
POWER CABLES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-964	Material Submittal for Power Cables	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-965	Material Approval for Power Cables	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
LIGHT FIXTURES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-966	Material Submittal for Light Fixtures	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-967	Material Approval for Light Fixtures	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-968	Material Submittal for CCTV	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-969	Material Approval for CCTV	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
POWER OUTLETS/SWITCHES		2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-970	Material Submittal for Power Outlets/Switches	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-971	Material Approval for Power Outlets/Switches	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		98.00	0%	0%	07-Apr-26	18-Jul-26	07-Apr-26A	27-Jul-26A	$000	$000	$0.00	-8.00
INTERLOCKING PAVING		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-974	Material Submittal for Interlocking Block Pavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-975	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
CURBSTONE		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-984	Material Submittal for Cubstone	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-985	Material Approval for Curbstone	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
PAVEMENT MARKING		6.00	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-907	Material Submittal for Pavement Makings	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-912	Material Approval for Pavement Makings	2.00	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
TRAFFIC SIGNS		65.00	0%	0%	06-May-26	11-Jul-26	06-May-26 A	18-Jul-26A	$000	$000	$0.00	-6.00
MLTX02-004EN-908	Material Submittal for Traffic Signs	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-909	Material Approval for Traffic Signs	6.00	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26 A	18-Jul-26A	$000	$000	$0.00	5.00
IRRGATION PIPES&SPRINKLERS		93.00	0%	0%	13-Apr-26	18-Jul-26	13-Apr-26A	27-Jul-26A	$000	$000	$0.00	-8.00
MLTX02-004EN-913	Material Submittal for Irrigation Pipes/Sprinkles	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-914	Material Approval for Irrigation Pipes/Sprinkles	6.00	100%	100%	12-Jul-26	18-Jul-26	27-Jul-26 A	27-Jul-26A	$000	$000	$0.00	5.00
AGRICULTURE SOIL		14.00	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-980	Material Submittal for Agriculture Soil	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-981	Material Approval for Agriculture Soil	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		14.00	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-982	Material Submittal for Track Suface	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-983	Material Approval for Track Surface	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
GRASS/TREES		14.00	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-986	Material Submittal for Grass/Trees	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-987	Material Approval for Grass/Trees	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
CABLES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-972	Material Submittal for Cables	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-973	Material Approval for Cables	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26A	22-Apr-26A	$000	$000	$0.00	0.00
LIGHT POLES		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-897	Material Submittal for Lightingpoles	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-898	Material Approval for Lightingpoles	1.00	100%	100%	07-Apr-26	07-Apr-26	07-Apr-26A	07-Apr-26A	$000	$000	$0.00	0.00
PROCUREMENT		246.00	0%	0%	06-May-26	07-Nov-26	06-May-26 A	21-Feb-27	$000	$000	$0.00	-91.00
SHORT HEAD ITEM		207.00	0%	0%	06-May-26	21-Oct-26	06-May-26 A	06-Jan-27	$000	$000	$0.00	-66.00
TOILETS SERVICE WORKS		182.00	0%	0%	06-May-26	24-Sep-26	06-May-26 A	11-Nov-26	$000	$000	$0.00	-41.00
STEEL REINFORCEMENT		13.00	0%	0%	13-May-26	31-May-26	13-May-26 A	31-May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-9970	PO for Steel Reinforcement	2.00	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26A	$000	$000	$0.00	0.00

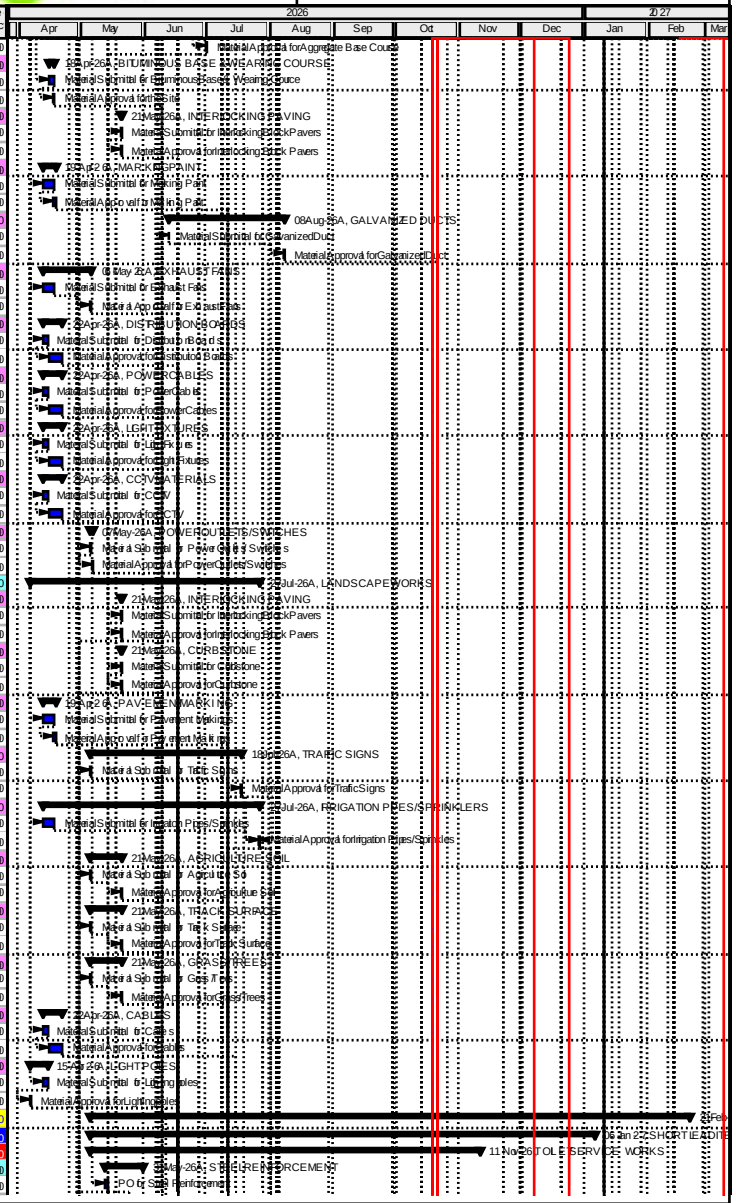

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX020040PR-10070	MaterialDelivery ofSteelReinforcement	1.0	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.0
CONCRETE BLOCKS		7200	0%	0%	06-May-26	09-Jul-26	06-May-26A	27-Jul-26A	$000	$000	$0.00	-1500
MLTX020040PR-10150	PO for ConcreteBlocks	1.0	100%	100%	06-May-26	06-May-26	06-May-26A	06-May-26A	$000	$000	$0.00	0.0
MLTX020040PR-10160	MaterialDelivery ofConcrete Blocks	5.0	100%	100%	05-Jul-26	09-Jul-26	27-Jul-26A	27-Jul-26A	$000	$000	$0.00	4.0
FLOORWALLTILES		2800	0%	0%	19-Jul-26	08-Aug-26	08-Aug-26A	12-Aug-26A	$000	$000	$0.00	13.0
MLTX020040PR-10170	PO for TilingMaterials	5.0	100%	100%	19-Jul-26	23-Jul-26	08-Aug-26A	08-Aug-26A	$000	$000	$0.00	4.0
MLTX020040PR-10180	MaterialDelivery ofTailingMaterial	1300	100%	100%	25-Jul-26	08-Aug-26	12-Aug-26A	12-Aug-26A	$000	$000	$0.00	12.0
SUSPENDED CEILING		1800	0%	0%	05-Jul-26	25-Jul-26	08-Aug-26A	10-Oct-26A	$000	$000	$0.00	-3600
MLTX020040PR-10190	PO for Suspend Ceiling	5.0	100%	100%	05-Jul-26	09-Jul-26	08-Aug-26A	08-Aug-26A	$000	$000	$0.00	4.0
MLTX020040PR-10200	MaterialDelivery ofSuspendCeiling	1300	100%	100%	11-Jul-26	25-Jul-26	10-Oct-26A	10-Oct-26A	$000	$000	$0.00	12.0
DOORS/WINDOWS		10700	0%	0%	24-Jun-26	15-Jul-26	24-Jun-26A	10-Oct-26A	$000	$000	$0.00	-7300
MLTX020040PR-10210	PO for Doors/Windows	1.0	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26A	24-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10220	MaterialDelivery for Doors/Windows	1000	100%	100%	05-Jul-26	15-Jul-26	10-Oct-26A	10-Oct-26A	$000	$000	$0.00	9.0
WATERSUPPLYPIPES		1.0	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10250	PO for Water Supply Pipes	1.0	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10260	MaterialDelivery for Water Supply Pipes	1.0	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
SEWAGEDRAINAGEPIPES		1.0	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10270	PO for Sewage/Drainage Pipes	1.0	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10280	MaterialDelivery for SewageDrainage Pipes	1.0	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.0
SANITARYFIXTURES		12600	0%	0%	16-Jun-26	29-Jul-26	16-Jun-26A	03-Aug-26A	$000	$000	$0.00	-400
MLTX020040PR-10230	PO for SanitaryFixtures	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10240	MaterialDelivery for SanitaryFixtures	1200	100%	100%	16-Jul-26	29-Jul-26	03-Aug-26A	03-Aug-26A	$000	$000	$0.00	11.0
PACKAGE ACUNITS		11700	0%	0%	16-Jun-26	10-Aug-26	16-Jun-26A	31-Oct-26	$000	$000	$0.00	-6900
MLTX020040PR-10380	MaterialDelivery for Package AC Units	1000	100%	0%	30-Jul-26	10-Aug-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.0
MLTX020040PR-10370	PO for Package AC Units	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
AIRDIFUSSERS/GRILLS		14600	0%	0%	16-Jun-26	22-Aug-26	16-Jun-26A	08-Aug-26A	$000	$000	$0.00	12.0
MLTX020040PR-10390	PO for AirDiffusersGrills	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10400	MaterialDelivery for AirDiffusersGrills	1000	100%	100%	11-Aug-26	22-Aug-26	08-Aug-26A	08-Aug-26A	$000	$000	$0.00	9.0
GALVANIZED DUCTS		11700	0%	0%	16-Jun-26	19-Jul-26	16-Jun-26A	08-Aug-26A	$000	$000	$0.00	-1700
MLTX020040PR-10410	PO for GalvanizedDucts	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10420	MaterialDelivery for GalvanizedDucts	1300	100%	100%	05-Jul-26	19-Jul-26	08-Aug-26A	08-Aug-26A	$000	$000	$0.00	12.0
EXHAUSTFANS		13200	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26A	17-Aug-26A	$000	$000	$0.00	-1000
MLTX020040PR-10430	PO for Exhaust Fans	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10440	MaterialDelivery for Exhaust Fans	1500	100%	100%	20-Jul-26	05-Aug-26	17-Aug-26A	17-Aug-26A	$000	$000	$0.00	14.0
LIGHTING FIXTURES		12200	0%	0%	16-Jun-26	23-Aug-26	16-Jun-26A	05-Nov-26	$000	$000	$0.00	-6300
MLTX020040PR-10300	MaterialDelivery for LightingFixtures	1500	100%	0%	06-Aug-26	23-Aug-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.0
MLTX020040PR-10290	PO for LightingFixtures	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
SWITCHES/SOCKETS		14300	0%	0%	24-Jun-26	31-Aug-26	24-Jun-26A	10-Oct-26A	$000	$000	$0.00	-3300
MLTX020040PR-10310	PO for Switches/Sockets	1.0	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26A	24-Jun-26A	$000	$000	$0.00	0.0
MLTX020040PR-10320	MaterialDelivery for Switches/Sockets	7.0	100%	100%	24-Aug-26	31-Aug-26	05-Oct-26A	10-Oct-26A	$000	$000	$0.00	2.0
EARTHINGSYSTEM		1.0	0%	0%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.0
MLTX020040PR-10110	PO for EarthingSystem	1.0	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.0
MLTX020040PR-10120	MaterialDelivery for EarthingSystem	1.0	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.0
DISTRIBUTION PANNELS		9100	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26A	05-Nov-26	$000	$000	$0.00	-7100
MLTX020040PR-10140	MaterialDelivery for Distibuton Panels	1500	100%	0%	11-Jul-26	27-Jul-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.0
MLTX020040PR-10130	PO for DistributionPanels	5.0	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.0
FURNITURES		12700	0%	0%	16-Jun-26	24-Sep-26	16-Jun-26A	11-Nov-26	$000	$000	$0.00	-4100
MLTX020040PR-10340	MaterialDelivery for Furnitures	2000	100%	0%	01-Sep-26	24-Sep-26	20-Oct-26	11-Nov-26	$000	$000	$0.00	0.0
MLTX020040PR-10330	PO for Furnitures	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
PLAYGROUND WORKS		20600	0%	0%	07-May-26	21-Oct-26	07-May-26A	06-Jan-27	$000	$000	$0.00	-6600
PVC MEMBRANE		11100	0%	0%	16-Jun-26	08-Jul-26	16-Jun-26A	24-Oct-26	$000	$000	$0.00	-9100
MLTX020040PR-10540	MaterialDelivery for PVC Membrane	4.0	100%	0%	05-Jul-26	08-Jul-26	20-Oct-26	24-Oct-26	$000	$000	$0.00	0.0
MLTX020040PR-10530	PO for PVC Membrane	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
ARTIFICIAL TURF		12300	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26A	07-Nov-26	$000	$000	$0.00	-9100
MLTX020040PR-10780	MaterialDelivery for Artificial TURF	1200	100%	0%	09-Jul-26	22-Jul-26	25-Oct-26	07-Nov-26	$000	$000	$0.00	0.0
MLTX020040PR-10770	PO for Artificial TURF	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
RUBBER GRANULES		13500	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26A	21-Nov-26	$000	$000	$0.00	-9100
MLTX020040PR-10800	MaterialDelivery for Rubber Granules	1200	100%	0%	23-Jul-26	05-Aug-26	08-Nov-26	21-Nov-26	$000	$000	$0.00	0.0
MLTX020040PR-10790	PO for Rubber Granules	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
PADEL GLASS		15300	0%	0%	16-Jun-26	26-Aug-26	16-Jun-26A	12-Dec-26	$000	$000	$0.00	-9100
MLTX020040PR-10820	MaterialDelivery for PadelGlass	1800	100%	0%	06-Aug-26	26-Aug-26	22-Nov-26	12-Dec-26	$000	$000	$0.00	0.0
MLTX020040PR-10810	PO for Padel Glass	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
PADEL WIRE MESH/STEEL SETS		16800	0%	0%	16-Jun-26	13-Sep-26	16-Jun-26A	29-Dec-26	$000	$000	$0.00	-9100
MLTX020040PR-10840	MaterialDelivery for Wire Mesh/SteelSets	1500	100%	0%	27-Aug-26	13-Sep-26	13-Dec-26	29-Dec-26	$000	$000	$0.00	0.0
MLTX020040PR-10830	PO for Wire Mesh/SteelSets	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0
AGGREGATE BASECOURSE		1.0	0%	0%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.0
MLTX020040PR-9980	PO for AggregateBase Course	1.0	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.0

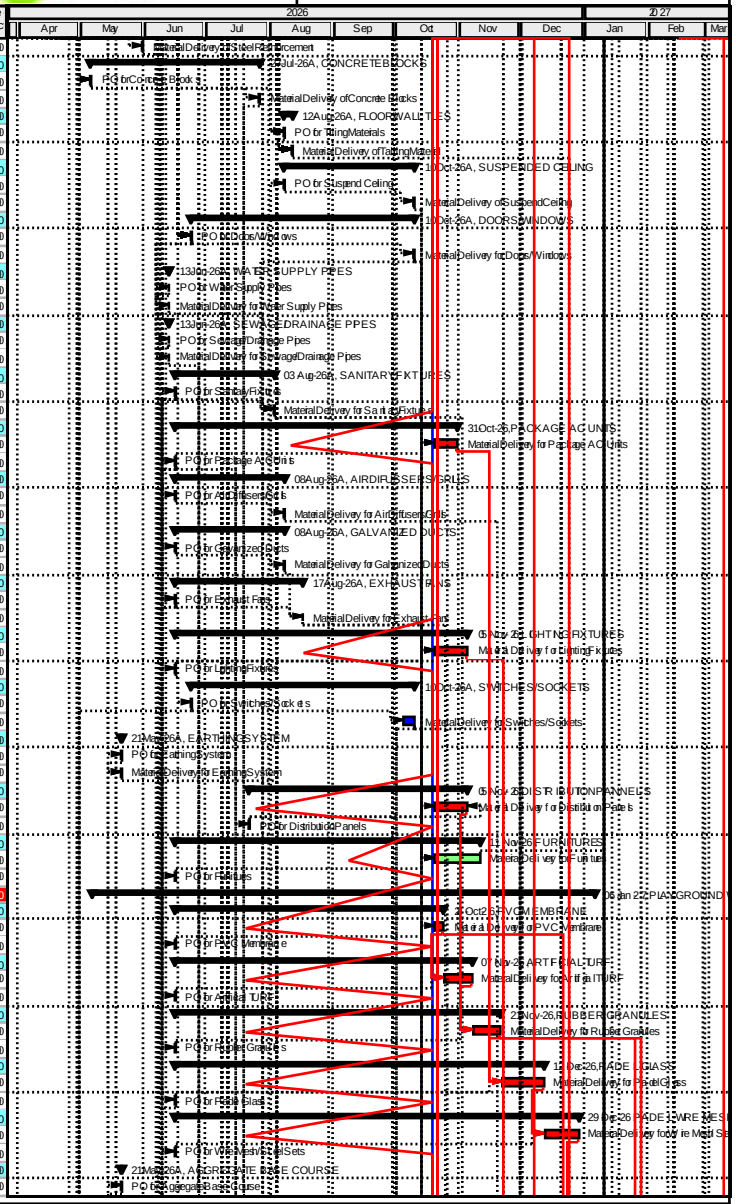

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX02.000.4PR-9990	MaterialDelivery for AggegateBase Course	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		7.00	0%	0%	16-Jun-26	23-Jun-26	16-Jun-26 A	23-Jun-26A	$000	$000	$0.00	0.00
MLTX02.000.4PR-10000	PO for BituminousBase &Wearing Course	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.000.4PR-10010	MaterialDelivery for theSite	1.00	100%	100%	23-Jun-26	23-Jun-26	23-Jun-26 A	23-Jun-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		206.00	0%	0%	07-May-26	21-Sep-26	07-May-26 A	06-Jan-27	$000	$000	$0.00	-91.00
MLTX02.000.4PR-10030	MaterialDelivery for Interlocking Block Pavers	7.00	100%	0%	14-Sep-26	21-Sep-26	30-Dec-26	06-Jan-27	$000	$000	$0.00	0.00
MLTX02.000.4PR-10020	PO for InterlockingBlock Pavers	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MARKINGPAINT		87.00	0%	0%	05-Jul-26	19-Jul-26	13-Jul-26A	27-Oct-26	$000	$000	$0.00	-74.00
MLTX02.000.4PR-10360	MaterialDelivery for Marking Paint	7.00	100%	0%	12-Jul-26	19-Jul-26	20-Oct-26	27-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10350	PO for Making Paint	6.00	100%	100%	05-Jul-26	11-Jul-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	5.00
PACKAGE ACUNITS		129.00	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26 A	14-Nov-26	$000	$000	$0.00	-85.00
MLTX02.000.4PR-10460	MaterialDelivery for Package AC Units	15.00	100%	0%	20-Jul-26	05-Aug-26	28-Oct-26	14-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10450	PO for Package AC Units	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/ GRILLS		141.00	0%	0%	16-Jun-26	23-Aug-26	16-Jun-26 A	08-Aug-26A	$000	$000	$0.00	13.00
MLTX02.000.4PR-10470	PO for AirDifussersGrills	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.000.4PR-10480	MaterialDelivery for AirDifussers/Grills	15.00	100%	100%	06-Aug-26	23-Aug-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.00	14.00
GALVANIZED D UCTS		156.00	0%	0%	16-Jun-26	09-Sep-26	16-Jun-26 A	08-Aug-26A	$000	$000	$0.00	28.00
MLTX02.000.4PR-10490	PO for GalvanizedDuct	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.000.4PR-10500	MaterialDelivery for GalvanizedDuct	15.00	100%	100%	24-Aug-26	09-Sep-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.00	14.00
EXHAUST FANS		171.00	0%	0%	16-Jun-26	28-Sep-26	16-Jun-26 A	17-Aug-26A	$000	$000	$0.00	35.00
MLTX02.000.4PR-10510	PO for Exhaust Fans	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.000.4PR-10520	MaterialDelivery for Exhaust Fans	15.00	100%	100%	10-Sep-26	28-Sep-26	17-Aug-26 A	17-Aug-26A	$000	$000	$0.00	14.00
DISTRBUTION BOARDS		91.00	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26A	05-Nov-26	$000	$000	$0.00	-71.00
MLTX02.000.4PR-10640	MaterialDelivery for Distibuton Boards	15.00	100%	0%	11-Jul-26	27-Jul-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10630	PO for DistributionBoards	5.00	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.00
POWERCABLES		71.00	0%	0%	28-Jul-26	13-Aug-26	22-Jul-26A	31-Oct-26	$000	$000	$0.00	-71.00
MLTX02.000.4PR-10660	MaterialDelivery for PowerCables	10.00	100%	0%	03-Aug-26	13-Aug-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10650	PO for PowerCables	5.00	100%	100%	28-Jul-26	02-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.00
LIGHTFIXTURES		21.00	0%	0%	15-Aug-26	07-Sep-26	01-Nov-26	24-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10670	PO for Light Fixtures	5.00	100%	0%	15-Aug-26	19-Aug-26	01-Nov-26	05-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10680	MaterialDelivery for Light Fixtures	16.00	100%	0%	20-Aug-26	07-Sep-26	07-Nov-26	24-Nov-26	$000	$000	$0.00	0.00
CCTV MATERIA IS		30.00	0%	0%	08-Sep-26	21-Oct-26	25-Nov-26	29-Dec-26	$000	$000	$0.00	7.00
MLTX02.000.4PR-10690	PO for CCTV	1.00	100%	0%	08-Sep-26	25-Nov-26	25-Nov-26	06-Dec-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10700	MaterialDelivery for CCTV	20.00	90%	0%	29-Sep-26	21-Oct-26	07-Dec-26	29-Dec-26	$000	$000	$0.00	0.00
POWEROUTLE TS/ SWITCHES		21.00	0%	0%	20-Sep-26	14-Oct-26	07-Dec-26	30-Dec-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10710	PO for PowerOutlets/Switches	6.00	100%	0%	20-Sep-26	27-Sep-26	07-Dec-26	13-Dec-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10720	MaterialDelivery for PowerOutlets/Switches	15.00	100%	0%	28-Sep-26	14-Oct-26	14-Dec-26	30-Dec-26	$000	$000	$0.00	0.00
LANDSCAPE WORKS		168.00	0%	0%	07-May-26	04-Oct-26	07-May-26 A	23-Nov-26	$000	$000	$0.00	-43.00
INTERLOCKING PAVING		148.00	0%	0%	07-May-26	15-Jul-26	07-May-26 A	31-Oct-26	$000	$000	$0.00	-91.00
MLTX02.000.4PR-10760	MaterialDelivery for Interlocking Block Pavers	10.00	100%	0%	05-Jul-26	15-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10750	PO for InterlockingBlock Pavers	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
CURBSTONE		148.00	0%	0%	07-May-26	15-Jul-26	07-May-26 A	31-Oct-26	$000	$000	$0.00	-91.00
MLTX02.000.4PR-10900	MaterialDelivery for Curbstone	10.00	100%	0%	05-Jul-26	15-Jul-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10890	PO for Cubstone	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
PAVEMENT MARKNG		80.00	0%	0%	16-Jul-26	02-Aug-26	13-Jul-26A	31-Oct-26	$000	$000	$0.00	-75.00
MLTX02.000.4PR-10050	MaterialDelivery for Pavement Makings	10.00	100%	0%	22-Jul-26	02-Aug-26	20-Oct-26	31-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10040	PO for Pavement Makings	5.00	100%	100%	16-Jul-26	21-Jul-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
TRAFFC SIGNS		79.00	0%	0%	03-Aug-26	18-Aug-26	13-Jul-26A	29-Oct-26	$000	$000	$0.00	-75.00
MLTX02.000.4PR-10080	MaterialDelivery for TrafficSigns	9.00	100%	0%	09-Aug-26	18-Aug-26	20-Oct-26	29-Oct-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10060	PO for TafficSigns	5.00	100%	100%	03-Aug-26	08-Aug-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
IRRGATION PIPES&SPRINKLERS		96.00	0%	0%	19-Aug-26	04-Oct-26	13-Jul-26A	19-Aug-26A	$000	$000	$0.00	10.00
MLTX02.000.4PR-10090	PO for Irrigation Pipes/Spimkles	5.00	100%	100%	19-Aug-26	24-Aug-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
MLTX02.000.4PR-10100	MaterialDelivery for Irrigation Pipes/Spimkles	8.00	100%	100%	26-Sep-26	04-Oct-26	19-Aug-26 A	19-Aug-26A	$000	$000	$0.00	7.00
AGRICULTURE SOL		92.00	0%	0%	05-Jul-26	23-Jul-26	13-Jul-26A	02-Nov-26	$000	$000	$0.00	-75.00
MLTX02.000.4PR-10860	MaterialDelivery for Agriculture Sol	12.00	100%	0%	11-Jul-26	23-Jul-26	20-Oct-26	02-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10850	PO for Agriculture Sol	5.00	100%	100%	05-Jul-26	09-Jul-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
TRACK SURFACE		122.00	0%	0%	24-Jun-26	04-Aug-26	24-Jun-26 A	14-Nov-26	$000	$000	$0.00	-86.00
MLTX02.000.4PR-10880	MaterialDelivery for Track Surface	10.00	100%	0%	25-Jul-26	04-Aug-26	03-Nov-26	14-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10870	PO for Track Suface	1.00	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26A	$000	$000	$0.00	0.00
GRASS/TREES		73.00	0%	0%	05-Aug-26	27-Aug-26	13-Jul-26A	05-Nov-26	$000	$000	$0.00	-75.00
MLTX02.000.4PR-10920	MaterialDelivery for Grass/Trees	15.00	100%	0%	11-Aug-26	27-Aug-26	20-Oct-26	05-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10910	PO for Grass/Trees	5.00	100%	100%	05-Aug-26	10-Aug-26	13-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
CABLES		106.00	0%	0%	22-Jul-26	14-Sep-26	22-Jul-26A	23-Nov-26	$000	$000	$0.00	-59.00
MLTX02.000.4PR-10740	MaterialDelivery for Cables	15.00	100%	0%	29-Aug-26	14-Sep-26	07-Nov-26	23-Nov-26	$000	$000	$0.00	0.00
MLTX02.000.4PR-10730	PO for Cables	5.00	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.00
LONG LEAD ITEM		217.00	0%	0%	13-Jun-26	07-Nov-26	13-Jun-26 A	21-Feb-27	$000	$000	$0.00	-91.00
PLAYGROUND WORKS		187.00	0%	0%	13-Jun-26	06-Oct-26	13-Jun-26 A	17-Jan-27	$000	$000	$0.00	-88.00

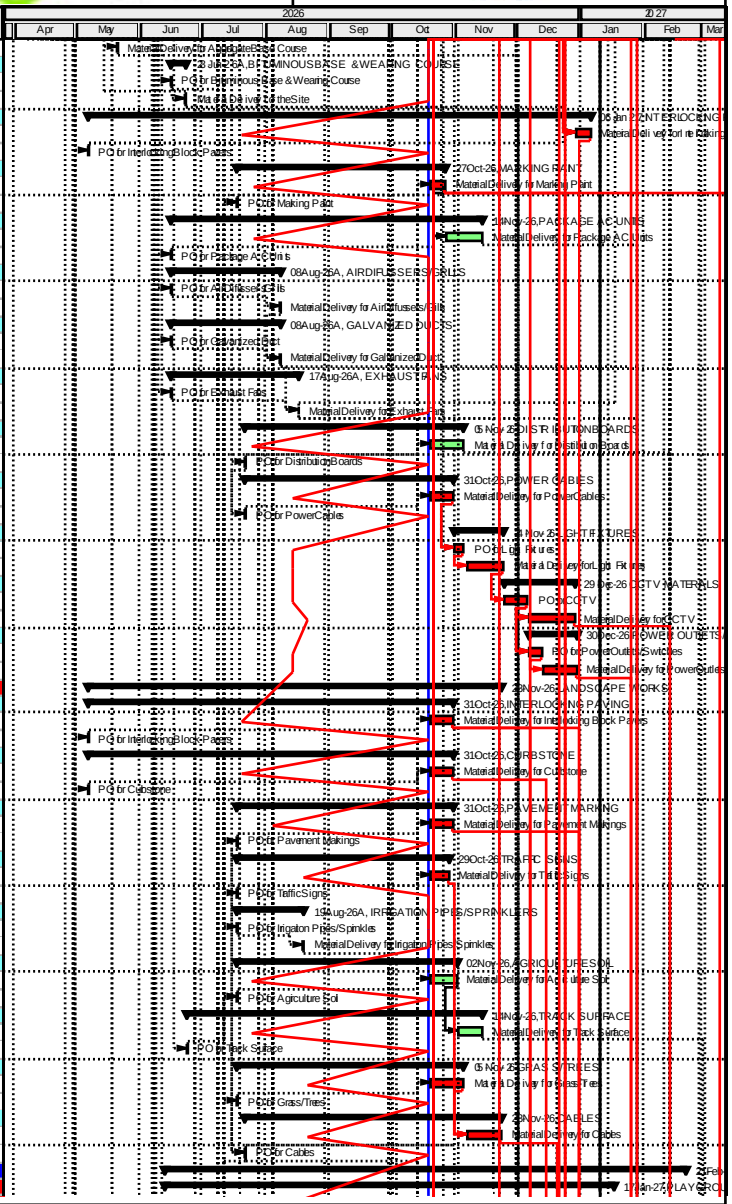

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation


MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

PROFAST

egis

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	STEELTENSION CABLES	16400	0%	0%	13 Jun 26	05Sep-26	13 Jun 26A	21Dec-26	$000	$000	$0.00	-9100
MLTX02.00.4PR-10560	MaterialDelivery for Steel Tension Cables	3000	100%	0%	25 Jul-26	27Aug-26	09 Nov 26	13Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10930	MaterialFabricationforSteelTension Cables	1000	100%	0%	13 Jul-26	23Jul-26	28 Oct 26	08Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10970	Staging time	7.00	100%	0%	29 Aug-26	05Sep-26	14 Dec 26	21Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10550	PO for Steel Tension Cables	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
	EMERGENCY DOORS	13400	0%	0%	28 Jul-26	10Sep-26	18 Jul-26A	27Dec-26	$000	$000	$0.00	-100.00
MLTX02.00.4PR-10580	MaterialDelivery for Emergency Doors	1500	100%	0%	15 Aug-26	31Aug-26	01 Nov 26	17Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10940	MaterialFabricationforEmergency Doors	1000	100%	0%	03 Aug-26	13Aug-26	20 Oct 26	31Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10980	Staging time	5.00	100%	0%	06 Sep-26	10Sep-26	22 Dec 26	27Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10570	PO for Emegency Doors	5.00	100%	100%	28 Jul-26	02Aug-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
	PRESSURE UNITS	6000	0%	0%	28 Jul-26	06Oct-26	20 Oct 26	28Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10590	PO for PressureUnits	1000	100%	0%	28 Jul-26	08Aug-26	20 Oct 26	31Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10600	MaterialDelivery for Pressure Units	2500	100%	0%	01 Sep-26	30Sep-26	24 Nov 26	22Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10950	MaterialFabricationforPressue Units	2000	100%	0%	09 Aug-26	31Aug-26	01 Nov 26	23Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10990	Staging time	5.00	100%	0%	01 Oct 26	06Oct-26	23 Dec 26	28Dec-26	$000	$000	$0.00	0.00
	AIRLOCK DOORS	6000	0%	0%	25 Jul-26	03Oct-26	09 Nov 26	17Jan-27	$000	$000	$0.00	0.00
MLTX02.00.4PR-10610	PO for Lock Doors	1000	100%	0%	25 Jul-26	04Aug-26	09 Nov 26	19Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-10620	MaterialDelivery for LockDoors	2500	100%	0%	29 Aug-26	27Sep-26	14 Dec 26	11Jan-27	$000	$000	$0.00	0.00
MLTX02.00.4PR-10960	MaterialFabricationforLock Doors	2000	100%	0%	05 Aug-26	27Aug-26	21 Nov 26	13Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11000	Staging time	5.00	100%	0%	28 Sep-26	03Oct-26	12 Jan 27	17Jan-27	$000	$000	$0.00	0.00
	LANDSCAPE WORKS	21200	0%	0%	18 Jun 26	07Nov-26	18 Jun 26A	21Feb-27	$000	$000	$0.00	-9100
	LIGHTPOLES	21200	0%	0%	18 Jun 26	07Nov-26	18 Jun 26A	21Feb-27	$000	$000	$0.00	-9100
MLTX02.00.4PR-9950	MaterialFabricationforLighting poles	3000	100%	0%	29 Aug-26	03Oct-26	14 Dec 26	17Jan-27	$000	$000	$0.00	0.00
MLTX02.00.4PR-9960	MaterialDelivery for Lightingpoles	2500	55%	0%	04 Oct 26	01Nov-26	18 Jan 27	15Feb-27	$000	$000	$0.00	0.00
MLTX02.00.4PR-11010	Staging time	5.00	0%	0%	02 Nov-26	07Nov-26	16 Feb 27	21Feb-27	$000	$000	$0.00	0.00
MLTX02.00.4PR-9940	PO for Lightingpoles	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
	CONSTR UCTION PHASE	31200	37%	2499%	02 May-26	25Jan-27	02 May 26A	09May-27	$3951,3583.1	$2669,0837.4	$10680,071.52	-8500
	SITEWORKS	31200	2872%	2219%	02 May-26	25Jan-27	02 May 26A	09May-27	$2699,8231.8	$2085,5466.0	$9 399 9 103 9	-8500
	EARTH WORKS	10900	100%	100%	02 May-26	23Jul-26	02 May 26A	10Oct-26A	$5 424 46.88	$542446.88	$5 424 46.88	-6600
MLTX-02-004CN-11 80	Excavation(inall types of soil) including Compaction(PlaygoundArea)	8.25	100%	100%	02 May-26	11May-26	02 May 26A	11May-26A	$1 330 98.00	$133098.00	$1 330 98.00	0.00
MLTX-02-004CN-11 90	Excavation(inall types of soil) including Compaction(Service/ToiletBuilding)	12.03	100%	100%	07 May-26	21May-26	07 May 26A	21May-26A	$3 232 1.25	$3 232 1.25	$32321.25	0.00
MLTX-02-004CN-11 00	Excavation(inall types of soil) including Compaction(Landscape Area)	14.14	100%	100%	06 May-26	23May-26	06 May 26A	23May-26A	$2 029 90.13	$202990.13	$2 029 90.13	0.00
MLTX-02-004CN-11 10	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	32.00	100%	100%	25 May-26	04Jul-26	25 May 26A	04Jul-26A	$2 218 1.25	$2 218 1.25	$22181.25	0.00
MLTX-02-004CN-11 20	Backfilling onLayers(Selected Soil)including Compaction (Sevice/ToiletBuilding)	14.20	100%	100%	25 May-26	14Jun-26	25 May 26A	14Jun-26A	$8 19.00	$8190.00	$8 190.00	0.00
MLTX-02-004CN-11 30	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)	9.00	100%	100%	05 Jul-26	14Jul-26	29 Aug 26A	10Oct-26A	$8 701 8.75	$8 701 8.75	$87018.75	-2700
MLTX-02-004CN-11 10R	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)Remair	8.00	100%	100%	15 Jul-26	23Jul-26	05 Jul-26A	22Aug-26A	$5 664 7.50	$5 664 7.50	$56647.50	-3320
	LANDSCAPE WORKS	21600	2463%	1762%	05 Jul-26	25Jan-27	15 Jul-26A	09May-27	$2157.3768.1	$1543.0997.3	$8 759 9 680 3	-7600
	PLAYGROUND AREA	16100	5355%	0%	05 Jul-26	16Jan-27	20 Oct 26	29Apr-27	$ 483 96.67	$000	$1 210 7 225 0	6.00
	FOOTBALLPLAYGROUND	11100	75%	0%	05 Jul-26	07Dec-26	20 Oct 26	27Feb-27	$2 583 62.50	$000	$3 451 53.00	22.00
MLTX-02-004CN-12(	Preparation andProofing for Subgrade (Football Playground)	17.00	100%	0%	05 Jul-26	23Jul-26	20 Oct 26	08Nov-26	$5 152 5.00	$000	$57525.00	0.00
MLTX-02-004CN-12(	Backfilling andCompacton ofBaseLayers(FootballPlayground)	25.00	100%	0%	25 Jul-26	22Aug-26	09 Nov 26	07Dec-26	$5 152 5.00	$000	$57525.00	0.00
MLTX-02-004CN-121	Finishingand SufaceFinish Works (Football Playground)	30.00	100%	0%	12 Sep-26	17Oct-26	28 Dec 26	31Jan-27	$1 438 12.50	$000	$1 488 12.50	0.00
MLTX-02-004CN-121	InstallSportEquipments -Goal /Nets- Football Playground	8.00	0%	0%	29 Nov-26	07Dec-26	17 Feb 27	27Feb-27	$000	$000	$71906.25	0.00
MLTX-02-004CN-121	Surface Makingand Painting(FootballPlayground)	8.00	0%	0%	29 Nov-26	07Dec-26	17 Feb 27	27Feb-27	$000	$000	$14381.25	0.00
	PADELPLAYGROUND	12300	5667%	0%	25 Jul-26	22Dec-26	09 Nov 26	05Apr-27	$1 215 50.00	$000	$2 165 0.00	6.00
MLTX-02-004CN-121	Preparation andProofing for Subgrade (PadelPlayground)	2500	100%	0%	25 Jul-26	22Aug-26	09 Nov 26	07Dec-26	$7 507 5.00	$000	$75075.00	0.00
MLTX-02-004CN-121	Backfilling andCompacton ofBaseLayers(PadelPlayground)	2000	100%	0%	23 Aug-26	14Sep-26	08 Dec 26	30Dec-26	$4 290 0.00	$000	$42900.00	0.00
MLTX-02-004CN-121	Finishingand SufaceFinish Works (Padel Playground)	3000	667%	0%	18 Oct 26	21Nov-26	01 Feb 27	08Mar-27	$3 575 0.00	$000	$53625.00	0.00
MLTX-02-004CN-121	InstallSportEquipments -Goal /Nets- Padel Playground)	1300	0%	0%	29 Nov-26	13Dec-26	09 Mar 27	27Mar-27	$000	$000	$32175.00	0.00
MLTX-02-004CN-121	Surface Makingand Painting(PadelPlayground)	8.00	0%	0%	14 Dec-26	22Dec-26	28 Mar 27	05Apr-27	$000	$000	$10725.00	0.00
	BASKETBALLPLAYGROUND	9800	1967%	0%	23 Aug-26	22Dec-26	08 Dec 26	05Apr-27	$6 136 0.00	$000	$3 120 0.00	6.00
MLTX-02-004CN-121	Preparation andProofing for Subgrade PadelPlayground)	2000	100%	0%	23 Aug-26	14Sep-26	08 Dec 26	30Dec-26	$3 120 0.00	$000	$31200.00	0.00
MLTX-02-004CN-121	Backfilling andCompacton ofBaseLayers(BasketballPlayground)	3000	9667%	0%	15 Sep-26	20Oct-26	31 Dec 26	09Feb-27	$3 016 0.00	$000	$31200.00	0.00
MLTX-02-004CN-122	Finishingand SufaceFinish Works (Basketball Playground)	3000	0%	0%	21 Oct 26	24Nov-26	04 Feb 27	15Mar-27	$000	$000	$1 550 0.00	0.00
MLTX-02-004CN-122	InstallSportEquipments -Goal /Nets- Basketball Playground)	1000	0%	0%	08 Dec-26	19Dec-26	16 Mar 27	27Mar-27	$000	$000	$78000.00	0.00
MLTX-02-004CN-122	Surface Makingand Painting(BasketballPlayground)	8.00	0%	0%	14 Dec-26	22Dec-26	28 Mar 27	05Apr-27	$000	$000	$15600.00	0.00
	PADELFENCE	2100	0%	0%	23 Dec-26	16Jan-27	06 Apr 27	29Apr-27	$000	$000	$82875.00	0.00
MLTX-02-004CN-122	ExcavationforFence	3.00	0%	0%	23 Dec-26	26Dec-26	06 Apr 27	08Apr-27	$000	$000	$8 287 5.00	0.00
MLTX-02-004CN-122	Concrete Foundation for Fence includingPostsFixaton	4.00	0%	0%	27 Dec-26	30Dec-26	10 Apr 27	13Apr-27	$000	$000	$16575.00	0.00
MLTX-02-004CN-122	Tempered Glass Fenc Installaton and Fixation	5.00	0%	0%	05 Jan 27	10Jan-27	19 Apr 27	24Apr-27	$000	$000	$33150.00	0.00
MLTX-02-004CN-122	Chain LinkFenceInstallation andFixation	5.00	0%	0%	05 Jan 27	10Jan-27	19 Apr 27	24Apr-27	$000	$000	$16575.00	0.00
MLTX-02-004CN-122	Installof Fence Gates	5.00	0%	0%	11 Jan 27	16Jan-27	25 Apr 27	29Apr-27	$000	$000	$4 143 7.50	0.00
MLTX-02-004CN-122	Backfilling andReinstatementforConcrete Foundation	4.00	0%	0%	31 Dec-26	04Jan-27	14 Apr 27	18Apr-27	$000	$000	$4 143 7.50	0.00
	CURBSTONE/ INTERLOCK	8300	8065%	0%	27 Sep-26	24Oct-26	20 Oct 26	24Jan-27	$2 065 24.17	$000	$2 561 97.50	-5900
MLTX-02-004CN-115	Interlock Installaton (Grey Scale)forLandScape(IncludingFinishingWorks)	1500	7333%	0%	07 Oct 26	24Oct-26	07 Jan 27	24Jan-27	$1 362 26.67	$000	$1 689 0.00	0.00
MLTX-02-004CN-12(	Concrete WorksUnder Curbstone	5.00	100%	0%	27 Sep-26	01Oct-26	20 Oct 26	25Oct-26	$1 599 0.00	$000	$15990.00	0.00

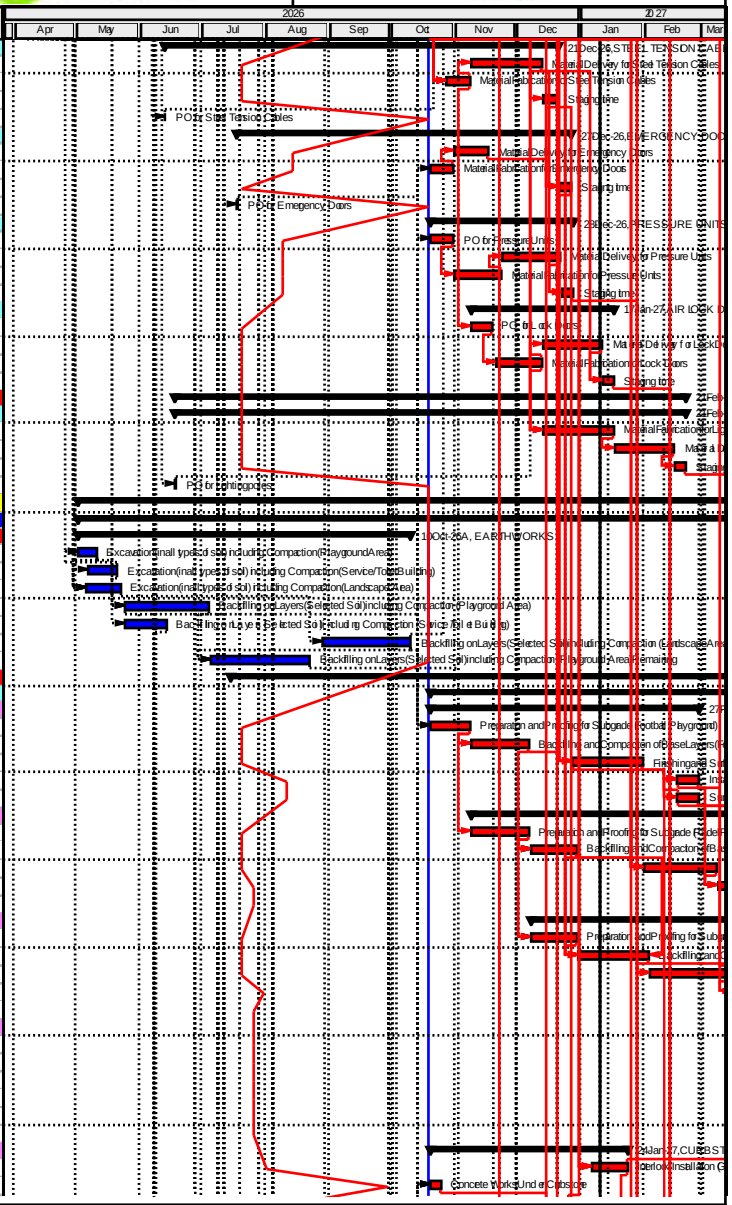


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004CN-120	CurbstoneInstalation	4.0d	100%	0%	03 Oct 26	06Oct-26	22 Dec 26	26Dec-26	$5,490.75	$0.00	$54307.50	0.0d
AIRDOME		17400	22%	207%	15 Sep-26	26Dec-26	15 Jul -26A	21Mar-27	$1233.375	$1160.49375	$5 606 250	- 122.0d
CIVIL WORKS		13900	5238%	4929%	15 Sep-26	15Nov-26	15 Jul -26A	03Feb-27	$1233.375	$1160.49375	$2 354 625	- 122.0d
MLTX-02-004CN-122	Installof Membane CoveringSystem (AirDome)	4.0d	0%	0%	08 Nov-26	11Nov-26	27 Jan 27	31Jan-27	$0.00	$0.00	$5 606 25.0	0.0d
MLTX-02-004CN-122	Themal Insulaton Works (Air Dome)	3.0d	0%	0%	12 Nov-26	15Nov-26	01 Feb 27	03Feb-27	$0.00	$0.00	$5 606 25.0	0.0d
MLTX-02-004CN-122	Cable System Installaton (Air Dome)	3.0d	100%	87%	27 Sep-26	29Sep-26	24 Sep 26 A	21Dec-26	$5 606 25.0	$487743.75	$5 606 25.0	-7300
MLTX-02-004CN-122	ExcavationforFoundaton & Playgound Aea (Air Dome)	5.0d	100%	100%	15 Sep-26	20Sep-26	15 Jul -26A	15Aug-26A	$2 803 125	$2803125	$2 803 12.5	-2100
MLTX-02-004CN-122	Concete Worksfor Foundations including Anchor Bolts (Air Dome)	4.0d	100%	100%	21 Sep-26	26Sep-26	29 Jul -26A	22Sep-26A	$3 923 437	$3924375	$3 924 37.5	-4400
MECHANICALWORKS		1300	0%	0%	16 Nov-26	30Nov-26	01 Feb 27	18Feb-27	$0.00	$0.00	$1 121 250	0.0d
MLTX-02-004CN-122	AirDuctsand GrillsInstallation (Air Dome)	1000	0%	0%	16 Nov-26	26Nov-26	01 Feb 27	15Feb-27	$0.00	$0.00	$2 803 12.5	0.0d
MLTX-02-004CN-122	AirUnitsInstallaton (Air Dome)	1300	0%	0%	16 Nov-26	30Nov-26	01 Feb 27	18Feb-27	$0.00	$0.00	$4 485 00.0	0.0d
MLTX-02-004CN-122	Exhaust Fans andDucts Instalation (Air Dome)	1100	0%	0%	16 Nov-26	28Nov-26	01 Feb 27	16Feb-27	$0.00	$0.00	$3 923 437	0.0d
ELECTRICAL WORKS		2200	0%	0%	01 Dec-26	26Dec-26	20 Feb 27	21Mar-27	$0.00	$0.00	$1 681 875	0.0d
MLTX-02-004CN-122	Light FixtureWorks(AirDome)	2000	0%	0%	01 Dec-26	23Dec-26	20 Feb 27	18Mar-27	$0.00	$0.00	$2 803 12.5	0.0d
MLTX-02-004CN-122	Distibuton Board and ElecticalWorks (Air Dome)	1800	0%	0%	01 Dec-26	21Dec-26	20 Feb 27	16Mar-27	$0.00	$0.00	$2 803 12.5	0.0d
MLTX-02-004CN-124	External ElecticalConnection Works (Air Dome)	2000	0%	0%	01 Dec-26	23Dec-26	20 Feb 27	18Mar-27	$0.00	$0.00	$2 803 12.5	0.0d
MLTX-02-004CN-124	Emergency GeneratorInstallaton (AirDome)	2000	0%	0%	01 Dec-26	23Dec-26	20 Feb 27	18Mar-27	$0.00	$0.00	$5 606 25.0	0.0d
MLTX-02-004CN-124	Contol System Installtion(AirDome)	2200	0%	0%	01 Dec-26	26Dec-26	20 Feb 27	21Mar-27	$0.00	$0.00	$2 803 12.5	0.0d
FINISHES WORKS		2500	0%	0%	19 Nov-26	17Dec-26	08 Feb 27	09Mar-27	$0.00	$0.00	$4 485 00.0	0.0d
MLTX-02-004CN-122	Doos Installaton Including Emegency,Entrance doos (Air Dome)	1000	0%	0%	19 Nov-26	30Nov-26	08 Feb 27	18Feb-27	$0.00	$0.00	$2 242 50.0	0.0d
MLTX-02-004CN-122	Logoand Signs Installaton(AirDome)	1500	0%	0%	01 Dec-26	17Dec-26	20 Feb 27	09Mar-27	$0.00	$0.00	$2 242 50.0	0.0d
IRRIGATION NETWORK		4400	6974%	3018%	07 Oct 26	01Nov-26	10 Oct 26A	20Jan-27	$1 866 637	$807.50	$2 676 70.0	-6700
MLTX-02-004CN-13200	Installing ofHDPE Pipes forIrrigation Network (BranchLines)	5.0d	100%	0%	13 Oct 26	18Oct-26	01 Dec 26	06Dec-26	$9 425.00	$0.00	$94250.00	0.0d
MLTX-02-004CN-13210	Installing ofValvesand fittings for IrigationNetwork	4.0d	25%	0%	19 Oct 26	22Oct-26	07 Dec 26	10Dec-26	$1 651.875	$0.00	$46475.00	0.0d
MLTX-02-004CN-13220	Installing ofBubblers andSprayers	3.0d	0%	0%	29 Oct 26	01Nov-26	18 Jan 27	20Jan-27	$0.00	$0.00	$46150.00	0.0d
MLTX-02-004CN-13190	Installing ofHDPE Pipes forIrrigation Network (Main Line)	5.0d	100%	100%	07 Oct 26	12Oct-26	10 Oct 26A	15Oct-26A	$8 079.50	$807.50	$80795.00	-100
NATURALGROUND		5.0d	0%	0%	24 Oct 26	28Oct-26	12 Jan 27	17Jan-27	$0.00	$0.00	$80291.25	0.0d
MLTX-02-004CN-11990	Compacted NaturalGroundSoilInstallation Woks for Landscape	5.0d	0%	0%	24 Oct 26	28Oct-26	12 Jan 27	17Jan-27	$0.00	$0.00	$80291.25	0.0d
PLANTING		2800	0%	0%	02 Nov-26	03Dec-26	21 Jan 27	23Feb-27	$0.00	$0.00	$5 734 62.5	0.0d
MLTX-02-004CN-12050	Placement of SweetAgricultual Soil (Including Levelling andGrading)	5.0d	0%	0%	02 Nov-26	07Nov-26	21 Jan 27	26Jan-27	$0.00	$0.00	$1 854 20.0	0.0d
MLTX-02-004CN-12060	Placement of LawnGroundCover(Rolling and Compacton)	3.0d	0%	0%	01 Dec-26	03Dec-26	20 Feb 27	23Feb-27	$0.00	$0.00	$1 751.75	0.0d
MLTX-02-004CN-12070	Placement and Fixationof Trees	3.0d	0%	0%	28 Nov-26	30Nov-26	16 Feb 27	18Feb-27	$0.00	$0.00	$2 118 67.5	0.0d
WALKING/BIKE PATHS		8.0d	0%	92%	05 Dec-26	13Dec-26	19 Aug 26 A	23Feb-27	$0.00	$254299.47	$2 764 12.47	- 152.0d
MLTX-02-004CN-12000	BikePathPreparationand InstallationWorks	8.0d	0%	92%	05 Dec-26	13Dec-26	19 Aug 26 A	23Feb-27	$0.00	$130681.66	$1 420 45.28	- 152.0d
MLTX-02-004CN-12010	WalkingPath Preparaton and InstallaionWorks	8.0d	0%	92%	05 Dec-26	13Dec-26	19 Aug 26 A	23Feb-27	$0.00	$123617.81	$1 343 67.19	- 152.0d
GENERAL/FURNITURE		11100	1194%	6.38%	07 Oct 26	25Jan-27	17 Oct 26A	09May-27	$8 894 00.9	$1 475 1.51	$7 451 51.31	-7700
MLTX-02-004CN-11970	Stamped Concete Worksfor landScape(IncludingFinishingWorks)	8.0d	0%	0%	14 Dec-26	22Dec-26	26 Feb 27	04Mar-27	$0.00	$0.00	$14040.00	0.0d
MLTX-02-004CN-12040	TrafficSignsPosts and Poles Installaion	7.0d	0%	0%	06 Jan 27	13Jan-27	23 Mar 27	30Mar-27	$0.00	$0.00	$9 750.00	0.0d
MLTX-02-004CN-12440	Fixationand Installationof Steel Frame for Benches	1200	0%	0%	14 Dec-26	27Dec-26	26 Feb 27	09Mar-27	$0.00	$0.00	$17276.03	0.0d
MLTX-02-004CN-12450	Fixationand Installationof Benches	8.0d	0%	0%	28 Dec-26	05Jan-27	16 Mar 27	22Mar-27	$0.00	$0.00	$40310.73	0.0d
MLTX-02-004CN-12460	Fixationand Installationof PecastConcrete Seats (Rectangular)	8.0d	0%	0%	28 Dec-26	05Jan-27	16 Mar 27	22Mar-27	$0.00	$0.00	$43680.00	0.0d
MLTX-02-004CN-12470	Fixationand Installationof PecastConcrete Seats (Circular)	8.0d	0%	0%	28 Dec-26	05Jan-27	16 Mar 27	22Mar-27	$0.00	$0.00	$17160.00	0.0d
MLTX-02-004CN-12480	Fixationand Installationof PecastConcrete Trash Bins	8.0d	0%	0%	17 Jan 27	25Jan-27	01 May 27	09May-27	$0.00	$0.00	$14625.00	0.0d
MLTX-02-004CN-12920	Preliminary Woks forSiteLightPoles IncludingCableand Bases Woks	1400	7857%	0%	07 Oct 26	22Oct-26	27 Dec 26	11Jan-27	$8 894 00.9	$0.00	$1 131 97.5	0.0d
MLTX-02-004CN-12930	Installing ofSiteLightPoles	1100	0%	10%	24 Dec-26	05Jan-27	17 Oct 26A	18Mar-27	$0.00	$1 475 1.51	$4 751 15.0	- 117.0d
PARKING		1200	0%	0%	23 Dec-26	05Jan-27	06 Mar 27	22Mar-27	$0.00	$0.00	$97500.48	0.0d
MLTX-02-004CN-11940	Interlock Installaton (8 Cm)for ParkingArea(IncludingFinishing Works)	7.0d	0%	0%	29 Dec-26	05Jan-27	15 Mar 27	22Mar-27	$0.00	$0.00	$68249.02	0.0d
MLTX-02-004CN-11950	Site Preparation & CompactionUnderInterlockfor ParkingArea	5.0d	0%	0%	23 Dec-26	28Dec-26	05 Mar 27	14Mar-27	$0.00	$0.00	$29251.46	0.0d
TOILETSERVICE BUILDING		17480	9776%	4558%	14 Jun 26	16Nov-26	14 Jun 26A	04Jan-27	$1251.539	$583537.16	$1 280 181	-4200
STRUCTUREWORKS		5680	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	09Aug-26A	$1 579 50.0	$157950.00	$1 579 50.0	9.0d
CONCRETE WORKS		5080	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	23Jul-26A	$1 137 82.5	$113782.50	$1 137 82.5	23.0d
SUB-STRUCTURE		1640	100%	100%	14 Jun 26	02Jul-26	14 Jun 26A	02Jul-26A	$33 345.00	$33345.00	$33345.00	0.0d
MLTX-02-004CN-124	Plain Concete Unter Footing	1.0d	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$1 170.00	$1170.00	$1 170.00	0.0d
MLTX-02-004CN-125	ReinforcedConcrete Woks for SlabonGrade Including Steel Fixing	1560	100%	100%	15 Jun 26	02Jul-26	15 Jun 26A	02Jul-26A	$32 175.00	$32175.00	$32175.00	0.0d
SUPER-STRUCTURE		1900	100%	100%	16 Jul -26	19Aug-26	19 Jul -26A	23Jul-26A	$80 043.75	$80043.75	$80437.50	24.0d
MLTX-02-004CN-125	AAC Panels Works for Walls	1100	100%	100%	16 Jul -26	28Jul-26	19 Jul -26A	21Jul-26A	$48 262.50	$48262.50	$48262.50	7.8d
MLTX-02-004CN-125	Parpet Works and Lintels	800	100%	100%	11 Aug-26	19Aug-26	23 Jul -26A	23Jul-26A	$16 087.50	$16087.50	$16087.50	7.0d
MLTX-02-004CN-125	AAC Panels Works for Slabs	1000	100%	100%	29 Jul -26	09Aug-26	21 Jul -26A	22Jul-26A	$16 087.50	$16087.50	$16087.50	8.0d
UNDER GROUNDSEPTIC TANK		3870	100%	100%	15 Jun 26	10Aug-26	15 Jun 26A	15Jul-26A	$33 930.00	$33930.00	$33930.00	22.4d
MLTX-02-004CN-13080	Plain Concete Unter Footing	1.0d	100%	100%	15 Jun 26	16Jun-26	15 Jun 26A	16Jun-26A	$1 170.00	$1170.00	$1 170.00	0.0d
MLTX-02-004CN-13090	ReinforcedConcrete Woks for Tank SlabIncludingShutteing and Steel Fixing	1600	100%	100%	23 Jul -26	10Aug-26	11 Jul -26A	15Jul-26A	$8 775.00	$8775.00	$8 775.00	11.4d
MLTX-02-004CN-13100	ReinforcedConcrete Woks for Tank FoundationIncludingShutteing and Steel Fixing	1330	100%	100%	16 Jun 26	01Jul-26	16 Jun 26A	01Jul-26A	$7 605.00	$7605.00	$7 605.00	0.0d
MLTX-02-004CN-13110	ReinforcedConcrete Woks for Tank Walls Including Steel Fixing	1600	100%	100%	05 Jul -26	22Jul-26	05 Jul -26A	07Jul-26A	$16 380.00	$1638.00	$16380.00	13.0d
THERMAL& MOISTERPROTECTION		5680	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	09Aug-26A	$1 023 75	$1023.750	$10237.50	9.0d
ANTITERMITCONTROL		1480	100%	100%	14 Jun 26	30Jun-26	14 Jun 26A	30Jun-26A	$4 387.50	$4387.50	$4 387.50	0.0d
MLTX-02-004CN-125	AntiTermite Works Under Fundation	1.1d	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$1 755.00	$1755.00	$1 755.00	0.0d

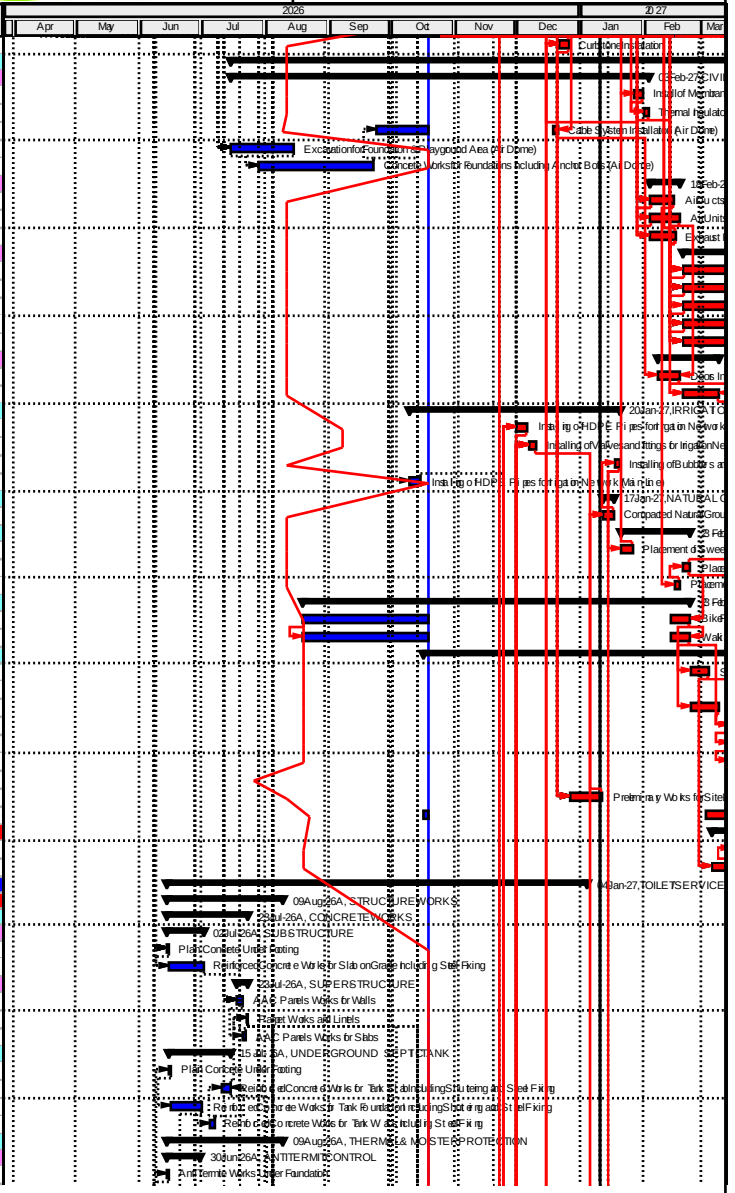

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: All Activities

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 19-10-2026

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004CN-125	Anti Termite Works Under Slab on Gradeand Grade Beams	4.00	100%	100%	27 Jun 26	30Jun-26	27 Jun 26A	30Jun-26A	$2,632.50	$2632.50	$2,632.50	0.00
POLYETHYLENESHEET		1480	100%	100%	14 Jun 26	30Jun-26	14 Jun 26A	30Jun-26A	$2,193.75	$2193.75	$2,193.75	0.00
MLTX-02-004CN-125	Water Proofing Under Blinding Concrete(Polythelen Sheet)	1.10	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$87.75	$87.750	$87.75	0.00
MLTX-02-004CN-125	Water Proofing Under Slab on Grade (Polythelen Sheet)	2.00	100%	100%	29 Jun 26	30Jun-26	29 Jun 26A	30Jun-26A	$1,316.25	$1316.25	$1,316.25	0.00
EPOXY		8.00	100%	100%	11 Aug-26	19Aug-26	08 Aug 26A	09Aug-26A	$3,656.25	$3656.25	$3,656.25	6.00
MLTX-02-004CN-125	Surface Preparaton for Epoxy Coating	3.00	100%	100%	11 Aug-26	13Aug-26	08 Aug 26A	08Aug-26A	$1,096.88	$1096.88	$1,096.88	2.00
MLTX-02-004CN-125	Epoxy Coating for Walls and Slabof Tank	5.00	100%	100%	15 Aug-26	19Aug-26	09 Aug 26A	09Aug-26A	$2,559.38	$2559.38	$2,559.38	4.00
MASONARY WORK		5.00	100%	100%	11 Jul-26	15Jul-26	26 Jul-26A	05Aug-26A	$1,228.50	$1,228.50	$12285.00	-450
MLTX-02-004CN-12 600	CMU Masonary Works Including all Accessories	5.00	100%	100%	11 Jul-26	15Jul-26	26 Jul-26A	05Aug-26A	$1,228.50	$1,228.50	$12285.00	-450
THERMAL& MOISTER PROTECTION		1500	100%	9282%	20 Aug-26	13Sep-26	29 Sep 26A	28Oct-26	$3,470.02	$32,209.05	$34700.25	-500
MLTX-02-004CN-12 650	Finalize Water Proofing Works for Roofing and Wet Areas	8.00	100%	85%	05 Sep-26	13Sep-26	29 Sep 26A	28Oct-26	$1,650.81	$1,411.69	$16608.15	-1800
MLTX-02-004CN-12 620	Preparing Surface and Preliminary Works for Toiles Waterpoofing	2.00	100%	100%	20 Aug-26	22Aug-26	10 Oct 26A	15Oct-26A	$2,106.00	$2106.00	$2,106.00	-400
MLTX-02-004CN-12 630	Finalize Water Proofing Works for Toilets	5.00	100%	100%	23 Aug-26	27Aug-26	10 Oct 26A	15Oct-26A	$4,914.00	$4914.00	$4,914.00	-100
MLTX-02-004CN-12 640	Preparing Surface and Preliminary Works for Roofing and Wet Areas Insulaton	6.00	100%	100%	29 Aug-26	03Sep-26	29 Sep 26A	29Sep-26A	$1,107.21	$1,107.21	$11072.10	5.00
MECHANICALWORK		8300	100%	3078%	29 Aug-26	18Oct-26	01 Jul -26A	06Dec-26	$4,332,851.25	$133350.75	$4,332,851.25	-9000
HVAC SYSTEM		1800	100%	4755%	12 Sep-26	18Oct-26	05 Oct 26A	06Dec-26	$2,788.50	$1,325.00	$27885.00	-2200
MLTX-02-004CN-12730	Installand Finish HVAC and Ventiltion Works Including Split Air Units	9.00	100%	0%	08 Oct 26	18Oct-26	26 Nov 26	06Dec-26	$1,462.50	$000	$14625.00	0.00
MLTX-02-004CN-12720	Preliminary HVAC and Ventilation Works	4.00	100%	100%	12 Sep-26	15Sep-26	05 Oct 26A	08Oct-26A	$9,360.00	$9360.00	$9,360.00	1.00
MLTX-02-004CN-12740	Exhaust, Air Ducts Installaionwithall Accessories	8.00	100%	100%	16 Sep-26	26Sep-26	10 Oct 26A	12Oct-26A	$3,900.00	$3900.00	$3,900.00	5.00
WATERSUPPLY SYSTEM		7400	100%	4291%	31 Aug-26	10Oct-26	04 Aug 26A	28Nov-26	$2,524,275.00	$108322.50	$2,524,275.00	-6500
MLTX-02-004CN-12770	Installing of Booster Pump Units Including fittings and accessories	5.00	100%	0%	27 Sep-26	01Oct-26	01 Nov 26	05Nov-26	$9,100.00	$000	$91000.00	0.00
MLTX-02-004CN-13170	Installing of Valves and Ritings	6.00	100%	0%	03 Sep-26	09Sep-26	20 Oct 26	26Oct-26	$9,750.00	$000	$9,750.00	0.00
MLTX-02-004CN-13260	Installing of Water Heater	7.00	100%	0%	03 Oct 26	10Oct-26	21 Nov 26	28Nov-26	$1,755.00	$000	$1,755.00	0.00
MLTX-02-004CN-12780	Installing of GRP Tanks	8.00	100%	60%	16 Sep-26	26Sep-26	15 Sep 26A	31Oct-26	$1,040.00.00	$6,240.00.00	$1,040.00.00	-3100
MLTX-02-004CN-12750	Installing of PPR Pipes and Fittings for Water Network	3.00	100%	100%	31 Aug-26	02Sep-26	04 Aug 26A	08Aug-26A	$6,922.50	$6922.50	$6,922.50	-055
MLTX-02-004CN-12760	Installing of HDPE Pipes and Valves for Water Supply Network	3.00	100%	100%	10 Sep-26	13Sep-26	05 Oct 26A	10Oct-26A	$3,900.00.00	$3,900.00.00	$39000.00	-200
SEWERDRAIN AGE SYSTEM		7800	100%	7.79%	29 Aug-26	12Oct-26	04 Jul -26A	30Nov-26	$1,510,228.68	$1,178,325.00	$1,510,228.68	-9000
MLTX-02-004CN-12800	Installing of Plumping Fixtures and Accessories	2.00	100%	0%	17 Sep-26	19Sep-26	07 Nov 26	08Nov-26	$1,035,938.00	$000	$10359.38	0.00
MLTX-02-004CN-13180	Installing UPVC Pipes for External Connecton for Sewage Network	7.00	100%	0%	09 Sep-26	16Sep-26	29 Oct 26	05Nov-26	$8,512.50	$000	$85312.50	0.00
MLTX-02-004CN-13250	Installing Inspection Chamber for Sewage Network	8.00	100%	0%	31 Aug-26	08Sep-26	20 Oct 26	28Oct-26	$1,218.75	$000	$12187.50	0.00
MLTX-02-004CN-13270	Installing of Toilet Fixtures and Accesses Such as Closets and Basins	9.00	100%	0%	03 Oct 26	12Oct-26	21 Nov 26	30Nov-26	$3,139.50	$000	$31395.00	0.00
MLTX-02-004CN-12790	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	29 Aug-26	30Aug-26	04 Jul -26A	08Aug-26A	$1,176,828.75	$1,176,828.75	$11768.25	-2820
FIREPROTECTION		7.00	100%	0%	11 Oct 26	18Oct-26	29 Nov 26	06Dec-26	$1,950.00	$000	$1,950.00	0.00
MLTX-02-004CN-12810	Installing of Fire Fighting Extinguisher and accessories (PIE-1, PIE-2)	7.00	100%	0%	11 Oct 26	18Oct-26	29 Nov 26	06Dec-26	$1,950.00	$000	$1,950.00	0.00
ELECTRICAL WORKS		11700	9271%	4943%	20 Aug-26	24Oct-26	11 Aug 26A	12Dec-26	$4,491,702.25	$186128.67	$3,765,252.75	-5000
ROUGH-N WORKS		2500	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$1,488,825.00	$1488825.00	$1,488,825.00	-500
MLTX-02-004CN-12830	Preliminary Works for Panel Boards	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$7,605.00	$7605.00	$76050.00	-500
MLTX-02-004CN-12850	Preliminary Works for Cable Works	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$1,070.00.04	$1,070.00.04	$10700.04	-500
MLTX-02-004CN-12860	Preliminary Works for Sockets and Power Points	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$9,230.91	$9230.91	$9,230.91	-500
MLTX-02-004CN-12880	Preliminary Works for Lightning Works	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$9,750.00	$9750.00	$9,750.00	-500
MLTX-02-004CN-12900	Preliminary Works for Data & Telecommunication System	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$1,228.50	$1,228.50	$12285.00	-500
MLTX-02-004CN-12940	Preliminary Works for Security and Access Contol System	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$1,526.65.55	$1,526.65.55	$15266.55	-500
MLTX-02-004CN-13230	Preliminary Works for Earthing Works	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 26A	26Aug-26A	$1,560.00.00	$1,560.00.00	$15600.00	-500
FIXTURE WORKS		2700	8794%	1636%	08 Oct 26	24Oct-26	06 Oct 26A	12Dec-26	$2,001,877.50	$32,721.63	$2,276,487.50	-4400
MLTX-02-004CN-12820	Installing of Fireautomationand Fie Alarm System	5.00	20%	0%	19 Oct 26	24Oct-26	07 Dec 26	12Dec-26	$5,868.00	$000	$34320.00	0.00
MLTX-02-004CN-12840	Installing and Finish Works of Panel Boards	1000	100%	0%	08 Oct 26	19Oct-26	26 Nov 26	07Dec-26	$8,407.50	$000	$84075.00	0.00
MLTX-02-004CN-12890	Installing and Finalize Works of Lighting Works including Light Fixtures	7.00	100%	0%	11 Oct 26	18Oct-26	29 Nov 26	06Dec-26	$1,605.00.06	$000	$16050.00	0.00
MLTX-02-004CN-12910	Installing Data and Telecommunication System with all Accessories	7.00	100%	0%	11 Oct 26	18Oct-26	29 Nov 26	06Dec-26	$1,842.75.00	$000	$18427.50	0.00
MLTX-02-004CN-12950	Installing and Finalize Works of Security and Access Control System	9.00	100%	0%	08 Oct 26	18Oct-26	26 Nov 26	06Dec-26	$22,899.83	$000	$22899.83	0.00
MLTX-02-004CN-12970	Installing and Finalize Works of Lightning Protection System	9.00	100%	0%	08 Oct 26	18Oct-26	26 Nov 26	06Dec-26	$1,462.50	$000	$14625.00	0.00
MLTX-02-004CN-12870	Installing and Finalize Works of Sockets and Power Points	7.00	100%	100%	11 Oct 26	18Oct-26	08 Oct 26A	10Oct-26A	$1,384.63.7	$1,384.63.7	$13846.37	5.00
MLTX-02-004CN-12960	Installing and Finalize Works of Eathing Works	9.00	100%	100%	08 Oct 26	18Oct-26	06 Oct 26A	10Oct-26A	$2,340.00.00	$2,340.00.00	$23400.00	5.00
DOORS/WINDOWS		3700	100%	0%	20 Aug-26	13Oct-26	20 Oct 26	01Dec-26	$6,825.00.00	$000	$68250.00	9.00
MLTX-02-004CN-12 660	Preliminary Works For Doors	1000	100%	0%	20 Aug-26	31Aug-26	20 Oct 26	31Oct-26	$3,900.00	$000	$3,900.00	0.00
MLTX-02-004CN-12 670	Finalize Metal Doors for Toilets Building	5.00	100%	0%	08 Oct 26	13Oct-26	26 Nov 26	01Dec-26	$5,850.00	$000	$5,850.00	0.00
MLTX-02-004CN-13 040	Finalize Glazzed Curtain Wall Works	5.00	100%	0%	08 Oct 26	13Oct-26	26 Nov 26	01Dec-26	$3,510.00.00	$000	$35100.00	0.00
MLTX-02-004CN-13 120	Preliminary Works For Windows/CutainWall	1200	100%	0%	20 Aug-26	02Sep-26	20 Oct 26	02Nov-26	$2,340.00.00	$000	$23400.00	0.00
METALWORKS		2500	100%	0%	20 Aug-26	04Oct-26	20 Oct 26	17Nov-26	$1,365.00.00	$000	$13650.00	13.00
MLTX-02-004CN-12 610	Installaionof Galvanized Steel Ladder	5.00	100%	0%	16 Sep-26	21Sep-26	01 Nov 26	05Nov-26	$5,850.00	$000	$5,850.00	0.00
MLTX-02-004CN-12 980	Installaionof DI Coverfor Tank	4.00	100%	0%	20 Aug-26	24Aug-26	20 Oct 26	24Oct-26	$3,900.00	$000	$3,900.00	0.00
MLTX-02-004CN-12 990	Installaionof Galvanized Steel Roof Scupper	1000	100%	0%	22 Sep-26	04Oct-26	07 Nov 26	17Nov-26	$3,900.00	$000	$3,900.00	0.00
FINISHING WORKS		9600	9919%	4263%	29 Aug-26	16Nov-26	05 Sep 26A	04Jan-27	$1,431,443.50	$5,161.35	$1,431,443.50	-3600
FLOORFINISHES		6600	9318%	6932%	03 Sep-26	16Nov-26	08 Oct 26A	04Jan-27	$1,599.00.00	$1,185.00	$17160.00	-1300
MLTX-02-004CN-13050	Granite Tiles Floor Finish Works	6.00	100%	0%	06 Sep-26	12Sep-26	20 Oct 26	26Oct-26	$2,925.00	$000	$2,925.00	0.00
MLTX-02-004CN-13060	Epoxy Coaton Concete floor	2000	0%	0%	25 Oct 26	16Nov-26	13 Dec 26	04Jan-27	$000	$000	$1,170.00	0.00
MLTX-02-004CN-13070	Ceramic Skirting Tiles Finish Works	4.00	100%	0%	13 Sep-26	16Sep-26	27 Oct 26	31Oct-26	$1,170.00	$000	$1,170.00	0.00

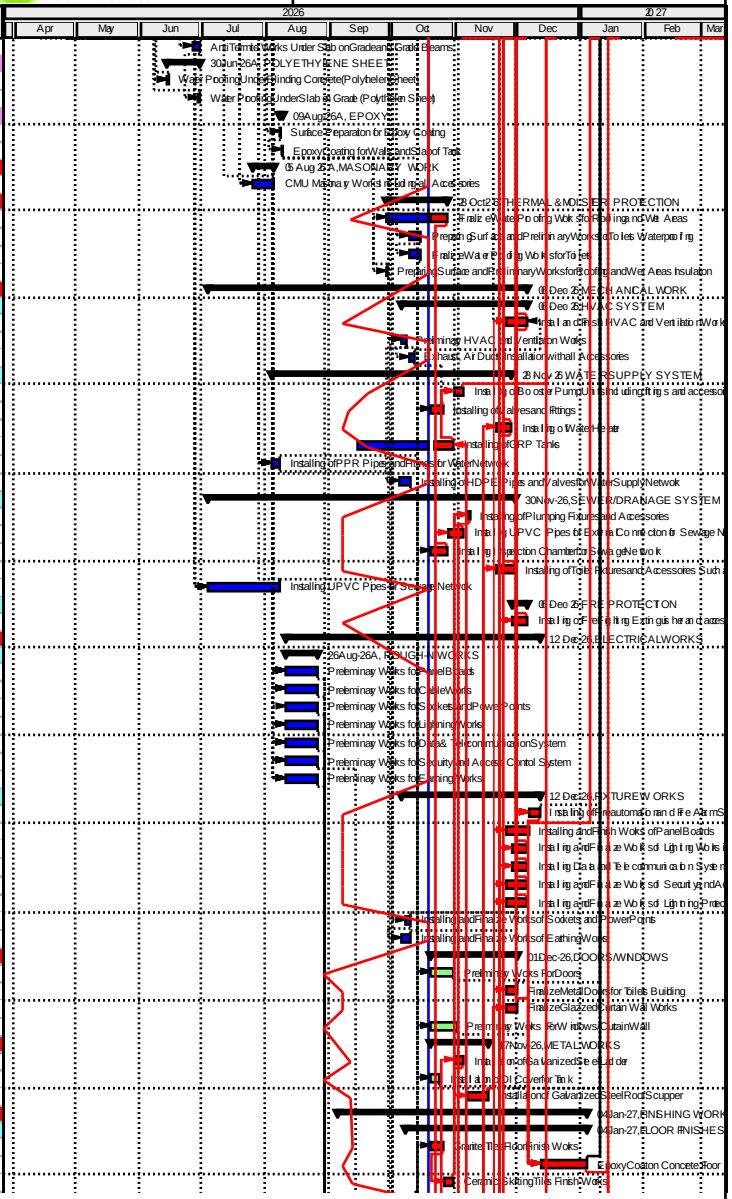


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Original Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance BL Project
MLTX-02-004CN-12680	Ceramic Tiles Floor FinishWorks	2.00	100%	100%	03-Sep-26	05-Sep-26	08-Oct-26A	12-Oct-26A	$1,189.50	$1,189.50	$11,895.00	-200
WALL FINISHES		64.00	100%	4355%	29-Aug-26	10-Oct-26	05-Sep-26A	28-Nov-26	$1,141,725.50	$84,971.85	$1,141,725.50	-3600
MLTX-02-004CN-13010	PaintingFinishWorks forExtenal Walls	3.00	100%	0%	14-Sep-26	16-Sep-26	20-Oct-26	22-Oct-26	$10,478.00	$000	$10,478.00	0.00
MLTX-02-004CN-13030	Phenolic Patitions for Toilets	7.00	100%	0%	24-Sep-26	01-Oct-26	12-Nov-26	19-Nov-26	$31,200.00	$000	$31,200.00	0.00
MLTX-02-004CN-13140	Glass Partitions includingallaccessoriesand doors	5.00	100%	0%	03-Oct-26	07-Oct-26	21-Nov-26	25-Nov-26	$12,285.00	$000	$12,285.00	0.00
MLTX-02-004CN-13150	Granite Cappingfor Papet	2.00	100%	0%	14-Sep-26	15-Sep-26	29-Oct-26	31-Oct-26	$8,151.00	$000	$8,151.00	0.00
MLTX-02-004CN-13240	PaintingFinishWorks forIntenalWalls	2.00	100%	0%	08-Oct-26	10-Oct-26	26-Nov-26	28-Nov-26	$2,340.00	$000	$2,340.00	0.00
MLTX-02-004CN-12690	Prelminary Woks for Wall Finish Worksincluding Plasteing (Intenal)	3.00	100%	100%	31-Aug-26	02-Sep-26	05-Sep-26A	12-Sep-26A	$1,836.90	$1,836.90	$18,369.00	-400
MLTX-02-004CN-13000	Prelminary Woks for Wall Finish Works(External)	1400	100%	100%	29-Aug-26	13-Sep-26	20-Sep-26A	30-Sep-26A	$6,552.00	$6552.00	$6,552.00	5.00
MLTX-02-004CN-13020	Ceramic Finish Worksfor Walls	5.00	100%	100%	06-Sep-26	10-Sep-26	04-Oct-26A	06-Oct-26A	$1,559.75	$1,567.50	$15,697.50	2.00
MLTX-02-004CN-13130	Stone Cladding FinishWorksforExternal Walls	5.00	100%	100%	17-Sep-26	22-Sep-26	10-Oct-26A	15-Oct-26A	$9,100.00	$9100.00	$9,100.00	-100
CELLING FINISHES		24.00	100%	0%	03-Sep-26	01-Oct-26	20-Oct-26	16-Nov-26	$13,182.00	$000	$13,182.00	0.00
MLTX-02-004CN-13280	PaintingFinishWorks forCeiling	9.00	100%	0%	21-Sep-26	01-Oct-26	07-Nov-26	16-Nov-26	$1,638.00	$000	$1,638.00	0.00
MLTX-02-004CN-13290	Gypsum BoardSuspended Ceiling FinishWorksForCeiling	4.00	100%	0%	16-Sep-26	20-Sep-26	20-Oct-26	24-Oct-26	$6,926.40	$000	$6,926.40	0.00
MLTX-02-004CN-13300	Prelminary Woks for Ceiling Painting Woks	1500	100%	0%	03-Sep-26	20-Sep-26	20-Oct-26	05-Nov-26	$4,617.60	$000	$4,617.60	0.00
SPECIALTES WORK		12.00	100%	0%	20-Sep-26	04-Oct-26	09-Nov-26	22-Nov-26	$3,900.00	$000	$39000.00	0.00
MLTX-02-004CN-12700	SantaryFixtues andAccessoiesWorks	3.00	100%	0%	20-Sep-26	22-Sep-26	09-Nov-26	11-Nov-26	$1,462.50	$000	$14625.00	0.00
MLTX-02-004CN-13150	Installationof PhenolicLocker	2.00	100%	0%	03-Oct-26	04-Oct-26	21-Nov-26	22-Nov-26	$2,437.50	$000	$24375.00	0.00
TESTING & COMMISSIONING		63.00	0%	0%	17-Nov-26	19-Jan-27	21-Jan-27	08-Apr-27	$000	$000	$0.00	-800
MLTX-02-004TC-11890	Testing and Commissioning forMEP Woks for PlaygroundArea	16.00	0%	0%	27-Dec-26	13-Jan-27	22-Mar-27	08-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004TC-11900	Testing and Commissioning forMEP Woks for ToiletServiceBuilding	25.00	0%	0%	17-Nov-26	15-Dec-26	21-Jan-27	18-Feb-27	$000	$000	$0.00	0.00
MLTX-02-004TC-11910	Testing and Commissioning forMEP Woks for LantscapeWorks	5.00	0%	0%	14-Jan-27	19-Jan-27	31-Mar-27	05-Apr-27	$000	$000	$0.00	0.00
PROJECT CLOSEOUT & DEMOBILIZATION		28.00	0%	0%	14-Jan-27	25-Jan-27	22-Mar-27	22-Apr-27	$000	$000	$0.00	-1800
As-Built DWGs		26.00	0%	0%	14-Jan-27	23-Jan-27	22-Mar-27	20-Apr-27	$000	$000	$0.00	-1800
As-Built DWGs Submittals		22.00	0%	0%	14-Jan-27	18-Jan-27	22-Mar-27	15-Apr-27	$000	$000	$0.00	-1800
MLTX-02-004CO-12000	As-BuiltDWGs SubmittalforPlaygound Aea Woks	4.00	0%	0%	14-Jan-27	18-Jan-27	12-Apr-27	15-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12010	As-BuiltDWGs Submittal forToilet/SeviceBuilding Woks	4.00	0%	0%	14-Jan-27	18-Jan-27	22-Mar-27	25-Mar-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12020	As-BuiltDWGs SubmittalforLandscape Woks	4.00	0%	0%	14-Jan-27	18-Jan-27	31-Mar-27	04-Apr-27	$000	$000	$0.00	0.00
As-BuiltDWGs Approvals		22.00	0%	0%	19-Jan-27	23-Jan-27	27-Mar-27	20-Apr-27	$000	$000	$0.00	-1800
MLTX-02-004CO-12040	As-BuiltDWGs ApprovalforPlaygound Aea Woks	4.00	0%	0%	19-Jan-27	23-Jan-27	17-Apr-27	20-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12050	As-BuiltDWGs Appovalfor ToiletService BuildingWorks	4.00	0%	0%	19-Jan-27	23-Jan-27	27-Mar-27	30-Mar-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12060	As-BuiltDWGs Appovalfor landscape Woks	4.00	0%	0%	19-Jan-27	23-Jan-27	05-Apr-27	08-Apr-27	$000	$000	$0.00	0.00
Demoblizaton		6.00	0%	0%	19-Jan-27	25-Jan-27	17-Apr-27	22-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12080	Demoblizaton d Manpower	2.00	0%	0%	19-Jan-27	20-Jan-27	17-Apr-27	18-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12090	Removal ofEquipment from Site	2.00	0%	0%	19-Jan-27	20-Jan-27	17-Apr-27	18-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12100	Site CleanUp	2.00	0%	0%	21-Jan-27	23-Jan-27	19-Apr-27	20-Apr-27	$000	$000	$0.00	0.00
MLTX-02-004CO-12110	Resbration ofGroundSurfaces	2.00	0%	0%	24-Jan-27	25-Jan-27	21-Apr-27	22-Apr-27	$000	$000	$0.00	0.00

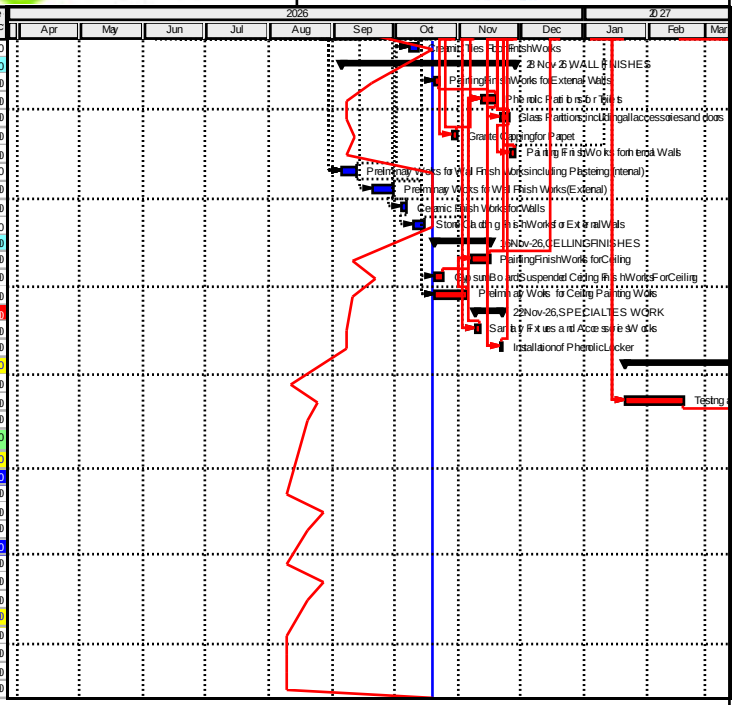

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation
