
WAS1 05 006

Improvement of Waad Al Shamal Industrial City Fence Gates

Baseline Time Schedule

CONSOLIDATED CONSULTANTS GROUP


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
Improvement of Waad Al Shamal Industrial City Fence & Gates -		128	06-May-26	05-Oct-26	64.4%	100%
Key Milestones		128	06-May-26	05-Oct-26	0%	0%
General Milestones		128	06-May-26	05-Oct-26	0%	0%
WAD.S.1080	Project Start	0	06-May-26		100%	100%
WAD.S.6490	Project Finish	0		05-Oct-26	0%	100%
Contractual Milestones		128	06-May-26	05-Oct-26	0%	0%
WAD.S.1470	Site Handover	0		06-May-26	100%	100%
WAD.S.7550	Contract Schedule (Baseline Program)	0		06-May-26	100%	100%
WAD.S.1320	Completion of Moblization	0		31-May-26	100%	100%
WAD.S.3850	Completion of Fences	0		26-Aug-26	0%	100%
WAD.S.3860	Completion of GUARD HOUSE 1	0		26-Aug-26	0%	100%
WAD.S.5070	Completion of Engineering Works	0		22-Sep-26	0%	100%
WAD.S.6110	Completion of EXT. WORKS	0		27-Sep-26	0%	100%
WAD.S.6250	Completion of Procurment Works	0		28-Sep-26	0%	100%
WAD.S.7560	Testing & Commissioning	0		05-Oct-26	0%	100%
Mobilization		19	06-May-26	31-May-26	0%	0%
Site Layout Plan		3	11-May-26	13-May-26	0%	0%
WAD.S.1120	Site Office Layout Drawing Proposal Submittal	1	11-May-26	11-May-26	100%	100%
WAD.S.1130	Site Office Layout Drawing Review & Approval	2	12-May-26	13-May-26	100%	100%
Construct Site Access Roads		5	14-May-26	20-May-26	0%	0%
WAD.S.1150	Site Preparation	1	14-May-26	14-May-26	100%	100%
WAD.S.1160	Grading & Leveling	2	16-May-26	17-May-26	100%	100%
WAD.S.1200	Temporary Access Road	3	17-May-26	20-May-26	100%	100%
Construct Site Office Fence		8	18-May-26	31-May-26	0%	0%
WAD.S.1230	Excavation for Fence Foundation	4	18-May-26	23-May-26	100%	100%
WAD.S.1270	Installation of Fence Posts	4	19-May-26	24-May-26	100%	100%
WAD.S.1280	Installation of Fence Mesh	4	23-May-26	31-May-26	100%	100%
Construct Site Offices		3	18-May-26	20-May-26	0%	0%
WAD.S.1210	Installation of Site Offices	3	18-May-26	20-May-26	100%	100%
WAD.S.1260	Installation of Furniture	3	18-May-26	20-May-26	100%	100%
WAD.S.1240	MEP Works	2	18-May-26	19-May-26	100%	100%
`	Installation of Site Offices	0			100%	0%
Mobilization of Manpower		6	16-May-26	21-May-26	0%	0%
WAD.S.1170	Mobilization of Manpower	6	16-May-26	21-May-26	100%	100%
Mobilization of Equipment		6	16-May-26	21-May-26	0%	0%
WAD.S.1180	Mobilization of Tools & Equipment	6	16-May-26	21-May-26	100%	100%
Site Survey		4	06-May-26	10-May-26	0%	0%
WAD.S.1020	Site Survey	2	06-May-26	07-May-26	100%	100%
WAD.S.1110	Survey Report	2	09-May-26	10-May-26	100%	100%
Preliminary Submittals		18	06-May-26	30-May-26	0%	0%
WAD.S.1000	Insurances	18	06-May-26	30-May-26	100%	100%
WAD.S.1010	Performance Bonds	10	06-May-26	17-May-26	100%	100%
WAD.S.1030	Contract Schedule (Baseline Program)	13	06-May-26	20-May-26	100%	100%
WAD.S.1040	HSE Plan	12	06-May-26	19-May-26	100%	100%
WAD.S.1050	Quality Control Plan	10	06-May-26	17-May-26	100%	100%

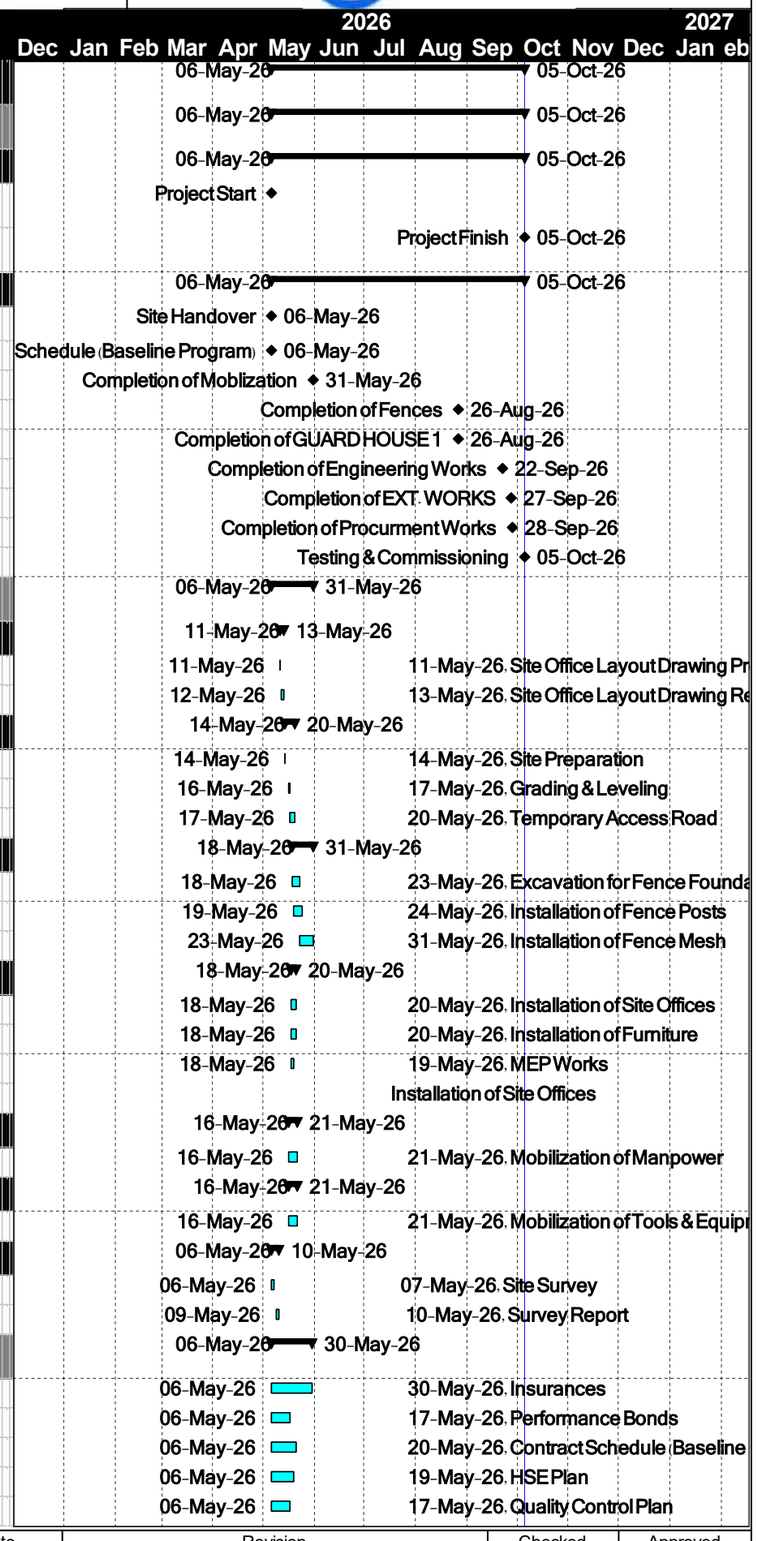

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.1060	Project Organization Chart	12	06-May-26	19-May-26	100%	100%
WAD.S.1070	Submission of Staff CVs	10	06-May-26	17-May-26	100%	100%
Engineering		117	06-May-26	22-Sep-26	37.96%	100%
Shop Drawings		29	06-May-26	11-Jun-26	0%	0%
Prepare & Submit		21	06-May-26	02-Jun-26	0%	0%
WAD.S.1090	FENCES Shop Drawings (Prepare & Submit)	10	06-May-26	17-May-26	100%	100%
WAD.S.1140	GUARD HOUSE 1 Shop Drawings (Prepare & Submit)	10	12-May-26	23-May-26	100%	100%
WAD.S.1190	GUARD HOUSE 1 Shop Drawings (Prepare & Submit)	10	16-May-26	30-May-26	100%	100%
WAD.S.1250	EXT. WORKS Shop Drawings (Prepare & Submit)	10	19-May-26	02-Jun-26	100%	100%
Review & Approve		19	18-May-26	11-Jun-26	0%	0%
WAD.S.1220	FENCES Shop Drawings (Review & Approve)	8	18-May-26	30-May-26	100%	100%
WAD.S.1300	GUARD HOUSE 1 Shop Drawings (Review & Approve)	8	31-May-26	08-Jun-26	100%	100%
WAD.S.1310	GUARD HOUSE 1 Shop Drawings (Review & Approve)	8	31-May-26	08-Jun-26	100%	100%
WAD.S.1330	EXT. WORKS Shop Drawings (Review & Approve)	8	03-Jun-26	11-Jun-26	100%	100%
Material Submittal		80	22-Jun-26	22-Sep-26	37.96%	100%
Material Prepare & Submit		74	22-Jun-26	15-Sep-26	0%	0%
Short Lead Items		74	22-Jun-26	15-Sep-26	0%	0%
WAD.S.1350	Backfilling Works (Material Prepare & Submit)	4	22-Jun-26	25-Jun-26	100%	100%
WAD.S.1360	structural steel beams, posts and rods for wall fence (Material Prepare & Submit)	4	22-Jun-26	25-Jun-26	100%	100%
WAD.S.1400	tubes, bolts, nuts and steel plates to strengthened the wall fence and posts	4	27-Jun-26	30-Jun-26	100%	100%
WAD.S.1500	bitumen waterproofing paint on concrete surfaces (Material Prepare & Submit)	4	01-Jul-26	05-Jul-26	100%	100%
WAD.S.2630	Manhole depth not exceeding 4.0m (Material Prepare & Submit) (GUARD	4	15-Aug-26	18-Aug-26	60%	100%
WAD.S.2690	GRP Pipes laid in trenches (Material Prepare & Submit) (GUARD HOUS	4	19-Aug-26	23-Aug-26	60%	100%
WAD.S.2700	100 mm GRP pipe service connections (Material Prepare & Submit) (GUARD	4	19-Aug-26	23-Aug-26	60%	100%
WAD.S.2830	Concrete Masonry (200mm thick) (Material Prepare & Submit) (GUARD HOUSE)	4	24-Aug-26	27-Aug-26	100%	100%
WAD.S.2880	Concrete Masonry (100mm thick) (Material Prepare & Submit) (GUARD HOUSE)	4	25-Aug-26	29-Aug-26	100%	100%
WAD.S.2900	SIDEWALKS AND CURBS (Material Prepare & Submit) (GUARD HOUSE)	4	25-Aug-26	29-Aug-26	60%	100%
WAD.S.3070	GROUNDING (Material Prepare & Submit) (GUARD HOUSE)	4	29-Aug-26	01-Sep-26	100%	100%
WAD.S.3080	ROAD WORKS (Material Prepare & Submit) (GUARD HOUSE)	4	29-Aug-26	01-Sep-26	100%	100%
WAD.S.3580	FIRE PROTECTION SYSTEM (fire extinguisher) (Material Prepare & Submit)	4	02-Sep-26	06-Sep-26	100%	100%
WAD.S.4700	UNDERGROUND DISTRIBUTION SYSTEM (Material Prepare & Submit)	4	12-Sep-26	15-Sep-26	60%	100%
Long Lead Items		47	15-Jul-26	07-Sep-26	0%	0%
WAD.S.1410	fix galvanized steel chain link gate including all necessary associated (Material	4	15-Jul-26	19-Jul-26	100%	100%
WAD.S.1490	Intrusion Detection system including processor control units items and joints	4	20-Jul-26	23-Jul-26	85%	100%
WAD.S.1520	Handholes\Manholes (Material Prepare & Submit) (FENCES)	4	25-Jul-26	28-Jul-26	85%	100%
WAD.S.1580	structural steel members and plates for main sliding gates (Material Prepare &	4	28-Jul-26	01-Aug-26	100%	100%
WAD.S.2840	ceramic floor tiles (Material Prepare & Submit) (GUARD HOUSE)	4	24-Aug-26	27-Aug-26	60%	100%
WAD.S.2850	Riyadh stone cladding (Material Prepare & Submit) (GUARD HOUSE)	4	24-Aug-26	27-Aug-26	60%	100%
WAD.S.2860	UPS (Material Prepare & Submit) (GUARD HOUSE)	4	24-Aug-26	27-Aug-26	60%	100%
WAD.S.2890	Panel boards (Material Prepare & Submit) (GUARD HOUSE)	4	25-Aug-26	29-Aug-26	60%	100%
WAD.S.3030	PANTRY CABINET (Material Prepare & Submit) (GUARD HOUSE)	4	29-Aug-26	01-Sep-26	60%	100%
WAD.S.3040	20mm thick black granite (Material Prepare & Submit) (GUARD HOUSE)	4	29-Aug-26	01-Sep-26	60%	100%
WAD.S.3050	Workstation chair (Material Prepare & Submit) (GUARD HOUSE)	4	29-Aug-26	01-Sep-26	60%	100%
WAD.S.3060	Safety Disconnect Switches complete with busbar, frame box (Material Prepare	4	29-Aug-26	01-Sep-26	60%	100%
WAD.S.3150	folding & sliding mounter combination ladder for building maintenance purpose	4	30-Aug-26	02-Sep-26	70%	100%
WAD.S.3160	overflow galvanized steel roof scupper (Material Prepare & Submit) (GUARD	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3170	counter desk (Material Prepare & Submit) (GUARD HOUSE)	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3180	install ceramic wall tiles (Material Prepare & Submit) (GUARD HOUSE)	4	30-Aug-26	02-Sep-26	60%	100%

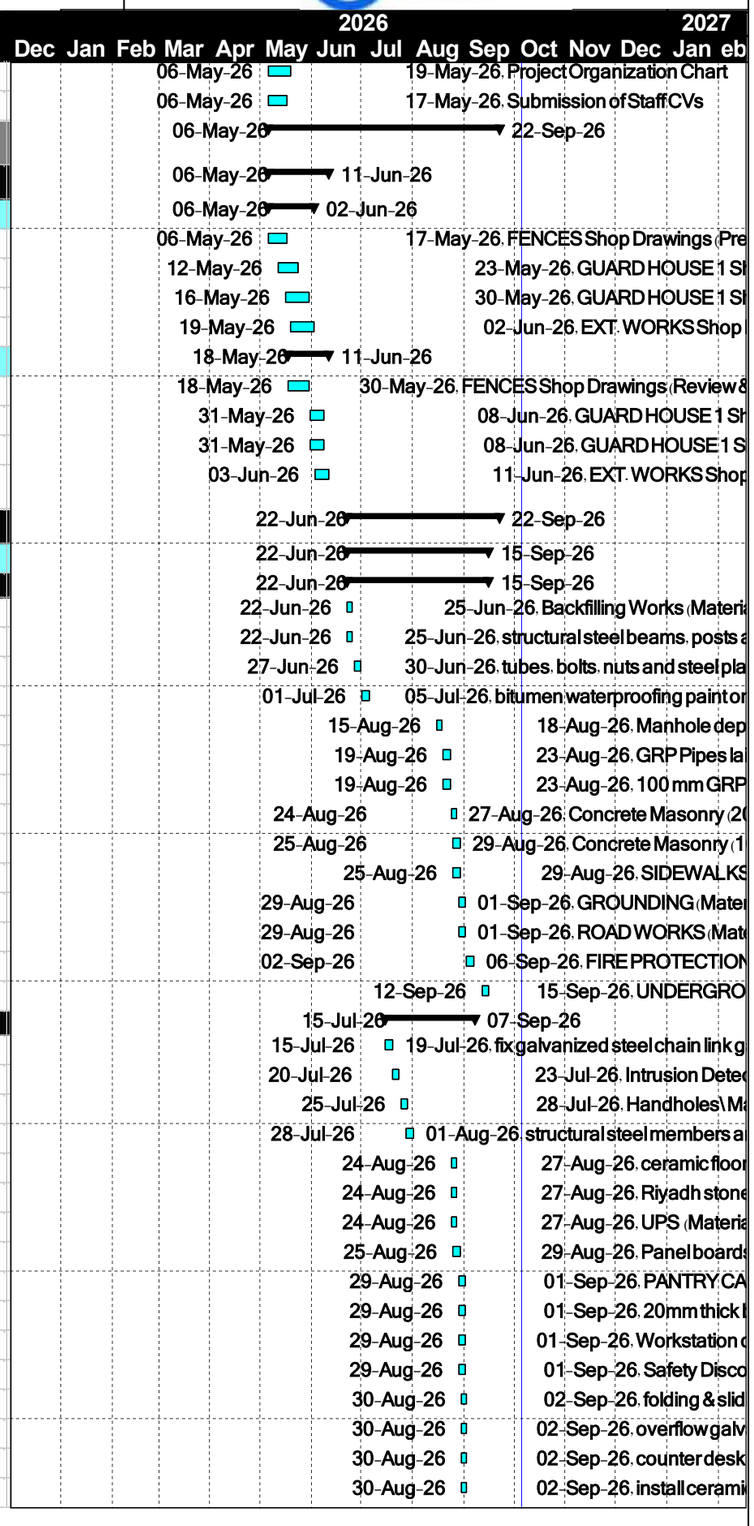

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.3190	PANEL SIGNAGE (Material Prepare & Submit) (GUARD HOUSE)	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3200	COMMUNICATIONS BACKBONE CABLING (Material Prepare & Submit)	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3210	card reader IN/OUT (Material Prepare & Submit) (GUARD HOUSE)	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3220	WATER SUPPLY SYSTEM (Material Prepare & Submit) (GUARD HOUSE)	4	30-Aug-26	02-Sep-26	70%	100%
WAD.S.3230	SEWER AND DRAINAGE SYSTEM (Material Prepare & Submit) (GUARD	4	30-Aug-26	02-Sep-26	70%	100%
WAD.S.3240	SUPPLY AND INSTALL PLUMBING FIXTURES (Material Prepare & Submit)	4	30-Aug-26	02-Sep-26	60%	100%
WAD.S.3250	HEATING, VENTILATION AND AIR CONDITIONING (Material Prepare & Submit)	4	30-Aug-26	02-Sep-26	80%	100%
WAD.S.3300	heavy steel cover with frame for tanks (Material Prepare & Submit) (GUARD	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3310	HOLLOW METAL DOORS AND FRAMES (Material Prepare & Submit) (GUARD	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3320	ALUMINIUM DOORS (Material Prepare & Submit) (GUARD HOUSE)	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3330	TOILET AND BATH ACCESSROIES (Material Prepare & Submit) (GUARD	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3340	Waste Receptacle (Material Prepare & Submit) (GUARD HOUSE)	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3350	LIGHTING FIXTURES (Material Prepare & Submit) (GUARD HOUSE)	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3360	Access control panel (Material Prepare & Submit) (GUARD HOUSE)	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3370	VIDEO SURVEILLANCE (Material Prepare & Submit) (GUARD HOUSE)	4	31-Aug-26	03-Sep-26	60%	100%
WAD.S.3560	aluminum framed double glazed windows (Material Prepare & Submit) (GUARD	4	02-Sep-26	06-Sep-26	60%	100%
WAD.S.3570	Roller blind (Material Prepare & Submit) (GUARD HOUSE)	4	02-Sep-26	06-Sep-26	60%	100%
WAD.S.3590	DATA COMMUNICATIONS (Material Prepare & Submit) (GUARD HOUSE)	4	02-Sep-26	06-Sep-26	60%	100%
WAD.S.3710	COMPUTERS AND RELATED PERIPHERALS (Material Prepare & Submit)	4	03-Sep-26	07-Sep-26	60%	100%
Material Review & Approve		76	27-Jun-26	22-Sep-26	37.96%	100%
Short Lead Items		76	27-Jun-26	22-Sep-26	75.71%	100%
WAD.S.1380	Backfilling Works (Material Review & Approve)	6	27-Jun-26	02-Jul-26	100%	100%
WAD.S.1390	structural steel beams, posts and rods for wall fence (Material Review &	6	27-Jun-26	02-Jul-26	100%	100%
WAD.S.1440	tubes, bolts, nuts and steel plates to strengthened the wall fence and posts	6	01-Jul-26	07-Jul-26	100%	100%
WAD.S.1550	bitumen waterproofing paint on concrete surfaces (Material Review & Approve)	6	06-Jul-26	12-Jul-26	100%	100%
WAD.S.2680	Manhole depth not exceeding 4.0m (Material Review & Approve) (GUARD	6	19-Aug-26	25-Aug-26	0%	100%
WAD.S.2810	GRP Pipes laid in trenches (Material Review & Approve) (GUARD HOUS	6	24-Aug-26	30-Aug-26	100%	100%
WAD.S.2820	100 mm GRP pipe service connections (Material Review & Approve) (GUARD	6	24-Aug-26	30-Aug-26	100%	100%
WAD.S.2990	Concrete Masonry (200mm thick) (Material Review & Approve) (GUARD	6	29-Aug-26	03-Sep-26	100%	100%
WAD.S.3120	Concrete Masonry (100mm thick) (Material Review & Approve) (GUARD	6	30-Aug-26	05-Sep-26	100%	100%
WAD.S.3140	SIDEWALKS AND CURBS (Material Review & Approve) (GUARD HOUSE)	6	30-Aug-26	05-Sep-26	0%	100%
WAD.S.3540	GROUNDING (Material Review & Approve) (GUARD HOUSE)	6	02-Sep-26	08-Sep-26	100%	100%
WAD.S.3550	ROAD WORKS (Material Review & Approve) (GUARD HOUSE)	6	02-Sep-26	08-Sep-26	60%	100%
WAD.S.4060	FIRE PROTECTION SYSTEM (fire extinguisher) (Material Review & Approve)	6	07-Sep-26	13-Sep-26	100%	100%
WAD.S.4840	UNDERGROUND DISTRIBUTION SYSTEM (Material Review & Approve)	6	16-Sep-26	22-Sep-26	0%	100%
Long Lead Items		49	20-Jul-26	14-Sep-26	22.86%	100%
WAD.S.1480	fix galvanized steel chain link gate including all necessary associated (Material	6	20-Jul-26	26-Jul-26	100%	100%
WAD.S.1510	Intrusion Detection system including processor control units items and joints	6	25-Jul-26	30-Jul-26	85%	100%
WAD.S.1650	Handholes\Manholes (Material Review & Approve) (FENCES)	6	29-Jul-26	04-Aug-26	0%	100%
WAD.S.2190	structural steel members and plates for main sliding gates (Material Review &	6	02-Aug-26	08-Aug-26	100%	100%
WAD.S.3000	ceramic floor tiles (Material Review & Approve) (GUARD HOUSE)	6	29-Aug-26	03-Sep-26	0%	100%
WAD.S.3010	install Riyadh stone cladding (Material Review & Approve) (GUARD HOUSE)	6	29-Aug-26	03-Sep-26	0%	100%
WAD.S.3020	UPS (Material Review & Approve) (GUARD HOUSE)	6	29-Aug-26	03-Sep-26	0%	100%
WAD.S.3130	Panel boards (Material Review & Approve) (GUARD HOUSE)	6	30-Aug-26	05-Sep-26	0%	100%
WAD.S.3500	PANTRY CABINET (Material Review & Approve) (GUARD HOUSE)	6	02-Sep-26	08-Sep-26	0%	100%
WAD.S.3510	20mm thick black granite (Material Review & Approve) (GUARD HOUSE)	6	02-Sep-26	08-Sep-26	0%	100%
WAD.S.3520	Workstation chair (Material Review & Approve) (GUARD HOUSE)	6	02-Sep-26	08-Sep-26	0%	100%
WAD.S.3530	Safety Disconnect Switches complete with busbar, frame box (Material Review	6	02-Sep-26	08-Sep-26	100%	100%
WAD.S.3600	folding & sliding mounter combination ladder for building maintenance purpose	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3610	overflow galvanized steel roof scupper (Material Review & Approve) (GUARD	6	03-Sep-26	09-Sep-26	0%	100%

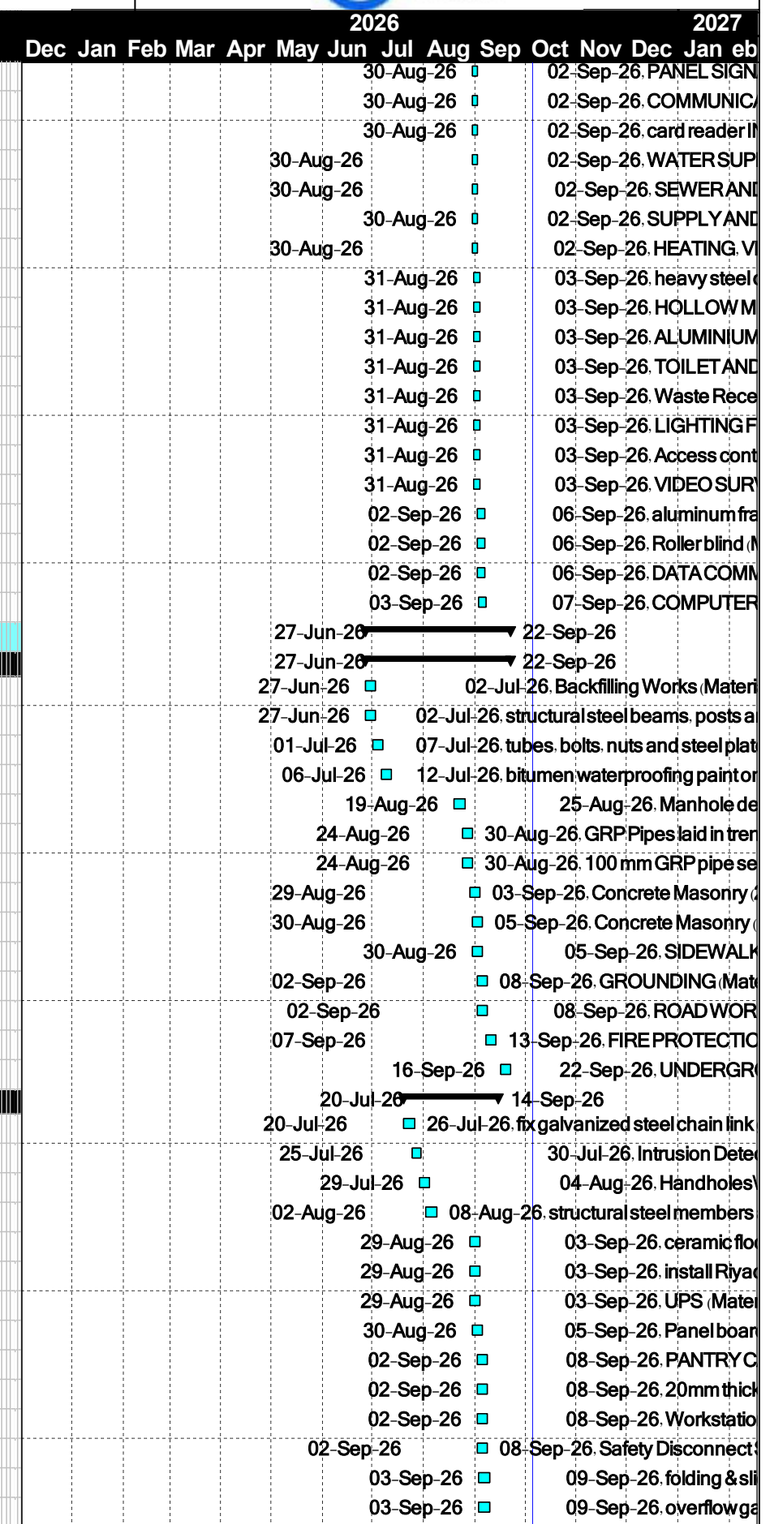

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.3620	counter desk (Material Review & Approve) (GUARD HOUSE)	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3630	install ceramic wall tiles (Material Review & Approve) (GUARD HOUSE)	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3640	PANEL SIGNAGE (Material Review & Approve) (GUARD HOUSE)	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3650	COMMUNICATIONS BACKBONE CABLING (Material Review & Approve)	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3660	card reader IN/OUT (Material Review & Approve) (GUARD HOUSE)	6	03-Sep-26	09-Sep-26	0%	100%
WAD.S.3670	WATER SUPPLY SYSTEM (Material Review & Approve) (GUARD HOUSE)	6	03-Sep-26	09-Sep-26	85%	100%
WAD.S.3680	SEWER AND DRAINAGE SYSTEM (Material Review & Approve) (GUARD	6	03-Sep-26	09-Sep-26	85%	100%
WAD.S.3690	SUPPLY AND INSTALL PLUMBING FIXTURES (Material Review & Approve)	6	03-Sep-26	09-Sep-26	75%	100%
WAD.S.3700	HEATING, VENTILATION AND AIR CONDITIONING (Material Review &	6	03-Sep-26	09-Sep-26	85%	100%
WAD.S.3770	heavy steel cover with frame for tanks (Material Review & Approve) (GUARD	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3780	HOLLOW METAL DOORS AND FRAMES (Material Review & Approve) (GUARD	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3790	ALUMINIUM DOORS (Material Review & Approve) (GUARD HOUSE)	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3800	TOILET AND BATH ACCESSROIES (Material Review & Approve) (GUARD	6	05-Sep-26	10-Sep-26	85%	100%
WAD.S.3810	Waste Receptacle (Material Review & Approve) (GUARD HOUSE)	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3820	LIGHTING FIXTURES (Material Review & Approve) (GUARD HOUSE)	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3830	Access control panel (Material Review & Approve) (GUARD HOUSE)	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.3840	VIDEO SURVEILLANCE (Material Review & Approve) (GUARD HOUSE)	6	05-Sep-26	10-Sep-26	0%	100%
WAD.S.4040	aluminum framed double glazed windows (Material Review & Approve) (GUARD	6	07-Sep-26	13-Sep-26	0%	100%
WAD.S.4050	Roller blind (Material Review & Approve) (GUARD HOUSE)	6	07-Sep-26	13-Sep-26	0%	100%
WAD.S.4070	DATA COMMUNICATIONS (Material Review & Approve) (GUARD HOUSE)	6	07-Sep-26	13-Sep-26	0%	100%
WAD.S.4080	COMPUTERS AND RELATED PERIPHERALS (Material Review & Approve)	6	08-Sep-26	14-Sep-26	0%	100%
Procurement		75	04-Jul-26	28-Sep-26	84.11%	100%
Fabrication & Delivery		75	04-Jul-26	28-Sep-26	84.11%	100%
Short Lead Items		73	04-Jul-26	26-Sep-26	95.12%	100%
WAD.S.1420	Backfilling Works	4	04-Jul-26	07-Jul-26	100%	100%
WAD.S.1430	structural steel beams, posts and rods for wall fence (FENCES)	4	04-Jul-26	07-Jul-26	95%	100%
WAD.S.1540	tubes, bolts, nuts and steel plates to strengthened the wall fence and posts	3	08-Jul-26	11-Jul-26	95%	100%
WAD.S.2180	bitumen waterproofing paint on concrete surfaces (FENCES)	4	13-Jul-26	16-Jul-26	100%	100%
WAD.S.2970	Manhole depth not exceeding 4.0m (GUARD HOUSE)	8	26-Aug-26	03-Sep-26	70%	100%
WAD.S.3280	GRP Pipes laid in trenches(Fabrication & Delivery) (GUARD HOUSE)	6	31-Aug-26	06-Sep-26	100%	100%
WAD.S.3290	100 mm GRP pipe service connections (GUARD HOUSE)	6	31-Aug-26	06-Sep-26	70%	100%
WAD.S.3730	Concrete Masonry (200mm thick) (GUARD HOUSE)	3	05-Sep-26	07-Sep-26	100%	100%
WAD.S.3890	Concrete Masonry (100mm thick) (GUARD HOUSE)	2	06-Sep-26	07-Sep-26	100%	100%
WAD.S.3910	SIDEWALKS AND CURBS (GUARD HOUSE)	7	06-Sep-26	13-Sep-26	70%	100%
WAD.S.4160	GROUNDING (GUARD HOUSE)	3	09-Sep-26	12-Sep-26	70%	100%
WAD.S.4170	ROAD WORKS (GUARD HOUSE)	6	09-Sep-26	15-Sep-26	70%	100%
WAD.S.4780	FIRE PROTECTION SYSTEM (fire extinguisher) (GUARD HOUSE)	5	14-Sep-26	19-Sep-26	70%	100%
WAD.S.5080	UNDERGROUND DISTRIBUTION SYSTEM (GUARD HOUSE)	3	23-Sep-26	26-Sep-26	70%	100%
Long Lead Items		55	27-Jul-26	28-Sep-26	76.66%	100%
WAD.S.1570	fix galvanized steel chain link gate including all necessary associated	15	27-Jul-26	12-Aug-26	95%	100%
WAD.S.2170	Intrusion Detection system including processor control units items and joints	12	01-Aug-26	13-Aug-26	70%	100%
WAD.S.2260	Handholes\Manholes (FENCES)	12	05-Aug-26	18-Aug-26	70%	100%
WAD.S.2470	structural steel members and plates for main sliding gates (FENCES)	14	09-Aug-26	24-Aug-26	95%	100%
WAD.S.3740	ceramic floor tiles (GUARD HOUSE)	12	05-Sep-26	17-Sep-26	70%	100%
WAD.S.3750	install Riyadh stone cladding (GUARD HOUSE)	12	05-Sep-26	17-Sep-26	70%	100%
WAD.S.3760	UPS (GUARD HOUSE)	18	05-Sep-26	24-Sep-26	50%	100%
WAD.S.3900	Panel boards (GUARD HOUSE)	18	06-Sep-26	26-Sep-26	50%	100%
WAD.S.4120	PANTRY CABINET (GUARD HOUSE)	15	09-Sep-26	26-Sep-26	50%	100%

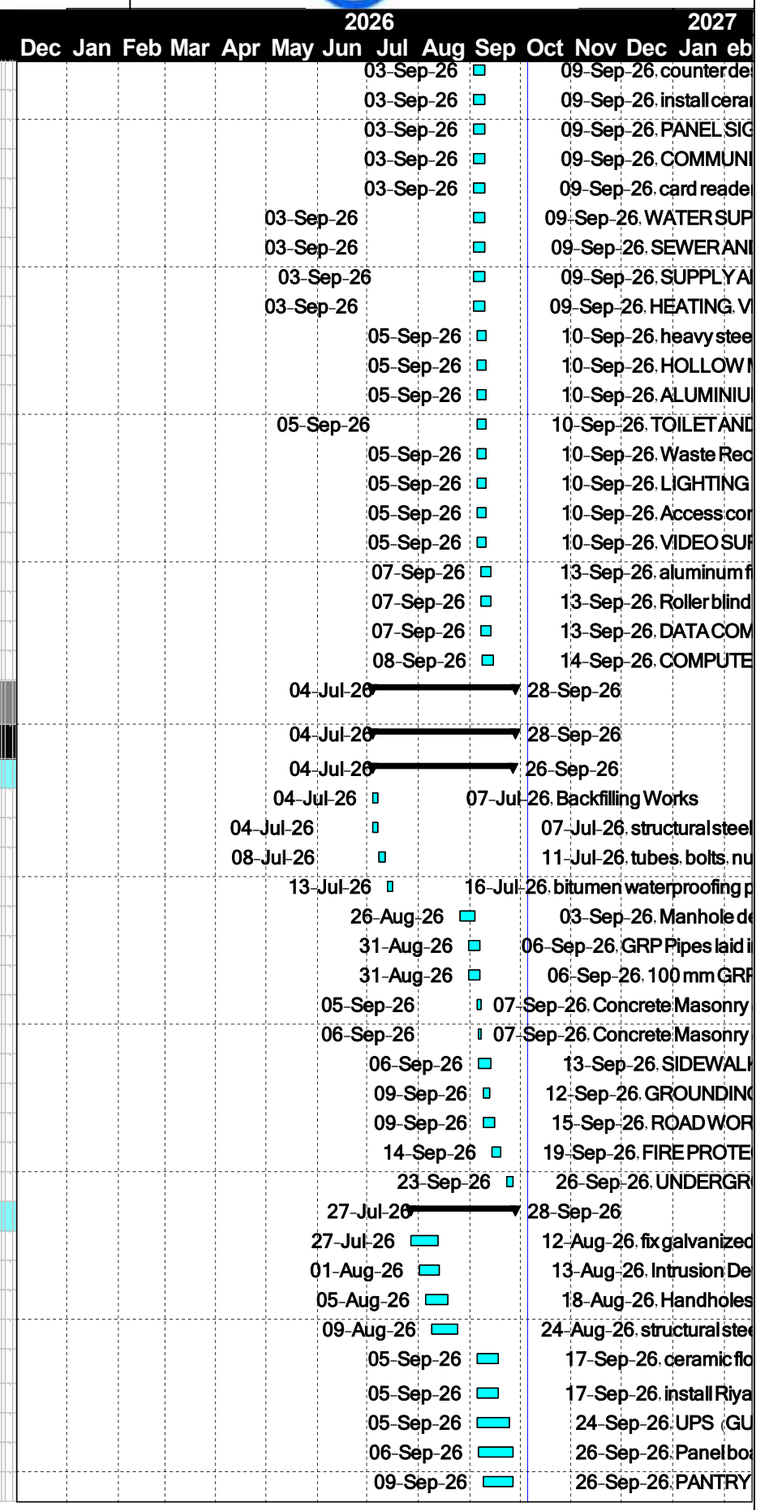

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.4130	20mm thick black granite (GUARD HOUSE)	13	09-Sep-26	23-Sep-26	50%	100%
WAD.S.4140	Workstation chair (GUARD HOUSE)	16	09-Sep-26	27-Sep-26	50%	100%
WAD.S.4150	Safety Disconnect Switches complete with busbar, frame box (GUARD	17	09-Sep-26	28-Sep-26	50%	100%
WAD.S.4510	folding & sliding mounter combination ladder for building maintenance purpose	13	10-Sep-26	24-Sep-26	50%	100%
WAD.S.4520	overflow galvanized steel roof scupper (GUARD HOUSE)	13	10-Sep-26	24-Sep-26	50%	100%
WAD.S.4530	counter desk (GUARD HOUSE)	14	10-Sep-26	26-Sep-26	50%	100%
WAD.S.4540	install ceramic wall tiles (GUARD HOUSE)	12	10-Sep-26	23-Sep-26	50%	100%
WAD.S.4550	PANEL SIGNAGE (GUARD HOUSE)	14	10-Sep-26	26-Sep-26	50%	100%
WAD.S.4560	COMMUNICATIONS BACKBONE CABLING (GUARD HOUSE)	13	10-Sep-26	24-Sep-26	50%	100%
WAD.S.4570	card reader IN/OUT (GUARD HOUSE)	15	10-Sep-26	27-Sep-26	50%	100%
WAD.S.4580	WATER SUPPLY SYSTEM (GUARD HOUSE)	13	10-Sep-26	24-Sep-26	50%	100%
WAD.S.4590	SEWER AND DRAINAGE SYSTEM (GUARD HOUSE)	14	10-Sep-26	26-Sep-26	50%	100%
WAD.S.4600	SUPPLY PLUMBING FIXTURES (GUARD HOUSE)	13	10-Sep-26	24-Sep-26	50%	100%
WAD.S.4610	HEATING, VENTILATION AND AIR CONDITIONING (GUARD HOUSE)	14	10-Sep-26	26-Sep-26	50%	100%
WAD.S.4620	heavy steel cover with frame for tanks (GUARD HOUSE)	13	12-Sep-26	26-Sep-26	50%	100%
WAD.S.4630	HOLLOW METAL DOORS AND FRAMES (GUARD HOUSE)	14	12-Sep-26	27-Sep-26	50%	100%
WAD.S.4640	ALUMINIUM DOORS (GUARD HOUSE)	13	12-Sep-26	26-Sep-26	50%	100%
WAD.S.4650	TOILET AND BATH ACCESSROIES (GUARD HOUSE)	13	12-Sep-26	26-Sep-26	50%	100%
WAD.S.4660	Waste Receptacle (GUARD HOUSE)	15	12-Sep-26	28-Sep-26	50%	100%
WAD.S.4670	LIGHTING FIXTURES (GUARD HOUSE)	12	12-Sep-26	24-Sep-26	50%	100%
WAD.S.4680	Access control panel (GUARD HOUSE)	14	12-Sep-26	27-Sep-26	50%	100%
WAD.S.4690	VIDEO SURVEILLANCE (GUARD HOUSE)	14	12-Sep-26	27-Sep-26	50%	100%
WAD.S.4760	aluminum framed double glazed windows (GUARD HOUSE)	12	14-Sep-26	27-Sep-26	50%	100%
WAD.S.4770	Roller blind (GUARD HOUSE)	12	14-Sep-26	27-Sep-26	50%	100%
WAD.S.4790	DATA COMMUNICATIONS (GUARD HOUSE)	13	14-Sep-26	28-Sep-26	50%	100%
WAD.S.4820	COMPUTERS AND RELATED PERIPHERALS (GUARD HOUSE)	10	15-Sep-26	26-Sep-26	50%	100%
Construction		87	27-Jun-26	05-Oct-26	69.31%	100%
FENCES		87	27-Jun-26	05-Oct-26	78.44%	100%
SITE WORKS		53	27-Jun-26	26-Aug-26	100%	100%
WAD.S.1340	Demolition Works	10	27-Jun-26	07-Jul-26	100%	100%
WAD.S.1370	Excavation Works	15	08-Jul-26	25-Jul-26	100%	100%
WAD.S.1530	Backfilling Works Before Foundation	18	26-Jul-26	15-Aug-26	100%	100%
WAD.S.3380	Backfilling Works After Foundation	5	22-Aug-26	26-Aug-26	100%	100%
CONCRETE WORKS		42	26-Jul-26	12-Sep-26	96%	100%
Part 1		21	26-Jul-26	18-Aug-26	96%	100%
WAD.S.1560	cast in place reinforced concrete for the sub-structures - Part 1	21	26-Jul-26	18-Aug-26	96%	100%
Part 2		21	19-Aug-26	12-Sep-26	96%	100%
WAD.S.2720	cast in place reinforced concrete for the sub-structures - Part 2	21	19-Aug-26	12-Sep-26	96%	100%
THERMAL & MOISTURE PROTECTION		42	28-Jul-26	14-Sep-26	89%	100%
Part 1		21	28-Jul-26	20-Aug-26	89%	100%
WAD.S.2330	Applying 2 coats of bitumen waterproofing paint on concrete surfaces - Part 1	21	28-Jul-26	20-Aug-26	89%	100%
Part 2		21	22-Aug-26	14-Sep-26	89%	100%
WAD.S.3420	Applying 2 coats of bitumen waterproofing paint on concrete surfaces - Part 2	21	22-Aug-26	14-Sep-26	89%	100%
SPECIAL CONSTRUCTION- STRUCTURAL STEEL		36	25-Aug-26	05-Oct-26	93.55%	100%
Part 1		36	25-Aug-26	05-Oct-26	99.86%	100%
WAD.S.2870	install structural steel beams, posts and rods for wall fence - Part 1	21	25-Aug-26	17-Sep-26	100%	100%
WAD.S.3260	Install tubes, bolts, nuts and steel plates to strengthened the wall fence and	21	31-Aug-26	23-Sep-26	100%	100%
WAD.S.3870	fix galvanized steel chain link fence wall including steel tube framing and posts,	21	06-Sep-26	29-Sep-26	100%	100%
WAD.S.4720	galvanized steel chain link gates Installation - Part 1	20	13-Sep-26	05-Oct-26	88%	100%
Part 2		36	25-Aug-26	05-Oct-26	87.25%	100%

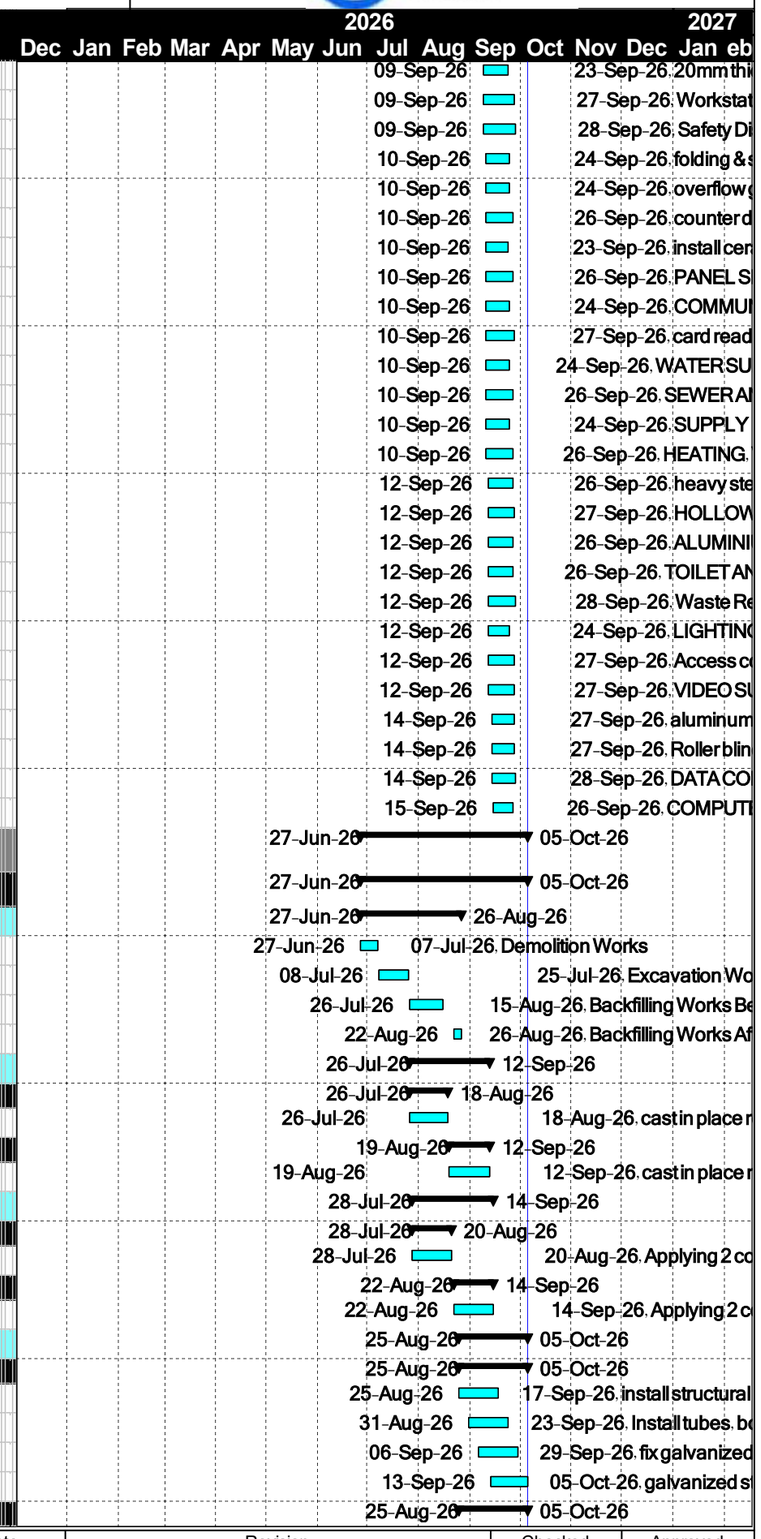

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.2920	install structural steel beams, posts and rods for wall fence - Part2	21	25-Aug-26	17-Sep-26	88%	100%
WAD.S.3430	Install tubes, bolts, nuts and steel plates to strengthened the wall fence and	21	31-Aug-26	23-Sep-26	88%	100%
WAD.S.3950	fix galvanized steel chain link fence wall including steel tube framing and posts,	21	06-Sep-26	29-Sep-26	88%	100%
WAD.S.4730	galvanized steel chain link gates Installation - Part2	20	13-Sep-26	05-Oct-26	25%	100%
ELECTRICAL WORKS		34	16-Aug-26	23-Sep-26	23.83%	100%
WAD.S.2640	Intrusion Detection system including processor control units items and joints -	9	16-Aug-26	25-Aug-26	0%	100%
WAD.S.2950	Fiber Optic Outdoor Cable	8	26-Aug-26	03-Sep-26	55%	100%
WAD.S.2960	Road crossing ducts for Fiber Optic Cable	7	26-Aug-26	02-Sep-26	0%	100%
WAD.S.2980	install 50mm diameter high-density polyethylene (HDPE) pipe including the	8	29-Aug-26	06-Sep-26	0%	100%
WAD.S.3720	Fiber Optic Outdoor Cable To Close The Loop	9	05-Sep-26	14-Sep-26	0%	100%
WAD.S.4810	Handholes\Manholes	8	15-Sep-26	23-Sep-26	87.99%	100%
ELECTRICAL GATE BARRIER		8	15-Sep-26	23-Sep-26	0%	100%
WAD.S.4830	Install Electrical gate barrier complete (cables, conduits, pipes, pulling cables in	8	15-Sep-26	23-Sep-26	0%	100%
GUARD HOUSE 1		65	19-Jul-26	01-Oct-26	30.72%	100%
SITE WORKS		56	19-Jul-26	21-Sep-26	77%	100%
Guard Rooms & Gates		17	19-Jul-26	06-Aug-26	100%	100%
WAD.S.1450	Excavation for guard rooms	8	19-Jul-26	27-Jul-26	100%	100%
WAD.S.1590	Replacment Under Foundation	2	28-Jul-26	29-Jul-26	100%	100%
WAD.S.2270	Backfilling Under G.Beam	2	05-Aug-26	06-Aug-26	100%	100%
WAD.S.2280	Backfilling Under S.O.G	2	05-Aug-26	06-Aug-26	100%	100%
Guard Rooms & Gates (CONCRETE Works)		48	28-Jul-26	21-Sep-26	73.98%	100%
WAD.S.1600	50 mm thickness lean concrete under the foundation.	3	28-Jul-26	30-Jul-26	100%	100%
WAD.S.1820	Isolated Footings & Column Neck	5	30-Jul-26	04-Aug-26	100%	100%
WAD.S.2340	50 mm thickness lean concrete under grade beams.	3	08-Aug-26	10-Aug-26	100%	100%
WAD.S.2600	Grade beams	5	11-Aug-26	16-Aug-26	100%	100%
WAD.S.2650	Columns	4	17-Aug-26	20-Aug-26	100%	100%
WAD.S.2710	Raft and R.C. walls	5	19-Aug-26	24-Aug-26	100%	100%
WAD.S.2750	Roof Slab	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.2760	Beams	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.3390	Provide and cast concrete floor slab on grade	5	31-Aug-26	05-Sep-26	100%	100%
WAD.S.3400	Concrete Pad	3	31-Aug-26	02-Sep-26	100%	100%
WAD.S.3410	Tanks Raft	5	31-Aug-26	05-Sep-26	0%	100%
WAD.S.3940	Tanks Walls	5	06-Sep-26	10-Sep-26	0%	100%
WAD.S.4850	Tanks Slab	4	17-Sep-26	21-Sep-26	0%	100%
MASONRY UNIT		3	25-Aug-26	27-Aug-26	100%	100%
WAD.S.2910	install Concrete Masonry Unit (CMU) for walls	3	25-Aug-26	27-Aug-26	100%	100%
THERMAL & MOISTURE PROTECTION		4	06-Sep-26	09-Sep-26	31.41%	100%
THERMAL & MOISTURE PROTECTION - Foundation		4	06-Sep-26	09-Sep-26	31.41%	100%
WAD.S.3920	apply 2 coats of bitumen waterproofing paint on concrete surface in contact with	2	06-Sep-26	07-Sep-26	100%	100%
WAD.S.3930	install liquid applied waterproofing coating single-component pitch modified	2	06-Sep-26	07-Sep-26	0%	100%
WAD.S.4090	install geotextile sheet	2	08-Sep-26	09-Sep-26	0%	100%
ROOFING SYSTEM		11	09-Sep-26	21-Sep-26	5.83%	100%
WAD.S.4180	install liquid applied waterproofing coating single-component pitch modified	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4190	install 4mm thick APP modified bituminous membrane - single layer	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4200	install 75mm thick rigid insulation (extruded polystyrene)	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4210	cast in place foam concrete screed, 50mm thick minimum laid to fall and cross	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4220	install 300 micron polyethylene sheet	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4230	install 50mm thick loose gravel toppings	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4240	install high density polyisocynurate cover board	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4250	install UV resistant geotextile sheet	11	09-Sep-26	21-Sep-26	0%	100%

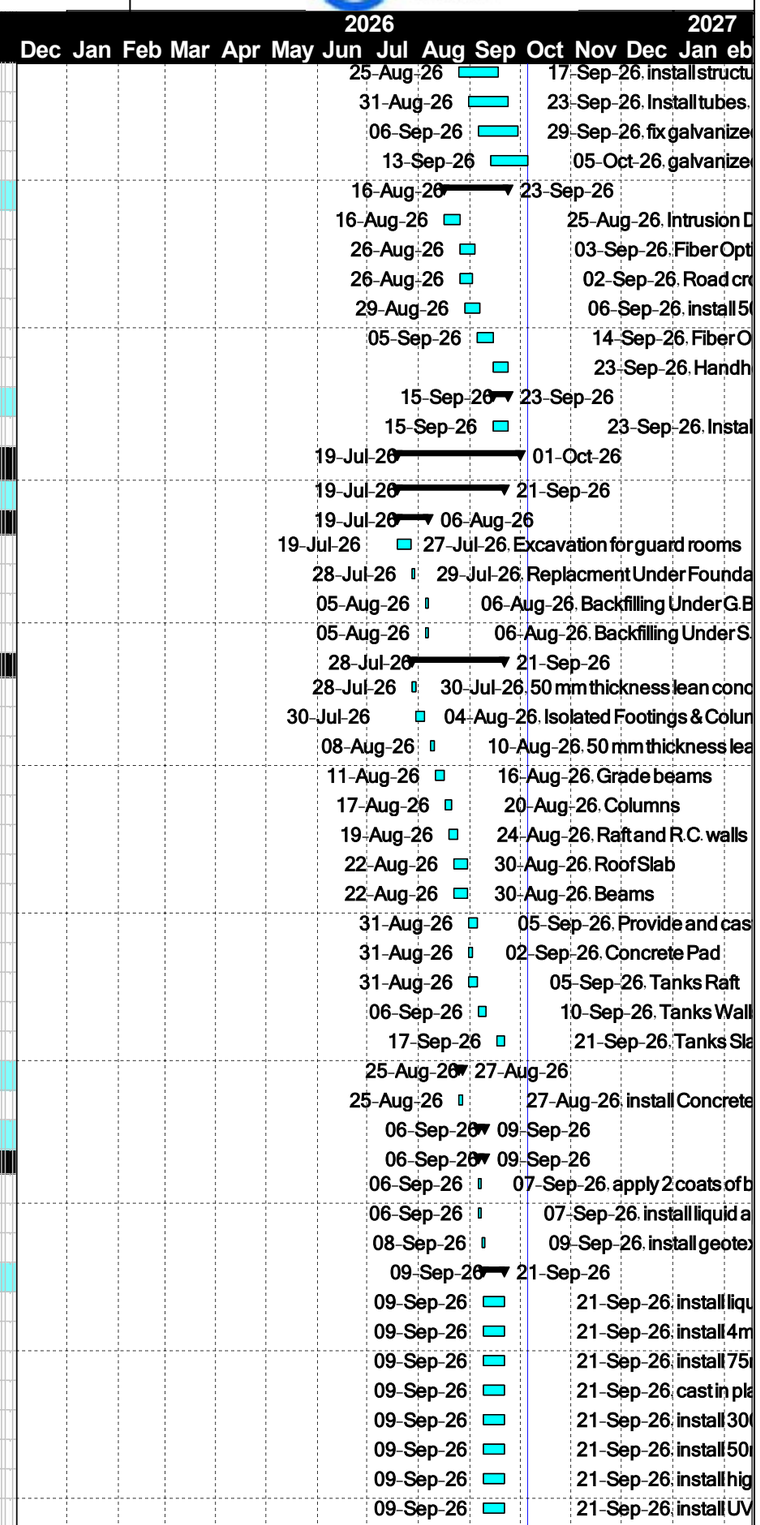

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.4260	fixing 3mm thick extruded aluminum flashing 40mm with sealant and all other	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4270	install Terrazzo tiles	11	09-Sep-26	21-Sep-26	0%	100%
THERMAL & MOISTURE PROTECTION - Tanks		11	09-Sep-26	21-Sep-26	35%	100%
WAD.S.4280	lay epoxy 2 coating for inner surfaces for bottom of the roof	11	09-Sep-26	21-Sep-26	35%	100%
WAD.S.4710	install water stop for tanks according to the drawings and specification	5	12-Sep-26	16-Sep-26	35%	100%
FINISHES		26	29-Aug-26	27-Sep-26	8.18%	100%
WAD.S.3090	install concrete plastering	4	29-Aug-26	01-Sep-26	90%	100%
WAD.S.4940	install ceramic floor tiles	3	19-Sep-26	21-Sep-26	0%	100%
WAD.S.4950	install granite flooring	2	19-Sep-26	20-Sep-26	0%	100%
WAD.S.5010	install granite saddles and thresholds	3	19-Sep-26	21-Sep-26	0%	100%
WAD.S.5020	install Riyadh stone cladding	3	19-Sep-26	21-Sep-26	0%	100%
WAD.S.5030	install 3mm steel CNC laser cut panels	3	19-Sep-26	21-Sep-26	0%	100%
WAD.S.5040	gypsum board suspended ceiling	5	19-Sep-26	23-Sep-26	0%	100%
WAD.S.5060	install aluminum cladding	2	20-Sep-26	21-Sep-26	0%	100%
WAD.S.5120	install ceramic wall tiles	3	24-Sep-26	27-Sep-26	0%	100%
WAD.S.5530	install two coats of acrylic paint on internal walls	2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.5540	install two coats of acrylic paint (suitable for exterior use) on external	2	26-Sep-26	27-Sep-26	0%	100%
MECHANICAL WORKS		53	30-Jul-26	29-Sep-26	50%	100%
MECHANICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1660	WATER SUPPLY SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1670	SEWER AND DRAINAGE SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1680	IRRIGATION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1710	HEATING, VENTILATION AND AIR CONDITIONING - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1720	Exhaust fans - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
MECHANICAL WORKS - Final Fix		5	24-Sep-26	29-Sep-26	22.22%	100%
WAD.S.5130	installation of Fire extinguishers as per drawings, specifications	3	24-Sep-26	27-Sep-26	50%	100%
WAD.S.5140	gully traps with heavy duty cover	3	24-Sep-26	27-Sep-26	50%	100%
WAD.S.5150	chamber with heavy duty cover	3	24-Sep-26	27-Sep-26	50%	100%
WAD.S.5160	INSTALL PLUMBING FIXTURES	3	24-Sep-26	27-Sep-26	50%	100%
WAD.S.5910	HEATING, VENTILATION AND AIR CONDITIONING - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5920	Exhaust fans - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5930	Bulbblers and Spreyers of IRRIGATION SYSTEM	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5980	WATER SUPPLY SYSTEM - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5990	IRRIGATION SYSTEM - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
ELECTRICAL WORKS		55	30-Jul-26	01-Oct-26	33.33%	100%
ELECTRICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1690	LIGHTING AND POWER TYPE PANELBOARDS - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1700	UPS 3KVA (installed inside the rack) - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1730	power source with built-in photocell sensor for automatic electrical connection	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1740	UNDERGROUND DISTRIBUTION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1750	LIGHTING FIXTURES - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1760	installation of Wiring devices includes switches and Receptacle outlets	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1770	GROUNDING - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1780	card reader IN/OUT - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1790	CCTV cameras - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1800	Access control panel - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.1810	fire alarm system including wires, conduit and other materials - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
ELECTRICAL WORKS - Final Fix		5	27-Sep-26	01-Oct-26	0%	100%
WAD.S.5940	power source with built-in photocell sensor for automatic electrical connection	3	27-Sep-26	29-Sep-26	0%	100%

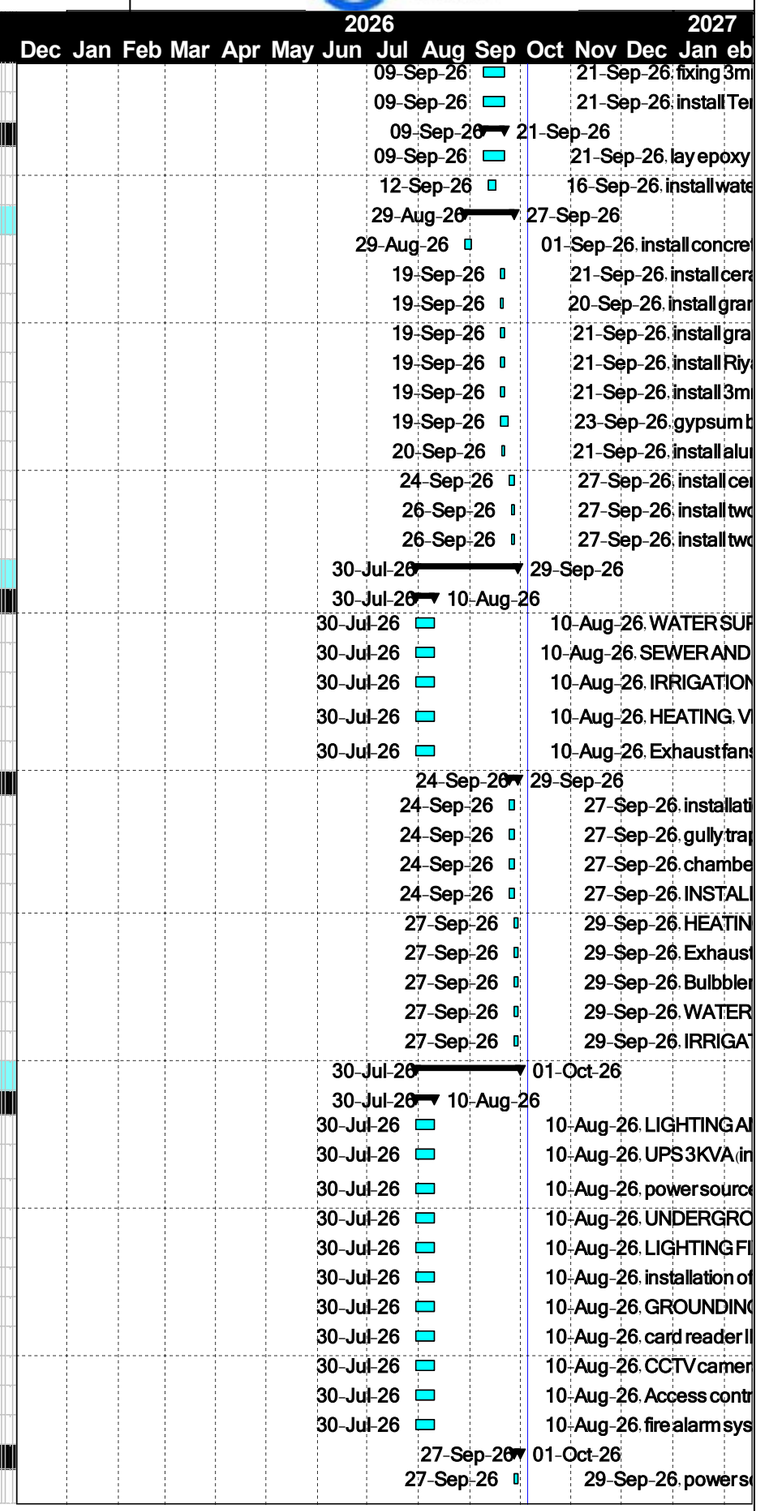

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.5950	LIGHTING FIXTURES - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5960	GROUNDING - Final Fix	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5970	12-Port, SMF, Fiber Optic Patch Panels	4	27-Sep-26	30-Sep-26	0%	100%
WAD.S.6140	UNDERGROUND DISTRIBUTION SYSTEM - Final Fix	2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6150	installation of Wiring devices includes switches and Receptacle outlets	2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6160	card reader IN/OUT - Final Fix	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6170	12-Port CAT6A UTP fully loaded patch panel	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6180	COMPUTERS AND RELATED PERIPHERALS	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6190	VIDEO SURVEILLANCE	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6200	CCTV storage system, as specified	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6270	Access control panel - Final Fix	2	29-Sep-26	30-Sep-26	0%	100%
WAD.S.6280	Central (Headend) System Components	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6290	VSS System, as specified	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6300	CCTV cameras - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6310	ELECTRICAL GATE BARRIER	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6320	fire alarm system including wires, conduit and other materials - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6330	Analog addressable fire alarm control panel with battery	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6340	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6420	20A, ATS (Automatic transfer switch) for UPS	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6430	LIGHTNING PROTECTION	2	30-Sep-26	01-Oct-26	0%	100%
WAD.S.6440	Intelligent Ionization / Photoelectric smoke and heat detector with base	2	30-Sep-26	01-Oct-26	0%	100%
METALS		2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.5500	folding & sliding mounter combination ladder for building maintenance purpose	2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.5510	install of overflow galvanized steel roof scupper with gray color with angular	2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.5520	install heavy steel cover with frame including all necessary fixings	2	26-Sep-26	27-Sep-26	0%	100%
WOODS AND PLASTICS		3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.5880	PANTRY CABINET	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.5890	COUNTER DESK	3	27-Sep-26	29-Sep-26	0%	100%
DOORS & WINDOWS		8	22-Sep-26	30-Sep-26	0%	100%
WAD.S.5050	install hollow metal door	4	22-Sep-26	26-Sep-26	0%	100%
WAD.S.5900	Install Aluminum Door	3	27-Sep-26	29-Sep-26	0%	100%
WAD.S.6120	Install aluminum framed double glazed windows	3	28-Sep-26	30-Sep-26	0%	100%
SPECIALTIES		4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6130	TOILET ACCESSROIES	2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6410	PANEL SIGNAGE	2	30-Sep-26	01-Oct-26	0%	100%
FURNISHINGS		1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6450	Workstation chair	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6460	Workstation table	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6470	Roller blind	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6480	Waste Receptacle	1	01-Oct-26	01-Oct-26	0%	100%
GUARD HOUSE 2		62	19-Jul-26	28-Sep-26	6.27%	100%
SITE WORKS		56	19-Jul-26	21-Sep-26	77%	100%
Guard Rooms & Gates		17	19-Jul-26	06-Aug-26	100%	100%
WAD.S.1460	Excavation for guard rooms	8	19-Jul-26	27-Jul-26	100%	100%
WAD.S.1610	Replacment Under Foundation	2	28-Jul-26	29-Jul-26	100%	100%
WAD.S.2290	Backfilling Under G.Beam	2	05-Aug-26	06-Aug-26	100%	100%
WAD.S.2300	Backfilling Under S.O.G	2	05-Aug-26	06-Aug-26	100%	100%
Guard Rooms & Gates (CONCRETE Works)		48	28-Jul-26	21-Sep-26	73.98%	100%
WAD.S.1620	50 mm thickness lean concrete under the foundation.	3	28-Jul-26	30-Jul-26	100%	100%

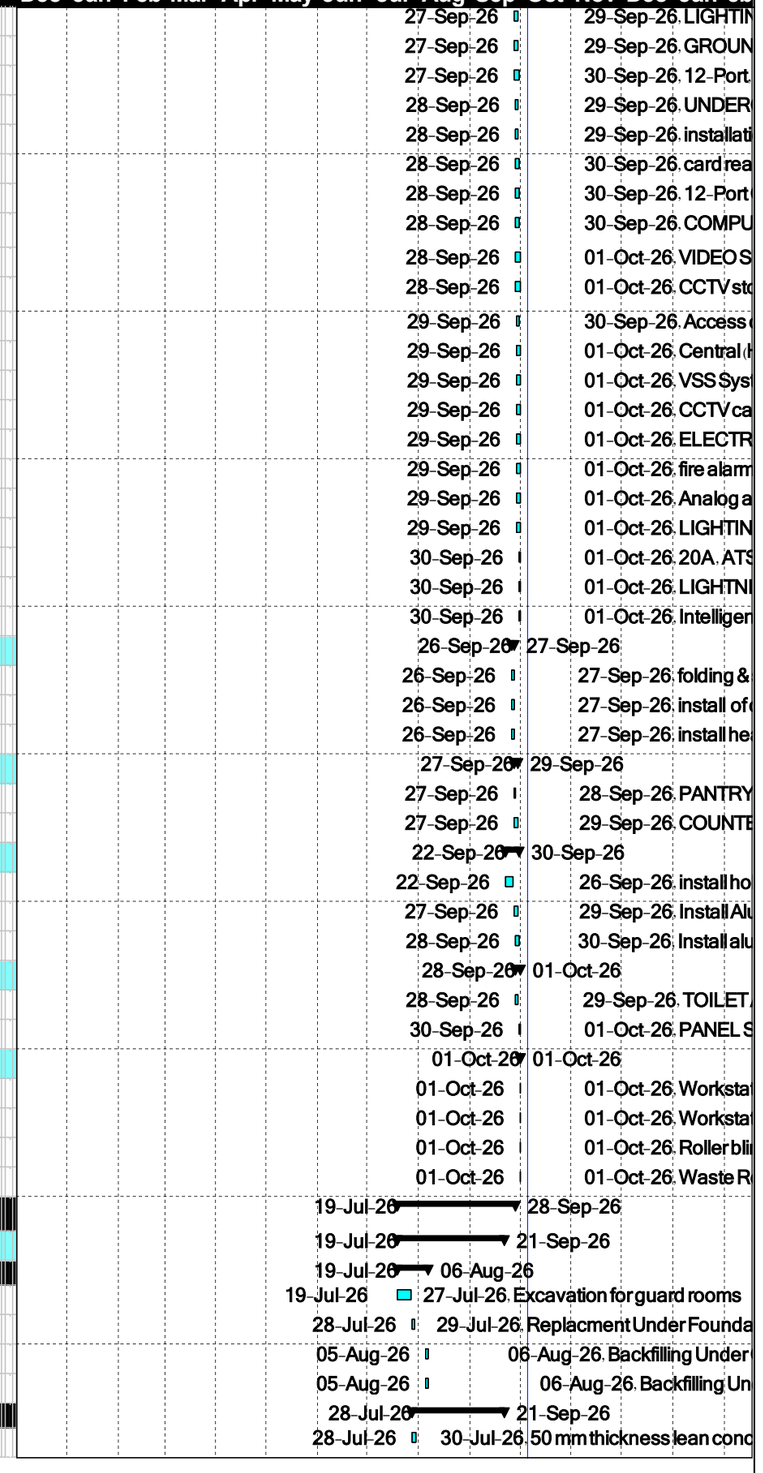

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.1990	Isolated Footings & Column Neck	5	30-Jul-26	04-Aug-26	100%	100%
WAD.S.2400	50 mm thickness lean concrete under grade beams.	3	08-Aug-26	10-Aug-26	100%	100%
WAD.S.2610	Grade beams	5	11-Aug-26	16-Aug-26	100%	100%
WAD.S.2660	Columns	4	17-Aug-26	20-Aug-26	100%	100%
WAD.S.2730	Raft and R.C. walls	5	19-Aug-26	24-Aug-26	100%	100%
WAD.S.2770	Roof Slab	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.2780	Beams	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.3440	Provide and cast concrete floor slab on grade	5	31-Aug-26	05-Sep-26	100%	100%
WAD.S.3450	Concrete Pad	3	31-Aug-26	02-Sep-26	100%	100%
WAD.S.3460	Tanks Raft	5	31-Aug-26	05-Sep-26	0%	100%
WAD.S.3980	Tanks Walls	5	06-Sep-26	10-Sep-26	0%	100%
WAD.S.4890	Tanks Slab	4	17-Sep-26	21-Sep-26	0%	100%
MASONRY UNIT		3	25-Aug-26	27-Aug-26	80%	100%
WAD.S.2930	install Concrete Masonry Unit (CMU) for walls	3	25-Aug-26	27-Aug-26	80%	100%
THERMAL & MOISTURE PROTECTION		4	06-Sep-26	09-Sep-26	31.41%	100%
THERMAL & MOISTURE PROTECTION - Foundation		4	06-Sep-26	09-Sep-26	31.41%	100%
WAD.S.3960	apply 2 coats of bitumen waterproofing paint on concrete surface in contact with	2	06-Sep-26	07-Sep-26	100%	100%
WAD.S.3970	install liquid applied waterproofing coating single-component pitch modified	2	06-Sep-26	07-Sep-26	0%	100%
WAD.S.4100	install geotextile sheet	2	08-Sep-26	09-Sep-26	0%	100%
ROOFING SYSTEM		11	09-Sep-26	21-Sep-26	2.92%	100%
WAD.S.4290	install liquid applied waterproofing coating single-component pitch modified	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4300	install 4mm thick APP modified bituminous membrane - single layer	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4310	install 75mm thick rigid insulation (extruded polystyrene)	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4320	cast in place foam concrete screed, 50mm thick minimum laid to fall and cross	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4330	install 300 micron polyethylene sheet	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4340	install 50mm thick loose gravel toppings	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4350	install high density polyisocynurate cover board	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4360	install UV resistant geotextile sheet	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4370	fixing 3mm thick extruded aluminum flashing 40mm with sealant and all other	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4380	install Terrazzo tiles	11	09-Sep-26	21-Sep-26	0%	100%
THERMAL & MOISTURE PROTECTION - Tanks		11	09-Sep-26	21-Sep-26	17.5%	100%
WAD.S.4390	lay epoxy 2 coating for inner surfaces for bottom of the roof	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.4740	install water stop for tanks according to the drawings and specification	5	12-Sep-26	16-Sep-26	35%	100%
FINISHES		38	08-Aug-26	20-Sep-26	1.82%	100%
WAD.S.2370	install ceramic floor tiles	3	08-Aug-26	10-Aug-26	0%	100%
WAD.S.2380	install granite flooring	2	08-Aug-26	09-Aug-26	0%	100%
WAD.S.2390	install ceramic wall tiles	3	08-Aug-26	10-Aug-26	0%	100%
WAD.S.2520	install two coats of acrylic paint on internal walls	2	09-Aug-26	10-Aug-26	0%	100%
WAD.S.2530	install two coats of acrylic paint (suitable for exterior use) on external	2	09-Aug-26	10-Aug-26	0%	100%
WAD.S.3100	install concrete plastering	4	29-Aug-26	01-Sep-26	20%	100%
WAD.S.2240	gypsum board suspended ceiling	4	03-Sep-26	07-Sep-26	0%	100%
WAD.S.4860	install granite saddles and thresholds	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.4870	install Riyadh stone cladding	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.4880	install 3mm steel CNC laser cut panels	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.4960	install aluminum cladding	2	19-Sep-26	20-Sep-26	0%	100%
MECHANICAL WORKS		52	30-Jul-26	28-Sep-26	5.36%	100%
MECHANICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	15%	100%
WAD.S.1830	WATER SUPPLY SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	15%	100%
WAD.S.1840	SEWER AND DRAINAGE SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	15%	100%
WAD.S.1850	IRRIGATION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	15%	100%

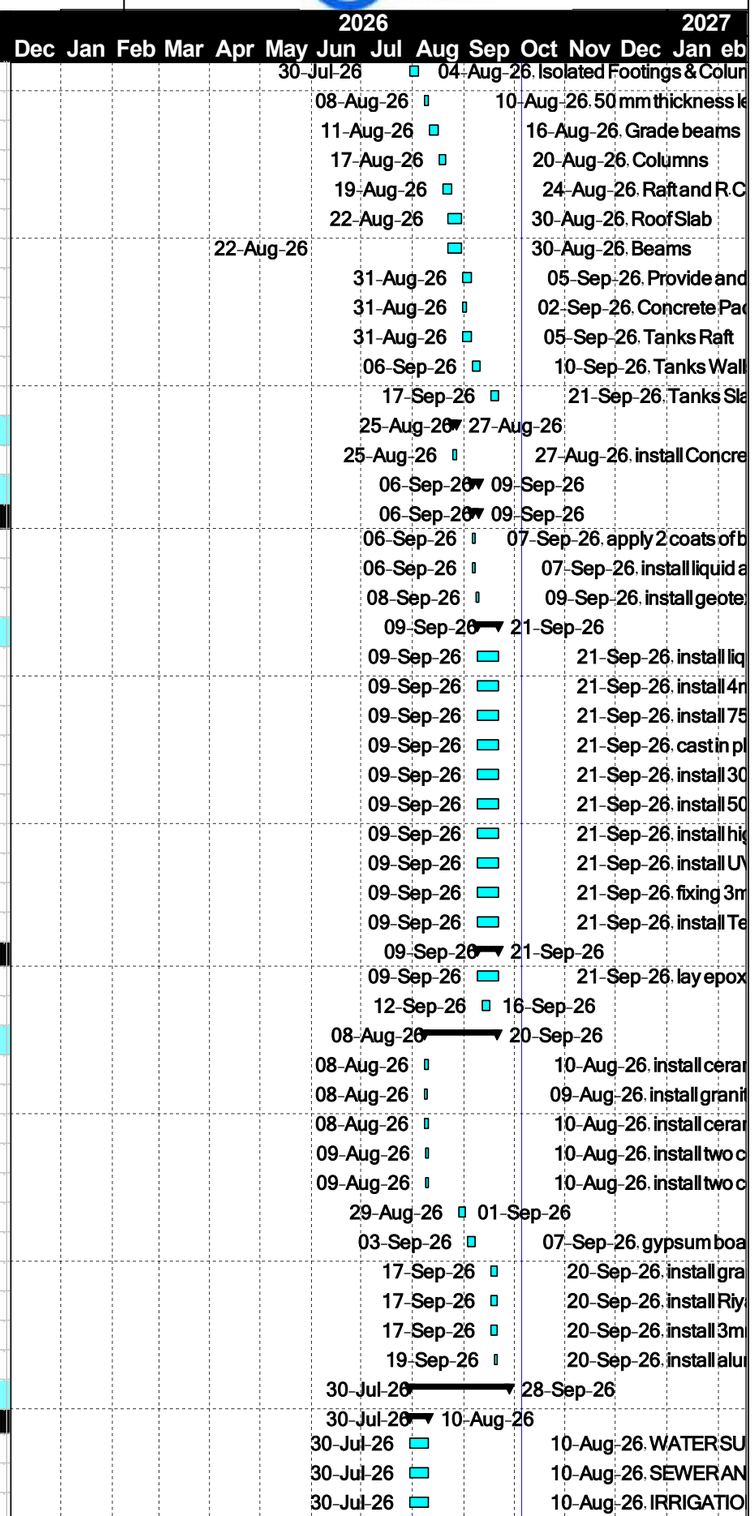

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.1880	HEATING, VENTILATION AND AIR CONDITIONING - 1st Fix	10	30-Jul-26	10-Aug-26	15%	100%
WAD.S.1890	Exhaust fans - 1st Fix	10	30-Jul-26	10-Aug-26	15%	100%
MECHANICAL WORKS - Final Fix		3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5560	installation of Fire extinguishers as per drawings, specifications	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5570	gully traps with heavy duty cover	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5580	chamber with heavy duty cover	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5590	INSTALL PLUMBING FIXTURES	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5600	HEATING, VENTILATION AND AIR CONDITIONING - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5610	Exhaust fans - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5620	Bulbblers and Spreyers of IRRIGATION SYSTEM	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5750	WATER SUPPLY SYSTEM - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5760	IRRIGATION SYSTEM - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
ELECTRICAL WORKS		52	30-Jul-26	28-Sep-26	0%	100%
ELECTRICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1860	LIGHTING AND POWER TYPE PANELBOARDS - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1870	UPS 3KVA (installed inside the rack) - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1900	power source with built-in photocell sensor for automatic electrical connection	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1910	UNDERGROUND DISTRIBUTION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1920	LIGHTING FIXTURES - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1930	installation of Wiring devices includes switches and Receptacle outlets	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1940	GROUNDING - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1950	card reader IN/OUT - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1960	CCTV cameras - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1970	Access control panel - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
WAD.S.1980	fire alarm system including wires, conduit and other materials - 1st Fix	10	30-Jul-26	10-Aug-26	0%	100%
ELECTRICAL WORKS - Final Fix		4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.5170	12-Port, SMF, Fiber Optic Patch Panels	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.5180	VIDEO SURVEILLANCE	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.5190	CCTV storage system, as specified	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.5630	power source with built-in photocell sensor for automatic electrical connection	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5640	LIGHTING FIXTURES - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5650	GROUNDING - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5660	card reader IN/OUT - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5670	12-Port CAT6A UTP fully loaded patch panel	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5680	COMPUTERS AND RELATED PERIPHERALS	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5690	Central (Headend) System Components	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5700	VSS System, as specified	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5710	CCTV cameras - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5720	ELECTRICAL GATE BARRIER	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5730	fire alarm system including wires, conduit and other materials - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5740	Analog addressable fire alarm control panel with battery	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5770	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6010	UNDERGROUND DISTRIBUTION SYSTEM - Final Fix	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.6020	installation of Wiring devices includes switches and Receptacle outlets	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.6030	Access control panel - Final Fix	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.6040	20A, ATS (Automatic transfer switch) for UPS	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.6050	LIGHTNING PROTECTION	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.6060	Intelligent Ionization / Photoelectric smoke and heat detector with base	2	27-Sep-26	28-Sep-26	0%	100%
METALS		2	08-Sep-26	09-Sep-26	0%	100%
WAD.S.2480	folding & sliding mounter combination ladder for building maintenance purpose	2	08-Sep-26	09-Sep-26	0%	100%

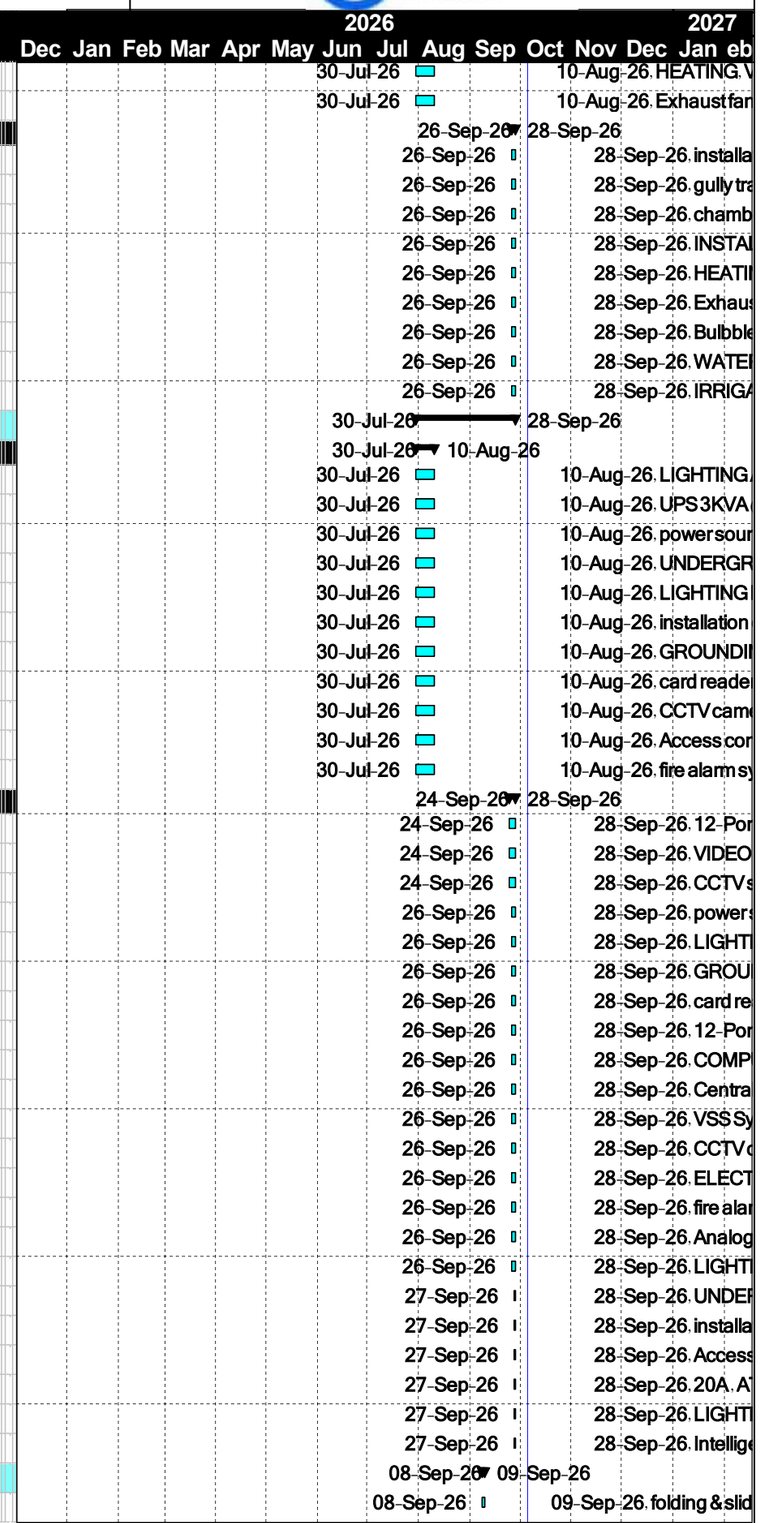

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.2490	install of overflow galvanized steel roof scupper with gray color with angular	2	08-Sep-26	09-Sep-26	0%	100%
WAD.S.2500	install heavy steel cover with frame including all necessary fixings	2	08-Sep-26	09-Sep-26	0%	100%
WOODS AND PLASTICS		3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.2350	COUNTER DESK	3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.2510	PANTRY CABINET	2	08-Sep-26	09-Sep-26	0%	100%
DOORS & WINDOWS		5	07-Sep-26	12-Sep-26	0%	100%
WAD.S.2360	Install Aluminum Door	3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.2200	install hollow metal door	4	08-Sep-26	12-Sep-26	0%	100%
WAD.S.2210	Install aluminum framed double glazed windows	3	08-Sep-26	10-Sep-26	0%	100%
SPECIALTIES		3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.5550	TOILET ACCESSROIES	2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.6000	PANEL SIGNAGE	2	27-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6210	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6220	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6230	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6240	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
GUARD HOUSE 3		62	19-Jul-26	28-Sep-26	29.45%	100%
SITE WORKS		56	19-Jul-26	21-Sep-26	77%	100%
Guard Rooms & Gates		17	19-Jul-26	06-Aug-26	100%	100%
WAD.S.7380	Excavation for guard rooms	8	19-Jul-26	27-Jul-26	100%	100%
WAD.S.7390	Replacment Under Foundation	2	28-Jul-26	29-Jul-26	100%	100%
WAD.S.7400	Backfilling Under G.Beam	2	05-Aug-26	06-Aug-26	100%	100%
WAD.S.7410	Backfilling Under S.O.G	2	05-Aug-26	06-Aug-26	100%	100%
Guard Rooms & Gates (CONCRETE Works)		48	28-Jul-26	21-Sep-26	73.98%	100%
WAD.S.7430	50 mm thickness lean concrete under the foundation.	3	28-Jul-26	30-Jul-26	100%	100%
WAD.S.7450	Isolated Footings & Column Neck	5	30-Jul-26	04-Aug-26	100%	100%
WAD.S.7420	50 mm thickness lean concrete under grade beams.	3	08-Aug-26	10-Aug-26	100%	100%
WAD.S.7460	Grade beams	5	11-Aug-26	16-Aug-26	100%	100%
WAD.S.7470	Columns	4	17-Aug-26	20-Aug-26	100%	100%
WAD.S.7510	Raft and R.C. walls	5	19-Aug-26	24-Aug-26	100%	100%
WAD.S.7490	Roof Slab	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.7500	Beams	8	22-Aug-26	30-Aug-26	100%	100%
WAD.S.7440	Provide and cast concrete floor slab on grade	5	31-Aug-26	05-Sep-26	100%	100%
WAD.S.7480	Concrete Pad	3	31-Aug-26	02-Sep-26	100%	100%
WAD.S.7520	Tanks Raft	5	31-Aug-26	05-Sep-26	0%	100%
WAD.S.7530	Tanks Walls	5	06-Sep-26	10-Sep-26	0%	100%
WAD.S.7540	Tanks Slab	4	17-Sep-26	21-Sep-26	0%	100%
MASONRY UNIT		3	25-Aug-26	27-Aug-26	100%	100%
WAD.S.6500	install Concrete Masonry Unit (CMU) for walls	3	25-Aug-26	27-Aug-26	100%	100%
THERMAL & MOISTURE PROTECTION		4	06-Sep-26	09-Sep-26	31.41%	100%
THERMAL & MOISTURE PROTECTION - Foundation		4	06-Sep-26	09-Sep-26	31.41%	100%
WAD.S.6560	apply 2 coats of bitumen waterproofing paint on concrete surface in contact with	2	06-Sep-26	07-Sep-26	100%	100%
WAD.S.6580	install liquid applied waterproofing coating single-component pitch modified	2	06-Sep-26	07-Sep-26	0%	100%
WAD.S.6590	install geotextile sheet	2	08-Sep-26	09-Sep-26	0%	100%
ROOFING SYSTEM		11	09-Sep-26	21-Sep-26	5.83%	100%
WAD.S.6570	install liquid applied waterproofing coating single-component pitch modified	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6610	install 4mm thick APP modified bituminous membrane - single layer	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6620	install 75mm thick rigid insulation (extruded polystyrene)	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6630	cast in place foam concrete screed, 50mm thick minimum laid to fall and cross	11	09-Sep-26	21-Sep-26	0%	100%

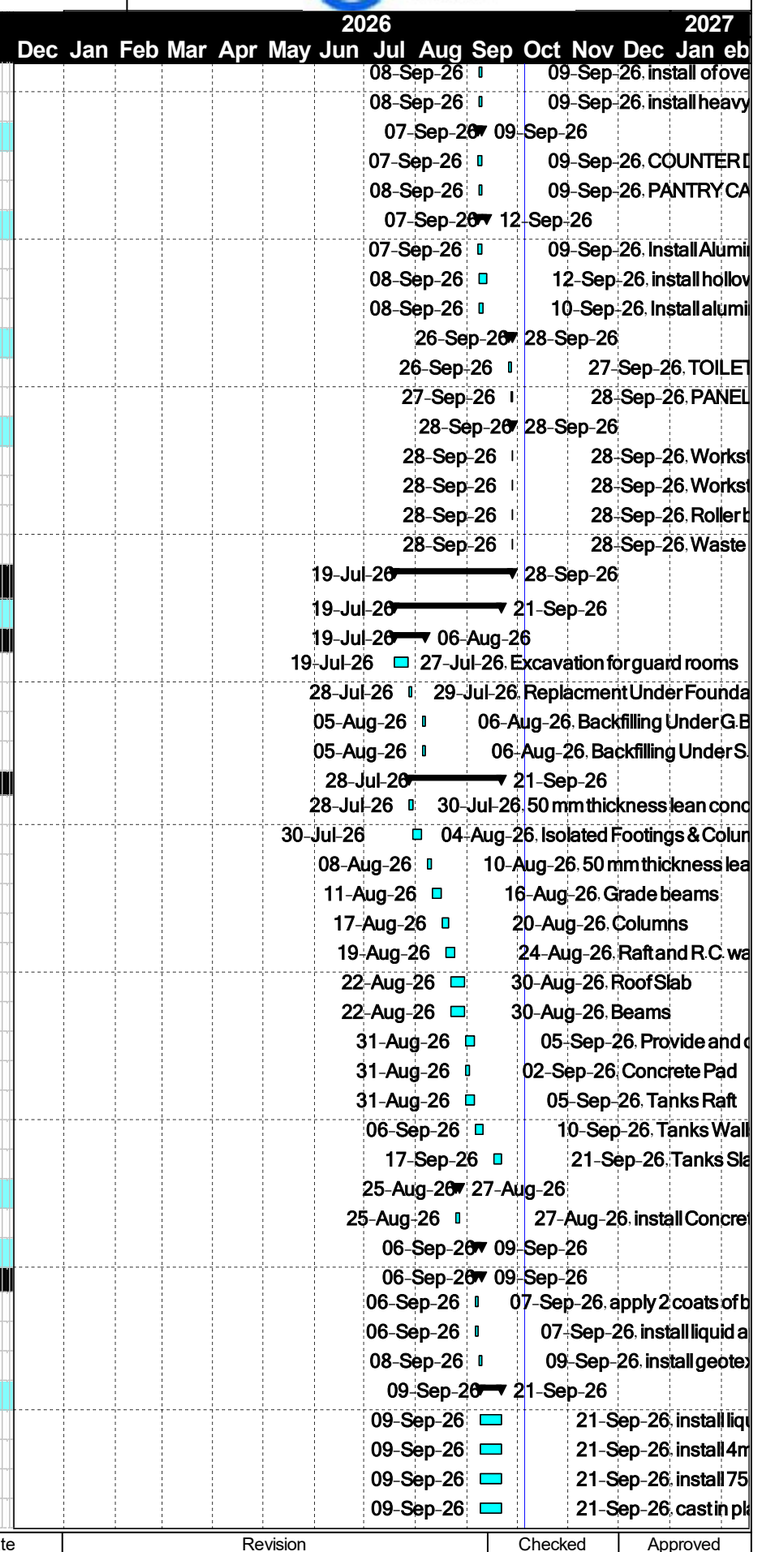

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.6640	install 300 micron polyethylene sheet	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6650	install 50mm thick loose gravel toppings	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6660	install high density polyisocynurate cover board	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6670	install UV resistant geotextile sheet	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6680	fixing 3mm thick extruded aluminum flashing 40mm with sealant and all other	11	09-Sep-26	21-Sep-26	0%	100%
WAD.S.6690	install Terrazzo tiles	11	09-Sep-26	21-Sep-26	0%	100%
THERMAL & MOISTURE PROTECTION - Tanks		11	09-Sep-26	21-Sep-26	35%	100%
WAD.S.7370	lay epoxy 2 coating for inner surfaces for bottom of the roof	11	09-Sep-26	21-Sep-26	35%	100%
WAD.S.6600	install water stop for tanks according to the drawings and specification	5	12-Sep-26	16-Sep-26	35%	100%
FINISHES		38	08-Aug-26	20-Sep-26	8.18%	100%
WAD.S.6730	install ceramic floor tiles	3	08-Aug-26	10-Aug-26	0%	100%
WAD.S.6740	install granite flooring	2	08-Aug-26	09-Aug-26	0%	100%
WAD.S.6770	install ceramic wall tiles	3	08-Aug-26	10-Aug-26	0%	100%
WAD.S.6780	install two coats of acrylic paint on internal walls	2	09-Aug-26	10-Aug-26	0%	100%
WAD.S.6790	install two coats of acrylic paint (suitable for exterior use) on external	2	09-Aug-26	10-Aug-26	0%	100%
WAD.S.6760	install concrete plastering	4	29-Aug-26	01-Sep-26	90%	100%
WAD.S.6830	gypsum board suspended ceiling	4	03-Sep-26	07-Sep-26	0%	100%
WAD.S.6750	install granite saddles and thresholds	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.6800	install Riyadh stone cladding	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.6820	install 3mm steel CNC laser cut panels	3	17-Sep-26	20-Sep-26	0%	100%
WAD.S.6810	install aluminum cladding	2	19-Sep-26	20-Sep-26	0%	100%
MECHANICAL WORKS		52	30-Jul-26	28-Sep-26	35.71%	100%
MECHANICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.6910	WATER SUPPLY SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.6920	SEWER AND DRAINAGE SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.6980	IRRIGATION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7260	HEATING, VENTILATION AND AIR CONDITIONING - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7270	Exhaust fans - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
MECHANICAL WORKS - Final Fix		3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6900	installation of Fire extinguishers as per drawings, specifications	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6930	gully traps with heavy duty cover	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6940	chamber with heavy duty cover	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6950	INSTALL PLUMBING FIXTURES	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6960	HEATING, VENTILATION AND AIR CONDITIONING - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6970	Exhaust fans - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6990	Bulbblers and Spreyers of IRRIGATION SYSTEM	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7230	WATER SUPPLY SYSTEM - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7240	IRRIGATION SYSTEM - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
ELECTRICAL WORKS		52	30-Jul-26	28-Sep-26	33.33%	100%
ELECTRICAL WORKS - 1st Fix		10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7000	LIGHTING AND POWER TYPE PANELBOARDS - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7010	UPS 3KVA (installed inside the rack) - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7280	power source with built-in photocell sensor for automatic electrical connection	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7290	UNDERGROUND DISTRIBUTION SYSTEM - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7300	LIGHTING FIXTURES - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7310	installation of Wiring devices includes switches and Receptacle outlets	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7320	GROUNDING - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7330	card reader IN/OUT - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7340	CCTV cameras - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
WAD.S.7350	Access control panel - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%

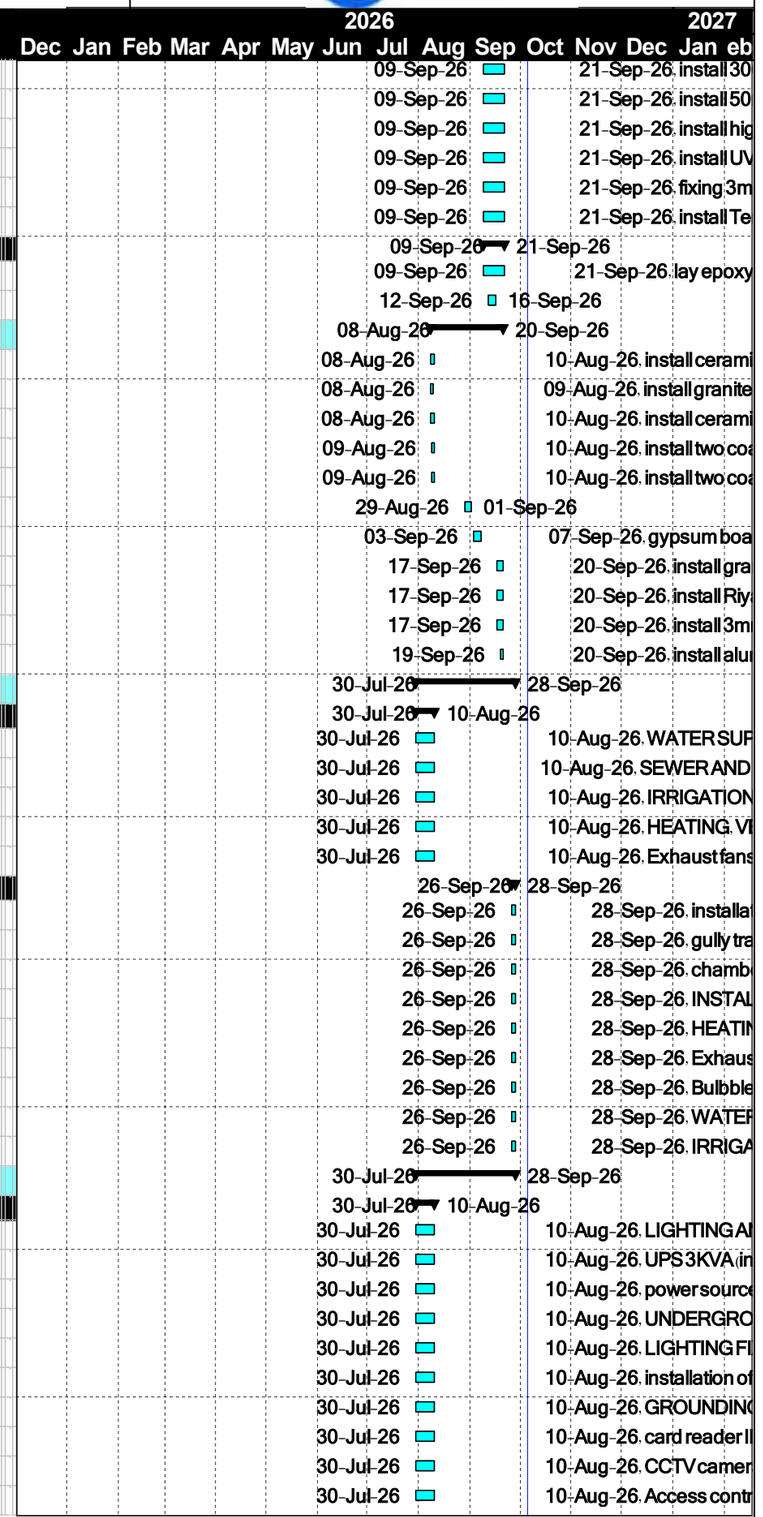

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.7360	fire alarm system including wires, conduit and other materials - 1st Fix	10	30-Jul-26	10-Aug-26	100%	100%
ELECTRICAL WORKS - Final Fix		4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.7100	12-Port, SMF, Fiber Optic Patch Panels	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.7120	VIDEO SURVEILLANCE	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.7150	CCTV storage system, as specified	4	24-Sep-26	28-Sep-26	0%	100%
WAD.S.7020	power source with built-in photocell sensor for automatic electrical connection	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7040	LIGHTING FIXTURES - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7060	GROUNDING - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7070	card reader IN/OUT - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7090	12-Port CAT6A UTP fully loaded patch panel	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7110	COMPUTERS AND RELATED PERIPHERALS	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7130	Central (Headend) System Components	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7140	VSS System, as specified	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7160	CCTV cameras - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7180	ELECTRICAL GATE BARRIER	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7200	fire alarm system including wires, conduit and other materials - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7210	Analog addressable fire alarm control panel with battery	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7250	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.7030	UNDERGROUND DISTRIBUTION SYSTEM - Final Fix	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.7050	installation of Wiring devices includes switches and Receptacle outlets	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.7080	Access control panel - Final Fix	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.7170	20A, ATS (Automatic transfer switch) for UPS	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.7190	LIGHTNING PROTECTION	2	27-Sep-26	28-Sep-26	0%	100%
WAD.S.7220	Intelligent Ionization / Photoelectric smoke and heat detector with base	2	27-Sep-26	28-Sep-26	0%	100%
METALS		2	08-Sep-26	09-Sep-26	0%	100%
WAD.S.6510	folding & sliding mounter combination ladder for building maintenance purpose	2	08-Sep-26	09-Sep-26	0%	100%
WAD.S.6520	install of overflow galvanized steel roof scupper with gray color with angular	2	08-Sep-26	09-Sep-26	0%	100%
WAD.S.6530	install heavy steel cover with frame including all necessary fixings	2	08-Sep-26	09-Sep-26	0%	100%
WOODS AND PLASTICS		3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.6550	COUNTER DESK	3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.6540	PANTRY CABINET	2	08-Sep-26	09-Sep-26	0%	100%
DOORS & WINDOWS		5	07-Sep-26	12-Sep-26	0%	100%
WAD.S.6700	Install Aluminum Door	3	07-Sep-26	09-Sep-26	0%	100%
WAD.S.6710	install hollow metal door	4	08-Sep-26	12-Sep-26	0%	100%
WAD.S.6720	Install aluminum framed double glazed windows	3	08-Sep-26	10-Sep-26	0%	100%
SPECIALTIES		3	26-Sep-26	28-Sep-26	0%	100%
WAD.S.6840	TOILET ACCESSROIES	2	26-Sep-26	27-Sep-26	0%	100%
WAD.S.6850	PANEL SIGNAGE	2	27-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6860	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6870	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6880	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6890	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
EXT. WORKS		41	11-Aug-26	27-Sep-26	0%	100%
EXTERNAL WORKS		41	11-Aug-26	27-Sep-26	0%	100%
WAD.S.1100	Excavation Works	15	11-Aug-26	27-Aug-26	0%	100%
WAD.S.1290	40 mm Pipes	12	29-Aug-26	10-Sep-26	0%	100%
WAD.S.3270	GRP Pipes laid in trenches	12	31-Aug-26	13-Sep-26	0%	100%
WAD.S.3880	100 mm Pipe in trench not exceeding 2.00 m depth to invert	7	06-Sep-26	13-Sep-26	0%	100%

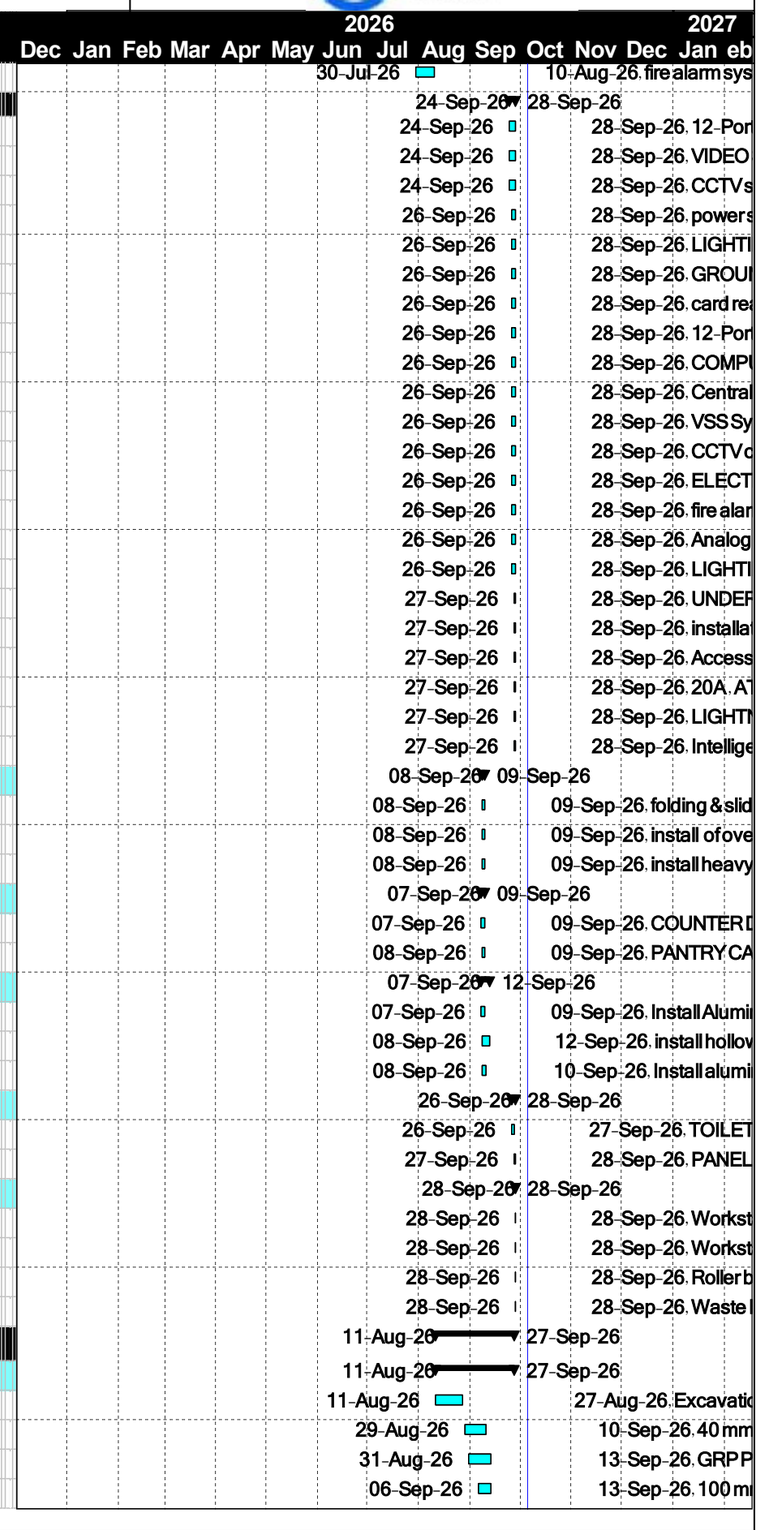

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.4020	install 100 mm GRP pipe service connections between building sewage	8	07-Sep-26	15-Sep-26	0%	100%
WAD.S.4030	Manhole depth not exceeding 4.0m	8	07-Sep-26	15-Sep-26	0%	100%
WAD.S.4800	Backfilling Works	5	14-Sep-26	19-Sep-26	0%	100%
WAD.S.4980	SIDEWALKS AND CURBS	7	20-Sep-26	27-Sep-26	0%	100%
WAD.S.4990	ROAD WORKS	7	20-Sep-26	27-Sep-26	0%	100%
WAD.S.5000	install flag pole 6 M height	5	20-Sep-26	24-Sep-26	0%	100%
Testing & Commissioning		9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5440	Testing & Commissioning - Electrical Systems	9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5490	Testing & Commissioning - Mechanical Systems	9	26-Sep-26	05-Oct-26	0%	100%
Engineering		9	26-Sep-26	05-Oct-26	0%	100%
As-Built Drawings		8	26-Sep-26	04-Oct-26	0%	100%
WAD.S.5430	Prepare & Submit	4	26-Sep-26	29-Sep-26	0%	100%
WAD.S.6260	Review & Approve	6	28-Sep-26	04-Oct-26	0%	100%
Operational Spares		9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5450	Prepare & Submit	4	26-Sep-26	29-Sep-26	0%	100%
WAD.S.6350	Inspection	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6370	Acceptance	5	30-Sep-26	05-Oct-26	0%	100%
Warranties and Guarantees		9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5460	Prepare & Submit	4	26-Sep-26	29-Sep-26	0%	100%
WAD.S.6360	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
Training and Manuals		9	26-Sep-26	05-Oct-26	0%	100%
Training		9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5470	Prepare & Submit	4	26-Sep-26	29-Sep-26	0%	100%
WAD.S.6380	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6400	Fabrication & Delivery	5	30-Sep-26	05-Oct-26	0%	100%
Manuals		9	26-Sep-26	05-Oct-26	0%	100%
WAD.S.5480	Prepare & Submit	4	26-Sep-26	29-Sep-26	0%	100%
WAD.S.6390	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
Demobilization		8	27-Sep-26	05-Oct-26	0%	100%
WAD.S.5850	Demobilize	8	27-Sep-26	05-Oct-26	0%	100%
Snaglist Rectification		8	27-Sep-26	05-Oct-26	0%	100%
WAD.S.5860	Snaglist Rectification	8	27-Sep-26	05-Oct-26	0%	100%
WAD.S.5870	Initial Handing Over	8	27-Sep-26	05-Oct-26	0%	100%

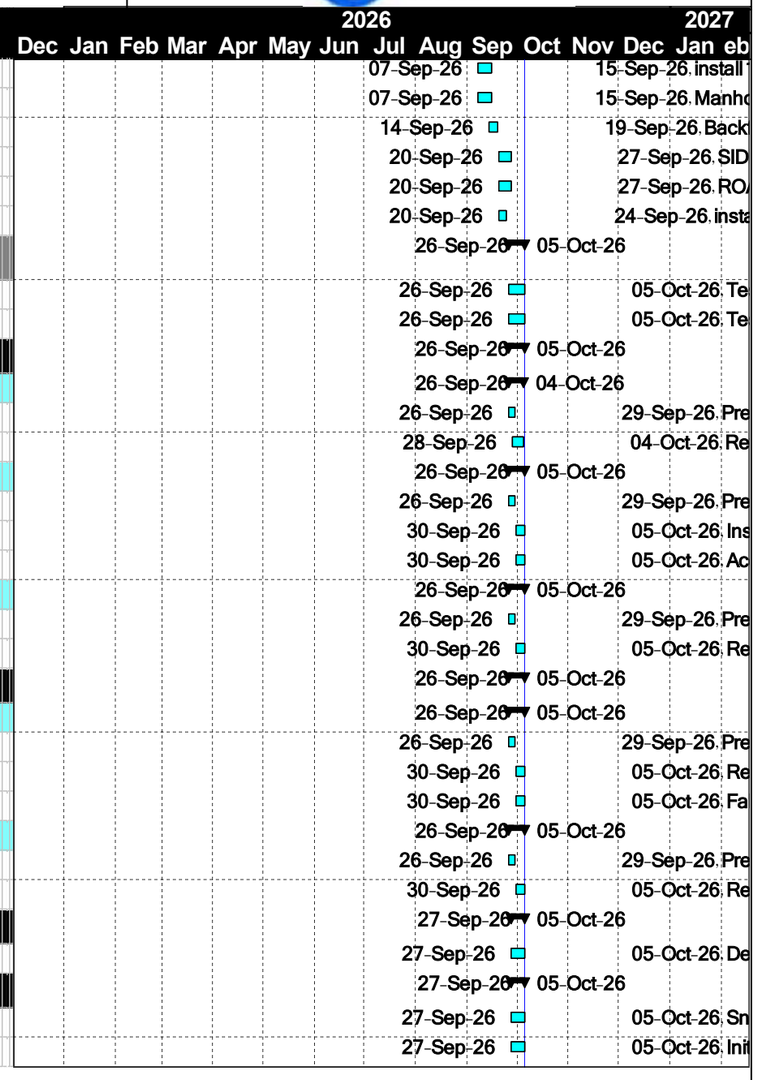

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		
