
WAS1 05 006

Improvement of Waad Al Shamal Industrial City Fence Gates

Baseline Time Schedule

CONSOLIDATED CONSULTANTS GROUP


Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
Improvement of Waad Al Shamal Industrial City Fence & Gates -		7	28-Sep-26	05-Oct-26	1.6%	100%
Key Milestones		6	28-Sep-26	05-Oct-26	0%	0%
General Milestones		0	05-Oct-26	05-Oct-26	0%	0%
WAD.S.6490	Project Finish	0		05-Oct-26	0%	100%
Contractual Milestones		6	28-Sep-26	05-Oct-26	0%	0%
WAD.S.6250	Completion of Procurment Works	0		28-Sep-26	0%	100%
WAD.S.7560	Testing & Commissioning	0		05-Oct-26	0%	100%
Construction		4	28-Sep-26	01-Oct-26	10.05%	100%
GUARD HOUSE 1		4	28-Sep-26	01-Oct-26	11.27%	100%
ELECTRICAL WORKS		4	28-Sep-26	01-Oct-26	12.31%	100%
ELECTRICAL WORKS - Final Fix		4	28-Sep-26	01-Oct-26	12.31%	100%
WAD.S.6150	installation of Wiring devices includes switches and Receptacle outlets	2	28-Sep-26	29-Sep-26	80%	100%
WAD.S.6160	card reader IN/OUT - Final Fix	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6170	12-Port CAT6A UTP fully loaded patch panel	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6180	COMPUTERS AND RELATED PERIPHERALS	3	28-Sep-26	30-Sep-26	0%	100%
WAD.S.6190	VIDEO SURVEILLANCE	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6200	CCTV storage system, as specified	4	28-Sep-26	01-Oct-26	0%	100%
WAD.S.6270	Access control panel - Final Fix	2	29-Sep-26	30-Sep-26	0%	100%
WAD.S.6280	Central (Headend) System Components	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6290	VSS System, as specified	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6300	CCTV cameras - Final Fix	3	29-Sep-26	01-Oct-26	0%	100%
WAD.S.6310	ELECTRICAL GATE BARRIER	3	29-Sep-26	01-Oct-26	30%	100%
WAD.S.6340	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	3	29-Sep-26	01-Oct-26	50%	100%
WAD.S.6420	20A, ATS (Automatic transfer switch) for UPS	2	30-Sep-26	01-Oct-26	0%	100%
SPECIALTIES		2	28-Sep-26	29-Sep-26	0%	100%
WAD.S.6130	TOILET ACCESSROIES	2	28-Sep-26	29-Sep-26	0%	100%
FURNISHINGS		1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6450	Workstation chair	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6460	Workstation table	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6470	Roller blind	1	01-Oct-26	01-Oct-26	0%	100%
WAD.S.6480	Waste Receptacle	1	01-Oct-26	01-Oct-26	0%	100%
GUARD HOUSE 2		1	28-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6210	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6220	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6230	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6240	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
GUARD HOUSE 3		1	28-Sep-26	28-Sep-26	0%	100%
FURNISHINGS		1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6860	Workstation chair	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6870	Workstation table	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6880	Roller blind	1	28-Sep-26	28-Sep-26	0%	100%
WAD.S.6890	Waste Receptacle	1	28-Sep-26	28-Sep-26	0%	100%
Testing & Commissioning		7	28-Sep-26	05-Oct-26	0%	100%
Engineering		7	28-Sep-26	05-Oct-26	0%	100%
As-Built Drawings		6	28-Sep-26	04-Oct-26	0%	100%

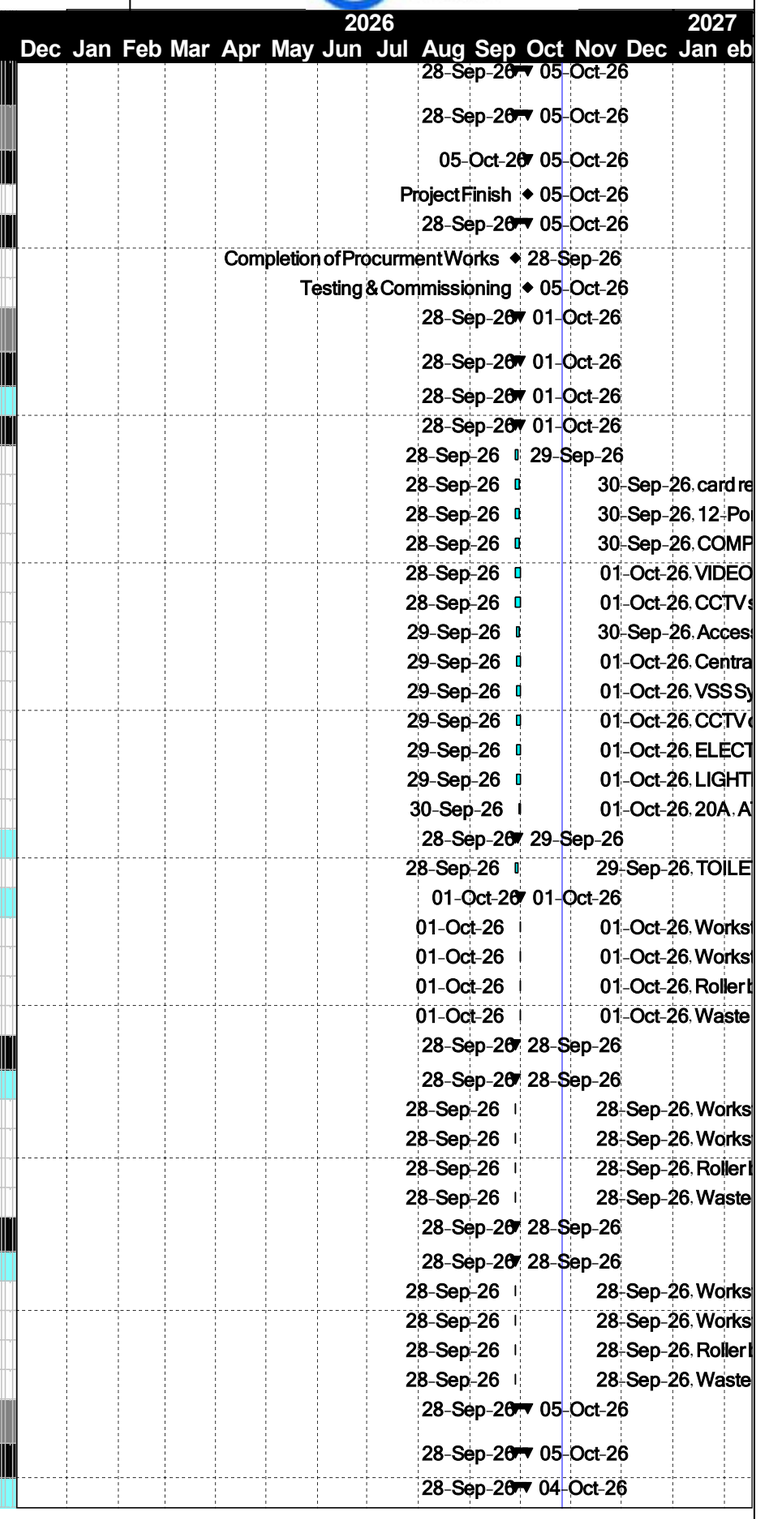

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
WAD.S.6260	Review & Approve	6	28-Sep-26	04-Oct-26	0%	100%
Operational Spares		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6350	Inspection	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6370	Acceptance	5	30-Sep-26	05-Oct-26	0%	100%
Warranties and Guarantees		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6360	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
Training and Manuals		5	30-Sep-26	05-Oct-26	0%	100%
Training		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6380	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6400	Fabrication & Delivery	5	30-Sep-26	05-Oct-26	0%	100%
Manuals		5	30-Sep-26	05-Oct-26	0%	100%
WAD.S.6390	Review & Approve	5	30-Sep-26	05-Oct-26	0%	100%

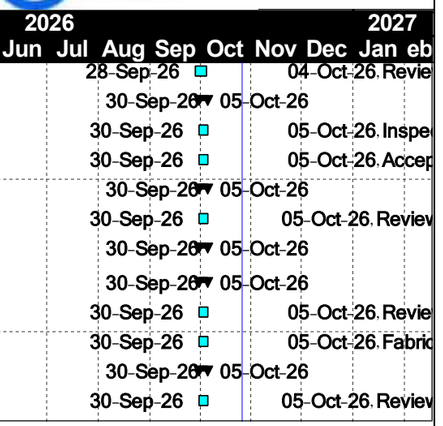

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Jul-26	Rev001-WAS-05-006		
