Construction of a SAR Train Passenger Drop-Off Station in Sudair

محطة ركاب لسار في سدير

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Zyad Al Shabat	07-Apr-2026	06-Aug-2027

Scope: a passenger station for the SAR railway at Sudair Industrial City (platform, canopy, finishes and station electrical, CCTV and voice evacuation systems) with its access roads RD-01 and RD-02 and their storm water, sewer, potable water, street lighting, telecom and MV/LV networks.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The 02-Nov-2026 report puts the project at 40.4% against 40.2% planned (SPI 1.01), up from 27.3% a week earlier. That 13.1% jump in one week is not supported by the rest of the report and should be verified before it is accepted.

PHYSICAL % COMPLETE
40.4% / 40.2% plan
? SPI 1.01, to be verified +0.2%

PROGRESS THIS WEEK
+13.1% / +0.2% plan
? Not supported by quantities

CONTRACT TIME ELAPSED
43.0% · day 209 of 486
● P6 finish 06-Aug-2027, no float

INVOICED TO DATE (GROSS)
22.2% · 7.34M SAR
3 invoices, last period ends 28-Oct-2026

The 13.1% jump in one week needs to be verified.

Most of it comes from Road Works 1, whose earned man-hours rose from 79,097 to 161,207. Road-01 now shows 122,462 earned man-hours against a budget of 106,900 (114.6%), yet the Major Quantities sheet is unchanged from last week. The man-hour budget also rose from 638,468 to 659,762, and the Physical-Chart Data sheet restates the October actual from 174,266 to 246,525 man-hours. Meanwhile procurement fell from 17,130 to 15,033 earned man-hours (16.3% against 80.1% planned) and the station package is still at 0%.

Site photos this week

Two photos from the Weekly Photos sheet of the 02-Nov-2026 weekly report; the other four are less than 600 px wide. Base course and subgrade works on Road 1 continue. Select a photo to view it larger, then use the arrows to move between photos.



Base course laying, Road 1

Paver laying the base course layer on Road 1.




Subgrade compaction, Road 1

Roller compacting the subgrade layer on Road 1.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

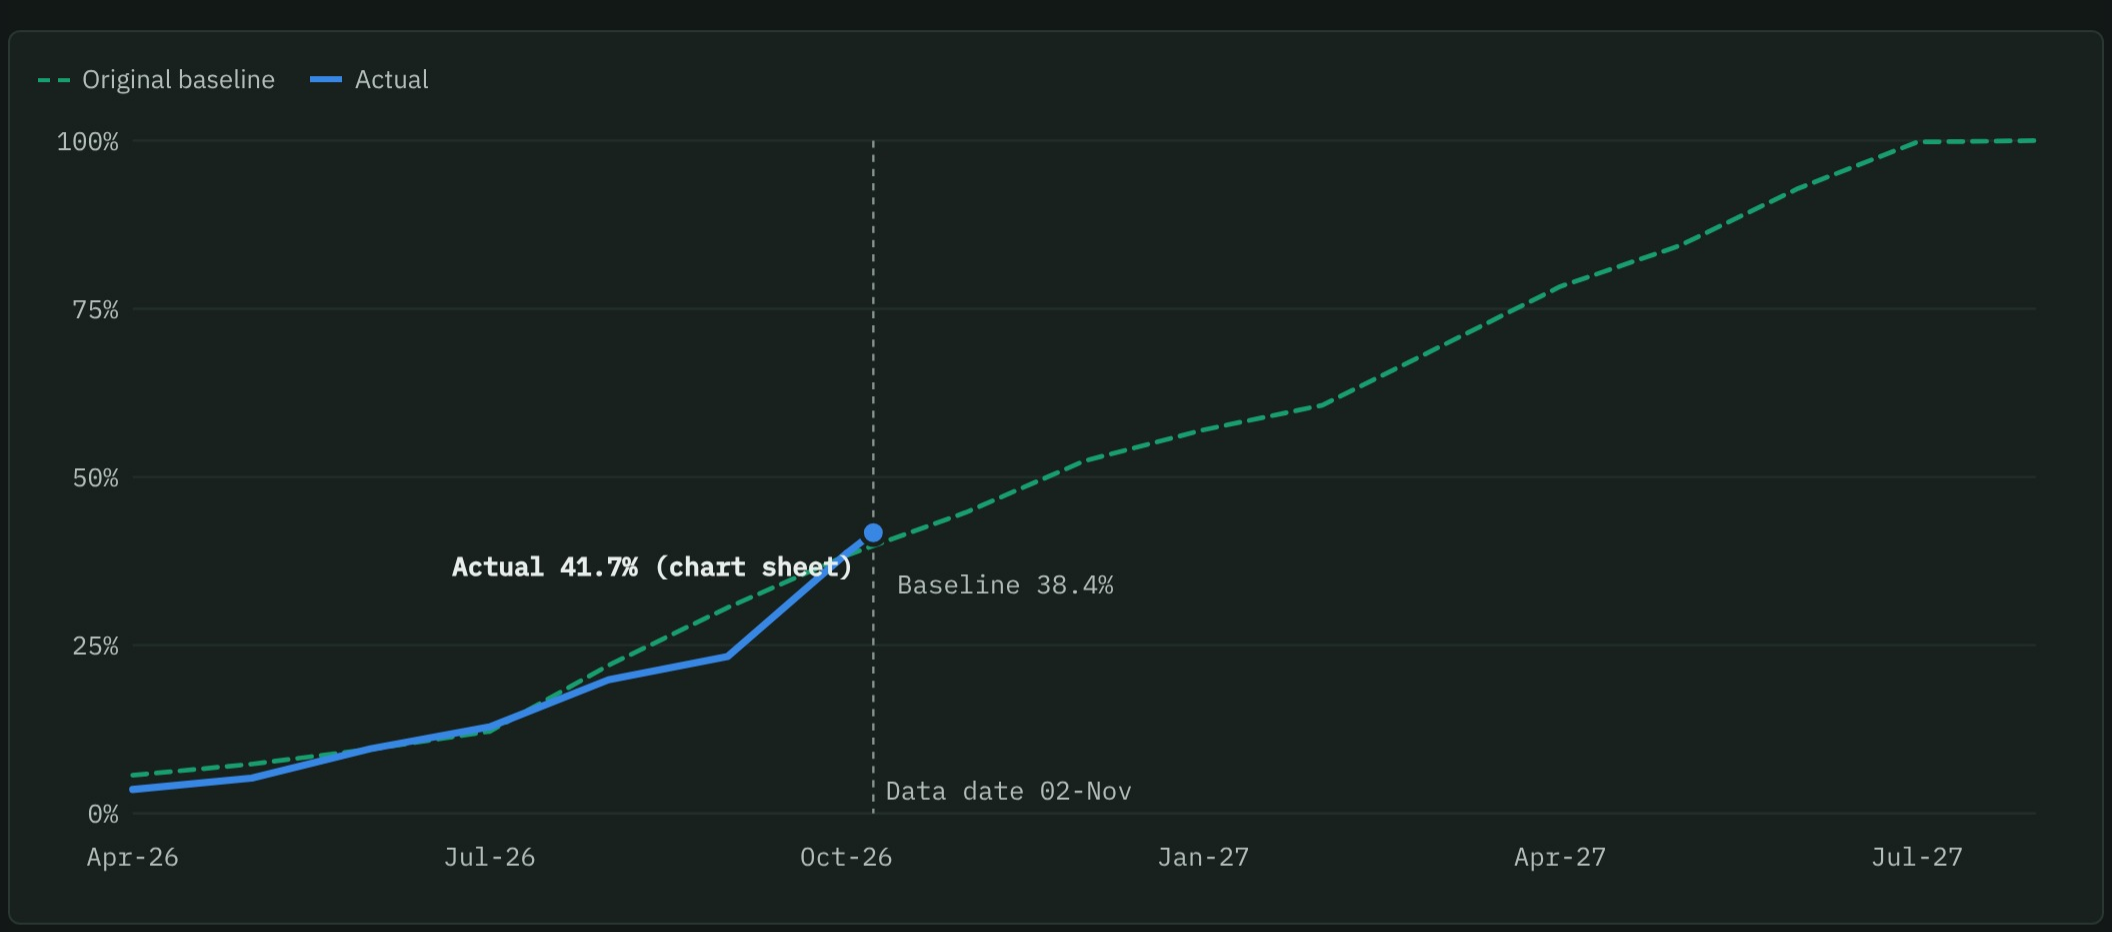

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
19-Oct-2026	38.1	26.1	−12.0	–	0.69
26-Oct-2026	40.0	27.3	−12.7	+1.2	0.68
02-Nov-2026	**40.2***	**40.4***	**+0.2**	**+13.1**	**1.01**

19-Oct and 26-Oct come from the 26-Oct-2026 report, 02-Nov from this week's. * The 02-Nov report uses a budget of 659,762 man-hours instead of 638,468. The S-curve keeps the chart sheet's 638,468 budget, so its 02-Nov point is 41.7%, and its October point is the restated 38.6%.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	5%	100.0%	95.0%	−5.0	0.95	▼ Behind
Procurement	14%	80.1%	16.3%	−63.8	0.20	▼ Far behind
Construction	75%	27.9%	40.5%	+12.6	1.45	? To be verified
· Package 1: roads and utilities	53.9%	35.3%	56.3%	+21.0	1.60	? To be verified
· Package 3: station (platform, canopy, systems)	21.1%	9.1%	0.0%	−9.1	0.00	▼ Not started
Testing & commissioning	2%	0.0%	0.0%	0.0	–	● Not yet due
Close-out	1%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**40.2%**	**40.4%**	**+0.2**	**1.01**	? To be verified

The P6 update (data date 01-Nov-2026) has 855 activities: 258 completed, 49 in progress and 548 not started. Its scheduled finish is 06-Aug-2027, the contract date, with zero float.

Scope of work: quantities

Major BOQ quantities from the Major Quantities sheet of the 02-Nov-2026 weekly report: total, finished to date and remaining. "This week" is the change since the 26-Oct-2026 report; no quantity changed.

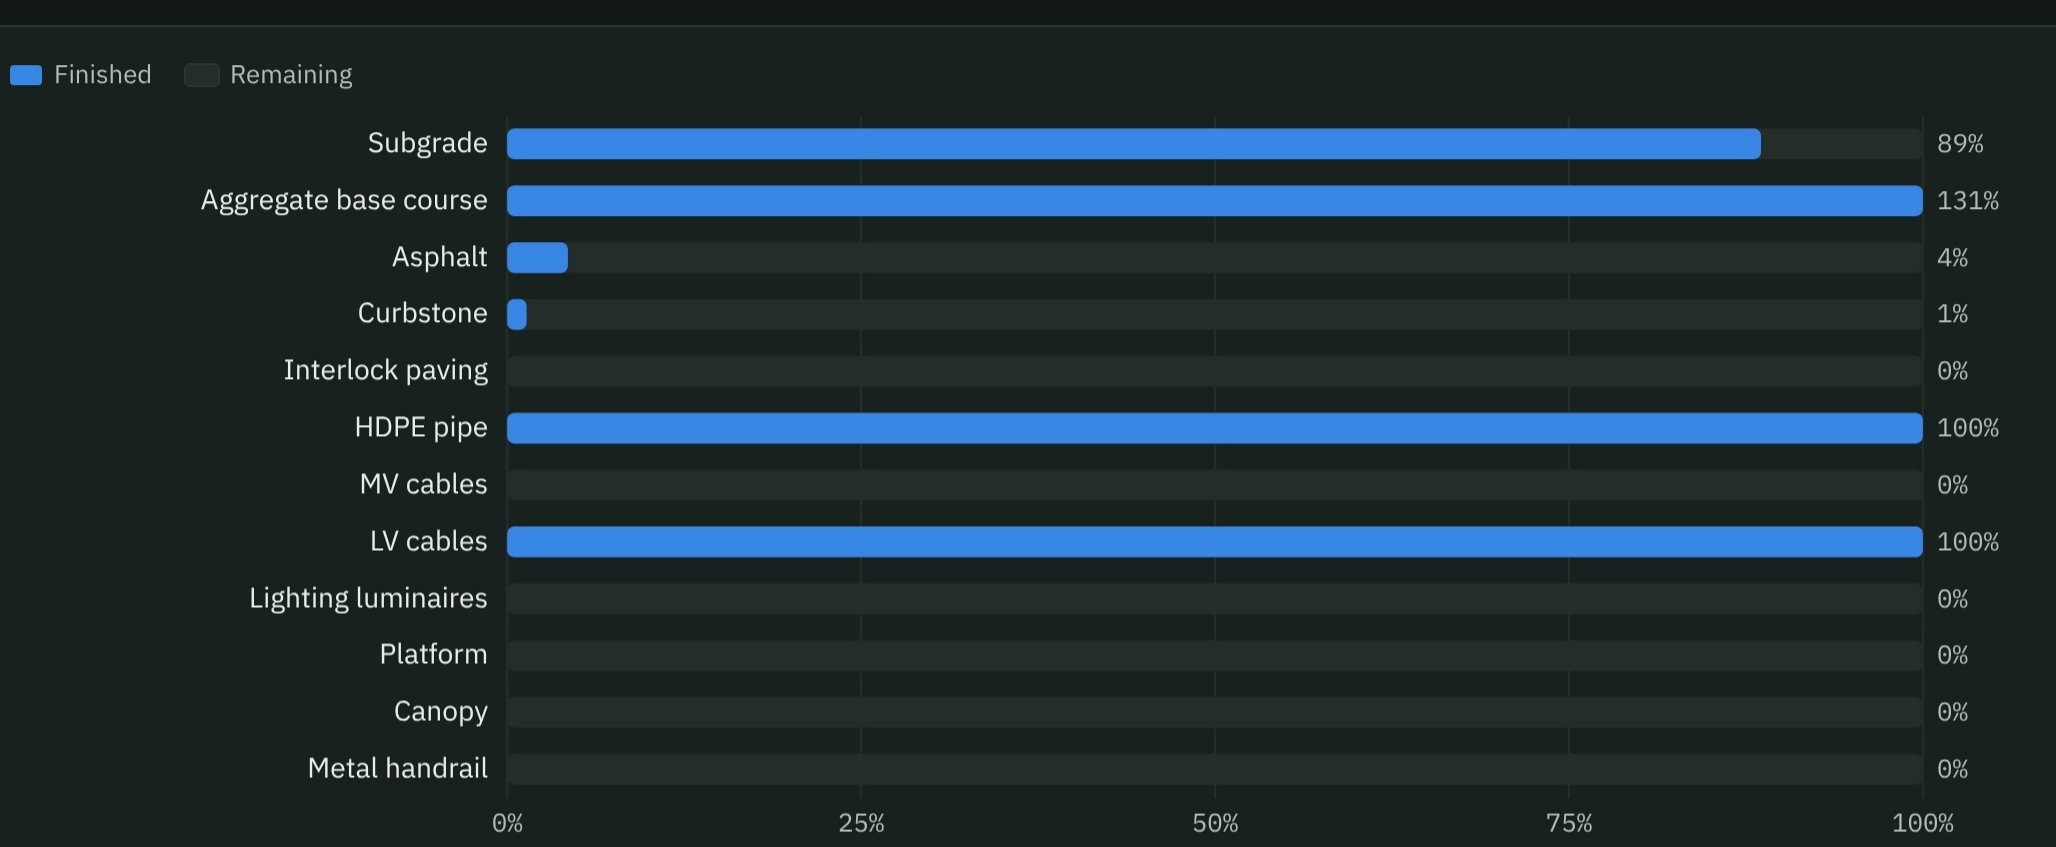

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Subgrade	B1.32 11 13.01	m³	20,530	18,182	0	2,348	88.6%
Aggregate base course	B1.32 11 23.01	m³	16,376	21,459	0	-5,083.2	131.0%
Asphalt	B1.32 12 16.01	m³	13,360	573	0	12,787	4.3%
Curbstone	B1.32 16 13.23.01	m²	20,555	282	0	20,273	1.4%
Interlock paving	B1.32 14 13.13.01	m²	27,900	0	0	27,900	0.0%
HDPE pipe	B4.33 31 23.01	LM	5,808	5,808	0	0	100.0%
MV cables	B2.31 23 00.01	LM	7,120	0	0	7,120	0.0%

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
LV cables	B2.33 71 00 02.01	LM	7,500	7,500	0	0	100.0%
Lighting luminaires	B2.26 56 19.01	EA	116	0	0	116	0.0%
Platform	03 00 00	m²	4,000	0	0	4,000	0.0%
Canopy	31 00 00	LM	4,000	0	0	4,000	0.0%
Metal handrail	B4.05 52 00.01	LM	440	0	0	440	0.0%

Station works not started

Platform (4,000 m²), canopy (4,000 m), metal handrail (440 m) and lighting luminaires (116) are all at 0%. The platform and canopy wait for the SAR fence permission and the client's design.

Figures to check

The quantities are identical to last week's, although the FIR log records subgrade and potable water work this week and the man-hours for roads nearly doubled. Aggregate base course is still 21,459 m³ against a total of 16,376 m³ (131%), and HDPE pipe and LV cables are still reported 100% finished.

Milestones

The weekly report and the P6 schedule update give different forecasts for the interim milestones. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	07-Apr-2026	07-Apr-2026	07-Apr-2026 (actual)	–	✓ Done
Mobilisation finish	06-May-2026	06-May-2026	06-May-2026 (actual)	–	✓ Done
Work plan and baseline submission	06-May-2026	16-Aug-2026 (+102 d)	15-Aug-2026 (actual)	–	✓ Done late
Engineering phase finish	06-May-2026	21-Sep-2026 (+138 d)	02-Nov-2026	59	▼ Late
Road and paving works	06-Dec-2026	31-Dec-2026 (+25 d)	02-Feb-2027	6	▼ Late
Procurement phase finish	15-Apr-2027	09-Jun-2027 (+55 d)	21-Mar-2027	54	? Forecasts differ
MV works	12-May-2027	05-May-2027	01-Jun-2027	7	▼ At risk
Site and platform works	20-Jul-2027	05-Aug-2027 (+16 d)	22-Apr-2027	85	? Forecasts differ
Finishing and general site works	20-Jul-2027	06-Aug-2027 (+17 d)	06-Aug-2027	0.5	▼ At risk
Project finish	06-Aug-2027	06-Aug-2027	06-Aug-2027	0	● No float

The weekly report and P6 disagree on the road, procurement and platform milestones.

The weekly report forecasts road and paving completion on 31-Dec-2026; P6 now has it on 02-Feb-2027 with 6 days of float. P6 completes site and platform works on 22-Apr-2027 with 85 days of float, although platform work has not started and is waiting for the SAR fence permission. The engineering phase, forecast for 21-Sep-2026 in the weekly report, is still open in P6. P6 now finishes the project on the contract date, one day earlier than last week, with no float.

Procurement of key materials

Share of the required quantity delivered, from the Completion Rate column. Source: Procurement sheet, weekly report 02-Nov-2026, unchanged from 26-Oct-2026.



Eight long-lead items not yet submitted


Metal railing, canopy, MV duct banks, MV cables, substations, lighting poles, street-lighting luminaires and outdoor lighting fixtures are all marked "Not submitted". The required PO dates for the railing (25-Aug-2026), the MV duct banks and cables (12-Oct-2026) and the substations (19-Oct-2026) have passed.

Items with no delivery figure

Interlock, waterproofing, the LV distribution panel, street-lighting feeder panels, CCTV, voice evacuation, manhole covers and valves have no delivery figure yet. Lighting poles show a purchase order (PO 12725, 01-Jul-2026) but are still marked "Not submitted". The summary counts 22 of 27 purchase orders issued.

Manpower

Monthly head count on site, planned vs actual. Source: Manpower sheet.

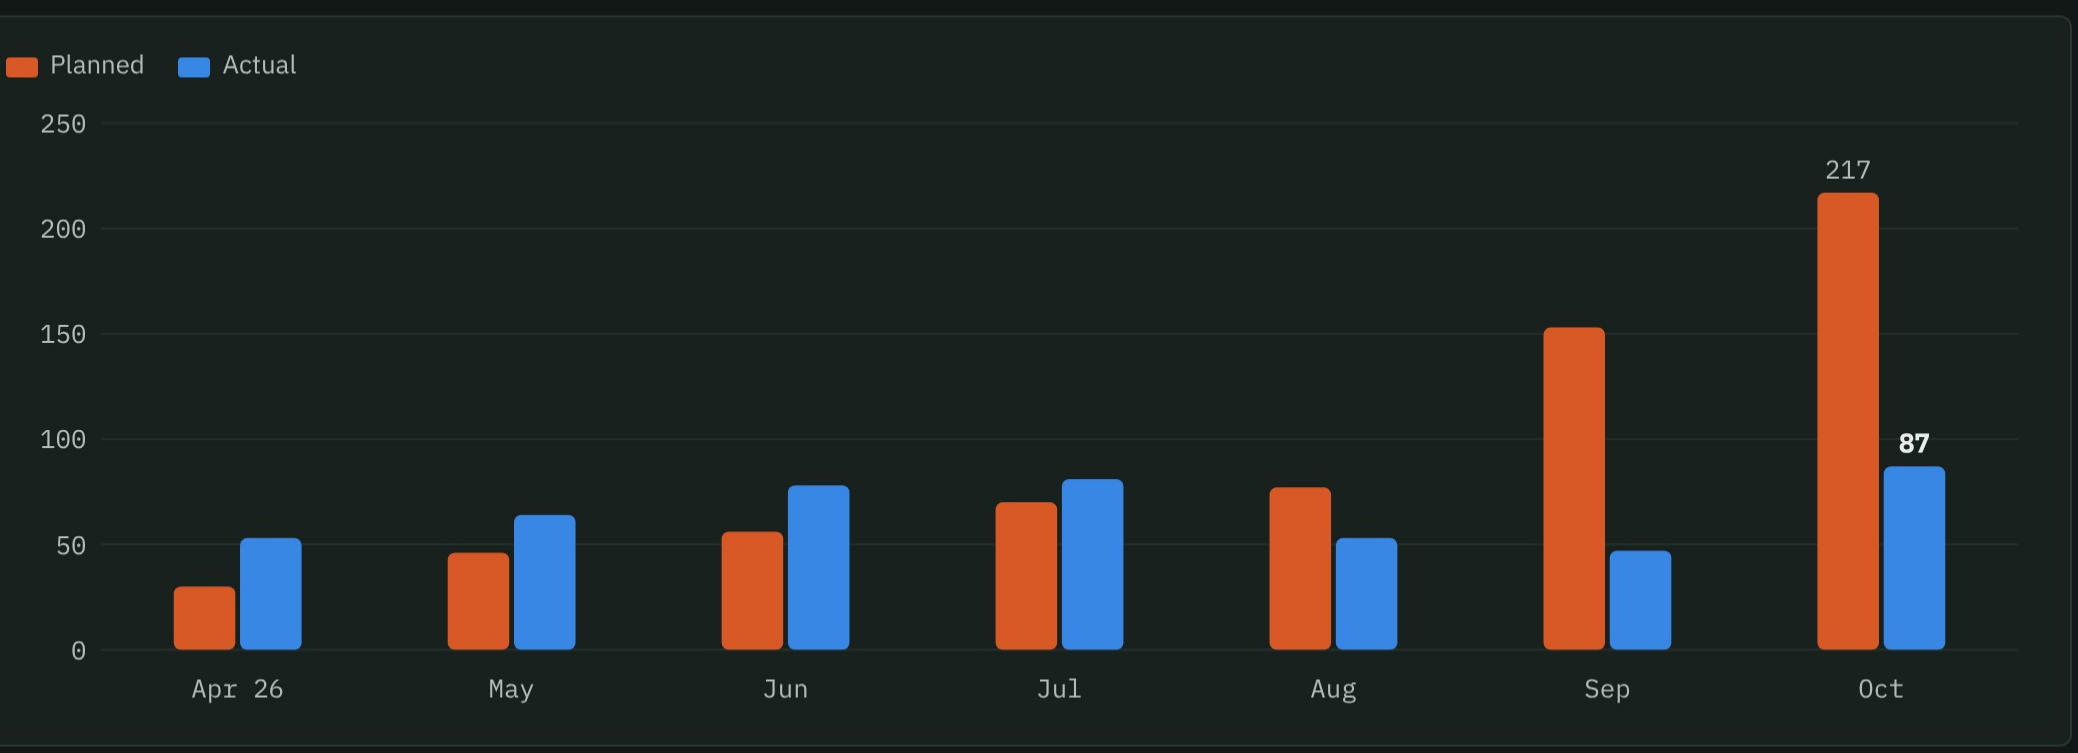

Manual and non-manual head count combined. October is 87 against 217 planned (−60%). The 02-Nov report adds a November column that repeats October's 87, against 232 planned, so November is not shown. The plan peaks at 263 in December 2026.

Cost and invoicing

Contract value

Original contract value	33,090,825
Change orders	0
Estimate at completion	33,090,825

All values in SAR. The change order log has no entries. The BOQ total on the Progress sheet is 33,090,852, 27 SAR more than the contract value.

Invoices

Invoices submitted	3
Gross value	7,337,445
VAT	1,100,617
Deductions and penalties	10,000
Net incl. VAT	8,428,062
PM-approved / paid	0 / 0

Invoicing is 22.2% of the contract value against 40.4% reported physical progress. Invoice 3 (4,289,046 SAR gross) covers 31-Aug-2026 to 28-Oct-2026. None of the three invoices is yet approved by the PM or paid.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	87,370
Man-hours this week	5,220
Internal trainings (cumulative)	24
Toolbox talks (cumulative)	22
HSE observations logged / open	19 / 0

Quality Score 0.89

FIRs issued / closed / pending	176 / 173 / 3
MIRs issued / closed	16 / 15
NCRs issued / closed	4 / 4
Site instructions	0
Shop drawings submitted (of 229)	229
Material submittals (of 45)	45

This week 19 FIRs and 1 MIR were added. Shop drawings: 174 approved (A), 42 approved as noted (B) and 13 C. Material submittals: 1 A, 41 B and 3 C.

Open issues and risks

ISSUE	OWNER	DETAIL
SAR fence permission	MODON / SAR	Permission to work inside the platform area is still pending, so the platform and canopy works cannot start. Rated very high (5 × 5) in the risk register, open since 16-Sep-2026.
Canopy and platform design	MODON (client)	The client has not yet issued the canopy and platform design, so the related shop drawings, procurement and construction cannot be finalised. Rated very high (5 × 5); value 9,867,379 SAR.
MV duct crossings	MODON (client)	Client approval of the proposed MV duct crossings is pending, and MV cable installation depends on it. Rated high (4 × 4).
Long-lead procurement	Contractor	Eight long-lead items are not yet submitted for approval, several past their required PO dates. Procurement is at 16.3% against 80.1% planned.
Progress reporting	Contractor / Consultant	The 13.1% jump in reported progress this week, the restated October actual and the new man-hour budget need to be checked and approved by the consultant.

The issue log lists 19 HSE observations from 02-Sep-2026 to 01-Nov-2026, all closed. Two older risks, the SAR permit for the geotechnical report and the platform tender drawing, are marked closed.

Data notes

- This week's values are compared with the 26-Oct-2026 weekly report (previous week folder). The 02-Nov report's own previous-week columns were not updated and still hold the 19-Oct-2026 values, so its weekly columns (21,907 planned and 99,941 earned man-hours) cover two weeks.
- The man-hour budget rose from 638,468 to 659,762. Mobilisation is now budgeted at 19,793 (so it reads 100%), procurement at 92,367 and construction at 494,821. No revision is explained in the report.
- Road-01 shows 122,462 earned man-hours against a budget of 106,900 (114.6%), and Road Works 1 rose from 79,097 to 161,207 earned man-hours, while all major quantities are unchanged since 26-Oct-2026.
- The Physical-Chart Data sheet restates the October actual from 174,266 to 246,525 man-hours and keeps the 638,468 budget, which gives 41.7% at 02-Nov against 40.4% on the Progress sheet.
- Earned man-hours went down this week for procurement (17,130 to 15,033), telecom (3,538 to 2,983) and low voltage (651 to 0).
- The cover sheet's headline "Earn Value" and its SPI are cost-based (BOQ value), not physical progress, and are not used in this report.
- Weekly planned man-hours for Road Works 1 (19,229) do not equal the sum of Road-01 and Road-02 (4,419), and Low Voltage Road-02 shows −11,263 planned this week.
- Major Quantities: aggregate base course is 21,459 m³ against a total of 16,376 m³, and HDPE pipe and LV cables are 100% finished. The asphalt total is 13,360 m³ there but 3,420 m³ on the Procurement sheet. The Procurement sheet gives kerbstone a completion rate of 1.4 (140%).
- Manpower: the October plan is 217 in the monthly histogram but 60 in the weekly summary panel, and the November actual repeats October.
- The cover sheet gives "Revised Completion" as 07-Apr-2026, the site handover date, and "Total Deduction" as 2,000 SAR, while the invoice log totals 10,000 SAR.
- The P6 update has a data date of 01-Nov-2026, one day before the weekly report.
- The project name changed this week to "Construction of a SAR Train Passenger Drop-Off Station in Sudair". The HSE inspection sheet and the FIR summary still carry project ID SUD1-02-011, and the Conclusion sheet describes a different project. The FIR summary total is 3,633,969 SAR at the top and 3,921,134 SAR at the bottom.
- The risk register describes the project as ahead of schedule. Risks 3120-4 and 3120-5 are marked Open in one column and Close in another.
- Four of the six weekly photos are less than 600 px wide and are not shown.

Compiled 03-Nov-2026 from the weekly report (data date 02-Nov-2026) and the P6 update uploaded for week 30, compared with the 26-Oct-2026 report.
