
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Upd		450	29-Oct-25 A	14-Sep-27	19-Mar-25	03-Jan-27	11,910,837.49
Procurement Cycle		439	29-Oct-25 A	13-Jan-27	11-Jun-25	31-Aug-26	0.00
Short Lead Time Items		439	29-Oct-25 A	13-Jan-27	11-Jun-25	05-Jul-26	0.00
Infrastructure Networks		439	11-Dec-25 A	13-Jan-27	11-Jun-25	05-Jul-26	0.00
Road Works		42	03-Nov-26	21-Dec-26	12-Aug-25	05-Jul-26	0.00
1st Material Delivery & Site Inspection		6	03-Nov-26	09-Nov-26	12-Aug-25	18-Aug-25	0.00
Traffic Signs Boards and Roads Marking		6	03-Nov-26	09-Nov-26	12-Aug-25	18-Aug-25	0.00
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	6	03-Nov-26	09-Nov-26	12-Aug-25	18-Aug-25	0.00
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	6	03-Nov-26	09-Nov-26	12-Aug-25	18-Aug-25	0.00
Material Delivery & Site Inspection		42	03-Nov-26	21-Dec-26	28-Dec-25	05-Jul-26	0.00
Road 18 Local 1 (479 LM)		31	10-Nov-26	15-Dec-26	28-Dec-25	25-Feb-26	0.00
Traffic Signs Boards and Roads Marking		31	10-Nov-26	15-Dec-26	28-Dec-25	25-Feb-26	0.00
PRO-R18-RD-DL-2	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	10-Nov-26	09-Dec-26	28-Dec-25	26-Jan-26	0.00
PRO-R18-RD-DL-2	Material Delivery & Site Inspection of Road Markings For Road Works	26	16-Nov-26	15-Dec-26	27-Jan-26	25-Feb-26	0.00
Road 17 Local 1 (500 LM)		31	16-Nov-26	21-Dec-26	27-Jan-26	31-Mar-26	0.00
Traffic Signs Boards and Roads Marking		31	16-Nov-26	21-Dec-26	27-Jan-26	31-Mar-26	0.00
PRO-R17-RD-DL-1	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	16-Nov-26	15-Dec-26	27-Jan-26	25-Feb-26	0.00
PRO-R17-RD-DL-1	Material Delivery & Site Inspection of Road Markings For Road Works	26	22-Nov-26	21-Dec-26	26-Feb-26	31-Mar-26	0.00
Road 16 Local 1 (527 LM)		26	22-Nov-26	21-Dec-26	26-Feb-26	31-Mar-26	0.00
Traffic Signs Boards and Roads Marking		26	22-Nov-26	21-Dec-26	26-Feb-26	31-Mar-26	0.00
PRO-R16-RD-DL-1	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	22-Nov-26	21-Dec-26	26-Feb-26	31-Mar-26	0.00
Road 10 Local 2 (2352 LM)		26	03-Nov-26	02-Dec-26	26-Feb-26	30-Apr-26	0.00
Bituminous Construction		26	03-Nov-26	02-Dec-26	26-Feb-26	30-Apr-26	0.00
PRO-R10-RD-DL-1	Material Delivery & Site Inspection for Prime Coat of Road Works	26	03-Nov-26	02-Dec-26	26-Feb-26	31-Mar-26	0.00
PRO-R10-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	03-Nov-26	02-Dec-26	01-Apr-26	30-Apr-26	0.00
Road 09 Local 2 (2278 LM)		26	03-Nov-26	02-Dec-26	02-May-26	05-Jul-26	0.00
Bituminous Construction		26	03-Nov-26	02-Dec-26	02-May-26	05-Jul-26	0.00
PRO-R09-RD-DL-1	Material Delivery & Site Inspection for Prime Coat of Road Works	26	03-Nov-26	02-Dec-26	02-May-26	04-Jun-26	0.00
PRO-R09-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	03-Nov-26	02-Dec-26	06-Jun-26	05-Jul-26	0.00
Sewage Network		41	03-Nov-26	20-Dec-26	26-Jul-25	24-Jan-26	0.00
Material Delivery & Site Inspection		41	03-Nov-26	20-Dec-26	26-Jul-25	24-Jan-26	0.00
Road 17 Local 1 (500 LM)		26	03-Nov-26	02-Dec-26	25-Aug-25	25-Oct-25	0.00
Testing and Finishes		26	03-Nov-26	02-Dec-26	25-Aug-25	25-Oct-25	0.00
PRO-R17-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	03-Nov-26	02-Dec-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	03-Nov-26	02-Dec-26	25-Sep-25	25-Oct-25	0.00
Road 16 Local 1 (527 LM)		26	09-Nov-26	08-Dec-26	25-Sep-25	24-Nov-25	0.00
Testing and Finishes		26	09-Nov-26	08-Dec-26	25-Sep-25	24-Nov-25	0.00
PRO-R16-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	09-Nov-26	08-Dec-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	09-Nov-26	08-Dec-26	26-Oct-25	24-Nov-25	0.00
Road 15 Local 1 (556 LM)		26	15-Nov-26	14-Dec-26	26-Oct-25	24-Dec-25	0.00
Testing and Finishes		26	15-Nov-26	14-Dec-26	26-Oct-25	24-Dec-25	0.00
PRO-R15-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	15-Nov-26	14-Dec-26	26-Oct-25	24-Nov-25	0.00
PRO-R15-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	15-Nov-26	14-Dec-26	25-Nov-25	24-Dec-25	0.00
Road 10 Local 2 (2352 LM)		26	21-Nov-26	20-Dec-26	25-Nov-25	24-Jan-26	0.00
Testing and Finishes		26	21-Nov-26	20-Dec-26	25-Nov-25	24-Jan-26	0.00

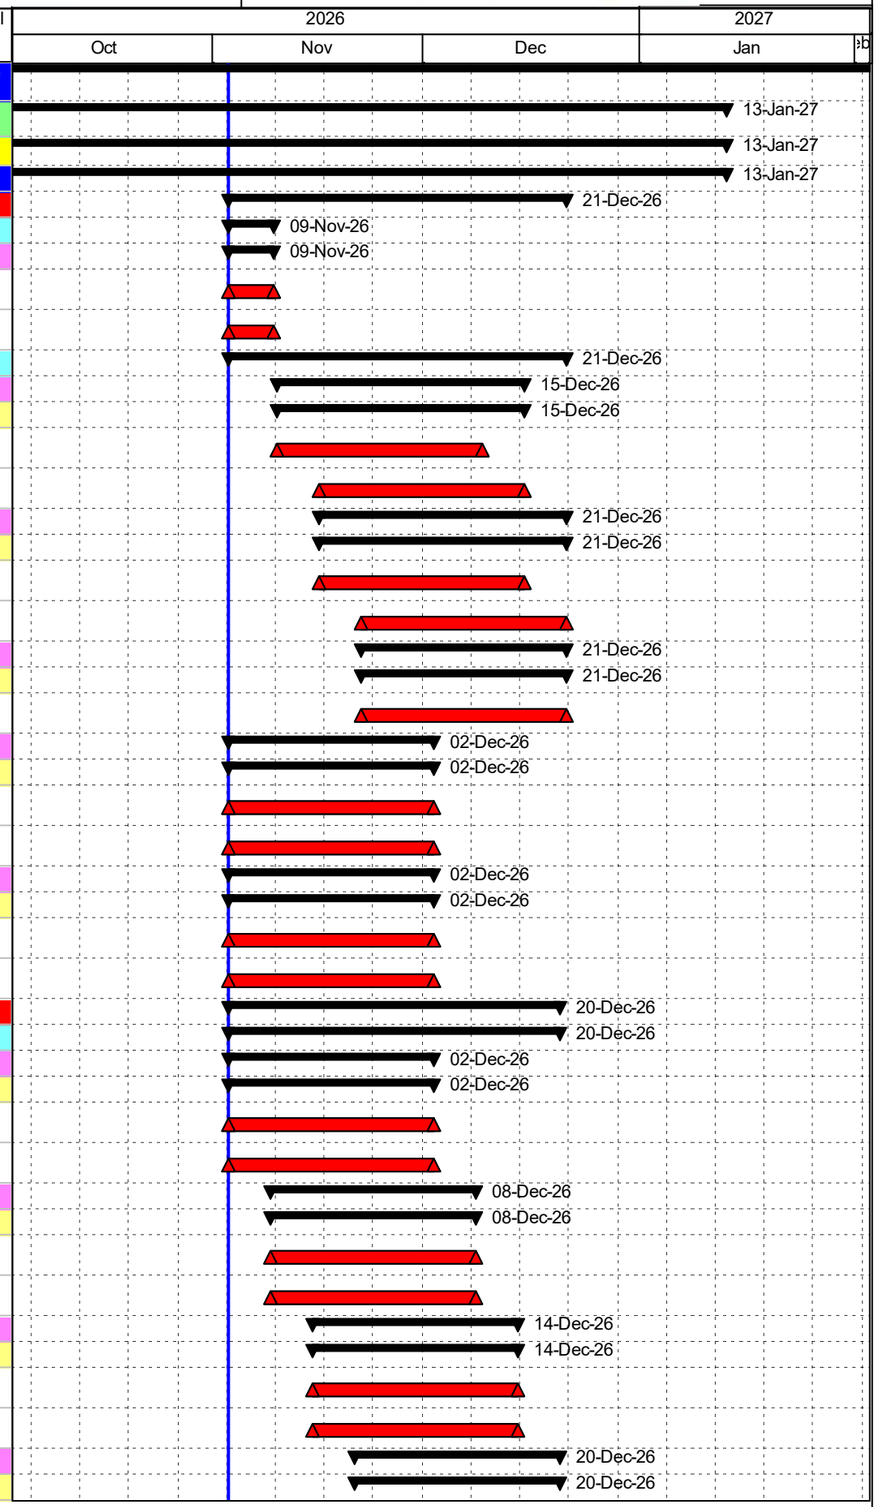

Primary Baseline | Actual Work | Summary

Remaining Work | Baseline Milestone


Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R10-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	21-Nov-26	20-Dec-26	25-Nov-25	24-Dec-25	0.00
PRO-R10-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	21-Nov-26	20-Dec-26	25-Dec-25	24-Jan-26	0.00
Road 09 Local 2 (2278 LM)		38	03-Nov-26	16-Dec-26	26-Jul-25	07-Sep-25	0.00
Testing and Finishes		38	03-Nov-26	16-Dec-26	26-Jul-25	07-Sep-25	0.00
PRO-R09-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Rising Main Network	38	03-Nov-26	16-Dec-26	26-Jul-25	07-Sep-25	0.00
PRO-R09-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Rising Main Network	38	03-Nov-26	16-Dec-26	26-Jul-25	07-Sep-25	0.00
Storm Drainage Network		405	20-Jun-26 A	20-Dec-26	26-Jul-25	23-Feb-26	0.00
Material Delivery & Site Inspection		405	20-Jun-26 A	20-Dec-26	26-Jul-25	23-Feb-26	0.00
Road 18 Local 1 (479 LM)		26	03-Nov-26	02-Dec-26	26-Jul-25	24-Aug-25	0.00
Testing and Finishes		26	03-Nov-26	02-Dec-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL-1	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	03-Nov-26	02-Dec-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL-2	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	03-Nov-26	02-Dec-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL-2	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	03-Nov-26	02-Dec-26	26-Jul-25	24-Aug-25	0.00
Road 17 Local 1 (500 LM)		395	20-Jun-26 A	08-Dec-26	25-Aug-25	24-Sep-25	0.00
Testing and Finishes		395	20-Jun-26 A	08-Dec-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL-1	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	20-Jun-26 A	08-Dec-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL-1	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	09-Nov-26	08-Dec-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	09-Nov-26	08-Dec-26	25-Aug-25	24-Sep-25	0.00
Road 16 Local 1 (527 LM)		26	15-Nov-26	14-Dec-26	25-Sep-25	25-Oct-25	0.00
Testing and Finishes		26	15-Nov-26	14-Dec-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SD-DL-1	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	15-Nov-26	14-Dec-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	15-Nov-26	14-Dec-26	25-Sep-25	25-Oct-25	0.00
Road 15 Local 1 (556 LM)		26	21-Nov-26	20-Dec-26	26-Oct-25	24-Nov-25	0.00
Testing and Finishes		26	21-Nov-26	20-Dec-26	26-Oct-25	24-Nov-25	0.00
PRO-R15-SD-DL-1	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	21-Nov-26	20-Dec-26	26-Oct-25	24-Nov-25	0.00
PRO-R15-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	21-Nov-26	20-Dec-26	26-Oct-25	24-Nov-25	0.00
Road 14 Local 1 (584 LM)		26	03-Nov-26	02-Dec-26	25-Dec-25	24-Jan-26	0.00
Testing and Finishes		26	03-Nov-26	02-Dec-26	25-Dec-25	24-Jan-26	0.00
PRO-R14-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	03-Nov-26	02-Dec-26	25-Dec-25	24-Jan-26	0.00
Road 09 Local 2 (2278 LM)		26	09-Nov-26	08-Dec-26	25-Jan-26	23-Feb-26	0.00
Testing and Finishes		26	09-Nov-26	08-Dec-26	25-Jan-26	23-Feb-26	0.00
PRO-R09-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	09-Nov-26	08-Dec-26	25-Jan-26	23-Feb-26	0.00
Potable Water Network		387	13-Dec-25 A	20-Dec-26	11-Jun-25	09-Feb-26	0.00
Material Delivery & Site Inspection		387	13-Dec-25 A	20-Dec-26	11-Jun-25	09-Feb-26	0.00
Road 18 Local 1 (479 LM)		26	03-Nov-26	02-Dec-26	11-Jun-25	10-Jul-25	0.00
Testing and Finishes		26	03-Nov-26	02-Dec-26	11-Jun-25	10-Jul-25	0.00
PRO-R18-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	03-Nov-26	02-Dec-26	11-Jun-25	10-Jul-25	0.00
Road 17 Local 1 (500 LM)		31	03-Nov-26	08-Dec-26	16-Jun-25	10-Aug-25	0.00
Main Line Sections		26	03-Nov-26	02-Dec-26	16-Jun-25	15-Jul-25	0.00
PRO-R17-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	26	03-Nov-26	02-Dec-26	16-Jun-25	15-Jul-25	0.00
Testing and Finishes		26	09-Nov-26	08-Dec-26	12-Jul-25	10-Aug-25	0.00
PRO-R17-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	09-Nov-26	08-Dec-26	12-Jul-25	10-Aug-25	0.00
Road 16 Local 1 (527 LM)		31	09-Nov-26	14-Dec-26	16-Jul-25	09-Sep-25	0.00
Main Line Sections		26	09-Nov-26	08-Dec-26	16-Jul-25	14-Aug-25	0.00
PRO-R16-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	26	09-Nov-26	08-Dec-26	16-Jul-25	14-Aug-25	0.00

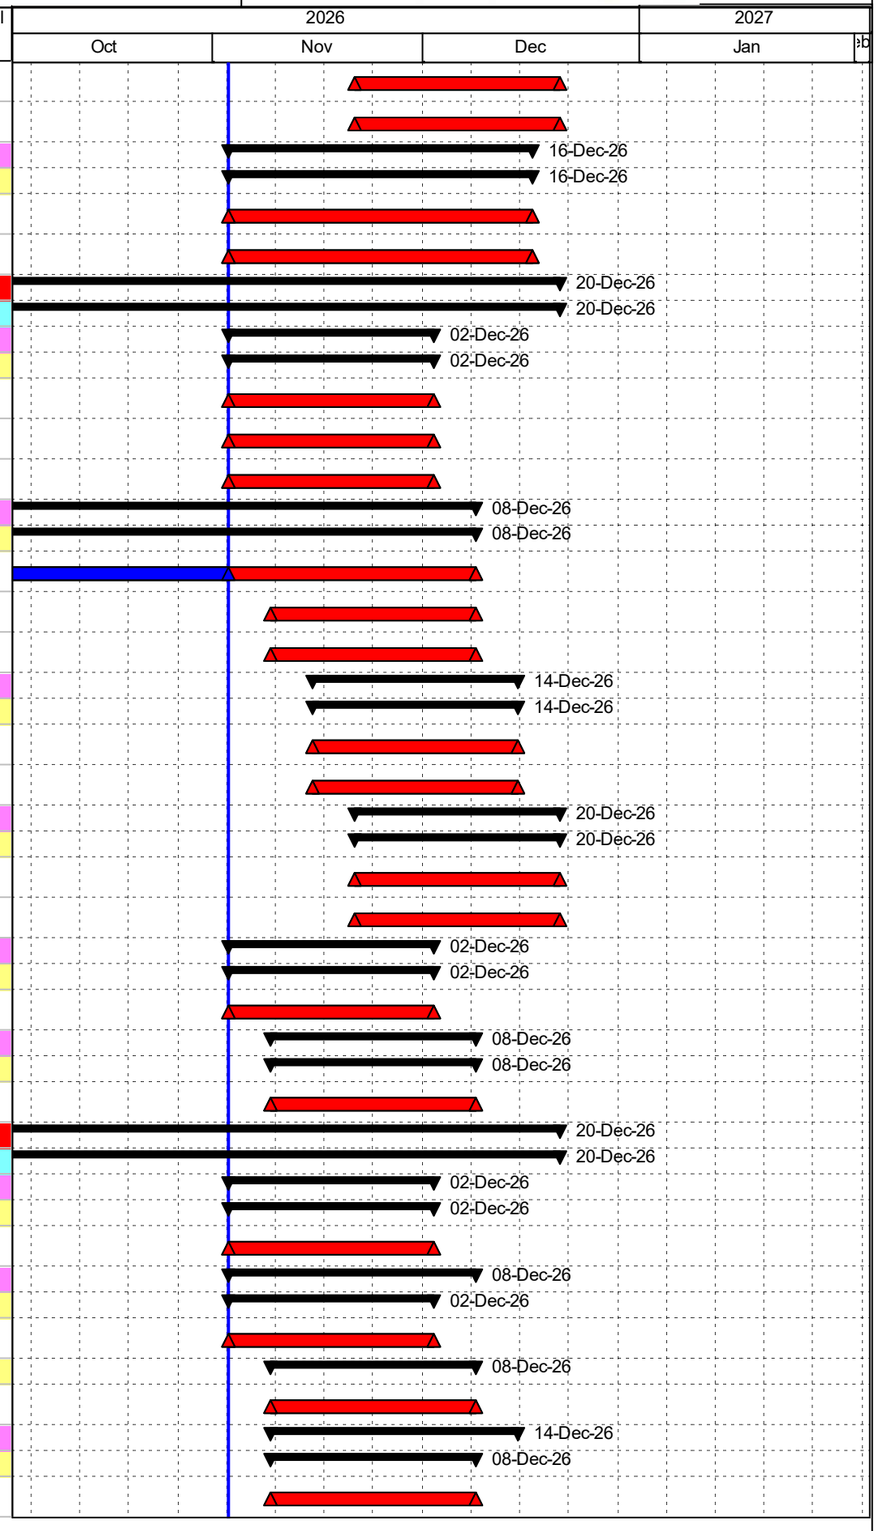


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Testing and Finishes		26	15-Nov-26	14-Dec-26	11-Aug-25	09-Sep-25	0.00
PRO-R16-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	15-Nov-26	14-Dec-26	11-Aug-25	09-Sep-25	0.00
Road 15 Local 1 (556 LM)		31	15-Nov-26	20-Dec-26	16-Aug-25	11-Oct-25	0.00
Main Line Sections		26	15-Nov-26	14-Dec-26	16-Aug-25	14-Sep-25	0.00
PRO-R15-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	26	15-Nov-26	14-Dec-26	16-Aug-25	14-Sep-25	0.00
Testing and Finishes		26	21-Nov-26	20-Dec-26	10-Sep-25	11-Oct-25	0.00
PRO-R15-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	21-Nov-26	20-Dec-26	10-Sep-25	11-Oct-25	0.00
Road 10 Local 2 (2352 LM)		26	13-Dec-25 A	20-Dec-26	15-Sep-25	15-Oct-25	0.00
Main Line Sections		26	13-Dec-25 A	20-Dec-26	15-Sep-25	15-Oct-25	0.00
PRO-R10-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-25 A	20-Dec-26	15-Sep-25	15-Oct-25	0.00
Road 14 Local 1 (584 LM)		26	10-Oct-26 A	17-Dec-26	16-Oct-25	15-Nov-25	0.00
Main Line Sections		26	10-Oct-26 A	17-Dec-26	16-Oct-25	15-Nov-25	0.00
PRO-R14-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	26	10-Oct-26 A	17-Dec-26	16-Oct-25	15-Nov-25	0.00
Road 09 Local 2 (2278 LM)		26	03-Nov-26	02-Dec-26	11-Dec-25	10-Jan-26	0.00
Testing and Finishes		26	03-Nov-26	02-Dec-26	11-Dec-25	10-Jan-26	0.00
PRO-R09-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	03-Nov-26	02-Dec-26	11-Dec-25	10-Jan-26	0.00
Road 11 Local 1 (670 LM)		26	09-Nov-26	08-Dec-26	11-Jan-26	09-Feb-26	0.00
Testing and Finishes		26	09-Nov-26	08-Dec-26	11-Jan-26	09-Feb-26	0.00
PRO-R11-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	09-Nov-26	08-Dec-26	11-Jan-26	09-Feb-26	0.00
Irrigation Network		430	11-Dec-25 A	10-Dec-26	17-Jul-25	07-Oct-25	0.00
1st Material Delivery & Site Inspection		6	11-Dec-25 A	04-Nov-26	17-Jul-25	23-Jul-25	0.00
Main Line Pipes		6	11-Dec-25 A	04-Nov-26	17-Jul-25	23-Jul-25	0.00
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	11-Dec-25 A	04-Nov-26	17-Jul-25	23-Jul-25	0.00
Material Delivery & Site Inspection		31	05-Nov-26	10-Dec-26	24-Jul-25	07-Oct-25	0.00
Road 18 Local 1 (479 LM)		16	05-Nov-26	23-Nov-26	24-Jul-25	11-Aug-25	0.00
Main Line Pipes		16	05-Nov-26	23-Nov-26	24-Jul-25	11-Aug-25	0.00
PRO-R18-IR-DL-13	Material Delivery & Site Inspection of Valves for Irrigation Network	16	05-Nov-26	23-Nov-26	24-Jul-25	11-Aug-25	0.00
Road 17 Local 1 (500 LM)		16	11-Nov-26	29-Nov-26	12-Aug-25	30-Aug-25	0.00
Main Line Pipes		16	11-Nov-26	29-Nov-26	12-Aug-25	30-Aug-25	0.00
PRO-R17-IR-DL-11	Material Delivery & Site Inspection of Valves for Irrigation Network	16	11-Nov-26	29-Nov-26	12-Aug-25	30-Aug-25	0.00
Road 16 Local 1 (527 LM)		16	17-Nov-26	05-Dec-26	31-Aug-25	17-Sep-25	0.00
Main Line Pipes		16	17-Nov-26	05-Dec-26	31-Aug-25	17-Sep-25	0.00
PRO-R16-IR-DL-11	Material Delivery & Site Inspection of Valves for Irrigation Network	16	17-Nov-26	05-Dec-26	31-Aug-25	17-Sep-25	0.00
Road 15 Local 1 (556 LM)		16	23-Nov-26	10-Dec-26	18-Sep-25	07-Oct-25	0.00
Main Line Pipes		16	23-Nov-26	10-Dec-26	18-Sep-25	07-Oct-25	0.00
PRO-R15-IR-DL-11	Material Delivery & Site Inspection of Valves for Irrigation Network	16	23-Nov-26	10-Dec-26	18-Sep-25	07-Oct-25	0.00
Street Lighting Network		426	21-Sep-26 A	13-Jan-27	26-Jul-25	16-Mar-26	0.00
1st Material Delivery & Site Inspection		6	03-Nov-26	09-Nov-26	26-Jul-25	31-Jul-25	0.00
Lighting Poles Works		6	03-Nov-26	09-Nov-26	26-Jul-25	31-Jul-25	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	03-Nov-26	09-Nov-26	26-Jul-25	31-Jul-25	0.00
Earthing System Works		6	03-Nov-26	09-Nov-26	26-Jul-25	31-Jul-25	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	03-Nov-26	09-Nov-26	26-Jul-25	31-Jul-25	0.00
Material Delivery & Site Inspection		426	21-Sep-26 A	13-Jan-27	02-Aug-25	16-Mar-26	0.00
Road 18 Local 1 (479 LM)		36	10-Nov-26	21-Dec-26	16-Aug-25	15-Nov-25	0.00
Lighting Poles Works		26	10-Nov-26	09-Dec-26	16-Aug-25	14-Sep-25	0.00
PRO-R18-SL-DL-22	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	10-Nov-26	09-Dec-26	16-Aug-25	14-Sep-25	0.00
Termination and Testing Works		31	16-Nov-26	21-Dec-26	15-Sep-25	15-Nov-25	0.00

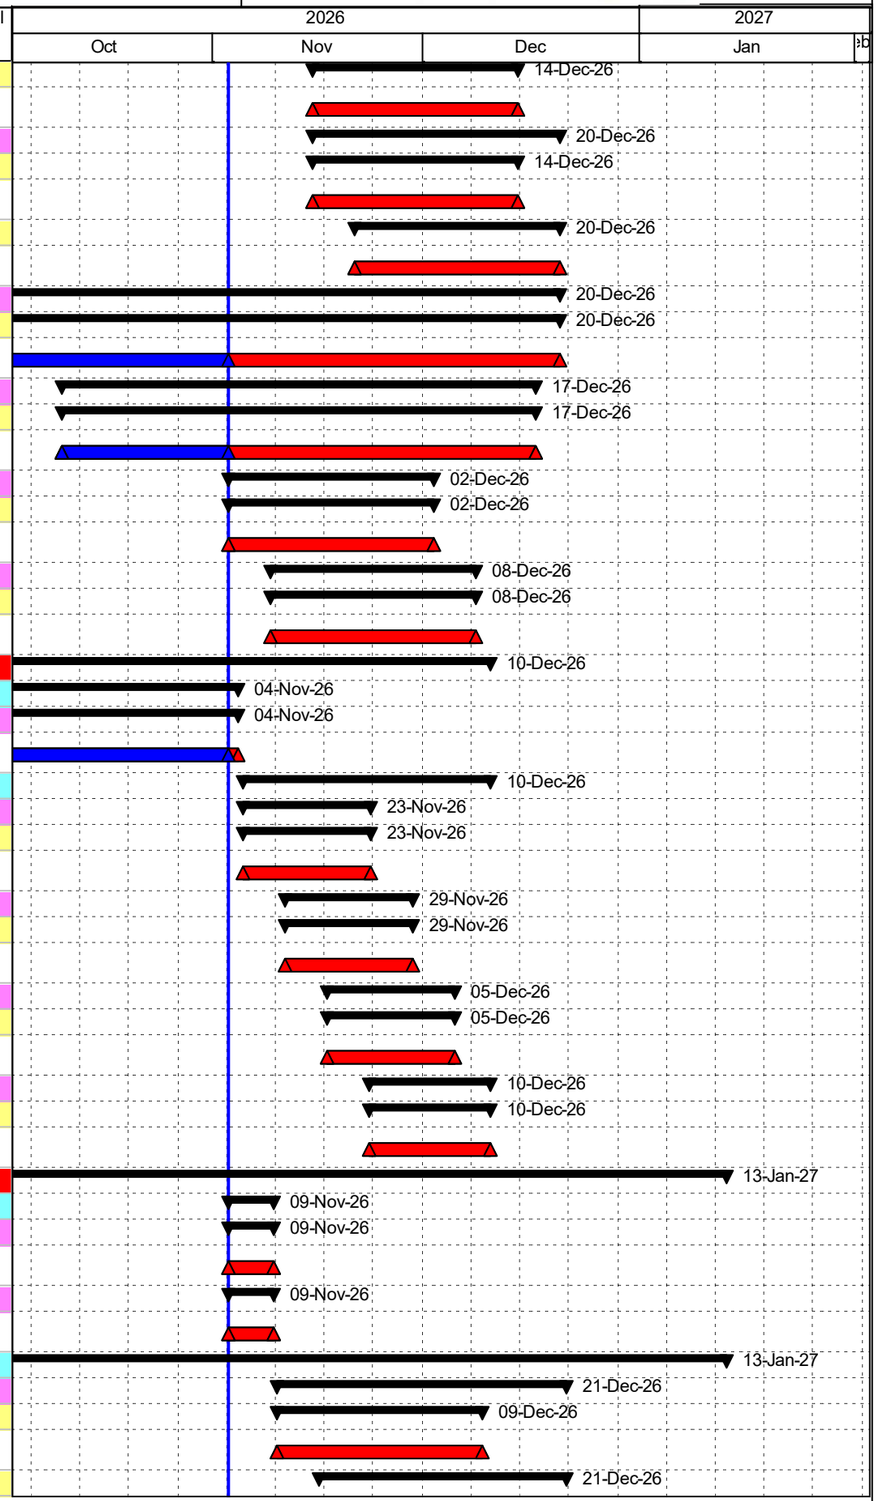


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	16-Nov-26	15-Dec-26	15-Sep-25	15-Oct-25	0.00
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
Road 17 Local 1 (500 LM)		31	16-Nov-26	21-Dec-26	15-Sep-25	15-Nov-25	0.00
Lighting Poles Works		26	16-Nov-26	15-Dec-26	15-Sep-25	15-Oct-25	0.00
PRO-R17-SL-DL-1	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	16-Nov-26	15-Dec-26	15-Sep-25	15-Oct-25	0.00
Termination and Testing Works		26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
PRO-R17-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
Road 16 Local 1 (527 LM)		26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
Lighting Poles Works		26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
PRO-R16-SL-DL-1	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	22-Nov-26	21-Dec-26	16-Oct-25	15-Nov-25	0.00
Road 10 Local 2 (2352 LM)		416	21-Sep-26 A	13-Jan-27	02-Aug-25	16-Mar-26	0.00
Distribution Panel Board		26	21-Sep-26 A	05-Nov-26	02-Aug-25	31-Aug-25	0.00
PRO-R10-SL-DL-1	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	26	21-Sep-26 A	05-Nov-26	02-Aug-25	31-Aug-25	0.00
Termination and Testing Works		52	21-Sep-26 A	13-Jan-27	15-Jan-26	16-Mar-26	0.00
PRO-R10-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Sep-26 A	07-Jan-27	15-Jan-26	14-Feb-26	0.00
PRO-R10-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Sep-26 A	13-Jan-27	15-Feb-26	16-Mar-26	0.00
Earthing System Works		26	10-Nov-26	09-Dec-26	02-Aug-25	31-Aug-25	0.00
PRO-R10-SL-DL-1	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	10-Nov-26	09-Dec-26	02-Aug-25	31-Aug-25	0.00
Road 09 Local 2 (2278 LM)		26	10-Nov-26	09-Dec-26	02-Aug-25	31-Aug-25	0.00
Earthing System Works		26	10-Nov-26	09-Dec-26	02-Aug-25	31-Aug-25	0.00
PRO-R09-SL-DL-1	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	10-Nov-26	09-Dec-26	02-Aug-25	31-Aug-25	0.00
Superstructure Works		130	29-Oct-25 A	09-Nov-26	15-Sep-25	14-Feb-26	0.00
Material Delivery & Site Inspection		130	29-Oct-25 A	09-Nov-26	15-Sep-25	14-Feb-26	0.00
Storm Drainage Ponds (PO-J1 , PO-J2)		130	29-Oct-25 A	09-Nov-26	15-Sep-25	14-Feb-26	0.00
PRO-DPO-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J1)	70	29-Oct-25 A	04-Nov-26	15-Sep-25	06-Dec-25	0.00
PRO-DPO-CV-DL-20	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J2)	70	09-Sep-26 A	09-Nov-26	25-Nov-25	14-Feb-26	0.00
Long Lead Time Items		50	05-Oct-26 A	19-Nov-26	05-Jul-26	31-Aug-26	0.00
Superstructure Works		50	05-Oct-26 A	19-Nov-26	05-Jul-26	31-Aug-26	0.00
Sewage Pump Stations (PS 06)		50	05-Oct-26 A	19-Nov-26	05-Jul-26	31-Aug-26	0.00
Material Site Inspection		50	05-Oct-26 A	19-Nov-26	05-Jul-26	31-Aug-26	0.00
PRO-SPS7-LL-MSI-1	Material Site Inspection for Electromechanical Works for Sewage Pump Stations (PS06)	50	05-Oct-26 A	19-Nov-26	05-Jul-26	31-Aug-26	0.00
Construction Works		365	05-Mar-26 A	31-Mar-27	19-Mar-25	04-Oct-26	11,910,837.49
Infrastructure Networks		365	05-Mar-26 A	31-Mar-27	19-Mar-25	04-Oct-26	11,685,949.39
Phase 2 Block "J"		365	05-Mar-26 A	28-Mar-27	19-Mar-25	01-Sep-26	10,213,405.68
Rising Main Network		344	18-Sep-26 A	22-Nov-26	08-Oct-25	01-Nov-25	687,138.66
Manholes		9	18-Sep-26 A	11-Nov-26	08-Oct-25	18-Oct-25	387,992.47
CO-RM-SW-350	Pouring Grp Liner Wall Works for Main Line Manholes of Rising Main Network	3	18-Sep-26 A	04-Nov-26	08-Oct-25	11-Oct-25	98,089.73
CO-RM-SW-360	Backfilling Works for Main Line Manholes of Rising Main Network	5	21-Sep-26 A	04-Nov-26	12-Oct-25	16-Oct-25	144,951.37
CO-RM-SW-370	Testing Works for Main Line Manholes of Rising Main Network	1	01-Oct-26 A	11-Nov-26	18-Oct-25	18-Oct-25	144,951.37
Valves Chamber		17	03-Nov-26	22-Nov-26	13-Oct-25	01-Nov-25	299,146.20
CO-RM-SW-410	RC Slab Works for Valve Chambers and Washout chamber of Rising Main Network	7	03-Nov-26	10-Nov-26	13-Oct-25	20-Oct-25	56,939.38
CO-RM-SW-420	Insulation Works for Valve Chambers and Washout chamber of Rising Main Network	2	11-Nov-26	12-Nov-26	21-Oct-25	22-Oct-25	56,939.38
CO-RM-SW-430	Backfilling Works for Valve Chambers and Washout chamber of Rising Main Network	5	14-Nov-26	18-Nov-26	23-Oct-25	28-Oct-25	67,019.16
CO-RM-SW-440	Testing and Covering Works for Valve Chambers and Washout chamber of Rising Main Network	3	19-Nov-26	22-Nov-26	29-Oct-25	01-Nov-25	118,248.27

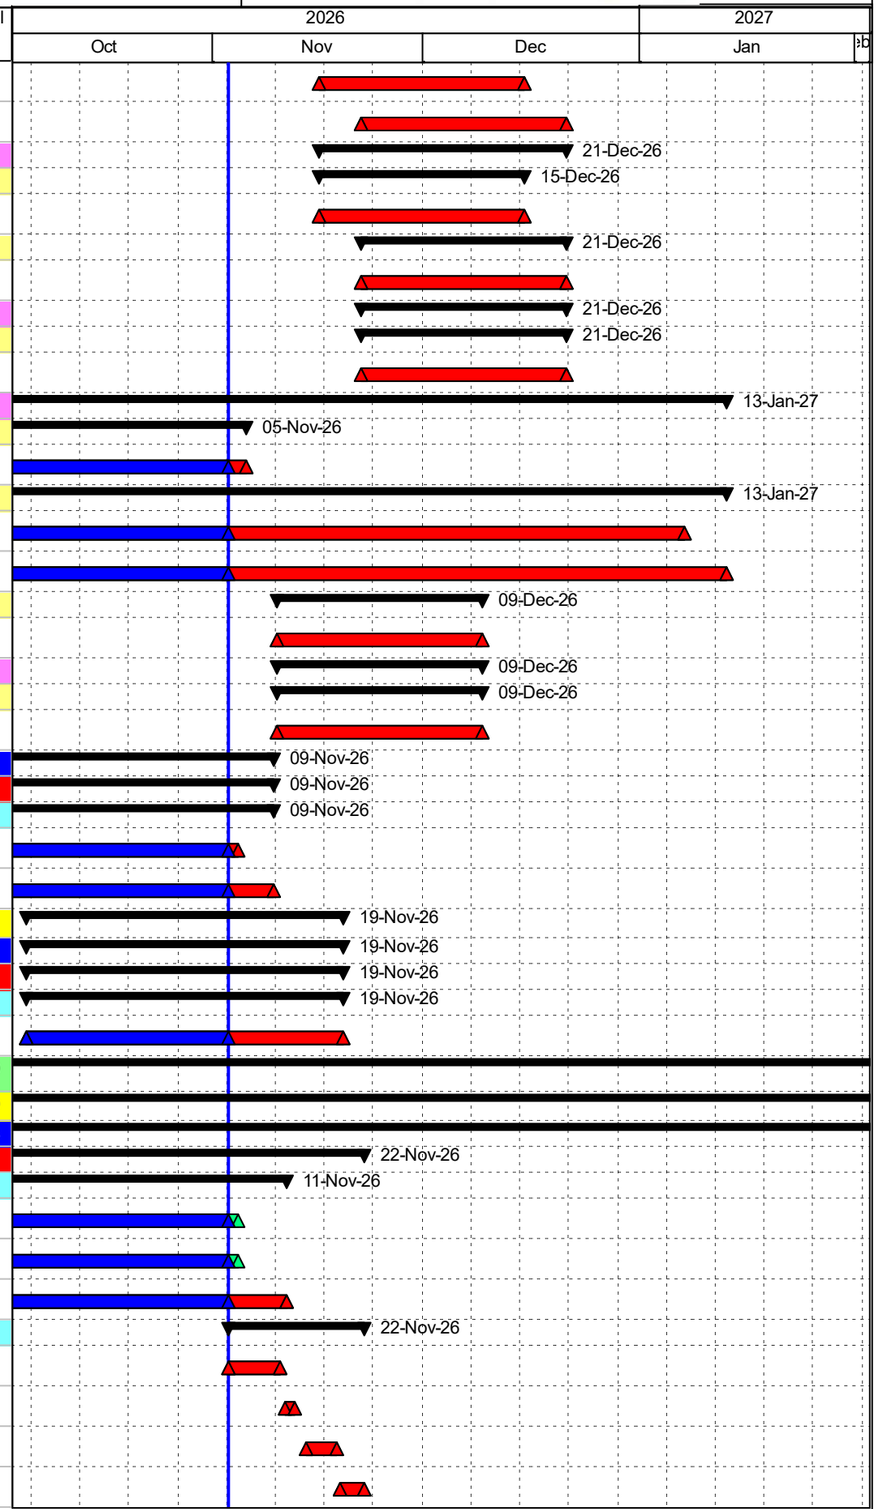


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Road 09 Local 2 (2278 LM)		356	05-Mar-26 A	28-Mar-27	05-Oct-25	28-Jul-26	4,670,833.71
SW_1		352	10-Jun-26 A	28-Feb-27	05-Oct-25	14-Jul-26	2,878,856.59
Storm Drainage Network		39	14-Jun-26 A	18-Nov-26	05-Oct-25	18-Nov-25	163,178.92
Manholes		2	07-Oct-26 A	18-Nov-26	05-Oct-25	06-Oct-25	42,635.10
CO-R09.S01-SD-2	Testing Works for Manholes of Storm Drainage Network-[Road 09] -[SW-1]	2	07-Oct-26 A	18-Nov-26	05-Oct-25	06-Oct-25	42,635.10
Catch Basin Sections		17	14-Jun-26 A	05-Nov-26	30-Oct-25	18-Nov-25	120,543.82
CO-R09.S01-SD-1	Testing Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	14-Jun-26 A	05-Nov-26	30-Oct-25	06-Nov-25	40,026.06
CO-R09.S01-SD-1	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	10	03-Aug-26 A	05-Nov-26	08-Nov-25	18-Nov-25	80,517.76
Irrigation Network		7	05-Nov-26	12-Nov-26	09-Dec-25	16-Dec-25	178,429.81
Main Line Pipes		7	05-Nov-26	12-Nov-26	09-Dec-25	16-Dec-25	178,429.81
CO-R09.S01-IR-12	Installation Works for Main Line Valves of Irrigation Network-[Road 09] -[SW-1]	7	05-Nov-26	12-Nov-26	09-Dec-25	16-Dec-25	178,429.81
Street Lighting Network		22	03-Nov-26	28-Nov-26	29-Dec-25	22-Jan-26	31,563.78
Lighting Poles Works		22	03-Nov-26	28-Nov-26	29-Dec-25	22-Jan-26	31,563.78
CO-R09.S01-SL-10	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	10	03-Nov-26	14-Nov-26	29-Dec-25	08-Jan-26	5,849.15
CO-R09.S01-SL-11	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 09] -[SW-1]	12	15-Nov-26	28-Nov-26	10-Jan-26	22-Jan-26	25,714.63
Cabling Works		10	15-Nov-26	25-Nov-26	10-Jan-26	20-Jan-26	0.00
CO-R09.S01-SL-14	Trench Excavation and Bedding Works for Street Lighting Network-[Road 09] -[SW-1]	10	15-Nov-26	25-Nov-26	10-Jan-26	20-Jan-26	0.00
Medium Voltage Network		16	30-Sep-26 A	19-Dec-26	14-Feb-26	03-Mar-26	1,745,206.36
Cabling Works		16	30-Sep-26 A	19-Dec-26	14-Feb-26	03-Mar-26	1,745,206.36
CO-R09.S01-MV-1	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 09] -[SW-1]	4	30-Sep-26 A	19-Dec-26	14-Feb-26	17-Feb-26	200,688.86
CO-R09.S01-MV-11	Cable Laying Works for Medium Voltage Network-[Road 09] -[SW-1]	5	07-Oct-26 A	19-Dec-26	18-Feb-26	23-Feb-26	1,080,991.51
CO-R09.S01-MV-1	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 09] -[SW-1]	7	13-Oct-26 A	19-Dec-26	24-Feb-26	03-Mar-26	463,525.99
Road Works		21	10-Jun-26 A	28-Feb-27	21-Jun-26	14-Jul-26	760,477.73
Pre-Bituminous Construction		21	10-Jun-26 A	28-Feb-27	21-Jun-26	14-Jul-26	760,477.73
CO-R09.S01-RD-P	Capping and Subgrade Layer for Road Works-[Road 09] -[SW-1]	21	10-Jun-26 A	28-Feb-27	21-Jun-26	14-Jul-26	760,477.73
SW_2		340	05-Mar-26 A	28-Mar-27	23-Oct-25	28-Jul-26	1,791,977.12
Storm Drainage Network		50	05-Mar-26 A	19-Nov-26	23-Oct-25	20-Dec-25	517,061.87
Manholes		9	05-Mar-26 A	19-Nov-26	23-Oct-25	02-Nov-25	155,360.98
CO-R09.S02-SD-2	Backfilling Works for Manholes of Storm Drainage Network-[Road 09]-[SW-2]	7	05-Mar-26 A	19-Nov-26	26-Oct-25	02-Nov-25	112,725.88
CO-R09.S02-SD-2	Testing Works for Manholes of Storm Drainage Network-[Road 09]-[SW-2]	2	25-Sep-26 A	18-Nov-26	23-Oct-25	25-Oct-25	42,635.10
Catch Basin Sections		41	24-Jun-26 A	19-Nov-26	03-Nov-25	20-Dec-25	361,700.89
CO-R09.S02-SD-1	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	6	24-Jun-26 A	19-Nov-26	03-Nov-25	09-Nov-25	60,189.71
CO-R09.S02-SD-1	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	25-Jun-26 A	19-Nov-26	30-Nov-25	07-Dec-25	180,967.37
CO-R09.S02-SD-1	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	28-Jun-26 A	19-Nov-26	13-Dec-25	20-Dec-25	80,517.76
CO-R09.S02-SD-1	Testing Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	4	17-Jul-26 A	19-Nov-26	08-Dec-25	11-Dec-25	40,026.06
Potable Water Network		290	30-Jun-26 A	22-Nov-26	11-Nov-25	29-Dec-25	508,588.36
Main Line Sections		17	30-Jun-26 A	22-Nov-26	10-Dec-25	29-Dec-25	255,751.36
CO-R09.S02-PW-1	Pipes Laying and accessories for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	30-Jun-26 A	08-Nov-26	10-Dec-25	18-Dec-25	139,503.53
CO-R09.S02-PW-1	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	01-Jul-26 A	22-Nov-26	21-Dec-25	29-Dec-25	116,247.83
Valve Chamber		6	04-Nov-26	10-Nov-26	11-Nov-25	17-Nov-25	89,903.16
CO-R09.S02-PW-2	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 09]-[SW-2]	6	04-Nov-26	10-Nov-26	11-Nov-25	17-Nov-25	89,903.16
Fire Hydrant		16	04-Nov-26	22-Nov-26	11-Nov-25	29-Dec-25	162,933.84
CO-R09.S02-PW-1	Excavation Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	04-Nov-26	09-Nov-26	11-Nov-25	16-Nov-25	23,276.12
CO-R09.S02-PW-1	Installation Works for Fire Hydrant of Potable Water Network-[Road 09]-[SW-2]	6	10-Nov-26	16-Nov-26	17-Dec-25	23-Dec-25	108,622.90

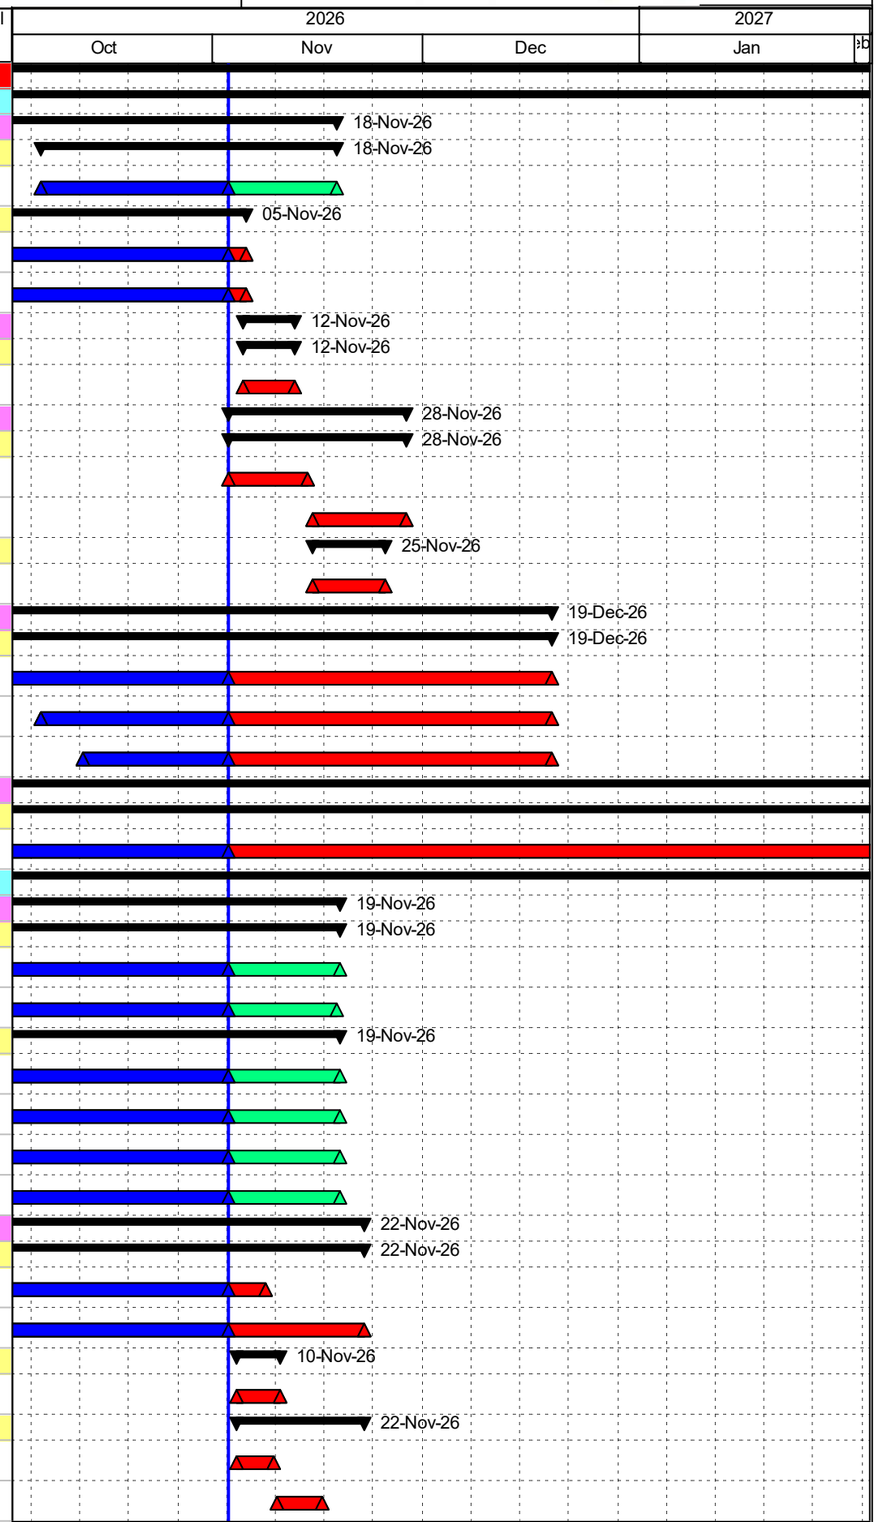


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R09.S02-PW-1	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	17-Nov-26	22-Nov-26	24-Dec-25	29-Dec-25	31,034.82
Street Lighting Network		9	23-Nov-26	02-Dec-26	30-Dec-25	08-Jan-26	5,849.15
Lighting Poles Works		9	23-Nov-26	02-Dec-26	30-Dec-25	08-Jan-26	5,849.15
CO-R09.S02-SL-10	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	9	23-Nov-26	02-Dec-26	30-Dec-25	08-Jan-26	5,849.15
Road Works		12	10-Jun-26 A	28-Mar-27	15-Jul-26	28-Jul-26	760,477.73
Pre-Bituminous Construction		12	10-Jun-26 A	28-Mar-27	15-Jul-26	28-Jul-26	760,477.73
CO-R09.S02-RD-P	Capping and Subgrade Layer for Road Works-[Road 09]-[SW-2]	12	10-Jun-26 A	28-Mar-27	15-Jul-26	28-Jul-26	760,477.73
Road 10 Local 2 (2352 LM)		263	21-Jun-26 A	14-Feb-27	19-Oct-25	08-Aug-26	4,017,372.61
SW-3		232	22-Aug-26 A	30-Jan-27	19-Oct-25	03-Aug-26	2,365,955.91
SW_3-East		232	10-Sep-26 A	30-Jan-27	19-Oct-25	30-Mar-26	1,236,412.75
Potable Water Network		15	03-Nov-26	19-Nov-26	19-Oct-25	04-Nov-25	85,346.78
Fire Hydrant		15	03-Nov-26	19-Nov-26	19-Oct-25	04-Nov-25	85,346.78
CO-R10.S03-ES-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	03-Nov-26	09-Nov-26	19-Oct-25	25-Oct-25	7,758.71
CO-R10.S03-ES-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	10-Nov-26	16-Nov-26	26-Oct-25	01-Nov-25	54,311.96
CO-R10.S03-ES-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	14-Nov-26	19-Nov-26	29-Oct-25	04-Nov-25	23,276.12
Irrigation Network		2	03-Nov-26	04-Nov-26	22-Nov-25	23-Nov-25	685,447.64
Main Line Pipes		2	03-Nov-26	04-Nov-26	22-Nov-25	23-Nov-25	685,447.64
CO-R10.S03-ES-I	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-3]	2	03-Nov-26	04-Nov-26	22-Nov-25	23-Nov-25	685,447.64
Street Lighting Network		33	03-Nov-26	10-Dec-26	02-Dec-25	16-Feb-26	84,226.58
Lighting Poles Works		33	03-Nov-26	10-Dec-26	02-Dec-25	16-Feb-26	84,226.58
CO-R10.S03-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	03-Nov-26	16-Nov-26	02-Dec-25	15-Dec-25	1,949.38
CO-R10.S03-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	09-Nov-26	22-Nov-26	08-Dec-25	21-Dec-25	12,670.44
CO-R10.S03-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	15-Nov-26	05-Dec-26	14-Dec-25	03-Jan-26	35,096.96
CO-R10.S03-ES-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	21-Nov-26	10-Dec-26	26-Jan-26	16-Feb-26	20,861.09
CO-R10.S03-ES-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	22-Nov-26	05-Dec-26	27-Jan-26	10-Feb-26	13,648.70
Road Works		18	10-Sep-26 A	30-Jan-27	07-Mar-26	30-Mar-26	381,391.75
Pre-Bituminous Construction		18	10-Sep-26 A	30-Jan-27	07-Mar-26	30-Mar-26	381,391.75
CO-R10.S03-ES-F	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	18	10-Sep-26 A	30-Jan-27	07-Mar-26	30-Mar-26	381,391.75
SW_3-West		122	22-Aug-26 A	25-Jan-27	08-Jan-26	03-Aug-26	1,129,543.16
Potable Water Network		15	03-Nov-26	19-Nov-26	08-Jan-26	25-Jan-26	85,346.78
Fire Hydrant		15	03-Nov-26	19-Nov-26	08-Jan-26	25-Jan-26	85,346.78
CO-R10.S03-WE-I	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	03-Nov-26	09-Nov-26	08-Jan-26	14-Jan-26	7,758.71
CO-R10.S03-WE-I	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	10-Nov-26	16-Nov-26	15-Jan-26	21-Jan-26	54,311.96
CO-R10.S03-WE-I	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	14-Nov-26	19-Nov-26	19-Jan-26	25-Jan-26	23,276.12
Irrigation Network		2	03-Nov-26	04-Nov-26	11-Feb-26	12-Feb-26	578,578.05
Main Line Pipes		2	03-Nov-26	04-Nov-26	11-Feb-26	12-Feb-26	578,578.05
CO-R10.S03-WE-I	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-3]	2	03-Nov-26	04-Nov-26	11-Feb-26	12-Feb-26	578,578.05
Street Lighting Network		33	03-Nov-26	10-Dec-26	22-Feb-26	04-Apr-26	84,226.58
Lighting Poles Works		33	03-Nov-26	10-Dec-26	22-Feb-26	04-Apr-26	84,226.58
CO-R10.S03-WE-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	03-Nov-26	16-Nov-26	22-Feb-26	07-Mar-26	1,949.38
CO-R10.S03-WE-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	09-Nov-26	22-Nov-26	28-Feb-26	12-Mar-26	12,670.44
CO-R10.S03-WE-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	15-Nov-26	05-Dec-26	05-Mar-26	29-Mar-26	35,096.96
CO-R10.S03-WE-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	21-Nov-26	10-Dec-26	11-Mar-26	04-Apr-26	20,861.09
CO-R10.S03-WE-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	22-Nov-26	05-Dec-26	12-Mar-26	29-Mar-26	13,648.70

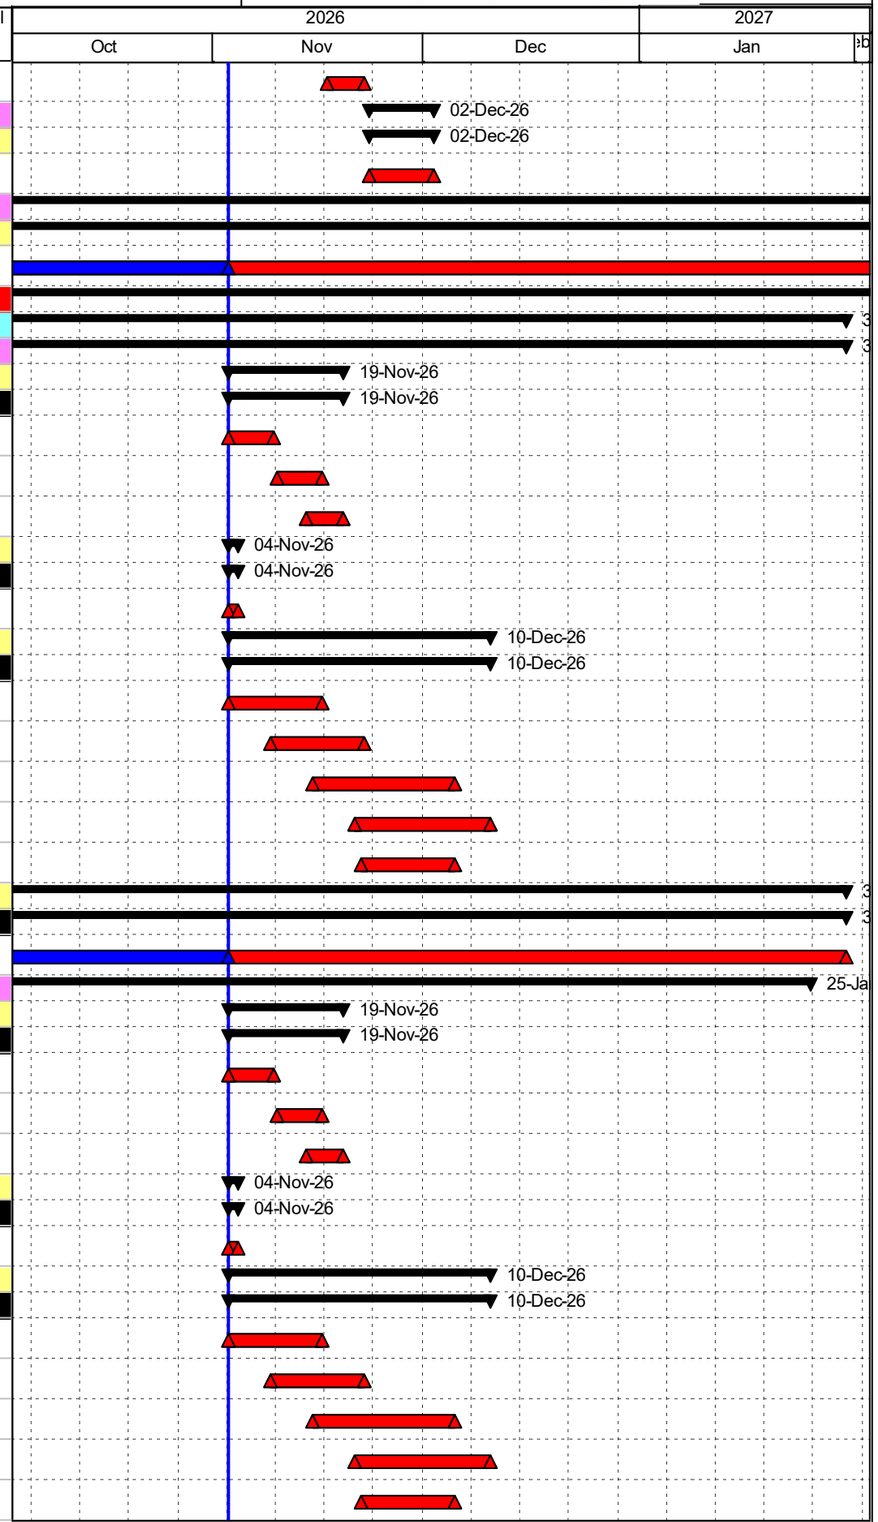

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Road Works		12	22-Aug-26 A	25-Jan-27	21-Jul-26	03-Aug-26	381,391.75
Pre-Bituminous Construction		12	22-Aug-26 A	25-Jan-27	21-Jul-26	03-Aug-26	381,391.75
CO-R10.S03-WE-I	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	12	22-Aug-26 A	25-Jan-27	21-Jul-26	03-Aug-26	381,391.75
SW-4		263	21-Jun-26 A	14-Feb-27	17-Jan-26	08-Aug-26	1,651,416.70
SW_4-East		111	20-Sep-26 A	07-Feb-27	19-Jan-26	08-Aug-26	472,114.89
Potable Water Network		21	03-Nov-26	26-Nov-26	19-Jan-26	11-Feb-26	0.00
Fire Hydrant		21	03-Nov-26	26-Nov-26	19-Jan-26	11-Feb-26	0.00
CO-R10.S04-ES-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	03-Nov-26	10-Nov-26	19-Jan-26	26-Jan-26	0.00
CO-R10.S04-ES-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	11-Nov-26	18-Nov-26	27-Jan-26	03-Feb-26	0.00
CO-R10.S04-ES-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	19-Nov-26	26-Nov-26	04-Feb-26	11-Feb-26	0.00
Irrigation Network		4	03-Nov-26	07-Nov-26	28-Feb-26	03-Mar-26	41,006.36
Main Line Pipes		4	03-Nov-26	07-Nov-26	28-Feb-26	03-Mar-26	41,006.36
CO-R10.S04-ES-I	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-4]	4	03-Nov-26	07-Nov-26	28-Feb-26	03-Mar-26	41,006.36
Street Lighting Network		24	03-Nov-26	30-Nov-26	10-Mar-26	09-Apr-26	49,716.78
Lighting Poles Works		17	03-Nov-26	22-Nov-26	10-Mar-26	01-Apr-26	49,716.78
CO-R10.S04-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	03-Nov-26	10-Nov-26	10-Mar-26	17-Mar-26	1,949.38
CO-R10.S04-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	7	09-Nov-26	16-Nov-26	16-Mar-26	26-Mar-26	12,670.44
CO-R10.S04-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	15-Nov-26	22-Nov-26	25-Mar-26	01-Apr-26	35,096.96
Cabling Works		7	23-Nov-26	30-Nov-26	02-Apr-26	09-Apr-26	0.00
CO-R10.S04-ES-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	7	23-Nov-26	30-Nov-26	02-Apr-26	09-Apr-26	0.00
Road Works		14	20-Sep-26 A	07-Feb-27	23-Jul-26	08-Aug-26	381,391.75
Pre-Bituminous Construction		14	20-Sep-26 A	07-Feb-27	23-Jul-26	08-Aug-26	381,391.75
CO-R10.S04-ES-F	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	14	20-Sep-26 A	07-Feb-27	23-Jul-26	08-Aug-26	381,391.75
SW_4-West		263	21-Jun-26 A	14-Feb-27	17-Jan-26	05-Aug-26	1,179,301.81
Potable Water Network		252	21-Jun-26 A	28-Nov-26	17-Jan-26	11-Feb-26	576,113.00
Valve Chamber		245	21-Jun-26 A	19-Nov-26	17-Jan-26	02-Feb-26	576,113.00
CO-R10.S04-WE-I	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	21-Jun-26 A	16-Nov-26	29-Jan-26	29-Jan-26	493,951.19
CO-R10.S04-WE-I	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	04-Nov-26	07-Nov-26	17-Jan-26	19-Jan-26	13,294.37
CO-R10.S04-WE-I	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	6	08-Nov-26	14-Nov-26	20-Jan-26	26-Jan-26	33,415.13
CO-R10.S04-WE-I	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	2	15-Nov-26	16-Nov-26	27-Jan-26	28-Jan-26	17,726.16
CO-R10.S04-WE-I	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	17-Nov-26	19-Nov-26	31-Jan-26	02-Feb-26	17,726.16
Fire Hydrant		21	04-Nov-26	28-Nov-26	19-Jan-26	11-Feb-26	0.00
CO-R10.S04-WE-I	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	04-Nov-26	11-Nov-26	19-Jan-26	26-Jan-26	0.00
CO-R10.S04-WE-I	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	12-Nov-26	19-Nov-26	27-Jan-26	03-Feb-26	0.00
CO-R10.S04-WE-I	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	21-Nov-26	28-Nov-26	04-Feb-26	11-Feb-26	0.00
Irrigation Network		223	13-Oct-26 A	08-Nov-26	12-Feb-26	08-Mar-26	172,080.29
Main Line Pipes		223	13-Oct-26 A	08-Nov-26	12-Feb-26	08-Mar-26	172,080.29
CO-R10.S04-WE-I	Trench Excavation and Bedding Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	6	13-Oct-26 A	04-Nov-26	12-Feb-26	18-Feb-26	30,929.64
CO-R10.S04-WE-I	Pipes Laying Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	7	15-Oct-26 A	04-Nov-26	19-Feb-26	26-Feb-26	92,941.08
CO-R10.S04-WE-I	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	5	17-Oct-26 A	08-Nov-26	03-Mar-26	08-Mar-26	15,540.90
CO-R10.S04-WE-I	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-4]	3	05-Nov-26	08-Nov-26	28-Feb-26	02-Mar-26	32,668.66
Street Lighting Network		28	09-Nov-26	10-Dec-26	09-Mar-26	13-Apr-26	49,716.78
Lighting Poles Works		28	09-Nov-26	10-Dec-26	09-Mar-26	13-Apr-26	49,716.78

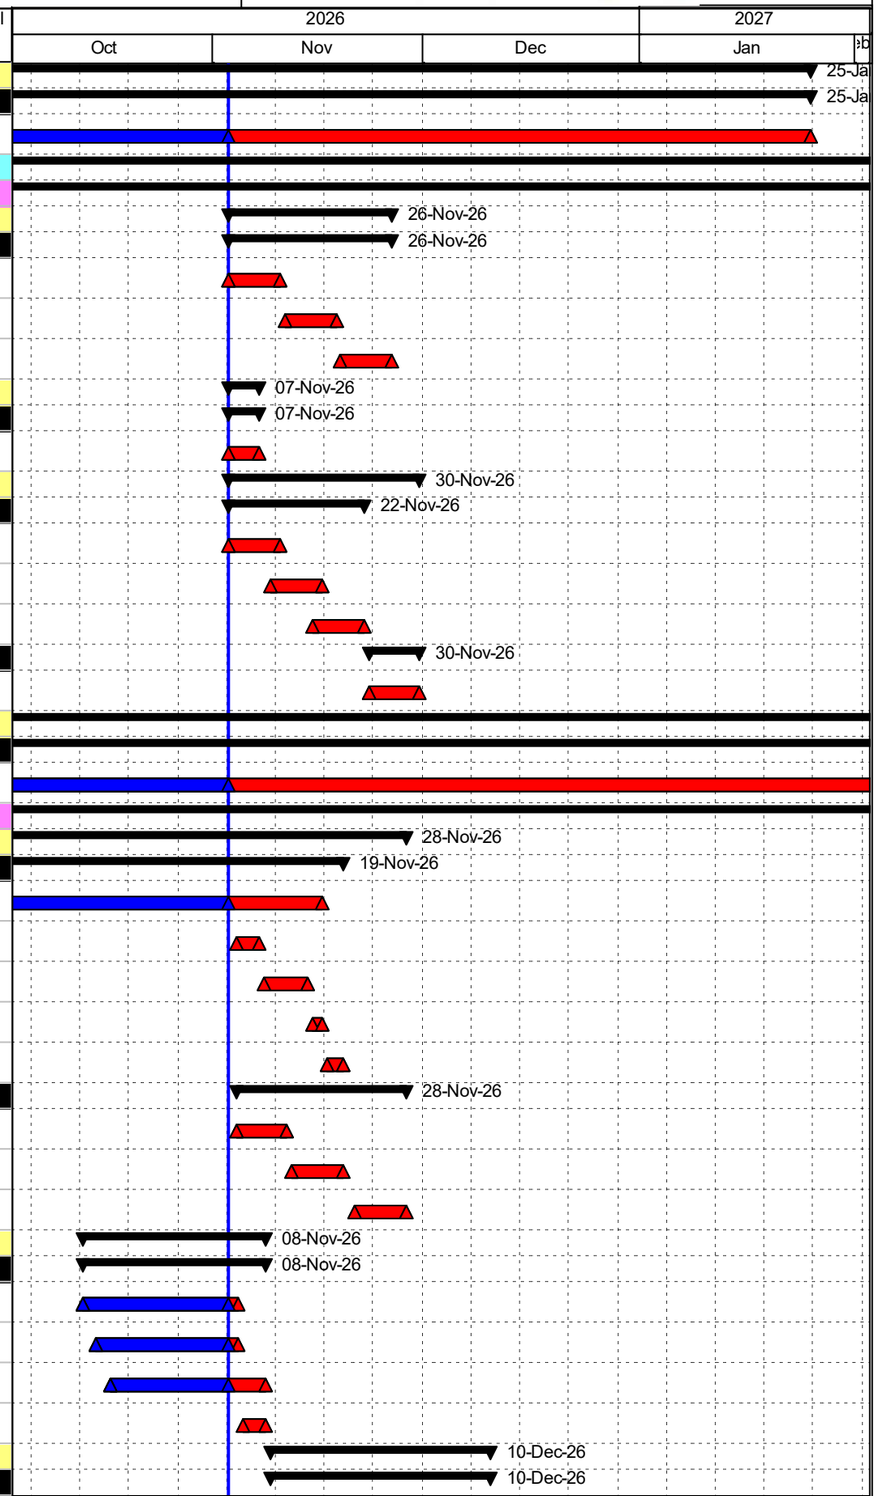

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R10.S04-WE-(	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	10	09-Nov-26	19-Nov-26	09-Mar-26	19-Mar-26	1,949.38
CO-R10.S04-WE-(	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	10	15-Nov-26	25-Nov-26	15-Mar-26	29-Mar-26	12,670.44
CO-R10.S04-WE-(	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	18	21-Nov-26	10-Dec-26	24-Mar-26	13-Apr-26	35,096.96
Road Works		12	30-Jul-26 A	14-Feb-27	23-Jul-26	05-Aug-26	381,391.75
Pre-Bituminous Construction		12	30-Jul-26 A	14-Feb-27	23-Jul-26	05-Aug-26	381,391.75
CO-R10.S04-WE-(	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	12	30-Jul-26 A	14-Feb-27	23-Jul-26	05-Aug-26	381,391.75
Road 11 Local 1 (670 LM)		275	25-Apr-26 A	28-Nov-26	03-Jan-26	19-Jul-26	232,569.19
SW_5		265	25-Apr-26 A	16-Nov-26	03-Jan-26	21-Jan-26	127,356.94
Irrigation Network		265	25-Apr-26 A	16-Nov-26	03-Jan-26	21-Jan-26	127,356.94
Main Line Pipes		265	25-Apr-26 A	16-Nov-26	03-Jan-26	21-Jan-26	127,356.94
CO-R11.S05-IR-11(	Pipes Laying Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	25-Apr-26 A	04-Nov-26	03-Jan-26	10-Jan-26	54,240.48
CO-R11.S05-IR-12(	Installation Works for Main Line Valves of Irrigation Network-[Road 11]-[SW-5]	3	05-Nov-26	08-Nov-26	11-Jan-26	13-Jan-26	64,050.68
CO-R11.S05-IR-13(	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	09-Nov-26	16-Nov-26	14-Jan-26	21-Jan-26	9,065.78
SW_6		22	03-Nov-26	28-Nov-26	28-Jan-26	19-Jul-26	105,212.26
Potable Water Network		21	03-Nov-26	26-Nov-26	28-Jan-26	28-Feb-26	68,250.67
Valve Chamber		6	03-Nov-26	09-Nov-26	28-Jan-26	03-Feb-26	21,698.44
CO-R11.S06-PW-2(	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 11]-[SW-6]	6	03-Nov-26	09-Nov-26	28-Jan-26	03-Feb-26	21,698.44
Fire Hydrant		21	03-Nov-26	26-Nov-26	04-Feb-26	28-Feb-26	46,552.23
CO-R11.S06-PW-1(	Excavation Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	03-Nov-26	10-Nov-26	04-Feb-26	11-Feb-26	7,758.71
CO-R11.S06-PW-1(	Installation Works for Fire Hydrant of Potable Water Network-[Road 11]-[SW-6]	7	11-Nov-26	18-Nov-26	12-Feb-26	19-Feb-26	31,034.82
CO-R11.S06-PW-1(	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	19-Nov-26	26-Nov-26	21-Feb-26	28-Feb-26	7,758.71
Street Lighting Network		22	03-Nov-26	28-Nov-26	19-May-26	19-Jul-26	36,961.58
Lighting Poles Works		22	03-Nov-26	28-Nov-26	24-Jun-26	19-Jul-26	31,196.16
CO-R11.S06-SL-21	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	15	03-Nov-26	19-Nov-26	24-Jun-26	11-Jul-26	15,598.08
CO-R11.S06-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	7	21-Nov-26	28-Nov-26	12-Jul-26	19-Jul-26	15,598.08
Cabling Works		10	03-Nov-26	14-Nov-26	19-May-26	03-Jun-26	5,765.42
CO-R11.S06-SL-16	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 11]-[SW-6]	10	03-Nov-26	14-Nov-26	19-May-26	03-Jun-26	5,765.42
Road 14 Local 1 (584 LM)		24	03-Nov-26	30-Nov-26	02-Aug-25	01-Jul-26	179,080.28
SW_7		24	03-Nov-26	30-Nov-26	02-Aug-25	11-Jun-26	87,802.65
Irrigation Network		7	03-Nov-26	10-Nov-26	31-Dec-25	07-Jan-26	74,779.91
Main Line Pipes		7	03-Nov-26	10-Nov-26	31-Dec-25	07-Jan-26	74,779.91
CO-R14.S07-IR-12(	Installation Works for Main Line Valves of Irrigation Network-[Road 14]-[SW-7]	7	03-Nov-26	10-Nov-26	31-Dec-25	07-Jan-26	74,779.91
Street Lighting Network		24	03-Nov-26	30-Nov-26	02-Aug-25	11-Jun-26	13,022.74
Lighting Poles Works		18	03-Nov-26	23-Nov-26	18-May-26	11-Jun-26	13,022.74
CO-R14.S07-SL-13	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 14]-[SW-7]	18	03-Nov-26	23-Nov-26	18-May-26	11-Jun-26	10,864.03
CO-R14.S07-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	5	03-Nov-26	08-Nov-26	07-Jun-26	11-Jun-26	2,158.71
Distrubution Panel Boards		24	03-Nov-26	30-Nov-26	02-Aug-25	28-Aug-25	0.00
CO-R14.S07-SL-17	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	03-Nov-26	23-Nov-26	02-Aug-25	21-Aug-25	0.00
CO-R14.S07-SL-18	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 14]-[SW-7]	18	07-Nov-26	26-Nov-26	05-Aug-25	25-Aug-25	0.00
CO-R14.S07-SL-22	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 14]-[SW-7]	18	07-Nov-26	26-Nov-26	05-Aug-25	25-Aug-25	0.00
CO-R14.S07-SL-19	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	10-Nov-26	30-Nov-26	09-Aug-25	28-Aug-25	0.00
SW_8		21	03-Nov-26	26-Nov-26	26-Feb-26	01-Jul-26	91,277.63
Potable Water Network		21	03-Nov-26	26-Nov-26	26-Feb-26	25-Mar-26	69,829.37
Fire Hydrant		21	03-Nov-26	26-Nov-26	26-Feb-26	25-Mar-26	69,829.37

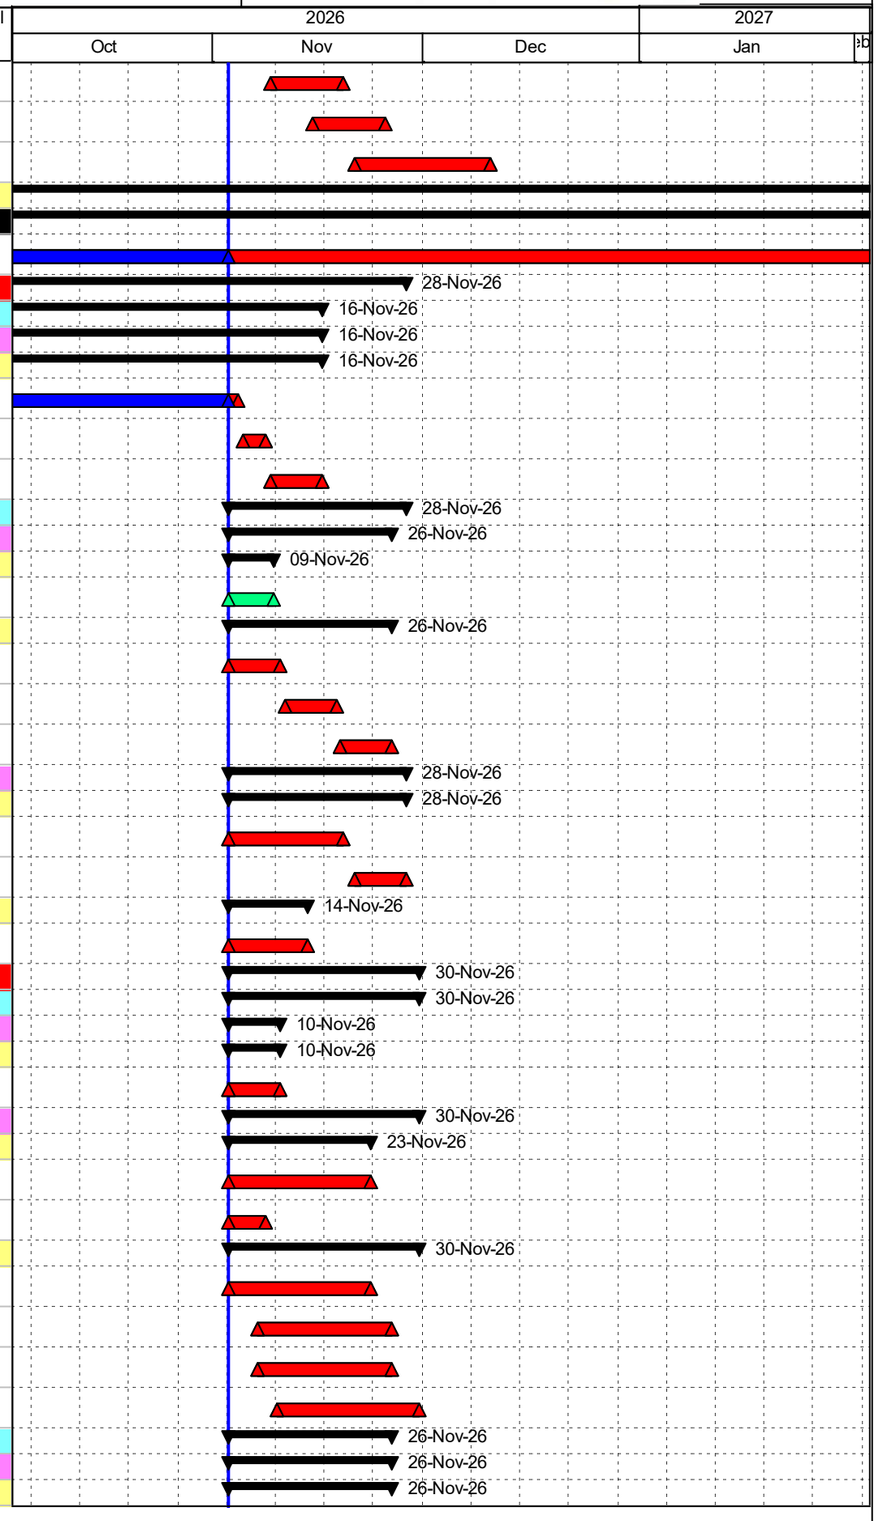


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R14.S08-PW-1	Excavation Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	03-Nov-26	10-Nov-26	26-Feb-26	05-Mar-26	7,758.71
CO-R14.S08-PW-1	Installation Works for Fire Hydrant of Potable Water Network-[Road 14]-[SW-8]	7	11-Nov-26	18-Nov-26	07-Mar-26	14-Mar-26	54,311.96
CO-R14.S08-PW-1	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	19-Nov-26	26-Nov-26	15-Mar-26	25-Mar-26	7,758.71
Street Lighting Network		7	03-Nov-26	10-Nov-26	24-Jun-26	01-Jul-26	21,448.26
Lighting Poles Works		7	03-Nov-26	10-Nov-26	24-Jun-26	01-Jul-26	21,448.26
CO-R14.S08-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-8]	7	03-Nov-26	10-Nov-26	24-Jun-26	01-Jul-26	21,448.26
Road 15 Local 1 (556 LM)		24	03-Nov-26	30-Nov-26	02-Jun-25	31-Mar-26	107,160.61
SW_10		24	03-Nov-26	30-Nov-26	02-Jun-25	31-Mar-26	107,160.61
Street Lighting Network		24	03-Nov-26	30-Nov-26	02-Jun-25	02-Feb-26	38,909.94
Lighting Poles Works		5	03-Nov-26	08-Nov-26	27-Jan-26	02-Feb-26	13,648.70
CO-R15.S10-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 15]-[SW-10]	5	03-Nov-26	08-Nov-26	27-Jan-26	02-Feb-26	13,648.70
Distrubution Panel Boards		24	03-Nov-26	30-Nov-26	02-Jun-25	03-Jul-25	25,261.23
CO-R15.S10-SL-17	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	03-Nov-26	23-Nov-26	02-Jun-25	26-Jun-25	0.00
CO-R15.S10-SL-18	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 15]-[SW-10]	18	07-Nov-26	26-Nov-26	10-Jun-25	30-Jun-25	0.00
CO-R15.S10-SL-22	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 15]-[SW-10]	18	07-Nov-26	26-Nov-26	10-Jun-25	30-Jun-25	25,261.23
CO-R15.S10-SL-19	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	10-Nov-26	30-Nov-26	14-Jun-25	03-Jul-25	0.00
Potable Water Network		18	03-Nov-26	23-Nov-26	08-Mar-26	31-Mar-26	68,250.67
Valve Chamber		6	03-Nov-26	09-Nov-26	11-Mar-26	17-Mar-26	21,698.44
CO-R15.S10-PW-2	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 15]-[SW-10]	6	03-Nov-26	09-Nov-26	11-Mar-26	17-Mar-26	21,698.44
Fire Hydrant		18	03-Nov-26	23-Nov-26	08-Mar-26	31-Mar-26	46,552.23
CO-R15.S10-PW-1	Excavation Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	03-Nov-26	09-Nov-26	08-Mar-26	14-Mar-26	7,758.71
CO-R15.S10-PW-1	Installation Works for Fire Hydrant of Potable Water Network-[Road 15]-[SW-10]	6	10-Nov-26	16-Nov-26	15-Mar-26	24-Mar-26	31,034.82
CO-R15.S10-PW-1	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	17-Nov-26	23-Nov-26	25-Mar-26	31-Mar-26	7,758.71
Road 16 Local 1 (527 LM)		24	03-Nov-26	30-Nov-26	29-Mar-26	18-Apr-26	46,552.23
SW_12		24	03-Nov-26	30-Nov-26	29-Mar-26	18-Apr-26	46,552.23
Potable Water Network		24	03-Nov-26	30-Nov-26	29-Mar-26	18-Apr-26	46,552.23
Fire Hydrant		24	03-Nov-26	30-Nov-26	29-Mar-26	18-Apr-26	46,552.23
CO-R16.S12-PW-1	Excavation Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	03-Nov-26	09-Nov-26	29-Mar-26	04-Apr-26	7,758.71
CO-R16.S12-PW-1	Installation Works for Fire Hydrant of Potable Water Network-[Road 16]-[SW-12]	6	17-Nov-26	23-Nov-26	05-Apr-26	11-Apr-26	31,034.82
CO-R16.S12-PW-1	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	24-Nov-26	30-Nov-26	12-Apr-26	18-Apr-26	7,758.71
Road 17 Local 1 (500 LM)		24	03-Nov-26	30-Nov-26	16-Apr-25	01-Sep-26	125,660.81
SW_14		24	03-Nov-26	30-Nov-26	16-Apr-25	01-Sep-26	125,660.81
Street Lighting Network		24	03-Nov-26	30-Nov-26	16-Apr-25	14-Dec-25	64,088.46
Lighting Poles Works		5	03-Nov-26	08-Nov-26	08-Dec-25	14-Dec-25	25,348.03
CO-R17.S14-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 17]-[SW-14]	5	03-Nov-26	08-Nov-26	08-Dec-25	14-Dec-25	25,348.03
Distrubution Panel Boards		24	03-Nov-26	30-Nov-26	16-Apr-25	13-May-25	38,740.43
CO-R17.S14-SL-17	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	03-Nov-26	23-Nov-26	16-Apr-25	06-May-25	0.00
CO-R17.S14-SL-18	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 17]-[SW-14]	18	07-Nov-26	26-Nov-26	20-Apr-25	10-May-25	0.00
CO-R17.S14-SL-22	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 17]-[SW-14]	18	07-Nov-26	26-Nov-26	20-Apr-25	10-May-25	38,740.43
CO-R17.S14-SL-19	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	10-Nov-26	30-Nov-26	23-Apr-25	13-May-25	0.00
Potable Water Network		24	03-Nov-26	30-Nov-26	21-Apr-26	04-May-26	53,878.99
Valve Chamber		6	03-Nov-26	09-Nov-26	23-Apr-26	30-Apr-26	27,122.79
CO-R17.S14-PW-2	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 17]-[SW-14]	6	03-Nov-26	09-Nov-26	23-Apr-26	30-Apr-26	27,122.79
Fire Hydrant		24	03-Nov-26	30-Nov-26	21-Apr-26	04-May-26	26,756.20

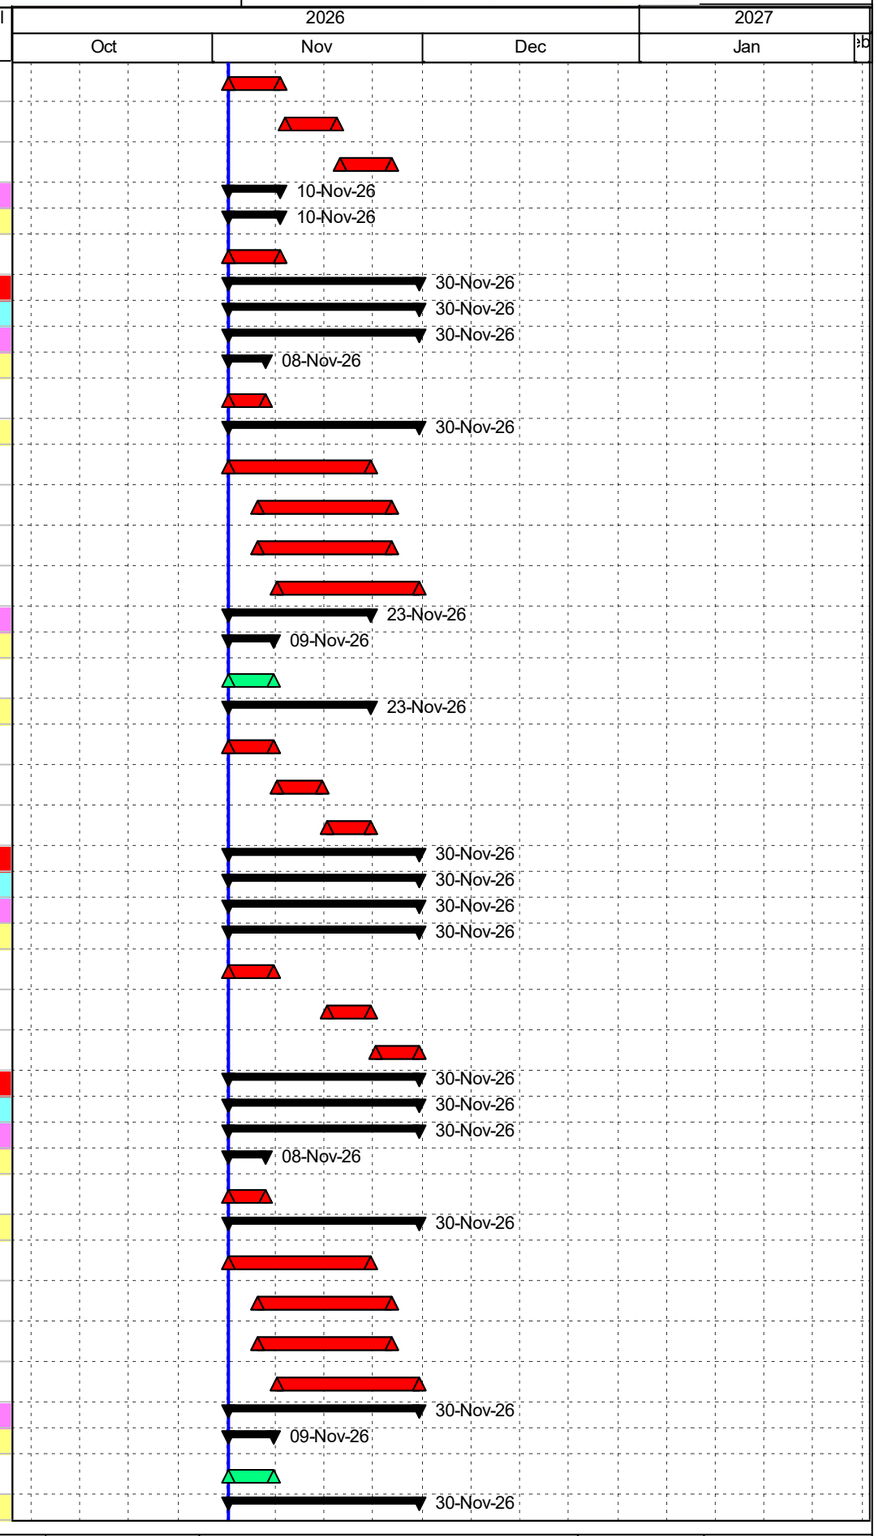


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R17.S14-PW-1	Excavation Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	03-Nov-26	09-Nov-26	21-Apr-26	27-Apr-26	3,480.08
CO-R17.S14-PW-1	Installation Works for Fire Hydrant of Potable Water Network-[Road 17]-[SW-14]	6	24-Nov-26	30-Nov-26	28-Apr-26	04-May-26	23,276.12
Telecom Network		21	03-Nov-26	26-Nov-26	09-Aug-26	01-Sep-26	7,693.35
Manholes Works		21	03-Nov-26	26-Nov-26	09-Aug-26	01-Sep-26	7,693.35
CO-R17.S14-TE-14	Excavation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	03-Nov-26	10-Nov-26	09-Aug-26	16-Aug-26	641.28
CO-R17.S14-TE-15	Installation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	11-Nov-26	18-Nov-26	17-Aug-26	24-Aug-26	6,410.79
CO-R17.S14-TE-16	Backfilling Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	19-Nov-26	26-Nov-26	25-Aug-26	01-Sep-26	641.28
Road 18 Local 1 (479 LM)		35	03-Nov-26	13-Dec-26	19-Mar-25	27-Nov-25	147,037.58
SW_15		7	19-Nov-26	26-Nov-26	11-Aug-25	18-Aug-25	52,670.97
Irrigation Network		7	19-Nov-26	26-Nov-26	11-Aug-25	18-Aug-25	52,670.97
Main Line Pipes		7	19-Nov-26	26-Nov-26	11-Aug-25	18-Aug-25	52,670.97
CO-R18.S15-IR-16	Installation Works for Main Line Valves of Irrigation Network-[Road 18]-[SW-15]	7	19-Nov-26	26-Nov-26	11-Aug-25	18-Aug-25	52,670.97
SW_16		35	03-Nov-26	13-Dec-26	19-Mar-25	27-Nov-25	94,366.61
Street Lighting Network		35	03-Nov-26	13-Dec-26	19-Mar-25	27-Nov-25	54,070.97
Lighting Poles Works		35	03-Nov-26	13-Dec-26	08-Nov-25	27-Nov-25	30,106.60
CO-R18.S16-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 18]-[SW-16]	5	03-Nov-26	08-Nov-26	22-Nov-25	27-Nov-25	11,699.33
CO-R18.S16-SL-13	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 18]-[SW-16]	18	23-Nov-26	13-Dec-26	08-Nov-25	27-Nov-25	18,407.27
Distrubution Panel Boards		24	03-Nov-26	30-Nov-26	19-Mar-25	20-Apr-25	23,964.37
CO-R18.S16-SL-17	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	03-Nov-26	23-Nov-26	19-Mar-25	13-Apr-25	0.00
CO-R18.S16-SL-18	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 18]-[SW-16]	18	07-Nov-26	26-Nov-26	23-Mar-25	16-Apr-25	0.00
CO-R18.S16-SL-22	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 18]-[SW-16]	18	07-Nov-26	26-Nov-26	23-Mar-25	16-Apr-25	23,964.37
CO-R18.S16-SL-19	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	10-Nov-26	30-Nov-26	26-Mar-25	20-Apr-25	0.00
Potable Water Network		18	03-Nov-26	23-Nov-26	23-Aug-25	11-Sep-25	40,295.64
Valve Chamber		6	03-Nov-26	09-Nov-26	25-Aug-25	01-Sep-25	27,122.79
CO-R18.S16-PW-3	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 18]-[SW-16]	6	03-Nov-26	09-Nov-26	25-Aug-25	01-Sep-25	27,122.79
Fire Hydrant		18	03-Nov-26	23-Nov-26	23-Aug-25	11-Sep-25	13,172.85
CO-R18.S16-PW-2	Excavation Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	03-Nov-26	09-Nov-26	23-Aug-25	28-Aug-25	2,320.06
CO-R18.S16-PW-2	Installation Works for Fire Hydrant of Potable Water Network-[Road 18]-[SW-16]	6	10-Nov-26	16-Nov-26	30-Aug-25	04-Sep-25	7,758.71
CO-R18.S16-PW-2	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	17-Nov-26	23-Nov-26	06-Sep-25	11-Sep-25	3,094.09
Finishes for Infrastructure Networks		112	01-Jun-26 A	31-Mar-27	19-Jul-26	04-Oct-26	1,472,543.71
Phase 2 Block "J"		112	01-Jun-26 A	31-Mar-27	19-Jul-26	04-Oct-26	1,472,543.71
Road 09 Local 2 (2278 LM)		12	01-Jun-26 A	31-Mar-27	19-Jul-26	01-Aug-26	301,477.49
Sewage Network		12	01-Jun-26 A	31-Mar-27	19-Jul-26	01-Aug-26	301,477.49
Testing and Finishes		12	01-Jun-26 A	31-Mar-27	19-Jul-26	01-Aug-26	301,477.49
CO-R09-SW-TF-10	Final Testing For Main Line of Sewage Network-[Road 09]	12	01-Jun-26 A	31-Mar-27	19-Jul-26	01-Aug-26	301,477.49
Road 10 Local 2 (2352 LM)		84	17-Jun-26 A	13-Mar-27	04-Aug-26	16-Sep-26	791,291.98
Storm Drainage Network		35	17-Jun-26 A	13-Mar-27	04-Aug-26	13-Sep-26	791,291.98
Testing and Finishes		35	17-Jun-26 A	13-Mar-27	04-Aug-26	13-Sep-26	791,291.98
CO-R10-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 10]	16	17-Jun-26 A	17-Feb-27	04-Aug-26	22-Aug-26	40,492.72
CO-R10-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	12	18-Jun-26 A	13-Mar-27	26-Aug-26	08-Sep-26	710,306.54
CO-R10-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	16	22-Jun-26 A	13-Mar-27	26-Aug-26	13-Sep-26	40,492.72
Medium Voltage Network		7	03-Nov-26	10-Nov-26	09-Sep-26	16-Sep-26	0.00
Termination and Testing Works		7	03-Nov-26	10-Nov-26	09-Sep-26	16-Sep-26	0.00
CO-R10-MV-TF-140	Termination Works of Medium Voltage Network-[Road 10]	7	03-Nov-26	10-Nov-26	09-Sep-26	16-Sep-26	0.00
Road 11 Local 1 (670 LM)		75	22-Jun-26 A	27-Mar-27	23-Aug-26	03-Oct-26	379,774.24

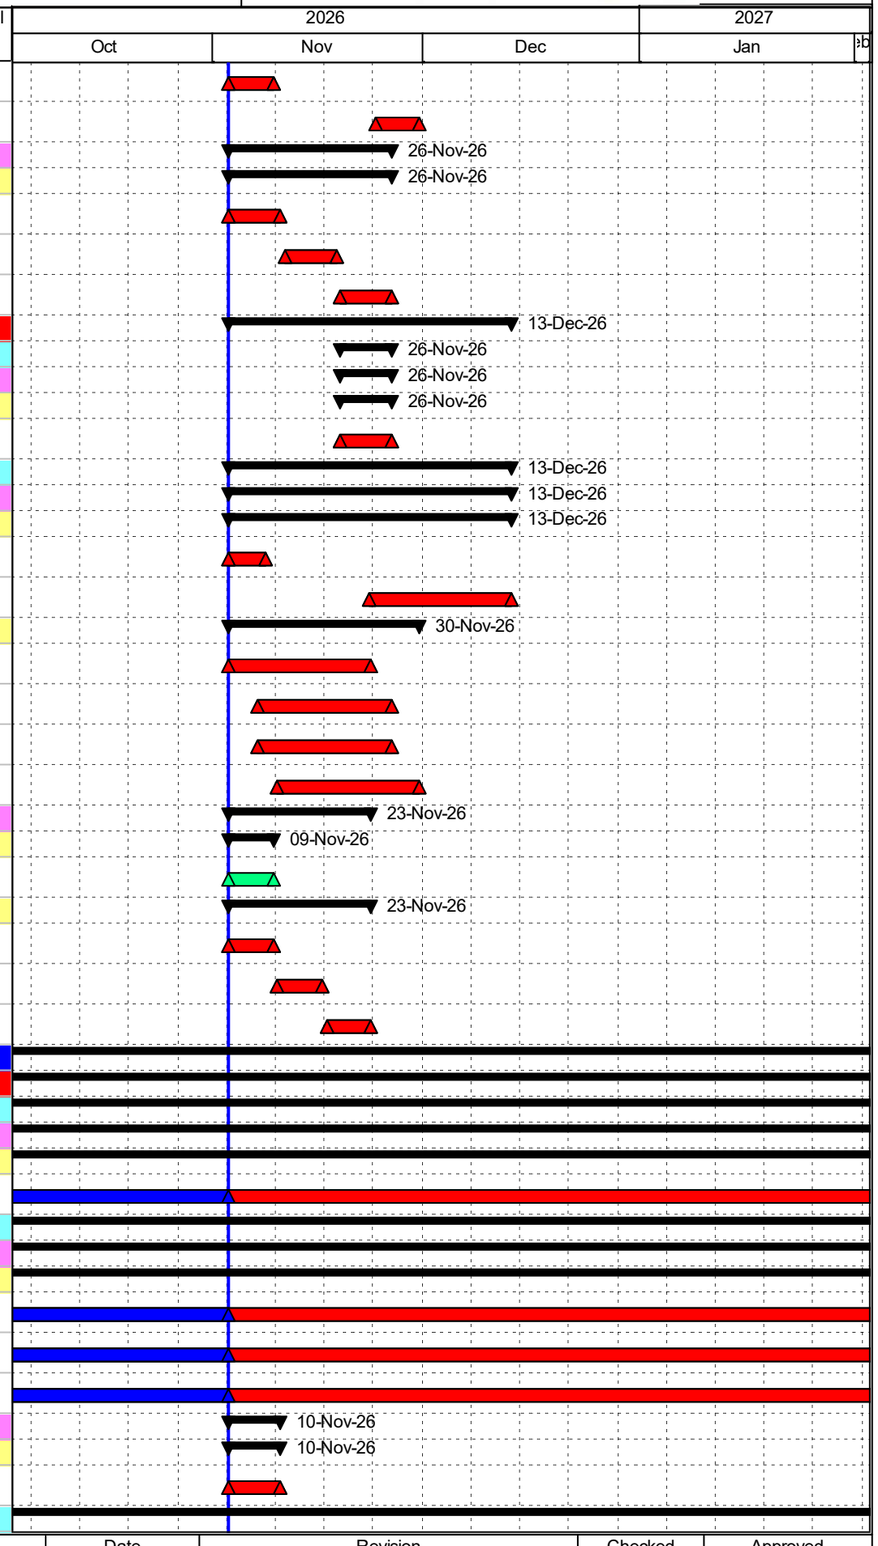


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Update 03-11-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Storm Drainage Network		35	22-Jun-26 A	27-Mar-27	23-Aug-26	03-Oct-26	379,774.24
Testing and Finishes		35	22-Jun-26 A	27-Mar-27	23-Aug-26	03-Oct-26	379,774.24
CO-R11-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	16	22-Jun-26 A	27-Mar-27	14-Sep-26	03-Oct-26	11,913.77
CO-R11-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	12	23-Jun-26 A	27-Mar-27	09-Sep-26	22-Sep-26	355,946.70
CO-R11-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 11]	12	27-Jun-26 A	17-Feb-27	23-Aug-26	05-Sep-26	11,913.77
Medium Voltage Network		7	11-Nov-26	18-Nov-26	17-Sep-26	26-Sep-26	0.00
Termination and Testing Works		7	11-Nov-26	18-Nov-26	17-Sep-26	26-Sep-26	0.00
CO-R11-MV-TF-160	Termination Works of Medium Voltage Network-[Road 11]	7	11-Nov-26	18-Nov-26	17-Sep-26	26-Sep-26	0.00
Road 14 Local 1 (584 LM)		7	19-Nov-26	26-Nov-26	27-Sep-26	04-Oct-26	0.00
Medium Voltage Network		7	19-Nov-26	26-Nov-26	27-Sep-26	04-Oct-26	0.00
Termination and Testing Works		7	19-Nov-26	26-Nov-26	27-Sep-26	04-Oct-26	0.00
CO-R11-MV-TF-180	Termination Works of Medium Voltage Network-[Road 14]	7	19-Nov-26	26-Nov-26	27-Sep-26	04-Oct-26	0.00
Independent Works		210	16-Sep-26 A	10-Dec-26	15-Feb-26	17-Jun-26	224,888.09
Sewage Pump Stations		210	16-Sep-26 A	10-Dec-26	05-Apr-26	17-Jun-26	117,643.75
Sewage Pump Station (PS 06)		210	16-Sep-26 A	10-Dec-26	05-Apr-26	17-Jun-26	117,643.75
Pump Station Main Building		210	16-Sep-26 A	10-Dec-26	05-Apr-26	17-Jun-26	117,545.72
CO-SW-PS7-MB-110	Concrete Works of Superstrucure	30	16-Sep-26 A	05-Nov-26	05-Apr-26	09-May-26	98,005.99
CO-SW-PS7-MB-120	Internal Finishes Works of Superstrucure	30	07-Nov-26	10-Dec-26	10-May-26	17-Jun-26	19,539.73
Motor Control Centre Building		16	07-Nov-26	24-Nov-26	10-May-26	01-Jun-26	98.03
CO-SW-PS7-MCC-10	Excavation Main Bulding	16	07-Nov-26	24-Nov-26	10-May-26	01-Jun-26	98.03
Storm Drainage Ponds		21	03-Nov-26	26-Nov-26	15-Feb-26	10-Mar-26	107,244.35
Storm Drainage Pond (PO-J1)		21	03-Nov-26	26-Nov-26	15-Feb-26	10-Mar-26	8,085.47
CO-SD-PO-K1-110-P1	Finished Grouted Riprap - PART 1	21	03-Nov-26	26-Nov-26	15-Feb-26	10-Mar-26	8,085.47
Storm Drainage Pond (PO-J2)		21	03-Nov-26	26-Nov-26	15-Feb-26	10-Mar-26	99,158.87
CO-SD-PO-K2-100-P1	Excavation & Filling Works - PART 1	21	03-Nov-26	26-Nov-26	15-Feb-26	10-Mar-26	99,158.87
Testing and Comissioning		50	01-Jun-26 A	14-Sep-27	07-Nov-26	03-Jan-27	0.00
Infrastructure Networks		50	01-Jun-26 A	14-Sep-27	07-Nov-26	03-Jan-27	0.00
Irrigation Network		12	05-Jun-26 A	24-May-27	12-Nov-26	25-Nov-26	0.00
T/C-IR	Testing and Commissioning of Irrigation Network	12	05-Jun-26 A	24-May-27	12-Nov-26	25-Nov-26	0.00
Potable Water Network		12	01-Jul-26 A	07-Aug-27	03-Dec-26	16-Dec-26	0.00
T/C-PW	Testing and Commissioning of Potable Water Network	12	01-Jul-26 A	07-Aug-27	03-Dec-26	16-Dec-26	0.00
Sewage Network		12	01-Jun-26 A	19-Jul-27	19-Dec-26	31-Dec-26	0.00
T/C-SW	Testing and Commissioning of Sewage Network	12	01-Jun-26 A	19-Jul-27	19-Dec-26	31-Dec-26	0.00
Storm Drainage Network		10	10-Jun-26 A	28-Jun-27	21-Dec-26	31-Dec-26	0.00
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	10-Jun-26 A	28-Jun-27	21-Dec-26	31-Dec-26	0.00
Street Lighting Network		18	05-Sep-26 A	10-Jul-27	07-Nov-26	26-Nov-26	0.00
T/C-SL	Testing and Commissioning of Street Lighting Network	18	05-Sep-26 A	10-Jul-27	07-Nov-26	26-Nov-26	0.00
Telecom Network		10	05-Sep-26 A	19-Jun-27	10-Nov-26	21-Nov-26	0.00
T/C-TE	Testing and Commissioning of Telecom Network	10	05-Sep-26 A	19-Jun-27	10-Nov-26	21-Nov-26	0.00
Medium Voltage Network		10	05-Sep-26 A	19-Jun-27	22-Nov-26	02-Dec-26	0.00
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	05-Sep-26 A	19-Jun-27	22-Nov-26	02-Dec-26	0.00
Road Works		5	16-Aug-26 A	14-Sep-27	29-Dec-26	03-Jan-27	0.00
T/C-RD	Testing and Commissioning of Road Works	5	16-Aug-26 A	14-Sep-27	29-Dec-26	03-Jan-27	0.00

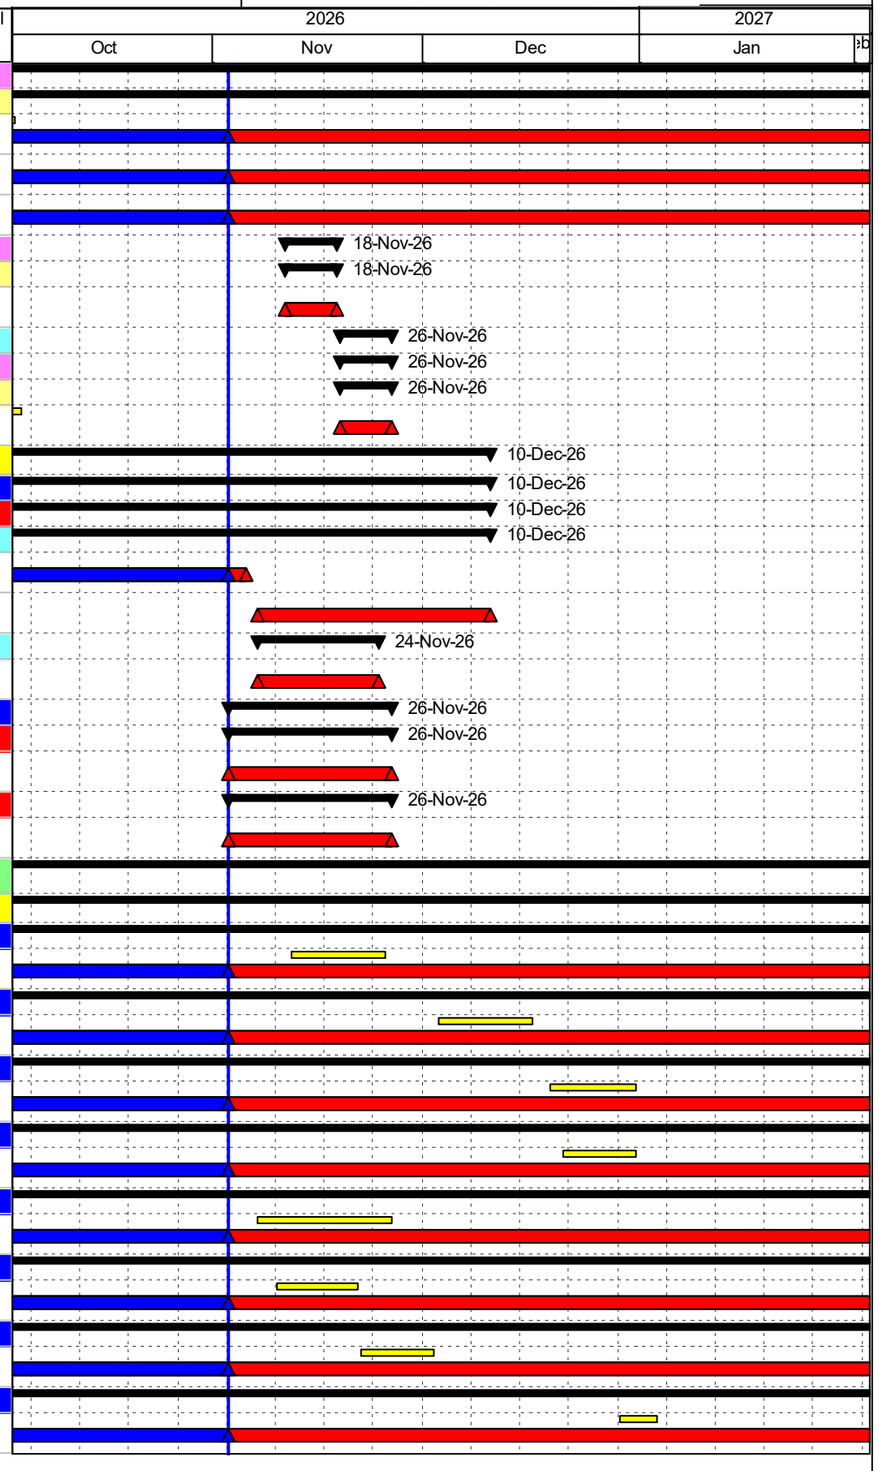

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
