
# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**2 Weeks look ahead schedule**
**D.D 12-10-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005 | Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R R( | 166 | 51.39% | 47.61% | 16-Apr-26 | 02-Dec-26 | 01-Jun-26 A | 14-Feb-27 | 1,005,954.15 | 931,932.63 | 1,957,375.53 | -63 |
| ARAR | | 123 | 53.43% | 46.77% | 27-Jun-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 391,949.80 | 343,117.21 | 733,614.61 | -44 |
| ENGINEERING | | 27 | 0% | 0% | 28-Jun-26 | 21-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| SHOP DRAWINGS | | 27 | 0% | 0% | 28-Jun-26 | 21-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| SHOP DRAWINGS SUBMISSION | | 27 | 0% | 0% | 19-Sep-26 | 20-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -20 |
| SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS | | 27 | 0% | 0% | 19-Sep-26 | 20-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -20 |
| ELECTRICAL WORKS | | 27 | 0% | 0% | 19-Sep-26 | 20-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN-2580 | Shop DWG Submittal for Power Layout | 27 | 74.07% | 0% | 19-Sep-26 | 20-Oct-26 | 13-Oct-26 | 12-Nov-26 | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN-2610 | Shop DWG Submittal for Fire Alarm Layout | 15 | 100% | 0% | 19-Sep-26 | 06-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -20 |
| SHOP DRAWINGS APPROVALS | | 23 | 0% | 0% | 28-Jun-26 | 21-Oct-26 | 13-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS | | 23 | 0% | 0% | 28-Jun-26 | 21-Oct-26 | 13-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| AIR DOME SYSTEM | | 15 | 0% | 0% | 28-Jun-26 | 14-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -91 |
| MLTX-02-005-EN-3560 | Shop DWG Approval for Membrane Panel Layout | 15 | 100% | 0% | 28-Jun-26 | 14-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -91 |
| MLTX-02-005-EN-3570 | Shop DWG Approval for Cable Tension Layout | 13 | 100% | 0% | 30-Jun-26 | 14-Jul-26 | 15-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -91 |
| ELECTRICAL WORKS | | 23 | 0% | 0% | 26-Sep-26 | 21-Oct-26 | 13-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN-3680 | Shop DWG Approval for Lighting Layout | 23 | 65.22% | 0% | 26-Sep-26 | 21-Oct-26 | 13-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| PROCUREMENT | | 40 | 0% | 0% | 27-Jun-26 | 24-Oct-26 | 13-Oct-26 | 28-Nov-26 | 0.00 | 0.00 | 0.00 | -30 |
| SHORT LEAD ITEM | | 40 | 0% | 0% | 27-Jun-26 | 24-Oct-26 | 13-Oct-26 | 28-Nov-26 | 0.00 | 0.00 | 0.00 | -30 |
| TOILET/SERVICE WORKS | | 40 | 0% | 0% | 27-Jun-26 | 10-Oct-26 | 13-Oct-26 | 28-Nov-26 | 0.00 | 0.00 | 0.00 | -42 |
| LIGHTING FIXTURES | | 40 | 0% | 0% | 27-Jun-26 | 11-Aug-26 | 13-Oct-26 | 28-Nov-26 | 0.00 | 0.00 | 0.00 | -92 |
| MLTX-02-005-PR-8490 | Material Delivery for Lighting Fixtures | 40 | 100% | 0% | 27-Jun-26 | 11-Aug-26 | 13-Oct-26 | 28-Nov-26 | 0.00 | 0.00 | 0.00 | -92 |
| SWITCHES/SOCKETS | | 15 | 0% | 0% | 22-Sep-26 | 10-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-PR-8510 | PO for Switches/Sockets | 15 | 100% | 0% | 22-Sep-26 | 10-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -17 |
| DISTRIBUTION PANNELS | | 5 | 0% | 0% | 27-Sep-26 | 01-Oct-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-8590 | PO for Distribution Panels | 5 | 100% | 0% | 27-Sep-26 | 01-Oct-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -14 |
| FURNITURES | | 29 | 0% | 0% | 30-Aug-26 | 03-Oct-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -37 |
| MLTX-02-005-PR-8150 | PO for Furnitures | 29 | 100% | 0% | 30-Aug-26 | 03-Oct-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -37 |
| PLAYGROUND WORKS | | 30 | 0% | 0% | 15-Jul-26 | 24-Oct-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -20 |
| PADEL WIRE MESH/STEEL SETS | | 15 | 0% | 0% | 31-Aug-26 | 16-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-PR-8970 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 31-Aug-26 | 16-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -36 |
| MARKING PAINT | | 15 | 0% | 0% | 10-Sep-26 | 28-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-PR-9090 | PO for Marking Paint | 15 | 100% | 0% | 10-Sep-26 | 28-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -27 |
| EXHAUST FANS | | 20 | 0% | 0% | 16-Sep-26 | 10-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-PR-9250 | PO for Exhaust Fans | 5 | 100% | 0% | 16-Sep-26 | 21-Sep-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-PR-9270 | Material Delivery for Exhaust Fans | 15 | 100% | 0% | 22-Sep-26 | 10-Oct-26 | 19-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -22 |
| CCTV MATERIALS | | 25 | 0% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-PR-9410 | PO for CCTV | 25 | 60% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| POWER OUTLETS/SWITCHES | | 30 | 0% | 0% | 15-Jul-26 | 18-Aug-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -76 |
| MLTX-02-005-PR-9470 | Material Delivery for Power Outlets/Switches | 30 | 100% | 0% | 15-Jul-26 | 18-Aug-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -76 |
| LANDSCAPE WORKS | | 20 | 0% | 0% | 15-Jul-26 | 17-Aug-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -67 |
| PAVEMENT MARKING | | 5 | 0% | 0% | 15-Jul-26 | 20-Jul-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -76 |
| MLTX-02-005-PR-9580 | PO for Pavement Markings | 5 | 100% | 0% | 15-Jul-26 | 20-Jul-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -76 |
| TRAFFIC SIGNS | | 15 | 0% | 0% | 27-Jul-26 | 12-Aug-26 | 19-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -71 |
| MLTX-02-005-PR-9620 | PO for Traffic Signs | 15 | 100% | 0% | 27-Jul-26 | 12-Aug-26 | 19-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -71 |
| AGRICULTURE SOIL | | 15 | 0% | 0% | 01-Aug-26 | 17-Aug-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -62 |
| MLTX-02-005-PR-9700 | PO for Agriculture Soil | 15 | 100% | 0% | 01-Aug-26 | 17-Aug-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -62 |
| LONG LEAD ITEM | | 20 | 0% | 0% | 08-Sep-26 | 01-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -29 |
| PLAYGROUND WORKS | | 20 | 0% | 0% | 08-Sep-26 | 01-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -29 |
| EMERGENCY DOORS | | 20 | 0% | 0% | 08-Sep-26 | 01-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-8710 | PO for Emergency Doors | 20 | 100% | 0% | 08-Sep-26 | 01-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -29 |
| PRESSURE UNITS | | 10 | 0% | 0% | 08-Sep-26 | 19-Sep-26 | 13-Oct-26 | 24-Oct-26 | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-8750 | PO for Pressure Units | 10 | 100% | 0% | 08-Sep-26 | 19-Sep-26 | 13-Oct-26 | 24-Oct-26 | 0.00 | 0.00 | 0.00 | -29 |
| CONSTRUCTION PHASE | | 100 | 53.43% | 46.77% | 07-Jul-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 391,949.80 | 343,117.21 | 733,614.61 | -44 |
| SITE WORKS | | 100 | 29.08% | 53.6% | 07-Jul-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 136,802.09 | 252,197.57 | 470,489.02 | -44 |
| LANDSCAPE WORKS | | 100 | 29.08% | 53.6% | 07-Jul-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 136,802.09 | 252,197.57 | 470,489.02 | -44 |
| PLAYGROUND AREA | | 17 | 100% | 0% | 10-Sep-26 | 30-Sep-26 | 13-Oct-26 | 01-Nov-26 | 3,834.68 | 0.00 | 3,834.68 | -27 |
| PADEL FENCE | | 17 | 100% | 0% | 10-Sep-26 | 30-Sep-26 | 13-Oct-26 | 01-Nov-26 | 3,834.68 | 0.00 | 3,834.68 | -27 |
| MLTX-02-005-CN-1025 | Backfilling and Reinstatement for Concrete Foundation | 17 | 100% | 0% | 10-Sep-26 | 30-Sep-26 | 13-Oct-26 | 01-Nov-26 | 3,834.68 | 0.00 | 3,834.68 | -27 |
| IRRIGATION NETWORK | | 4 | 100% | 80% | 07-Jul-26 | 11-Jul-26 | 10-Sep-26 A | 17-Oct-26 | 23,560.84 | 18,848.67 | 23,560.84 | -83 |
| MLTX-02-005-CN-11450 | Installing of Valves and fittings for Irrigation Network | 4 | 100% | 80% | 07-Jul-26 | 11-Jul-26 | 10-Sep-26 A | 17-Oct-26 | 23,560.84 | 18,848.67 | 23,560.84 | -83 |
| WALKING/BIKE PATHS | | 24 | 29.76% | 45% | 05-Oct-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 109,406.57 | 165,435.26 | 367,633.90 | -43 |
| MLTX-02-005-CN-10510 | Bike Path Preparation and Installation Works | 12 | 58.33% | 45% | 05-Oct-26 | 18-Oct-26 | 11-Jun-26 A | 22-Dec-26 | 109,406.57 | 84,399.35 | 187,554.12 | -55 |
| MLTX-02-005-CN-10520 | Walking Path Preparation and Installation Works | 12 | 0% | 45% | 19-Oct-26 | 01-Nov-26 | 11-Jun-26 A | 22-Dec-26 | 0.00 | 81,035.90 | 180,079.78 | -43 |




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

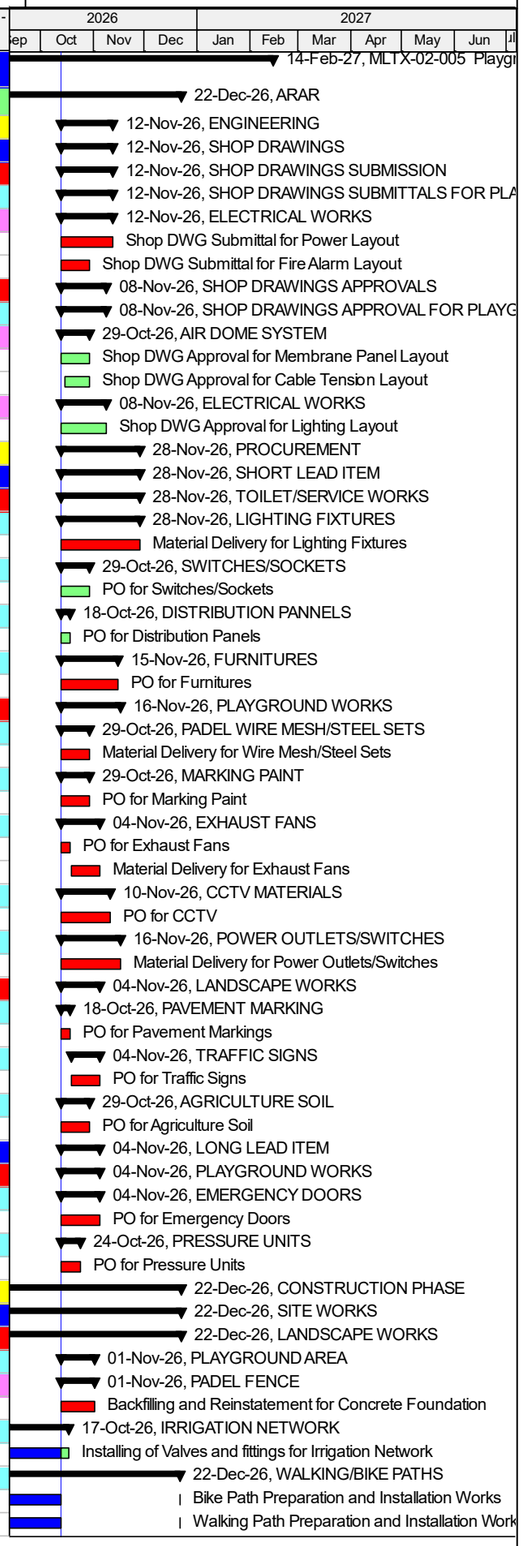


TASK filter: 2 weeks look ahead .

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

## 2 Weeks look ahead schedule
D.D 12-10-2026

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| GENERAL/FURNITURE | | 7 | 0% | 90% | 19-Oct-26 | 26-Oct-26 | 03-Oct-26 A | 22-Dec-26 | 0.00 | 67,913.64 | 75,459.60 | -49 |
| MLTX-02-005-CN-11710 | Preleminary Works for Site Light Poles Including Cable and Bases Works | 7 | 0% | 90% | 19-Oct-26 | 26-Oct-26 | 03-Oct-26 A | 22-Dec-26 | 0.00 | 67,913.64 | 75,459.60 | -49 |
| TOILET/SERVICE BUILDING | | 40 | 96.97% | 34.55% | 31-Aug-26 | 19-Oct-26 | 28-Sep-26 A | 29-Oct-26 | 255,147.71 | 90,919.64 | 263,125.59 | -9 |
| THERMAL & MOISTER PROTECTION | | 31 | 100% | 54.02% | 31-Aug-26 | 21-Sep-26 | 03-Oct-26 A | 21-Oct-26 | 21,520.94 | 11,625.10 | 21,520.94 | -25 |
| MLTX-02-005-CN-11070 | Finalize Water Proofing Works for Toilets | 6 | 100% | 0% | 31-Aug-26 | 06-Sep-26 | 13-Oct-26 | 19-Oct-26 | 4,913.66 | 0.00 | 4,913.66 | -36 |
| MLTX-02-005-CN-11080 | Finalize Water Proofing Works for Roofing and Wet Areas | 8 | 100% | 70% | 13-Sep-26 | 21-Sep-26 | 03-Oct-26 A | 21-Oct-26 | 16,607.28 | 11,625.10 | 16,607.28 | -25 |
| MECHANICAL WORK | | 19 | 100% | 67.54% | 29-Sep-26 | 10-Oct-26 | 28-Sep-26 A | 22-Oct-26 | 117,398.06 | 79,294.54 | 117,398.06 | -11 |
| WATER SUPPLY SYSTEM | | 8 | 100% | 87.14% | 01-Oct-26 | 10-Oct-26 | 28-Sep-26 A | 21-Oct-26 | 90,993.76 | 79,294.54 | 90,993.76 | -10 |
| MLTX-02-005-CN-11530 | Installing of HDPE Pipes and Valves for Water Supply Network | 3 | 100% | 80% | 01-Oct-26 | 04-Oct-26 | 29-Sep-26 A | 15-Oct-26 | 25,998.40 | 20,798.72 | 25,998.40 | -10 |
| MLTX-02-005-CN-11560 | Installing of GRP Tanks | 8 | 100% | 90% | 01-Oct-26 | 10-Oct-26 | 28-Sep-26 A | 21-Oct-26 | 64,995.36 | 58,495.82 | 64,995.36 | -10 |
| SEWER/DRAINAGE SYSTEM | | 9 | 100% | 0% | 29-Sep-26 | 08-Oct-26 | 13-Oct-26 | 22-Oct-26 | 26,404.30 | 0.00 | 26,404.30 | -12 |
| MLTX-02-005-CN-11580 | Installing UPVC Pipes for External Connection for Sewage Network | 4 | 100% | 0% | 05-Oct-26 | 08-Oct-26 | 19-Oct-26 | 22-Oct-26 | 14,217.67 | 0.00 | 14,217.67 | -12 |
| MLTX-02-005-CN-11850 | Installing Inspection Chamber for Sewage Network | 5 | 100% | 0% | 29-Sep-26 | 04-Oct-26 | 13-Oct-26 | 18-Oct-26 | 12,186.63 | 0.00 | 12,186.63 | -12 |
| DOORS/WINDOWS | | 5 | 100% | 0% | 17-Sep-26 | 22-Sep-26 | 13-Oct-26 | 18-Oct-26 | 60,445.68 | 0.00 | 60,445.68 | -21 |
| MLTX-02-005-CN-11100 | Preliminary Works For Windows/Curtain Wall | 2 | 100% | 0% | 17-Sep-26 | 19-Sep-26 | 13-Oct-26 | 14-Oct-26 | 52,646.24 | 0.00 | 52,646.24 | -21 |
| MLTX-02-005-CN-11110 | Preliminary Works For Doors | 3 | 100% | 0% | 20-Sep-26 | 22-Sep-26 | 15-Oct-26 | 18-Oct-26 | 7,799.44 | 0.00 | 7,799.44 | -21 |
| METAL WORKS | | 4 | 100% | 0% | 14-Sep-26 | 17-Sep-26 | 13-Oct-26 | 17-Oct-26 | 3,899.72 | 0.00 | 3,899.72 | -24 |
| MLTX-02-005-CN-11160 | Installation of DI Cover for Tank | 4 | 100% | 0% | 14-Sep-26 | 17-Sep-26 | 13-Oct-26 | 17-Oct-26 | 3,899.72 | 0.00 | 3,899.72 | -24 |
| FINISHING WORKS | | 15 | 86.67% | 0% | 04-Oct-26 | 19-Oct-26 | 13-Oct-26 | 29-Oct-26 | 51,883.31 | 0.00 | 59,861.19 | -9 |
| FLOOR FINISHES | | 10 | 96.34% | 0% | 04-Oct-26 | 14-Oct-26 | 19-Oct-26 | 29-Oct-26 | 15,404.15 | 0.00 | 15,989.09 | -13 |
| MLTX-02-005-CN-11200 | Creamic Tiles Floor Finish Works | 2 | 100% | 0% | 04-Oct-26 | 05-Oct-26 | 19-Oct-26 | 20-Oct-26 | 11,894.39 | 0.00 | 11,894.39 | -13 |
| MLTX-02-005-CN-11210 | Granite Tiles Floor Finish Works | 4 | 100% | 0% | 06-Oct-26 | 10-Oct-26 | 21-Oct-26 | 25-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -13 |
| MLTX-02-005-CN-11230 | Ceramic Skirting Tiles Finish Works | 4 | 50% | 0% | 11-Oct-26 | 14-Oct-26 | 26-Oct-26 | 29-Oct-26 | 584.94 | 0.00 | 1,169.88 | -13 |
| WALL FINISHES | | 12 | 80.6% | 0% | 06-Oct-26 | 19-Oct-26 | 17-Oct-26 | 29-Oct-26 | 30,707.64 | 0.00 | 38,100.58 | -9 |
| MLTX-02-005-CN-11250 | Stone Cladding Finish Works for External Walls | 5 | 0% | 0% | 14-Oct-26 | 19-Oct-26 | 25-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 2,275.00 | -9 |
| MLTX-02-005-CN-11300 | Painting Finish Works for External Walls | 7 | 85.71% | 0% | 06-Oct-26 | 13-Oct-26 | 17-Oct-26 | 24-Oct-26 | 30,707.64 | 0.00 | 35,825.58 | -9 |
| CELLING FINISHES | | 7 | 100% | 0% | 12-Oct-26 | 19-Oct-26 | 13-Oct-26 | 20-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -1 |
| MLTX-02-005-CN-11360 | Gypsum Board Suspended Ceiling Finish Works For Ceiling | 7 | 14.29% | 0% | 12-Oct-26 | 19-Oct-26 | 13-Oct-26 | 20-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -1 |
| HASA OASIS | | 107 | 47.66% | 52.25% | 04-May-26 | 02-Dec-26 | 01-Jun-26 A | 14-Feb-27 | 492,270.74 | 539,604.09 | 1,032,813.68 | -63 |
| ENGINEERING | | 25 | 0% | 0% | 04-May-26 | 02-Nov-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -7 |
| SHOP DRAWINGS | | 25 | 0% | 0% | 04-May-26 | 02-Nov-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -7 |
| SHOP DRAWINGS SUBMISSION | | 25 | 0% | 0% | 04-May-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS | | 25 | 0% | 0% | 04-May-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| MECHANCAL WORKS | | 25 | 0% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN-8760 | Shop DWG Submittal for HVAC Plan | 25 | 60% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN-8770 | Shop DWG Submittal for Exhaust Air Plan | 25 | 60% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| ELECTRICAL WORKS | | 25 | 0% | 0% | 04-May-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN-8650 | Shop DWG Submittal for Lighting Layout | 25 | 60% | 0% | 26-Sep-26 | 24-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN-8660 | Shop DWG Submittal for Power Layout | 25 | 100% | 0% | 04-May-26 | 04-Jun-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -135 |
| MLTX-02-005-EN-8670 | Shop DWG Submittal for Power Single Line Diagram | 25 | 48% | 0% | 29-Sep-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN-8680 | Shop DWG Submittal for Panel Board Schedules | 25 | 48% | 0% | 29-Sep-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN-8690 | Shop DWG Submittal for Power Installation Details | 25 | 48% | 0% | 29-Sep-26 | 27-Oct-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -12 |
| SHOP DRAWINGS APPROVALS | | 21 | 0% | 0% | 10-Oct-26 | 02-Nov-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -3 |
| SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS | | 21 | 0% | 0% | 10-Oct-26 | 02-Nov-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -3 |
| SPORTS EQUIPMENT | | 21 | 0% | 0% | 10-Oct-26 | 02-Nov-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN-1207( | Shop DWG Approval for Football Turf Installation | 21 | 14.29% | 0% | 10-Oct-26 | 02-Nov-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -3 |
| PROCUREMENT | | 30 | 0% | 0% | 10-Jun-26 | 03-Nov-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -11 |
| SHORT LEAD ITEM | | 30 | 0% | 0% | 16-Jun-26 | 03-Nov-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -11 |
| TOILET/SERVICE WORKS | | 20 | 0% | 0% | 16-Jun-26 | 19-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| LIGHTING FIXTURES | | 20 | 0% | 0% | 16-Jun-26 | 08-Jul-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -101 |
| MLTX-02-005-PR-10300 | Material Delivery for Lighting Fixtures | 20 | 100% | 0% | 16-Jun-26 | 08-Jul-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -101 |
| SWITCHES/SOCKETS | | 15 | 0% | 0% | 16-Jun-26 | 02-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -101 |
| MLTX-02-005-PR-10310 | PO for Switches/Sockets | 15 | 100% | 0% | 16-Jun-26 | 02-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -101 |
| DISTRIBUTION PANNELS | | 20 | 0% | 0% | 27-Sep-26 | 19-Oct-26 | 13-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-10130 | PO for Distribution Panels | 5 | 100% | 0% | 27-Sep-26 | 01-Oct-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-10140 | Material Delivery for Distribution Panels | 15 | 60% | 0% | 03-Oct-26 | 19-Oct-26 | 19-Oct-26 | 04-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| FURNITURES | | 19 | 0% | 0% | 16-Jun-26 | 07-Jul-26 | 13-Oct-26 | 03-Nov-26 | 0.00 | 0.00 | 0.00 | -101 |
| MLTX-02-005-PR-10330 | PO for Furnitures | 19 | 100% | 0% | 16-Jun-26 | 07-Jul-26 | 13-Oct-26 | 03-Nov-26 | 0.00 | 0.00 | 0.00 | -101 |
| PLAYGROUND WORKS | | 30 | 0% | 0% | 28-Jun-26 | 03-Nov-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -11 |
| ARTIFICIAL TURF | | 30 | 0% | 0% | 30-Sep-26 | 03-Nov-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-PR-10780 | Material Delivery for Artificial TURF | 30 | 36.67% | 0% | 30-Sep-26 | 03-Nov-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -11 |
| RUBBER GRANULES | | 30 | 0% | 0% | 20-Sep-26 | 25-Oct-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-PR-10800 | Material Delivery for Rubber Granules | 30 | 63.33% | 0% | 20-Sep-26 | 25-Oct-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| PADEL GLASS | | 30 | 0% | 0% | 16-Sep-26 | 21-Oct-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -22 |

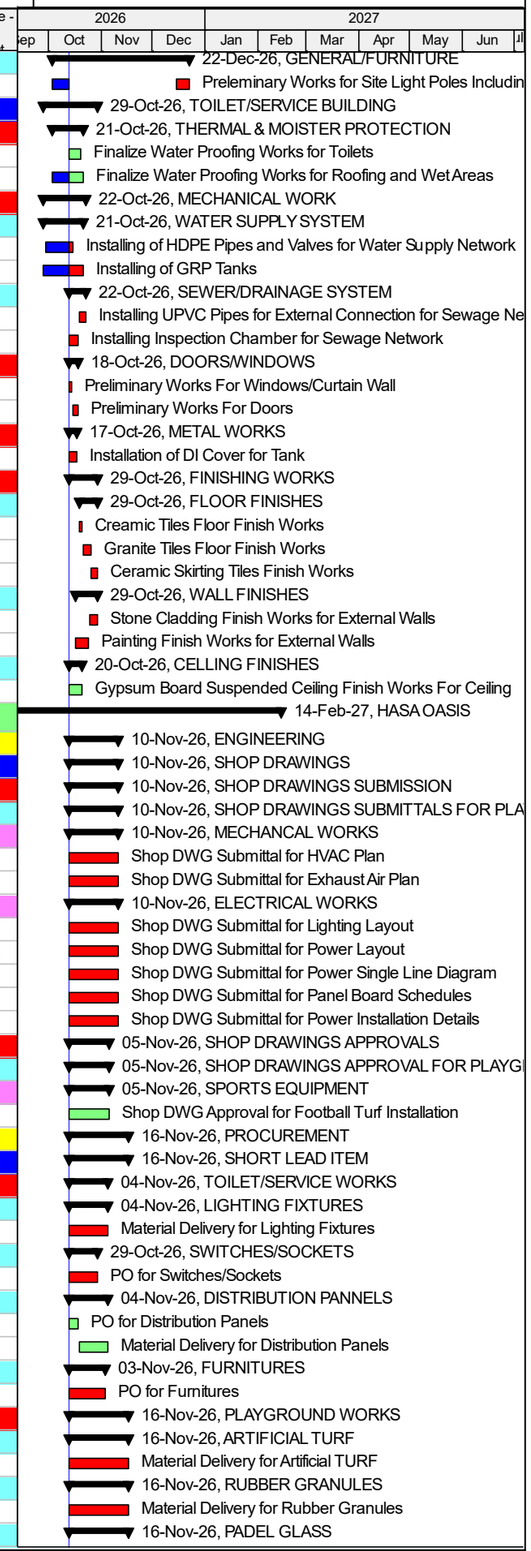


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: 2 weeks look ahead .

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

## 2 Weeks look ahead schedule
D.D 12-10-2026

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-10820 | Material Delivery for Padel Glass | 30 | 73.33% | 0% | 16-Sep-26 | 21-Oct-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -22 |
| PADEL WIRE MESH/STEEL SETS | | 15 | 0% | 0% | 16-Sep-26 | 04-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-PR-10840 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 16-Sep-26 | 04-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -22 |
| MARKING PAINT | | 15 | 0% | 0% | 28-Jun-26 | 14-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -91 |
| MLTX-02-005-PR-10350 | PO for Marking Paint | 15 | 100% | 0% | 28-Jun-26 | 14-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -91 |
| AIR DIFUSSERS/GRILLS | | 15 | 0% | 0% | 24-Sep-26 | 11-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-PR-10470 | PO for Air Difussers/Grills | 15 | 100% | 0% | 24-Sep-26 | 11-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -16 |
| GALVANIZED DUCTS | | 15 | 0% | 0% | 24-Sep-26 | 11-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-PR-10490 | PO for Galvanized Duct | 15 | 100% | 0% | 24-Sep-26 | 11-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -16 |
| EXHAUST FANS | | 15 | 0% | 0% | 10-Sep-26 | 28-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-PR-10510 | PO for Exhaust Fans | 15 | 100% | 0% | 10-Sep-26 | 28-Sep-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -27 |
| CCTV MATERIALS | | 15 | 0% | 0% | 04-Jul-26 | 20-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -86 |
| MLTX-02-005-PR-10690 | PO for CCTV | 15 | 100% | 0% | 04-Jul-26 | 20-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -86 |
| LONG LEAD ITEM | | 30 | 0% | 0% | 10-Jun-26 | 14-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -106 |
| PLAYGROUND WORKS | | 30 | 0% | 0% | 10-Jun-26 | 14-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -106 |
| EMERGENCY DOORS | | 30 | 0% | 0% | 10-Jun-26 | 14-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -106 |
| MLTX-02-005-PR-10570 | PO for Emergency Doors | 10 | 100% | 0% | 10-Jun-26 | 21-Jun-26 | 13-Oct-26 | 24-Oct-26 | 0.00 | 0.00 | 0.00 | -106 |
| MLTX-02-005-PR-10940 | Material Fabrication for Emergency Doors | 20 | 100% | 0% | 22-Jun-26 | 14-Jul-26 | 25-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -106 |
| CONSTRUCTION PHASE | | 107 | 47.66% | 52.25% | 30-Jul-26 | 02-Dec-26 | 01-Jun-26 A | 14-Feb-27 | 492,270.74 | 539,604.09 | 1,032,813.68 | -63 |
| SITE WORKS | | 56 | 47.58% | 50.25% | 29-Sep-26 | 02-Dec-26 | 01-Jun-26 A | 14-Feb-27 | 458,114.68 | 483,838.47 | 962,832.04 | -63 |
| LANDSCAPE WORKS | | 56 | 47.58% | 50.25% | 29-Sep-26 | 02-Dec-26 | 01-Jun-26 A | 14-Feb-27 | 458,114.68 | 483,838.47 | 962,832.04 | -63 |
| PLAYGROUND AREA | | 3 | 100% | 60% | 29-Sep-26 | 01-Oct-26 | 21-Sep-26 A | 15-Oct-26 | 180,520.67 | 108,312.40 | 180,520.67 | -12 |
| CURBSTOEN/INTERLOCK | | 3 | 100% | 60% | 29-Sep-26 | 01-Oct-26 | 21-Sep-26 A | 15-Oct-26 | 180,520.67 | 108,312.40 | 180,520.67 | -12 |
| MLTX-02-005-CN-1196( | Interlock Installation (Grey Scale) for LandScape (Including Finishing Works) | 3 | 100% | 60% | 29-Sep-26 | 01-Oct-26 | 21-Sep-26 A | 15-Oct-26 | 180,520.67 | 108,312.40 | 180,520.67 | -12 |
| IRRIGATION NETWORK | | 10 | 0% | 80% | 17-Nov-26 | 28-Nov-26 | 10-Sep-26 A | 14-Nov-26 | 0.00 | 18,848.67 | 23,560.84 | 12 |
| MLTX-02-005-CN-13210 | Installing of Valves and fittings for Irrigation Network | 10 | 0% | 80% | 17-Nov-26 | 28-Nov-26 | 10-Sep-26 A | 14-Nov-26 | 0.00 | 18,848.67 | 23,560.84 | 12 |
| PLANTING | | 3 | 0% | 70% | 24-Oct-26 | 26-Oct-26 | 03-Oct-26 A | 15-Oct-26 | 0.00 | 72,922.81 | 104,175.44 | 9 |
| MLTX-02-005-CN-12050 | Placement of Sweet/Agricultural Soil (Including Levelling and Grading) | 3 | 0% | 70% | 24-Oct-26 | 26-Oct-26 | 03-Oct-26 A | 15-Oct-26 | 0.00 | 72,922.81 | 104,175.44 | 9 |
| WALKING/BIKE PATHS | | 16 | 75.51% | 70% | 29-Sep-26 | 17-Oct-26 | 01-Jun-26 A | 13-Oct-26 | 277,594.01 | 257,343.73 | 367,633.90 | 4 |
| MLTX-02-005-CN-12000 | Bike Path Preparation and Installation Works | 8 | 100% | 70% | 29-Sep-26 | 07-Oct-26 | 01-Jun-26 A | 13-Oct-26 | 187,554.12 | 131,287.88 | 187,554.12 | -4 |
| MLTX-02-005-CN-12010 | Walking Path Preparation and Installation Works | 8 | 50% | 70% | 08-Oct-26 | 17-Oct-26 | 10-Jun-26 A | 13-Oct-26 | 90,039.89 | 126,055.85 | 180,079.78 | 4 |
| GENERAL/FURNITURE | | 44 | 0% | 9.2% | 15-Oct-26 | 02-Dec-26 | 01-Oct-26 A | 14-Feb-27 | 0.00 | 26,410.86 | 286,941.19 | -63 |
| MLTX-02-005-CN-11970 | Stamped Concrete Works for LandScape (Including Finishing Works) | 18 | 0% | 0% | 18-Oct-26 | 07-Nov-26 | 13-Oct-26 | 02-Nov-26 | 0.00 | 0.00 | 93,594.00 | 4 |
| MLTX-02-005-CN-12440 | Fixation and Installation of Steel Frame for Benches | 28 | 0% | 0% | 15-Oct-26 | 16-Nov-26 | 13-Oct-26 | 14-Nov-26 | 0.00 | 0.00 | 17,274.79 | 2 |
| MLTX-02-005-CN-12930 | Installing of Site Light Poles | 22 | 0% | 15% | 08-Nov-26 | 02-Dec-26 | 01-Oct-26 A | 14-Feb-27 | 0.00 | 26,410.86 | 176,072.40 | -63 |
| TOILET/SERVICE BUILDING | | 70 | 48.81% | 79.69% | 30-Jul-26 | 20-Oct-26 | 20-Sep-26 A | 02-Nov-26 | 34,156.06 | 55,765.62 | 69,981.64 | -11 |
| THERMAL & MOISTER PROTECTION | | 18 | 100% | 80% | 30-Jul-26 | 19-Aug-26 | 20-Sep-26 A | 02-Nov-26 | 16,607.28 | 13,285.82 | 16,607.28 | -63 |
| MLTX-02-005-CN-12650 | Finalize Water Proofing Works for Roofing and Wet Areas | 18 | 100% | 80% | 30-Jul-26 | 19-Aug-26 | 20-Sep-26 A | 02-Nov-26 | 16,607.28 | 13,285.82 | 16,607.28 | -63 |
| FINISHING WORKS | | 7 | 7.55% | 83.21% | 27-Sep-26 | 20-Oct-26 | 27-Sep-26 A | 19-Oct-26 | 2,924.82 | 32,243.02 | 38,750.40 | 1 |
| FLOOR FINISHES | | 6 | 100% | 0% | 27-Sep-26 | 03-Oct-26 | 13-Oct-26 | 19-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -14 |
| MLTX-02-005-CN-13050 | Granite Tiles Floor Finish Works | 6 | 100% | 0% | 27-Sep-26 | 03-Oct-26 | 13-Oct-26 | 19-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -14 |
| WALL FINISHES | | 3 | 0% | 90% | 18-Oct-26 | 20-Oct-26 | 27-Sep-26 A | 15-Oct-26 | 0.00 | 32,243.02 | 35,825.58 | 4 |
| MLTX-02-005-CN-13010 | Painting Finish Works for External Walls | 3 | 0% | 90% | 18-Oct-26 | 20-Oct-26 | 27-Sep-26 A | 15-Oct-26 | 0.00 | 32,243.02 | 35,825.58 | 4 |
| SPECIALTIES WORK | | 3 | 100% | 70% | 27-Sep-26 | 29-Sep-26 | 04-Oct-26 A | 15-Oct-26 | 14,623.96 | 10,236.77 | 14,623.96 | -14 |
| MLTX-02-005-CN-12700 | Sanitary Fixtures and Accessories Works | 3 | 100% | 70% | 27-Sep-26 | 29-Sep-26 | 04-Oct-26 A | 15-Oct-26 | 14,623.96 | 10,236.77 | 14,623.96 | -14 |
| DAMMAM | | 130 | 63.75% | 25.77% | 16-Apr-26 | 31-Oct-26 | 06-Sep-26 A | 07-Dec-26 | 121,733.61 | 49,211.34 | 190,947.24 | -32 |
| ENGINEERING | | 30 | 0% | 0% | 16-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| SHOP DRAWINGS | | 30 | 0% | 0% | 16-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| SHOP DRAWINGS SUBMISSION | | 30 | 0% | 0% | 16-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS | | 30 | 0% | 0% | 16-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| AIR DOME SYSTEM | | 30 | 0% | 0% | 16-Apr-26 | 07-Jun-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -138 |
| MLTX-02-005-EN-1316( | Shop DWG Submittal for Cable Tension Layout | 15 | 100% | 0% | 16-Apr-26 | 03-May-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -150 |
| MLTX-02-005-EN-1317( | Shop DWG Submittal for Airlock Door Details | 25 | 100% | 0% | 30-Apr-26 | 01-Jun-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -138 |
| MLTX-02-005-EN-1318( | Shop DWG Submittal for Emergency Exit Details | 30 | 100% | 0% | 30-Apr-26 | 07-Jun-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -138 |
| MECHANCAL WORKS | | 15 | 0% | 0% | 30-Apr-26 | 14-Jun-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1303( | Shop DWG Submittal for HVAC Plan | 15 | 100% | 0% | 30-Apr-26 | 17-May-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -138 |
| MLTX-02-005-EN-1304( | Shop DWG Submittal for Exhaust Air Plan | 15 | 100% | 0% | 25-May-26 | 14-Jun-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -117 |
| ELECTRICAL WORKS | | 30 | 0% | 0% | 25-May-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1293( | Shop DWG Submittal for Power Layout | 25 | 100% | 0% | 25-May-26 | 25-Jun-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1294( | Shop DWG Submittal for Power Single Line Diagram | 25 | 100% | 0% | 25-May-26 | 25-Jun-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1295( | Shop DWG Submittal for Panel Board Schedules | 25 | 100% | 0% | 25-May-26 | 25-Jun-26 | 13-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1296( | Shop DWG Submittal for Power Installation Details | 30 | 100% | 0% | 25-May-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| SHOP DRAWINGS APPROVALS | | 30 | 0% | 0% | 30-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS | | 30 | 0% | 0% | 30-Apr-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |

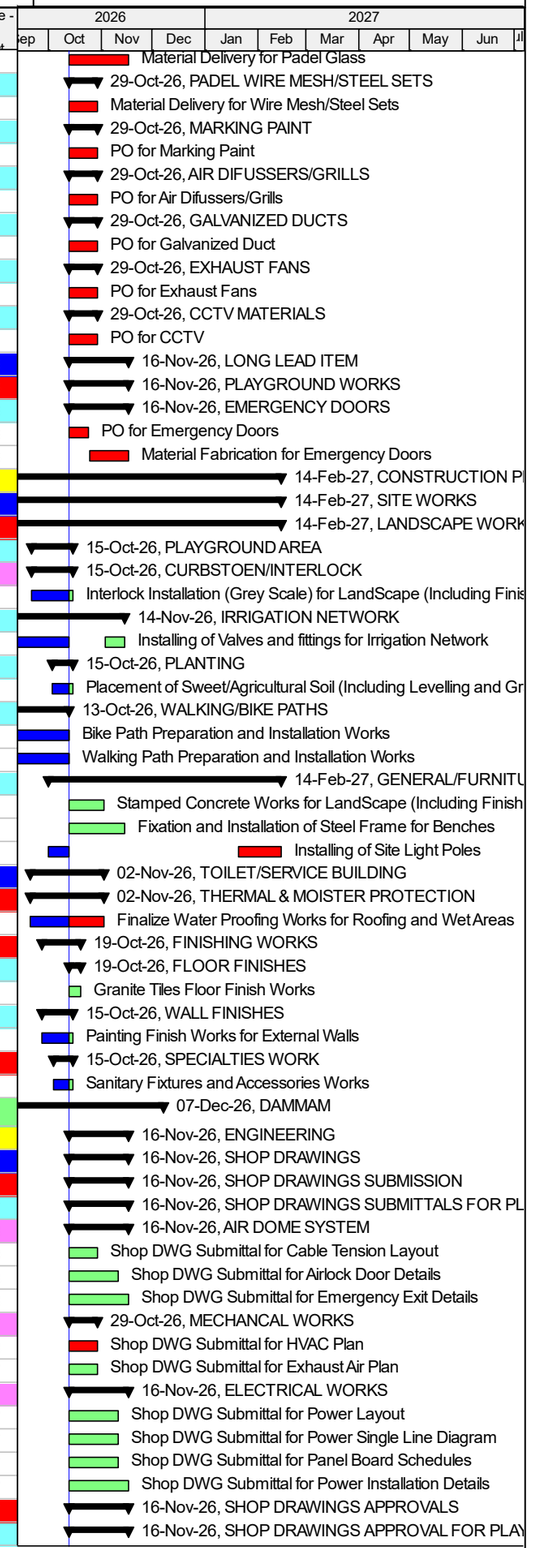


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: 2 weeks look ahead .

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

## 2 Weeks look ahead schedule
D.D 12-10-2026

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| AIR DOME SYSTEM | | 15 | 0% | 0% | 30-Apr-26 | 17-May-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -138 |
| MLTX-02-005-EN-1627( | Shop DWG Approval for Air Dome Structural Layout | 15 | 100% | 0% | 30-Apr-26 | 17-May-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -138 |
| SPORTS EQUIPMENT | | 30 | 0% | 0% | 25-May-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN-1634( | Shop DWG Approval for Football Turf Installation | 30 | 100% | 0% | 25-May-26 | 01-Jul-26 | 13-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -117 |
| PROCUREMENT | | 29 | 0% | 0% | 21-May-26 | 29-Oct-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| SHORT LEAD ITEM | | 29 | 0% | 0% | 21-May-26 | 29-Oct-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| TOILET/SERVICE WORKS | | 29 | 0% | 0% | 17-Jun-26 | 29-Oct-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -14 |
| DISTRIBUTION PANNELS | | 15 | 0% | 0% | 13-Oct-26 | 29-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-PR-11210 | PO for Distribution Panels | 15 | 0% | 0% | 13-Oct-26 | 29-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | 0 |
| FURNITURES | | 29 | 0% | 0% | 17-Jun-26 | 20-Jul-26 | 13-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-PR-11410 | PO for Furnitures | 9 | 100% | 0% | 17-Jun-26 | 27-Jun-26 | 13-Oct-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-PR-11420 | Material Delivery for Furnitures | 20 | 100% | 0% | 28-Jun-26 | 20-Jul-26 | 24-Oct-26 | 15-Nov-26 | 0.00 | 0.00 | 0.00 | -100 |
| PLAYGROUND WORKS | | 21 | 0% | 0% | 21-May-26 | 18-Oct-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -16 |
| PVC MEMBRANE | | 21 | 0% | 0% | 21-May-26 | 17-Jun-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| MLTX-02-005-PR-11620 | Material Delivery for PVC Membrane | 21 | 100% | 0% | 21-May-26 | 17-Jun-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| RUBBER GRANULES | | 12 | 0% | 0% | 31-May-26 | 13-Jun-26 | 13-Oct-26 | 26-Oct-26 | 0.00 | 0.00 | 0.00 | -115 |
| MLTX-02-005-PR-11880 | Material Delivery for Rubber Granules | 12 | 100% | 0% | 31-May-26 | 13-Jun-26 | 13-Oct-26 | 26-Oct-26 | 0.00 | 0.00 | 0.00 | -115 |
| PADEL WIRE MESH/STEEL SETS | | 15 | 0% | 0% | 06-Jun-26 | 22-Jun-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-11920 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 06-Jun-26 | 22-Jun-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -110 |
| AIR DIFUSSERS/GRILLS | | 15 | 0% | 0% | 01-Oct-26 | 18-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-PR-11550 | PO for Air Difussers/Grills | 15 | 66.67% | 0% | 01-Oct-26 | 18-Oct-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -10 |
| EXHAUST FANS | | 15 | 0% | 0% | 17-Jun-26 | 04-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-PR-11590 | PO for Exhaust Fans | 15 | 100% | 0% | 17-Jun-26 | 04-Jul-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -100 |
| CCTV MATERIALS | | 5 | 0% | 0% | 30-Jul-26 | 04-Aug-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -63 |
| MLTX-02-005-PR-11770 | PO for CCTV | 5 | 100% | 0% | 30-Jul-26 | 04-Aug-26 | 13-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -63 |
| LANDSCAPE WORKS | | 15 | 0% | 0% | 05-Aug-26 | 22-Aug-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -58 |
| AGRICULTURE SOIL | | 15 | 0% | 0% | 05-Aug-26 | 22-Aug-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-PR-11930 | PO for Agriculture Soil | 15 | 100% | 0% | 05-Aug-26 | 22-Aug-26 | 13-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 0.00 | -58 |
| LONG LEAD ITEM | | 18 | 0% | 0% | 21-May-26 | 14-Jun-26 | 13-Oct-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| PLAYGROUND WORKS | | 18 | 0% | 0% | 21-May-26 | 14-Jun-26 | 13-Oct-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| STEEL TENSION CABLES | | 18 | 0% | 0% | 21-May-26 | 14-Jun-26 | 13-Oct-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| MLTX-02-005-PR-11630 | PO for Steel Tension Cables | 8 | 100% | 0% | 21-May-26 | 02-Jun-26 | 13-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -120 |
| MLTX-02-005-PR-12010 | Material Fabrication for Steel Tension Cables | 10 | 100% | 0% | 03-Jun-26 | 14-Jun-26 | 22-Oct-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -120 |
| CONSTRUCTION PHASE | | 130 | 63.75% | 25.77% | 18-Aug-26 | 31-Oct-26 | 06-Sep-26 A | 07-Dec-26 | 121,733.61 | 49,211.34 | 190,947.24 | -32 |
| SITE WORKS | | 36 | 41.28% | 21.28% | 17-Sep-26 | 26-Oct-26 | 19-Sep-26 A | 29-Oct-26 | 36,560.84 | 18,848.67 | 88,560.84 | -3 |
| LANDSCAPE WORKS | | 36 | 41.28% | 21.28% | 17-Sep-26 | 26-Oct-26 | 19-Sep-26 A | 29-Oct-26 | 36,560.84 | 18,848.67 | 88,560.84 | -3 |
| IRRIGATION NETWORK | | 3 | 100% | 80% | 17-Sep-26 | 20-Sep-26 | 19-Sep-26 A | 15-Oct-26 | 23,560.84 | 18,848.67 | 23,560.84 | -21 |
| MLTX-02-005-CN-14640 | Installing of Valves and fittings for Irrigation Network | 3 | 100% | 80% | 17-Sep-26 | 20-Sep-26 | 19-Sep-26 A | 15-Oct-26 | 23,560.84 | 18,848.67 | 23,560.84 | -21 |
| NATURAL GROUND | | 15 | 20% | 0% | 10-Oct-26 | 26-Oct-26 | 13-Oct-26 | 29-Oct-26 | 13,000.00 | 0.00 | 65,000.00 | -3 |
| MLTX-02-005-CN-13420 | Compacted Natural Ground Soil Installation Works for Landscape | 15 | 20% | 0% | 10-Oct-26 | 26-Oct-26 | 13-Oct-26 | 29-Oct-26 | 13,000.00 | 0.00 | 65,000.00 | -3 |
| TOILET/SERVICE BUILDING | | 130 | 83.19% | 29.65% | 18-Aug-26 | 31-Oct-26 | 06-Sep-26 A | 07-Dec-26 | 85,172.77 | 30,362.66 | 102,386.40 | -32 |
| THERMAL & MOISTER PROTECTION | | 8 | 100% | 90% | 18-Aug-26 | 26-Aug-26 | 06-Sep-26 A | 21-Oct-26 | 16,607.28 | 14,946.55 | 16,607.28 | -47 |
| MLTX-02-005-CN-14080 | Finalize Water Proofing Works for Roofing and Wet Areas | 8 | 100% | 90% | 18-Aug-26 | 26-Aug-26 | 06-Sep-26 A | 21-Oct-26 | 16,607.28 | 14,946.55 | 16,607.28 | -47 |
| MECHANICAL WORK | | 4 | 75% | 50% | 10-Oct-26 | 13-Oct-26 | 04-Oct-26 A | 26-Oct-26 | 7,769.01 | 5,179.34 | 10,358.68 | -11 |
| SEWER/DRAINAGE SYSTEM | | 4 | 75% | 50% | 10-Oct-26 | 13-Oct-26 | 04-Oct-26 A | 26-Oct-26 | 7,769.01 | 5,179.34 | 10,358.68 | -11 |
| MLTX-02-005-CN-14230 | Installing of Plumping Fixtures and Accessories | 4 | 75% | 50% | 10-Oct-26 | 13-Oct-26 | 04-Oct-26 A | 26-Oct-26 | 7,769.01 | 5,179.34 | 10,358.68 | -11 |
| DOORS/WINDOWS | | 12 | 100% | 0% | 19-Sep-26 | 03-Oct-26 | 13-Oct-26 | 26-Oct-26 | 52,646.24 | 0.00 | 52,646.24 | -20 |
| MLTX-02-005-CN-14550 | Preliminary Works For Windows/Curtain Wall | 12 | 100% | 0% | 19-Sep-26 | 03-Oct-26 | 13-Oct-26 | 26-Oct-26 | 52,646.24 | 0.00 | 52,646.24 | -20 |
| FINISHING WORKS | | 12 | 100% | 0% | 27-Aug-26 | 09-Sep-26 | 22-Oct-26 | 04-Nov-26 | 8,150.24 | 0.00 | 8,150.24 | -47 |
| WALL FINISHES | | 12 | 100% | 0% | 27-Aug-26 | 09-Sep-26 | 22-Oct-26 | 04-Nov-26 | 8,150.24 | 0.00 | 8,150.24 | -47 |
| MLTX-02-005-CN-14580 | Granite Capping for Parpet | 12 | 100% | 0% | 27-Aug-26 | 09-Sep-26 | 22-Oct-26 | 04-Nov-26 | 8,150.24 | 0.00 | 8,150.24 | -47 |
| SPECIALTIES WORK | | 4 | 0% | 70% | 27-Oct-26 | 31-Oct-26 | 12-Oct-26 A | 07-Dec-26 | 0.00 | 10,236.77 | 14,623.96 | -32 |
| MLTX-02-005-CN-14130 | Sanitary Fixtures and Accessories Works | 4 | 0% | 70% | 27-Oct-26 | 31-Oct-26 | 12-Oct-26 A | 07-Dec-26 | 0.00 | 10,236.77 | 14,623.96 | -32 |

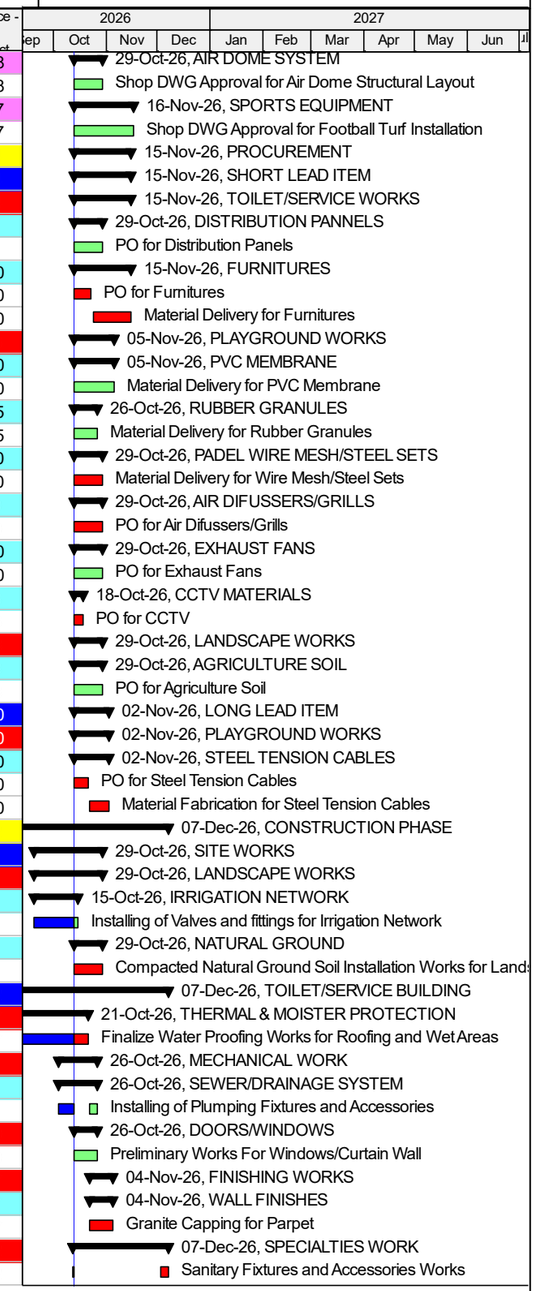


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary



TASK filter: 2 weeks look ahead .

© Oracle Corporation
