
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	338	35.6%	36.68%	03-Mar-26	02-Jan-27	03-Mar-26 A	13-Apr-27	10,680,031.43	11,002,889.60	29,997,851.67	-83
KEY MILESTONES		338	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	13-Apr-27	0.00	0.00	0.00	-83
GENERAL MILESTONES		338	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	13-Apr-27	0.00	0.00	0.00	-83
CONTRACTUAL MILESTONE		306	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	12-Apr-27	0.00	0.00	0.00	-82
ARAR		312	32.97%	33.8%	03-Mar-26	02-Jan-27	04-Mar-26 A	14-Mar-27	3,372,187.27	3,456,892.58	10,226,640.03	-57
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		250	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	30-Dec-26	0.00	0.00	0.00	-15
PROCUREMENT		214	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	14-Feb-27	0.00	0.00	0.00	-52
CONSTRUCTION PHASE		278	32.97%	33.8%	15-Apr-26	31-Dec-26	04-Apr-26 A	14-Mar-27	3,372,187.27	3,456,892.58	10,226,640.03	-58
SITE WORKS		278	29.14%	31.89%	15-Apr-26	30-Dec-26	04-Apr-26 A	14-Mar-27	2,639,549.36	2,888,482.74	9,058,565.25	-59
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
LANDSCAPE WORKS		245	25.22%	27.46%	24-May-26	30-Dec-26	17-May-26 A	14-Mar-27	2,144,662.34	2,335,102.39	8,505,184.90	-59
PLAYGROUND AREA		245	34.53%	49.61%	24-May-26	27-Dec-26	19-May-26 A	14-Mar-27	473,057.17	679,629.48	1,369,978.66	-62
FOOTBALL PLAYGROUND		203	35%	35%	24-May-26	13-Dec-26	19-May-26 A	19-Jan-27	110,897.50	110,897.50	316,849.99	-32
PADEL PLAYGROUND		183	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	19-Jan-27	105,292.80	163,788.80	233,984.00	-27
BASKETBALL PLAYGROUND		166	59.39%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	24-Jan-27	188,923.65	221,133.58	318,089.68	-27
PADEL FENCE		92	15.28%	1.46%	01-Sep-26	16-Nov-26	08-Aug-26 A	17-Dec-26	21,198.68	2,025.26	138,749.98	-27
CURBSTOEN/INTERLOCK		133	12.9%	50.17%	06-Oct-26	27-Dec-26	15-Aug-26 A	14-Mar-27	46,744.54	181,784.34	362,305.01	-62
AIR DOME		128	21.93%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	21-Feb-27	1,229,370.97	1,299,527.51	5,605,894.61	-53
CIVIL WORKS		95	45.69%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	13-Jan-27	1,229,370.97	1,299,527.51	2,690,829.42	-32
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	14-Jan-27	25-Jan-27	0.00	0.00	1,233,296.81	-31
ELECTRICAL WORKS		7	0%	0%	13-Dec-26	20-Dec-26	18-Jan-27	25-Jan-27	0.00	0.00	1,513,591.54	-31
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	15-Feb-27	21-Feb-27	0.00	0.00	168,176.84	-53
IRRIGATION NETWORK		164	83.53%	80.44%	28-Jun-26	30-Nov-26	18-Aug-26 A	05-Jan-27	127,308.67	122,596.50	152,414.87	-31
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	23-Dec-26	05-Jan-27	0.00	0.00	191,740.00	-31
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	10-Dec-26	27-Dec-26	205,518.96	0.00	347,251.46	-49
WALKING/BIKE PATHS		24	29.76%	45%	05-Oct-26	01-Nov-26	11-Jun-26 A	22-Dec-26	109,406.57	165,435.26	367,633.90	-43
GENERAL/FURNITURE		107	0%	14.44%	19-Oct-26	30-Dec-26	03-Oct-26 A	20-Feb-27	0.00	67,913.64	470,271.40	-44
PARKING		24	0%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	0.00	58,493.33	58,493.33	40
TOILET/SERVICE BUILDING		209	62.72%	48.66%	02-Jul-26	31-Dec-26	21-May-26 A	04-Mar-27	732,637.91	568,409.84	1,168,074.78	-53
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		44	100%	71.48%	29-Aug-26	21-Sep-26	26-Sep-26 A	21-Oct-26	34,698.32	24,802.48	34,698.32	-25
MECHANICAL WORK		164	58.88%	44.49%	16-Jul-26	19-Dec-26	18-Jul-26 A	24-Jan-27	155,846.41	117,742.89	264,673.10	-31
ELECTRICAL WORKS		114	53.29%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	24-Jan-27	206,217.32	206,217.32	386,998.59	-31
DOORS/WINDOWS		122	88.57%	0%	17-Sep-26	31-Dec-26	13-Oct-26	04-Mar-27	60,445.68	0.00	68,245.12	-53
METAL WORKS		65	57.14%	28.57%	14-Sep-26	23-Nov-26	16-Sep-26 A	12-Dec-26	7,799.44	3,899.72	13,649.02	-16
FINISHING WORKS		100	55.65%	24.42%	22-Sep-26	12-Dec-26	10-Aug-26 A	17-Jan-27	92,446.91	40,563.60	166,130.97	-31
SPECIALTIES WORK		71	0%	0%	18-Oct-26	17-Dec-26	02-Nov-26	23-Jan-27	0.00	0.00	58,495.83	-31
TESTING & COMMISSIONING		17	0%	0%	20-Dec-26	02-Jan-27	18-Feb-27	14-Mar-27	0.00	0.00	0.00	-57
HASA OASIS		337	37.07%	39.89%	03-Mar-26	02-Jan-27	04-Mar-26 A	12-Apr-27	3,690,448.74	3,971,230.60	9,955,979.43	-82
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
ENGINEERING		238	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	15-Dec-26	0.00	0.00	0.00	2
PROCUREMENT		242	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	03-Mar-27	0.00	0.00	0.00	-78
CONSTRUCTION PHASE		316	37.07%	39.89%	29-Mar-26	31-Dec-26	04-Apr-26 A	10-Apr-27	3,690,448.74	3,971,230.60	9,955,979.43	-81
SITE WORKS		316	33.28%	36.05%	29-Mar-26	31-Dec-26	04-Apr-26 A	10-Apr-27	2,925,374.93	3,168,457.26	8,789,975.14	-81
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
LANDSCAPE WORKS		275	31.18%	33.37%	16-May-26	31-Dec-26	16-May-26 A	10-Apr-27	2,630,548.62	2,815,137.62	8,436,655.50	-81
PLAYGROUND AREA		275	72.47%	73.83%	16-May-26	31-Dec-26	18-May-26 A	10-Apr-27	943,212.39	960,876.61	1,301,449.27	-81
FOOTBALL PLAYGROUND		230	80%	85%	16-May-26	09-Dec-26	18-May-26 A	11-Feb-27	253,479.99	269,322.49	316,849.99	-55
PADEL PLAYGROUND		231	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	09-Mar-27	105,292.80	163,788.80	233,984.00	-57
BASKETBALL PLAYGROUND		209	66.63%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	09-Mar-27	222,134.59	236,425.54	333,381.64	-57
PADEL FENCE		111	0%	2.26%	28-Nov-26	31-Dec-26	06-Aug-26 A	10-Apr-27	0.00	1,243.04	54,928.63	-81
CURBSTOEN/INTERLOCK		19	100%	80.07%	09-Sep-26	01-Oct-26	12-Aug-26 A	15-Oct-26	362,305.01	290,096.74	362,305.01	-12
AIR DOME		197	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	22-Mar-27	1,299,527.51	1,299,527.51	5,605,894.61	-83
CIVIL WORKS		185	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	04-Mar-27	1,299,527.51	1,299,527.51	2,690,829.42	-74
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	02-Mar-27	22-Mar-27	0.00	0.00	1,233,296.81	-86
ELECTRICAL WORKS		8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	1,513,591.54	-83
FINISHES WORKS		25	0%	0%	15-Nov-26	10-Dec-26	17-Feb-27	22-Mar-27	0.00	0.00	168,176.84	-83
IRRIGATION NETWORK		153	35.18%	80.44%	03-Sep-26	07-Dec-26	18-Jul-26 A	02-Mar-27	53,620.00	122,596.50	152,414.87	-72
NATURAL GROUND		15	0%	0%	29-Nov-26	07-Dec-26	13-Feb-27	02-Mar-27	0.00	0.00	191,740.00	-72
PLANTING		98	0%	21%	24-Oct-26	02-Nov-26	03-Oct-26 A	14-Feb-27	0.00	72,922.81	347,251.46	-89
WALKING/BIKE PATHS		16	75.51%	70%	29-Sep-26	17-Oct-26	01-Jun-26 A	13-Oct-26	277,594.01	257,343.73	367,633.90	4

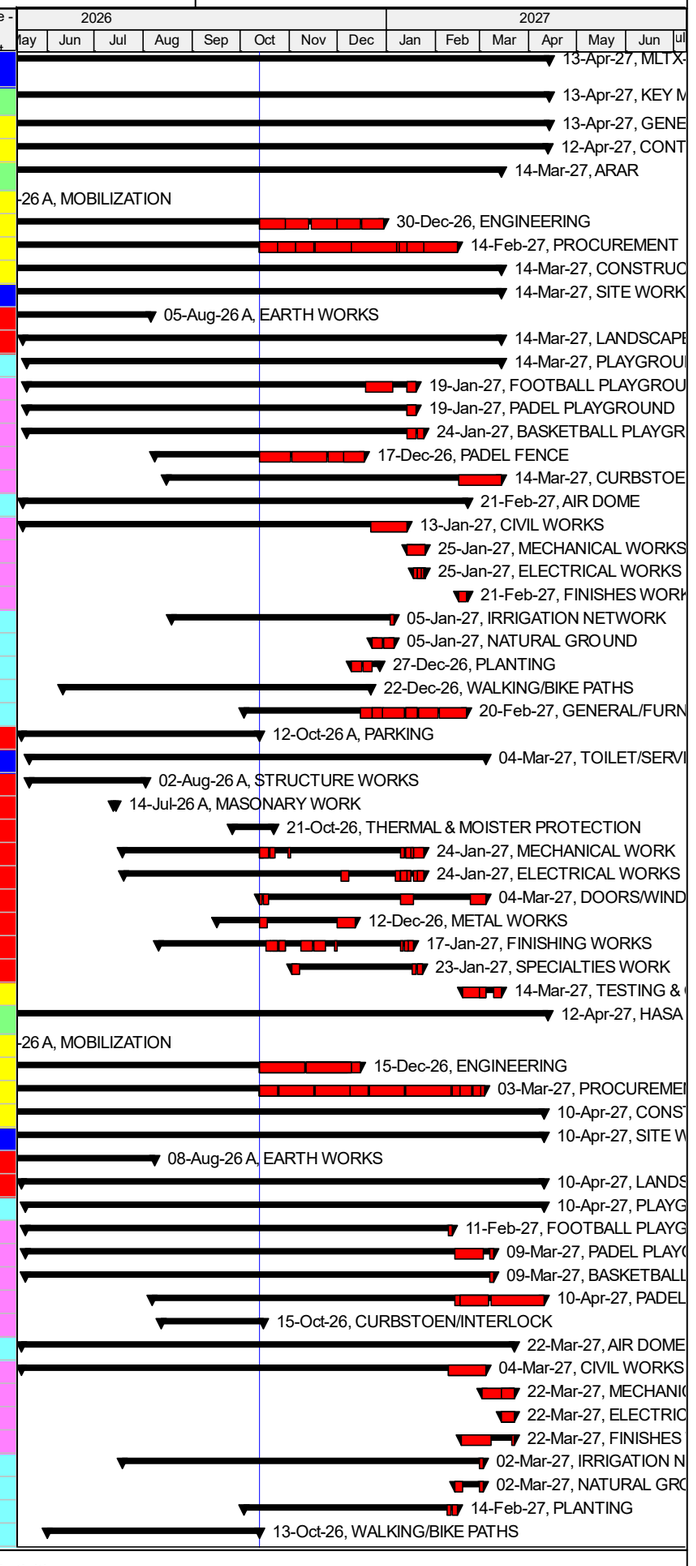

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	133	12.03%	21.66%	06-Oct-26	24-Dec-26	03-Sep-26 A	14-Mar-27	56,594.70	101,870.46	470,271.40	-64
	PARKING	12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
	TOILET/SERVICE BUILDING	265	65.62%	68.85%	09-May-26	23-Dec-26	24-May-26 A	22-Mar-27	765,073.82	802,773.34	1,166,004.29	-72
	STRUCTURE WORKS	45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
	MASONARY WORK	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
	THERMAL & MOISTER PROTECTION	41	100%	90.43%	04-Jul-26	19-Aug-26	10-Sep-26 A	02-Nov-26	34,698.32	31,376.86	34,698.32	-63
	MECHANICAL WORK	165	87.38%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	06-Mar-27	231,268.53	262,723.23	264,673.10	-63
	ELECTRICAL WORKS	158	53.29%	53.29%	03-Sep-26	21-Dec-26	14-Jul-26 A	08-Mar-27	206,217.58	206,217.58	386,998.85	-65
	DOORS/WINDOWS	214	14.29%	14.29%	04-Jul-26	16-Dec-26	28-Sep-26 A	15-Mar-27	9,749.30	9,749.30	68,245.12	-72
	METAL WORKS	66	85.71%	28.57%	03-Sep-26	20-Oct-26	06-Sep-26 A	19-Dec-26	11,699.16	3,899.72	13,649.02	-51
	FINISHING WORKS	151	49.76%	63.02%	20-Aug-26	16-Dec-26	17-Aug-26 A	15-Mar-27	81,633.14	103,386.04	164,060.22	-72
	SPECIALTIES WORK	148	25%	17.5%	27-Sep-26	23-Dec-26	04-Oct-26 A	22-Mar-27	14,623.96	10,236.77	58,495.83	-72
	TESTING & COMMISSIONING	23	0%	0%	08-Dec-26	02-Jan-27	17-Mar-27	12-Apr-27	0.00	0.00	0.00	-82
	DAMMAM	307	36.85%	36.42%	03-Mar-26	02-Jan-27	04-Mar-26 A	04-Mar-27	3,617,395.42	3,574,766.42	9,815,232.20	-52
	MOBILIZATION	33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
	ENGINEERING	250	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	02-Jan-27	0.00	0.00	0.00	-18
	PROCUREMENT	241	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	02-Feb-27	0.00	0.00	0.00	-37
	CONSTRUCTION PHASE	272	36.85%	36.42%	16-Apr-26	31-Dec-26	04-Apr-26 A	04-Mar-27	3,617,395.42	3,574,766.42	9,815,232.20	-53
	SITE WORKS	256	32.53%	32.05%	16-Apr-26	31-Dec-26	04-Apr-26 A	13-Feb-27	2,813,195.85	2,771,929.18	8,649,227.95	-37
	EARTH WORKS	44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
	LANDSCAPE WORKS	234	30.62%	29.42%	12-May-26	31-Dec-26	19-May-26 A	13-Feb-27	2,549,958.08	2,450,198.07	8,327,496.85	-37
	PLAYGROUND AREA	231	77.64%	52.78%	12-May-26	31-Dec-26	19-May-26 A	09-Feb-27	998,526.21	678,847.26	1,286,157.31	-34
	FOOTBALL PLAYGROUND	205	85%	35%	12-May-26	15-Dec-26	19-May-26 A	10-Jan-27	269,322.49	110,897.50	316,849.99	-22
	PADEL PLAYGROUND	216	69.05%	70%	24-May-26	24-Dec-26	19-May-26 A	03-Feb-27	161,560.38	163,788.80	233,984.00	-35
	BASKETBALL PLAYGROUND	167	64.55%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	06-Feb-27	205,338.33	221,133.58	318,089.68	-31
	PADEL FENCE	40	0%	2.26%	25-Nov-26	24-Dec-26	08-Aug-26 A	10-Jan-27	0.00	1,243.04	54,928.63	-14
	CURBSTOEN/INTERLOCK	142	100%	50.17%	27-Aug-26	21-Sep-26	10-Aug-26 A	09-Feb-27	362,305.01	181,784.34	362,305.01	-120
	AIR DOME	192	21.28%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	28-Jan-27	1,193,123.42	1,299,527.51	5,605,894.61	-30
	CIVIL WORKS	169	44.34%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	02-Jan-27	1,193,123.42	1,299,527.51	2,690,829.42	-22
	MECHANICAL WORKS	5	0%	0%	08-Dec-26	13-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	1,233,296.81	-35
	ELECTRICAL WORKS	10	0%	0%	08-Dec-26	24-Dec-26	18-Jan-27	28-Jan-27	0.00	0.00	1,513,591.54	-30
	FINISHES WORKS	4	0%	0%	12-Dec-26	15-Dec-26	21-Jan-27	25-Jan-27	0.00	0.00	168,176.84	-35
	IRRIGATION NETWORK	104	83.53%	80.44%	10-Sep-26	02-Dec-26	24-Aug-26 A	10-Jan-27	127,308.67	122,596.50	152,414.87	-33
	NATURAL GROUND	30	6.78%	0%	10-Oct-26	12-Nov-26	13-Oct-26	16-Nov-26	13,000.00	0.00	191,740.00	-3
	PLANTING	27	0%	0%	06-Dec-26	31-Dec-26	11-Jan-27	10-Feb-27	0.00	0.00	347,251.46	-35
	WALKING/BIKE PATHS	31	51.37%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	140,620.76	273,767.20	273,767.20	35
	GENERAL/FURNITURE	123	16.45%	16.05%	22-Sep-26	31-Dec-26	20-Sep-26 A	13-Feb-27	77,379.02	75,459.60	470,271.40	-37
	PARKING	15	0%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	35
	TOILET/SERVICE BUILDING	236	68.97%	68.85%	01-Jun-26	29-Dec-26	23-May-26 A	04-Mar-27	804,199.57	802,837.24	1,166,004.25	-55
	TESTING & COMMISSIONING	23	0%	0%	24-Dec-26	02-Jan-27	06-Feb-27	04-Mar-27	0.00	0.00	0.00	-52
	PROJECT CLOSEOUT & DEMOBILIZATION	24	0%	0%	08-Dec-26	02-Jan-27	17-Mar-27	13-Apr-27	0.00	0.00	0.00	-83
	As-Built DWGs	20	0%	0%	08-Dec-26	31-Dec-26	17-Mar-27	08-Apr-27	0.00	0.00	0.00	-80
	Demobilization	8	0%	0%	28-Dec-26	02-Jan-27	05-Apr-27	13-Apr-27	0.00	0.00	0.00	-83

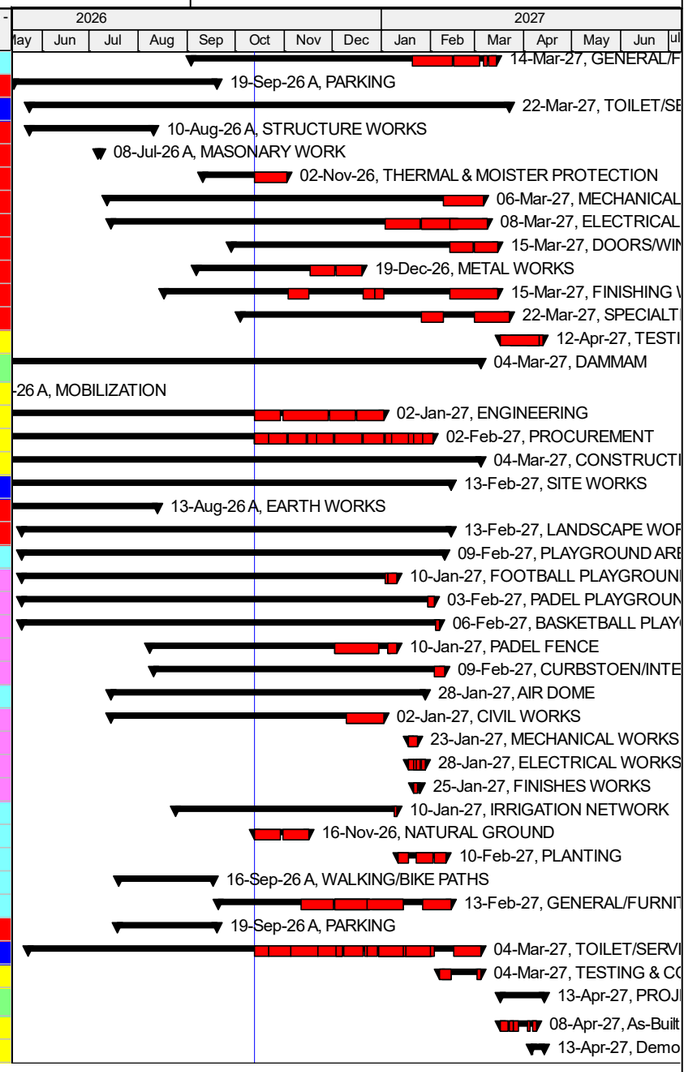

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
