
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		236	7.98%	4.68%	16-Apr-26	02-Jan-27	01-Jun-26 A	13-Apr-27	1,590,033.30	931,932.63	19,926,894.70	-83
KEY MILESTONES		83	0%	0%	17-Dec-26	02-Jan-27	02-Jan-27	13-Apr-27	0.00	0.00	0.00	-83
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	13-Apr-27	13-Apr-27	0.00	0.00	0.00	-83
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		13-Apr-27	0.00	0.00	0.00	-83
CONTRACTUAL MILESTONE		82	0%	0%	17-Dec-26	02-Jan-27	02-Jan-27	12-Apr-27	0.00	0.00	0.00	-82
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		12-Apr-27	0.00	0.00	0.00	-82
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		02-Jan-27	0.00	0.00	0.00	-13
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		10-Apr-27	0.00	0.00	0.00	-81
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		10-Apr-27	0.00	0.00	0.00	-81
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		10-Apr-27	0.00	0.00	0.00	-81
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		14-Mar-27	0.00	0.00	0.00	-58
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		10-Apr-27	0.00	0.00	0.00	-81
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		04-Mar-27	0.00	0.00	0.00	-53
ARAR		210	8.62%	4.82%	27-Jun-26	02-Jan-27	11-Jun-26 A	14-Mar-27	612,807.50	343,117.21	7,112,864.66	-57
ENGINEERING		68	0%	0%	28-Jun-26	08-Dec-26	13-Oct-26	30-Dec-26	0.00	0.00	0.00	-19
SHOP DRAWINGS		68	0%	0%	28-Jun-26	08-Dec-26	13-Oct-26	30-Dec-26	0.00	0.00	0.00	-19
SHOP DRAWINGS SUBMISSION		42	0%	0%	19-Sep-26	07-Nov-26	13-Oct-26	30-Nov-26	0.00	0.00	0.00	-20
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		42	0%	0%	19-Sep-26	07-Nov-26	13-Oct-26	30-Nov-26	0.00	0.00	0.00	-20
ELECTRICAL WORKS		42	0%	0%	19-Sep-26	07-Nov-26	13-Oct-26	30-Nov-26	0.00	0.00	0.00	-20
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	27	74.07%	0%	19-Sep-26	20-Oct-26	13-Oct-26	12-Nov-26	0.00	0.00	0.00	-20
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Layout	15	100%	0%	19-Sep-26	06-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-20
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Riser Diagram	15	0%	0%	21-Oct-26	07-Nov-26	14-Nov-26	30-Nov-26	0.00	0.00	0.00	-20
SHOP DRAWINGS APPROVALS		68	0%	0%	28-Jun-26	08-Dec-26	13-Oct-26	30-Dec-26	0.00	0.00	0.00	-19
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		68	0%	0%	28-Jun-26	08-Dec-26	13-Oct-26	30-Dec-26	0.00	0.00	0.00	-19
ARCHITECTURE WORKS		26	0%	0%	15-Jul-26	13-Aug-26	31-Oct-26	29-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Dome Internal Layout	26	100%	0%	15-Jul-26	13-Aug-26	31-Oct-26	29-Nov-26	0.00	0.00	0.00	-91
AIR DOME SYSTEM		41	0%	0%	28-Jun-26	13-Aug-26	13-Oct-26	29-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Membrane Panel Layout	15	100%	0%	28-Jun-26	14-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Cable Tension Layout	13	100%	0%	30-Jun-26	14-Jul-26	15-Oct-26	29-Oct-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	13	100%	0%	15-Jul-26	29-Jul-26	31-Oct-26	14-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	13	100%	0%	30-Jul-26	13-Aug-26	15-Nov-26	29-Nov-26	0.00	0.00	0.00	-91
SPORTS EQUIPMENT		13	0%	0%	15-Aug-26	29-Aug-26	30-Nov-26	14-Dec-26	0.00	0.00	0.00	-91
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	13	100%	0%	15-Aug-26	29-Aug-26	30-Nov-26	14-Dec-26	0.00	0.00	0.00	-91
ELECTRICAL WORKS		68	0%	0%	26-Sep-26	08-Dec-26	13-Oct-26	30-Dec-26	0.00	0.00	0.00	-19
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	23	65.22%	0%	26-Sep-26	21-Oct-26	13-Oct-26	08-Nov-26	0.00	0.00	0.00	-15
MLTX-02-005-EI	Shop DWG Approval for Power Layout	13	0%	0%	09-Nov-26	23-Nov-26	01-Dec-26	15-Dec-26	0.00	0.00	0.00	-19
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	13	0%	0%	24-Nov-26	08-Dec-26	16-Dec-26	30-Dec-26	0.00	0.00	0.00	-19
PROCUREMENT		107	0%	0%	27-Jun-26	15-Dec-26	13-Oct-26	14-Feb-27	0.00	0.00	0.00	-52
SHORT LEAD ITEM		107	0%	0%	27-Jun-26	15-Dec-26	13-Oct-26	14-Feb-27	0.00	0.00	0.00	-52
TOILET/SERVICE WORKS		69	0%	0%	27-Jun-26	28-Nov-26	13-Oct-26	31-Dec-26	0.00	0.00	0.00	-29
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	-92
MLTX-02-005-PR-E	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	-92
SWITCHES/SOCKETS		42	0%	0%	22-Sep-26	28-Nov-26	13-Oct-26	30-Nov-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-E	PO for Switches/Sockets	15	100%	0%	22-Sep-26	10-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-E	Material Delivery for Switches/Sockets	27	0%	0%	28-Oct-26	28-Nov-26	31-Oct-26	30-Nov-26	0.00	0.00	0.00	-2
DISTRIBUTION PANNELS		44	0%	0%	27-Sep-26	20-Oct-26	13-Oct-26	02-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-E	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	13-Oct-26	18-Oct-26	0.00	0.00	0.00	-14
MLTX-02-005-PR-E	Material Delivery for Distribution Panels	15	53.33%	0%	04-Oct-26	20-Oct-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-37
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	13-Oct-26	31-Dec-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-E	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	13-Oct-26	15-Nov-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-E	Material Delivery for Furnitures	40	17.5%	0%	05-Oct-26	19-Nov-26	16-Nov-26	31-Dec-26	0.00	0.00	0.00	-36
PLAYGROUND WORKS		107	0%	0%	15-Jul-26	15-Dec-26	13-Oct-26	14-Feb-27	0.00	0.00	0.00	-52
PVC MEMBRANE		21	0%	0%	29-Sep-26	22-Oct-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-E	Material Delivery for PVC Membrane	21	57.14%	0%	29-Sep-26	22-Oct-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-27
ARTIFICIAL TURF		12	0%	0%	26-Oct-26	08-Nov-26	11-Jan-27	24-Jan-27	0.00	0.00	0.00	-66
MLTX-02-005-PR-E	Material Delivery for Artificial TURF	12	0%	0%	26-Oct-26	08-Nov-26	11-Jan-27	24-Jan-27	0.00	0.00	0.00	-66
RUBBER GRANULES		32	0%	0%	10-Oct-26	15-Nov-26	31-Oct-26	06-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-E	Material Delivery for Rubber Granules	32	9.38%	0%	10-Oct-26	15-Nov-26	31-Oct-26	06-Dec-26	0.00	0.00	0.00	-18
PADEL GLASS		18	0%	0%	16-Nov-26	06-Dec-26	25-Jan-27	14-Feb-27	0.00	0.00	0.00	-60
MLTX-02-005-PR-E	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	25-Jan-27	14-Feb-27	0.00	0.00	0.00	-60
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-36
MLTX-02-005-PR-E	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-36
BITUMINOUS BASE & WEARING COURSE		27	0%	0%	29-Sep-26	29-Oct-26	31-Oct-26	30-Nov-26	0.00	0.00	0.00	-27

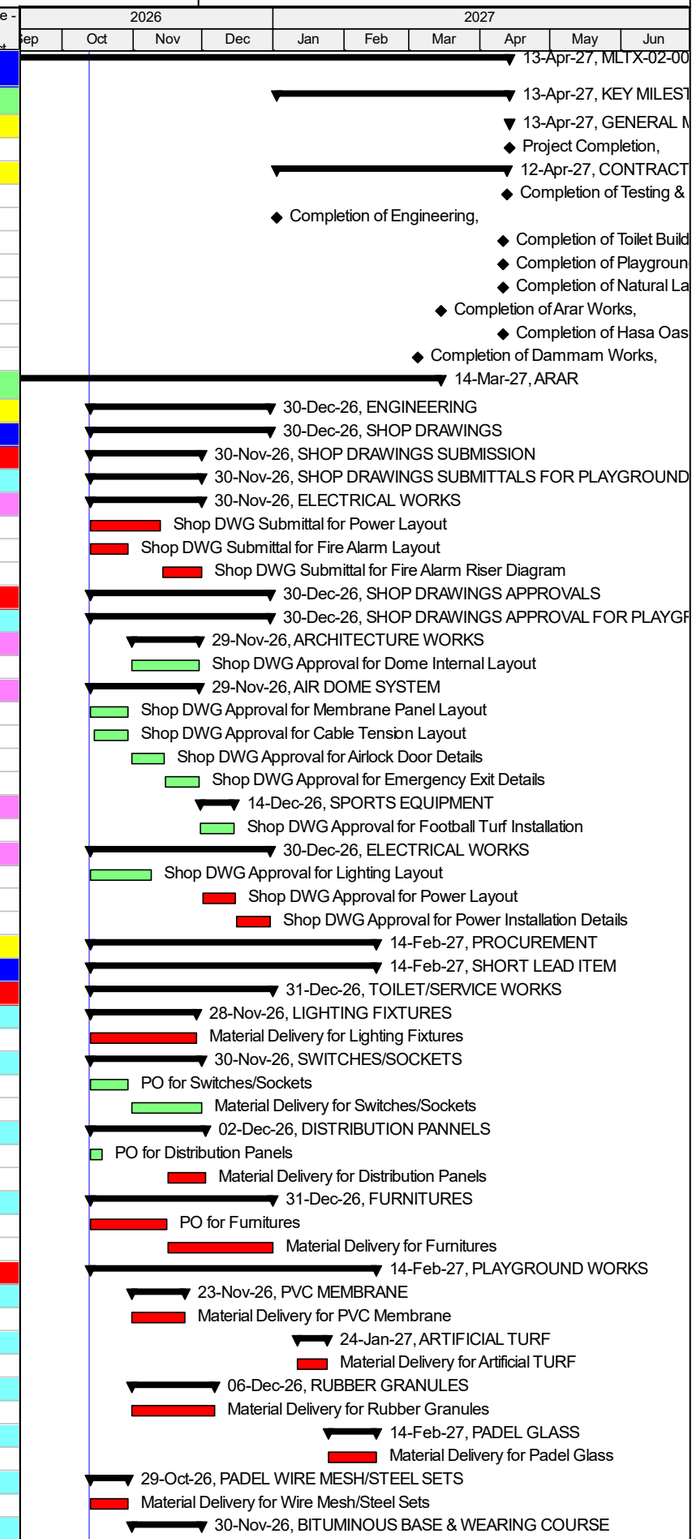

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for the Site	27	44.44%	0%	29-Sep-26	29-Oct-26	31-Oct-26	30-Nov-26	0.00	0.00	0.00	-27
INTERLOCKING PAVING		17	0%	0%	11-Nov-26	30-Nov-26	10-Dec-26	29-Dec-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-9	Material Delivery for Interlocking Block Pavers	17	0%	0%	11-Nov-26	30-Nov-26	10-Dec-26	29-Dec-26	0.00	0.00	0.00	-25
MARKING PAINT		77	0%	0%	10-Sep-26	19-Oct-26	13-Oct-26	10-Jan-27	0.00	0.00	0.00	-71
MLTX-02-005-PR-9	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Marking Paint	17	64.71%	0%	30-Sep-26	19-Oct-26	22-Dec-26	10-Jan-27	0.00	0.00	0.00	-71
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	31-Oct-26	04-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Air Difussers/Grills	15	46.67%	0%	05-Oct-26	21-Oct-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	-27
GALVANIZED DUCTS		20	0%	0%	29-Sep-26	21-Oct-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	PO for Galvanized Duct	5	100%	0%	29-Sep-26	04-Oct-26	31-Oct-26	04-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Galvanized Duct	15	46.67%	0%	05-Oct-26	21-Oct-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	-27
EXHAUST FANS		20	0%	0%	16-Sep-26	10-Oct-26	13-Oct-26	04-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-9	PO for Exhaust Fans	5	100%	0%	16-Sep-26	21-Sep-26	13-Oct-26	18-Oct-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-9	Material Delivery for Exhaust Fans	15	100%	0%	22-Sep-26	10-Oct-26	19-Oct-26	04-Nov-26	0.00	0.00	0.00	-22
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	31-Oct-26	04-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Distribution Boards	15	46.67%	0%	05-Oct-26	21-Oct-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	-27
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	05-Nov-26	13-Jan-27	0.00	0.00	0.00	-25
MLTX-02-005-PR-9	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	05-Nov-26	10-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	10-Dec-26	13-Jan-27	0.00	0.00	0.00	-25
LIGHT FIXTURES		10	0%	0%	11-Oct-26	21-Oct-26	11-Nov-26	22-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	20%	0%	11-Oct-26	21-Oct-26	11-Nov-26	22-Nov-26	0.00	0.00	0.00	-27
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	13-Oct-26	09-Dec-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-9	PO for CCTV	25	60%	0%	26-Sep-26	24-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-15
MLTX-02-005-PR-9	Material Delivery for CCTV	15	0%	0%	25-Oct-26	10-Nov-26	23-Nov-26	09-Dec-26	0.00	0.00	0.00	-25
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-76
LANDSCAPE WORKS		107	0%	0%	15-Jul-26	23-Nov-26	13-Oct-26	14-Feb-27	0.00	0.00	0.00	-71
PAVEMENT MARKING		107	0%	0%	15-Jul-26	23-Nov-26	13-Oct-26	14-Feb-27	0.00	0.00	0.00	-71
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	13-Oct-26	18-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	30	0%	0%	20-Oct-26	23-Nov-26	11-Jan-27	14-Feb-27	0.00	0.00	0.00	-71
TRAFFIC SIGNS		45	0%	0%	27-Jul-26	16-Sep-26	19-Oct-26	09-Dec-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-9	PO for Traffic Signs	15	100%	0%	27-Jul-26	12-Aug-26	19-Oct-26	04-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	30	100%	0%	13-Aug-26	16-Sep-26	05-Nov-26	09-Dec-26	0.00	0.00	0.00	-71
AGRICULTURE SOIL		42	0%	0%	01-Aug-26	12-Sep-26	13-Oct-26	30-Nov-26	0.00	0.00	0.00	-67
MLTX-02-005-PR-9	PO for Agriculture Soil	15	100%	0%	01-Aug-26	17-Aug-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-62
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	05-Nov-26	30-Nov-26	0.00	0.00	0.00	-67
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	10-Dec-26	21-Dec-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	10-Dec-26	21-Dec-26	0.00	0.00	0.00	-71
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-9
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	25	0%	0%	20-Oct-26	17-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-9
LONG LEAD ITEM		89	0%	0%	18-Aug-26	10-Dec-26	13-Oct-26	24-Jan-27	0.00	0.00	0.00	-38
PLAYGROUND WORKS		89	0%	0%	18-Aug-26	10-Dec-26	13-Oct-26	24-Jan-27	0.00	0.00	0.00	-38
STEEL TENSION CABLES		49	0%	0%	18-Aug-26	27-Oct-26	29-Nov-26	24-Jan-27	0.00	0.00	0.00	-76
MLTX-02-005-PR-8	PO for Steel Tension Cables	7	100%	0%	18-Aug-26	25-Aug-26	29-Nov-26	06-Dec-26	0.00	0.00	0.00	-87
MLTX-02-005-PR-8	Material Fabrication for Steel Tension Cables	15	100%	0%	08-Sep-26	26-Sep-26	07-Dec-26	23-Dec-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	15	93.33%	0%	27-Sep-26	13-Oct-26	24-Dec-26	10-Jan-27	0.00	0.00	0.00	-76
MLTX-02-005-PR-9	Staging time	12	0%	0%	14-Oct-26	27-Oct-26	11-Jan-27	24-Jan-27	0.00	0.00	0.00	-76
EMERGENCY DOORS		75	0%	0%	08-Sep-26	05-Dec-26	13-Oct-26	07-Jan-27	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	PO for Emergency Doors	20	100%	0%	08-Sep-26	01-Oct-26	13-Oct-26	04-Nov-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Fabrication for Emergency Doors	20	45%	0%	03-Oct-26	25-Oct-26	05-Nov-26	28-Nov-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	20	0%	0%	26-Oct-26	17-Nov-26	29-Nov-26	21-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-9	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	22-Dec-26	07-Jan-27	0.00	0.00	0.00	-29
PRESSURE UNITS		70	0%	0%	08-Sep-26	29-Nov-26	13-Oct-26	02-Jan-27	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	PO for Pressure Units	10	100%	0%	08-Sep-26	19-Sep-26	13-Oct-26	24-Oct-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Fabrication for Pressure Units	20	45%	0%	03-Oct-26	25-Oct-26	05-Nov-26	28-Nov-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	0%	0%	26-Oct-26	23-Nov-26	29-Nov-26	27-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-9	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	28-Dec-26	02-Jan-27	0.00	0.00	0.00	-29
AIR LOCK DOORS		60	0%	0%	03-Oct-26	10-Dec-26	05-Nov-26	13-Jan-27	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	PO for Lock Doors	10	90%	0%	03-Oct-26	13-Oct-26	05-Nov-26	16-Nov-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	0%	0%	14-Oct-26	05-Nov-26	17-Nov-26	09-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	0%	0%	07-Nov-26	05-Dec-26	10-Dec-26	07-Jan-27	0.00	0.00	0.00	-29
MLTX-02-005-PR-9	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	09-Jan-27	13-Jan-27	0.00	0.00	0.00	-29

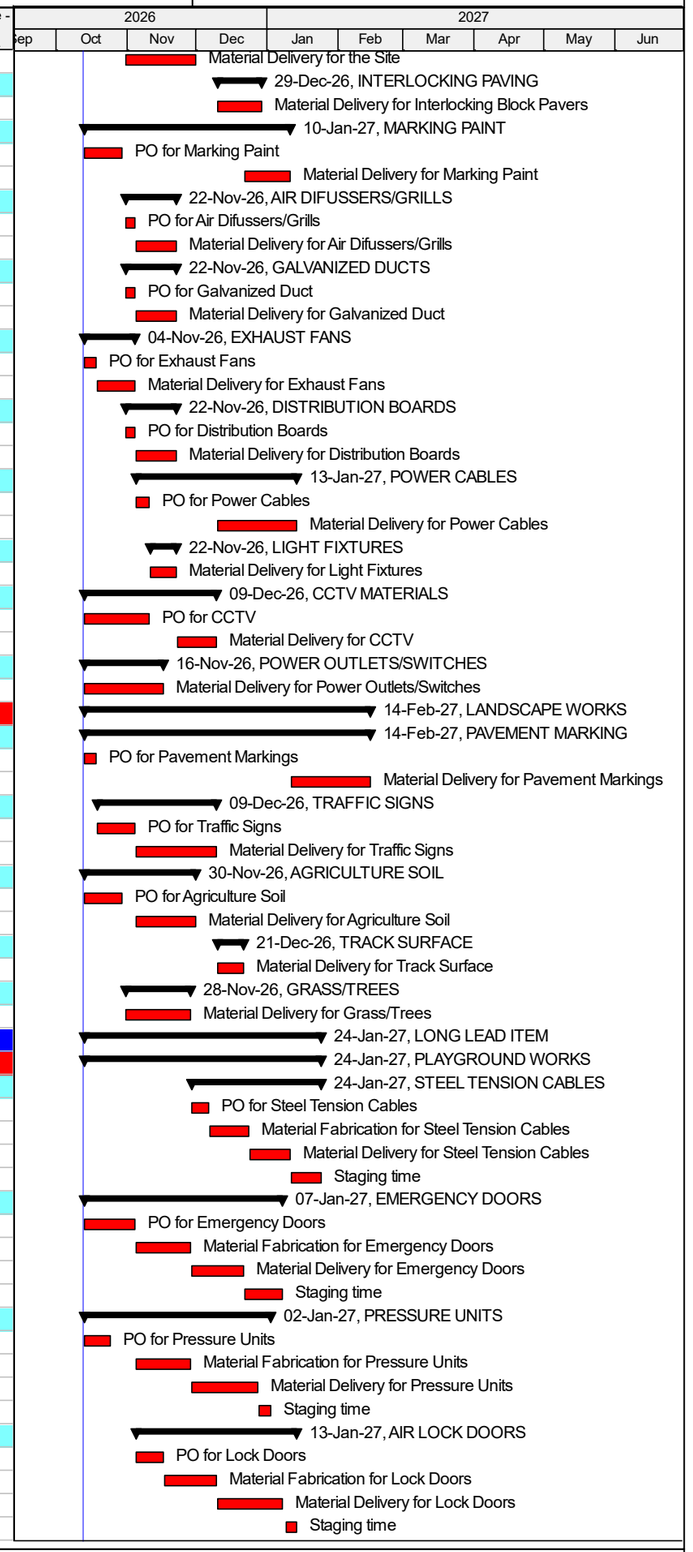

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CONSTRUCTION PHASE		210	8.62%	4.82%	07-Jul-26	31-Dec-26	11-Jun-26 A	14-Mar-27	612,807.50	343,117.21	7,112,864.66	-58
SITE WORKS		210	5.57%	3.93%	07-Jul-26	30-Dec-26	11-Jun-26 A	14-Mar-27	357,659.79	252,197.57	6,422,280.08	-59
LANDSCAPE WORKS		210	5.57%	3.93%	07-Jul-26	30-Dec-26	11-Jun-26 A	14-Mar-27	357,659.79	252,197.57	6,422,280.08	-59
PLAYGROUND AREA		127	2.78%	0%	10-Sep-26	27-Dec-26	13-Oct-26	14-Mar-27	19,173.42	0.00	690,349.18	-62
FOOTBALL PLAYGROUND		28	0%	0%	17-Nov-26	13-Dec-26	19-Dec-26	19-Jan-27	0.00	0.00	205,952.49	-32
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	19-Dec-26	04-Jan-27	0.00	0.00	158,424.99	-27
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	31,685.00	-32
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	15,842.50	-32
PADEL PLAYGROUND		5	0%	0%	14-Dec-26	19-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	70,195.20	-27
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	58,496.00	-27
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	11,699.20	-27
BASKETBALL PLAYGROUND		9	0%	0%	14-Dec-26	23-Dec-26	14-Jan-27	24-Jan-27	0.00	0.00	96,956.10	-27
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	14-Jan-27	19-Jan-27	0.00	0.00	80,796.75	-27
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	20-Jan-27	24-Jan-27	0.00	0.00	16,159.35	-27
PADEL FENCE		57	14.02%	0%	10-Sep-26	16-Nov-26	13-Oct-26	17-Dec-26	19,173.42	0.00	136,724.72	-27
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	17	100%	0%	10-Sep-26	30-Sep-26	13-Oct-26	01-Nov-26	3,834.68	0.00	3,834.68	-27
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	50%	0%	01-Oct-26	24-Oct-26	02-Nov-26	24-Nov-26	15,338.74	0.00	30,677.48	-27
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	0%	0%	25-Oct-26	16-Nov-26	25-Nov-26	17-Dec-26	0.00	0.00	15,338.75	-27
MLTX-02-005-CI	Install of Fence Gates	12	0%	0%	03-Nov-26	16-Nov-26	05-Dec-26	17-Dec-26	0.00	0.00	86,873.81	-27
CURBSTOEN/INTERLOCK		20	0%	0%	05-Dec-26	27-Dec-26	15-Feb-27	14-Mar-27	0.00	0.00	180,520.67	-62
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	05-Dec-26	27-Dec-26	15-Feb-27	14-Mar-27	0.00	0.00	180,520.67	-62
AIR DOME		53	0%	0%	15-Nov-26	21-Dec-26	22-Dec-26	21-Feb-27	0.00	0.00	4,306,367.09	-53
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	22-Dec-26	13-Jan-27	0.00	0.00	1,391,301.90	-32
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	22-Dec-26	13-Jan-27	0.00	0.00	942,830.33	-32
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	22-Dec-26	13-Jan-27	0.00	0.00	448,471.57	-32
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	14-Jan-27	25-Jan-27	0.00	0.00	1,233,296.81	-31
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	14-Jan-27	25-Jan-27	0.00	0.00	728,766.30	-31
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	14-Jan-27	25-Jan-27	0.00	0.00	336,353.67	-31
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	14-Jan-27	25-Jan-27	0.00	0.00	168,176.84	-31
ELECTRICAL WORKS		7	0%	0%	13-Dec-26	20-Dec-26	18-Jan-27	25-Jan-27	0.00	0.00	1,513,591.54	-31
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	18-Jan-27	25-Jan-27	0.00	0.00	224,235.78	-31
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	20-Jan-27	25-Jan-27	0.00	0.00	168,176.84	-31
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	20-Jan-27	25-Jan-27	0.00	0.00	168,176.84	-31
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	23-Jan-27	25-Jan-27	0.00	0.00	504,530.51	-31
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	24-Jan-27	25-Jan-27	0.00	0.00	448,471.57	-31
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	15-Feb-27	21-Feb-27	0.00	0.00	168,176.84	-53
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	15-Feb-27	20-Feb-27	0.00	0.00	112,117.89	-53
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	21-Feb-27	21-Feb-27	0.00	0.00	56,058.95	-53
IRRIGATION NETWORK		156	48.41%	38.73%	07-Jul-26	30-Nov-26	10-Sep-26 A	05-Jan-27	23,560.84	18,848.67	48,667.04	-31
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	4	100%	80%	07-Jul-26	11-Jul-26	10-Sep-26 A	17-Oct-26	23,560.84	18,848.67	23,560.84	-83
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	03-Jan-27	05-Jan-27	0.00	0.00	25,106.20	-31
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	23-Dec-26	05-Jan-27	0.00	0.00	191,740.00	-31
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	30-Dec-26	05-Jan-27	0.00	0.00	126,740.00	-31
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	17-Nov-26	23-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	65,000.00	-31
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	10-Dec-26	27-Dec-26	205,518.96	0.00	347,251.46	-49
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	0%	17-Sep-26	24-Sep-26	10-Dec-26	16-Dec-26	104,175.44	0.00	104,175.44	-71
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	0%	0%	27-Oct-26	31-Oct-26	23-Dec-26	27-Dec-26	0.00	0.00	141,732.50	-49
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	0%	26-Sep-26	30-Sep-26	17-Dec-26	22-Dec-26	101,343.52	0.00	101,343.52	-71
WALKING/BIKE PATHS		24	29.76%	45%	05-Oct-26	01-Nov-26	11-Jun-26 A	22-Dec-26	109,406.57	165,435.26	367,633.90	-43
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	58.33%	45%	05-Oct-26	18-Oct-26	11-Jun-26 A	22-Dec-26	109,406.57	84,399.35	187,554.12	-55
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	0%	45%	19-Oct-26	01-Nov-26	11-Jun-26 A	22-Dec-26	0.00	81,035.90	180,079.78	-43
GENERAL/FURNITURE		107	0%	14.44%	19-Oct-26	30-Dec-26	03-Oct-26 A	20-Feb-27	0.00	67,913.64	470,271.40	-44
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	02-Nov-26	07-Nov-26	23-Dec-26	28-Dec-26	0.00	0.00	93,594.00	-44
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	03-Feb-27	20-Feb-27	0.00	0.00	9,749.30	-44
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	27-Oct-26	03-Nov-26	23-Dec-26	30-Dec-26	0.00	0.00	17,274.79	-49
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	13-Jan-27	20-Jan-27	0.00	0.00	40,307.84	-44
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	13-Jan-27	20-Jan-27	0.00	0.00	32,757.76	-44
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	13-Jan-27	20-Jan-27	0.00	0.00	12,869.04	-44
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	21-Jan-27	02-Feb-27	0.00	0.00	12,186.67	-44
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	7	0%	90%	19-Oct-26	26-Oct-26	03-Oct-26 A	22-Dec-26	0.00	67,913.64	75,459.60	-49
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	0%	08-Nov-26	22-Nov-26	29-Dec-26	12-Jan-27	0.00	0.00	176,072.40	-44
TOILET/SERVICE BUILDING		147	36.95%	13.17%	31-Aug-26	31-Dec-26	28-Sep-26 A	04-Mar-27	255,147.71	90,919.64	690,584.58	-53
THERMAL & MOISTER PROTECTION		31	100%	54.02%	31-Aug-26	21-Sep-26	03-Oct-26 A	21-Oct-26	21,520.94	11,625.10	21,520.94	-25
MLTX-02-005-CN-110	Finalize Water Proofing Works for Toilets	6	100%	0%	31-Aug-26	06-Sep-26	13-Oct-26	19-Oct-26	4,913.66	0.00	4,913.66	-36

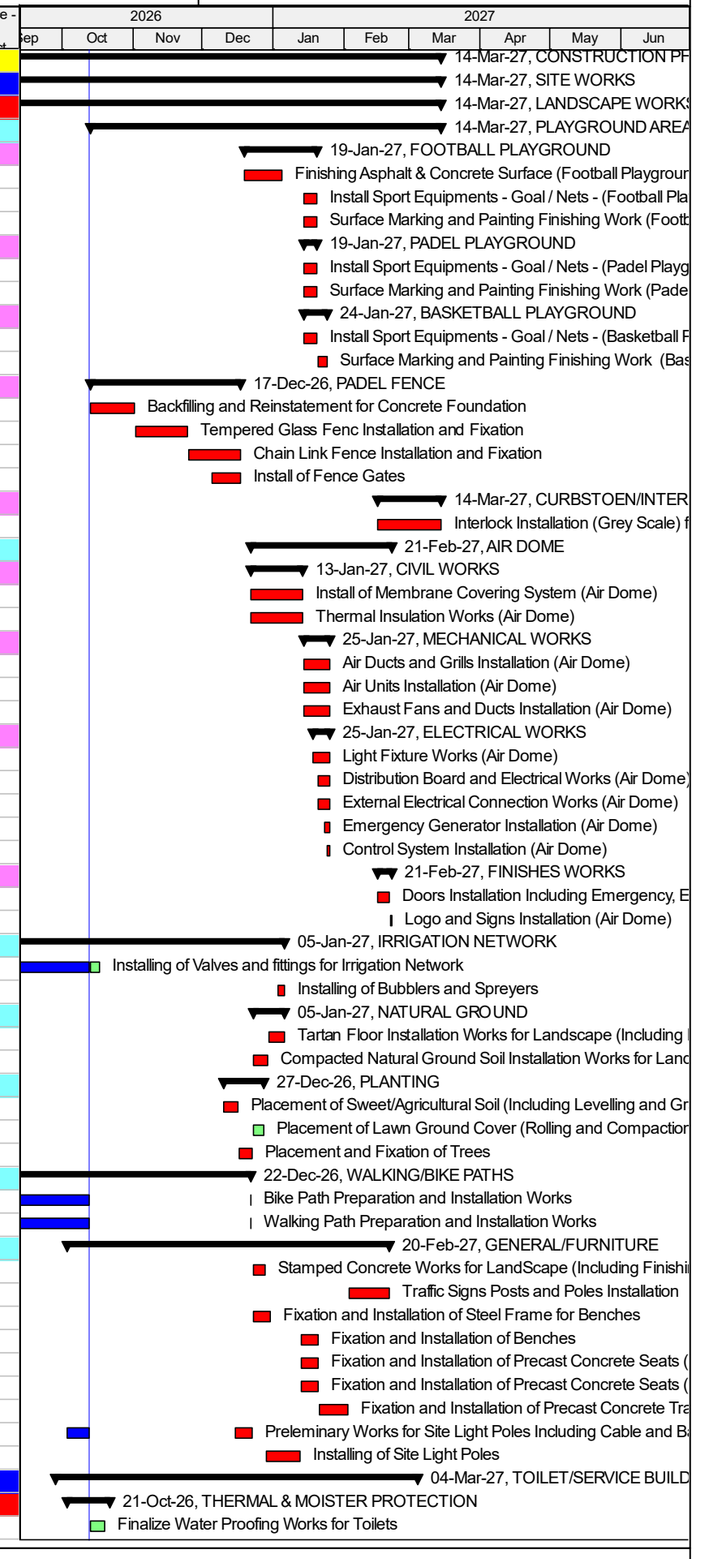

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-110	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	70%	13-Sep-26	21-Sep-26	03-Oct-26 A	21-Oct-26	16,607.28	11,625.10	16,607.28	-25
MECHANICAL WORK		99	51.89%	35.05%	29-Sep-26	19-Dec-26	28-Sep-26 A	24-Jan-27	117,398.06	79,294.54	226,224.75	-31
HVAC SYSTEM		3	0%	0%	05-Dec-26	07-Dec-26	10-Jan-27	12-Jan-27	0.00	0.00	14,623.96	-31
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	0%	0%	05-Dec-26	07-Dec-26	10-Jan-27	12-Jan-27	0.00	0.00	14,623.96	-31
WATER SUPPLY SYSTEM		99	64.31%	56.04%	01-Oct-26	19-Dec-26	28-Sep-26 A	24-Jan-27	90,993.76	79,294.54	141,495.15	-31
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	80%	01-Oct-26	04-Oct-26	29-Sep-26 A	15-Oct-26	25,998.40	20,798.72	25,998.40	-10
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	17-Jan-27	24-Jan-27	0.00	0.00	48,746.52	-31
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	90%	01-Oct-26	10-Oct-26	28-Sep-26 A	21-Oct-26	64,995.36	58,495.82	64,995.36	-10
MLTX-02-005-CN-1	Installing of Water Heater	4	0%	0%	08-Dec-26	12-Dec-26	13-Jan-27	17-Jan-27	0.00	0.00	1,754.87	-31
SEWER/DRAINAGE SYSTEM		83	38.74%	0%	29-Sep-26	12-Dec-26	13-Oct-26	17-Jan-27	26,404.30	0.00	68,155.77	-31
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	05-Oct-26	08-Oct-26	19-Oct-26	22-Oct-26	14,217.67	0.00	14,217.67	-12
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	0%	0%	15-Oct-26	17-Oct-26	31-Oct-26	01-Nov-26	0.00	0.00	10,358.68	-13
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	29-Sep-26	04-Oct-26	13-Oct-26	18-Oct-26	12,186.63	0.00	12,186.63	-12
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	0%	0%	08-Dec-26	12-Dec-26	13-Jan-27	17-Jan-27	0.00	0.00	31,392.79	-31
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	16-Jan-27	17-Jan-27	0.00	0.00	1,949.87	-28
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	16-Jan-27	17-Jan-27	0.00	0.00	1,949.87	-28
ELECTRICAL WORKS		45	0%	0%	09-Nov-26	19-Dec-26	03-Dec-26	24-Jan-27	0.00	0.00	180,781.27	-31
FIXTURE WORKS		45	0%	0%	09-Nov-26	19-Dec-26	03-Dec-26	24-Jan-27	0.00	0.00	180,781.27	-31
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	0%	0%	09-Nov-26	14-Nov-26	03-Dec-26	08-Dec-26	0.00	0.00	102,367.69	-21
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	18-Jan-27	21-Jan-27	0.00	0.00	6,239.59	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	12-Jan-27	16-Jan-27	0.00	0.00	7,085.10	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	06-Jan-27	09-Jan-27	0.00	0.00	6,824.51	-31
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	20-Jan-27	24-Jan-27	0.00	0.00	34,317.53	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	12-Jan-27	16-Jan-27	0.00	0.00	14,259.43	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	10-Jan-27	16-Jan-27	0.00	0.00	2,437.33	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	10-Jan-27	13-Jan-27	0.00	0.00	7,250.09	-31
DOORS/WINDOWS		122	88.57%	0%	17-Sep-26	31-Dec-26	13-Oct-26	04-Mar-27	60,445.68	0.00	68,245.12	-53
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	17-Sep-26	19-Sep-26	13-Oct-26	14-Oct-26	52,646.24	0.00	52,646.24	-21
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	0%	20-Sep-26	22-Sep-26	15-Oct-26	18-Oct-26	7,799.44	0.00	7,799.44	-21
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	9	0%	0%	22-Dec-26	31-Dec-26	23-Feb-27	04-Mar-27	0.00	0.00	1,949.86	-53
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	0%	0%	05-Dec-26	12-Dec-26	10-Jan-27	17-Jan-27	0.00	0.00	5,849.58	-31
METAL WORKS		52	40%	0%	14-Sep-26	23-Nov-26	13-Oct-26	12-Dec-26	3,899.72	0.00	9,749.30	-16
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	10	0%	0%	12-Nov-26	23-Nov-26	01-Dec-26	12-Dec-26	0.00	0.00	5,849.58	-16
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	13-Oct-26	17-Oct-26	3,899.72	0.00	3,899.72	-24
FINISHING WORKS		83	41.32%	0%	04-Oct-26	12-Dec-26	13-Oct-26	17-Jan-27	51,883.31	0.00	125,567.37	-31
FLOOR FINISHES		78	89.77%	0%	04-Oct-26	12-Dec-26	19-Oct-26	17-Jan-27	15,404.15	0.00	17,159.03	-31
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	04-Oct-26	05-Oct-26	19-Oct-26	20-Oct-26	11,894.39	0.00	11,894.39	-13
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	21-Oct-26	25-Oct-26	2,924.82	0.00	2,924.82	-13
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	14-Jan-27	17-Jan-27	0.00	0.00	1,169.94	-31
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	50%	0%	11-Oct-26	14-Oct-26	26-Oct-26	29-Oct-26	584.94	0.00	1,169.88	-13
WALL FINISHES		75	32.86%	0%	06-Oct-26	06-Dec-26	17-Oct-26	11-Jan-27	30,707.64	0.00	93,437.44	-31
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	0%	0%	14-Oct-26	19-Oct-26	25-Oct-26	29-Oct-26	0.00	0.00	2,275.00	-9
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	0%	0%	01-Nov-26	08-Nov-26	16-Nov-26	23-Nov-26	0.00	0.00	13,649.02	-13
MLTX-02-005-CN-1	Granite Capping for Parpet	2	0%	0%	10-Nov-26	11-Nov-26	29-Nov-26	30-Nov-26	0.00	0.00	8,150.24	-16
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	85.71%	0%	06-Oct-26	13-Oct-26	17-Oct-26	24-Oct-26	30,707.64	0.00	35,825.58	-9
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	0%	0%	24-Oct-26	31-Oct-26	08-Nov-26	15-Nov-26	0.00	0.00	31,197.60	-13
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	0%	0%	05-Dec-26	06-Dec-26	10-Jan-27	11-Jan-27	0.00	0.00	2,340.00	-31
CELLING FINISHES		81	38.55%	0%	12-Oct-26	09-Dec-26	13-Oct-26	14-Jan-27	5,771.52	0.00	14,970.90	-31
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	15	0%	0%	15-Nov-26	01-Dec-26	24-Nov-26	10-Dec-26	0.00	0.00	5,771.52	-8
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	0%	0%	07-Dec-26	09-Dec-26	12-Jan-27	14-Jan-27	0.00	0.00	3,427.86	-31
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	14.29%	0%	12-Oct-26	19-Oct-26	13-Oct-26	20-Oct-26	5,771.52	0.00	5,771.52	-1
SPECIALTIES WORK		71	0%	0%	18-Oct-26	17-Dec-26	02-Nov-26	23-Jan-27	0.00	0.00	58,495.83	-31
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	20-Jan-27	23-Jan-27	0.00	0.00	24,373.26	-31
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	0%	0%	18-Oct-26	22-Oct-26	02-Nov-26	07-Nov-26	0.00	0.00	14,623.96	-13
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	17-Jan-27	19-Jan-27	0.00	0.00	19,498.61	-31
TESTING & COMMISSIONING		17	0%	0%	20-Dec-26	02-Jan-27	18-Feb-27	14-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	09-Mar-27	14-Mar-27	0.00	0.00	0.00	-58
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	18-Feb-27	04-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	28-Feb-27	04-Mar-27	0.00	0.00	0.00	-53
HASA OASIS		215	7.79%	8.27%	04-May-26	02-Jan-27	01-Jun-26 A	12-Apr-27	508,220.42	539,604.09	6,524,352.93	-82
ENGINEERING		55	0%	0%	04-May-26	01-Dec-26	13-Oct-26	15-Dec-26	0.00	0.00	0.00	-12
SHOP DRAWINGS		55	0%	0%	04-May-26	01-Dec-26	13-Oct-26	15-Dec-26	0.00	0.00	0.00	-12
SHOP DRAWINGS SUBMISSION		55	0%	0%	04-May-26	01-Dec-26	13-Oct-26	15-Dec-26	0.00	0.00	0.00	-12
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		55	0%	0%	04-May-26	01-Dec-26	13-Oct-26	15-Dec-26	0.00	0.00	0.00	-12

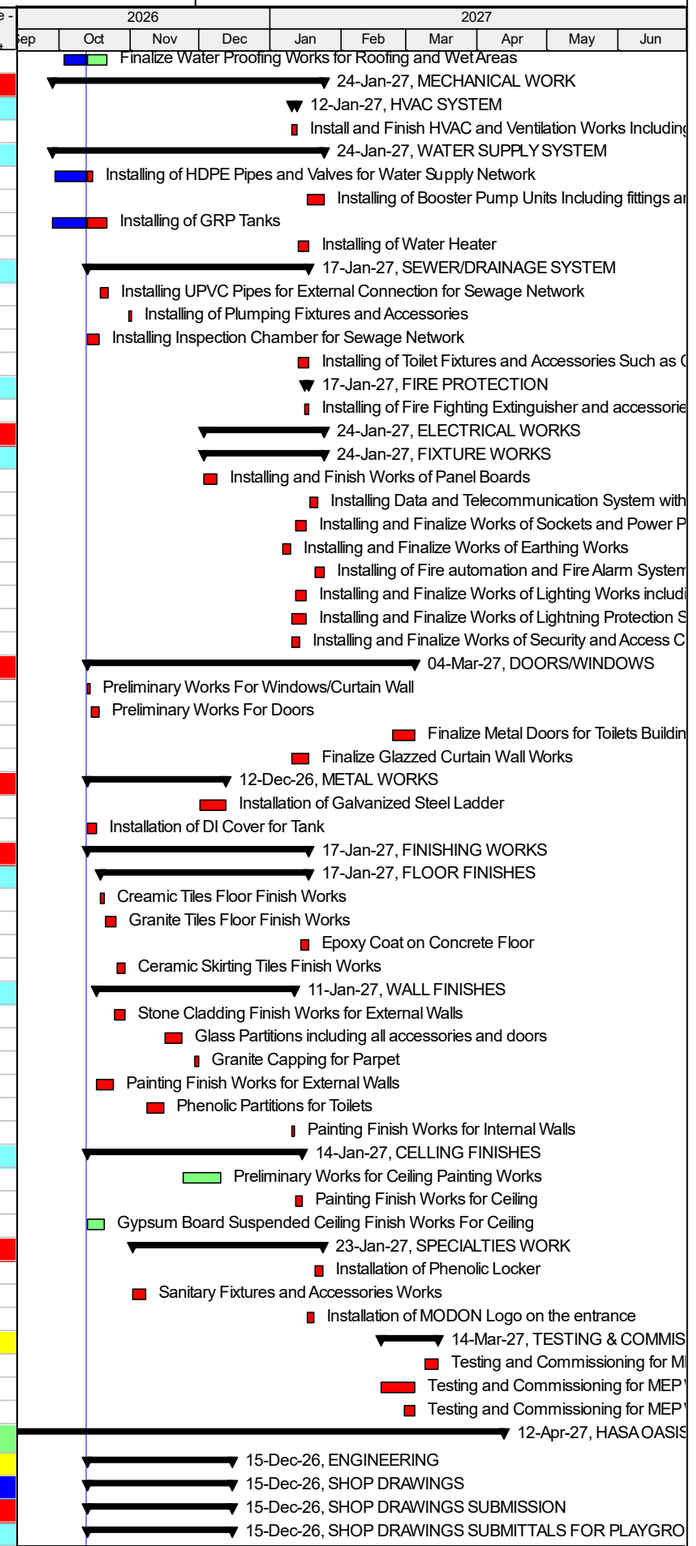

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MECHANCAL WORKS		25	0%	0%	26-Sep-26	24-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	25	60%	0%	26-Sep-26	24-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	25	60%	0%	26-Sep-26	24-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-15
ELECTRICAL WORKS		55	0%	0%	04-May-26	01-Dec-26	13-Oct-26	15-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	25	60%	0%	26-Sep-26	24-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-135
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	25	48%	0%	29-Sep-26	27-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	25	48%	0%	29-Sep-26	27-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	25	48%	0%	29-Sep-26	27-Oct-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	30	0%	0%	25-Oct-26	28-Nov-26	11-Nov-26	15-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	0%	0%	25-Oct-26	28-Nov-26	11-Nov-26	15-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	30	0%	0%	28-Oct-26	01-Dec-26	11-Nov-26	15-Dec-26	0.00	0.00	0.00	-12
SHOP DRAWINGS APPROVALS		50	0%	0%	06-Jun-26	25-Nov-26	13-Oct-26	09-Dec-26	0.00	0.00	0.00	-12
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		50	0%	0%	06-Jun-26	25-Nov-26	13-Oct-26	09-Dec-26	0.00	0.00	0.00	-12
SPORTS EQUIPMENT		21	0%	0%	10-Oct-26	02-Nov-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-3
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	21	14.29%	0%	10-Oct-26	02-Nov-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-3
MECHANCAL WORKS		23	0%	0%	25-Oct-26	19-Nov-26	11-Nov-26	07-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Approval for HVAC Plan	23	0%	0%	25-Oct-26	19-Nov-26	11-Nov-26	07-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Approval for Exhaust Air Plan	23	0%	0%	25-Oct-26	19-Nov-26	11-Nov-26	07-Dec-26	0.00	0.00	0.00	-15
ELECTRICAL WORKS		25	0%	0%	06-Jun-26	25-Nov-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	25	0%	0%	25-Oct-26	22-Nov-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-135
MLTX-02-005-EM	Shop DWG Approval for Power Single Line Diagram	25	0%	0%	28-Oct-26	25-Nov-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Approval for Panel Board Schedules	25	0%	0%	28-Oct-26	25-Nov-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	25	0%	0%	28-Oct-26	25-Nov-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-12
PROCUREMENT		121	0%	0%	10-Jun-26	01-Dec-26	13-Oct-26	03-Mar-27	0.00	0.00	0.00	-78
SHORT LEAD ITEM		121	0%	0%	16-Jun-26	01-Dec-26	13-Oct-26	03-Mar-27	0.00	0.00	0.00	-78
TOILET/SERVICE WORKS		49	0%	0%	16-Jun-26	19-Oct-26	13-Oct-26	08-Dec-26	0.00	0.00	0.00	-43
LIGHTING FIXTURES		20	0%	0%	16-Jun-26	08-Jul-26	13-Oct-26	04-Nov-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	20	100%	0%	16-Jun-26	08-Jul-26	13-Oct-26	04-Nov-26	0.00	0.00	0.00	-101
SWITCHES/SOCKETS		32	0%	0%	16-Jun-26	22-Jul-26	13-Oct-26	18-Nov-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	PO for Switches/Sockets	15	100%	0%	16-Jun-26	02-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	17	100%	0%	04-Jul-26	22-Jul-26	31-Oct-26	18-Nov-26	0.00	0.00	0.00	-101
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	13-Oct-26	04-Nov-26	0.00	0.00	0.00	-14
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	13-Oct-26	18-Oct-26	0.00	0.00	0.00	-14
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	60%	0%	03-Oct-26	19-Oct-26	19-Oct-26	04-Nov-26	0.00	0.00	0.00	-14
FURNITURES		49	0%	0%	16-Jun-26	11-Aug-26	13-Oct-26	08-Dec-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	13-Oct-26	03-Nov-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Furnitures	30	100%	0%	08-Jul-26	11-Aug-26	04-Nov-26	08-Dec-26	0.00	0.00	0.00	-101
PLAYGROUND WORKS		121	0%	0%	28-Jun-26	01-Dec-26	13-Oct-26	03-Mar-27	0.00	0.00	0.00	-78
PVC MEMBRANE		30	0%	0%	29-Sep-26	02-Nov-26	31-Oct-26	03-Dec-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	40%	0%	29-Sep-26	02-Nov-26	31-Oct-26	03-Dec-26	0.00	0.00	0.00	-27
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	36.67%	0%	30-Sep-26	03-Nov-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-11
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	63.33%	0%	20-Sep-26	25-Oct-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-19
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	73.33%	0%	16-Sep-26	21-Oct-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-22
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-22
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	13-Oct-26	18-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-91
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	31-Oct-26	18-Nov-26	0.00	0.00	0.00	-91
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	4%	0%	12-Oct-26	09-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-16
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	4%	0%	12-Oct-26	09-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-16
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	28%	0%	05-Oct-26	02-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-22
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	PO for Distribution Boards	5	60%	0%	10-Oct-26	14-Oct-26	31-Oct-26	04-Nov-26	0.00	0.00	0.00	-18



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	0%	0%	15-Oct-26	01-Nov-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	-18
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	17-Nov-26	27-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	PO for Power Cables	15	0%	0%	22-Oct-26	08-Nov-26	17-Nov-26	03-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0%	0%	09-Nov-26	01-Dec-26	05-Dec-26	27-Dec-26	0.00	0.00	0.00	-22
LIGHT FIXTURES		20	0%	0%	09-Nov-26	01-Dec-26	08-Feb-27	03-Mar-27	0.00	0.00	0.00	-78
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	09-Nov-26	01-Dec-26	08-Feb-27	03-Mar-27	0.00	0.00	0.00	-78
CCTV MATERIALS		88	0%	0%	04-Jul-26	29-Nov-26	13-Oct-26	23-Jan-27	0.00	0.00	0.00	-47
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	06-Jan-27	23-Jan-27	0.00	0.00	0.00	-47
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	19-Nov-26	05-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	19-Nov-26	07-Dec-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	13-Oct-26	10-Nov-26	08-Dec-26	05-Jan-27	0.00	0.00	0.00	-48
LANDSCAPE WORKS		53	0%	0%	11-Aug-26	04-Nov-26	08-Dec-26	07-Feb-27	0.00	0.00	0.00	-81
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	08-Dec-26	14-Jan-27	0.00	0.00	0.00	-61
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	08-Dec-26	22-Dec-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	0%	0%	13-Oct-26	04-Nov-26	23-Dec-26	14-Jan-27	0.00	0.00	0.00	-61
TRAFFIC SIGNS		20	0%	0%	03-Sep-26	27-Sep-26	23-Dec-26	14-Jan-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Traffic Signs	15	100%	0%	03-Sep-26	20-Sep-26	23-Dec-26	09-Jan-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	10-Jan-27	14-Jan-27	0.00	0.00	0.00	-94
TRACK SURFACE		2	0%	0%	29-Aug-26	30-Aug-26	23-Dec-26	24-Dec-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	23-Dec-26	24-Dec-26	0.00	0.00	0.00	-99
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	10-Jan-27	07-Feb-27	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	52%	0%	28-Sep-26	26-Oct-26	10-Jan-27	07-Feb-27	0.00	0.00	0.00	-89
LONG LEAD ITEM		119	0%	0%	10-Jun-26	16-Nov-26	13-Oct-26	01-Mar-27	0.00	0.00	0.00	-89
PLAYGROUND WORKS		119	0%	0%	10-Jun-26	16-Nov-26	13-Oct-26	01-Mar-27	0.00	0.00	0.00	-89
STEEL TENSION CABLES		43	0%	0%	01-Sep-26	21-Oct-26	21-Dec-26	08-Feb-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Steel Tension Cables	7	100%	0%	01-Sep-26	08-Sep-26	21-Dec-26	28-Dec-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	10-Jan-27	27-Jan-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	09-Sep-26	20-Sep-26	29-Dec-26	09-Jan-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Staging time	10	20%	0%	11-Oct-26	21-Oct-26	28-Jan-27	08-Feb-27	0.00	0.00	0.00	-94
EMERGENCY DOORS		60	0%	0%	10-Jun-26	18-Aug-26	13-Oct-26	21-Dec-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	10-Jun-26	21-Jun-26	13-Oct-26	24-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	17-Nov-26	15-Dec-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	22-Jun-26	14-Jul-26	25-Oct-26	16-Nov-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	16-Dec-26	21-Dec-26	0.00	0.00	0.00	-106
PRESSURE UNITS		60	0%	0%	07-Sep-26	16-Nov-26	21-Dec-26	01-Mar-27	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	07-Sep-26	17-Sep-26	21-Dec-26	31-Dec-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	0%	0%	13-Oct-26	10-Nov-26	25-Jan-27	23-Feb-27	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	19-Sep-26	12-Oct-26	02-Jan-27	24-Jan-27	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	24-Feb-27	01-Mar-27	0.00	0.00	0.00	-89
AIR LOCK DOORS		60	0%	0%	20-Aug-26	05-Nov-26	09-Dec-26	16-Feb-27	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	20-Aug-26	31-Aug-26	09-Dec-26	20-Dec-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	36%	0%	03-Oct-26	31-Oct-26	13-Jan-27	10-Feb-27	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	08-Sep-26	01-Oct-26	21-Dec-26	12-Jan-27	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	Staging time	5	0%	0%	01-Nov-26	05-Nov-26	11-Feb-27	16-Feb-27	0.00	0.00	0.00	-88
CONSTRUCTION PHASE		213	7.79%	8.27%	30-Jul-26	31-Dec-26	01-Jun-26 A	10-Apr-27	508,220.42	539,604.09	6,524,352.93	-81
SITE WORKS		162	7.5%	7.92%	29-Sep-26	31-Dec-26	01-Jun-26 A	10-Apr-27	458,114.68	483,838.47	6,105,356.36	-81
LANDSCAPE WORKS		162	7.5%	7.92%	29-Sep-26	31-Dec-26	01-Jun-26 A	10-Apr-27	458,114.68	483,838.47	6,105,356.36	-81
PLAYGROUND AREA		162	40.22%	24.13%	29-Sep-26	31-Dec-26	21-Sep-26 A	10-Apr-27	180,520.67	108,312.40	448,885.06	-81
FOOTBALL PLAYGROUND		77	0%	0%	17-Nov-26	09-Dec-26	15-Nov-26	11-Feb-27	0.00	0.00	47,527.50	-55
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	15-Nov-26	07-Dec-26	0.00	0.00	31,685.00	2
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	09-Feb-27	11-Feb-27	0.00	0.00	15,842.50	-72
PADEL PLAYGROUND		21	0%	0%	12-Dec-26	31-Dec-26	13-Feb-27	09-Mar-27	0.00	0.00	70,195.20	-57
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	13-Feb-27	02-Mar-27	0.00	0.00	58,496.00	-54
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	07-Mar-27	09-Mar-27	0.00	0.00	11,699.20	-57
BASKETBALL PLAYGROUND		98	0%	0%	17-Nov-26	31-Dec-26	15-Nov-26	09-Mar-27	0.00	0.00	96,956.10	-57
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	15-Nov-26	25-Nov-26	0.00	0.00	80,796.75	2
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	07-Mar-27	09-Mar-27	0.00	0.00	16,159.35	-57
PADEL FENCE		45	0%	0%	29-Nov-26	31-Dec-26	13-Feb-27	10-Apr-27	0.00	0.00	53,685.59	-81
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	18	0%	0%	29-Nov-26	19-Dec-26	13-Feb-27	06-Mar-27	0.00	0.00	3,834.68	-65
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	30,677.48	-65
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	15,338.75	-65
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	08-Mar-27	10-Apr-27	0.00	0.00	3,834.68	-81
CURBSTOEN/INTERLOCK		3	100%	60%	29-Sep-26	01-Oct-26	21-Sep-26 A	15-Oct-26	180,520.67	108,312.40	180,520.67	-12

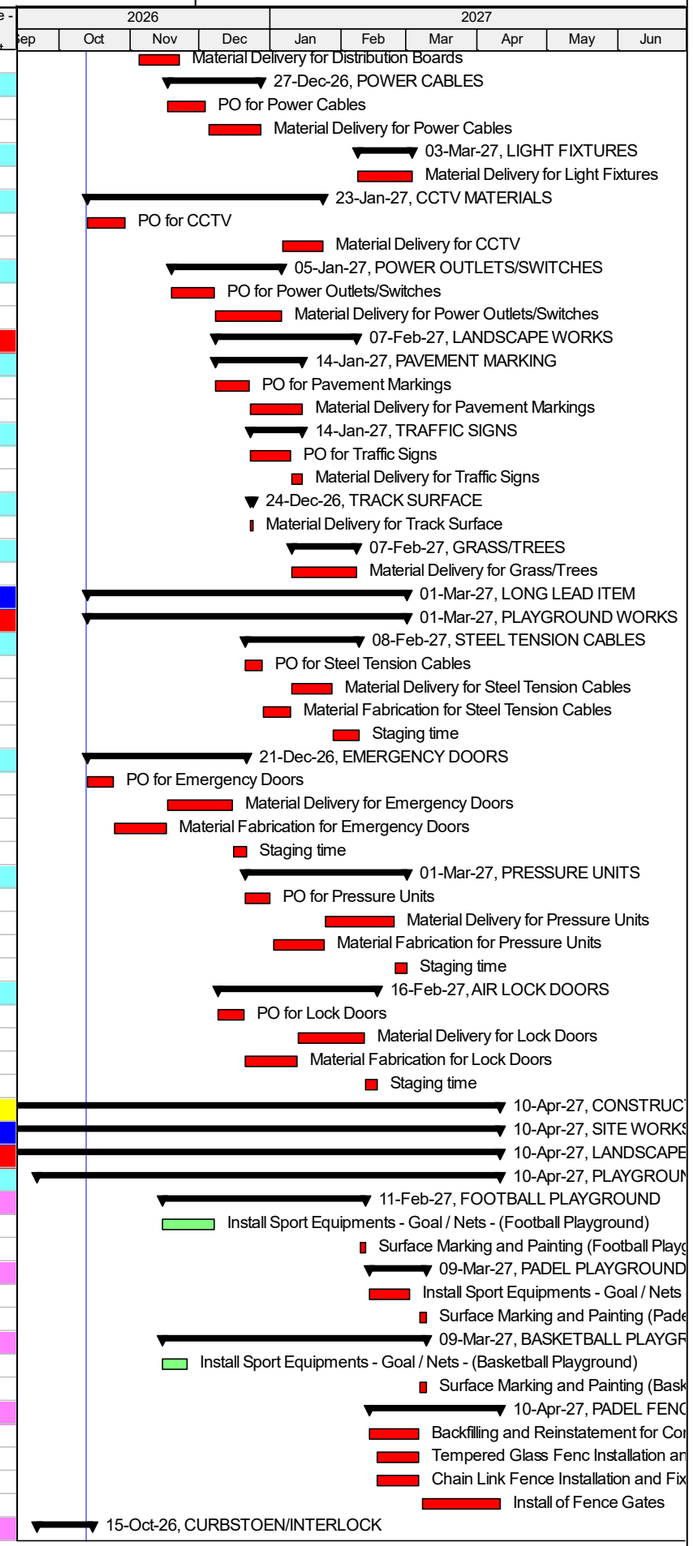

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	60%	29-Sep-26	01-Oct-26	21-Sep-26 A	15-Oct-26	180,520.67	108,312.40	180,520.67	-12
AIR DOME		32	0%	0%	15-Nov-26	10-Dec-26	09-Feb-27	22-Mar-27	0.00	0.00	4,306,367.09	-83
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	09-Feb-27	04-Mar-27	0.00	0.00	1,391,301.90	-74
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	09-Feb-27	04-Mar-27	0.00	0.00	942,830.33	-74
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	09-Feb-27	04-Mar-27	0.00	0.00	448,471.57	-74
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	02-Mar-27	22-Mar-27	0.00	0.00	1,233,296.81	-86
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	02-Mar-27	22-Mar-27	0.00	0.00	728,766.30	-86
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	336,353.67	-86
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	168,176.84	-86
ELECTRICAL WORKS		8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	1,513,591.54	-83
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	224,235.78	-83
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	168,176.84	-83
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	168,176.84	-83
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	504,530.51	-83
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	14-Mar-27	22-Mar-27	0.00	0.00	448,471.57	-83
FINISHES WORKS		25	0%	0%	15-Nov-26	10-Dec-26	17-Feb-27	22-Mar-27	0.00	0.00	168,176.84	-83
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	17-Feb-27	07-Mar-27	0.00	0.00	112,117.89	-81
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	21-Mar-27	22-Mar-27	0.00	0.00	56,058.95	-83
IRRIGATION NETWORK		90	0%	38.73%	17-Nov-26	07-Dec-26	10-Sep-26 A	02-Mar-27	0.00	18,848.67	48,667.04	-72
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	10	0%	80%	17-Nov-26	28-Nov-26	10-Sep-26 A	14-Nov-26	0.00	18,848.67	23,560.84	12
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	28-Feb-27	02-Mar-27	0.00	0.00	25,106.20	-72
NATURAL GROUND		15	0%	0%	29-Nov-26	07-Dec-26	13-Feb-27	02-Mar-27	0.00	0.00	191,740.00	-72
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	05-Dec-26	07-Dec-26	28-Feb-27	02-Mar-27	0.00	0.00	126,740.00	-72
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	29-Nov-26	03-Dec-26	13-Feb-27	17-Feb-27	0.00	0.00	65,000.00	-65
PLANTING		98	0%	21%	24-Oct-26	02-Nov-26	03-Oct-26 A	14-Feb-27	0.00	72,922.81	347,251.46	-89
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	0%	70%	24-Oct-26	26-Oct-26	03-Oct-26 A	15-Oct-26	0.00	72,922.81	104,175.44	9
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	31-Oct-26	02-Nov-26	11-Feb-27	14-Feb-27	0.00	0.00	141,732.50	-89
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	0%	0%	27-Oct-26	29-Oct-26	08-Feb-27	10-Feb-27	0.00	0.00	101,343.52	-89
WALKING/BIKE PATHS		16	75.51%	70%	29-Sep-26	17-Oct-26	01-Jun-26 A	13-Oct-26	277,594.01	257,343.73	367,633.90	4
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	70%	29-Sep-26	07-Oct-26	01-Jun-26 A	13-Oct-26	187,554.12	131,287.88	187,554.12	-4
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	50%	70%	08-Oct-26	17-Oct-26	10-Jun-26 A	13-Oct-26	90,039.89	126,055.85	180,079.78	4
GENERAL/FURNITURE		127	0%	6.69%	15-Oct-26	24-Dec-26	01-Oct-26 A	14-Mar-27	0.00	26,410.86	394,811.80	-64
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	0%	0%	18-Oct-26	07-Nov-26	13-Oct-26	02-Nov-26	0.00	0.00	93,594.00	4
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	06-Mar-27	08-Mar-27	0.00	0.00	9,749.30	-64
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	0%	0%	15-Oct-26	16-Nov-26	13-Oct-26	14-Nov-26	0.00	0.00	17,274.79	2
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	15-Nov-26	30-Nov-26	0.00	0.00	40,307.84	2
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	15-Feb-27	03-Mar-27	0.00	0.00	32,757.76	-63
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	15-Feb-27	03-Mar-27	0.00	0.00	12,869.04	-63
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	09-Mar-27	14-Mar-27	0.00	0.00	12,186.67	-64
MLTX-02-005-CN-1	Installing of Site Light Poles	22	0%	15%	08-Nov-26	02-Dec-26	01-Oct-26 A	14-Feb-27	0.00	26,410.86	176,072.40	-63
TOILET/SERVICE BUILDING		197	11.96%	13.31%	30-Jul-26	23-Dec-26	20-Sep-26 A	22-Mar-27	50,105.74	55,765.62	418,996.57	-72
THERMAL & MOISTER PROTECTION		18	100%	80%	30-Jul-26	19-Aug-26	20-Sep-26 A	02-Nov-26	16,607.28	13,285.82	16,607.28	-63
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	80%	30-Jul-26	19-Aug-26	20-Sep-26 A	02-Nov-26	16,607.28	13,285.82	16,607.28	-63
MECHANICAL WORK		21	0%	0%	28-Nov-26	21-Dec-26	09-Feb-27	06-Mar-27	0.00	0.00	1,949.87	-63
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	09-Feb-27	06-Mar-27	0.00	0.00	1,949.87	-63
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	09-Feb-27	06-Mar-27	0.00	0.00	1,949.87	-63
ELECTRICAL WORKS		55	0%	0%	04-Nov-26	21-Dec-26	03-Jan-27	08-Mar-27	0.00	0.00	180,781.27	-65
FIXTURE WORKS		55	0%	0%	04-Nov-26	21-Dec-26	03-Jan-27	08-Mar-27	0.00	0.00	180,781.27	-65
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	26-Jan-27	15-Feb-27	0.00	0.00	34,317.53	-51
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	0%	0%	04-Nov-26	26-Nov-26	03-Jan-27	25-Jan-27	0.00	0.00	102,367.69	-51
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	0%	0%	28-Nov-26	20-Dec-26	26-Jan-27	17-Feb-27	0.00	0.00	7,085.10	-51
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	0%	0%	28-Nov-26	21-Dec-26	26-Jan-27	18-Feb-27	0.00	0.00	14,259.43	-51
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	26-Jan-27	17-Feb-27	0.00	0.00	6,239.59	-51
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	13-Feb-27	08-Mar-27	0.00	0.00	7,250.09	-72
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	0%	0%	28-Nov-26	20-Dec-26	26-Jan-27	17-Feb-27	0.00	0.00	6,824.51	-51
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	0%	0%	21-Nov-26	13-Dec-26	13-Feb-27	08-Mar-27	0.00	0.00	2,437.33	-72
DOORS/WINDOWS		23	0%	0%	21-Nov-26	16-Dec-26	13-Feb-27	15-Mar-27	0.00	0.00	58,495.82	-72
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	11	0%	0%	05-Dec-26	16-Dec-26	28-Feb-27	15-Mar-27	0.00	0.00	5,849.58	-72
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	12	0%	0%	21-Nov-26	03-Dec-26	13-Feb-27	27-Feb-27	0.00	0.00	52,646.24	-72
METAL WORKS		28	80%	0%	03-Sep-26	20-Oct-26	17-Nov-26	19-Dec-26	7,799.44	0.00	9,749.30	-51
MLTX-02-005-CN-126	Installation of Galvanized Steel Ladder	14	100%	0%	03-Sep-26	19-Sep-26	17-Nov-26	02-Dec-26	5,849.58	0.00	5,849.58	-63
MLTX-02-005-CN-129	Installation of DI Cover for Tank	14	50%	0%	05-Oct-26	20-Oct-26	03-Dec-26	19-Dec-26	1,949.86	0.00	3,899.72	-51
FINISHING WORKS		128	11.92%	34.7%	20-Aug-26	16-Dec-26	27-Sep-26 A	15-Mar-27	11,075.06	32,243.02	92,917.20	-72
FLOOR FINISHES		128	71.43%	0%	27-Sep-26	16-Dec-26	13-Oct-26	15-Mar-27	2,924.82	0.00	4,094.76	-72

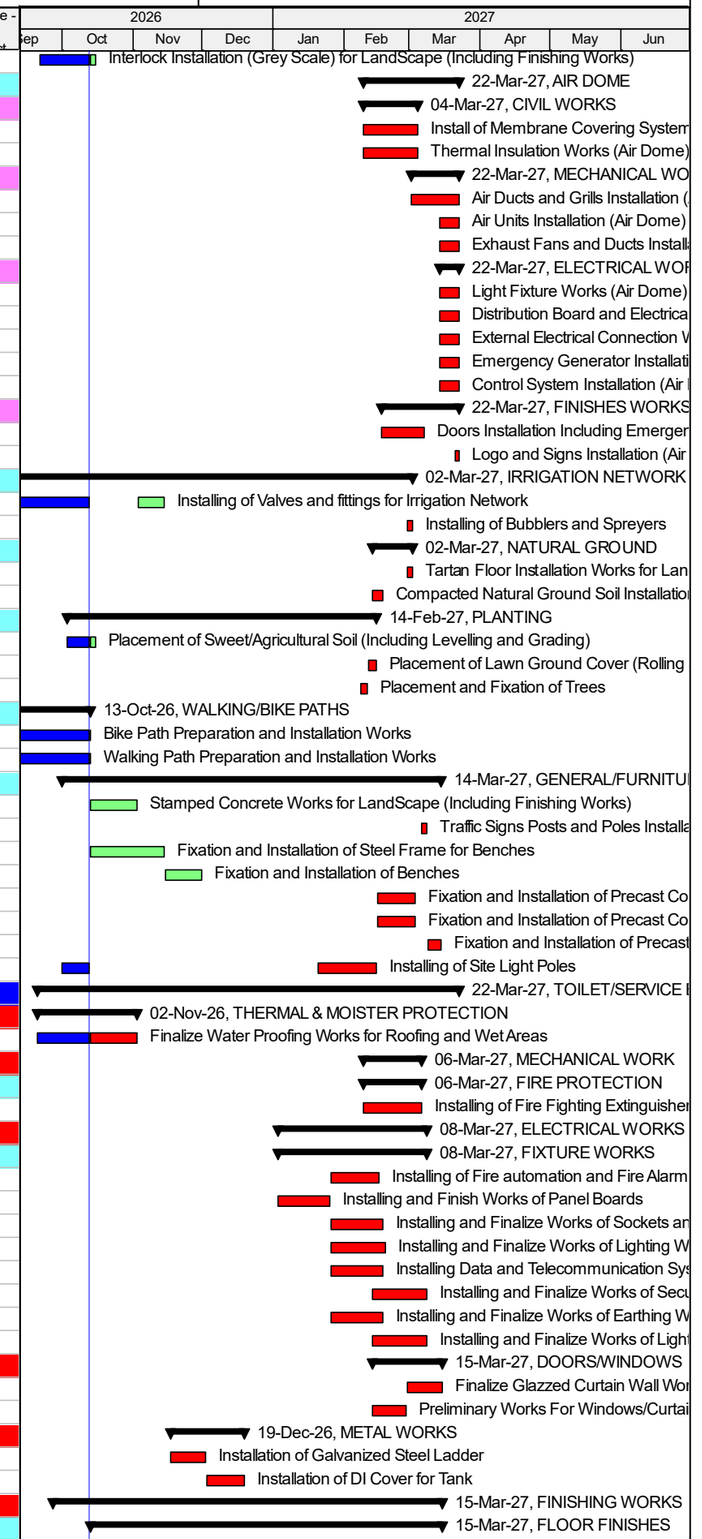

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 12-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	27-Sep-26	03-Oct-26	13-Oct-26	19-Oct-26	2,924.82	0.00	2,924.82	-14
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	13-Feb-27	15-Mar-27	0.00	0.00	1,169.94	-72
WALL FINISHES		66	9.18%	36.3%	20-Aug-26	03-Nov-26	27-Sep-26 A	02-Jan-27	8,150.24	32,243.02	88,822.44	-51
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	0%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	15-Oct-26	0.00	32,243.02	35,825.58	4
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	0%	0%	21-Oct-26	28-Oct-26	20-Dec-26	27-Dec-26	0.00	0.00	31,197.60	-51
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	0%	0%	29-Oct-26	03-Nov-26	28-Dec-26	02-Jan-27	0.00	0.00	13,649.02	-51
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	0%	20-Aug-26	02-Sep-26	03-Nov-26	16-Nov-26	8,150.24	0.00	8,150.24	-63
SPECIALTIES WORK		148	25%	17.5%	27-Sep-26	23-Dec-26	04-Oct-26 A	22-Mar-27	14,623.96	10,236.77	58,495.83	-72
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	70%	27-Sep-26	29-Sep-26	04-Oct-26 A	15-Oct-26	14,623.96	10,236.77	14,623.96	-14
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	28-Feb-27	22-Mar-27	0.00	0.00	19,498.61	-72
MLTX-02-005-CN-131	Installation of Phenolic Locker	12	0%	0%	28-Nov-26	10-Dec-26	26-Jan-27	08-Feb-27	0.00	0.00	24,373.26	-51
TESTING & COMMISSIONING		23	0%	0%	08-Dec-26	02-Jan-27	17-Mar-27	12-Apr-27	0.00	0.00	0.00	-82
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	23-Mar-27	12-Apr-27	0.00	0.00	0.00	-83
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	03-Apr-27	10-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	17-Mar-27	10-Apr-27	0.00	0.00	0.00	-81
DAMMAM		169	7.46%	0.78%	16-Apr-26	02-Jan-27	06-Sep-26 A	04-Mar-27	469,005.37	49,211.34	6,289,677.12	-52
ENGINEERING		70	0%	0%	16-Apr-26	02-Aug-26	13-Oct-26	02-Jan-27	0.00	0.00	0.00	-130
SHOP DRAWINGS		70	0%	0%	16-Apr-26	02-Aug-26	13-Oct-26	02-Jan-27	0.00	0.00	0.00	-130
SHOP DRAWINGS SUBMISSION		30	0%	0%	16-Apr-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	16-Apr-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
AIR DOME SYSTEM		30	0%	0%	16-Apr-26	07-Jun-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Submittal for Cable Tension Layout	15	100%	0%	16-Apr-26	03-May-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-150
MLTX-02-005-EN	Shop DWG Submittal for Airlock Door Details	25	100%	0%	30-Apr-26	01-Jun-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Submittal for Emergency Exit Details	30	100%	0%	30-Apr-26	07-Jun-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-138
MECHANCAL WORKS		15	0%	0%	30-Apr-26	14-Jun-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	15	100%	0%	30-Apr-26	17-May-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	15	100%	0%	25-May-26	14-Jun-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-117
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	25	100%	0%	25-May-26	25-Jun-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	25	100%	0%	25-May-26	25-Jun-26	13-Oct-26	10-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
SHOP DRAWINGS APPROVALS		70	0%	0%	30-Apr-26	02-Aug-26	13-Oct-26	02-Jan-27	0.00	0.00	0.00	-130
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		70	0%	0%	30-Apr-26	02-Aug-26	13-Oct-26	02-Jan-27	0.00	0.00	0.00	-130
AIR DOME SYSTEM		60	0%	0%	30-Apr-26	12-Jul-26	13-Oct-26	21-Dec-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Air Dome Structural Layout	15	100%	0%	30-Apr-26	17-May-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Membrane Panel Layout	15	100%	0%	18-May-26	07-Jun-26	31-Oct-26	16-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Cable Tension Layout	15	100%	0%	18-May-26	07-Jun-26	31-Oct-26	16-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Airlock Door Details	15	100%	0%	08-Jun-26	24-Jun-26	17-Nov-26	03-Dec-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Emergency Exit Details	15	100%	0%	25-Jun-26	12-Jul-26	05-Dec-26	21-Dec-26	0.00	0.00	0.00	-138
SPORTS EQUIPMENT		30	0%	0%	25-May-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Approval for Football Turf Installation	30	100%	0%	25-May-26	01-Jul-26	13-Oct-26	16-Nov-26	0.00	0.00	0.00	-117
MECHANCAL WORKS		40	0%	0%	18-May-26	06-Jul-26	31-Oct-26	15-Dec-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	25	100%	0%	18-May-26	18-Jun-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	-138
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	15	100%	0%	20-Jun-26	06-Jul-26	29-Nov-26	15-Dec-26	0.00	0.00	0.00	-138
ELECTRICAL WORKS		45	0%	0%	27-Jun-26	02-Aug-26	11-Nov-26	02-Jan-27	0.00	0.00	0.00	-130
MLTX-02-005-EN	Shop DWG Approval for Power Layout	25	100%	0%	02-Jul-26	30-Jul-26	17-Nov-26	15-Dec-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	25	100%	0%	27-Jun-26	25-Jul-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	25	100%	0%	27-Jun-26	25-Jul-26	11-Nov-26	09-Dec-26	0.00	0.00	0.00	-117
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	15	100%	0%	16-Jul-26	02-Aug-26	16-Dec-26	02-Jan-27	0.00	0.00	0.00	-130
PROCUREMENT		97	0%	0%	21-May-26	21-Dec-26	13-Oct-26	02-Feb-27	0.00	0.00	0.00	-37
SHORT LEAD ITEM		97	0%	0%	21-May-26	21-Dec-26	13-Oct-26	02-Feb-27	0.00	0.00	0.00	-37
TOILET/SERVICE WORKS		41	0%	0%	17-Jun-26	28-Nov-26	13-Oct-26	29-Nov-26	0.00	0.00	0.00	-1
LIGHTING FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	16-Nov-26	26-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	16-Nov-26	26-Nov-26	0.00	0.00	0.00	-99
SWITCHES/SOCKETS		12	0%	0%	22-Jul-26	04-Aug-26	16-Nov-26	29-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	22-Jul-26	27-Jul-26	16-Nov-26	21-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	28-Jul-26	04-Aug-26	22-Nov-26	29-Nov-26	0.00	0.00	0.00	-99
DISTRIBUTION PANNELS		40	0%	0%	13-Oct-26	28-Nov-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	0
MLTX-02-005-PR-1	PO for Distribution Panels	15	0%	0%	13-Oct-26	29-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	0
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	25	0%	0%	31-Oct-26	28-Nov-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	0
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	13-Oct-26	15-Nov-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	13-Oct-26	22-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-100

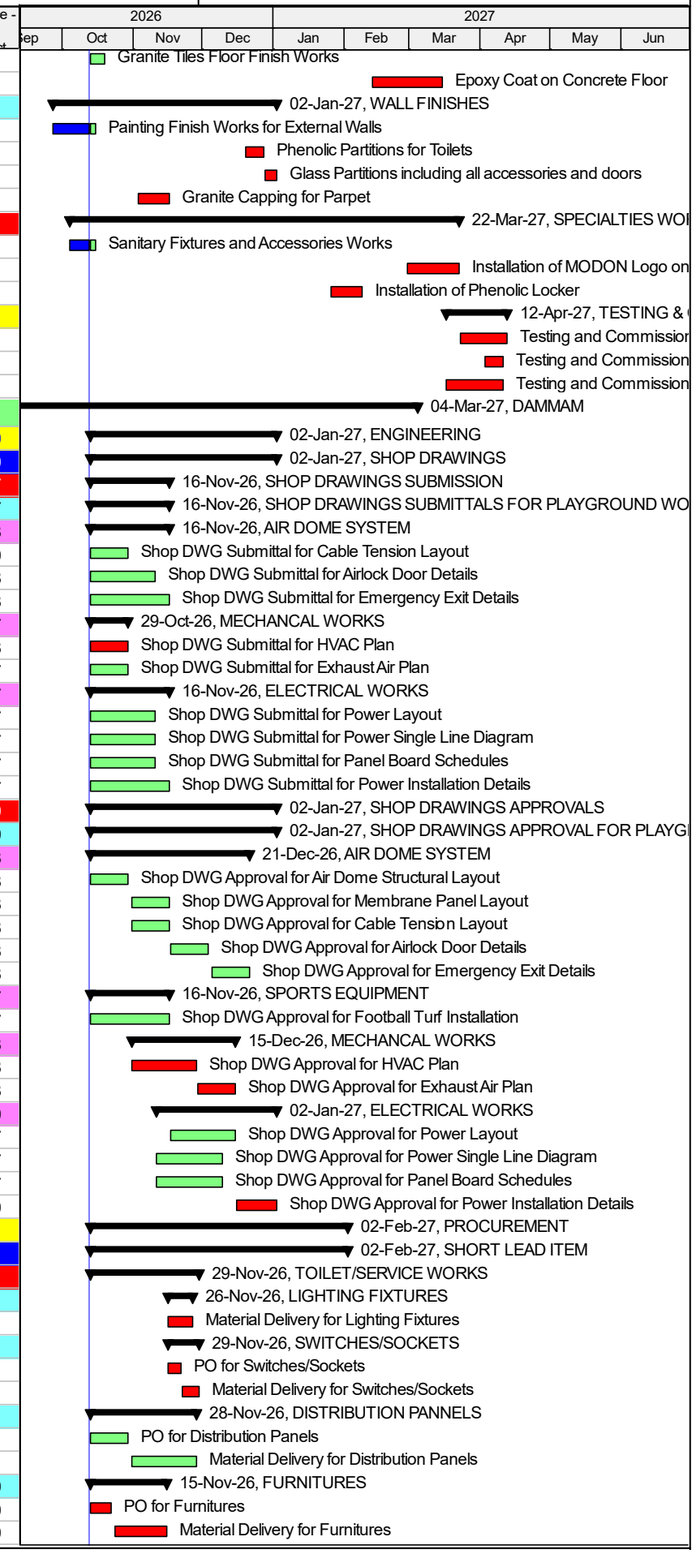

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PLAYGROUND WORKS		97	0%	0%	21-May-26	21-Dec-26	13-Oct-26	02-Feb-27	0.00	0.00	0.00	-37
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-120
ARTIFICIAL TURF		12	0%	0%	18-Jun-26	01-Jul-26	07-Nov-26	19-Nov-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	07-Nov-26	19-Nov-26	0.00	0.00	0.00	-120
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	13-Oct-26	26-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	13-Oct-26	26-Oct-26	0.00	0.00	0.00	-115
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	31-Oct-26	01-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	0%	0%	19-Oct-26	19-Nov-26	31-Oct-26	01-Dec-26	0.00	0.00	0.00	-10
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-110
BITUMINOUS BASE & WEARING COURSE		32	0%	0%	15-Jun-26	21-Jul-26	03-Nov-26	09-Dec-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	03-Nov-26	19-Nov-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for the Site	17	100%	0%	02-Jul-26	21-Jul-26	21-Nov-26	09-Dec-26	0.00	0.00	0.00	-120
INTERLOCKING PAVING		32	0%	0%	09-Aug-26	14-Sep-26	28-Dec-26	02-Feb-27	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	15	100%	0%	09-Aug-26	25-Aug-26	28-Dec-26	13-Jan-27	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	17	100%	0%	26-Aug-26	14-Sep-26	14-Jan-27	02-Feb-27	0.00	0.00	0.00	-120
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	21-Nov-26	27-Dec-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	21-Nov-26	07-Dec-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	08-Dec-26	27-Dec-26	0.00	0.00	0.00	-120
AIR DIFUSSERS/GRILLS		40	0%	0%	01-Oct-26	02-Dec-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	4
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	66.67%	0%	01-Oct-26	18-Oct-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	0%	0%	04-Nov-26	02-Dec-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	4
GALVANIZED DUCTS		40	0%	0%	19-Oct-26	03-Dec-26	31-Oct-26	15-Dec-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	PO for Galvanized Duct	15	0%	0%	19-Oct-26	04-Nov-26	31-Oct-26	16-Nov-26	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	0%	0%	05-Nov-26	03-Dec-26	17-Nov-26	15-Dec-26	0.00	0.00	0.00	-10
EXHAUST FANS		40	0%	0%	17-Jun-26	02-Dec-26	13-Oct-26	28-Nov-26	0.00	0.00	0.00	4
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	17-Jun-26	04-Jul-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	0%	0%	04-Nov-26	02-Dec-26	31-Oct-26	28-Nov-26	0.00	0.00	0.00	4
DISTRIBUTION BOARDS		20	0%	0%	23-Jun-26	26-Nov-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	4
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	23-Jun-26	28-Jun-26	31-Oct-26	04-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	0%	0%	10-Nov-26	26-Nov-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	4
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	05-Nov-26	22-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	05-Nov-26	10-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	11-Nov-26	22-Nov-26	0.00	0.00	0.00	-110
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	11-Nov-26	03-Dec-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	11-Nov-26	03-Dec-26	0.00	0.00	0.00	-1
CCTV MATERIALS		80	0%	0%	30-Jul-26	21-Dec-26	13-Oct-26	13-Jan-27	0.00	0.00	0.00	-20
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	13-Oct-26	18-Oct-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	28-Dec-26	13-Jan-27	0.00	0.00	0.00	-20
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	30-Nov-26	04-Jan-27	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	30-Nov-26	06-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	07-Dec-26	04-Jan-27	0.00	0.00	0.00	-23
LANDSCAPE WORKS		91	0%	0%	05-Aug-26	13-Dec-26	13-Oct-26	26-Jan-27	0.00	0.00	0.00	-38
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	07-Dec-26	23-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	07-Dec-26	12-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	13-Dec-26	23-Dec-26	0.00	0.00	0.00	-97
TRAFFIC SIGNS		39	0%	0%	04-Nov-26	13-Dec-26	13-Dec-26	26-Jan-27	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	PO for Traffic Signs	15	0%	0%	04-Nov-26	21-Nov-26	13-Dec-26	29-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	19	0%	0%	22-Nov-26	13-Dec-26	05-Jan-27	26-Jan-27	0.00	0.00	0.00	-38
IRRIGATION PIPES/SPRINKLERS		23	0%	0%	10-Nov-26	30-Nov-26	13-Dec-26	07-Jan-27	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	0%	0%	10-Nov-26	15-Nov-26	13-Dec-26	17-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	0%	0%	22-Nov-26	30-Nov-26	30-Dec-26	07-Jan-27	0.00	0.00	0.00	-33
AGRICULTURE SOIL		37	0%	0%	05-Aug-26	05-Dec-26	13-Oct-26	24-Nov-26	0.00	0.00	0.00	9
MLTX-02-005-PR-1	PO for Agriculture Soil	15	100%	0%	05-Aug-26	22-Aug-26	13-Oct-26	29-Oct-26	0.00	0.00	0.00	-58
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	22	0%	0%	10-Nov-26	05-Dec-26	31-Oct-26	24-Nov-26	0.00	0.00	0.00	9
TRACK SURFACE		10	0%	0%	10-Nov-26	21-Nov-26	24-Dec-26	04-Jan-27	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	24-Dec-26	04-Jan-27	0.00	0.00	0.00	-38
GRASS/TREES		15	0%	0%	22-Nov-26	08-Dec-26	05-Jan-27	21-Jan-27	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	0%	22-Nov-26	08-Dec-26	05-Jan-27	21-Jan-27	0.00	0.00	0.00	-38
LONG LEAD ITEM		83	0%	0%	21-May-26	30-Nov-26	13-Oct-26	17-Jan-27	0.00	0.00	0.00	-41
PLAYGROUND WORKS		83	0%	0%	21-May-26	30-Nov-26	13-Oct-26	17-Jan-27	0.00	0.00	0.00	-41
STEEL TENSION CABLES		50	0%	0%	21-May-26	19-Oct-26	13-Oct-26	09-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	13-Oct-26	21-Oct-26	0.00	0.00	0.00	-120

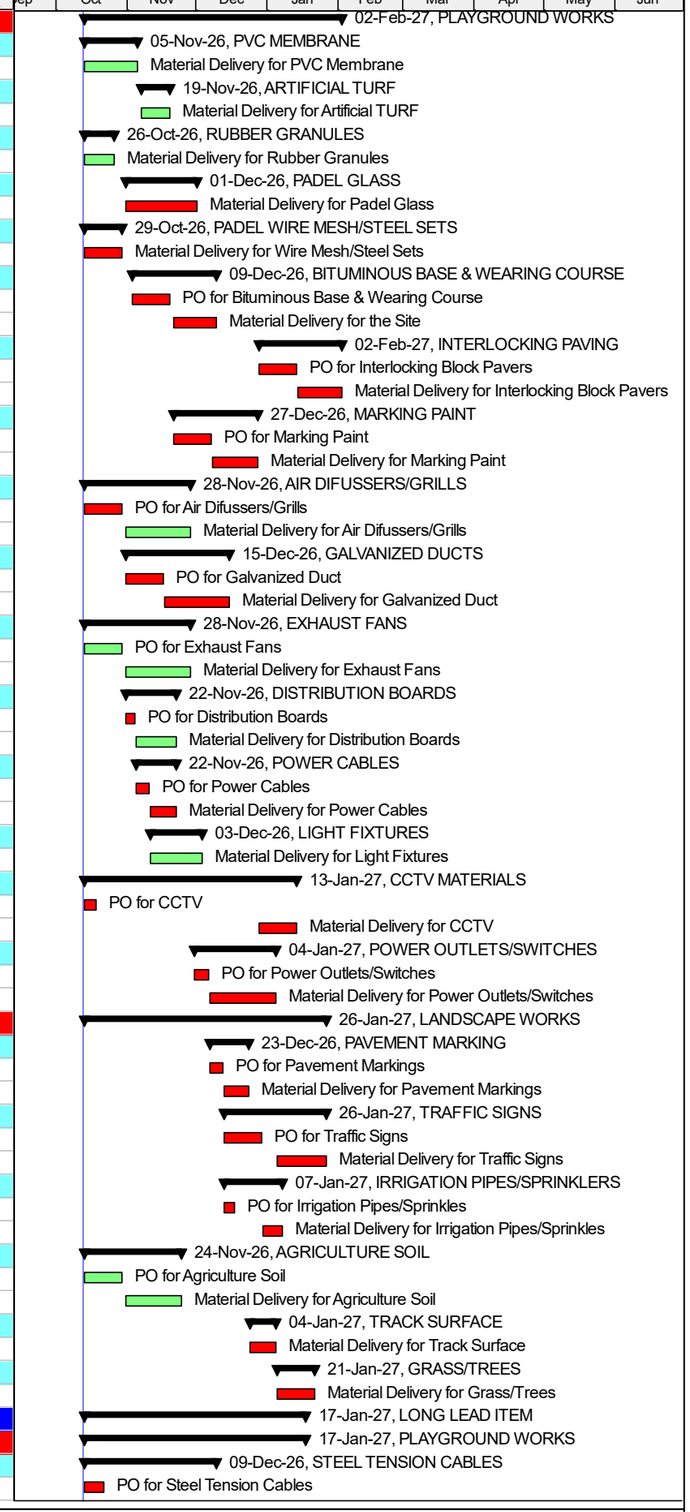

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	03-Nov-26	19-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	03-Jun-26	14-Jun-26	22-Oct-26	02-Nov-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Staging time	7	14.29%	0%	12-Oct-26	19-Oct-26	02-Dec-26	09-Dec-26	0.00	0.00	0.00	-44
EMERGENCY DOORS		48	0%	0%	15-Jun-26	24-Nov-26	03-Nov-26	28-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	15-Jun-26	25-Jun-26	03-Nov-26	14-Nov-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	08-Dec-26	24-Dec-26	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	27-Jun-26	19-Jul-26	15-Nov-26	07-Dec-26	0.00	0.00	0.00	-120
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	26-Dec-26	28-Dec-26	0.00	0.00	0.00	-29
PRESSURE UNITS		40	0%	0%	12-Oct-26	30-Nov-26	02-Dec-26	17-Jan-27	0.00	0.00	0.00	-41
MLTX-02-005-PR-1	PO for Pressure Units	10	10%	0%	12-Oct-26	22-Oct-26	02-Dec-26	13-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	26-Dec-26	05-Jan-27	0.00	0.00	0.00	-43
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	10	0%	0%	24-Oct-26	03-Nov-26	14-Dec-26	24-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	06-Jan-27	17-Jan-27	0.00	0.00	0.00	-41
AIR LOCK DOORS		42	0%	0%	30-Sep-26	26-Nov-26	21-Nov-26	07-Jan-27	0.00	0.00	0.00	-36
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	30-Sep-26	11-Oct-26	21-Nov-26	01-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	20-Dec-26	02-Jan-27	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	15	0%	0%	19-Oct-26	04-Nov-26	02-Dec-26	19-Dec-26	0.00	0.00	0.00	-38
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	03-Jan-27	07-Jan-27	0.00	0.00	0.00	-36
CONSTRUCTION PHASE		169	7.46%	0.78%	02-Jul-26	31-Dec-26	06-Sep-26 A	04-Mar-27	469,005.37	49,211.34	6,289,677.12	-53
SITE WORKS		127	6.4%	0.32%	02-Jul-26	31-Dec-26	19-Sep-26 A	13-Feb-27	377,425.92	18,848.67	5,896,147.45	-37
LANDSCAPE WORKS		127	6.4%	0.32%	02-Jul-26	31-Dec-26	19-Sep-26 A	13-Feb-27	377,425.92	18,848.67	5,896,147.45	-37
PLAYGROUND AREA		70	55.81%	0%	02-Jul-26	31-Dec-26	21-Nov-26	09-Feb-27	338,945.66	0.00	607,310.05	-34
FOOTBALL PLAYGROUND		44	76.92%	0%	02-Jul-26	15-Dec-26	21-Nov-26	10-Jan-27	158,424.99	0.00	205,952.49	-22
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	02-Jul-26	25-Jul-26	21-Nov-26	13-Dec-26	158,424.99	0.00	158,424.99	-120
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	05-Jan-27	10-Jan-27	0.00	0.00	31,685.00	-22
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	03-Jan-27	04-Jan-27	0.00	0.00	15,842.50	-22
PADEL PLAYGROUND		5	0%	0%	20-Dec-26	24-Dec-26	30-Jan-27	03-Feb-27	0.00	0.00	70,195.20	-35
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	30-Jan-27	03-Feb-27	0.00	0.00	58,496.00	-35
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	30-Jan-27	03-Feb-27	0.00	0.00	11,699.20	-35
BASKETBALL PLAYGROUND		2	0%	0%	30-Dec-26	31-Dec-26	04-Feb-27	06-Feb-27	0.00	0.00	96,956.10	-31
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	04-Feb-27	06-Feb-27	0.00	0.00	80,796.75	-31
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	04-Feb-27	06-Feb-27	0.00	0.00	16,159.35	-31
PADEL FENCE		34	0%	0%	26-Nov-26	24-Dec-26	02-Dec-26	10-Jan-27	0.00	0.00	53,685.59	-14
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	2	0%	0%	20-Dec-26	21-Dec-26	05-Jan-27	06-Jan-27	0.00	0.00	3,834.68	-14
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	02-Dec-26	30-Dec-26	0.00	0.00	30,677.48	-5
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	02-Dec-26	30-Dec-26	0.00	0.00	15,338.75	-5
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	05-Jan-27	10-Jan-27	0.00	0.00	3,834.68	-14
CURBSTOEN/INTERLOCK		6	100%	0%	15-Sep-26	21-Sep-26	03-Feb-27	09-Feb-27	180,520.67	0.00	180,520.67	-120
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	0%	15-Sep-26	21-Sep-26	03-Feb-27	09-Feb-27	180,520.67	0.00	180,520.67	-120
AIR DOME		43	0%	0%	15-Nov-26	24-Dec-26	10-Dec-26	28-Jan-27	0.00	0.00	4,306,367.09	-30
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	10-Dec-26	02-Jan-27	0.00	0.00	1,391,301.90	-22
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	10-Dec-26	02-Jan-27	0.00	0.00	942,830.33	-22
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	10-Dec-26	02-Jan-27	0.00	0.00	448,471.57	-22
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	1,233,296.81	-35
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	18-Jan-27	21-Jan-27	0.00	0.00	728,766.30	-35
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	336,353.67	-35
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	168,176.84	-35
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	18-Jan-27	28-Jan-27	0.00	0.00	1,513,591.54	-30
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	18-Jan-27	28-Jan-27	0.00	0.00	224,235.78	-35
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	21-Jan-27	28-Jan-27	0.00	0.00	168,176.84	-35
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	23-Jan-27	28-Jan-27	0.00	0.00	168,176.84	-35
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	25-Jan-27	28-Jan-27	0.00	0.00	504,530.51	-35
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	26-Jan-27	28-Jan-27	0.00	0.00	448,471.57	-30
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	21-Jan-27	25-Jan-27	0.00	0.00	168,176.84	-35
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	21-Jan-27	23-Jan-27	0.00	0.00	112,117.89	-35
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	24-Jan-27	25-Jan-27	0.00	0.00	56,058.95	-35
IRRIGATION NETWORK		98	48.41%	38.73%	17-Sep-26	02-Dec-26	19-Sep-26 A	10-Jan-27	23,560.84	18,848.67	48,667.04	-33
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	3	100%	80%	17-Sep-26	20-Sep-26	19-Sep-26 A	15-Oct-26	23,560.84	18,848.67	23,560.84	-21
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	09-Jan-27	10-Jan-27	0.00	0.00	25,106.20	-33
NATURAL GROUND		30	6.78%	0%	10-Oct-26	12-Nov-26	13-Oct-26	16-Nov-26	13,000.00	0.00	191,740.00	-3
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	27-Oct-26	12-Nov-26	31-Oct-26	16-Nov-26	0.00	0.00	126,740.00	-3
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	20%	0%	10-Oct-26	26-Oct-26	13-Oct-26	29-Oct-26	13,000.00	0.00	65,000.00	-3
PLANTING		27	0%	0%	06-Dec-26	31-Dec-26	11-Jan-27	10-Feb-27	0.00	0.00	347,251.46	-35
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	0%	06-Dec-26	12-Dec-26	11-Jan-27	17-Jan-27	0.00	0.00	104,175.44	-31

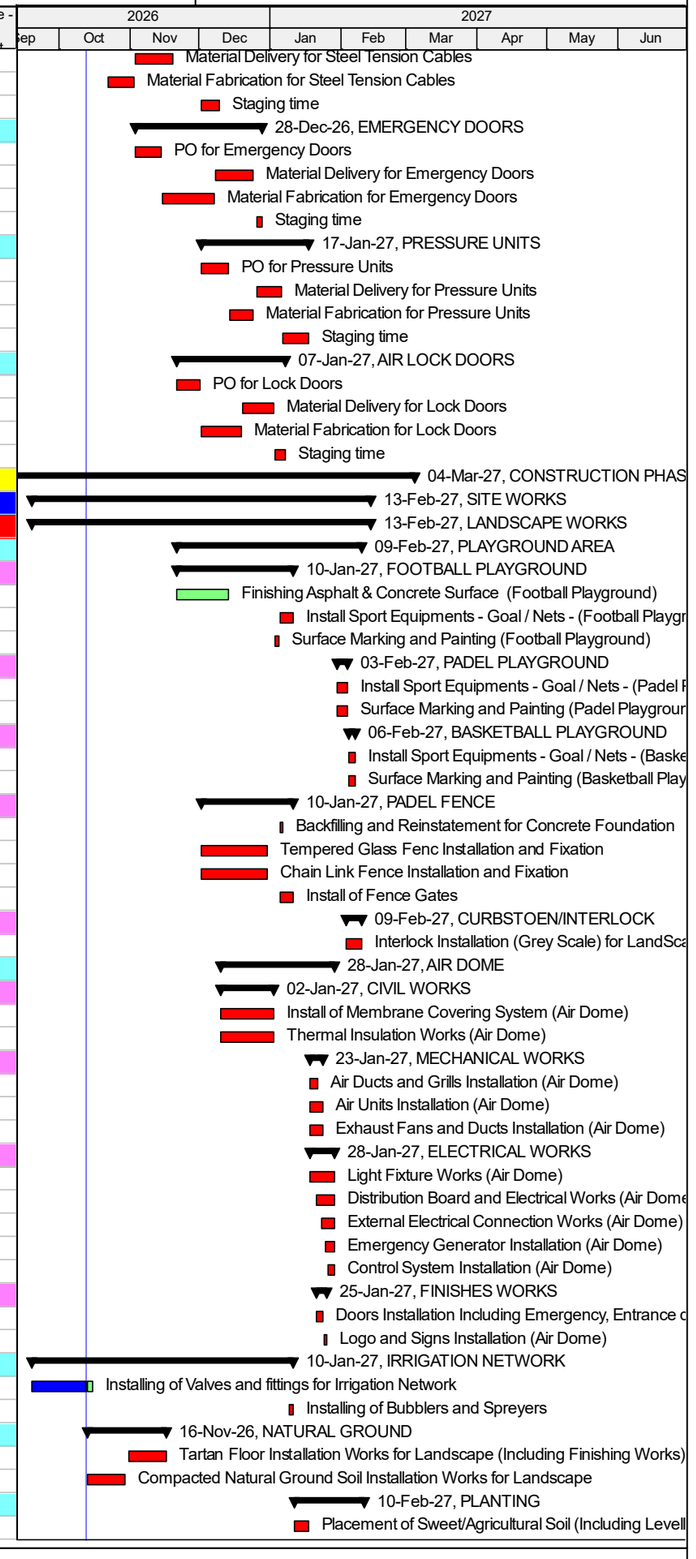

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 12-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	24-Dec-26	31-Dec-26	03-Feb-27	10-Feb-27	0.00	0.00	141,732.50	-35
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	13-Dec-26	23-Dec-26	23-Jan-27	02-Feb-27	0.00	0.00	101,343.52	-35
GENERAL/FURNITURE		81	0.49%	0%	11-Oct-26	31-Dec-26	11-Nov-26	13-Feb-27	1,919.42	0.00	394,811.80	-37
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	0%	0%	01-Nov-26	21-Nov-26	02-Dec-26	22-Dec-26	0.00	0.00	93,594.00	-27
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	27-Jan-27	13-Feb-27	0.00	0.00	9,749.30	-37
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	11.11%	0%	11-Oct-26	31-Oct-26	11-Nov-26	01-Dec-26	1,919.42	0.00	17,274.79	-27
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	0%	0%	01-Nov-26	23-Nov-26	02-Dec-26	24-Dec-26	0.00	0.00	40,307.84	-27
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	0%	0%	01-Nov-26	23-Nov-26	02-Dec-26	24-Dec-26	0.00	0.00	32,757.76	-27
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	0%	0%	01-Nov-26	23-Nov-26	02-Dec-26	24-Dec-26	0.00	0.00	12,869.04	-27
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	26-Dec-26	14-Jan-27	0.00	0.00	12,186.67	-27
MLTX-02-005-CN-1	Installing of Site Light Poles	20	0%	0%	22-Nov-26	14-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	176,072.40	-27
TOILET/SERVICE BUILDING		169	23.27%	7.72%	18-Aug-26	29-Dec-26	06-Sep-26 A	04-Mar-27	91,579.45	30,362.66	393,529.67	-55
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	21-Oct-26	16,607.28	14,946.55	16,607.28	-47
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	21-Oct-26	16,607.28	14,946.55	16,607.28	-47
MECHANICAL WORK		82	63.12%	42.08%	10-Oct-26	26-Dec-26	04-Oct-26 A	12-Jan-27	7,769.01	5,179.34	12,308.55	-15
SEWER/DRAINAGE SYSTEM		4	75%	50%	10-Oct-26	13-Oct-26	04-Oct-26 A	26-Oct-26	7,769.01	5,179.34	10,358.68	-11
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	4	75%	50%	10-Oct-26	13-Oct-26	04-Oct-26 A	26-Oct-26	7,769.01	5,179.34	10,358.68	-11
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	30-Dec-26	12-Jan-27	0.00	0.00	1,949.87	-15
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	30-Dec-26	12-Jan-27	0.00	0.00	1,949.87	-15
ELECTRICAL WORKS		31	0%	0%	23-Nov-26	29-Dec-26	30-Dec-26	03-Feb-27	0.00	0.00	180,781.27	-31
FIXTURE WORKS		31	0%	0%	23-Nov-26	29-Dec-26	30-Dec-26	03-Feb-27	0.00	0.00	180,781.27	-31
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	16-Jan-27	01-Feb-27	0.00	0.00	34,317.53	-30
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	0%	06-Dec-26	29-Dec-26	30-Dec-26	23-Jan-27	0.00	0.00	102,367.69	-21
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	13	0%	0%	12-Dec-26	26-Dec-26	16-Jan-27	30-Jan-27	0.00	0.00	7,085.10	-30
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	14	0%	0%	12-Dec-26	27-Dec-26	16-Jan-27	31-Jan-27	0.00	0.00	14,259.43	-30
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	16-Jan-27	31-Jan-27	0.00	0.00	6,239.59	-30
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	30-Dec-26	14-Jan-27	0.00	0.00	7,250.09	-30
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	30-Dec-26	25-Jan-27	0.00	0.00	6,824.51	-32
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	15	0%	0%	13-Dec-26	29-Dec-26	18-Jan-27	03-Feb-27	0.00	0.00	2,437.33	-31
DOORS/WINDOWS		95	90%	0%	19-Sep-26	27-Dec-26	13-Oct-26	31-Jan-27	52,646.24	0.00	58,495.82	-30
MLTX-02-005-CN-144	Finalize Glazzed Curtain Wall Works	14	0%	0%	12-Dec-26	27-Dec-26	16-Jan-27	31-Jan-27	0.00	0.00	5,849.58	-30
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	12	100%	0%	19-Sep-26	03-Oct-26	13-Oct-26	26-Oct-26	52,646.24	0.00	52,646.24	-20
METAL WORKS		28	65.71%	0%	10-Sep-26	26-Oct-26	05-Nov-26	07-Dec-26	6,406.68	0.00	9,749.30	-36
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	14	100%	0%	10-Sep-26	27-Sep-26	05-Nov-26	21-Nov-26	5,849.58	0.00	5,849.58	-47
MLTX-02-005-CN-144	Installation of DI Cover for Tank	14	14.29%	0%	11-Oct-26	26-Oct-26	22-Nov-26	07-Dec-26	557.10	0.00	3,899.72	-36
FINISHING WORKS		73	14.28%	0%	27-Aug-26	21-Dec-26	22-Oct-26	14-Jan-27	8,150.24	0.00	57,091.62	-21
FLOOR FINISHES		69	0%	0%	17-Oct-26	21-Dec-26	27-Oct-26	14-Jan-27	0.00	0.00	4,094.76	-21
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	0%	0%	17-Oct-26	20-Oct-26	27-Oct-26	31-Oct-26	0.00	0.00	2,924.82	-9
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	14	0%	0%	06-Dec-26	21-Dec-26	30-Dec-26	14-Jan-27	0.00	0.00	1,169.94	-21
WALL FINISHES		59	15.38%	0%	27-Aug-26	22-Nov-26	22-Oct-26	29-Dec-26	8,150.24	0.00	52,996.86	-32
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	0%	0%	01-Nov-26	12-Nov-26	08-Dec-26	20-Dec-26	0.00	0.00	31,197.60	-32
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	0%	0%	16-Nov-26	22-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	13,649.02	-32
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	0%	27-Aug-26	09-Sep-26	22-Oct-26	04-Nov-26	8,150.24	0.00	8,150.24	-47
SPECIALTIES WORK		63	0%	17.5%	27-Oct-26	23-Dec-26	12-Oct-26 A	04-Mar-27	0.00	10,236.77	58,495.83	-60
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	0%	70%	27-Oct-26	31-Oct-26	12-Oct-26 A	07-Dec-26	0.00	10,236.77	14,623.96	-32
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	15-Feb-27	04-Mar-27	0.00	0.00	19,498.61	-60
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	0%	0%	14-Nov-26	15-Nov-26	21-Dec-26	22-Dec-26	0.00	0.00	24,373.26	-32
TESTING & COMMISSIONING		23	0%	0%	24-Dec-26	02-Jan-27	06-Feb-27	04-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	08-Feb-27	13-Feb-27	0.00	0.00	0.00	-37
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	02-Mar-27	04-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	06-Feb-27	13-Feb-27	0.00	0.00	0.00	-37
PROJECT CLOSEOUT & DEMOBILIZATION		24	0%	0%	08-Dec-26	02-Jan-27	17-Mar-27	13-Apr-27	0.00	0.00	0.00	-83
As-Built DWGs		20	0%	0%	08-Dec-26	31-Dec-26	17-Mar-27	08-Apr-27	0.00	0.00	0.00	-80
As-Built DWGs Submittals		16	0%	0%	08-Dec-26	27-Dec-26	17-Mar-27	04-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	23-Mar-27	24-Mar-27	0.00	0.00	0.00	-83
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	03-Apr-27	04-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	17-Mar-27	21-Mar-27	0.00	0.00	0.00	-81
As-Built DWGs Approvals		16	0%	0%	15-Dec-26	31-Dec-26	22-Mar-27	08-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	25-Mar-27	28-Mar-27	0.00	0.00	0.00	-79
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	06-Apr-27	08-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	22-Mar-27	24-Mar-27	0.00	0.00	0.00	-79
Demobilization		8	0%	0%	28-Dec-26	02-Jan-27	05-Apr-27	13-Apr-27	0.00	0.00	0.00	-83
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	05-Apr-27	05-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	05-Apr-27	05-Apr-27	0.00	0.00	0.00	-80

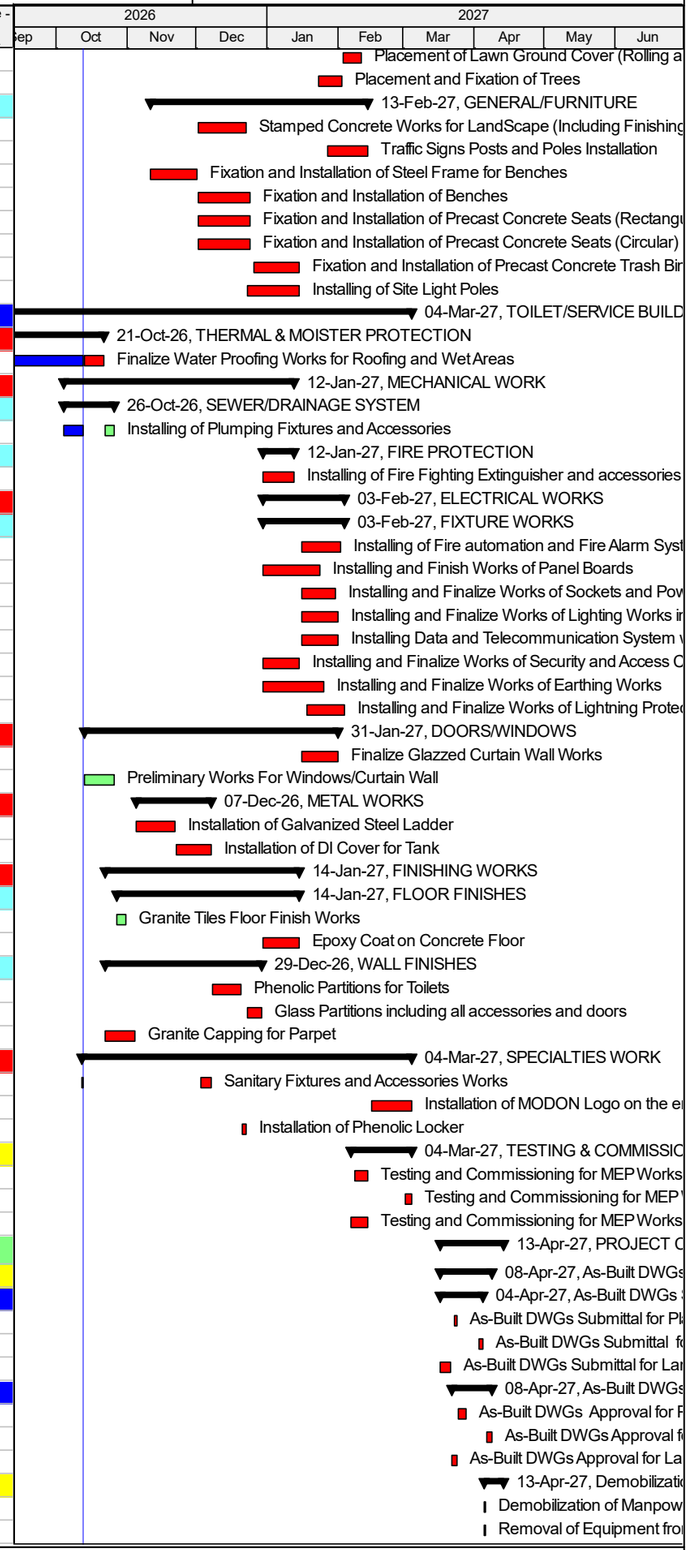

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	06-Apr-27	06-Apr-27	0.00	0.00	0.00	-78
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	13-Apr-27	13-Apr-27	0.00	0.00	0.00	-83



© Oracle Corporation
