Improvement of Waad Al Shamal Industrial City Fence & Gates

تسوير المنطقة المطورة بوعد الشمال

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Hamza Mohammad Alderi Construction Co.	Consolidated Consultants Group	Muhammed H. Al-Essa	06-May-2026	05-Oct-2026

Scope: 35,400 m of galvanised chain-link fence with gates and electric gate barriers, an intrusion detection system on fibre-optic cable, three guard houses and external works.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. All work was planned to finish by the contract completion date of 05-Oct-2026, so planned progress is 100%. The project is at 91.9%, behind by 8.1%, up 14.8% from the 26-Oct-2026 report.

PHYSICAL % COMPLETE
91.9% / 100% plan
▼ SPI 0.92 –8.1%

PROGRESS THIS WEEK
+14.8% / +0.0% plan
● The report itself states +2.0%

CONTRACT TIME ELAPSED
119.1% · day 181 of 152
▼ P6 finish 26-Nov-2026

INVOICED TO DATE (GROSS)
55.3% · 8.80M SAR
4 invoices, last period ends 05-Oct-2026

The contract completion date has passed with 8.1% of the work still to do.

The contract was due to finish on 05-Oct-2026, four weeks before this data date. The P6 update uploaded with this week's report (data date 02-Nov-2026) still schedules project finish on 26-Nov-2026, 52 days after the contract date, with –44.2 days of float. The weekly report still forecasts 05-Oct-2026 with no variance. Testing and commissioning, 4% of the man-hours, has not started.

Site photos this week

Four photos from the "Weekly Photos" sheet of the 03-Nov-2026 weekly report. The photos carry no date or GPS stamp. They show the external stair ladder, paving outside a guard house, the MEP final fix and furniture inside the rooms. Select a photo to view it larger, then use the arrows to move between photos.



External stair installation

Steel access ladder being fixed to a guard-house wall.



Landscape works

Interlock paving laid outside a guard house, next to the fence.



Rooms MEP final fix

Ceiling light panels installed in a guard-house room.




Furniture works

Desks and chairs delivered to a guard-house room.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

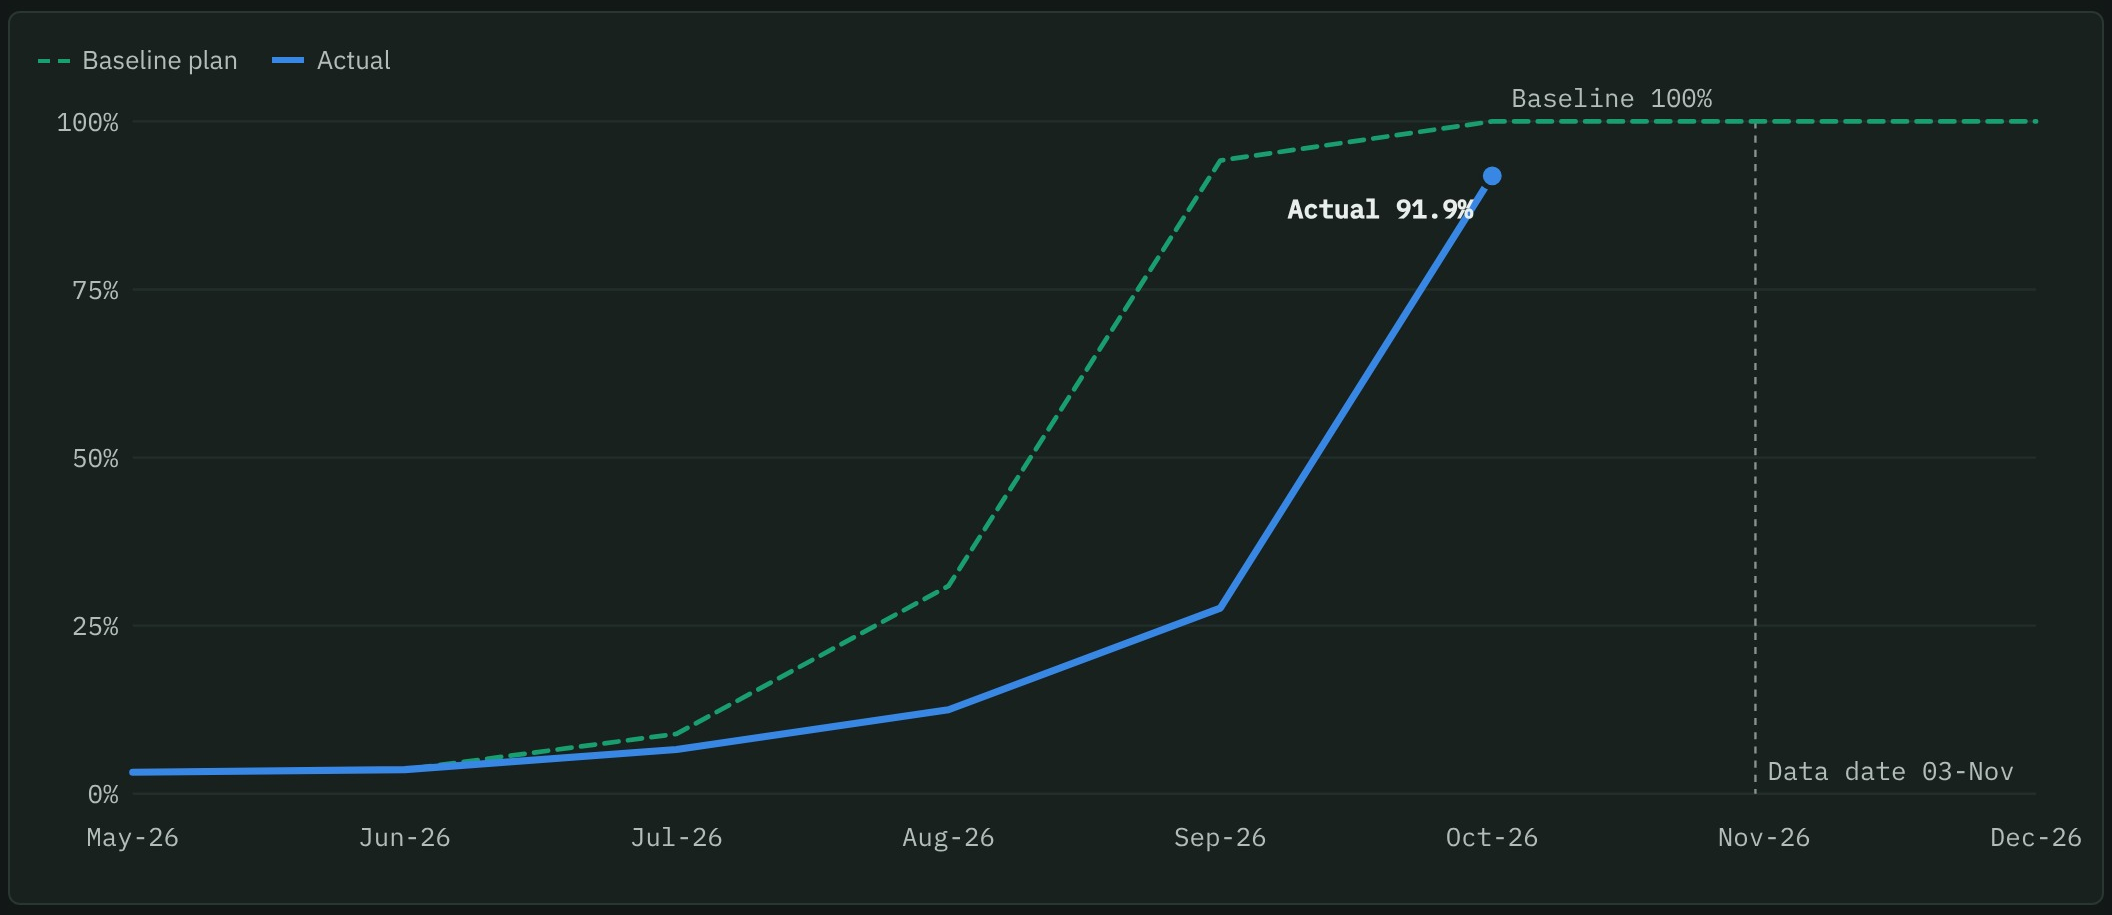

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
26-Oct-2026	100.0	77.1	−22.9%	+20.2%	0.77
03-Nov-2026	**100.0**	**91.9**	**−8.1%**	**+14.8%**	**0.92**

Physical % complete from the weekly reports of 26-Oct-2026 and 03-Nov-2026. "Gained this week" is the difference between the two reports; the 26-Oct gain is that report's own figure. Earlier weeks are not shown.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	13%	100.0%	98.9%	−1.1%	0.99	▼ Behind
Construction	75%	100.0%	94.8%	−5.2%	0.95	▼ Behind
· Fences	5.0%	100.0%	85.8%	−14.2%	0.86	▼ Behind
· Guard house 1	22.6%	100.0%	92.8%	−7.2%	0.93	▼ Behind
· Guard house 2	22.6%	100.0%	96.4%	−3.6%	0.96	▼ Behind
· Guard house 3	22.6%	100.0%	96.7%	−3.3%	0.97	▼ Behind
· External works	2.2%	100.0%	100.0%	0.0%	1.00	✓ Complete
Testing & commissioning	4%	100.0%	0.0%	−100.0%	0.00	▼ Not started
Total	100%	**100.0%**	**91.9%**	**−8.1%**	**0.92**	▼ Behind

Weights are shares of the 98,544 budgeted man-hours; the construction items (·) are part of Construction. Since the 26-Oct report Engineering gained 25.2%, Construction 16.6% and Procurement 8.5% of their own man-hours. The P6 update (data date 02-Nov-2026) has 554 activities: 465 completed, 62 in progress and 27 not started.

Milestones

Baseline dates from the P6 schedule print-out, weekly report forecasts from its Milestones sheet, and P6 forecasts and float from the P6 update (data date 02-Nov-2026).


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	06-May-2026	06-May-2026	07-Jul-2026 (actual)	–	✓ Done
Complete mobilisation	31-May-2026	06-May-2026	09-Jul-2026 (actual)	–	✓ Done
Complete fences	26-Aug-2026	–	03-Nov-2026	−24.0	▼ Late
Complete guard house 1	26-Aug-2026	–	03-Nov-2026	−24.0	▼ Late
Complete engineering	22-Sep-2026	22-Sep-2026	03-Nov-2026	−24.0	▼ Late
Complete external works	27-Sep-2026	–	03-Nov-2026	−24.2	▼ Late
Complete procurement	28-Sep-2026	28-Sep-2026	03-Nov-2026	−24.0	▼ Late
Testing & commissioning	05-Oct-2026	05-Oct-2026	14-Nov-2026	−33.2	▼ Late
Project finish	05-Oct-2026	05-Oct-2026	26-Nov-2026	−44.2	▼ Late

The weekly report's forecasts are already in the past.

The weekly report forecasts engineering, procurement and completion on their baseline dates (22-Sep, 28-Sep and 05-Oct-2026), all before the 03-Nov data date, and none is marked achieved. The P6 update forecasts five milestones on 03-Nov-2026, testing and commissioning on 14-Nov-2026 and project finish on 26-Nov-2026, with float from −24 to −44.2 days. It also records site handover on 07-Jul-2026, not 06-May-2026.

Manpower

Monthly head count on site, planned vs actual (staff plus labour). Source: Manpower sheet.

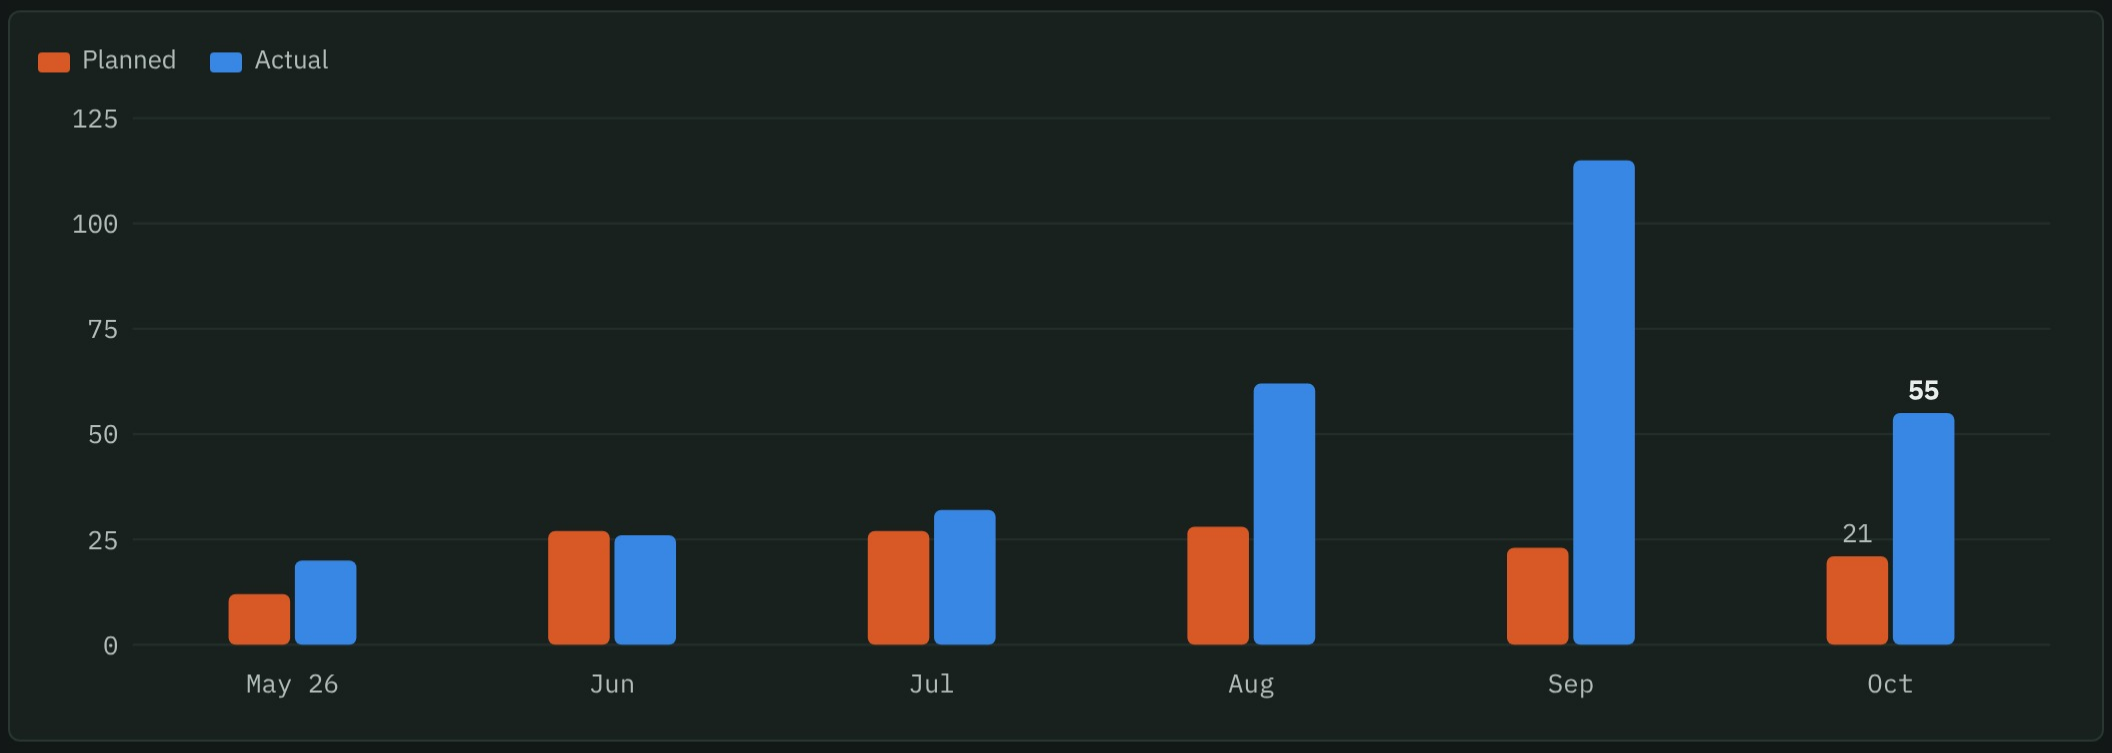

October head count is 55 (10 staff, 45 labour) against 21 planned; last week's report gave 60 for October. The sheet has no November column yet. Actual head count has been above plan since July and peaked at 115 in September.

Cost and invoicing

Contract value

Original contract value	15,898,659
Revised contract value	15,898,659
Change orders	0
Potential changes	0

All values in SAR. The contract change order log is empty. The invoice log header shows different values; see Data notes.

Invoices

Invoices submitted	4
Gross value	8,797,318
Approved by CM / PgM	4
Approved by MODON PM	0
Paid	0
Net incl. VAT	9,756,785

Invoicing is 55.3% of the contract value against 77.1% physical progress. The last invoice covers 25-Sep to 05-Oct-2026. No retention, advance payment or deduction is recorded.

Health, safety and quality

Safety Score 0.86

Safe man-hours (cumulative)	45,776
Man-hours this week	3,660
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	24 / 26

Sessions to date: 150 attended inductions and 380 attended toolbox talks.

Quality Score 0.86

NCRs issued (cumulative)	0
Site instructions	0
FIRs issued / closed	573 / 545
FIRs pending	28
MIRs issued / closed	68 / 63
MIRs pending	5
Shop drawings: code A / B / D	11 / 26 / 1
Material submittals	94

Consultant QC observation No. 18, 31-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Contract date passed	Contractor	The contract was due to finish on 05-Oct-2026. At 03-Nov-2026 the work is 91.9% complete and P6 schedules finish on 26-Nov-2026, with −44.2 days of float.
Materials approval and delivery	Contractor	Open risk in the register since 06-Jun-2026: delay in materials approval and delivery could delay completion. The treatment (expedite approvals and deliveries) was due 23-Oct-2026 and is still open, rated very high.
Remaining procurement	Contractor	In P6, 18 of 147 procurement activities are still in progress, with float between −24.1 and −44.2 days. The weekly report puts procurement at 98.9%.
Testing and commissioning	Contractor	Not started. Planned for 26-Sep to 05-Oct-2026; P6 now forecasts the milestone on 14-Nov-2026.
Invoice approval	MODON	Four invoices (8.80M SAR gross) are approved by the CM / PgM, but none is recorded as approved by the MODON PM or paid. No new invoice was added this week.

The weekly report's issue log and top-5 issues are empty. The risk register holds one open risk.

Data notes

- Progress rose from 77.1% in the 26-Oct-2026 report to 91.9% in this report (+14.8%), but this report's own weekly column shows +2.0% (1,965 man-hours) and gives the previous week as 90.0%. The guard houses' to-date man-hours rose by 3,271 to 4,248 each while their weekly column shows 0, and the Engineering weekly figure (830) repeats last week's. The two reports do not reconcile; please confirm.
- The workbook's data date is 03-Nov-2026; the P6 update and the file names give 02-Nov-2026. The "Two Weeks Look Ahead" print-out (DD 03-11-2026) still covers 28-Sep to 05-Oct-2026.
- The weekly report still gives 05-Oct-2026 as the forecast completion with 0 days of variance. The P6 update schedules 26-Nov-2026.
- Site handover is 06-May-2026 in the weekly report but 07-Jul-2026 in the P6 update. The week number (25) counts from 06-May-2026.
- The P6 update records actual start or finish dates after its 02-Nov-2026 data date for 183 activities (up to 24-Nov-2026), up from 107 last week, so its progress status is not reliable.
- The weekly report's activity counts (195 completed, 123 in progress, 236 not started) are unchanged from last week; the P6 update shows 465, 62 and 27.
- Engineering is 100% in the weekly report, but the P6 "Completion of Engineering Works" milestone is not started and forecast for 03-Nov-2026.
- The P6 print-out labels a cost-based progress figure as "Actual %". This report uses physical (man-hour) progress only.
- Several sheets still hold another project's data: Major Quantities (sewer, storm and water items dated 2024), the lower table of the Milestones sheet (SUD1-05-015) and Sheet1 (KUMT-05-001). The Procurement sheet's P6 activity column shows KHJ1-05010. The scope quantities section is therefore left out.
- The Procurement sheet marks 156 of 166 items as delivered, with no quantities delivered, while P6 shows 18 procurement activities still in progress. The procurement section is left out until the two agree.
- The invoice log header shows a revised contract value of 21,100,000 SAR, an estimate at completion of 20,900,000 SAR and potential changes of 200,000 SAR; all other sheets show 15,898,659.13 SAR and 0. Invoice 4's net amount incl. VAT repeats invoice 3's (2,864,258.52 SAR).
- October labour on site is now 45 (last week 50). Labour by trade totals 45 in the Weekly Progress Report sheet and 109 in the Manpower sheet.
- The Weekly Progress Report sheet shows MIRs and FIRs shifted by one column (63 / 5 and 545 / 28); the Quality-Stat sheet gives 68 issued, 63 closed, 5 pending and 573, 545, 28.
- Cumulative man-hours are 45,776, which is last week's 42,166 plus this week's 3,660 less 50. The safety score is 0.86 in the summary, 0.90 for the consultant's 31-Oct inspection and 0.8977 in the 01-Nov HSE inspection.
- One of the six photos in the "Weekly Photos" sheet is narrower than 600 px and is left out.
- The DB sheet shows #REF ! for the project scope and for several key dates.

Compiled 08-Nov-2026 from the weekly report, P6 update and schedule print-outs uploaded for the week of 05-Nov-2026 (data date 03-Nov-2026), compared with the 26-Oct-2026 report.
