Development of Infrastructure Networks, Al-Kharj Industrial City

تطوير شبكات البنية التحتية بالمدينة الصناعية بالخرج

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER
MODON	Moffreh Group (MMAH)	EGIS	Rakan Alotaibi	03-Dec-2025

CONTRACT COMPLETION
02-Dec-2027

Scope: infrastructure networks over about 3.5 km² in Zones A and B and the Labour Community Area, around 100 km south-east of Riyadh.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. A new revised plan was issued this week: planned progress to date is now 48.4%, down from 52.5% under the previous plan. Against it the project is 0.9% ahead, after gaining 2.2% this week.

PHYSICAL % COMPLETE
49.3% / 48.4% plan
▲ SPI 1.02 +0.9 pts

PROGRESS THIS WEEK
+2.2 pts / +1.0 plan
▲ 1.2 pts above the weekly plan

CONTRACT TIME ELAPSED
44.8% · day 327 of 730
▼ P6 finish 27-Apr-2028


INVOICED TO DATE (GROSS)
16.1% · 49.7M SAR
5 invoices, last period ends 30-Sep-2026

The schedule now finishes the project about five months late.

The P6 update uploaded with this week's report schedules project finish on 27-Apr-2028, 147 days after the contract completion date of 02-Dec-2027, with −126 days of float. The weekly report still forecasts 02-Dec-2027. Open activities with negative float rose from 701 to 1,243. Against the original baseline, which called for 83.0% by the end of October, the project remains far behind at 49.3%.

Site photos this week

Six photos from the 26-Oct-2026 weekly report, GPS-stamped 27-Oct-2026 where the stamp is visible. Asphalt, curbs and street lighting continue, and the site office cabin and a concrete building shell are progressing. Select a photo to view it larger, then use the arrows to move between photos.

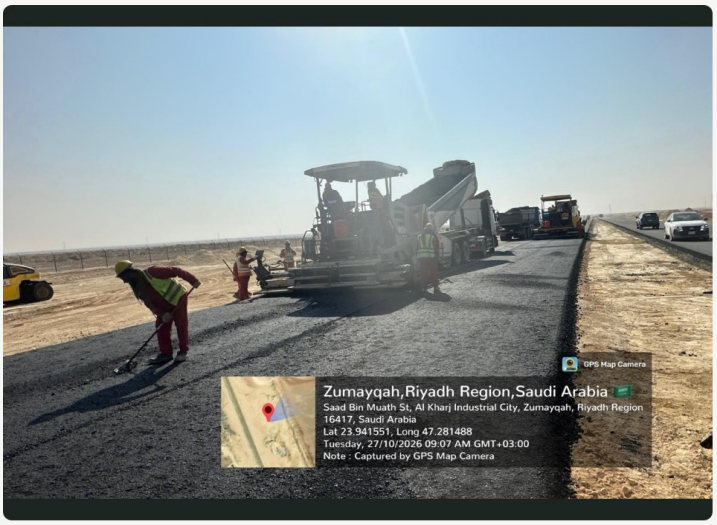


Asphalt paving

Paver and crew on the binder course. GPS-stamped 27-Oct-2026, 09:07.



Asphalt compaction

Pneumatic and tandem rollers on the new layer.

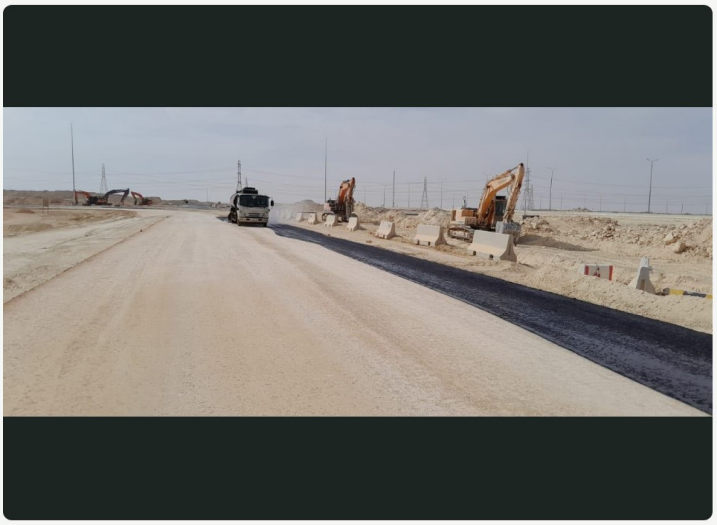

Road works

Finished asphalt lane beside the base course, with excavators working ahead.



Curbs and street lighting

Curbstones set along the road edge, with lighting poles installed.



Site office cabin

Prefabricated cabin with its cladding fitted.




Concrete building shell

Reinforced concrete shell completed.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

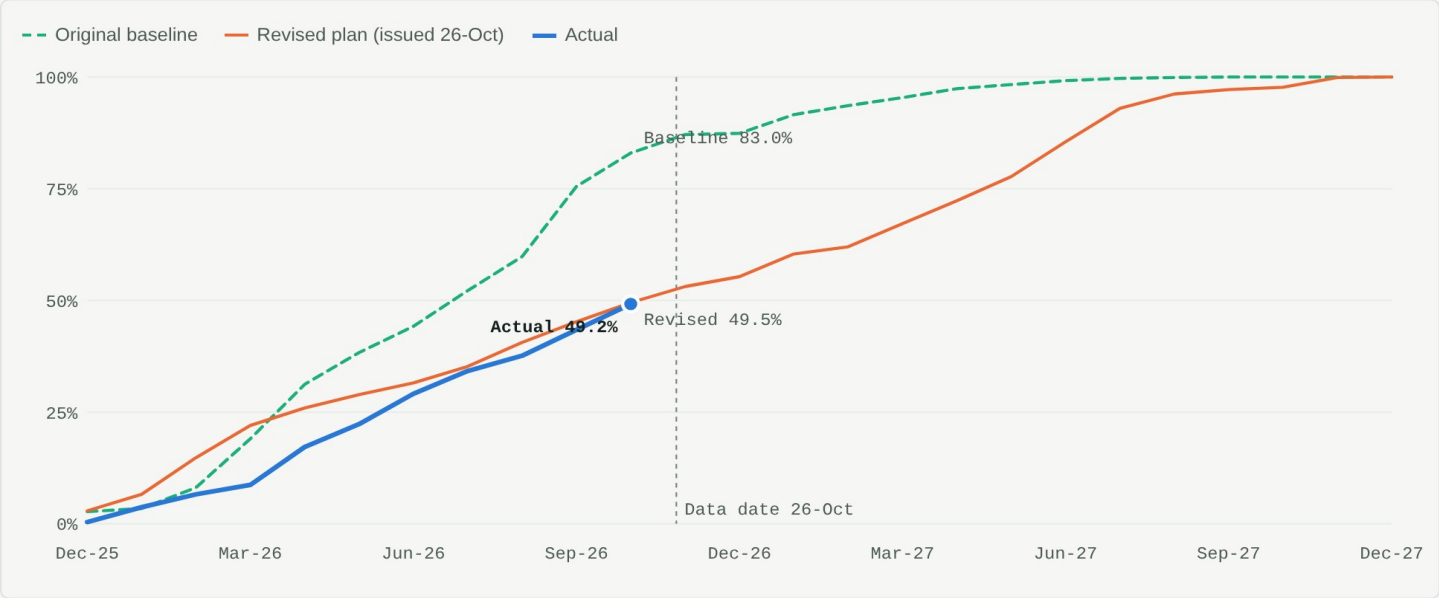

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
28-Sep-2026	47.2	42.5	−4.7	+0.8	0.90
05-Oct-2026	50.1	43.4	−6.7	+0.9	0.87
12-Oct-2026	51.4	45.7	−5.7	+2.3	0.89
19-Oct-2026	52.5	47.0	−5.5	+1.3	0.89
26-Oct-2026	**48.4***	**49.3**	**+0.9**	**+2.2**	**1.02**

Physical % complete from the weekly reports for 28 Sep to 26 Oct. * From 26 Oct the planned value comes from the new revised plan, so the move from −5.5 to +0.9 reflects the new plan as well as this week's progress.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	3%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	20%	68.6%	76.5%	+7.9	1.12	▲ Ahead
Construction	67%	44.8%	46.2%	+1.4	1.03	▲ On track
Testing & commissioning	10%	16.0%	0.0%	−16.0	0.00	▼ Not started
Total	100%	**48.4%**	**49.3%**	**+0.9**	**1.02**	▲ On track

The P6 update (schedule revision ICKM01-22.Oct.2026, data date 17-Oct-2026) has 5,877 activities: 3,671 completed, 254 in progress and 1,952 not started. Its scheduled finish is 27-Apr-2028, 147 days after the contract date.

Scope of work: quantities

Total scope, quantity finished and quantity remaining for each network, from the quantity tables on the layout pages of the 26-Oct-2026 progress presentation. For pipes, cables and manholes, "finished" means installed; the last column shows how much is also backfilled. "This week" is the quantity executed since the 19-Oct-2026 presentation.

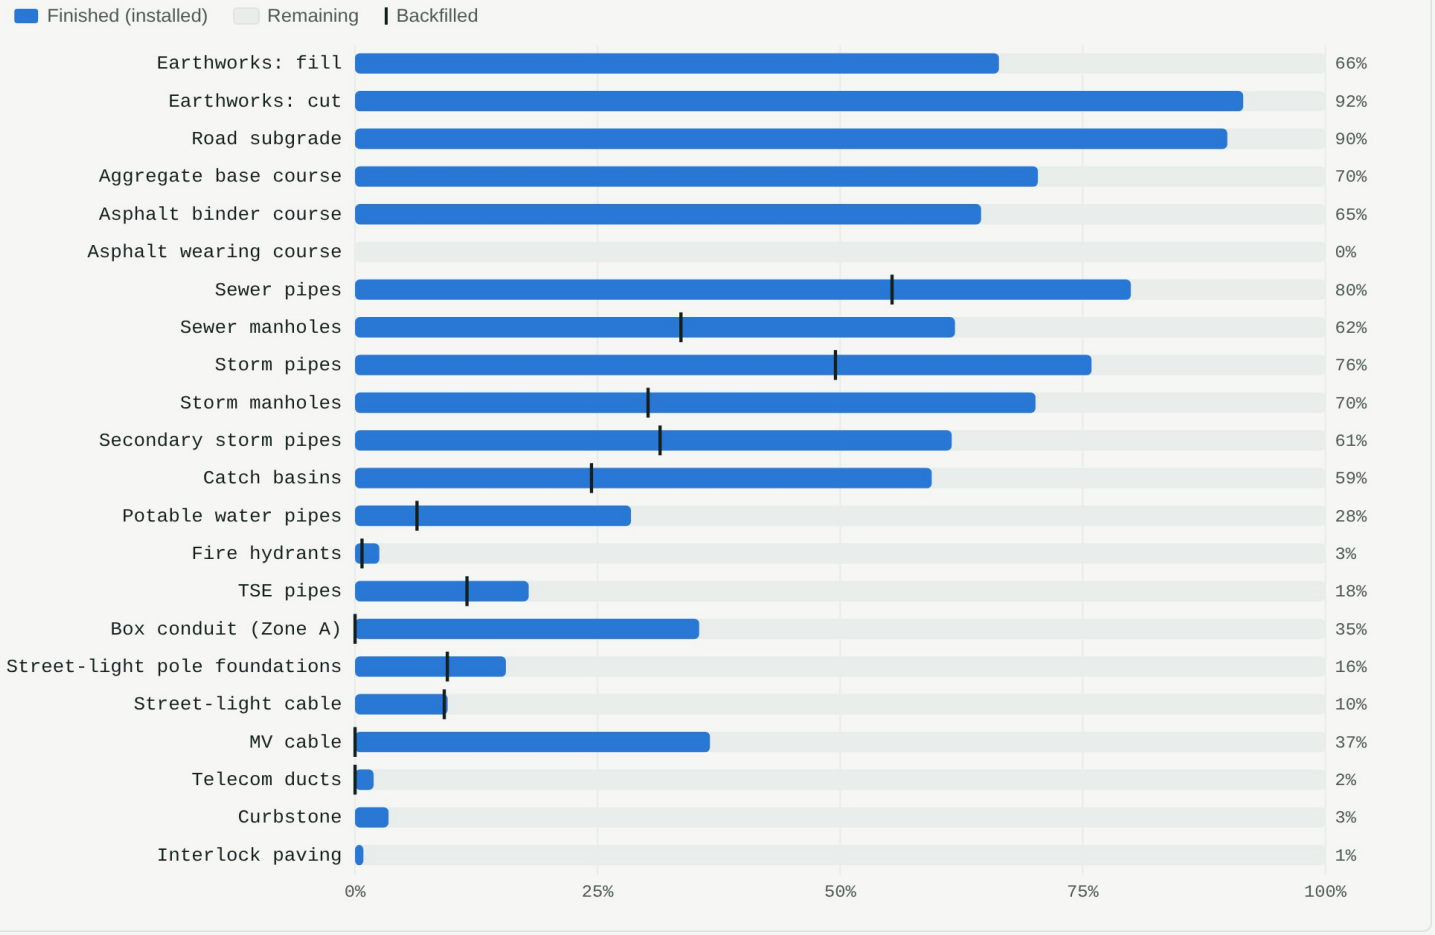

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Earthworks: fill	A	m³	357,335	268,632	0	88,703	75.2%	–
	B	m³	499,555	300,000	+18,324	199,555	60.1%	–
	Total	m³	**856,890**	**568,632**	**+18,324**	**288,258**	**66.4%**	–
Earthworks: cut	A	m³	97,475	89,831	0	7,644	92.2%	–
	B	m³	40,190	36,189	0	4,001	90.0%	–
	Total	m³	**137,665**	**126,020**	**0**	**11,645**	**91.5%**	–
Road subgrade	A	m³	82,330	73,996	+16,762	8,334	89.9%	–
	B	m³	78,595	70,682	+1,223	7,913	89.9%	–
	Total	m³	**160,926**	**144,678**	**+17,985**	**16,248**	**89.9%**	–
Aggregate base course	A	m³	52,379	35,604	+4,336	16,775	68.0%	–
	B	m³	47,537	34,715	+3,444	12,822	73.0%	–
	Total	m³	**99,916**	**70,319**	**+7,780**	**29,597**	**70.4%**	–
Asphalt binder course	A	m³	19,245	12,211	+1,955	7,034	63.5%	–
	B	m³	24,948	16,303	+1,614	8,645	65.3%	–
	Total	m³	**44,192**	**28,514**	**+3,569**	**15,678**	**64.5%**	–
Asphalt wearing course	A	m³	12,400	0	0	12,400	0.0%	–
	B	m³	11,205	0	0	11,205	0.0%	–
	Total	m³	**23,605**	**0**	**0**	**23,605**	**0.0%**	–
Sewer pipes	A	LM	14,308	11,541	+1,011	2,767	80.7%	50.7%
	B	LM	7,539	5,928	0	1,611	78.6%	64.1%
	Total	LM	**21,847**	**17,468**	**+1,011**	**4,378**	**80.0%**	55.3%
Sewer manholes	A	EA	286	160	+25	126	55.9%	39.5%
	B	EA	107	83	0	24	77.6%	17.8%
	Total	EA	**393**	**243**	**+25**	**150**	**61.8%**	33.6%
Storm pipes	A	LM	14,482	10,911	+331.4	3,571	75.3%	52.4%
	B	LM	8,544	6,568	+264	1,977	76.9%	44.6%
	Total	LM	**23,026**	**17,479**	**+595.4**	**5,547**	**75.9%**	49.5%
Storm manholes	A + Labour Camp	EA	194	124	+13	70	63.9%	33.5%
	B	EA	104	85	0	19	81.7%	24.0%
	Total	EA	**298**	**209**	**+13**	**89**	**70.1%**	30.2%
Secondary storm pipes	A	LM	7,207	4,544	+217.6	2,663	63.0%	44.4%
	B	LM	5,323	3,162	+91.5	2,161	59.4%	13.9%
	Total	LM	**12,529**	**7,705**	**+309.1**	**4,824**	**61.5%**	31.4%
Catch basins	A	EA	416	221	+18	195	53.1%	25.5%
	B	EA	257	179	0	78	69.6%	22.6%
	Total	EA	**673**	**400**	**+18**	**273**	**59.4%**	24.4%
Potable water pipes	A + Labour Camp	LM	20,475	2,445	–	18,030	11.9%	1.4%
	B	LM	10,308	6,310	+125.3	3,998	61.2%	16.2%
	Total	LM	**30,783**	**8,754**	**–**	**22,029**	**28.4%**	6.4%
Fire hydrants	A	EA	170	3	0	167	1.8%	1.2%
	B	EA	110	4	0	106	3.6%	0.0%
	Total	EA	**280**	**7**	**0**	**273**	**2.5%**	0.7%
TSE pipes	A	LM	13,023	130	0	12,893	1.0%	0.0%
	B	LM	10,991	4,167	+220	6,824	37.9%	25.2%
	Total	LM	**24,014**	**4,297**	**+220**	**19,717**	**17.9%**	11.5%
Box conduit (Zone A)	A	LM	1,500	532	0	968	35.5%	0.0%
Street-light pole foundations	A	EA	509	68	0	441	13.4%	0.0%
	B	EA	353	66	0	287	18.7%	23.2%
	Total	EA	**862**	**134**	**0**	**728**	**15.5%**	9.5%
Street-light cable	A	LM	26,093	1,831	0	24,262	7.0%	7.0%
	B	LM	18,277	2,403	0	15,873	13.1%	12.3%
	Total	LM	**44,370**	**4,234**	**0**	**40,136**	**9.5%**	9.2%
MV cable	A	LM	27,225	5,313	0	21,912	19.5%	0.0%
	B	LM	44,775	21,024	0	23,751	47.0%	0.0%
	Total	LM	**72,000**	**26,337**	**0**	**45,663**	**36.6%**	0.0%
Telecom ducts	A	LM	34,149	0	0	34,149	0.0%	0.0%
	B	LM	20,299	1,042	0	19,257	5.1%	0.0%
	Total	LM	**54,448**	**1,042**	**0**	**53,406**	**1.9%**	0.0%
Curbstone	A	LM	81,768	1,041	0	80,727	1.3%	–
	B	LM	74,109	4,333	0	69,776	5.8%	–
	Total	LM	**155,877**	**5,374**	**0**	**150,503**	**3.4%**	–
Interlock paving	A	m²	71,538	0	0	71,538	0.0%	–
	B	m²	68,822	1,206	+1,206	67,616	1.8%	–
	Total	m²	**140,359**	**1,206**	**+1,206**	**139,154**	**0.9%**	–

Culverts

Culverts 01 (Local Road 19) and 02 (Local Road 20) are complete. Culvert 05 (Local Road 23) has all 35 precast units installed. Culvert 06 (Local Road 24) has 37 units installed with excavation still ongoing. Box conduit in Zone A is 35% installed and not yet backfilled.

Not yet started or barely started

Asphalt wearing course and Zone A telecom are at 0%. Interlock is at 0.9% (Zone B only), curbstone about 3%, fire hydrants 2–4%, Zone A TSE 1% and Zone A potable water 12%. The storm network in the Factory Area appears in this week's presentation for the first time, with no work started yet.

Milestones

The weekly report and the P6 schedule update give different forecasts for the interim milestones. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	03-Dec-2025	03-Dec-2025	03-Dec-2025 (actual)	–	✓ Done
Complete mobilisation	02-Jan-2026	02-Jan-2026	–	–	✓ Done
Road works	02-Oct-2026	07-Nov-2026 (+36 d)	20-Dec-2026	−68	▼ Late
Medium-voltage network	02-Oct-2026	31-Oct-2026 (+29 d)	28-Jan-2027	−102	▼ Late
Storm network	–	–	03-Mar-2027	−24	▼ At risk
Sewage network	–	–	14-Mar-2027	−33	▼ At risk
Telecom network	–	–	25-May-2027	−94	▼ Late
Irrigation network	–	–	18-Jul-2027	−141	▼ Late
Potable water network	–	–	30-Oct-2027	−230	▼ Late
All networks	02-Feb-2027	02-Feb-2027	–	–	? Conflicts with P6
Landscape	–	–	19-Apr-2028	−118	▼ Late
Project handover	02-Dec-2027	02-Dec-2027	27-Apr-2028	−126	▼ Late

The P6 dates conflict with the "All networks" milestone of 02-Feb-2027 and with the contract completion date.

This week's P6 update finishes the networks between December 2026 and October 2027 and the project on 27-Apr-2028. The weakest point is the potable water network at −230 days, driven by gate valves. Negative float now covers 1,243 open activities, led by traffic signage (74), ground cover and shrubs (64), trees and palms (61), landscaping items (60) and precast curbs (47).

Procurement of key materials

Share of total quantity delivered to site. Source: Procurement sheet, weekly report 26-Oct-2026.



Interlock paving: 3% delivered


3,780 of 129,381 LM. The sample is still not approved and supply remains on hold, yet 1,206 m² is now reported as installed in Zone B.

Valves, ICT manholes and planting

Sluice valves 347 of 2,723 delivered (13%). ICT manholes 0 of 214, due by 20-Nov. Planting (30,556 m²) waits for the final quantity to be agreed. MV cable is at 61 of 72 km, waiting for SEC to waive the factory acceptance test.

Workforce

Monthly head count on site, planned vs actual. Source: Manpower sheet.

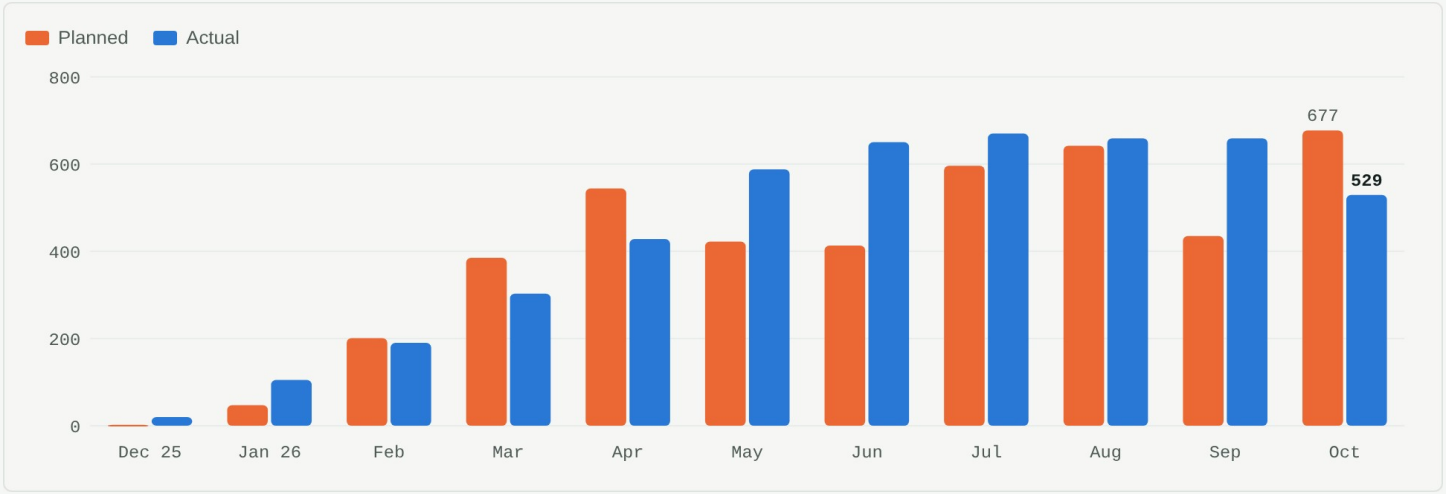

October head count is 529 against 677 planned (−22%). The 26-Oct report repeats last week's October figure. The plan peaks at 841 in November 2026.

Cost and invoicing

Contract value

Package 01: infrastructure, 3.5 km²	226,527,683
Package 02: Labour Camp area	18,085,168
Package 03: mosque, helipad, stormwater, road rehab	23,118,731
BOQ total (excl. VAT)	**267,731,582**
Contract value incl. 15% VAT	307,891,320
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. No change orders are registered.

Invoices

Invoices submitted	5
Gross value	49,710,656
Retention (10%)	4,971,066
Deductions and penalties	111,000
Net incl. VAT	51,339,529
FIR value to date	61,710,656

Invoicing is 16.1% of the contract value against 49.3% physical progress. The invoice log records approval dates for all five invoices, but its summary shows 0 PM-approved and 0 paid. The payment status needs confirming.

Health, safety and quality

Safety Score 0.90

Safe man-hours (cumulative)	1,135,445
Man-hours this week	30,630
Lost-time injuries	0
Fatalities	0
First-aid cases	6
Near misses	2
Property damage	3
Inductions / toolbox talks	1,944 / 217

Quality Score 0.93

FIRs this week: approved	294
FIRs this week: rejected	9
FIRs under review	49
Tests performed (cumulative)	2,450
NCRs issued (cumulative)	37
RFIs open / closed	1 / 122
Approved MIRs	49
Approved shop drawings	2,087

Quality week: 18–24 Oct 2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Site obstacles	Client	Obstacles between the factory boundary and Local Roads 19–20. Old rooms, a fenced store and signage on Local Road 18. A diesel tank whose removal is unassigned. The crusher area is not yet officially handed over.
MV network clashes	Contractor	The MV route runs too close to the water and irrigation networks, which is preventing internal MV works from starting.
Box culvert, Zone A	Contractor	Excavation for the stormwater box culvert conflicts with existing LV/MV cables and water and irrigation pipelines.
Asphalt continuity	Contractor	Asphalt works need to continue without interruption to recover the road milestone.
Milestone recovery	Contractor	Engineering and procurement recovery are closed; construction recovery is ongoing.
Cost savings	Contractor	Identify potential financial and technical savings.

Open risks in the register: weather (rain, wind, dust), supply of subgrade fill, manholes and pipes, deep excavation safety, existing services and roads, and delays in key materials.

Data notes

- Several summary panels in the weekly report workbook (submittals, procurement, manpower by trade, top issues) show #REF! errors, so figures were taken from the detail sheets.
- Milestone forecasts in the weekly report do not match the P6 update, and the two now disagree on the completion date as well; see Milestones.
- A new revised plan was issued with the 26-Oct report. Planned progress to date fell from 52.5% to 48.4%, so most of the change from −5.5% to +0.9% comes from the new plan rather than from this week's work.
- The P6 update uploaded on 26 Oct has a data date of 17-Oct-2026, the same as the previous week's file, so it does not include the last week of work.
- The manpower sheet repeats last week's October figure (529).
- Approved MIRs show 49 cumulative this week against 213 last week; the counter appears to have been reset.
- The quality sheet lists 53,207 approved FIRs for the previous week, which looks like a data-entry error.
- Weekly reports are in W1–W5 (28 Sep to 26 Oct). Copies of the original Excel and PDF files were also uploaded into W1's MD Files folder; they belong in All Files.
- Scope quantities: this week's presentation adds the missing Potable Water Zone A table and corrects the Zone A telecom total from 155,000 LM to 34,149 LM. Street-light pole counts are still labelled LM in the source but are counted in units (EA).

Compiled 28-Oct-2026 from the weekly reports uploaded for weeks ending 28 Sep to 26 Oct 2026.
