# 44 Ready-Built Factories (900 m²), Dammam 3rd Industrial City

## إنشاء 44 مصنع جاهز (900 متر مربع) في المدينة الصناعية بالدمام الثالثة

| CLIENT | CONTRACTOR | CONSULTANT | MODON PM | SITE HANDOVER | CONTRACT COMPLETION |
|---|---|---|---|---|---|
| MODON | Saudi Zaas Construction | EGIS | Engr. Affat Al-Enezi | 07-Jan-2026 | 06-Mar-2027 |

Scope: 44 ready-built factories of 900 m² each in 11 blocks (B1–B11), with external utilities, roads, parking and street lighting.

---

## Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (225,761 man-hours in total). At the 03-Nov-2026 data date the project is 81.4% complete against 80.6% planned, 0.8% ahead. This week added 1.3% against 1.4% planned. Construction of the factory blocks remains 0.9% behind, and Blocks B4 and B5 are still about 21% and 20% behind their plan.

**PHYSICAL % COMPLETE**
**81.4%** / 80.6% plan
▲ SPI 1.01 +0.8%

**PROGRESS THIS WEEK**
**+1.3**% / +1.4% plan
▼ Slightly below the weekly plan

**CONTRACT TIME ELAPSED**
**70.9%** · day 300 of 423
● P6 finish 03-Mar-2027

**INVOICED TO DATE (GROSS)**
**52.1%** · 50.1M SAR
7 invoices, last period ends 31-Oct-2026

**On plan overall, but almost no float is left at the finish.**

The P6 update finishes the project on 03-Mar-2027, three days before the contract completion date of 06-Mar-2027, with zero float on project completion. All 100 activities in progress are counted as behind schedule, and 229 activities have missed their start. Construction is 75.8% complete against 76.7% planned, and the civil works milestone slipped another week in P6, to 28-Nov-2026.


## Site photos this week

Six of the 20 photos uploaded this week. The photos carry no date stamp; the weekly report's photo sheet lists fire pump works, solar panels at Block 6, partition walls at Block 9 and cladding at Block 5. Select a photo to view it larger, then use the arrows to move between photos.



**Fire pump works**

Pumps and red fire-fighting pipework, with scaffolding at the tank.

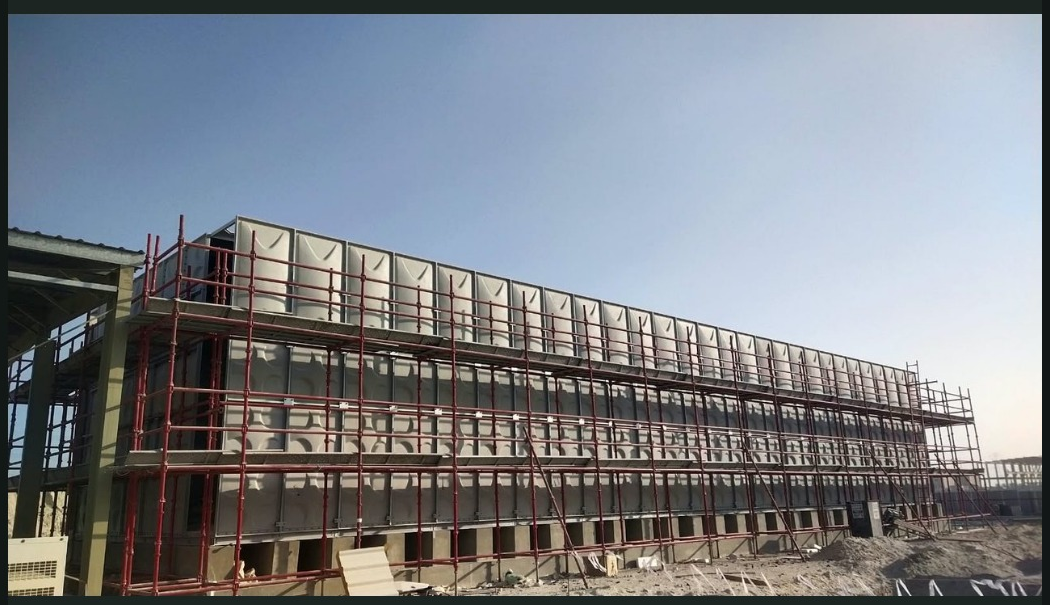

**Water tank**

Sectional panel tank with scaffolding around it.




**Partition wall works**

Blockwork partition wall inside a factory hall.



**Cladding**

Wall and roof cladding on a factory corner.

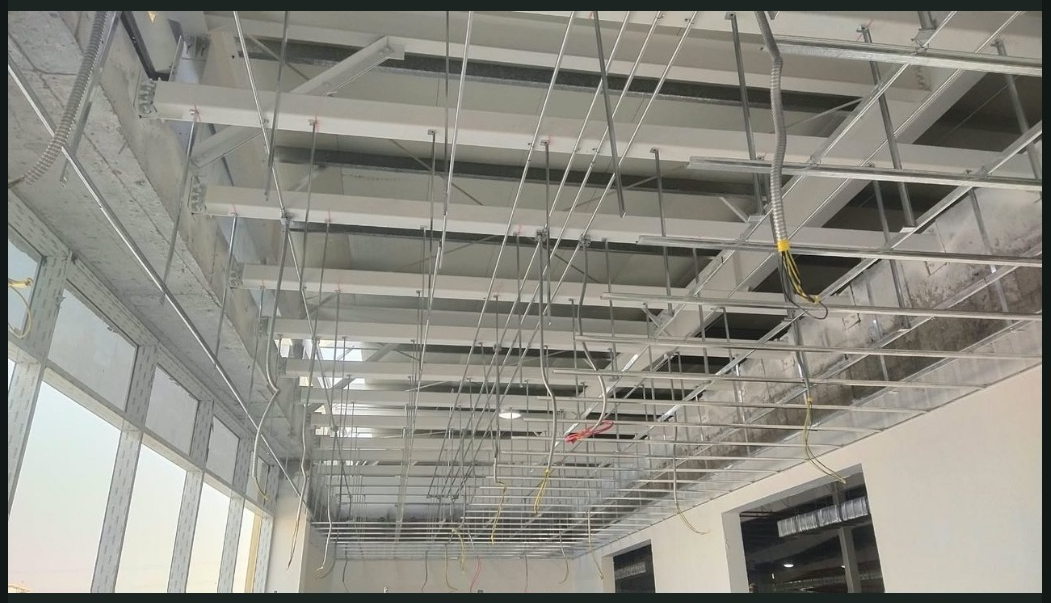

**Office ceiling framing**

Hangers and frame for the gypsum board ceiling.




**Factory hall**

Lighting and fire-fighting pipes installed; materials staged on the floor.

## Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

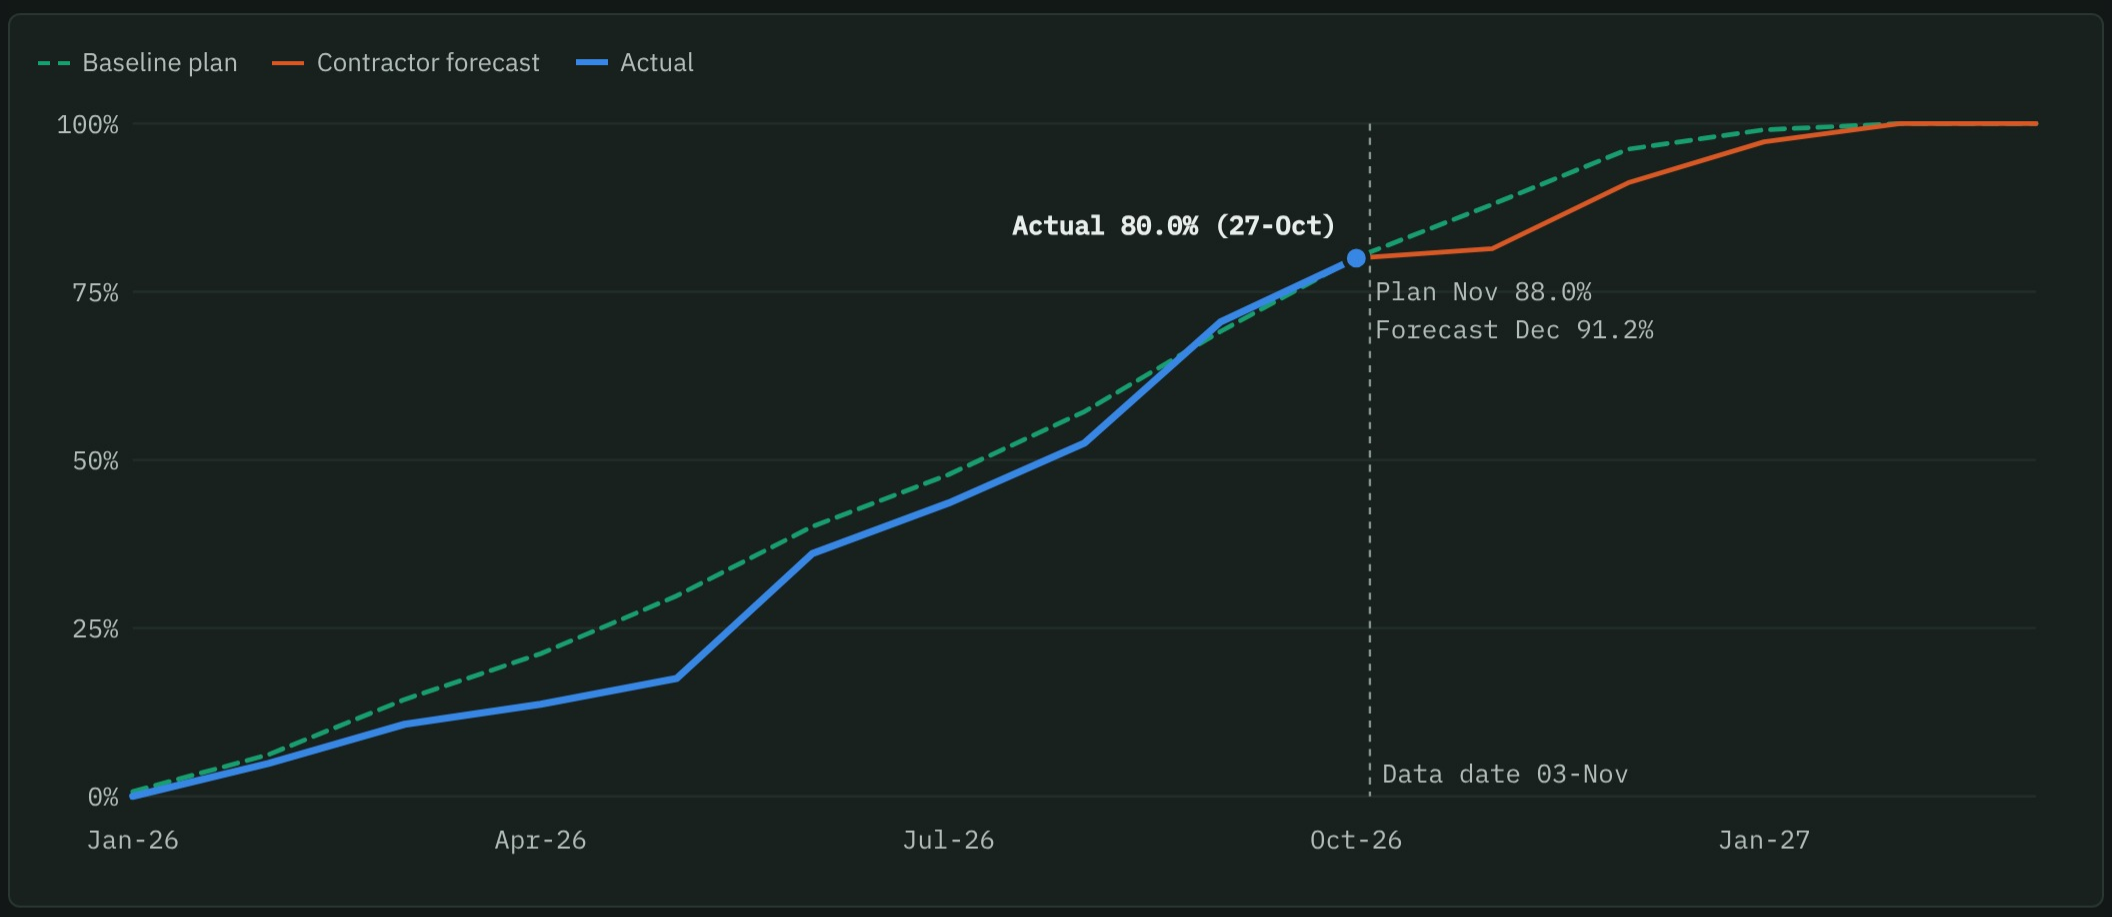


| PERIOD ENDING | PLANNED % | ACTUAL % | VARIANCE | GAINED IN PERIOD | SPI |
|---|---|---|---|---|---|
| 31-Jul-2026 | 47.8 | 43.6 | −4.2% | +7.5 | 0.91 |
| 31-Aug-2026 | 57.2 | 52.5 | −4.7% | +8.9 | 0.92 |
| 30-Sep-2026 | 69.1 | 70.5 | +1.4% | +18.0 | 1.02 |
| 27-Oct-2026 | 79.2 | 80.0 | +0.8% | +9.5* | 1.01 |
| **03-Nov-2026** | **80.6** | **81.4** | **+0.8%** | **+1.3** | **1.01** |

Month-end values from the Physical-Chart Data sheet; the 27-Oct-2026 and 03-Nov-2026 rows are from the weekly reports' progress tables (WPR #36 and #37). The baseline and revised plans in the file are identical, so one plan line is shown; the chart's actual line ends at the October value, and its forecast line starts from the 03-Nov actual. * Gained from 01 to 27 Oct. The 03-Nov gain is this week's: 3,015 earned man-hours against 3,061 planned.

## Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

| PHASE | WEIGHT | PLANNED | ACTUAL | VARIANCE | SPI | STATUS |
|---|---|---|---|---|---|---|
| Mobilisation | 0.4% | 100.0% | 100.0% | 0.0% | 1.00 | ✓ Complete |
| Engineering | 5.4% | 100.0% | 100.0% | 0.0% | 1.00 | ✓ Complete |
| Procurement | 25.5% | 99.9% | 100.0% | +0.1% | 1.00 | ✓ Complete |
| Construction | 63.4% | 76.7% | 75.8% | −0.9% | 0.99 | ▼ Slightly behind |
| Testing & commissioning | 5.1% | 13.6% | 40.6% | +27.0% | 2.99 | ? Check |
| Project closeout | 0.3% | 0.0% | 0.0% | 0.0% | – | ● Not yet due |
| **Total** | 100% | **80.6%** | **81.4%** | **+0.8%** | **1.01** | ▲ On track |

The P6 update (data date 03-Nov-2026) has 2,517 activities: 1,796 completed, 100 in progress and 621 not started. Its scheduled finish is 03-Mar-2027, three days before the contract date. Critical-path activities fell from 85 to 74 this week. Testing and commissioning earned nothing this week.

## Scope of work: quantities


Physical progress of each factory block and of the external works, then the major quantities tracked in the weekly report. Source: weekly report 03-Nov-2026, progress table and Major Quantities sheet; "this week" is the change since the 27-Oct-2026 report.

### Physical progress by block

| BLOCK | MAN-HOURS | PLANNED | ACTUAL | VARIANCE | SPI | EARNED THIS WEEK (MAN-HOURS) |
|---|---|---|---|---|---|---|
| Block B1 | 11,840 | 74.8% | 73.6% | −1.3% | 0.98 | 104 |
| Block B2 | 11,584 | 78.3% | 75.4% | −2.9% | 0.96 | 176 |
| Block B3 | 11,824 | 76.3% | 75.5% | −0.8% | 0.99 | 256 |
| Block B4 | 11,824 | 99.1% | 77.5% | −21.6% | 0.78 | 248 |
| Block B5 | 11,728 | 99.0% | 78.8% | −20.2% | 0.80 | 382 |
| Block B6 | 11,824 | 95.5% | 3.7%* | −91.8% | 0.04 | 0 |
| Block B7 | 11,840 | 79.9% | 81.8% | +1.9% | 1.02 | 152 |
| Block B8 | 11,840 | 72.8% | 80.9% | +8.1% | 1.11 | 209 |
| Block B9 | 11,840 | 71.9% | 79.8% | +7.9% | 1.11 | 68 |
| Block B10 | 11,840 | 70.7% | 78.7% | +8.0% | 1.11 | 224 |
| Block B11 | 11,840 | 69.5% | 77.9% | +8.5% | 1.12 | 247 |
| External works | 13,232 | 37.4% | 52.8% | +15.5% | 1.41 | 507 |
| **Construction total** | **143,056** | **76.7%** | **75.8%** | **−0.9%** | **0.99** | **3,015** |

* Block B6 is still recorded with 437 of 11,824 man-hours earned, while the progress tracking sheet shows its structure, walls and first-fix works complete and the weekly report lists solar panel works there this week. The figure is probably an entry error; see Data notes.

### Major quantities

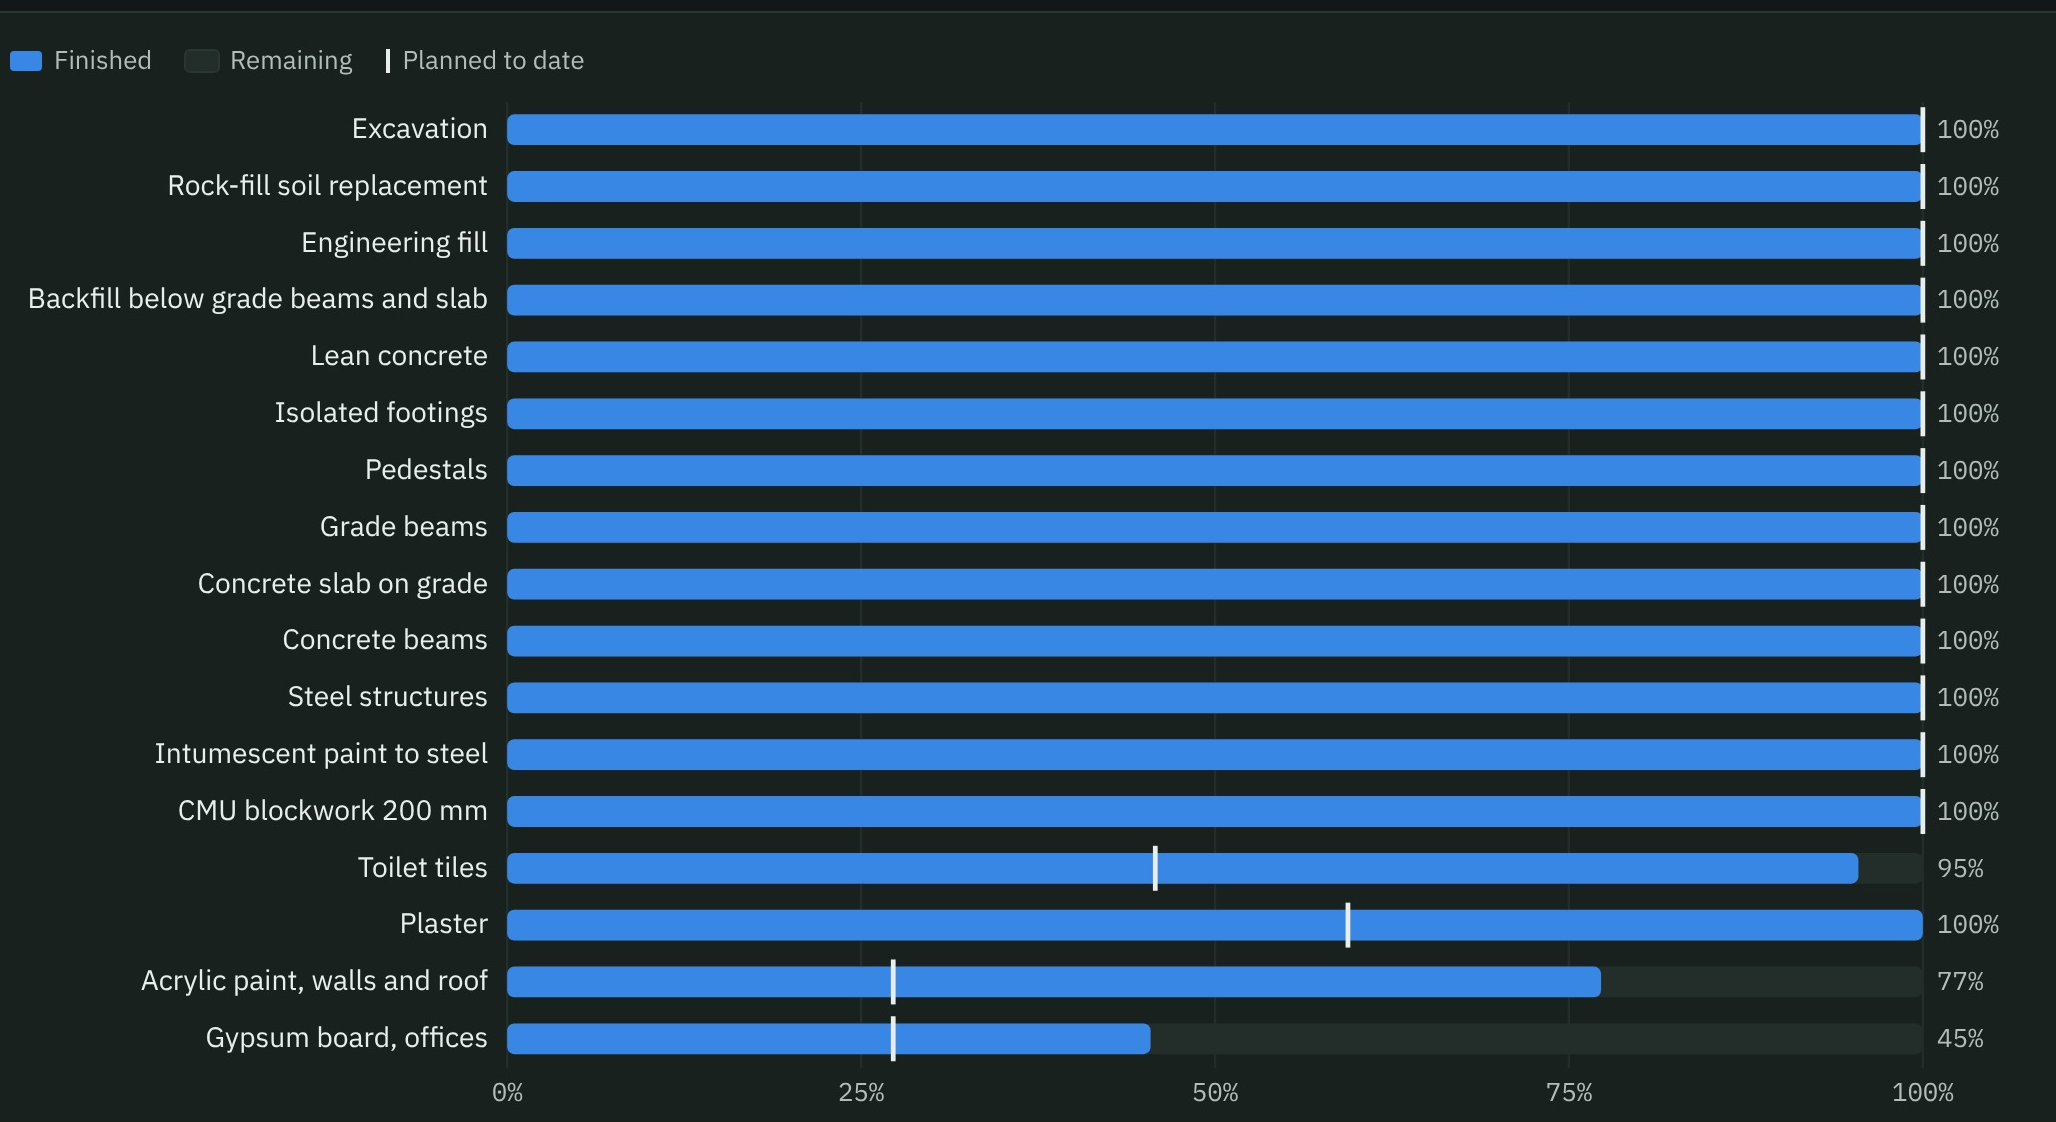


| SCOPE ITEM | ZONE | UNIT | TOTAL | FINISHED | THIS WEEK | REMAINING | % FINISHED | PLANNED TO DATE |
|---|---|---|---|---|---|---|---|---|
| **Excavation** | All blocks | m³ | 40,940 | 40,940 | 0 | 0 | 100.0% | 100.0% |
| **Rock-fill soil replacement** | All blocks | m³ | 48,560 | 48,560 | 0 | 0 | 100.0% | 100.0% |
| **Engineering fill** | All blocks | m³ | 12,727 | 12,727 | 0 | 0 | 100.0% | 100.0% |
| **Backfill below grade beams and slab** | All blocks | m³ | 11,559 | 11,559 | 0 | 0 | 100.0% | 100.0% |
| **Lean concrete** | All blocks | m² | 8,010 | 8,010 | 0 | 0 | 100.0% | 100.0% |
| **Isolated footings** | All blocks | m³ | 2,807 | 2,807 | 0 | 0 | 100.0% | 100.0% |
| **Pedestals** | All blocks | m³ | 395 | 395 | 0 | 0 | 100.0% | 100.0% |
| **Grade beams** | All blocks | m³ | 540 | 540 | 0 | 0 | 100.0% | 100.0% |
| **Concrete slab on grade** | All blocks | m³ | 7,260 | 7,260 | 0 | 0 | 100.0% | 100.0% |
| **Concrete beams** | All blocks | m³ | 255 | 255 | 0 | 0 | 100.0% | 100.0% |
| **Steel structures** | All blocks | nos | 11 | 11 | 0 | 0 | 100.0% | 100.0% |
| **Intumescent paint to steel** | All blocks | items | 11 | 11 | 0 | 0 | 100.0% | 100.0% |
| **CMU blockwork 200 mm** | All blocks | m² | 9,630 | 9,630 | 0 | 0 | 100.0% | 100.0% |
| **Toilet tiles** | All blocks | m² | 820 | 782.7 | +55.8 | 37.3 | 95.5% | 45.8% |
| **Plaster** | All blocks | m² | 16,770 | 16,770 | 0 | 0 | 100.0% | 59.4% |
| **Acrylic paint, walls and roof** | All blocks | m² | 16,770 | 12,958 | +1,982 | 3,812 | 77.3% | 27.3% |
| **Gypsum board, offices** | All blocks | m² | 4,425 | 2,011 | +603.1 | 2,414 | 45.4% | 27.3% |

**Substructure, steel and blockwork complete**

Excavation, rock-fill replacement, engineering fill, footings, pedestals, grade beams, slab on grade, the 11 steel structures with intumescent paint, and 9,630 m² of blockwork are all reported 100% complete. Plaster is also complete (16,770 m²). No change in these items this week.

**Finishes still open**

This week added 1,982 m² of acrylic paint (now 77.3%, 3,812 m² remaining), 603 m² of office gypsum board (45.4%, 2,414 m² remaining) and 56 m² of toilet tiles (95.5%, 37 m² remaining).

## Milestones

Milestones from the weekly report, with the P6 update's forecast and float. Where the weekly report has no such milestone, the P6 baseline is shown and marked (P6).

| MILESTONE | BASELINE | WEEKLY REPORT FORECAST | P6 UPDATE FORECAST | P6 FLOAT (DAYS) | STATUS |
|---|---|---|---|---|---|
| Site handover | 07-Jan-2026 | 07-Jan-2026 | 07-Jan-2026 (actual) | – | ✓ Done |
| Existing-condition survey and final reports | 14-Jan-2026 | 14-Jan-2026 | 12-Feb-2026 (actual) | – | ✓ Done |
| Complete mobilisation | 16-Feb-2026 | 16-Feb-2026 | 18-Jan-2026 (actual) | – | ✓ Done |
| Submittals and long-lead orders | 14-May-2026 | 22-Mar-2026 (−53 d) | 05-Jul-2026 (actual) | – | ✓ Done |
| Delivery of all equipment and materials | 07-Nov-2026 | 27-Sep-2026 (−41 d) | – | – | ✓ Done |
| Site levelling, local roads and parking | 12-Feb-2026 (P6) | – | 03-Nov-2026 | 9 | ▼ Late |
| Civil works | 21-Feb-2027 | 21-Feb-2027 | 28-Nov-2026 | 43 | ? Baselines differ |
| Testing and commissioning | 06-Feb-2027 (P6) | – | 27-Dec-2026 | 56 | ● Float available |
| Mechanical works | 27-Jan-2027 | 27-Jan-2027 | 27-Dec-2026 | 51 | ● Float available |
| Earthworks | 01-Feb-2027 | 21-Jan-2027 (−11 d) | – | – | ● On time |
| Electrical works | 18-Feb-2027 | 13-Feb-2027 (−5 d) | 02-Feb-2027 | 19 | ● Float available |
| Construction completion | 21-Feb-2027 (P6) | – | 23-Feb-2027 | 7 | ▼ At risk |
| All works complete, ready for handover | 06-Mar-2027 | 03-Mar-2027 (−3 d) | 03-Mar-2027 | 0 | ● On time, no float |

**The weekly report and the P6 update use different baselines for the discipline milestones.**

For civil works the weekly report's baseline is 21-Feb-2027, while the P6 baseline is 01-Oct-2026 and the P6 forecast is now 28-Nov-2026, 58 days after its own baseline and one week later than last week. Mechanical works slipped six days to 27-Dec-2026. Electrical and architectural works stay at 02-Feb-2027, 43 days after their P6 baseline of 21-Dec-2026. The contractual milestone for site levelling, local roads and parking (P6 baseline 12-Feb-2026) has still not started and is again forecast for the data date itself.

## Procurement of key materials

Share of materials delivered to site, by discipline. Source: weekly report summary, 03-Nov-2026.




**All 83 materials approved, ordered and on site**


The weekly report records 83 of 83 materials approved, 83 purchase orders placed and 83 materials delivered, with delivery completed on 13-Oct-2026. Its milestone sheet gives 27-Sep-2026 for the same event.

**Installation now under way**

Solar power plant installation has started this week, and the buried gate valve issue is closed (Risk & Issue log, 03-Nov-2026). The procurement tracker still shows a purchase-order status of "ISSUED" for only 20 of its 83 items.

## Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

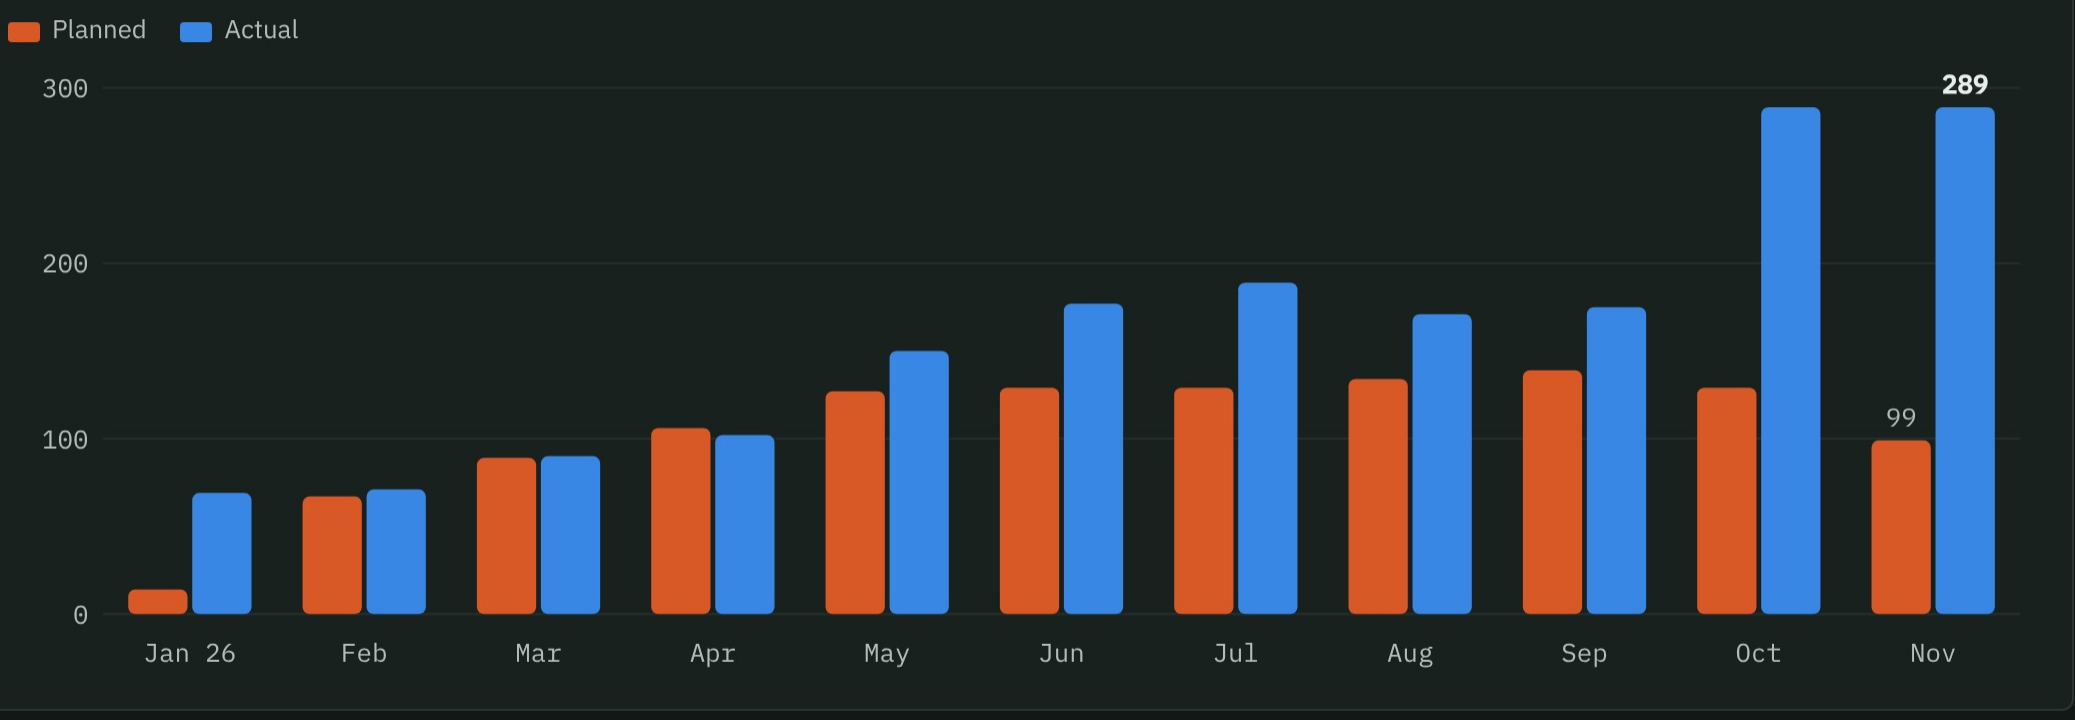


November head count is 289 against 99 planned: 267 labourers against 95 and 22 staff against 4, the same actual figures as October. Equipment on site: 20 against 4 planned.

## Cost and invoicing

### Contract value

| | |
|---|---|
| Original contract value | 95,996,525 |
| Revised contract value | 95,996,525 |
| Estimate at completion | 95,996,525 |
| Potential changes | 0 |
| Change orders | 0 |

All values in SAR. The change order log is empty.

### Invoices

| | |
|---|---|
| Invoices submitted | 7 |
| Gross value | 50,050,337 |
| Advance payment recovery (10%) | 5,005,034 |
| Net value | 45,045,303 |
| Invoices paid | 6 |
| Amount paid | 37,076,227 |

Invoicing is 52.1% of the contract value against 81.4% physical progress. Invoice 6 was paid on 29-Oct-2026. Invoice 7 (October, 8,854,529 gross) was submitted on 01-Nov-2026 and approved by the consultant the same day; it awaits PM approval.

## Health, safety and quality

### Safety Score 0.87

| | |
|---|---|
| Safe man-hours (cumulative) | 304,980 |
| Man-hours this week | 16,440 |
| Lost-time injuries | 0 |
| Fatalities | 0 |
| First-aid cases (cumulative) | 1 |
| Near misses (cumulative) | 1 |
| Property damage | 0 |
| Induction / toolbox sessions (cumulative) | 81 / 95 |

### Quality Score 0.93

| | |
|---|---|
| FIRs issued / closed / pending | 999 / 969 / 30 |
| MIRs issued / closed / pending | 95 / 87 / 8 |
| NCRs issued / closed / pending | 24 / 23 / 1 |
| Site instructions | 0 |
| Shop drawings approved | 158 of 158 |
| Material submittals approved | 83 of 83 |

Cumulative to 03-Nov-2026.

## Open issues and risks

| ISSUE | OWNER | DETAIL |
|---|---|---|
| Fire hose cabinets (high risk) | Contractor | Installation is under way; any slippage would delay fire-protection testing and inspection. |
| Blocks B4 and B5 | Contractor | B4 is 77.5% complete against 99.1% planned and B5 78.8% against 99.0%, about 21% and 20% behind. |
| Irrigation excavation (medium risk) | Contractor | Excavation for the HDPE irrigation pipes has still not started; the start and finish dates need to be confirmed. |
| Site levelling, local roads and parking | Contractor | The contractual milestone has not started and P6 keeps forecasting it for the data date. |
| Float at completion | Contractor | Zero float on project completion and all 100 active activities behind schedule. |
| Invoice 7 | MODON | Submitted on 01-Nov-2026 and approved by the consultant; awaiting PM approval. |

Other open low risks in the log: ceiling gypsum board, aluminium composite panels and the solar power plant, whose installation has started. Closed this week: the external platform (completed 03-Nov-2026), water-supply excavation (completed) and the buried gate valves. The log now has no open issues.

## Data notes

- The weekly report workbook (WPR #37, .xlsb) has no text version in MD Files, so its figures were read from the original workbook in All Files. This week's values are the change from WPR #36 (27-Oct-2026, in the W05 folder).
- The workbook's weekly columns do not match the change in its to-date figures: the report page gives 3,317 planned and 3,606 earned man-hours this week, while the to-date totals rose by 3,061 and 3,015. The to-date change is used here.
- The block rows add up to 99,461 earned man-hours against a construction total of 108,367; the gap of 8,906 is consistent with Block B6 being under-recorded (437 of 11,824 man-hours, against 95.5% planned), unchanged since last week.
- Testing and commissioning is still recorded at 40.6% earned against 13.6% planned, while the Testing sheet shows mechanical testing 8% complete and electrical and fire testing not started.
- The report page's headline plan and earned values and the Risk & Issue log are cost-based; the log labels this cost-based figure as actual progress. This report uses the physical (man-hour) figures only.
- The weekly report's general information gives a forecast completion of 06-Mar-2027 (no variance), while its milestone sheet and the P6 update give 03-Mar-2027. Its milestone baselines also differ from the P6 baseline (for example civil works 21-Feb-2027 against 01-Oct-2026).
- The November manpower and equipment actuals (22 staff, 267 labourers, 20 items of equipment) repeat October's figures. The safety sheet gives 16,440 man-hours this week, the same as last week, but only 13,700 for the month to date.
- Failed-start activities: this report gives 272 for last week, while last week's report gave 270.
- The P6 file's project code is still DAM3-02-3 with a planned start of 14-Mar-2023, and the procurement sheets carry project ID DAM-05-009. The invoice summary still shows 0 submitted invoices although seven are listed.
- The Risk & Issue log names Engr Hamdi as MODON PM; the weekly report names Engr. Affat Al-Enezi. Its dashboard shows 244 open risks and 128 open issues, against 5 open risks and no open issues in the logs.
- No P6 PDF layout was uploaded this week; P6 dates come from the XER file. The photos have no date or GPS stamp.

Compiled 04-Nov-2026 from weekly report WPR #37 (data date 03-Nov-2026), the P6 update and the Risk & Issue log uploaded for the week ending 05-Nov-2026, compared with WPR #36 (27-Oct-2026).
