Completion of Infrastructure Works, Second Industrial City in Makkah

استكمال شبكات البنية التحتية بالمدينة الصناعية الثانية بمكة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Engr. Abdallah Aljulaifi	15-Feb-2026	14-Aug-2027

Scope: road works, box culverts, open drain channels and dike walls, street lighting and low-voltage cables, and concrete ducts at road crossings. Contract value 52,025,516 SAR excluding VAT, 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 82.1% against 52.3% planned, the project is 29.8% ahead of plan. This week it gained 0.79% against 1.20% planned, below the weekly plan.

PHYSICAL % COMPLETE
82.1% / 52.3% plan
▲ SPI 1.57 +29.8%

PROGRESS THIS WEEK
+0.79% / +1.20% plan
▼ 0.41% below the weekly plan

CONTRACT TIME ELAPSED
47.9% · day 261 of 545
▼ Forecast finish 11-Sep-2027

INVOICED TO DATE (GROSS)
73.6% · 38.3M SAR
8 invoices, invoice 8 not yet approved by MODON; last period ends 26-Oct-2026

Well ahead of plan, but the forecast finish slipped to 28 days after the contract date.

The weekly report and the P6 update (UP 35, data date 03-Nov-2026) both forecast completion on 11-Sep-2027, 28 days after the contract completion date of 14-Aug-2027 and six days later than last week. Total float fell from −19 to −24 days. The negative float now runs through the pavement-marking procurement, the asphalt and finishing works on the connection to the 5th Ring Road, testing and commissioning, and close-out. Additional scope on Collector 9 and Road 52 is still open.

Site photos this week

Six photos from the Tracking Sheet presentation (file 11) of the 03-Nov-2026 weekly report, time-stamped 31-Oct and 01-Nov-2026 where a stamp is visible. The photos carry no GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.



Cutting works, Collector 9

Excavator loading a dump truck. Stamped 31-Oct-2026, 11:41.



Base course, Local Road 62

Paver working on the road base. Stamped 31-Oct-2026, 10:25.



Curbstone installation, Arterial Road 4

Curb line along the asphalt, with a concrete mixer. Stamped 31-Oct-2026, 10:53.



Interlock paving, Roundabout 5

Workers laying interlock on the sidewalk. Stamped 31-Oct-2026, 11:45.



Box culvert 5 apron

Concrete pour for the culvert apron. No time stamp.




Riprap protection, Open Channel 3A

Riprap and grouted lining on the channel slope. Stamped 01-Nov-2026, 12:00.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

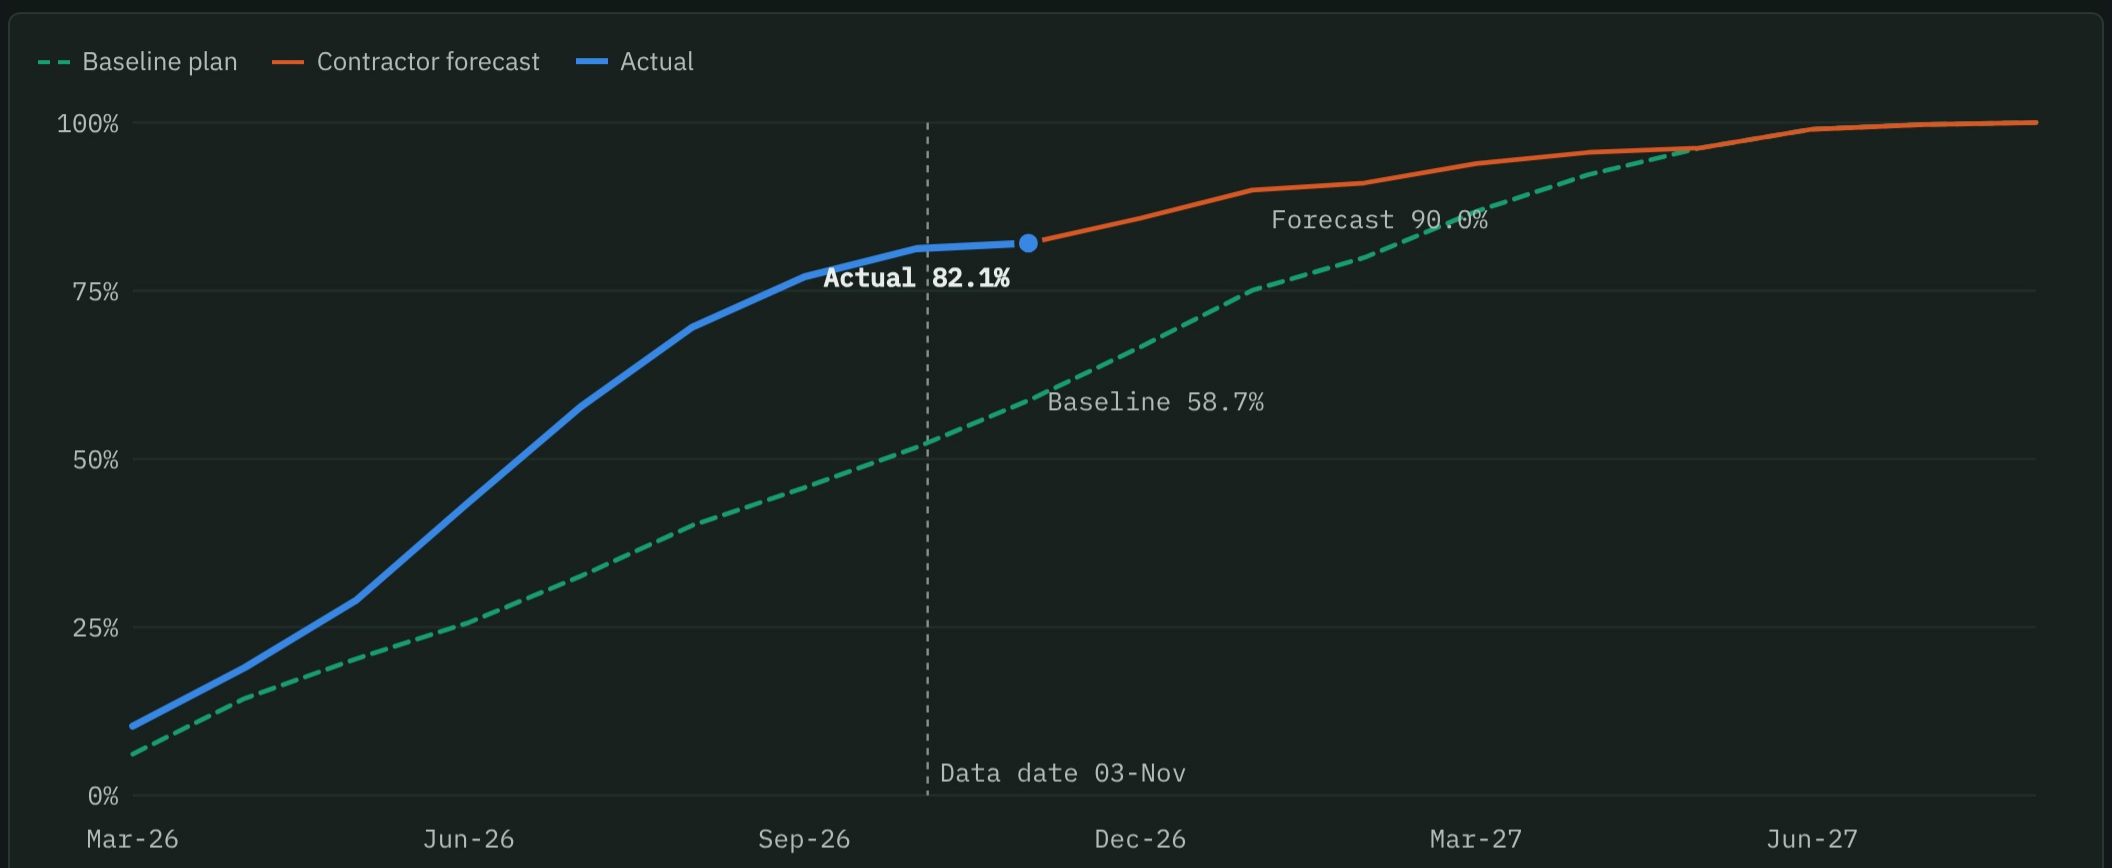

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	48.66	79.31	+30.65	—	1.63
20-Oct-2026	49.99	80.05	+30.06	+0.74	1.60
27-Oct-2026	51.12	81.28	+30.16	+1.23	1.59
03-Nov-2026	**52.32**	**82.08**	**+29.75**	**+0.79**	**1.57**

Physical % complete from the man-hour totals in the weekly reports of 20-Oct, 27-Oct and 03-Nov-2026; the 20-Oct report also gives the 13-Oct cumulative values. The revised plan in the source is identical to the baseline, so the orange line shows the contractor's forecast: actual to October, then the forecast from November.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	12.0%	100.0%	92.8%	−7.2%	0.93	▼ Behind
Road works	24.0%	52.1%	65.4%	+13.3%	1.26	▲ Ahead
Electrical works	8.3%	31.8%	71.8%	+39.9%	2.25	▲ Ahead
Demolition	1.3%	100.0%	67.6%	−32.4%	0.68	▼ Behind
Box culverts	3.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Open drain channels	37.6%	33.0%	96.6%	+63.6%	2.93	▲ Ahead
Testing & commissioning	3.0%	0.0%	21.1%	+21.1%	–	▲ Started early
Close-out & demobilisation	2.0%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**52.3%**	**82.1%**	**+29.8%**	**1.57**	▲ Ahead

The P6 update UP 35 (data date 03-Nov-2026) has 399 activities: 318 completed, 27 in progress and 54 not started. Its scheduled finish is 11-Sep-2027, 28 days after the contract date. There are 34 critical-path activities (42 last week). Testing of the electrical networks, started on 20-Oct-2026, is 75% complete in the Testing sheet.

Scope of work: quantities

Total, finished and remaining quantity for each network and major item. Network totals come from the Progress Summary sheet and item quantities from the Major Quantities sheet of the 03-Nov-2026 report. "This week" is this week's finished quantity minus the 27-Oct-2026 report's.

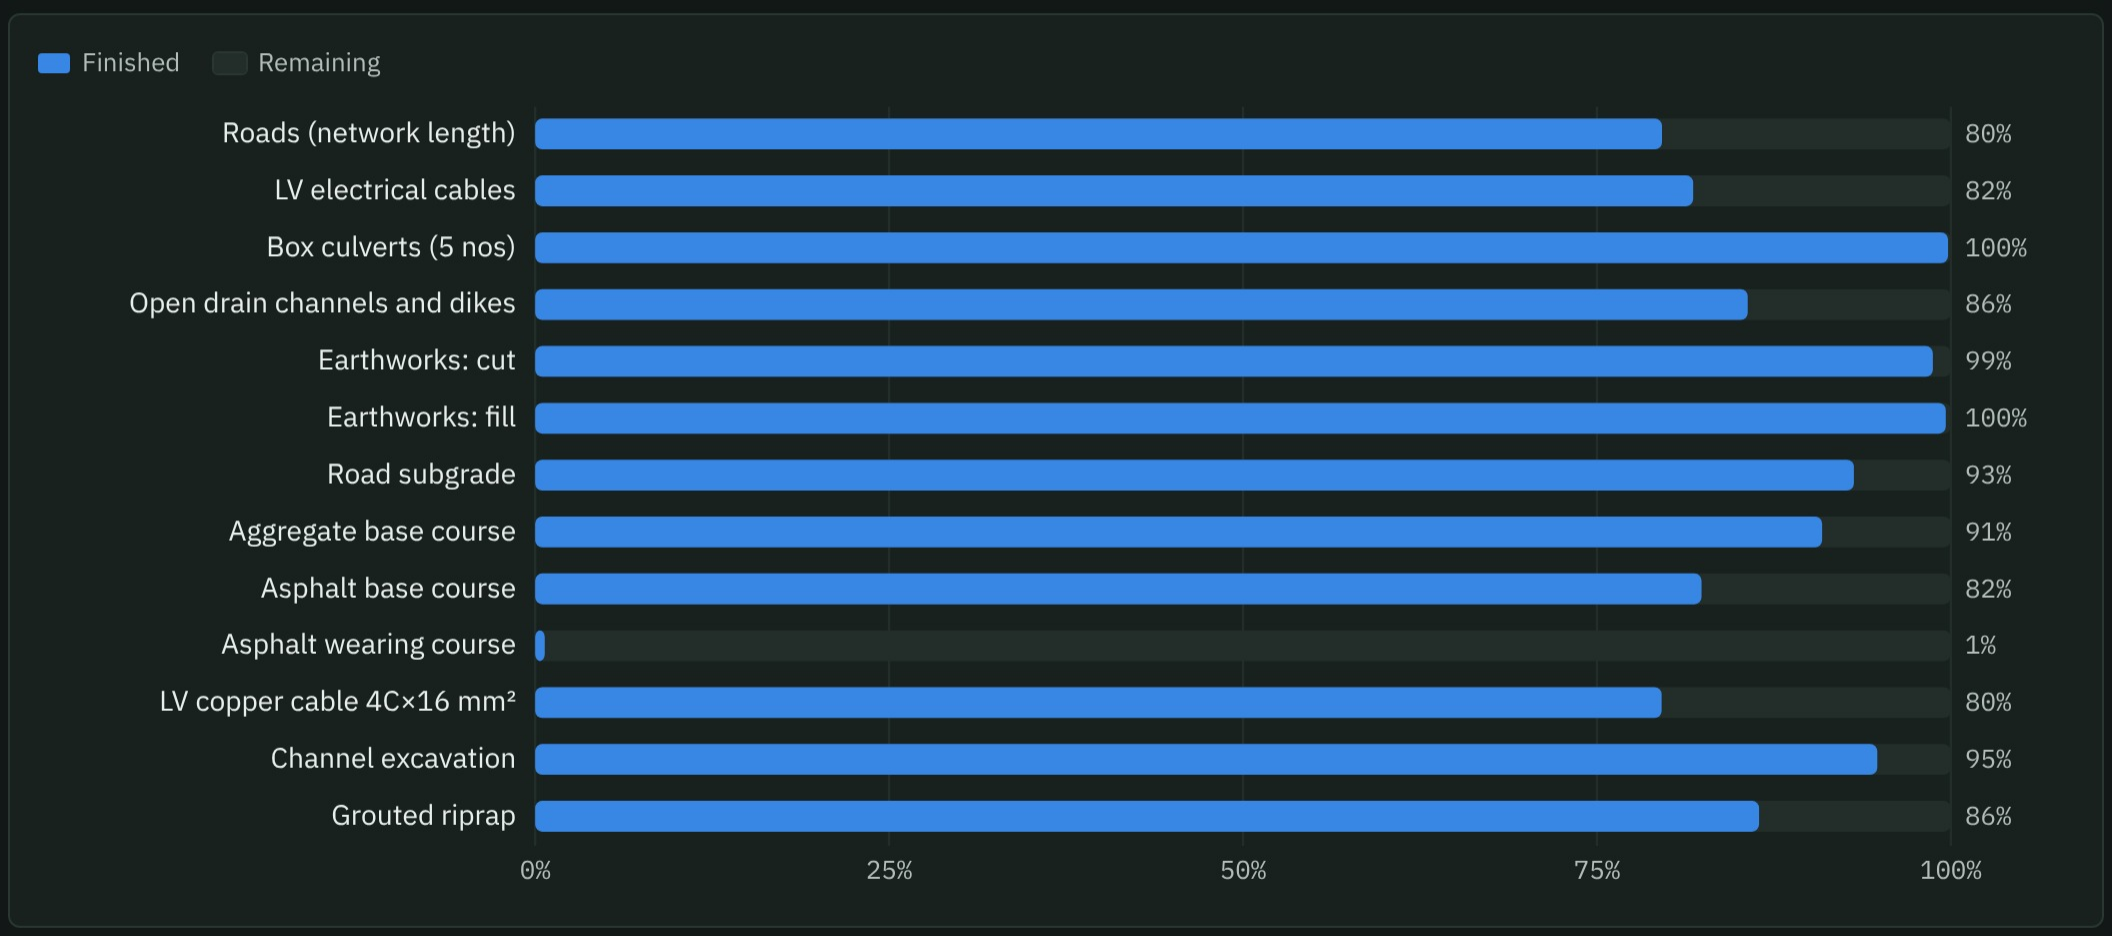

SCOPE ITEM	SOURCE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Roads (network length)	Progress Summary	LM	3,754	2,988	0	766	79.6%
LV electrical cables	Progress Summary	LM	8,464	6,923	0	1,541	81.8%

SCOPE ITEM	SOURCE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Box culverts (5 nos)	Progress Summary	%	100	99.8	0	0.2	99.8%
Open drain channels and dikes	Progress Summary	LM	3,921	3,358	0	562.6	85.6%
Earthworks: cut	B1.31 22 00.01	m³	537,044	530,209	+8,999	6,835	98.7%
Earthworks: fill	B1.31 22 00.02	m³	438,397	436,820	+443.7	1,577	99.6%
Road subgrade	B1.31 22 00.03	m³	37,334	34,776	+820.5	2,558	93.1%
Aggregate base course	B1.32 11 23.01	m³	24,889	22,626	+1,008	2,264	90.9%
Asphalt base course	B1.32 11 26.01	m³	11,676	9,619	0	2,056	82.4%
Asphalt wearing course	B1.32 12 16.01	m³	5,253	35.6	0	5,218	0.7%
LV copper cable 4C×16 mm²	B2.26 05 19.01	m	8,007	6,371	0	1,636	79.6%
Channel excavation	B6.31 22 00.04	m³	115,262	109,271	0	5,991	94.8%
Grouted riprap	B6.31 25 00.02	m²	49,594	42,875	0	6,719	86.5%

Box culverts and open channels

The five box culverts are 99.8% complete, and the apron of culvert 5 was poured this week. Open drain channels and dikes stay at 85.7% of their length and grouted riprap at 86.5%: neither moved in the Major Quantities sheet, although the FIR summary lists 999.9 m² of riprap grouting on Dike Wall 1.

Not yet started or barely started

The asphalt wearing course is still at 0.7% (35.6 of 5,253 m³), and the asphalt base course, LV copper cable and channel excavation did not move this week. The summary sheets list 611 m² of interlock paving on Arterial Road 4, but the report has no current total for interlock.

Milestones

Baseline and forecast dates from the weekly report's milestone sheet, with the forecast and float from the P6 update UP 35.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	15-Feb-2026	15-Feb-2026	15-Feb-2026 (actual)	–	✓ Done
Baseline programme approval	14-Mar-2026	01-Mar-2026	01-Mar-2026 (actual)	–	✓ Done
Completion of mobilisation	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Prequalification and material approval	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Long-lead materials delivered	16-Aug-2026	29-Aug-2026 (+13 d)	29-Aug-2026 (actual)	–	✓ Done
Completion of road works	14-Dec-2026	14-Jan-2027 (+31 d)	14-Jan-2027	42	▼ Later than baseline
Completion of open drain channels	14-Jun-2027	16-Jun-2027 (+2 d)	16-Jun-2027	14	▼ Later than baseline
Completion of all works	14-Aug-2027	11-Sep-2027 (+28 d)	11-Sep-2027	−24	▼ Late
Final handover	14-Aug-2027	11-Sep-2027 (+28 d)	11-Sep-2027	−24	▼ Late

The weekly report and the P6 update agree on every forecast date: the interim milestones recovered, but completion slipped again.

Completion of all works and final handover moved from 05-Sep to 11-Sep-2027, 28 calendar days after the contract date (P6 float −24 days). Road works moved forward from 18-Jan to 14-Jan-2027 (float 42 days), and the open drain channels from 06-Jul to 16-Jun-2027, two days after baseline (float 14 days).

Procurement of key materials

Share of the required quantity procured, per material. Source: Procurement Log, weekly report 03-Nov-2026.



Pavement markings: no purchase order


5,712 m² required, 0% procured. P6 UP 35 now starts material fabrication on 04-Nov-2026 and the first delivery on 02-Dec-2026, 199 days after baseline, and the procurement WBS carries −24 days of float.

Asphalt and kerbs still being supplied

Bituminous base and wearing course is 57% procured (9,655 of 16,929 m³) and precast kerbs 83% (18,155 of 21,915 m). The report shows 17 of 18 planned materials on site; the last road-works material is now due by 14-Nov-2026 instead of 10-Nov-2026.

Manpower

Monthly average head count on site, manual and non-manual combined, planned vs actual. Source: Manpower sheet.

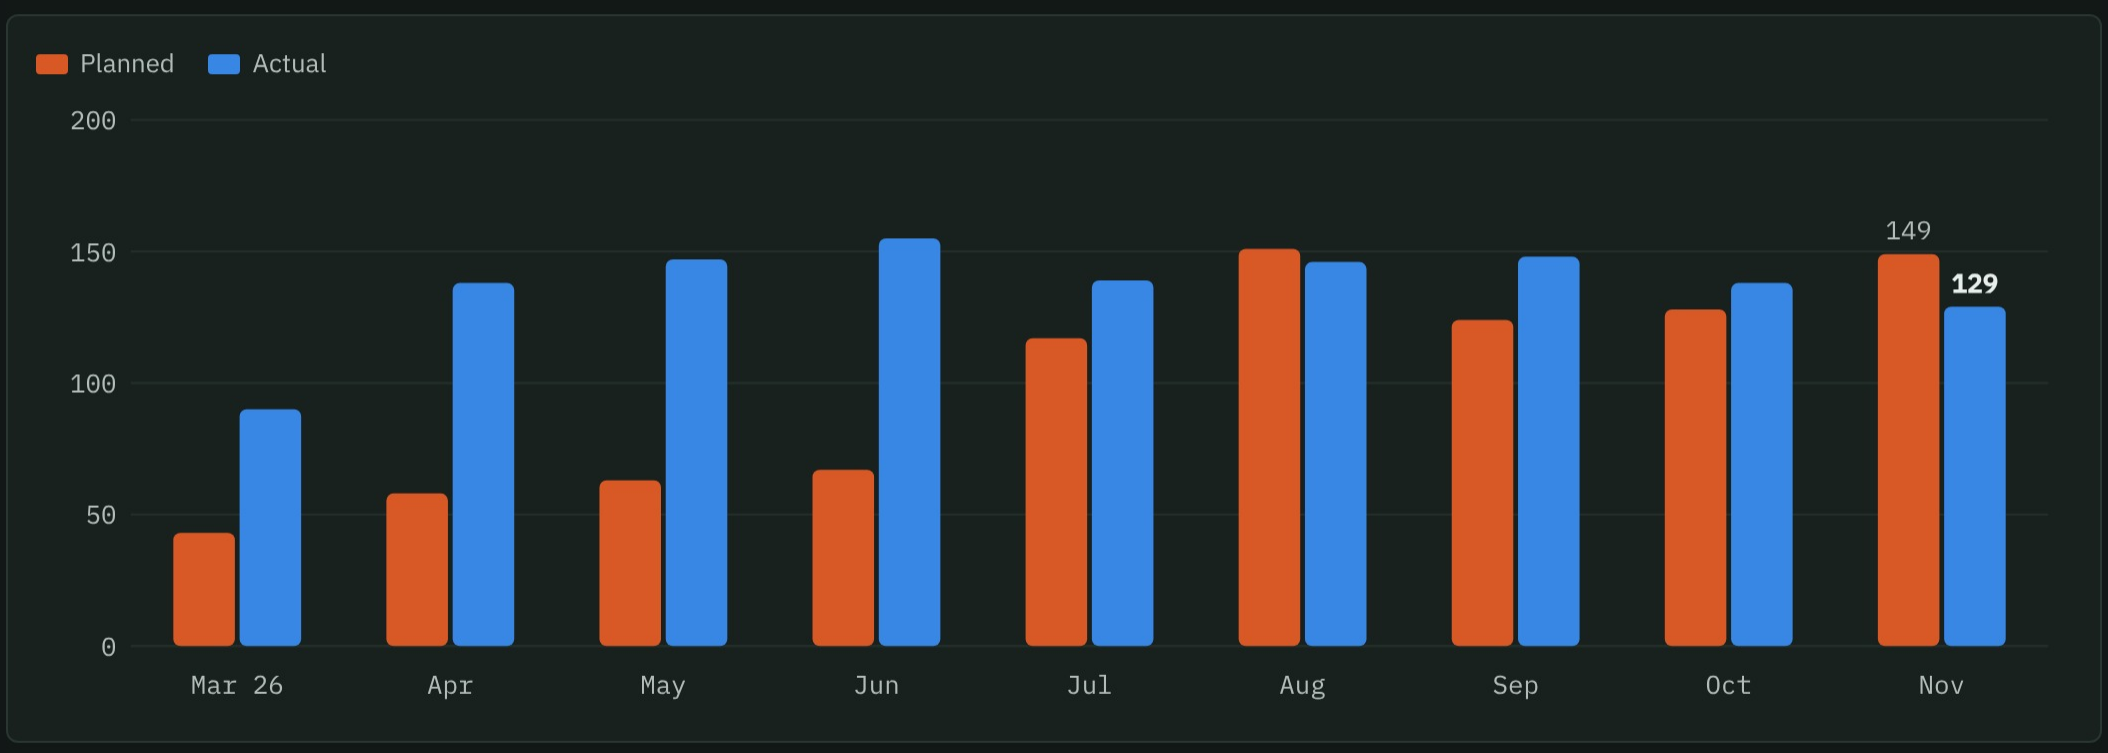

November so far averages 129 against 149 planned: 107 manual (137 planned) and 22 staff (12 planned), so manual labour is 30 below plan. October averaged 138 against 128. Equipment on site averages 63 units against 50 planned. The manual plan peaks at 161 in January 2027.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	52,025,516
Contract value incl. 15% VAT	59,829,343
Change orders	0
Potential changes	0
Estimate at completion	52,025,516
FIR value to date	41,515,115

All values in SAR. No change orders are registered.

Invoices

Invoices submitted	8
Gross value	38,305,734
Deductions and penalties	2,000
Net incl. VAT	44,053,595
Paid (7 invoices)	34,269,317
Invoice 8 awaiting MODON approval	9,784,277

Invoicing is 73.6% of the contract value against 82.1% physical progress. Invoice 8 (28-Sep to 26-Oct-2026, gross 8,508,067) was approved by the consultant on 27-Oct-2026 and awaits MODON approval and payment. No retention or advance payment is recorded.

Health, safety and quality

Safety Score 87.5%

Safe man-hours (cumulative)	205,780
Man-hours this week	4,560
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses (cumulative)	1
Property damage	0
Inductions / toolbox talks	12 / 53

Consultant HSE inspection, 03-Nov-2026. Average score to date 85.3%.

Quality Score 90.3%

FIRs issued / closed	972 / 949
FIRs pending	23
NCRs issued / closed	2 / 2
Site instructions issued / closed	25 / 25
MIRs issued / closed	31 / 31
Shop drawings approved / submitted	35 / 38
Material submittals approved / submitted	63 / 65

Cumulative to 03-Nov-2026. Consultant quality inspection score 90.31% this week; average to date 85.0%. FIRs rose by 19 this week, and 3 new shop drawings (2 road works, 1 electrical) are pending.

Open issues and risks

ISSUE	OWNER	DETAIL
Additional works, Collector 9	Contractor / MODON	Scope change adding works on Collector 9. Open in the risk register, target date 14-Nov-2026.
New Road 52	Contractor / MODON	Scope change to build Road 52, rated very high (score 25 after treatment). Open, target date 28-Dec-2026.
New Al Gloud Road	Contractor / MODON	Listed as a project challenge in the Progress Summary. The risk register shows it open; the risk log shows it closed, target date 01-Dec-2026.
Pavement markings	Contractor	No purchase order. The failed-start list shows material fabrication starting 04-Nov-2026 and the first delivery 02-Dec-2026, 199 days after baseline.
Milling of the existing asphalt	Contractor	Failed start: planned to start 23-Jun-2026, now 04-Nov-2026 (134 days late).
Connection to the 5th Ring Road	Contractor	Asphalt works started 08-Oct-2026 and are 35.0% complete by man-hours (3,792 of 10,830), with no progress this week; with the finishing works they carry −24 days of float.

The weekly report's issue log and top-five issues table are empty this week, and the risk log (file 17) is unchanged. Other register entries (design of Open Channel 3A, culvert 3, Hajj-period permits) are closed.

Data notes

- The two summary sheets (files 15 and 16) label a cost-based progress figure as "actual" and give a cost-based planned figure. This report uses physical % complete (man-hour weighted) only.
- Files 15 and 16 give this week's progress change with opposite signs (negative in file 15, positive in file 16).
- File 15 names the MODON PM as عبد الله الجليفي and file 16 as عبد الله الشنيفي. File 16 also gives project start 24-Nov-2025 and contract end 23-May-2026, against site handover 15-Feb-2026 and completion 14-Aug-2027 everywhere else.
- This week's quantities in the summary sheets (files 15 and 16) match the change in the Major Quantities sheet for cut (8,999 m³), subgrade (820 m³) and aggregate base course (1,008 m³), but give fill as 950 m³ against +443.7 m³. The report uses the Major Quantities change. The weekly table has no gain for 13-Oct-2026 because earlier reports were not used.
- The Tracking Sheet presentation (file 11) repeats last week's cost-based progress figures and gives no physical progress.
- The revised plan in the Physical-Chart Data sheet is identical to the baseline.
- The Major Quantities sheet has an older block of items at zero (subgrade 21,604 m³, base course 14,403 m³, kerbs 23,250 "m³", 15 kV cable 5,632 "m²", substation, RMU, 7 m lighting poles and others) next to the current items with progress. Only the current items are used.
- LV cable: the Major Quantities sheet gives 6,371 of 8,007 m installed; the Progress Summary gives 6,923 of 8,463.65 m.
- Luminaires are 264 in the Procurement sheet and 247 in the Progress Summary; earthing units 17 and 15. Procurement is 92.8% complete by man-hours although 17 of 18 materials are reported on site.
- The invoice summary shows 0 submitted invoices although 8 are logged, and a submitted value (44,051,595) 2,000 SAR below the consultant-approved value (44,053,595). The revised contract value and EAC cells also hold 21,100,000 and 20,900,000 next to 52,025,516.
- General Information dates baseline schedule approval 01-Mar-2025, before contract award; the milestone sheet and P6 give 01-Mar-2026. The FIR summary for 28-Oct to 03-Nov lists FIR-0960 dated 27-Oct-2026, before the period.
- Manual head count in November is 107 against 137 planned in the Manpower sheet, but the trade breakdown in the Weekly Progress Report sheet uses a plan of 105 (107 actual).
- The risk dashboard (file 17) shows 240 open risks and 133 open issues but zero in every category; the log lists 8 risks, 3 of them open. Culvert 4 and Al Gloud Road are open in the weekly report's risk register but closed in file 17.
- The P6 milestone table inside the Milestones sheet (for example mobilisation 02-Apr-2026) is out of date; milestone forecasts and float are taken from the P6 file UP 35.
- The weekly report measures the delay as 28 calendar days; P6 gives –24 days of float. In P6 the open-drain-channel milestone has 14 days of float but the Open Drain Channels WBS –2. The Testing sheet shows testing of the electrical networks at 75% since 20-Oct-2026, against a planned start of 08-May-2027, and testing and commissioning has 3,105 man-hours earned with none planned.

Compiled 04-Nov-2026 from the weekly report of 03-Nov-2026 (report no. 38) and its P6 update UP 35, with the 27-Oct-2026 report for this week's changes.
