Construction of Passenger Station for SAR Railway, Sudair Industrial City

محطة ركاب لسار في سدير

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Zyad Al Shabat	07-Apr-2026	06-Aug-2027

Scope: a passenger station for the SAR railway at Sudair Industrial City (platform, canopy, finishes and station electrical, CCTV and voice evacuation systems) with its access roads RD-01 and RD-02 and their storm water, sewer, potable water, street lighting, telecom and MV/LV networks.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 26-Oct-2026 the project is 27.3% complete against 40.0% planned, 12.7% behind (SPI 0.68). This week it gained 1.2% against 1.9% planned, so the gap widened by 0.7%.

PHYSICAL % COMPLETE
27.3% / 40.0% plan
▼ SPI 0.68 –12.7%

PROGRESS THIS WEEK
+1.2% / +1.9% plan
▼ 0.7% below the weekly plan

CONTRACT TIME ELAPSED
41.6% · day 202 of 486
▼ P6 finish 07-Aug-2027


INVOICED TO DATE (GROSS)
9.2% · 3.05M SAR
2 invoices, last period ends 30-Aug-2026

Procurement and the station works are holding the project back.

Procurement is 19.2% complete against 80.0% planned. The station package (platform, canopy and station systems) has not started: 0% against 9.4% planned, because the SAR fence permission and the client's canopy and platform design are still outstanding. Roads and utilities are closer to plan at 30.7% against 34.2%. To finish by 06-Aug-2027 the project needs about 1.8% a week for the remaining 40 weeks; this week it achieved 1.2%.

Site photos this week

Six photos from the Weekly Photos sheet of the 26-Oct-2026 weekly report. Road works on Road 1 dominate the week: bituminous base course, aggregate base course and subgrade. Select a photo to view it larger, then use the arrows to move between photos.

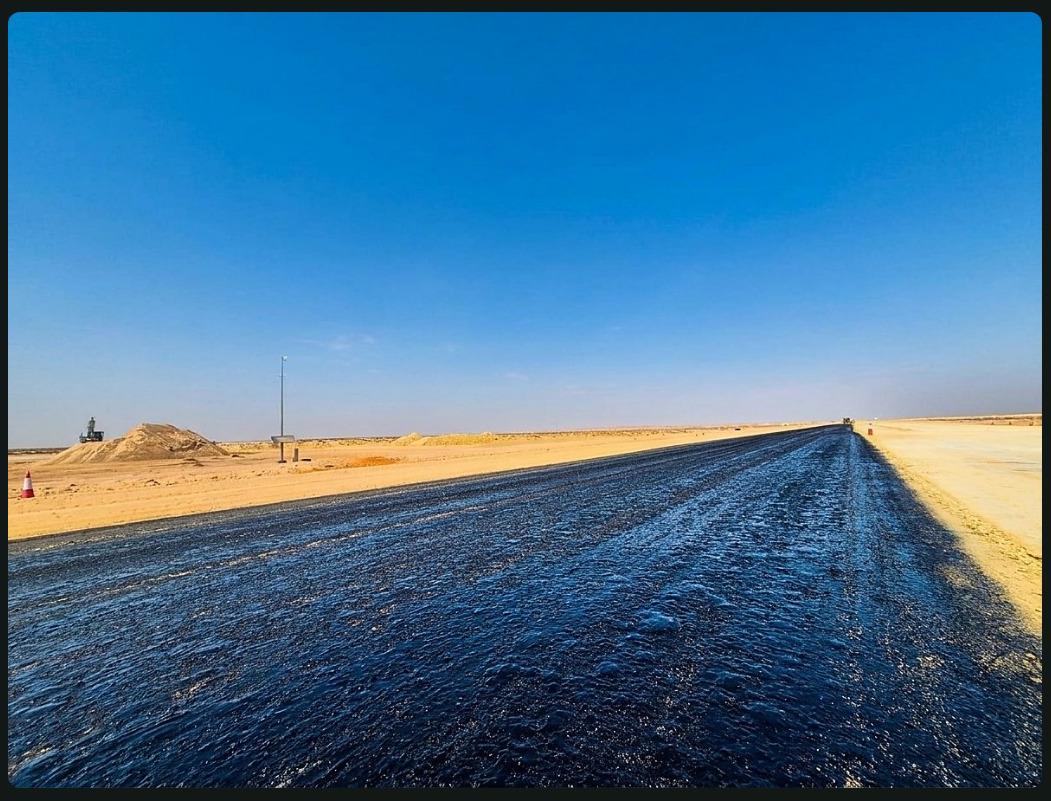

Bituminous base course, Road 1

Bituminous base course MC-01 on Road 1.



Bituminous layer, Road 1

The PDF captions this photo as backfilling for the roundabout at MC20 with Road 1.



Aggregate base course compaction

Road 1, St 1+500 to 1+850. Stamped 24-Oct-2026, 10:45.



Aggregate base course

Layer works on Road 1, St 1+500 to 1+850.



Subgrade grading, Road 1

Second subgrade layer, St 0+950 to 1+200, right side.



Parking area compaction

Fifth layer at the parking area on Road 1.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.



WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
19-Oct-2026	38.1	26.1	−12.0	–	0.69
26-Oct-2026	**40.0**	**27.3**	**−12.7**	**+1.2**	**0.68**

The 19-Oct-2026 row comes from the previous-week columns of this week's Progress sheet; no earlier weekly report has been uploaded. The S-curve has no revised plan, and its plan for 26-Oct-2026 is 38.4%, against 40.0% on the Progress sheet.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	103.3%	103.3%	0.0	1.00	✓ Complete
Engineering	5%	103.3%	98.2%	−5.2	0.95	▼ Behind
Procurement	14%	80.0%	19.2%	−60.9	0.24	▼ Far behind
Construction	75%	27.3%	22.1%	−5.2	0.81	▼ Behind
· Package 1: roads and utilities	54.2%	34.2%	30.7%	−3.6	0.90	▼ Behind
· Package 3: station (platform, canopy, systems)	20.8%	9.4%	0.0%	−9.4	0.00	▼ Not started
Testing & commissioning	2%	0.0%	0.0%	0.0	–	● Not yet due
Close-out	1%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**40.0%**	**27.3%**	**−12.7**	**0.68**	▼ Behind

The P6 update (data date 26-Oct-2026) has 855 activities: 247 completed, 51 in progress and 557 not started. Its scheduled finish is 07-Aug-2027, one day after the contract date, with −0.5 days of float on the finish milestones.

Scope of work: quantities

Major BOQ quantities from the Major Quantities sheet of the 26-Oct-2026 weekly report: total, finished to date and remaining. No earlier weekly report has been uploaded, so the this-week column is blank.

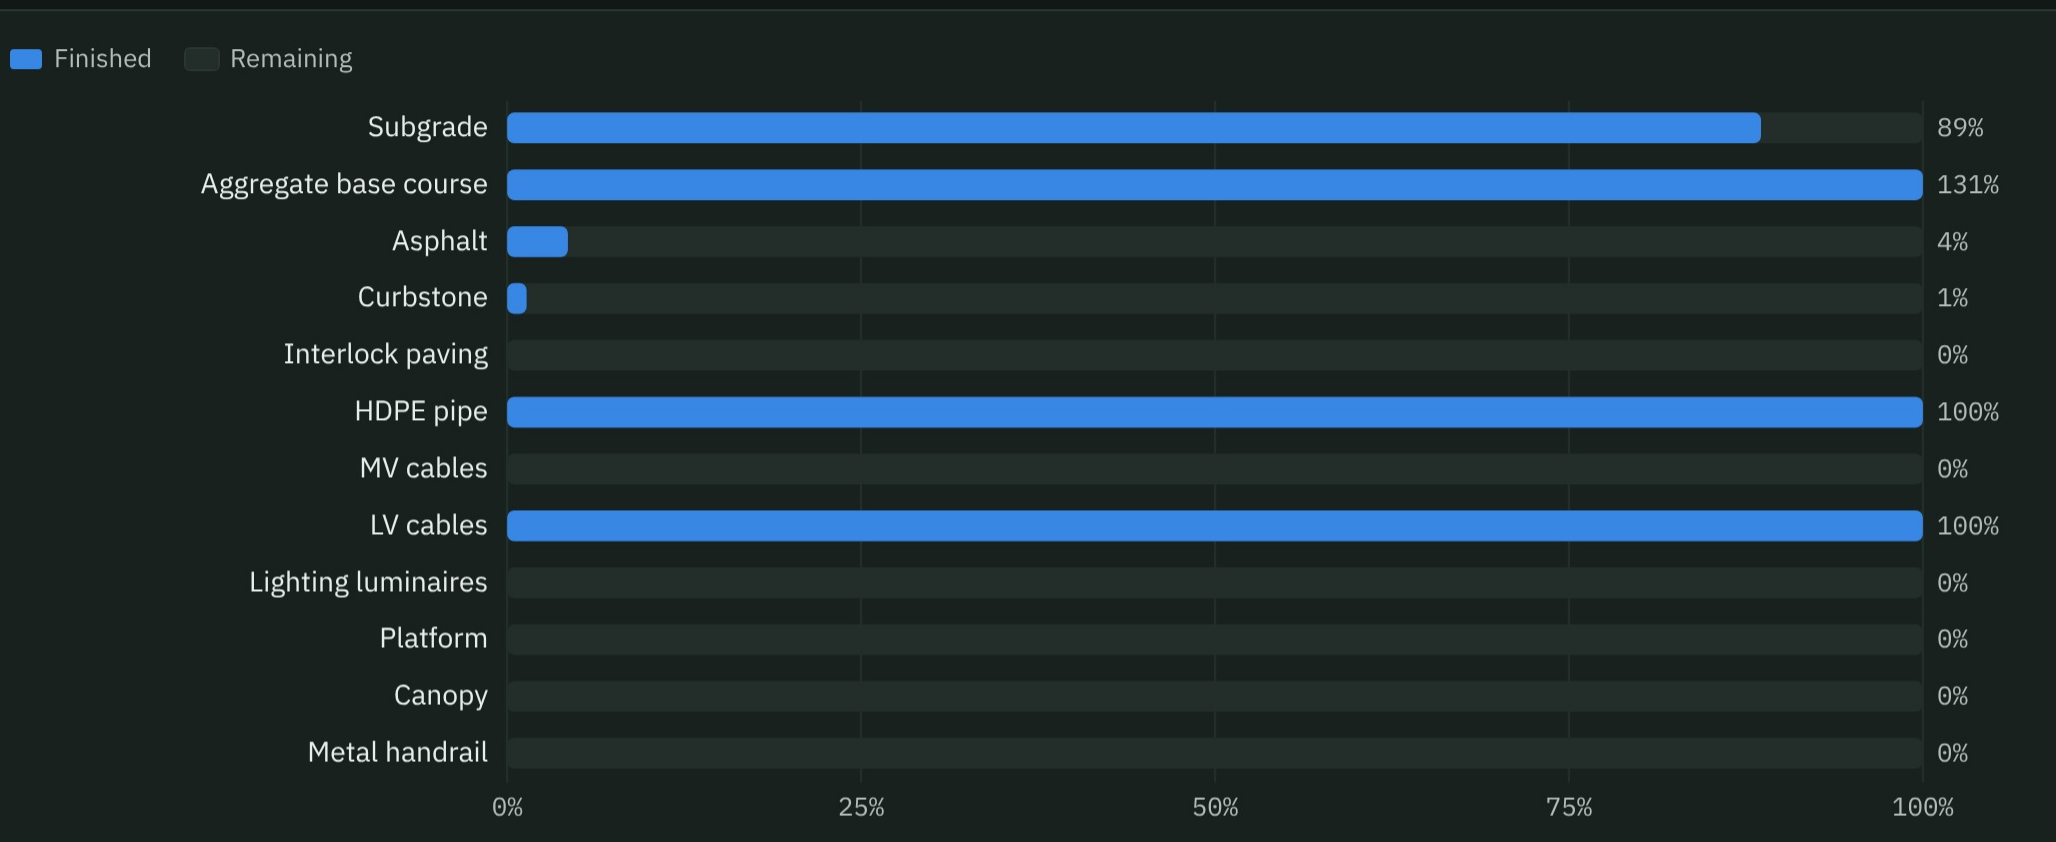

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Subgrade	B1.32 11 13.01	m³	20,530	18,182	–	2,348	88.6%
Aggregate base course	B1.32 11 23.01	m³	16,376	21,459	–	-5,083.2	131.0%
Asphalt	B1.32 12 16.01	m³	13,360	573	–	12,787	4.3%
Curbstone	B1.32 16 13.23.01	m²	20,555	282	–	20,273	1.4%
Interlock paving	B1.32 14 13.13.01	m²	27,900	0	–	27,900	0.0%
HDPE pipe	B4.33 31 23.01	LM	5,808	5,808	–	0	100.0%
MV cables	B2.31 23 00.01	LM	7,120	0	–	7,120	0.0%

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
LV cables	B2.33 71 00 02.01	LM	7,500	7,500	–	0	100.0%
Lighting luminaires	B2.26 56 19.01	EA	116	0	–	116	0.0%
Platform	03 00 00	m²	4,000	0	–	4,000	0.0%
Canopy	31 00 00	LM	4,000	0	–	4,000	0.0%
Metal handrail	B4.05 52 00.01	LM	440	0	–	440	0.0%

Station works not started

Platform (4,000 m²), canopy (4,000 m), metal handrail (440 m) and lighting luminaires (116) are all at 0%. The platform and canopy wait for the SAR fence permission and the client's design.

Figures to check

Aggregate base course is reported at 21,459 m³ against a total of 16,376 m³ (131%). HDPE pipe and LV cables are reported 100% finished, while the Progress sheet puts potable water at 28.3% and low voltage at 9.8% physical progress.

Milestones

The weekly report and the P6 schedule update give different forecasts for the interim milestones. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	07-Apr-2026	07-Apr-2026	07-Apr-2026 (actual)	–	✓ Done
Mobilisation finish	06-May-2026	06-May-2026	06-May-2026 (actual)	–	✓ Done
Work plan and baseline submission	06-May-2026	16-Aug-2026 (+102 d)	15-Aug-2026 (actual)	–	✓ Done late
Engineering phase finish	06-May-2026	21-Sep-2026 (+138 d)	27-Oct-2026	59	▼ Late
Road and paving works	06-Dec-2026	31-Dec-2026 (+25 d)	27-Jan-2027	0	▼ Late
Procurement phase finish	15-Apr-2027	09-Jun-2027 (+55 d)	16-Mar-2027	53	? Forecasts differ
MV works	12-May-2027	05-May-2027	26-May-2027	6	▼ At risk
Site and platform works	20-Jul-2027	05-Aug-2027 (+16 d)	17-Apr-2027	90	? Forecasts differ
Finishing and general site works	20-Jul-2027	06-Aug-2027 (+17 d)	06-Aug-2027	−0.5	▼ At risk
Project finish	06-Aug-2027	06-Aug-2027	07-Aug-2027	−0.5	▼ At risk

The weekly report and P6 disagree on the road, procurement and platform milestones.

The weekly report forecasts road and paving completion on 31-Dec-2026; P6 has it on 27-Jan-2027 with zero float. P6 completes site and platform works on 17-Apr-2027 with 90 days of float, although platform work has not started and is waiting for the SAR fence permission. Engineering finish was forecast for 21-Sep-2026 in the weekly report but is still open in P6.

Procurement of key materials

Share of the required quantity delivered, from the Completion Rate column. Source: Procurement sheet, weekly report 26-Oct-2026.



Eight long-lead items not yet submitted


Metal railing, canopy, MV duct banks, MV cables, substations, lighting poles, street-lighting luminaires and outdoor lighting fixtures are all marked "Not submitted". The required PO dates for the railing (25-Aug-2026), the MV duct banks and cables (12-Oct-2026) and the substations (19-Oct-2026) have passed.

Items with no delivery figure

Interlock, waterproofing, the LV distribution panel, street-lighting feeder panels, CCTV, voice evacuation, manhole covers and valves have no delivery figure yet. Lighting poles show a purchase order (PO 12725, 01-Jul-2026) but are still marked "Not submitted". The summary counts 22 of 27 purchase orders issued.

Manpower

Monthly head count on site, planned vs actual. Source: Manpower sheet.

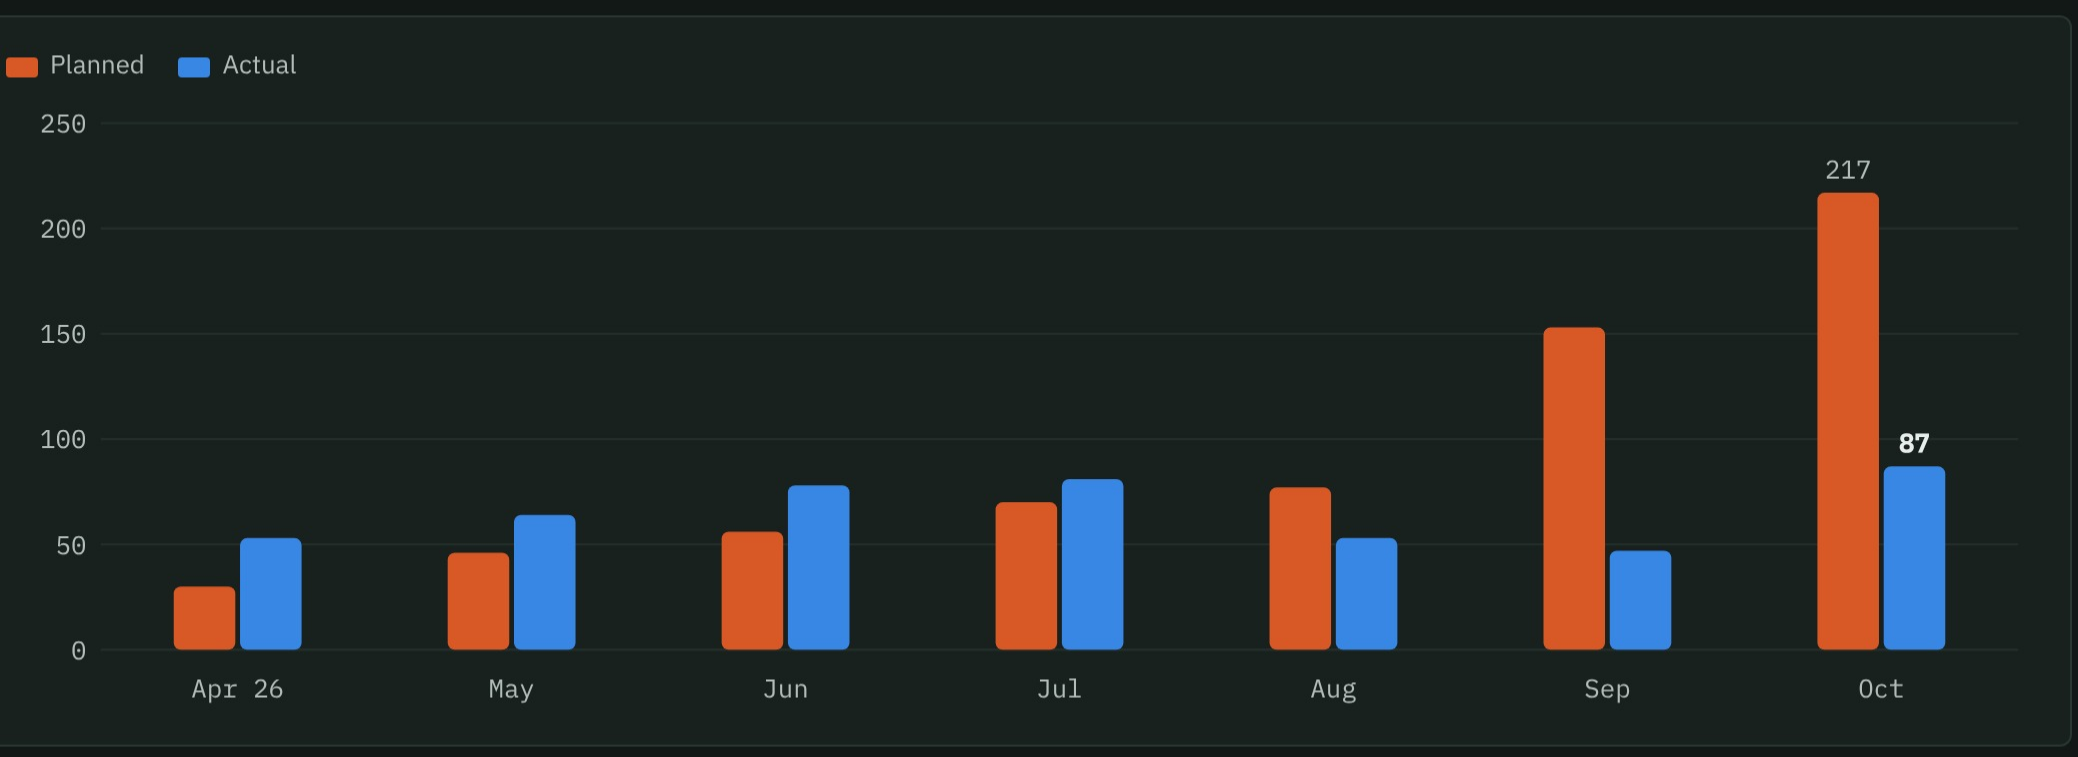

Manual and non-manual head count combined. October is 87 against 217 planned (−60%). The weekly summary panel gives 60 planned for October instead. The plan peaks at 263 in December 2026.

Cost and invoicing

Contract value

Original contract value	33,090,825
Change orders	0
Estimate at completion	33,090,825

All values in SAR. The change order log has no entries. The BOQ total on the Progress sheet is 33,090,852, 27 SAR more than the contract value.

Invoices

Invoices submitted	2
Gross value	3,048,399
VAT	457,260
Deductions and penalties	2,000
Net incl. VAT	3,503,659
PM-approved / paid	0 / 0

Invoicing is 9.2% of the contract value against 27.3% physical progress. Invoice 1 covers 07-Apr-2026 to 18-Jul-2026 and invoice 2 covers 19-Jul-2026 to 30-Aug-2026; neither is yet approved by the PM or paid.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	82,150
Man-hours this week	5,100
Man-hours this month	14,640
Internal trainings (cumulative)	23
Toolbox talks (cumulative)	21
HSE observations logged / open	17 / 0

Quality Score 0.89

FIRs issued / closed / pending	157 / 152 / 5
MIRs issued / closed	15 / 15
NCRs issued / closed	4 / 4
Site instructions	0
Shop drawings submitted (of 204)	179
Material submittals (of 45)	45

Shop drawings: 122 approved (A) and 57 approved as noted (B). Material submittals: 1 A, 41 B and 3 C.

Open issues and risks

ISSUE	OWNER	DETAIL
SAR fence permission	MODON / SAR	Permission to work inside the platform area is still pending, so the platform and canopy works cannot start. Rated very high (5 × 5) in the risk register, open since 16-Sep-2026.
Canopy and platform design	MODON (client)	The client has not yet issued the canopy and platform design, so the related shop drawings, procurement and construction cannot be finalised. Rated very high (5 × 5); value 9,867,379 SAR.
MV duct crossings	MODON (client)	Client approval of the proposed MV duct crossings is pending, and MV cable installation depends on it. Rated high (4 × 4).
Long-lead procurement	Contractor	Eight long-lead items are not yet submitted for approval, several past their required PO dates. Procurement is at 19.2% against 80.0% planned.

The issue log lists 17 HSE observations from 02-Sep-2026 to 25-Oct-2026, all closed. Two older risks, the SAR permit for the geotechnical report and the platform tender drawing, are marked closed.

Data notes

- No earlier weekly report has been uploaded for this project (W01 to W03 are empty), so the this-week quantity column shows "–". This week's physical progress and the 19-Oct-2026 values come from the weekly and previous-week columns of the 26-Oct-2026 Progress sheet.
- The cover sheet's headline "Earn Value" and its SPI are cost-based (BOQ value), not physical progress, and are not used in this report.

- Planned progress at 26-Oct-2026 is 40.0% on the Progress sheet but 38.4% on the Physical-Chart Data sheet. That sheet's percentage column for April and May (4.24% and 8.17%) does not match its own man-hours, so the S-curve uses man-hours divided by the 638,468 man-hour budget.

- Mobilisation shows 19,793 man-hours planned and earned against a budget of 19,154, and Engineering 32,988 planned against 31,923, both 103.3%.
- Weekly planned man-hours for Road Works 1 (17,222) do not equal the sum of Road-01 and Road-02 (2,412), and Low Voltage Road-02 shows −11,285 planned this week.
- Major Quantities: aggregate base course is 21,459 m³ against a total of 16,376 m³, and HDPE pipe and LV cables are 100% finished, out of line with the Progress sheet. The asphalt total is 13,360 m³ there but 3,420 m³ on the Procurement sheet; curbstone is in m² there and in m on the Procurement sheet.
- The Procurement sheet gives kerbstone a completion rate of 1.4 (140%).
- Manpower: the October plan is 217 in the monthly histogram but 60 in the weekly summary panel.

- The cover sheet gives "Revised Completion" as 07-Apr-2026, the site handover date. The MV works milestone has a baseline of 22-May-2027 on the cover sheet and 12-May-2027 on the Milestones sheet.
- P6 finishes the project on 07-Aug-2027 with −0.5 days of float, one day after the contract date; the weekly report forecasts 06-Aug-2027 with no variance.
- The HSE inspection sheet and the FIR summary carry project ID SUD1-02-011, and the Conclusion sheet describes a different project (Sudair infrastructure networks, Phase 2 Part 2). The FIR summary total is 3,646,339 SAR at the top and 3,923,633 SAR at the bottom.
- The risk register describes the project as ahead of schedule, which the physical progress figures do not support. Risks 3120-4 and 3120-5 are marked Open in one column and Close in another.
- Photo 2 is captioned "Bituminous base course MC-01 at Road 1" in the workbook and "backfilling for roundabout at MC20 with road 1" in the PDF.

Compiled 01-Nov-2026 from the weekly report (data date 26-Oct-2026) and the P6 update uploaded for week 29.
