
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026		162	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Feb-27	10,521,555.88	8,404,268.87	12,347,192.88	85.21%	68.07%	-47
MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	0%	0%	5
GENERAL MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	0%	0%	5
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	15-Dec-26	0.00	0.00	0.00	77.03%	77%	5
CONTRACUAL MILESTONES		0	28-Oct-26	28-Oct-26	19-Nov-26	19-Nov-26	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26		19-Nov-26	0.00	0.00	0.00	100%	0%	0
QASSIM		138	25-Jun-26	14-Dec-26	30-Jul-26 A	13-Feb-27	4,886,049.95	3,933,621.50	5,800,661.64	84.23%	67.81%	-21
ENGINEERING		37	25-Jun-26	27-Jul-26	30-Jul-26 A	10-Nov-26	0.00	0.00	0.00	0%	0%	-60
SHOP DRAWINGS SUBMITTALS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	08-Nov-26	0.00	0.00	0.00	0%	0%	-68
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	08-Nov-26	0.00	0.00	0.00	0%	0%	-68
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	08-Nov-26	0.00	0.00	0.00	0%	0%	-68
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	08-Nov-26	0.00	0.00	0.00	100%	90%	-68
SHOP DRAWINGS APPROVALS		10	16-Jul-26	27-Jul-26	20-Aug-26 A	10-Nov-26	0.00	0.00	0.00	0%	0%	-60
MECHANICAL DRAWINGS		10	16-Jul-26	27-Jul-26	20-Aug-26 A	10-Nov-26	0.00	0.00	0.00	0%	0%	-60
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	10-Nov-26	0.00	0.00	0.00	0%	0%	-60
PG-Q-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	16-Jul-26	27-Jul-26	20-Aug-26 A	10-Nov-26	0.00	0.00	0.00	100%	80%	-60
PROCUREMENT		92	25-Jun-26	27-Aug-26	14-Aug-26 A	12-Nov-26	2,532,361.21	2,103,969.02	2,532,361.21	100%	83.08%	-22
LONG LEAD ITEMS		85	07-Jul-26	27-Aug-26	14-Aug-26 A	12-Nov-26	2,378,642.27	1,965,621.98	2,378,642.27	100%	82.64%	-32
DELIVERY TO SITE		85	07-Jul-26	27-Aug-26	14-Aug-26 A	12-Nov-26	2,378,642.27	1,965,621.98	2,378,642.27	100%	82.64%	-32
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	08-Nov-26	14,428.69	12,985.82	14,428.69	100%	90%	-58
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	08-Nov-26	14,428.69	12,985.82	14,428.69	100%	90%	-58
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	12-Nov-26	2,119,264.56	1,731,502.01	2,119,264.56	100%	81.7%	-41
PG-Q-PR-LL-SP-DL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	07-Nov-26	26,778.60	25,439.67	26,778.60	100%	95%	-57
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	07-Nov-26	46,985.40	44,636.13	46,985.40	100%	95%	-57
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	07-Nov-26	10,152.00	9,644.40	10,152.00	100%	95%	-57
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	07-Nov-26	156,686.40	148,852.08	156,686.40	100%	95%	-57
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	29-Oct-26 A	12-Nov-26	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	-3
METAL WORK		15	25-Jul-26	10-Aug-26	05-Oct-26 A	09-Nov-26	3,427.65	2,742.12	3,427.65	100%	80%	-16
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26	10-Aug-26	05-Oct-26 A	09-Nov-26	3,427.65	2,742.12	3,427.65	100%	80%	-16
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	07-Nov-26	20,455.88	19,433.08	20,455.88	100%	95%	-58
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	07-Nov-26	20,455.88	19,433.08	20,455.88	100%	95%	-58
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	08-Nov-26	221,065.50	198,958.95	221,065.50	100%	90%	-48
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	07-Nov-26	1,785.24	1,606.72	1,785.24	100%	90%	-62
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	08-Nov-26	3,124.17	2,811.75	3,124.17	100%	90%	-58
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	08-Nov-26	182,755.44	164,479.90	182,755.44	100%	90%	-58
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	08-Nov-26	8,081.83	7,273.65	8,081.83	100%	90%	-58
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	08-Nov-26	6,326.40	5,693.76	6,326.40	100%	90%	-47
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	08-Nov-26	6,170.09	5,553.08	6,170.09	100%	90%	-47
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	08-Nov-26	7,811.37	7,030.23	7,811.37	100%	90%	-47
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	08-Nov-26	5,010.96	4,509.86	5,010.96	100%	90%	-47
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	08-Nov-26	153,718.94	138,347.04	153,718.94	100%	90%	-58
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	08-Nov-26	153,718.94	138,347.04	153,718.94	100%	90%	-58
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Nov-26	78,553.04	70,697.74	78,553.04	100%	90%	-49
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Nov-26	1,892.27	1,703.04	1,892.27	100%	90%	-49
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Nov-26	714.10	642.69	714.10	100%	90%	-49
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Nov-26	34,366.68	30,930.01	34,366.68	100%	90%	-49
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Nov-26	41,580.00	37,422.00	41,580.00	100%	90%	-49
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	1,724.00	1,551.60	1,724.00	100%	90%	-25
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	1,302.70	1,172.43	1,302.70	100%	90%	-25
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	112.75	101.48	112.75	100%	90%	-25
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	308.56	277.70	308.56	100%	90%	-25
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	08-Nov-26	71,118.65	64,006.78	71,118.65	100%	90%	-60
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	08-Nov-26	7,186.00	6,467.40	7,186.00	100%	90%	-60
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	08-Nov-26	63,932.65	57,539.39	63,932.65	100%	90%	-55
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26 A	08-Nov-26	2,200.61	1,980.55	2,200.61	100%	90%	-23
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26 A	08-Nov-26	2,200.61	1,980.55	2,200.61	100%	90%	-23
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	122.63	110.37	122.63	100%	90%	-25
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Nov-26	122.63	110.37	122.63	100%	90%	-25
CONSTRUCTION STAGE		121	05-Jul-26	14-Dec-26	06-Aug-26 A	19-Jan-27	2,353,688.74	1,407,874.64	2,619,411.44	89.86%	53.75%	-3
PLAYGROUND AND LANDSCAPING WORKS		121	05-Jul-26	14-Dec-26	06-Aug-26 A	16-Dec-26	1,143,293.41	1,127,246.60	1,409,016.12	81.14%	80%	26
PLAYGROUND WORKS		103	11-Aug-26	02-Dec-26	06-Aug-26 A	29-Nov-26	285,033.05	270,892.26	325,784.34	87.49%	83.15%	-1
FOOTBALL PLAYGROUND WORKS		72	19-Aug-26	17-Nov-26	14-Aug-26 A	19-Nov-26	85,345.29	87,473.03	109,254.66	78.12%	80.06%	-6
PG-Q-CON-EXFB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	08-Nov-26	24,360.00	21,924.00	24,360.00	100%	90%	-55
PG-Q-CON-EXFB-90	Turfing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	10-Nov-26	23,667.00	18,933.60	23,667.00	100%	80%	-64
PG-Q-CON-EXFB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	14-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-51
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	17-Nov-26	1,817.79	1,648.13	2,060.16	88.24%	80%	-53
PG-Q-CON-EXFB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	25-Oct-26 A	19-Nov-26	0.00	16,566.90	23,667.00	0%	70%	-15
BASKETBALL PLAYGROUND WORKS		70	31-Aug-26	17-Nov-26	20-Aug-26 A	23-Nov-26	42,342.32	34,560.58	43,200.72	98.01%	80%	-13
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	10-Nov-26	13,091.76	10,473.41	13,091.76	100%	80%	-55
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	15-Nov-26	15,472.08	12,377.66	15,472.08	100%	80%	-56
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	18-Nov-26	13,091.76	10,473.41	13,091.76	100%	80%	-24
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	27-Sep-26 A	23-Nov-26	686.72	1,236.10	1,545.12	44.44%	80%	-31
PADEL PLAYGROUND WORKS		93	11-Aug-26	02-Dec-26	06-Aug-26 A	29-Nov-26	157,345.44	148,858.66	173,328.96	90.78%	85.88%	-1

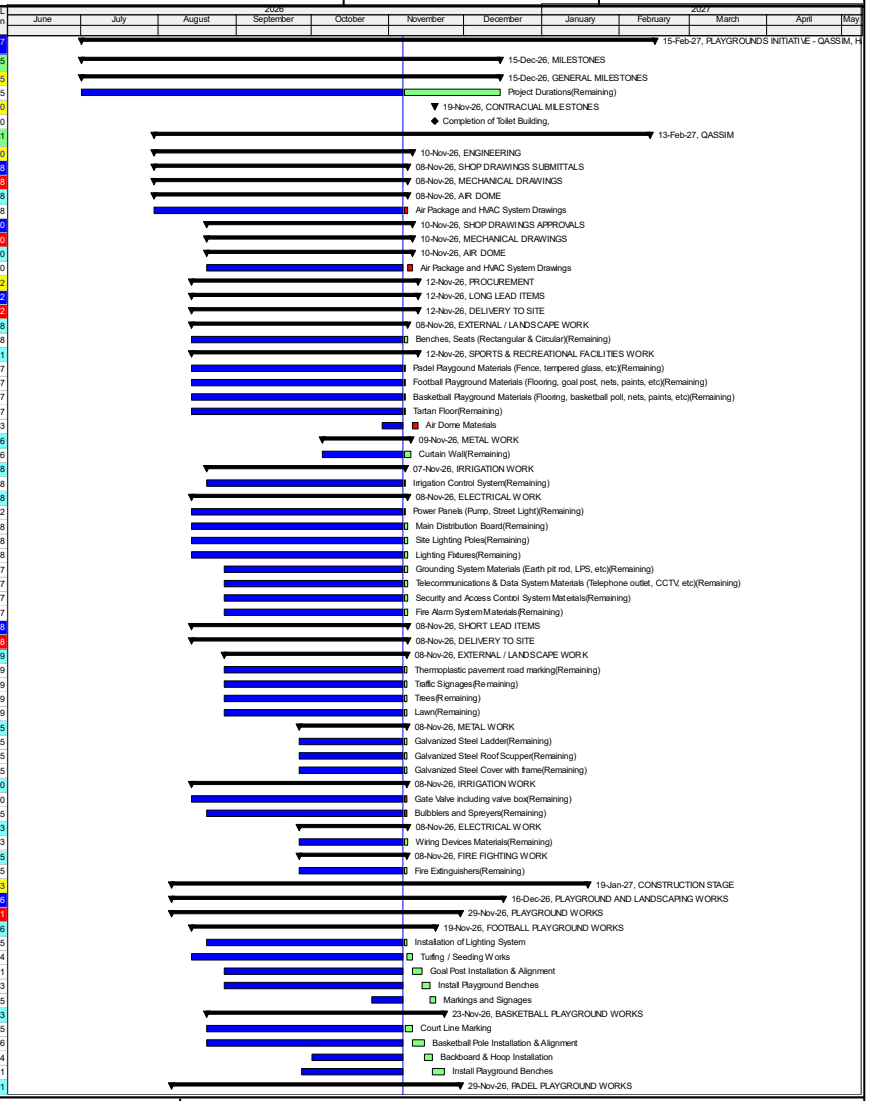


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EX-PD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	11-Nov-26	3,534.96	2,827.97	3,534.96	100%	80%	-52
PG-Q-CON-EX-PD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	15-Nov-26	5,302.44	4,241.95	5,302.44	100%	80%	-58
PG-Q-CON-EX-PD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	12-Oct-26 A	18-Nov-26	5,302.44	4,241.95	5,302.44	100%	80%	-16
PG-Q-CON-EX-PD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	18-Nov-26	130,572.00	117,514.80	130,572.00	100%	90%	-73
PG-Q-CON-EX-PD-70	Court Accessories Installation	15	29-Oct-26	15-Nov-26	22-Oct-26 A	24-Nov-26	12,633.60	18,950.40	27,072.00	46.67%	70%	-13
PG-Q-CON-EX-PD-80	Install Playground Benches	15	16-Nov-26	02-Dec-26	25-Oct-26 A	29-Nov-26	0.00	1,081.58	1,545.12	0%	70%	-16
GENERAL SITE WORKS		119	05-Jul-26	28-Nov-26	14-Aug-26 A	16-Dec-26	642,396.60	527,053.10	653,316.48	98.33%	80.67%	19
MECHANICAL WORK		85	05-Jul-26	16-Aug-26	20-Aug-26 A	01-Dec-26	348,762.60	284,634.78	348,762.60	100%	81.61%	-50
STORM WATER AND UTILITY WORK		85	05-Jul-26	16-Aug-26	20-Aug-26 A	01-Dec-26	21,060.00	13,381.20	21,060.00	100%	63.54%	-50
PG-Q-CON-EX-GN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	07-Nov-26	4,128.00	3,715.20	4,128.00	100%	90%	-61
PG-Q-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	08-Nov-26	10,740.00	9,666.00	10,740.00	100%	90%	-61
PG-Q-CON-EX-GN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	08-Nov-26	16-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	16-Nov-26	23-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	24-Nov-26	01-Dec-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-26	09-Aug-26	20-Aug-26 A	24-Nov-26	327,702.60	271,253.58	327,702.60	100%	82.77%	-75
PG-Q-CON-EX-GN-M-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	23-Nov-26	90,915.00	81,823.50	90,915.00	100%	90%	-78
PG-Q-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	24-Nov-26	236,787.60	189,430.08	236,787.60	100%	80%	-72
ELECTRICAL WORK		65	29-Aug-26	01-Nov-26	20-Aug-26 A	16-Dec-26	287,842.08	230,273.66	287,842.08	100%	80%	-45
POWER, LIGHTING & GROUNDING		30	29-Aug-26	20-Sep-26	20-Aug-26 A	08-Dec-26	230,771.88	184,617.50	230,771.88	100%	80%	-73
PG-Q-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	03-Dec-26	8,265.00	6,612.00	8,265.00	100%	80%	-81
PG-Q-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	01-Sep-26	02-Sep-26	13-Oct-26 A	05-Dec-26	4,586.70	3,669.36	4,586.70	100%	80%	-43
PG-Q-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	03-Sep-26	08-Sep-26	14-Oct-26 A	06-Dec-26	17,397.90	13,918.32	17,397.90	100%	80%	-40
PG-Q-CON-EX-GN-E-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	06-Dec-26	174,052.80	139,242.24	174,052.80	100%	80%	-89
PG-Q-CON-EX-GN-E-70	Wiring Works	3	13-Sep-26	15-Sep-26	10-Oct-26 A	07-Dec-26	4,224.00	3,379.20	4,224.00	100%	80%	-47
PG-Q-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-26	20-Sep-26	12-Oct-26 A	08-Dec-26	22,245.48	17,796.38	22,245.48	100%	80%	-45
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-26	20-Oct-26	07-Oct-26 A	14-Dec-26	43,146.00	34,516.80	43,146.00	100%	80%	-33
PG-Q-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	21-Sep-26	24-Sep-26	07-Oct-26 A	08-Dec-26	619.80	495.84	619.80	100%	80%	-51
PG-Q-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-26	28-Sep-26	10-Oct-26 A	09-Dec-26	619.80	495.84	619.80	100%	80%	-49
PG-Q-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	29-Sep-26	03-Oct-26	10-Oct-26 A	10-Dec-26	3,718.80	2,975.04	3,718.80	100%	80%	-49
PG-Q-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26	07-Oct-26	12-Oct-26 A	10-Dec-26	15,249.12	12,199.30	15,249.12	100%	80%	-48
PG-Q-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26	12-Oct-26	11-Oct-26 A	12-Dec-26	1,446.48	1,157.18	1,446.48	100%	80%	-50
PG-Q-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26	17-Oct-26	13-Oct-26 A	13-Dec-26	6,612.00	5,289.60	6,612.00	100%	80%	-49
PG-Q-CON-EX-GN-E-150	IP Camera Installation	3	18-Oct-26	20-Oct-26	14-Oct-26 A	14-Dec-26	14,880.00	11,904.00	14,880.00	100%	80%	-49
FIRE ALARM SYSTEM		32	26-Sep-26	01-Nov-26	11-Oct-26 A	16-Dec-26	13,924.20	11,139.36	13,924.20	100%	80%	-25
PG-Q-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	26-Sep-26	04-Oct-26	11-Oct-26 A	10-Dec-26	1,983.60	1,586.88	1,983.60	100%	80%	-44
PG-Q-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26	13-Oct-26	12-Oct-26 A	12-Dec-26	2,644.80	2,115.84	2,644.80	100%	80%	-45
PG-Q-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26	22-Oct-26	13-Oct-26 A	14-Dec-26	8,097.60	6,478.08	8,097.60	100%	80%	-46
PG-Q-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	24-Oct-26	01-Nov-26	15-Oct-26 A	16-Dec-26	1,198.20	958.56	1,198.20	100%	80%	-45
PARKING WORK		5	04-Nov-26	09-Nov-26	27-Oct-26 A	16-Dec-26	5,791.92	10,135.86	14,479.80	40%	70%	-38
PG-Q-CON-EX-GN-PR-30	Marking & Signages	5	04-Nov-26	09-Nov-26	27-Oct-26 A	16-Dec-26	5,791.92	10,135.86	14,479.80	40%	70%	-38
SERVICE CONNECTION		8	19-Nov-26	28-Nov-26	14-Aug-26 A	16-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-98
PG-Q-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26	28-Nov-26	14-Aug-26 A	16-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-98
LANDSCAPING WORKS		58	30-Sep-26	14-Dec-26	20-Aug-26 A	24-Nov-26	215,863.76	329,301.24	429,915.30	50.21%	76.6%	-16
HARDSCAPE WORK		58	30-Sep-26	14-Dec-26	20-Aug-26 A	24-Nov-26	55,440.00	103,253.04	123,489.30	44.89%	83.61%	-16
PG-Q-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26	14-Oct-26	27-Aug-26 A	08-Nov-26	55,440.00	49,896.00	55,440.00	100%	90%	-48
PG-Q-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26	02-Dec-26	20-Aug-26 A	19-Nov-26	0.00	50,109.84	62,637.30	0%	80%	-67
PG-Q-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-26	14-Dec-26	12-Oct-26 A	24-Nov-26	0.00	3,247.20	5,412.00	0%	60%	-27
SOFTSCAPE WORK		31	15-Oct-26	21-Nov-26	27-Aug-26 A	17-Nov-26	160,423.76	226,048.20	306,426.00	52.35%	73.77%	-37
PG-Q-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	11-Nov-26	115,500.00	92,400.00	115,500.00	100%	80%	-49
PG-Q-CON-EX-LS-SS-10	Planting Trees	17	02-Nov-26	21-Nov-26	25-Oct-26 A	17-Nov-26	44,923.76	133,648.20	190,926.00	23.53%	70%	-3
AIR DOME CONSTRUCTION		76	17-Aug-26	04-Nov-26	27-Aug-26 A	19-Jan-27	1,168,945.34	250,488.29	1,168,945.34	100%	21.43%	-56
CIVIL WORK		18	22-Aug-26	10-Sep-26	10-Nov-26	01-Dec-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EX-AD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	10-Nov-26	22-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EX-AD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	22-Nov-26	01-Dec-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		8	27-Oct-26	04-Nov-26	27-Aug-26 A	19-Jan-27	250,488.29	125,244.14	250,488.29	100%	50%	-116
PG-Q-CON-EX-AD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	19-Jan-27	250,488.29	125,244.14	250,488.29	100%	50%	-116
ELECTRICAL WORK		61	17-Aug-26	13-Sep-26	27-Aug-26 A	25-Nov-26	417,480.48	125,244.14	417,480.48	100%	30%	-53
PG-Q-CON-EX-AD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	11-Nov-26	208,740.24	125,244.14	208,740.24	100%	60%	-53
PG-Q-CON-EX-AD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	11-Nov-26	25-Nov-26	208,740.24	0.00	208,740.24	100%	0%	0
TOILET BUILDING WORKS		39	20-Aug-26	20-Oct-26	27-Aug-26 A	11-Nov-26	41,449.98	30,139.75	41,449.98	100%	72.71%	-12
CIVIL WORK		28	08-Oct-26	19-Oct-26	27-Aug-26 A	11-Nov-26	30,403.20	22,407.00	30,403.20	100%	73.7%	-54
ARCHITECTURAL WORK		28	08-Oct-26	19-Oct-26	27-Aug-26 A	11-Nov-26	30,403.20	22,407.00	30,403.20	100%	73.7%	-54
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	11-Nov-26	20,825.40	16,660.32	20,825.40	100%	80%	-54
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	10-Nov-26	13,273.80	10,619.04	13,273.80	100%	80%	-58
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	11-Nov-26	7,551.60	6,041.28	7,551.60	100%	80%	-40
ROOF FINISHES		1	19-Oct-26	19-Oct-26	14-Oct-26 A	11-Nov-26	9,577.80	5,746.68	9,577.80	100%	60%	-23
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26	19-Oct-26	14-Oct-26 A	11-Nov-26	9,577.80	5,746.68	9,577.80	100%	60%	-23
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	11-Nov-26	11,046.78	7,732.75	11,046.78	100%	70%	17
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	11-Nov-26	11,046.78	7,732.75	11,046.78	100%	70%	17
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	11-Nov-26	136.26	95.38	136.26	100%	70%	-34
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	11-Nov-26	136.26	95.38	136.26	100%	70%	-34
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	09-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-31
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	09-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-31

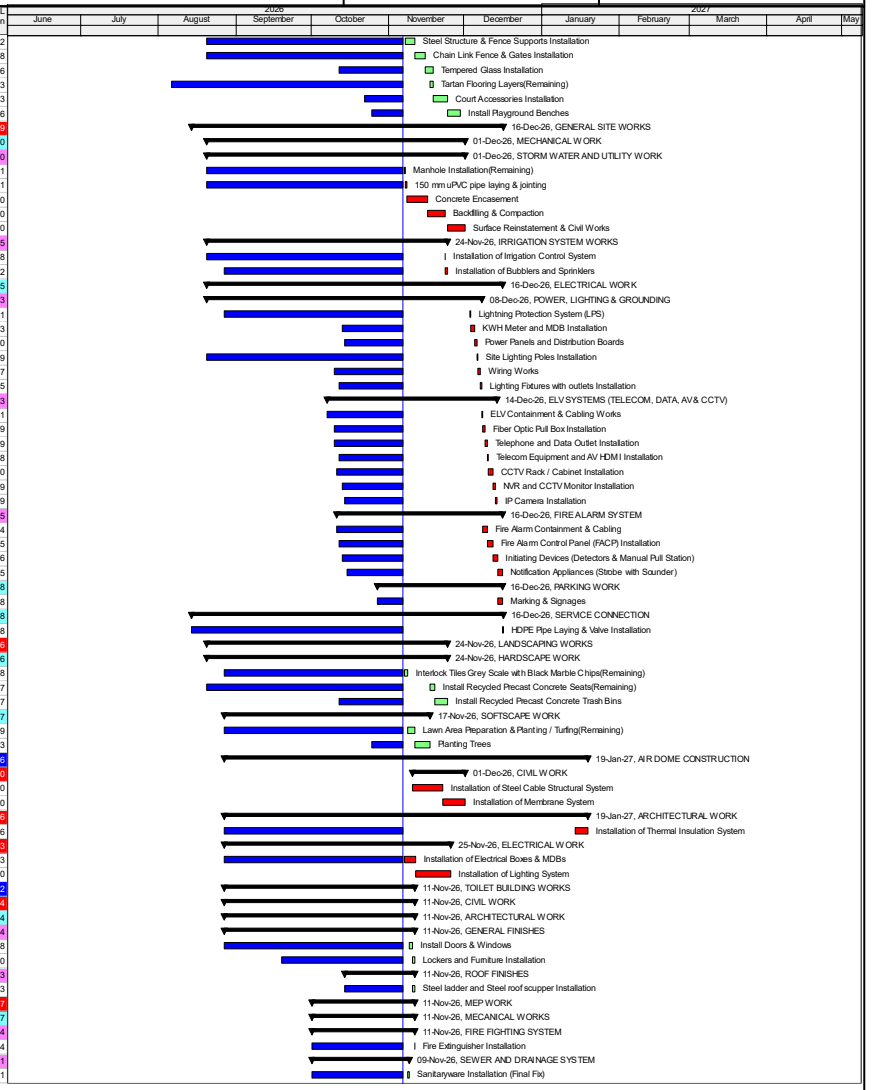


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	07-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-29
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	01-Oct-26 A	07-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-29
PROJECT CLOSOUT		18	16-Nov-26	02-Dec-26	29-Oct-26 A	13-Feb-27	0.00	421,777.84	648,888.98	0%	65%	-76
PG-Q-PCL-20	As-Built Drawings	15	16-Nov-26	02-Dec-26	29-Oct-26 A	13-Feb-27	0.00	113,994.01	175,375.40	0%	65%	-76
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	16-Nov-26	26-Nov-26	29-Oct-26 A	10-Feb-27	0.00	307,783.83	473,513.58	0%	65%	-80
HAIL		130	25-Jun-26	03-Dec-26	09-Jul-26 A	27-Dec-26	1,989,033.90	1,747,403.38	2,354,607.43	84.47%	74.21%	-7
PROCUREMENT		48	04-Jul-26	26-Aug-26	20-Aug-26 A	09-Nov-26	233,418.94	209,665.73	233,418.94	100%	89.82%	-21
LONG LEAD ITEMS		48	25-Jul-26	26-Aug-26	20-Aug-26 A	09-Nov-26	177,157.99	159,030.87	177,157.99	100%	89.77%	-39
DELIVERY TO SITE		48	25-Jul-26	26-Aug-26	20-Aug-26 A	09-Nov-26	177,157.99	159,030.87	177,157.99	100%	89.77%	-39
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	09-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-50
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	09-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-50
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	08-Nov-26	173,044.81	155,740.33	173,044.81	100%	90%	-43
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	07-Nov-26	3,124.17	2,811.75	3,124.17	100%	90%	-53
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	07-Nov-26	2,499.34	2,249.40	2,499.34	100%	90%	-53
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	07-Nov-26	6,326.40	5,693.76	6,326.40	100%	90%	-53
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	08-Nov-26	134,020.66	120,618.59	134,020.66	100%	90%	-55
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	08-Nov-26	8,081.83	7,273.65	8,081.83	100%	90%	-55
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV	12	13-Aug-26	26-Aug-26	27-Aug-26 A	08-Nov-26	6,170.09	5,553.08	6,170.09	100%	90%	-49
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	08-Nov-26	7,811.37	7,030.23	7,811.37	100%	90%	-49
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	08-Nov-26	5,010.96	4,509.86	5,010.96	100%	90%	-49
SHORT LEAD ITEMS		12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-49
DELIVERY TO SITE		12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-49
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	56,260.95	50,634.86	56,260.95	100%	90%	-49
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	1,249.67	1,124.70	1,249.67	100%	90%	-49
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	30,441.29	27,397.16	30,441.29	100%	90%	-49
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	08-Nov-26	24,570.00	22,113.00	24,570.00	100%	90%	-49
CONSTRUCTION STAGE		130	25-Jun-26	26-Nov-26	09-Jul-26 A	27-Dec-26	1,682,016.72	1,373,845.27	1,732,753.32	97.07%	79.29%	-13
PLAYGROUND AND LANDSCAPING WORKS		127	25-Jun-26	26-Nov-26	09-Jul-26 A	27-Dec-26	1,533,104.10	1,268,538.16	1,583,840.70	96.8%	80.09%	-13
PLAYGROUND WORKS		71	18-Aug-26	17-Nov-26	06-Aug-26 A	26-Nov-26	457,017.90	407,112.42	480,684.90	95.08%	84.69%	-18
FOOTBALL PLAYGROUND WORKS		71	18-Aug-26	17-Nov-26	06-Aug-26 A	26-Nov-26	457,017.90	407,112.42	480,684.90	95.08%	84.69%	-18
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	09-Nov-26	48,720.00	38,976.00	48,720.00	100%	80%	-50
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	11-Nov-26	23,667.00	18,933.60	23,667.00	100%	80%	-64
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	11-Nov-26	343,980.00	309,582.00	343,980.00	100%	90%	-68
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	15-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-61
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	18-Nov-26	5,150.40	4,120.32	5,150.40	100%	80%	-56
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	02-Nov-26 A	26-Nov-26	0.00	7,100.10	23,667.00	0%	30%	-12
GENERAL SITE WORKS		127	25-Jun-26	26-Nov-26	14-Aug-26 A	27-Dec-26	691,917.54	535,506.98	693,963.54	99.71%	77.17%	18
MECHANICAL WORK		84	25-Jun-26	06-Aug-26	14-Aug-26 A	23-Nov-26	344,669.34	282,172.04	344,669.34	100%	81.87%	-48
STORM WATER AND UTILITY WORK		84	25-Jun-26	04-Aug-26	14-Aug-26 A	22-Nov-26	23,124.00	14,164.80	23,124.00	100%	61.26%	-50
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	07-Nov-26	1,032.00	928.80	1,032.00	100%	90%	-62
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	08-Nov-26	5,160.00	4,644.00	5,160.00	100%	90%	-57
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	13-Oct-26 A	09-Nov-26	10,740.00	8,592.00	10,740.00	100%	80%	-19
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	09-Nov-26	12-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	12-Nov-26	16-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	17-Nov-26	22-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		46	21-Jul-26	30-Jul-26	14-Aug-26 A	17-Nov-26	321,227.40	267,816.48	321,227.40	100%	83.37%	-72
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	16-Nov-26	108,345.60	97,511.04	108,345.60	100%	90%	-76
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	16-Nov-26	90,915.00	72,732.00	90,915.00	100%	80%	-67
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	10-Oct-26 A	17-Nov-26	121,966.80	97,573.44	121,966.80	100%	80%	-31
FIRE PROTECTION SYSTEM		2	05-Aug-26	06-Aug-26	11-Oct-26 A	23-Nov-26	317.94	190.76	317.94	100%	60%	-35
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26	06-Aug-26	11-Oct-26 A	23-Nov-26	317.94	190.76	317.94	100%	60%	-35
ELECTRICAL WORK		55	17-Aug-26	20-Oct-26	10-Oct-26 A	12-Dec-26	241,428.00	168,999.60	241,428.00	100%	70%	0
POWER, LIGHTING & GROUNDING		20	17-Aug-26	08-Sep-26	10-Oct-26 A	30-Nov-26	184,357.80	129,050.46	184,357.80	100%	70%	-24
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26	19-Aug-26	10-Oct-26 A	24-Nov-26	8,265.00	5,785.50	8,265.00	100%	70%	-36
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26	22-Aug-26	11-Oct-26 A	24-Nov-26	4,586.70	3,210.69	4,586.70	100%	70%	-37
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26	27-Aug-26	11-Oct-26 A	26-Nov-26	17,397.90	12,178.53	17,397.90	100%	70%	-35
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26	31-Aug-26	12-Oct-26 A	28-Nov-26	127,638.72	89,347.10	127,638.72	100%	70%	-37
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26	03-Sep-26	10-Oct-26 A	29-Nov-26	4,224.00	2,956.80	4,224.00	100%	70%	-40
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26	08-Sep-26	13-Oct-26 A	30-Nov-26	22,245.48	15,571.84	22,245.48	100%	70%	-37
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26	08-Oct-26	10-Oct-26 A	08-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-27
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26	12-Sep-26	11-Oct-26 A	01-Dec-26	619.80	433.86	619.80	100%	70%	-41
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26	15-Sep-26	12-Oct-26 A	02-Dec-26	619.80	433.86	619.80	100%	70%	-41
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26	20-Sep-26	12-Oct-26 A	03-Dec-26	3,718.80	2,603.16	3,718.80	100%	70%	-41
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26	26-Sep-26	13-Oct-26 A	05-Dec-26	15,249.12	10,674.38	15,249.12	100%	70%	-42
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26	30-Sep-26	10-Oct-26 A	06-Dec-26	1,446.48	1,012.54	1,446.48	100%	70%	-46
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26	05-Oct-26	10-Oct-26 A	07-Dec-26	6,612.00	4,628.40	6,612.00	100%	70%	-47
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26	08-Oct-26	10-Oct-26 A	08-Dec-26	14,880.00	10,416.00	14,880.00	100%	70%	-49
FIRE ALARM SYSTEM		32	13-Sep-26	20-Oct-26	10-Oct-26 A	12-Dec-26	13,924.20	9,746.94	13,924.20	100%	70%	-23
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26	21-Sep-26	10-Oct-26 A	03-Dec-26	1,983.60	1,388.52	1,983.60	100%	70%	-40
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26	01-Oct-26	10-Oct-26 A	06-Dec-26	2,644.80	1,851.36	2,644.80	100%	70%	-42
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26	11-Oct-26	10-Oct-26 A	09-Dec-26	8,097.60	5,668.32	8,097.60	100%	70%	-44
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26	20-Oct-26	10-Oct-26 A	12-Dec-26	1,198.20	838.74	1,198.20	100%	70%	-47
PARKING WORK		11	10-Oct-26	20-Oct-26	20-Aug-26 A	12-Dec-26	104,146.20	81,545.34	104,146.20	100%	78.3%	-87

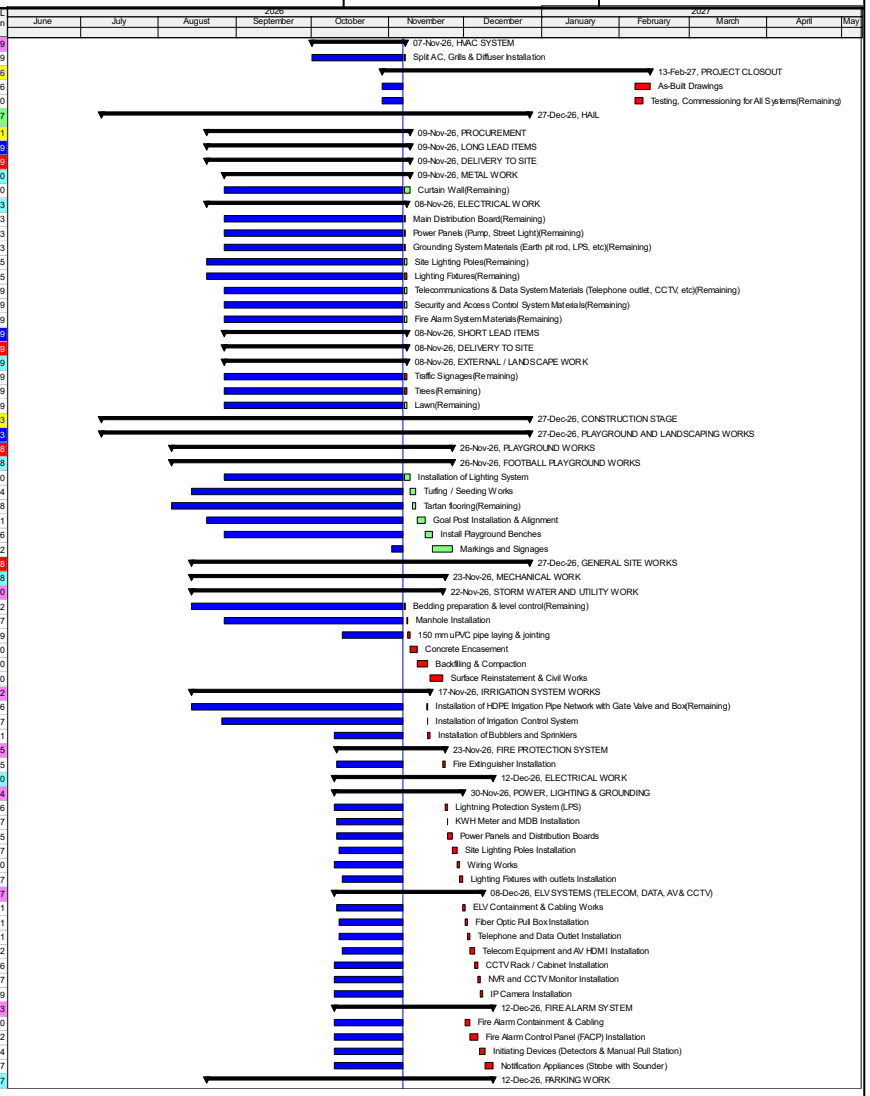


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	09-Dec-26	86,430.00	69,144.00	86,430.00	100%	80%	-90
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26	20-Oct-26	27-Oct-26 A	12-Dec-26	17,716.20	12,401.34	17,716.20	100%	70%	-35
SERVICE CONNECTION		11	31-Oct-26	26-Nov-26	20-Aug-26 A	27-Dec-26	1,674.00	2,790.00	3,720.00	45%	75%	-85
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	13-Dec-26	1,674.00	1,897.20	2,232.00	75%	85%	-90
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-2	26-Nov-26	27-Aug-26 A	27-Dec-26	0.00	892.80	1,488.00	0%	60%	-95
LANDSCAPING WORKS		34	06-Oct-26	09-Nov-26	09-Jul-26 A	25-Nov-26	384,168.66	325,918.76	409,192.26	93.88%	79.65%	-89
HARDSCAPE WORK		28	08-Oct-26	09-Nov-26	09-Jul-26 A	25-Nov-26	256,329.66	224,255.36	257,953.26	99.37%	86.94%	-91
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	12-Nov-26	148,149.00	140,741.55	148,149.00	100%	95%	-99
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	14-Nov-26	104,392.26	83,513.81	104,392.26	100%	80%	-81
PG-H-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-26	09-Nov-26	14-Nov-26	25-Nov-26	3,788.40	0.00	5,412.00	70%	0%	0
SOFTSCAPE WORK		14	06-Oct-26	09-Nov-26	27-Aug-26 A	25-Nov-26	127,839.00	101,663.40	151,239.00	84.53%	67.22%	-47
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26	17-Oct-26	26-Oct-26 A	12-Nov-26	96,639.00	57,983.40	96,639.00	100%	60%	-5
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-2	09-Nov-26	27-Aug-26 A	25-Nov-26	31,200.00	43,680.00	54,600.00	57.14%	80%	-70
TOILET BUILDING WORKS		84	03-Aug-2	06-Oct-26	30-Jul-26 A	19-Nov-26	148,912.62	105,307.10	148,912.62	100%	70.72%	-40
CIVIL WORK		32	09-Sep-2	05-Oct-26	20-Aug-26 A	18-Nov-26	82,010.40	54,268.92	82,010.40	100%	66.17%	-54
ARCHITECTURAL WORK		32	09-Sep-2	05-Oct-26	20-Aug-26 A	18-Nov-26	82,010.40	54,268.92	82,010.40	100%	66.17%	-54
GENERAL FINISHES		32	09-Sep-2	05-Oct-26	20-Aug-26 A	18-Nov-26	72,432.60	52,353.36	72,432.60	100%	72.28%	-54
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-2	12-Sep-26	20-Aug-26 A	12-Nov-26	2,958.00	2,366.40	2,958.00	100%	80%	-69
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-2	20-Sep-26	20-Aug-26 A	15-Nov-26	273.60	218.88	273.60	100%	80%	-66
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-2	27-Sep-26	27-Aug-26 A	16-Nov-26	13,273.80	10,619.04	13,273.80	100%	80%	-63
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-2	05-Oct-26	04-Oct-26 A	18-Nov-26	55,927.20	39,149.04	55,927.20	100%	70%	-32
ROOF FINISHES		2	04-Oct-26	05-Oct-26	27-Oct-26 A	18-Nov-26	9,577.80	1,915.56	9,577.80	100%	20%	-17
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26	05-Oct-26	27-Oct-26 A	18-Nov-26	9,577.80	1,915.56	9,577.80	100%	20%	-17
MEP WORK		84	03-Aug-2	06-Oct-26	30-Jul-26 A	19-Nov-26	66,902.22	51,038.18	66,902.22	100%	76.29%	-40
MECANICAL WORKS		84	03-Aug-2	06-Oct-26	30-Jul-26 A	19-Nov-26	50,638.50	37,214.02	50,638.50	100%	73.49%	-40
FIRE FIGHTING SYSTEM		1	06-Oct-26	06-Oct-26	18-Nov-26	19-Nov-26	136.26	0.00	136.26	100%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26	06-Oct-26	18-Nov-26	19-Nov-26	136.26	0.00	136.26	100%	0%	0
SEWER AND DRAINAGE SYSTEM		77	03-Aug-2	23-Aug-26	30-Jul-26 A	10-Nov-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-70
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-2	04-Aug-26	30-Jul-26 A	07-Nov-26	3,225.72	2,741.86	3,225.72	100%	85%	-82
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-2	23-Aug-26	08-Nov-26	10-Nov-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-2	15-Aug-26	26-Sep-26 A	07-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-34
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-2	15-Aug-26	26-Sep-26 A	07-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-34
WATER SUPPLY SYSTEM		3	18-Aug-2	20-Aug-26	27-Aug-26 A	08-Nov-26	36,366.00	29,092.80	36,366.00	100%	80%	-59
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-2	20-Aug-26	27-Aug-26 A	08-Nov-26	36,366.00	29,092.80	36,366.00	100%	80%	-59
ELECTRICAL WORKS		11	27-Aug-2	08-Sep-26	20-Aug-26 A	12-Nov-26	16,263.72	13,824.16	16,263.72	100%	85%	-60
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-2	29-Aug-26	20-Aug-26 A	10-Nov-26	1,983.60	1,686.06	1,983.60	100%	85%	-68
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-2	01-Sep-26	20-Aug-26 A	11-Nov-26	1,983.60	1,686.06	1,983.60	100%	85%	-67
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-2	05-Sep-26	20-Aug-26 A	11-Nov-26	4,959.00	4,215.15	4,959.00	100%	85%	-68
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-2	08-Sep-26	20-Aug-26 A	12-Nov-26	7,337.52	6,236.89	7,337.52	100%	85%	-68
PROJECT CLOSOUT		32	02-Nov-2	03-Dec-26	20-Oct-26 A	05-Dec-26	73,598.24	163,892.38	388,435.16	18.95%	42.19%	-12
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-2	12-Nov-26	29-Oct-26 A	25-Nov-26	73,598.24	119,597.14	183,995.60	40%	65%	-14
PG-H-PCL-20	As-Built Drawings	18	14-Nov-2	03-Dec-26	20-Oct-26 A	03-Dec-26	0.00	44,295.24	68,146.52	0%	65%	-20
PG-H-PCL-30	Snag list Submission	8	14-Nov-2	22-Nov-26	25-Nov-26	05-Dec-26	0.00	0.00	136,293.04	0%	0%	0
TABUK		144	25-Jun-26	08-Dec-26	12-Jul-26 A	15-Feb-27	3,646,472.03	2,723,244.00	4,191,923.82	86.99%	64.96%	-44
PROCUREMENT		63	25-Jun-26	27-Aug-26	06-Aug-26 A	10-Nov-26	2,148,284.30	1,744,361.48	2,148,284.30	100%	81.2%	-27
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	10-Nov-26	2,111,605.20	1,711,350.29	2,111,605.20	100%	81.04%	-32
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	10-Nov-26	2,111,605.20	1,711,350.29	2,111,605.20	100%	81.04%	-32
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	08-Nov-26	13,928.65	12,535.79	13,928.65	100%	90%	-60
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	08-Nov-26	13,928.65	12,535.79	13,928.65	100%	90%	-60
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	08-Nov-26	2,013,812.01	1,624,564.59	2,013,812.01	100%	80.67%	-50
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	08-Nov-26	58,731.75	52,858.58	58,731.75	100%	90%	-60
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	08-Nov-26	10,152.00	9,136.80	10,152.00	100%	90%	-60
PG-T-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	08-Nov-26	26,778.60	24,100.74	26,778.60	100%	90%	-60
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	08-Nov-26	39,487.50	35,538.75	39,487.50	100%	90%	-67
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	29-Oct-26 A	08-Nov-26	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	1
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-52
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	10-Nov-26	3,427.65	2,399.36	3,427.65	100%	70%	-52
IRRIGATION WORK		4	01-Jul-26	05-Jul-26	20-Aug-26 A	07-Nov-26	16,364.70	14,728.23	16,364.70	100%	90%	-62
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	05-Jul-26	20-Aug-26 A	07-Nov-26	16,364.70	14,728.23	16,364.70	100%	90%	-62
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	08-Nov-26	64,072.19	57,122.33	64,072.19	100%	89.15%	-46
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	07-Nov-26	3,615.08	3,253.58	3,615.08	100%	90%	-67
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	08-Nov-26	1,785.24	1,606.72	1,785.24	100%	90%	-60
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	08-Nov-26	1,428.19	1,285.37	1,428.19	100%	90%	-60
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	08-Nov-26	41,772.67	37,595.40	41,772.67	100%	90%	-60
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	08-Nov-26	4,618.19	4,156.37	4,618.19	100%	90%	-60
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-2	24-Aug-26	27-Aug-26 A	08-Nov-26	3,525.77	2,996.90	3,525.77	100%	85%	-50
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	08-Nov-26	4,463.64	3,794.09	4,463.64	100%	85%	-50
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	08-Nov-26	2,863.40	2,433.89	2,863.40	100%	85%	-50
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Nov-26	36,679.10	33,011.19	36,679.10	100%	90%	-54
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Nov-26	36,679.10	33,011.19	36,679.10	100%	90%	-54
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	07-Nov-26	19,978.06	17,980.25	19,978.06	100%	90%	-51
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	07-Nov-26	714.10	642.69	714.10	100%	90%	-51
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	07-Nov-26	8,301.96	7,471.76	8,301.96	100%	90%	-51

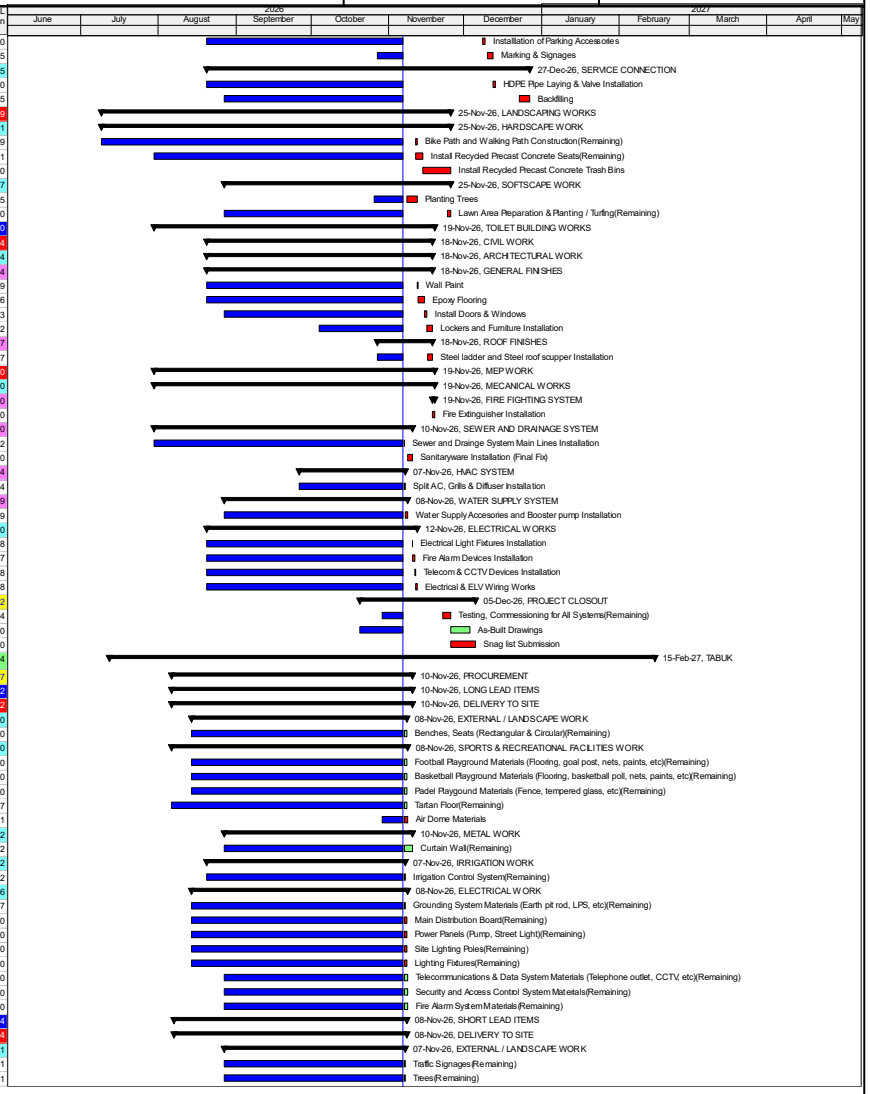


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	07-Nov-26	10,962.00	9,865.80	10,962.00	100%	90%	-51
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Nov-26	1,724.00	1,551.60	1,724.00	100%	90%	-26
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Nov-26	1,302.70	1,172.43	1,302.70	100%	90%	-26
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Nov-26	112.75	101.48	112.75	100%	90%	-26
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Nov-26	308.56	277.70	308.56	100%	90%	-26
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	07-Nov-26	14,977.04	13,479.33	14,977.04	100%	90%	-69
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	07-Nov-26	1,859.76	1,673.78	1,859.76	100%	90%	-69
PG-T-PR-SL-IR-DL-20_R	Bubblers and Sprayers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	07-Nov-26	13,117.28	11,805.55	13,117.28	100%	90%	-58
CONSTRUCTION STAGE		133	01-Jul-26	07-Dec-26	12-Jul-26 A	22-Dec-26	1,498,187.73	705,727.40	1,623,400.88	92.29%	43.47%	-4
PLAYGROUND AND LANDSCAPING WORKS		133	01-Jul-26	07-Dec-26	12-Jul-26 A	22-Dec-26	689,732.29	665,847.62	814,945.44	84.64%	81.7%	-4
PLAYGROUND WORKS		92	08-Aug-26	07-Dec-26	14-Aug-26 A	06-Dec-26	175,055.52	165,278.65	221,537.34	79.02%	74.61%	7
FOOTBALL PLAYGROUND WORKS		76	19-Aug-26	17-Nov-26	14-Aug-26 A	21-Nov-26	85,587.66	85,106.33	109,254.66	78.34%	77.9%	-7
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	08-Nov-26	24,360.00	21,924.00	24,360.00	100%	90%	-54
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	09-Nov-26	23,667.00	21,300.30	23,667.00	100%	90%	-62
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	12-Nov-26	35,500.50	28,400.40	35,500.50	100%	80%	-57
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	15-Nov-26	2,060.16	1,648.13	2,060.16	100%	80%	-56
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	27-Oct-26 A	21-Nov-26	0.00	11,833.50	23,667.00	0%	50%	-12
BASKETBALL PLAYGROUND WORKS		72	31-Aug-26	17-Nov-26	20-Aug-26 A	28-Nov-26	42,235.02	31,025.59	43,200.72	97.76%	71.82%	-17
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	09-Nov-26	13,091.76	11,782.58	13,091.76	100%	90%	-53
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	11-Nov-26	15,472.08	13,924.87	15,472.08	100%	90%	-53
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	28-Oct-26 A	25-Nov-26	13,091.76	3,927.53	13,091.76	100%	30%	-8
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	28-Nov-26	579.42	1,390.61	1,545.12	37.5%	90%	-62
PADEL PLAYGROUND WORKS		78	08-Aug-26	07-Dec-26	20-Aug-26 A	06-Dec-26	47,232.84	49,146.73	69,081.96	68.37%	71.14%	12
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	10-Nov-26	3,534.96	3,181.46	3,534.96	100%	90%	-49
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	11-Nov-26	5,302.44	4,772.20	5,302.44	100%	90%	-53
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	20-Oct-26 A	22-Nov-26	5,302.44	2,651.22	5,302.44	100%	50%	-11
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	24-Nov-26	26,325.00	23,692.50	26,325.00	100%	90%	-65
PG-T-CON-EXPD-70	Court Accessories Installation	16	02-Nov-26	19-Nov-26	26-Oct-26 A	03-Dec-26	6,768.00	13,536.00	27,072.00	25%	50%	-18
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	06-Dec-26	0.00	1,313.35	1,545.12	0%	85%	-71
GENERAL SITE WORKS		133	01-Jul-26	23-Nov-26	12-Jul-26 A	22-Dec-26	371,488.51	313,375.78	384,213.00	96.69%	81.56%	-16
MECHANICAL WORK		100	01-Jul-26	10-Aug-26	12-Jul-26 A	28-Nov-26	206,336.28	177,179.71	206,336.28	100%	85.87%	-83
STORM WATER AND UTILITY WORK		78	01-Jul-26	04-Aug-26	20-Aug-26 A	22-Nov-26	22,092.00	11,646.00	22,092.00	100%	52.72%	-49
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	07-Nov-26	5,160.00	4,128.00	5,160.00	100%	80%	-62
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	09-Nov-26	10,740.00	7,518.00	10,740.00	100%	70%	-38
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	09-Nov-26	12-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	12-Nov-26	16-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	17-Nov-26	22-Nov-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	17-Nov-26	183,926.34	165,533.71	183,926.34	100%	90%	-94
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	16-Nov-26	34,712.34	31,241.11	34,712.34	100%	90%	-104
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	16-Nov-26	90,915.00	81,823.50	90,915.00	100%	90%	-69
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	17-Nov-26	58,299.00	52,469.10	58,299.00	100%	90%	-70
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	22-Nov-26	28-Nov-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	22-Nov-26	28-Nov-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		79	11-Aug-26	07-Nov-26	20-Aug-26 A	22-Dec-26	161,015.15	124,051.42	161,164.92	99.91%	76.97%	-31
POWER, LIGHTING & GROUNDING		43	11-Aug-26	19-Sep-26	20-Aug-26 A	03-Dec-26	104,094.72	84,102.28	104,094.72	100%	80.79%	-56
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	29-Nov-26	8,265.00	7,438.50	8,265.00	100%	90%	-77
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	30-Nov-26	4,586.70	3,669.36	4,586.70	100%	80%	-57
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	01-Dec-26	17,397.90	13,918.32	17,397.90	100%	80%	-56
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	02-Dec-26	69,621.12	55,696.90	69,621.12	100%	80%	-59
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26	19-Sep-26	04-Oct-26 A	03-Dec-26	4,224.00	3,379.20	4,224.00	100%	80%	-49
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	19-Dec-26	43,146.00	30,202.20	43,146.00	100%	70%	-50
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	12-Dec-26	619.80	433.86	619.80	100%	70%	-65
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	13-Dec-26	619.80	433.86	619.80	100%	70%	-66
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	14-Dec-26	3,718.80	2,603.16	3,718.80	100%	70%	-66
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	15-Dec-26	15,249.12	10,674.38	15,249.12	100%	70%	-68
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	16-Dec-26	1,446.48	1,012.54	1,446.48	100%	70%	-69
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	19-Dec-26	6,612.00	4,628.40	6,612.00	100%	70%	-70
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	19-Dec-26	14,880.00	10,416.00	14,880.00	100%	70%	-72
FIRE ALARM SYSTEM		32	01-Oct-26	07-Nov-26	13-Oct-26 A	22-Dec-26	13,774.43	9,746.94	13,924.20	98.92%	70%	-29
PG-T-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26	10-Oct-26	13-Oct-26 A	14-Dec-26	1,983.60	1,388.52	1,983.60	100%	70%	-46
PG-T-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26	19-Oct-26	14-Oct-26 A	17-Dec-26	2,644.80	1,851.36	2,644.80	100%	70%	-47
PG-T-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26	28-Oct-26	15-Oct-26 A	20-Dec-26	8,097.60	5,668.32	8,097.60	100%	70%	-49
PG-T-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26	07-Nov-26	17-Oct-26 A	22-Dec-26	1,048.43	838.74	1,198.20	87.5%	70%	-50
PARKING WORK		7	04-Nov-26	11-Nov-26	26-Oct-26 A	22-Dec-26	4,137.09	10,135.86	14,479.80	28.57%	70%	-43
PG-T-CON-EXGN-PR-30	Marking & Signages	7	04-Nov-26	11-Nov-26	26-Oct-26 A	22-Dec-26	4,137.09	10,135.86	14,479.80	28.57%	70%	-43
SERVICE CONNECTION		10	12-Nov-26	23-Nov-26	14-Aug-26 A	22-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-101
PG-T-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	22-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-101
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	14-Nov-26	143,188.26	187,193.19	209,195.10	68.45%	89.48%	-58
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	14-Nov-26	97,066.26	112,797.39	126,533.10	76.71%	89.14%	-42
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	07-Nov-26	60,984.00	54,885.60	60,984.00	100%	90%	-51
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	10-Nov-26	36,082.26	54,123.39	60,137.10	60%	90%	-77
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	14-Nov-26	0.00	3,788.40	5,412.00	0%	70%	-33
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	14-Nov-26	46,122.00	74,395.80	82,662.00	55.8%	90%	-68

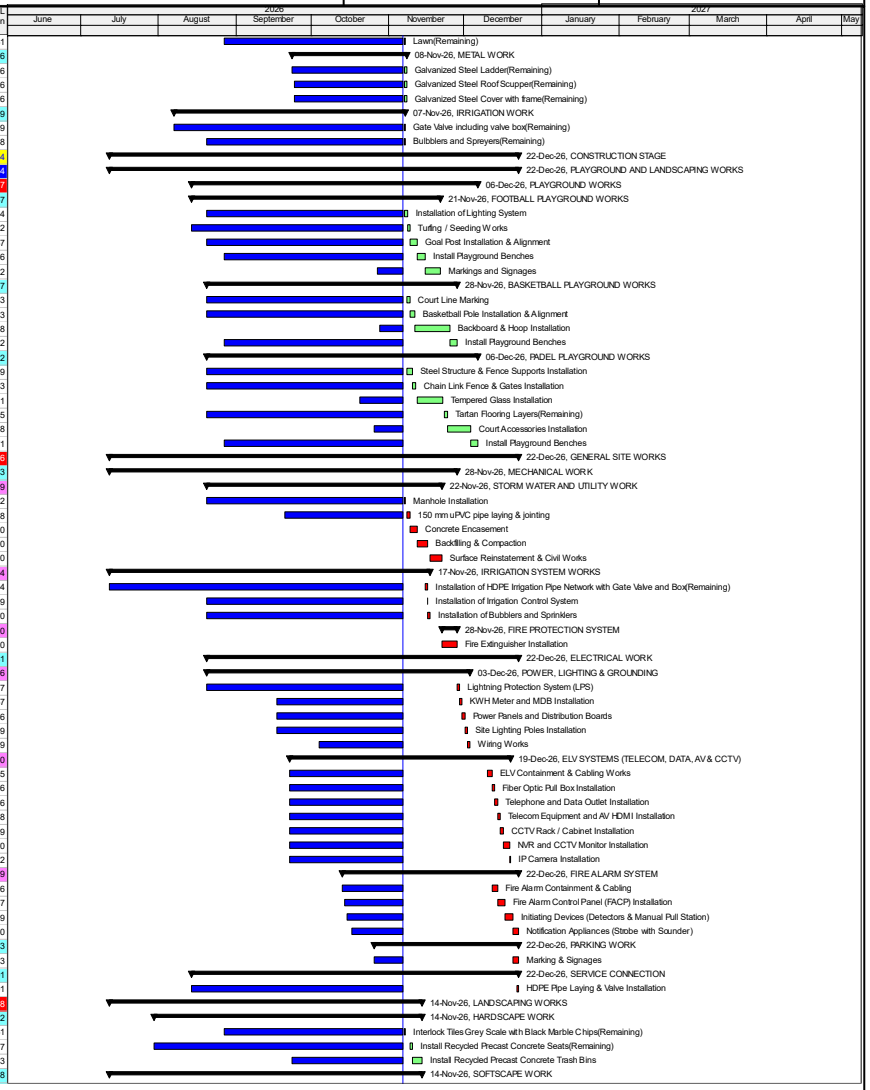


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 08-Nov-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	09-Nov-26	46,122.00	41,509.80	46,122.00	100%	90%	-28
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-2	22-Nov-26	12-Jul-26 A	14-Nov-26	0.00	32,886.00	36,540.00	0%	90%	-100
AIR DOME CONSTRUCTION		22	26-Aug-2	20-Sep-26	07-Nov-26	01-Dec-26	751,464.86	0.00	751,464.86	100%	0%	0
CIVIL WORK		17	26-Aug-2	14-Sep-26	07-Nov-26	25-Nov-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-2	05-Sep-26	07-Nov-26	16-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-80	Installation of Membrane System	8	06-Sep-2	14-Sep-26	17-Nov-26	25-Nov-26	250,488.29	0.00	250,488.29	100%	0%	0
MECHANICAL WORK		5	15-Sep-2	20-Sep-26	26-Nov-26	01-Dec-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-ME-10	Installation of Main Air Package Units	5	15-Sep-2	20-Sep-26	26-Nov-26	01-Dec-26	250,488.29	0.00	250,488.29	100%	0%	0
TOILET BUILDING WORKS		16	31-Aug-2	26-Oct-26	19-Sep-26 A	11-Nov-26	56,990.58	39,879.78	56,990.58	100%	69.96%	5
CIVIL WORK		3	24-Oct-26	26-Oct-26	19-Sep-26 A	10-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-41
ARCHITECTURAL WORK		3	24-Oct-26	26-Oct-26	19-Sep-26 A	10-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-41
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	10-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-41
PG-T-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	10-Nov-26	9,577.80	6,704.46	9,577.80	100%	70%	-41
MEP WORK		16	31-Aug-2	28-Oct-26	20-Sep-26 A	11-Nov-26	47,412.78	33,175.32	47,412.78	100%	69.97%	6
MECANICAL WORKS		16	31-Aug-2	28-Oct-26	20-Sep-26 A	11-Nov-26	47,412.78	33,175.32	47,412.78	100%	69.97%	6
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	11-Nov-26	136.26	81.76	136.26	100%	60%	-39
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	11-Nov-26	136.26	81.76	136.26	100%	60%	-39
SEWER AND DRAINAGE SYSTEM		2	03-Sep-2	05-Sep-26	23-Sep-26 A	08-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-37
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-2	05-Sep-26	23-Sep-26 A	08-Nov-26	3,225.72	2,258.00	3,225.72	100%	70%	-37
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	09-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-40
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	09-Nov-26	7,684.80	5,379.36	7,684.80	100%	70%	-40
WATER SUPPLY SYSTEM		3	31-Aug-2	02-Sep-26	23-Sep-26 A	07-Nov-26	36,366.00	25,456.20	36,366.00	100%	70%	-35
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-2	02-Sep-26	23-Sep-26 A	07-Nov-26	36,366.00	25,456.20	36,366.00	100%	70%	-35
PROJECT CLOSOUT		140	22-Nov-2	08-Dec-26	29-Oct-26 A	15-Feb-27	0.00	273,155.11	420,238.64	0%	65%	-78
PG-T-PCL-20	As-Built Drawings	15	22-Nov-2	08-Dec-26	29-Oct-26 A	15-Feb-27	0.00	73,825.71	113,578.01	0%	65%	-78
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-2	03-Dec-26	29-Oct-26 A	13-Feb-27	0.00	199,329.41	306,660.63	0%	65%	-81

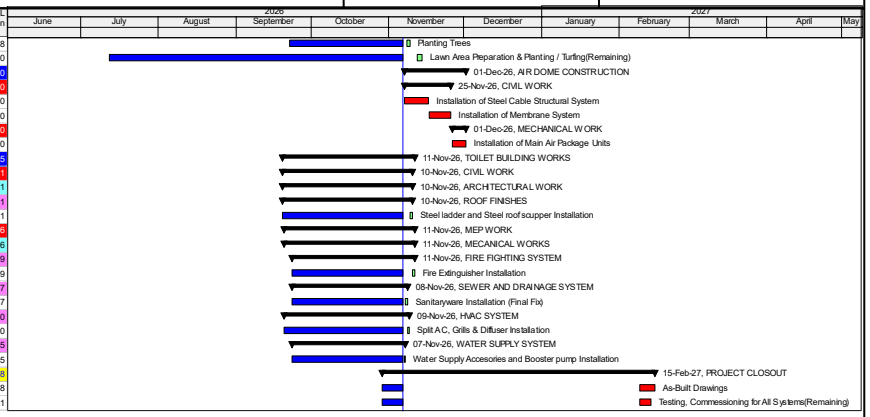

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
