44 Ready-Built Factories (900 m²), Dammam 3rd Industrial City

إنشاء 44 مصنع جاهز (900 متر مربع) في المدينة الصناعية بالدمام الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Saudi Zaas Construction	EGIS	Engr. Affat M. Al-Enezi	07-Jan-2026	06-Mar-2027

Scope: 44 ready-built factories of 900 m² each in 11 blocks (B1–B11), with external utilities, roads, parking and street lighting.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (225,761 man-hours in total). At the 27-Oct-2026 data date the project is 80.0% complete against 79.2% planned, 0.8% ahead. The lead comes from testing and commissioning and external works; construction of the factory blocks is 1.0% behind, and Blocks B4 and B5 are each about 23% behind their plan.

PHYSICAL % COMPLETE
80.0% / 79.2% plan
▲ SPI 1.01 +0.8%

PROGRESS THIS WEEK
— no earlier week
No earlier weekly report uploaded to compare with

CONTRACT TIME ELAPSED
69.3% · day 293 of 423
● P6 finish 03-Mar-2027

INVOICED TO DATE (GROSS)
42.9% · 41.2M SAR
6 invoices, last period ends 30-Sep-2026

On plan overall, but almost no float is left at the finish.

The P6 update finishes the project on 03-Mar-2027, three days before the contract completion date of 06-Mar-2027, with zero float on project completion. Of the 99 activities in progress, the weekly report counts 98 as behind schedule, and failed-start activities rose from 205 to 270 this week. Construction is 73.6% complete against 74.6% planned.

Site photos this week

Four photos from this week's upload, dated 25-Oct-2026 in their file names, with titles from the weekly report's photo sheet. Select a photo to view it larger, then use the arrows to move between photos.




Fire pump works

Fire pumps and headers installed beside the water tank. 25-Oct-2026.



HVAC duct installation, Block 11

Duct runs hung from the roof steel, beside the fire-fighting pipes and lights.

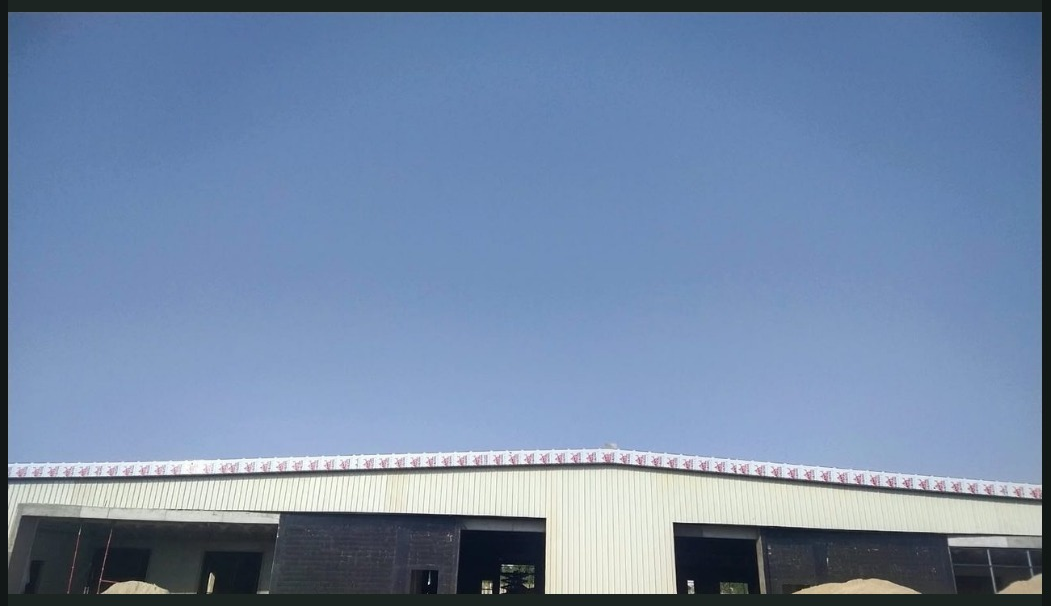

Cladding, Block 6

Wall and roof sheeting on the factory front.




Fire hose cabinet and partition wall

Cabinet fitted; block partition wall in progress.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

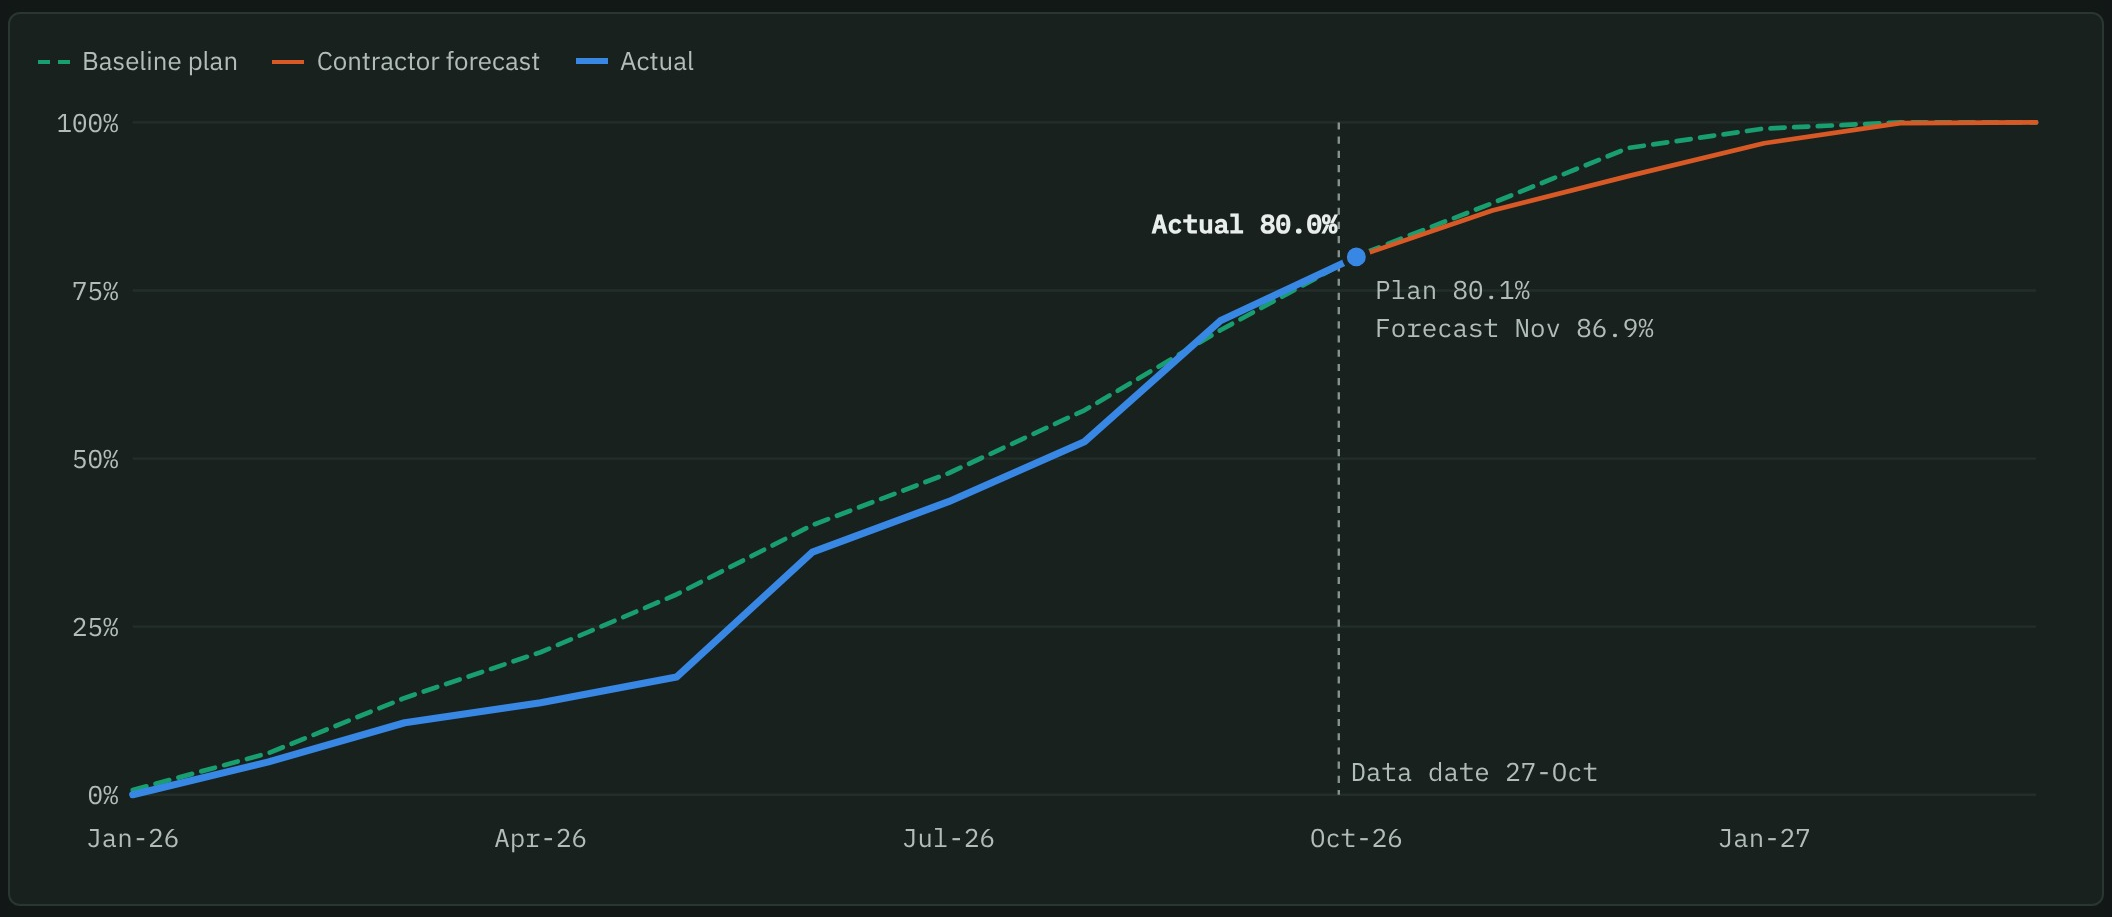

PERIOD ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED IN PERIOD	SPI
30-Jun-2026	40.1	36.1	−4.0%	+18.6	0.90
31-Jul-2026	47.8	43.6	−4.2%	+7.5	0.91
31-Aug-2026	57.2	52.5	−4.7%	+8.9	0.92
30-Sep-2026	69.1	70.5	+1.4%	+18.0	1.02
27-Oct-2026	**79.2**	**80.0**	**+0.8%**	**+9.5***	**1.01**

Month-end values from the Physical-Chart Data sheet; the 27-Oct-2026 row is from the weekly report's progress table. The baseline and revised plans in the file are identical, so one plan line is shown. * Gained from 01 to 27 Oct; the gain for this week alone is not available because no earlier weekly report was uploaded.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	25.5%	99.7%	100.0%	+0.3%	1.00	✓ Complete
Construction	63.4%	74.6%	73.6%	−1.0%	0.99	▼ Slightly behind
Testing & commissioning	5.1%	13.6%	40.6%	+27.0%	2.99	? Check
Project closeout	0.3%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**79.2%**	**80.0%**	**+0.8%**	**1.01**	▲ On track

The P6 update (data date 27-Oct-2026) has 2,517 activities: 1,753 completed, 99 in progress and 665 not started. Its scheduled finish is 03-Mar-2027, three days before the contract date. Critical-path activities fell from 131 to 85 this week.

Scope of work: quantities


Physical progress of each factory block and of the external works, then the major quantities tracked in the weekly report. Source: weekly report 27-Oct-2026, progress table and Major Quantities sheet.

Physical progress by block

BLOCK	MAN-HOURS	PLANNED	ACTUAL	VARIANCE	SPI	EARNED THIS WEEK (MAN-HOURS)
Block B1	11,840	73.2%	72.7%	−0.6%	0.99	1,087
Block B2	11,584	75.7%	73.9%	−1.8%	0.98	1,114
Block B3	11,824	76.3%	73.3%	−3.0%	0.96	364
Block B4	11,824	98.1%	75.4%	−22.8%	0.77	96
Block B5	11,728	99.0%	75.6%	−23.5%	0.76	96
Block B6	11,824	91.9%	3.7%*	−88.2%	0.04	0
Block B7	11,840	77.4%	80.5%	+3.1%	1.04	99
Block B8	11,840	70.7%	79.2%	+8.5%	1.12	88
Block B9	11,840	69.5%	79.3%	+9.8%	1.14	169
Block B10	11,840	68.2%	76.8%	+8.6%	1.13	117
Block B11	11,840	67.0%	75.9%	+8.8%	1.13	333
External works	13,232	33.4%	49.0%	+15.6%	1.47	382
Construction total	**143,056**	**74.6%**	**73.6%**	**−1.0%**	**0.99**	**4,354**

* Block B6 is recorded with 437 of 11,824 man-hours earned, while the progress tracking sheet shows its structure, walls and first-fix works complete and this week's photos show cladding there. The figure is probably an entry error; see Data notes.

Major quantities

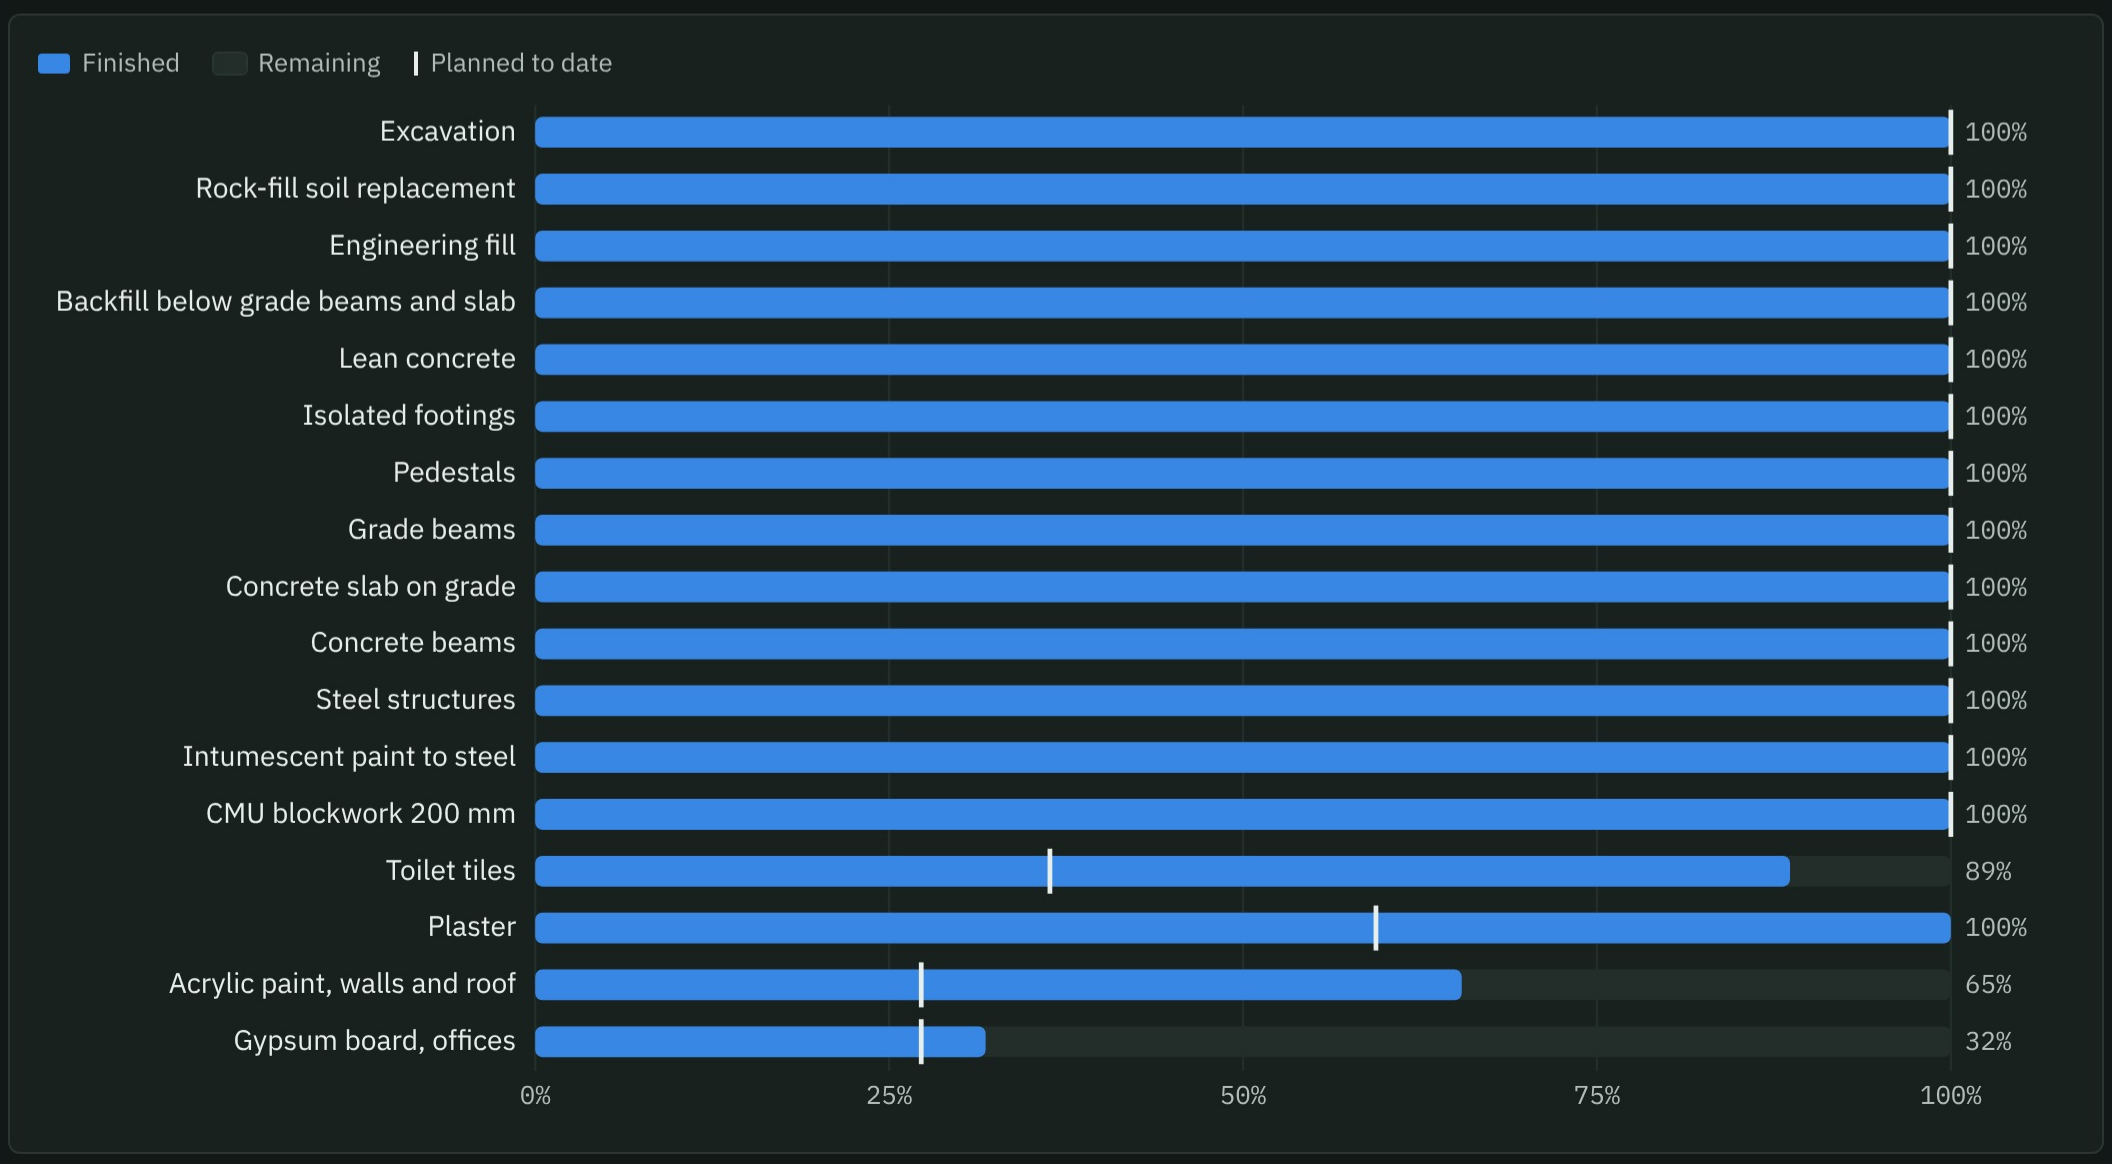

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED TO DATE

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED TO DATE
Excavation	All blocks	m³	40,940	40,940	–	0	100.0%	100.0%
Rock-fill soil replacement	All blocks	m³	48,560	48,560	–	0	100.0%	100.0%
Engineering fill	All blocks	m³	12,727	12,727	–	0	100.0%	100.0%
Backfill below grade beams and slab	All blocks	m³	11,559	11,559	–	0	100.0%	100.0%
Lean concrete	All blocks	m²	8,010	8,010	–	0	100.0%	100.0%
Isolated footings	All blocks	m³	2,807	2,807	–	0	100.0%	100.0%
Pedestals	All blocks	m³	395	395	–	0	100.0%	100.0%
Grade beams	All blocks	m³	540	540	–	0	100.0%	100.0%
Concrete slab on grade	All blocks	m³	7,260	7,260	–	0	100.0%	100.0%
Concrete beams	All blocks	m³	255	255	–	0	100.0%	100.0%
Steel structures	All blocks	nos	11	11	–	0	100.0%	100.0%
Intumescent paint to steel	All blocks	items	11	11	–	0	100.0%	100.0%
CMU blockwork 200 mm	All blocks	m²	9,630	9,630	–	0	100.0%	100.0%
Toilet tiles	All blocks	m²	820	726.9	–	93.1	88.6%	36.4%
Plaster	All blocks	m²	16,770	16,770	–	0	100.0%	59.4%
Acrylic paint, walls and roof	All blocks	m²	16,770	10,976	–	5,794	65.5%	27.3%
Gypsum board, offices	All blocks	m²	4,425	1,408	–	3,017	31.8%	27.3%

Substructure, steel and blockwork complete

Excavation, rock-fill replacement, engineering fill, footings, pedestals, grade beams, slab on grade, the 11 steel structures with intumescent paint, and 9,630 m² of blockwork are all reported 100% complete. Plaster is also complete (16,770 m²).

Finishes still open

Acrylic paint is 65.4% finished (5,794 m² remaining), gypsum board for offices 31.8% (3,017 m² remaining) and toilet tiles 88.6% (93 m² remaining). The "this week" column shows "–" because no earlier week was uploaded.

Milestones

Milestones from the weekly report, with the P6 update's forecast and float. Where the weekly report has no such milestone, the P6 baseline is shown and marked (P6).

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	07-Jan-2026	07-Jan-2026	07-Jan-2026 (actual)	–	✓ Done
Existing-condition survey and final reports	14-Jan-2026	14-Jan-2026	12-Feb-2026 (actual)	–	✓ Done
Complete mobilisation	16-Feb-2026	16-Feb-2026	18-Jan-2026 (actual)	–	✓ Done
Submittals and long-lead orders	14-May-2026	22-Mar-2026 (−53 d)	05-Jul-2026 (actual)	–	✓ Done
Delivery of all equipment and materials	07-Nov-2026	27-Sep-2026 (−41 d)	–	–	✓ Done
Site levelling, local roads and parking	12-Feb-2026 (P6)	–	27-Oct-2026	9	▼ Late
Civil works	21-Feb-2027	21-Feb-2027	21-Nov-2026	43	? Baselines differ
Testing and commissioning	06-Feb-2027 (P6)	–	24-Dec-2026	58	● Float available

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Mechanical works	27-Jan-2027	27-Jan-2027	21-Dec-2026	56	Float available
Earthworks	01-Feb-2027	21-Jan-2027 (−11 d)	–	–	On time
Electrical works	18-Feb-2027	13-Feb-2027 (−5 d)	02-Feb-2027	19	Float available
Construction completion	21-Feb-2027 (P6)	–	23-Feb-2027	7	At risk
All works complete, ready for handover	06-Mar-2027	03-Mar-2027 (−3 d)	03-Mar-2027	0	On time, no float

The weekly report and the P6 update use different baselines for the discipline milestones.

For civil works the weekly report's baseline is 21-Feb-2027, while the P6 baseline is 01-Oct-2026 and the P6 forecast 21-Nov-2026, 51 days after its own baseline. Electrical and architectural works are forecast for 02-Feb-2027 in P6, 43 days after their P6 baseline of 21-Dec-2026. The contractual milestone for site levelling, local roads and parking (P6 baseline 12-Feb-2026) has still not started and is forecast for the data date itself.

Procurement of key materials

Share of materials delivered to site, by discipline. Source: weekly report summary, 27-Oct-2026.



All 83 materials approved, ordered and on site


The weekly report records 83 of 83 materials approved, 83 purchase orders placed and 83 materials delivered, with delivery completed on 13-Oct-2026. Its milestone sheet gives 27-Sep-2026 for the same event.

Installation now under way

HVAC ducts and directly buried gate valves have been delivered and their installation has started (Risk & Issue log, 27-Oct-2026). The procurement tracker shows a purchase-order status of "ISSUED" for only 20 of its 83 items.

Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

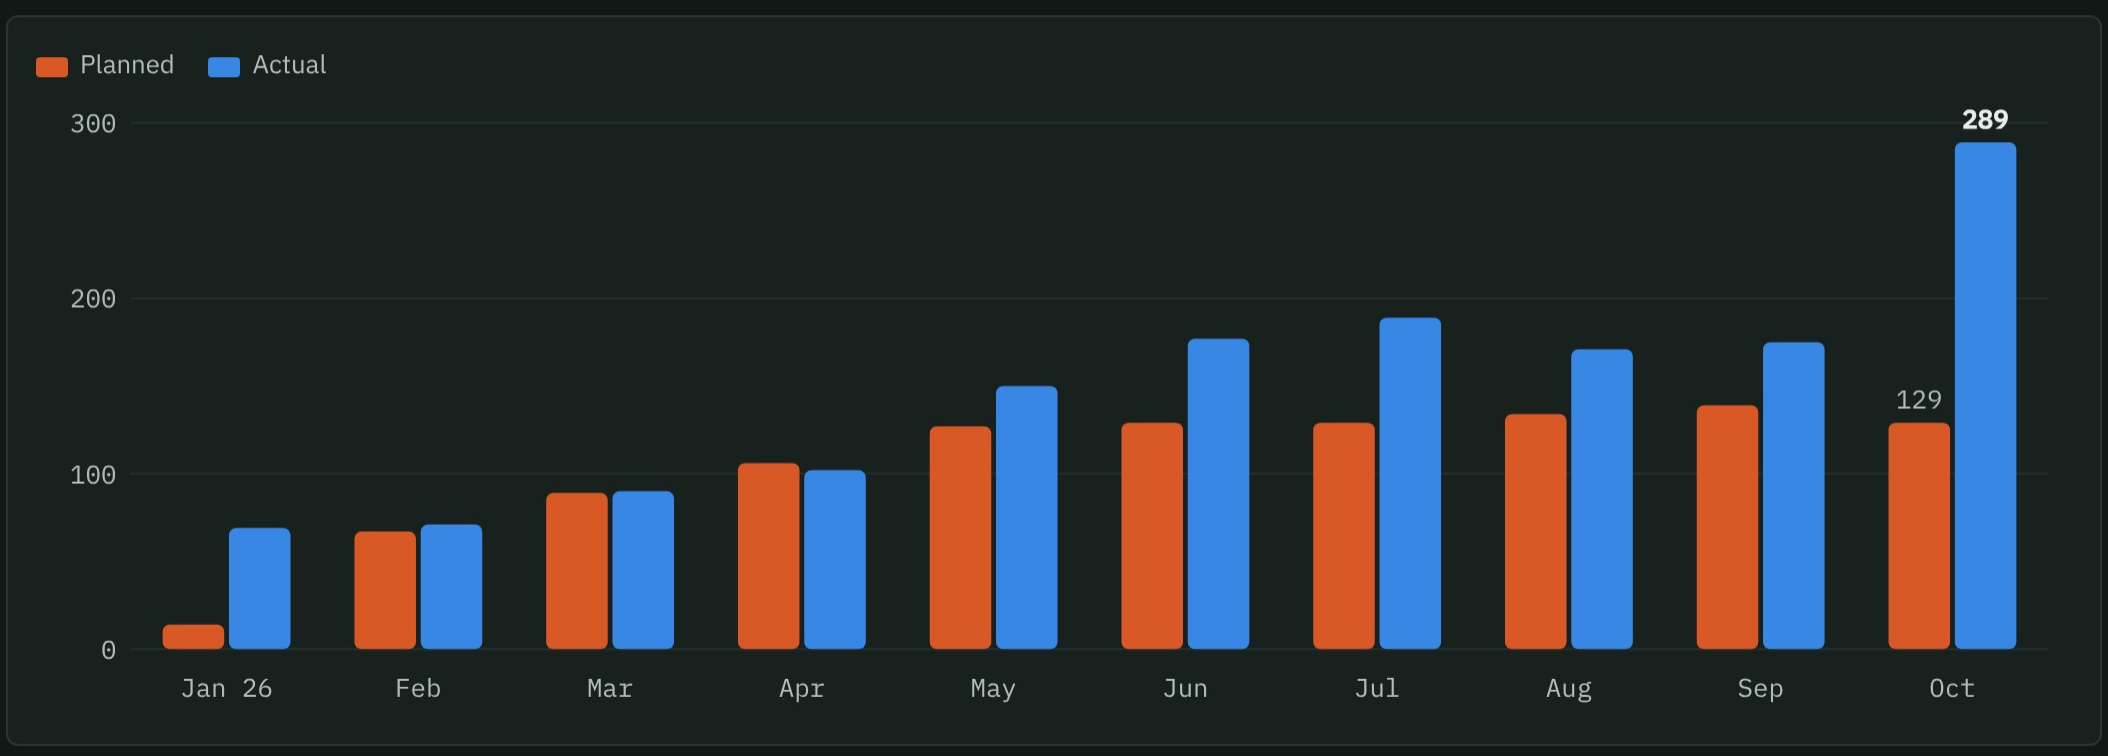

October head count is 289 against 129 planned: 267 labourers against 125 and 22 staff against 4. Equipment on site: 20 against 7 planned. The plan falls to 99 in November 2026.

Cost and invoicing

Contract value

Original contract value	95,996,525
Revised contract value	95,996,525
Estimate at completion	95,996,525
Potential changes	0
Change orders	0

All values in SAR. The change order log is empty.

Invoices

Invoices approved by the PM	6
Gross value	41,195,808
Advance payment recovery (10%)	4,119,581
Net value	37,076,227
Invoices paid	5
Amount paid	28,782,457

Invoicing is 42.9% of the contract value against 80.0% physical progress. Invoice 6 (September, 9,215,300 gross) was approved on 13-Oct-2026 and is not yet paid.

Health, safety and quality

Safety Score 0.87

Safe man-hours (cumulative)	288,540
Man-hours this week	16,440
Lost-time injuries	0
Fatalities	0
First-aid cases (cumulative)	1
Near misses (cumulative)	1
Property damage	0
Induction / toolbox sessions (cumulative)	78 / 93

Quality Score 0.93

FIRs issued / closed / pending	972 / 964 / 8
MIRs issued / closed / pending	92 / 77 / 15
NCRs issued / closed / pending	24 / 22 / 2
Site instructions	0
Shop drawings approved	158 of 158
Material submittals approved	83 of 83

Cumulative to 27-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
External platform (high)	Contractor	The external platform is behind its activity schedule. If not recovered it may delay area completion and handover.
Fire hose cabinets (high risk)	Contractor	Installation has started; any slippage would delay fire-protection testing and inspection.
Blocks B4 and B5	Contractor	B4 is 75.4% complete against 98.1% planned and B5 75.6% against 99.0%, each about 23% behind.
Irrigation excavation (medium risk)	Contractor	Excavation for the HDPE irrigation pipes has not started; the start and finish dates need to be confirmed.
Buried gate valves	Contractor	Material delivered and installation started; to be monitored until complete.
Float at completion	Contractor	Zero float on project completion and 98 of 99 active activities behind schedule.

Other open low risks in the log: ceiling gypsum board, aluminium composite panels, solar power plant and water-supply excavation. Closed this week: wall sandwich panels, plaster and HVAC duct delivery.

Data notes

- The weekly report workbook (WPR #36, .xlsb) has no text version in MD Files, so its figures were read from the original workbook in All Files.
- No earlier week has been uploaded for this project, so progress this week, the "this week" quantities and the weekly gain are shown as "—".
- The workbook's weekly physical figures disagree with each other: the Progress sheet gives 3,981 planned and 5,797 earned man-hours this week, the report page 4,323 and 4,538, its WBS rows add up to 4,019 and 4,354, and its block rows add up to 3,945 earned. None was used for the weekly rate.
- Block B6 shows 437 of 11,824 man-hours earned (3.7%) against 91.9% planned, while the progress tracking sheet shows B6 complete for structure, walls and first-fix works and a photo shows its cladding. This also lowers the construction total.
- Testing and commissioning is recorded at 40.6% earned against 13.6% planned, while the Testing sheet shows mechanical testing 8% complete and electrical and fire testing not started.
- The report page's headline plan and earned values, the P6 layouts and the Risk & Issue log ("Planned progress … Actual progress …") are cost-based; the log labels this cost-based figure as actual progress. This report uses the physical (man-hour) figures only.
- The weekly report's general information gives a forecast completion of 06-Mar-2027 (no variance), while its milestone sheet and the P6 update give 03-Mar-2027.
- Discipline milestone baselines in the weekly report differ from the P6 baseline (for example civil works 21-Feb-2027 against 01-Oct-2026). The survey milestone is shown as achieved on 14-Jan-2026 in the weekly report and on 12-Feb-2026 in P6.
- Material delivery completion is 13-Oct-2026 in the report summary and 27-Sep-2026 in the milestone sheet. The procurement sheets carry project ID DAM-05-009, not DAM3-05-11, and the tracker marks only 20 of 83 purchase orders as issued.
- The P6 file's project code is DAM3-02-3 with a planned start of 14-Mar-2023, which does not match this project.
- The invoice summary shows 0 submitted invoices although six are listed and approved.
- The Risk & Issue log names Engr Hamdi as MODON PM; the weekly report names Engr. Affat M. Al-Enezi. Its dashboard shows 245 open risks and 130 open issues, against 6 open risks and 2 open issues in the logs.
- The general information sheet still gives the project stage as "Mobilization". In Major Quantities the backfill unit is written "m4" (shown here as m³), and BOQ item 2.1.4 is used for two items.

Compiled 01-Nov-2026 from weekly report WPR #36 (data date 27-Oct-2026), the P6 update and the Risk & Issue log uploaded for the week of 22-Oct-2026.
