Playgrounds Initiative: Qassim Oasis, Hail and Tabuk Industrial City

مبادرة الملاعب بالمنطقة الوسطى (حائل, واحة القصيم, تبوك)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Advanced Construction & Contracting Co.	Egis	Bader Alrowaidan	17-Feb-2026	16-Dec-2026

Scope: playgrounds at three locations (Qassim Oasis, Hail and Tabuk Industrial City), with civil, architectural, electrical, mechanical and landscape works and general site works, including air domes at Qassim and Tabuk and a toilet building at each site.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (weekly report, Physical Progress sheet). At 08-Nov-2026 the project is 82.22% complete against 87.77% planned, behind by 5.55% (SPI 0.94). It gained 2.16% this week against 2.31% planned, so the gap widened slightly.

PHYSICAL % COMPLETE

82.22% / 87.77%

plan

▼ SPI 0.94 5.55% behind plan

PROGRESS THIS WEEK

+2.16% / +2.31%

plan

▼ 0.15% below the weekly plan

CONTRACT TIME ELAPSED

87.4% · day 264 of 302

▼ P6 finish 02-Mar-2027

INVOICED TO DATE (GROSS)

11.9% · 4.24M SAR

3 invoices, last period ends 31-Oct-2026

The schedule now finishes the project 76 days after the contract date.

The P6 update (data date 06-Nov-2026) and the weekly report both forecast handover on 02-Mar-2027 against the contract completion date of 16-Dec-2026, with −64.8 days of float; last week the forecast was 23-Feb-2027. 176 of the 284 open activities have negative float and 36 activities have failed to start. The air domes are furthest behind: Qassim 39.96% against 87.01% planned and Tabuk 35.13% against 81.77%, with no progress for the fourth week running.

Site photos this week

Six photos from the weekly report of 08-Nov-2026; two are stamped 07-Nov-2026 at Tabuk. Interlock, tartan, duct, toilet fit-out, GRP tank and roof waterproofing works continue. Select a photo to view it larger, then use the arrows to move between photos.




Interlock tiles installation

Pavers being laid along the walkway. No date stamp.




Tartan flooring installation

Tartan tiles being fixed on a circular play area. No date stamp.

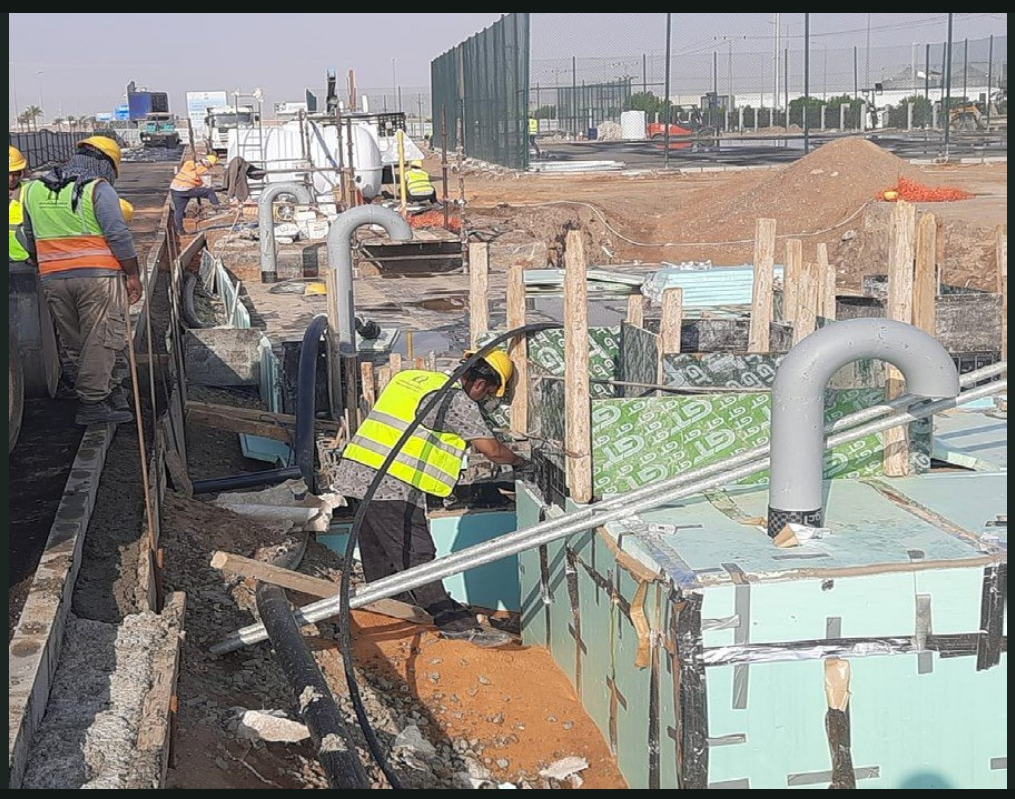

Duct work

Pre-insulated duct sections being joined in a trench. No date stamp.

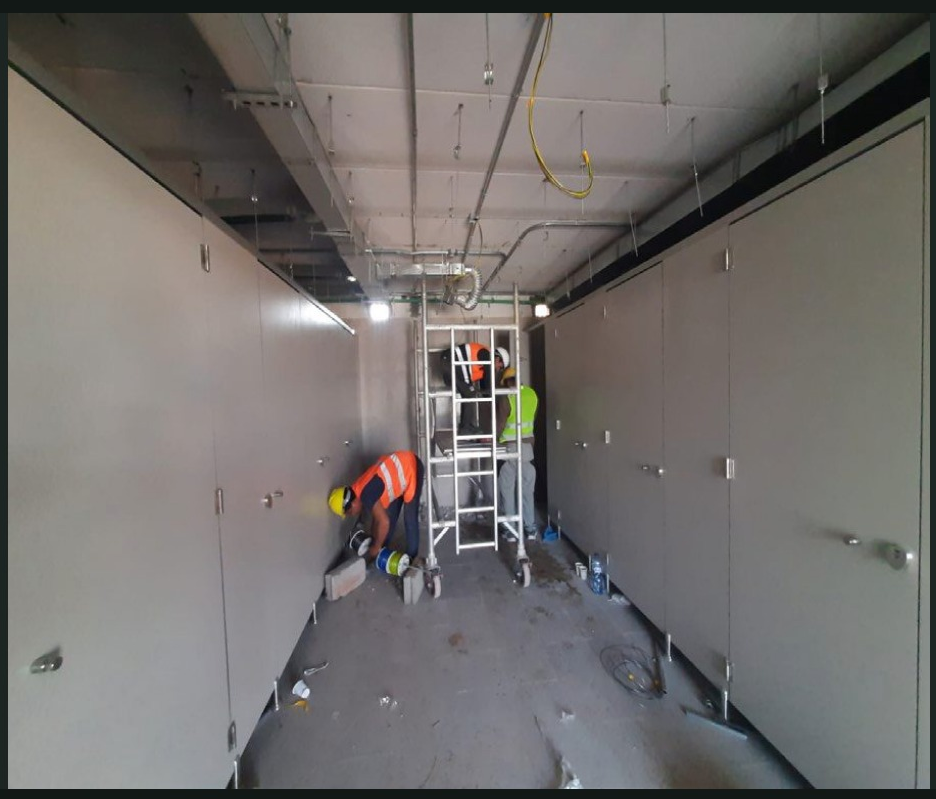


Phenolic door installation

Partitions and doors fitted in the toilet building. No date stamp.



GRP tank base frame, Tabuk

Frame set on the tank plinth. Stamped 07-Nov-2026, 09:18, Tabuk Industrial City.

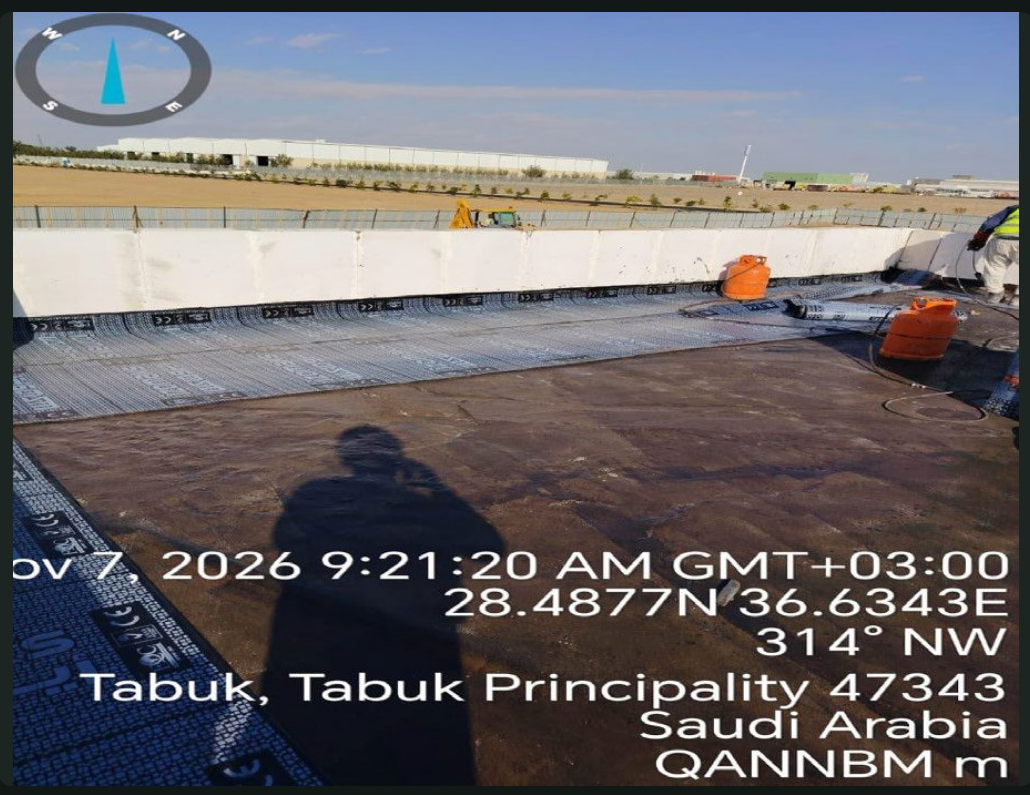


Roof waterproofing, Tabuk

Membrane laid on the roof. GPS-stamped 07-Nov-2026, 09:21, Tabuk.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet of the weekly report.

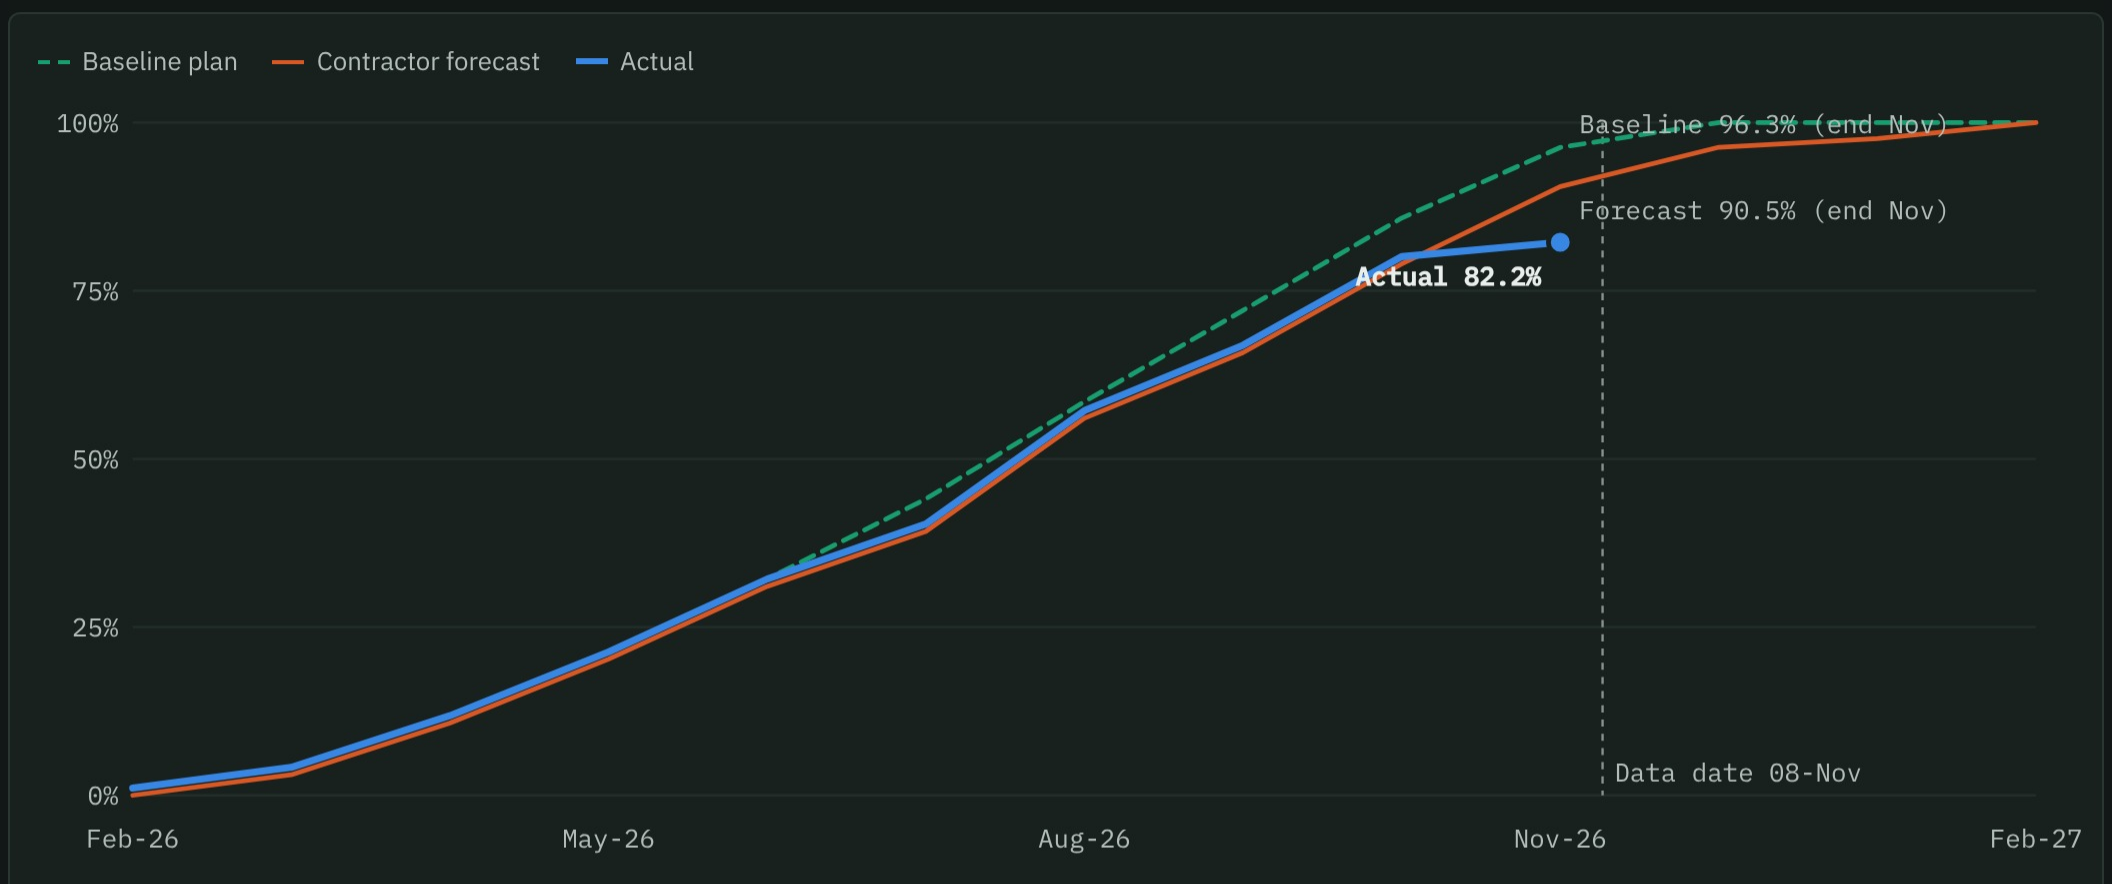

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
18-Oct-2026	80.25	74.79	−5.46	–	0.93
25-Oct-2026	83.26	77.64	−5.62	+2.85	0.93
01-Nov-2026	85.46	80.06	−5.40	+2.42	0.94
08-Nov-2026	**87.77**	**82.22**	**−5.55**	**+2.16**	**0.94**

Physical % complete from the weekly reports of 18 Oct to 08 Nov 2026, the only four weekly reports uploaded so far. The monthly baseline in the chart reaches 96.29% at the end of November and 100% at the end of December; the contractor forecast reaches 90.49% and 96.35%.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (weekly report, Progress sheet). Engineering and procurement carry no man-hours in the report, so they are not shown.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Project milestone (management time)	**30.0%**	**86.45%**	**86.43%**	**-0.02%**	**1.00**	▼ Behind
Construction	**66.6%**	**92.60%**	**83.55%**	**-9.04%**	**0.90**	▼ Behind
Qassim Oasis	24.3%	91.23%	83.43%	-7.81%	0.91	▼ Behind
Hail	17.9%	96.32%	86.22%	-10.10%	0.90	▼ Behind
Tabuk	24.3%	91.22%	81.73%	-9.49%	0.90	▼ Behind
Closeout	**3.5%**	**6.42%**	**19.98%**	**+13.56%**	**3.11**	▲ Ahead
Total	100%	**87.77%**	**82.22%**	**-5.55%**	**0.94**	▼ Behind

Within construction, the air domes are furthest behind: Qassim 446 of 1,116 man-hours earned against 971 planned, and Tabuk 392 against 912.57; neither has earned any man-hours for four weeks. The P6 update (data date 06-Nov-2026) has 1,929 activities: 1,645 completed, 221 in progress and 63 not started.

Scope of work: quantities

Total, finished and remaining quantity of the major items, all three sites together, from the Major Quantities sheet of the 08-Nov-2026 weekly report. The last column is the quantity planned to date. “This week” compares with the 01-Nov-2026 report.

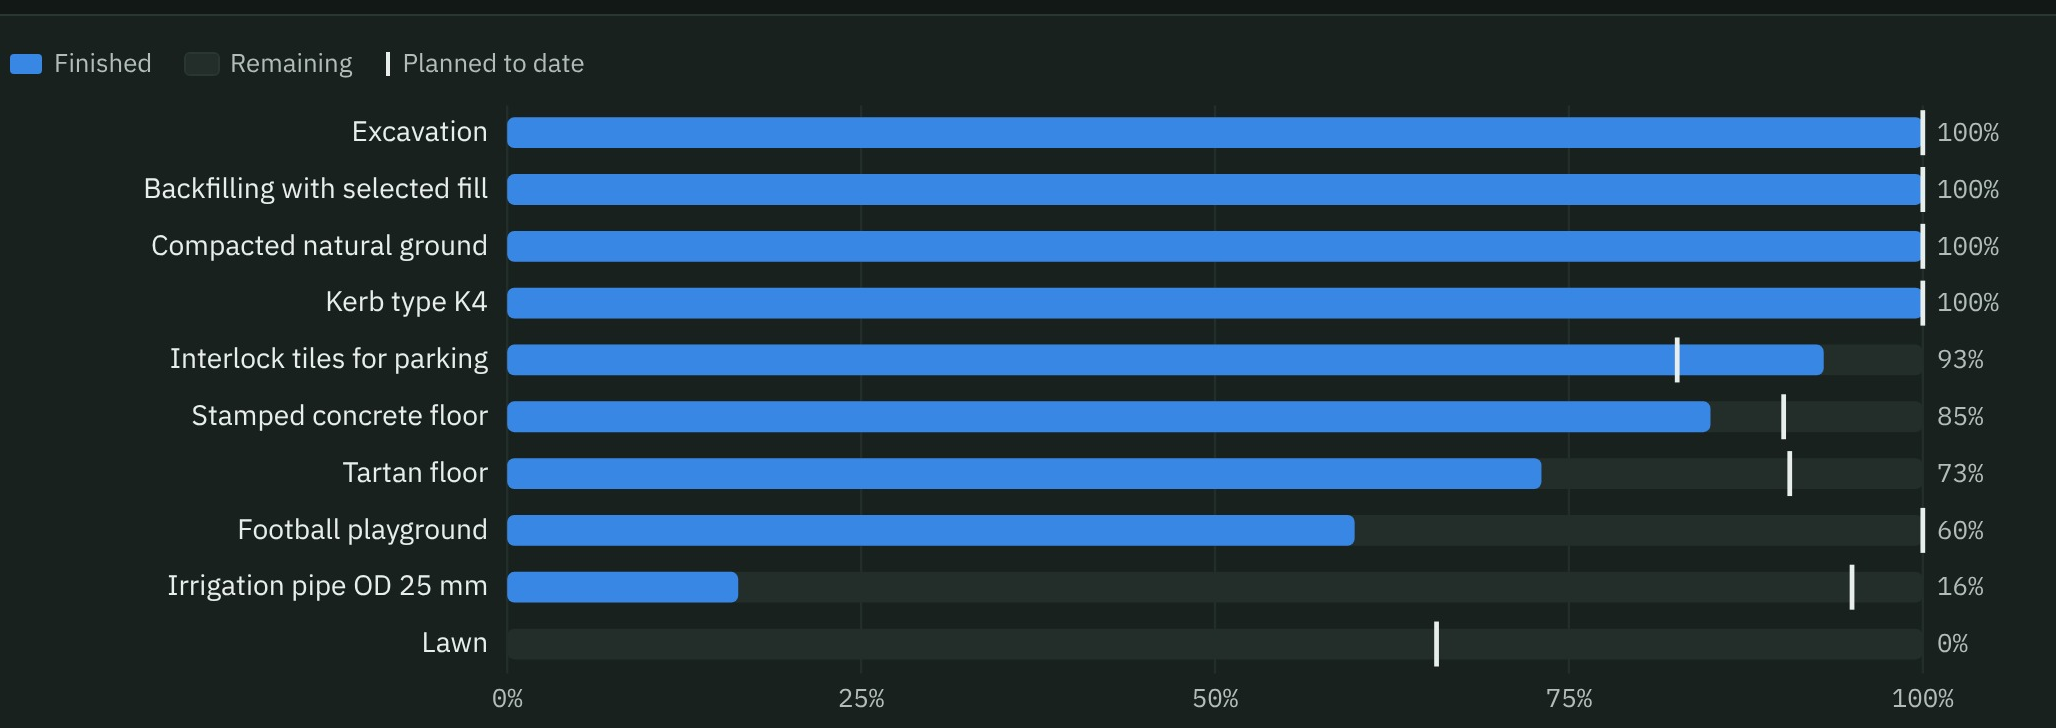

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Excavation	All	m³	29,400	29,400	0	0	100.0%	100.0%
Backfilling with selected fill	All	m³	29,400	29,400	0	0	100.0%	100.0%
Compacted natural ground	All	m²	33,300	33,300	0	0	100.0%	100.0%
Kerb type K4	All	LM	27,100	27,100	0	0	100.0%	100.0%
Interlock tiles for parking	All	m²	7,140	6,640	0	499.8	93.0%	82.7%
Stamped concrete floor	All	m²	7,800	6,630	0	1,170	85.0%	90.2%
Tartan floor	All	m²	10,950	8,000	0	2,950	73.1%	90.6%
Football playground	All	m²	7,350	4,400	0	2,950	59.9%	100.0%

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Irrigation pipe OD 25 mm	All	m	11,100	1,812	0	9,288	16.3%	95.0%
Lawn	All	m²	19,100	0	0	19,100	0.0%	65.6%

Reported this week

Interlock tiles, excavation for curbstone, phenolic doors, GRP tank, duct work, gates for the football court, epoxy floor, stone cladding in the toilet building, tartan and backfilling of irrigation lines (weekly executive summary). Next week: tartan, cable pulling for the toilet area, irrigation, curbstone, light pole foundations and interlock tiles.

Lawn, irrigation pipe and playgrounds lag

Lawn is at 0 of 12,539 m² planned to date, the 25 mm irrigation pipe at 1,812 of 10,545 m, the football playground at 4,400 of 7,350 m² and the tartan floor at 8,000 of 9,921 m². All major quantities are unchanged for the third week running, although interlock, tartan, curbstone and irrigation work was reported.

Milestones

The weekly report's milestone sheet and the P6 update disagree on some dates. Both are shown so the difference can be resolved with the contractor. P6 float is from the update with data date 06-Nov-2026.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	17-Feb-2026	17-Feb-2026	17-Feb-2026 (actual)	–	✓ Done
Complete mobilisation	18-Mar-2026	14-Apr-2026	–	–	✓ Done late
Complete engineering	16-Aug-2026	10-Nov-2026 (+86 d)	–	–	▼ Late
Complete procurement	27-Aug-2026	12-Nov-2026 (+77 d)	–	–	▼ Late
Completion of toilet building	28-Oct-2026	–	19-Nov-2026	+5.5	▼ At risk
Completion of playground works	07-Dec-2026	–	06-Dec-2026	+9.1	▼ At risk
Complete construction	14-Dec-2026	13-Feb-2026 (0 d as stated)	13-Feb-2027	–	? Conflicts with P6
Completion of landscape works	16-Dec-2026	–	12-Jan-2027	−23.0	▼ Late
Complete all works, ready for initial handover	16-Dec-2026	25-Feb-2027 (+71 d)	02-Mar-2027	−64.8	▼ Late
Complete demobilisation	16-Dec-2026	01-Mar-2027 (+75 d)	–	–	▼ Late
Project handover	16-Dec-2026	02-Mar-2027 (+76 d)	02-Mar-2027	−64.8	▼ Late

The weekly report gives “Complete construction” as 13-Feb-2026, a date already past.

P6 finishes the construction stage on 10-Feb-2027 at Qassim, 27-Dec-2026 at Hail and 13-Feb-2027 at Tabuk, so the intended date is probably 13-Feb-2027. The handover forecast moved from 23-Feb-2027 to 02-Mar-2027 this week, the third weekly slip in a row (07-Feb, 14-Feb, 23-Feb, then 02-Mar-2027). Of the contractual milestones, only the toilet building (+5.5 days) and the playground works (+9.1 days) keep positive float.

Procurement of key materials

Physical % complete of the open “delivery to site” activities with the lowest progress (P6 update, data date 06-Nov-2026). All other open delivery activities are at 85–95%.



Air dome materials: 80% delivered


At both Qassim and Tabuk, unchanged, with −64.8 and −61.0 days of float; Qassim's equals the float of project completion. The procurement log still shows the air dome purchase order as “under process” with a 150-day lead time.

Purchase orders and materials on site

The weekly report's procurement summary lists 57 materials: 33 purchase orders issued, 25 remaining and 8 materials on site, unchanged. The curtain wall remainder is at 80% at Qassim (70% last week) and Hail, and 70% at Tabuk.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet of the weekly report.

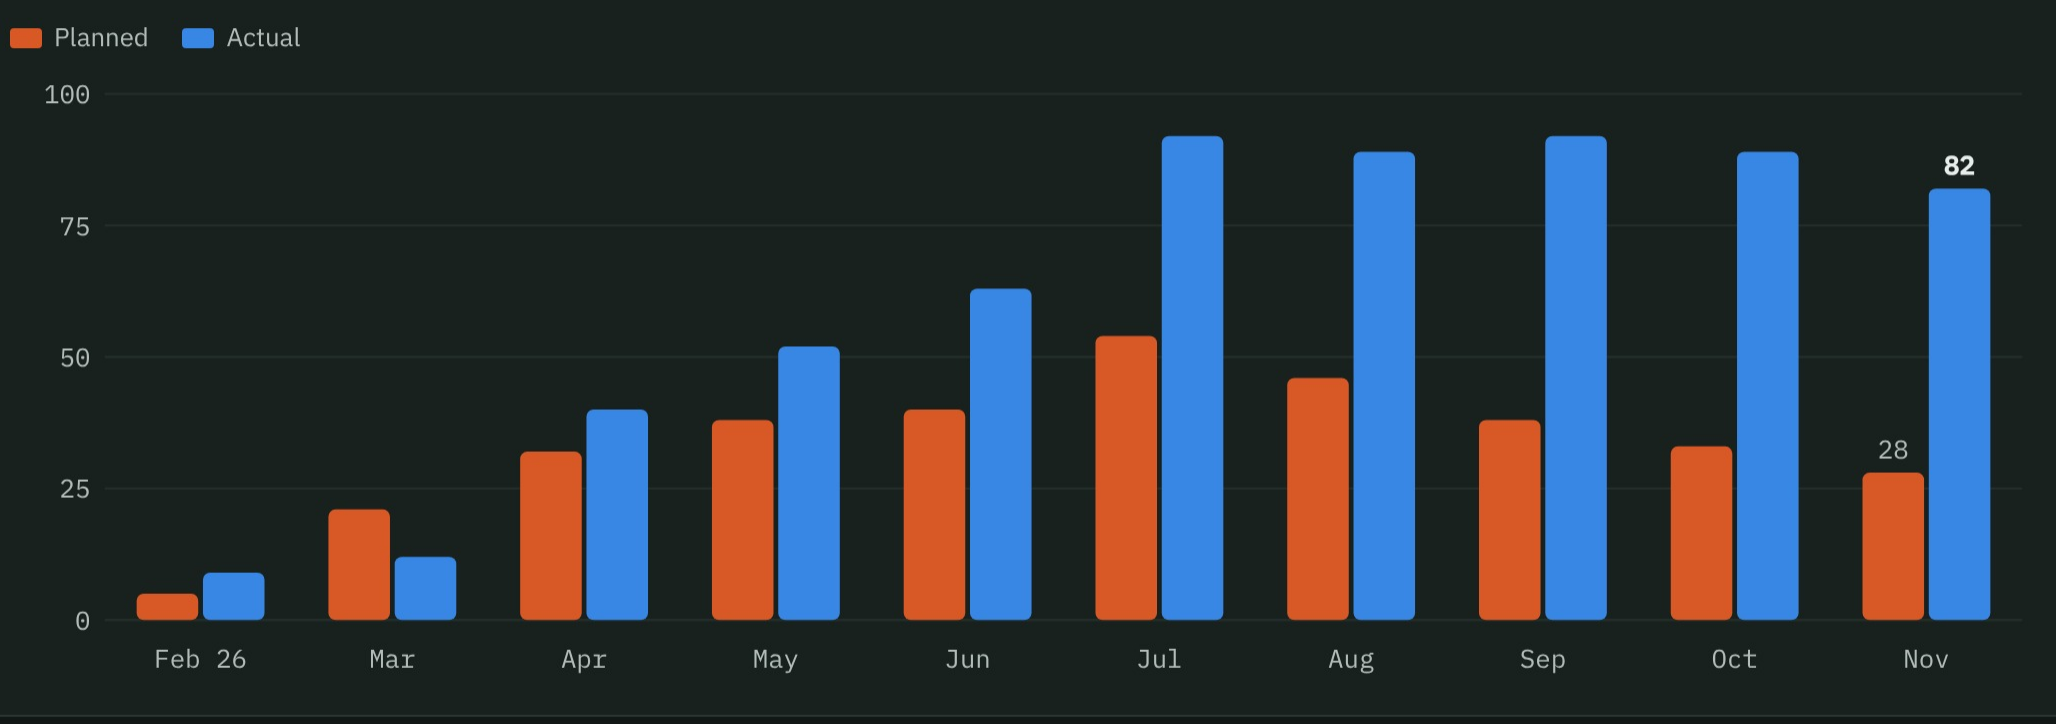

November head count is 82 against 28 planned (17 non-manual and 65 manual). The dashboard of the 08-Nov-2026 report shows 46 manual against 24 planned and 17 non-manual against 8, 63 in total against 32. Equipment on site in November: 20 against 3 planned.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	35,709,993
Revised contract value	35,709,993
Change orders	0
Potential changes	0

All values in SAR. No contract change orders are registered.

Invoices

Invoices in the log	3
Gross value	4,244,771
Advance payment recovery	−424,477
Deductions and penalties	−45,000
Approved by MODON PM	0
FIR value to date	4,244,771

Invoicing is 11.9% of the contract value against 82.22% physical progress. IPC-01 (2,317,493), IPC-02 (1,039,612) and IPC-03 (887,665, period 16–31 Oct 2026) are approved by the consultant; none is approved by the MODON PM.

Health, safety and quality

Safety Score 0.95

Safe man-hours (cumulative)	129,170
Man-hours this week	11,640
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	277 / 710

MODON HSE inspection no. 31 (05-Nov-2026): 18 items good practice, 5 need improvement, 0 fail.

Quality Score 0.91

FIRs issued / closed / pending	776 / 656 / 120
MIRs issued / closed / pending	99 / 77 / 22
NCRs issued / closed / pending	22 / 10 / 12
Site instructions issued / closed	7 / 6
Shop drawings approved (A+B) / total	333 / 445
Material approvals (A+B) / total	138 / 156

25 shop drawings and 6 material submittals are pending.

Open issues and risks

The issue log of the weekly report has one issue, now closed (Hail work permit, closed 19-Apr-2026). The items below come from the progress, quantity, schedule and risk sheets.

ISSUE	SITE	DETAIL
Air dome works	Qassim, Tabuk	Physical progress 39.96% (Qassim) and 35.13% (Tabuk) against 87.01% and 81.77% planned; no air dome man-hours were earned for the fourth week running, and the steel cable and membrane installation at both sites has failed to start. Air dome materials are 80% delivered.
Schedule slippage	All sites	Forecast handover moved from 07-Feb-2027 (18-Oct report) to 14-Feb, 23-Feb and now 02-Mar-2027. 176 of 284 open activities have negative float, 176 activities are on the critical path and 36 have failed to start (Qassim 14, Hail 6, Tabuk 16).
Landscaping and irrigation	All sites	Lawn not started against 12,539 m² planned to date; 25 mm irrigation pipe at 1,812 of 10,545 m planned. Landscape completion is forecast for 12-Jan-2027 (−23.0 days of float).
Playground surfaces	All sites	Football playground at 4,400 of 7,350 m² and tartan floor at 8,000 of 9,921 m² planned to date.
Procurement	All sites	25 of 57 purchase orders remain to be issued and 8 materials are on site; the curtain wall remainder is at 70–80%.
Soil investigation (risk register)	Tabuk	Open risk: borehole test results take 7–10 days from the laboratory, which may delay the start of excavation.

Data notes

- Progress figures are the weekly report's physical progress (effort), weighted by 33,340 budgeted man-hours. 10,000 of them (30%) sit on the time-based “Project Durations” activities (management line), which earn progress as time passes and stand at 86.43% (8,643 man-hours). Without them the project would be 80.42% complete against 88.34% planned, behind by 7.92% rather than 5.55%. The two air domes carry only 1,116 man-hours each (6.7% of all man-hours) although they are 23.4% of the contract value, so their stoppage hardly moves the physical %. By comparison, invoiced and FIR value to date are both 4,244,771 SAR, 11.9% of the contract value. This week's files do not change this; the report still shows the contractor's physical % as given. The report's dashboard shows cost-based progress labelled as actual; this report uses physical progress only.
- The report states “Current Contract Weeks: 0 of 0”, so the week number is counted from site handover (17-Feb-2026): 264 days, week 37.
- The “Weekly Physical Progress” columns hold 79.55% planned and 71.94% earned, which match neither week's to-date figures. Progress this week is taken as the change in to-date progress since the 01-Nov-2026 report.
- All major quantities are identical in the 18-Oct, 25-Oct, 01-Nov and 08-Nov-2026 reports, although interlock, tartan, curbstone and irrigation work was reported; the sheet appears not to have been updated.
- Man-hours by site: Tabuk toilet building still shows 0 of 1,708 man-hours earned with only 40 planned, and Tabuk closeout has no budget but 76.72 man-hours earned.
- The milestone sheet gives complete construction as 13-Feb-2026 with 0 days change, and complete mobilisation as 14-Apr-2026 against 18-Mar-2026 with 0 days change.
- Procurement: the summary has 8 of 57 materials on site, unchanged for three weeks, while the P6 delivery activities are 70–95% complete. The procurement log has no delivered quantities or dates.
- Invoices: the summary shows 0 submitted invoices while the log lists IPC-01 to IPC-03. Paid invoices (4,348,338 SAR) exceed the gross submitted value although none is PM-approved. The FIR summary total now equals the gross invoiced value exactly (it was 3,688,354 last week) and lists FIR-0630 twice. The dashboard's penalties of –469,477 combine advance payment recovery and deductions.
- Manpower and safety: the dashboard shows 46 manual workers while the Manpower sheet has 65 for November; the safety statistics give 10,000 safe man-hours this week against 11,640 man-hours worked, while both cumulative totals are 129,170. The DB sheet still holds another project's data (HAL1-02-005).
- The P6 update has a data date of 06-Nov-2026, against 08-Nov-2026 for the weekly report; 131 in-progress activities have a finish date before the data date. Three PDFs are named MLTX-05-047 although they belong to MLTX-02-003.
- The contractor forecast in the Physical-Chart Data sheet starts at 0 in February, 365 man-hours below the actual, so it stays slightly below actual until October.

Compiled 10-Nov-2026 from the weekly reports of 18 Oct to 08 Nov 2026 and the P6 update with data date 06-Nov-2026.
