Development of Infrastructure Networks, 3rd Industrial City in Dammam, Phase 2 Part 2, Zone J

تطوير شبكات البنية التحتية للمدينة الصناعية الثالثة بالدمام المرحلة الثانية الجزء الثاني - المنطقة J

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ANSAB General Contracting	EGIS	Eng. Mohammed Al-Aissa	12-Jan-2025	11-Jan-2027

Scope: collector and local roads, potable water, sewerage, storm drainage, irrigation, medium-voltage, street lighting and telecom networks, a sewage pump station and storm drainage ponds for Block J. Contract value 117.4M SAR excluding VAT, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted effort (man-days, as the updated report now measures it). At the 27-Oct-2026 data date the project is 78.5% complete against 86.6% planned, behind by 8.1% (SPI 0.91). The report states 0.92% gained this week. The updated workbook changed the progress basis, so these figures cannot be compared with report 92 (54.8% on a man-hour basis).

PHYSICAL % COMPLETE

78.5% / 86.6% plan

▼ SPI 0.91 −8.1%

PROGRESS THIS WEEK

+0.92% / +14.1% plan

? Weekly plan figure looks wrong

CONTRACT TIME ELAPSED

89.6% · day 653 of 729

▼ P6 finish 07-Sep-2027

INVOICED TO DATE (GROSS)

43.1% · 50.6M SAR

20 invoices, last period ends 30-Sep-2026

The updated weekly report now forecasts finishing only 7 days late, but the P6 update still shows almost eight months.

The updated weekly report forecasts completion on 18-Jan-2027, 7 days after the contract date of 11-Jan-2027, and brings every network milestone forward by four to six months. The P6 update uploaded with it (data date 27-Oct-2026) is unchanged and still finishes on 07-Sep-2027, 239 days late, with −195.5 days of float. No schedule file supports the new dates. With 89.6% of the contract time used, 21.5% of the physical work remains.

Site photos this week

The six new photos uploaded with report 94; they carry no visible date stamp. They show road formation compaction, waterproofing on the concrete walls of the lift station and fill handling. Select a photo to view it larger, then use the arrows to move between photos.



Road formation

Compacted formation, with a roller working further along.



Road formation compaction

Rollers working along the compacted formation.



Lift station wall waterproofing

Protection membrane fixed to the cast wall, with starter bars above.



Lift station walls

Waterproofed wall section with reinforcement for the next pour.



Pipe sleeve in the wall

GRP pipe sleeve cast into the waterproofed wall.




Fill handling

Wheel loader moving fill material.

Progress S-curve

Cumulative physical progress (effort weighted), monthly. Source: Physical-Chart Data sheet.

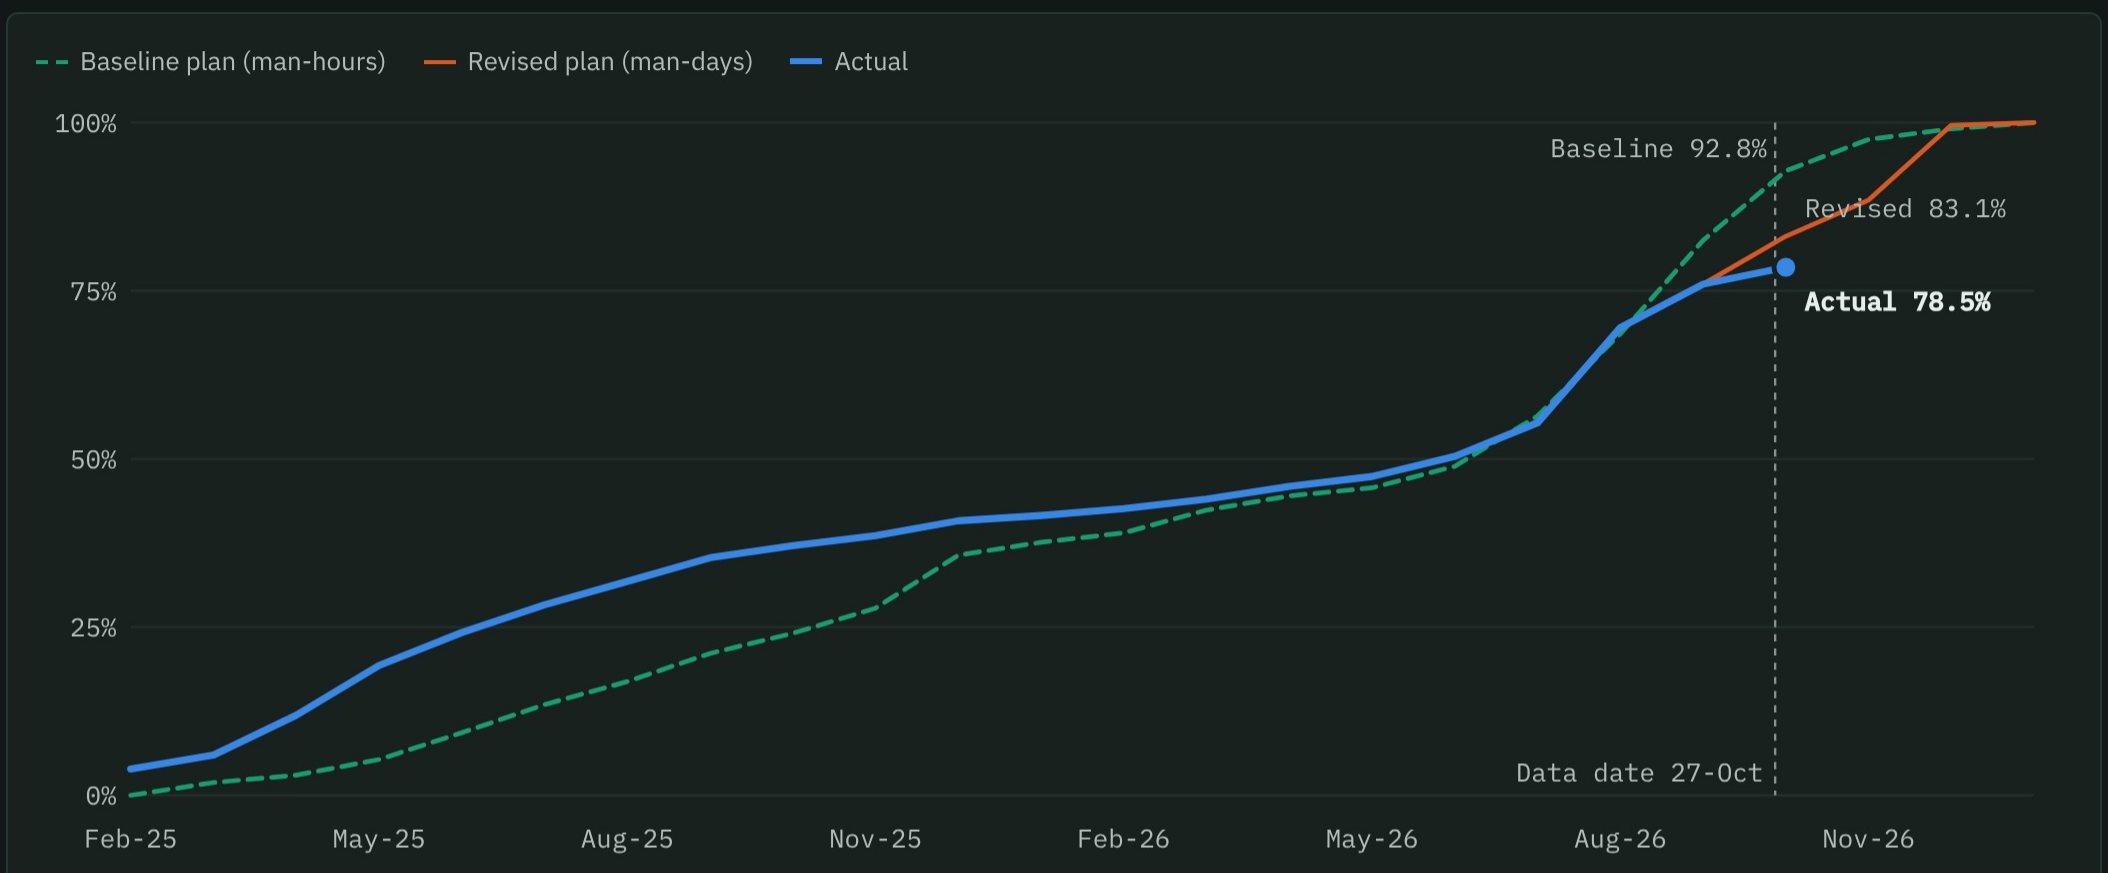

PERIOD ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED IN PERIOD	SPI
Jun-2026	50.4	50.4	0.0	+3.0	1.00
Jul-2026	55.4	55.4	0.0	+5.0	1.00
Aug-2026	69.5	69.5	0.0	+14.1	1.00
Sep-2026	76.0	76.0	0.0	+6.5	1.00
27-Oct-2026	**86.6***	**78.5**	**−8.1**	**+2.5**	**0.91**

Month-end values against the revised plan (man-days) from the Physical-Chart Data sheet. Up to September the sheet's actual equals the revised plan exactly, so SPI shows 1.00. * Planned value at the data date from the report cover; the revised plan for the end of October is 83.1%, lower than this. The original man-hour baseline called for 92.8% by the end of October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted effort (man-days). Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.3%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	2.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	20.3%	100.0%	95.4%	−4.6	0.95	▼ Behind
Earthworks network	6.7%	100.0%	100.0%	0.0	1.00	✓ Complete
Irrigation network	1.9%	99.9%	53.3%	−46.6	0.53	▼ Behind
Potable water network	2.9%	99.2%	68.4%	−30.9	0.69	▼ Behind
Medium-voltage network	1.6%	99.8%	94.3%	−5.5	0.94	▼ Behind
Street lighting network	3.7%	100.0%	9.2%	−90.8	0.09	▼ Behind
Telecom network	1.5%	100.0%	61.2%	−38.8	0.61	▼ Behind
Roads network	23.9%	84.6%	65.2%	−19.5	0.77	▼ Behind
Sewage network	12.6%	96.6%	86.8%	−9.8	0.90	▼ Behind
Storm drainage network	12.7%	98.4%	83.9%	−14.5	0.85	▼ Behind
Testing & commissioning	9.1%	0.0%	70.3%	+70.3	–	? No plan to date
Total	100%	**86.6%**	**78.5%**	**−8.1**	**0.91**	▼ Behind

The updated workbook measures effort in man-days (65,420 in total) and now includes mobilisation, engineering, procurement and testing, which the previous man-hour measure left out. This week 604.9 man-days were earned, mostly in roads (205), sewage (112), storm drainage (109) and earthworks (64). Testing and commissioning shows 70.3% earned with no planned value and no test started, which needs checking. The P6 update (data date 27-Oct-2026) has 1,921 activities: 1,227 completed, 64 in progress and 630 not started. Its scheduled finish is 07-Sep-2027, 239 days after the contract date.

Scope of work: quantities

Total, executed and remaining length of each network, from the execution summary in the Arabic progress summary sheet. "This week" is the change since the same sheet in the previous week's folder (report 92, 13-Oct-2026), so it covers 14 days.

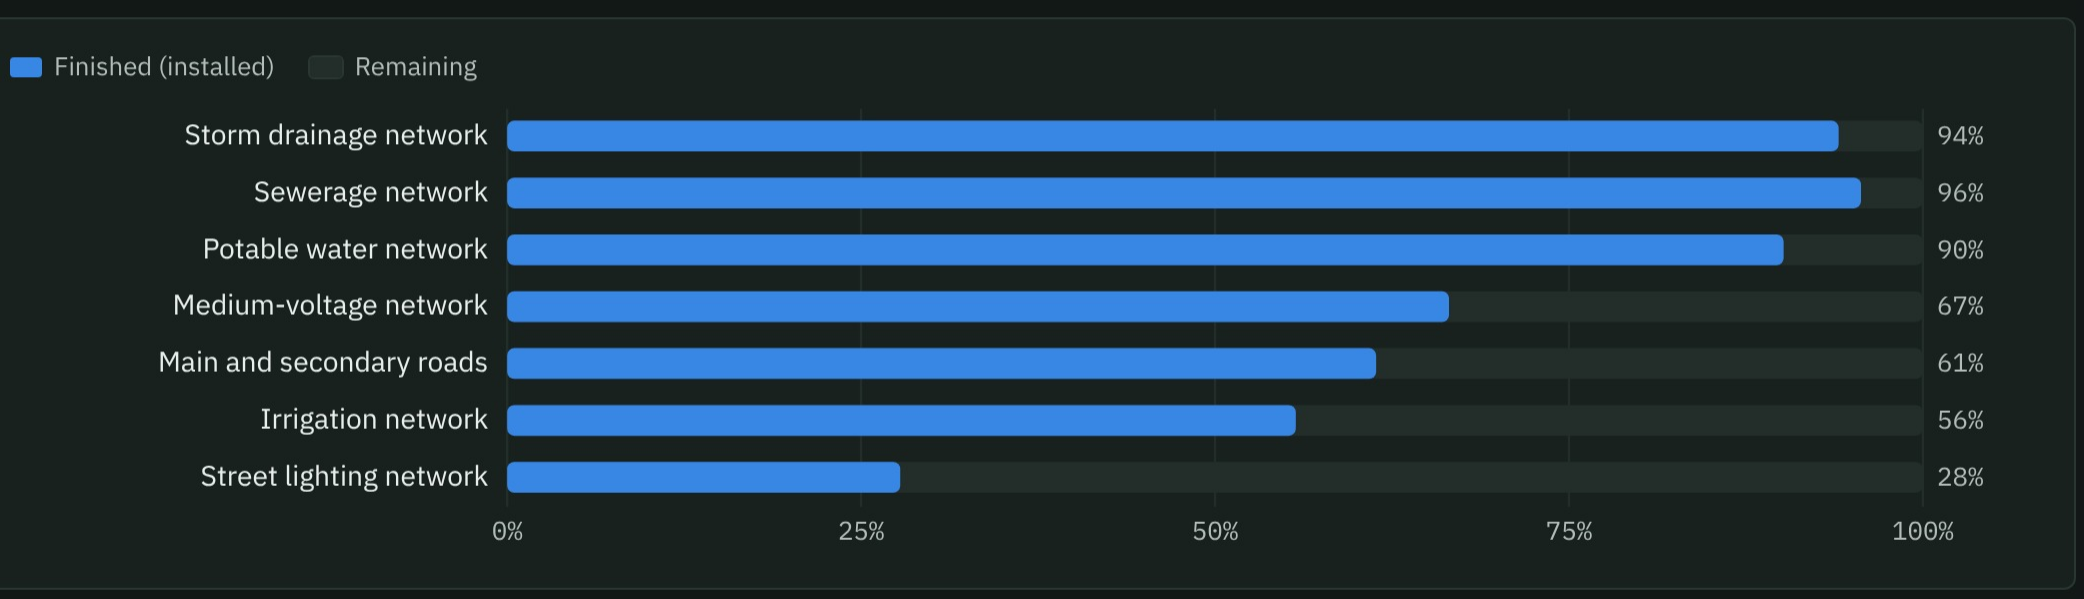

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Storm drainage network	Block J	LM	18,554	17,450	0	1,104	94.0%	–
Sewerage network	Block J	LM	9,152	8,752	0	400	95.6%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Potable water network	Block J	LM	12,200	11,000	+200	1,200	90.2%	–
Medium-voltage network	Block J	LM	17,328	11,528	+200	5,800	66.5%	–
Main and secondary roads	Block J	LM	8,146	5,000	0	3,146	61.4%	–
Irrigation network	Block J	LM	14,494	8,074	0	6,420	55.7%	–
Street lighting network	Block J	LM	12,786	3,550	0	9,236	27.8%	–

Work executed this week

NETWORK	ACTIVITY	UNIT	THIS WEEK	SOURCE
Potable water	Network executed (10,800 → 11,000)	LM	200	Summary sheet
Medium voltage	Network executed (11,328 → 11,528)	LM	200	Summary sheet
Roads	Physical progress earned	Man-days	205	Progress sheet
Sewerage	Physical progress earned	Man-days	112	Progress sheet
Storm drainage	Physical progress earned	Man-days	109	Progress sheet
Earthworks	Physical progress earned	Man-days	64	Progress sheet
Irrigation	Physical progress earned	Man-days	34	Progress sheet
Potable water	Physical progress earned	Man-days	30	Progress sheet
Sewage pump station	Wall pouring	–	–	Weekly activities sheet

The weekly activities sheet repeats the activity list of report 92 and its quantity table is empty this time. Planned next: complete the 630 mm water line, the 500 mm irrigation line and the 800 mm line, about 1,000 m of MV cable on street 9, road works on street 10 and asphalt on road 14.

Furthest behind

Street lighting is 27.8% executed (3,550 of 12,786 LM): no LED luminaires, earthing, road-crossing ducts or draw pits have been installed. Irrigation is 55.7% and roads 61.4%. Traffic markings, signs and fire hydrants (0 of 55) have not started.

Close to finished

Sewerage is 95.6% and storm drainage 94.1% executed by length, and potable water 90.2%. The storm box conduit (2,051 m) is complete. Catch basins remain at 207 of 505 and the storm drainage ponds and sewage pump station are still under construction.

Milestones

Baseline and forecast dates from the updated weekly report's milestone table, against the P6 update of 27-Oct-2026. Days in brackets are the delay the weekly report gives against the baseline.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	12-Jan-2025	12-Jan-2025	12-Jan-2025 (actual)	–	✓ Done
Complete mobilisation	12-Mar-2025	12-Mar-2025	09-Mar-2025 (actual)	–	✓ Done
Shop drawings and materials approved	10-Feb-2025	11-Feb-2025	24-May-2025 (actual)	–	✓ Done
Earthworks network	24-May-2026	31-May-2025	–	–	✓ Done
Telecom network	28-Sep-2026	27-Dec-2026 (+90 d)	18-Mar-2027	−165	▼ Late
Irrigation network	23-Aug-2026	24-Dec-2026 (+123 d)	11-May-2027	−163	▼ Late
Potable water network	05-Oct-2026	02-Jan-2027 (+89 d)	27-Jun-2027	−180	▼ Late
Sewage network	06-Oct-2026	31-Dec-2026 (+86 d)	21-Jun-2027	−184	▼ Late
Medium-voltage network	17-Oct-2026	29-Dec-2026 (+73 d)	07-Apr-2027	−134	▼ Late


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Road works	21-Oct-2026	05-Jan-2027 (+76 d)	24-Aug-2027	−195.5	▼ Late
Street lighting network	20-Dec-2026	12-Jan-2027 (+23 d)	30-Jun-2027	−212	▼ Late
Storm drainage network	–	29-Dec-2026	11-Jul-2027	−172	▼ Late
Storm drainage ponds	–	–	02-May-2027	−110	▼ Late
Sewage pump station	–	–	30-May-2027	−129	▼ Late
Tie-in to existing networks	–	–	24-Aug-2027	−192.5	▼ Late
Project completion	11-Jan-2027	18-Jan-2027 (+7 d)	07-Sep-2027	−195.5	▼ Late

The weekly report and the P6 update now disagree by almost eight months.

The updated weekly report forecasts completion on 18-Jan-2027 and every network between 24-Dec-2026 and 12-Jan-2027. The uploaded P6 update, unchanged, finishes the networks between 18-Mar and 24-Aug-2027 and the project on 07-Sep-2027. The weekly report's own schedule extract lists a programme ending 18-Jan-2027 that does not match the uploaded P6 file. A revised schedule must be submitted before the new dates can be accepted. The Employer's NOC for the medium-voltage network is still the only control milestone not achieved (P6: 22-Dec-2026, −46 days).

Procurement of key materials

Share of the required quantity delivered to site. Source: Procurement sheet, weekly report 27-Oct-2026, unchanged since report 92. All listed materials are approved.

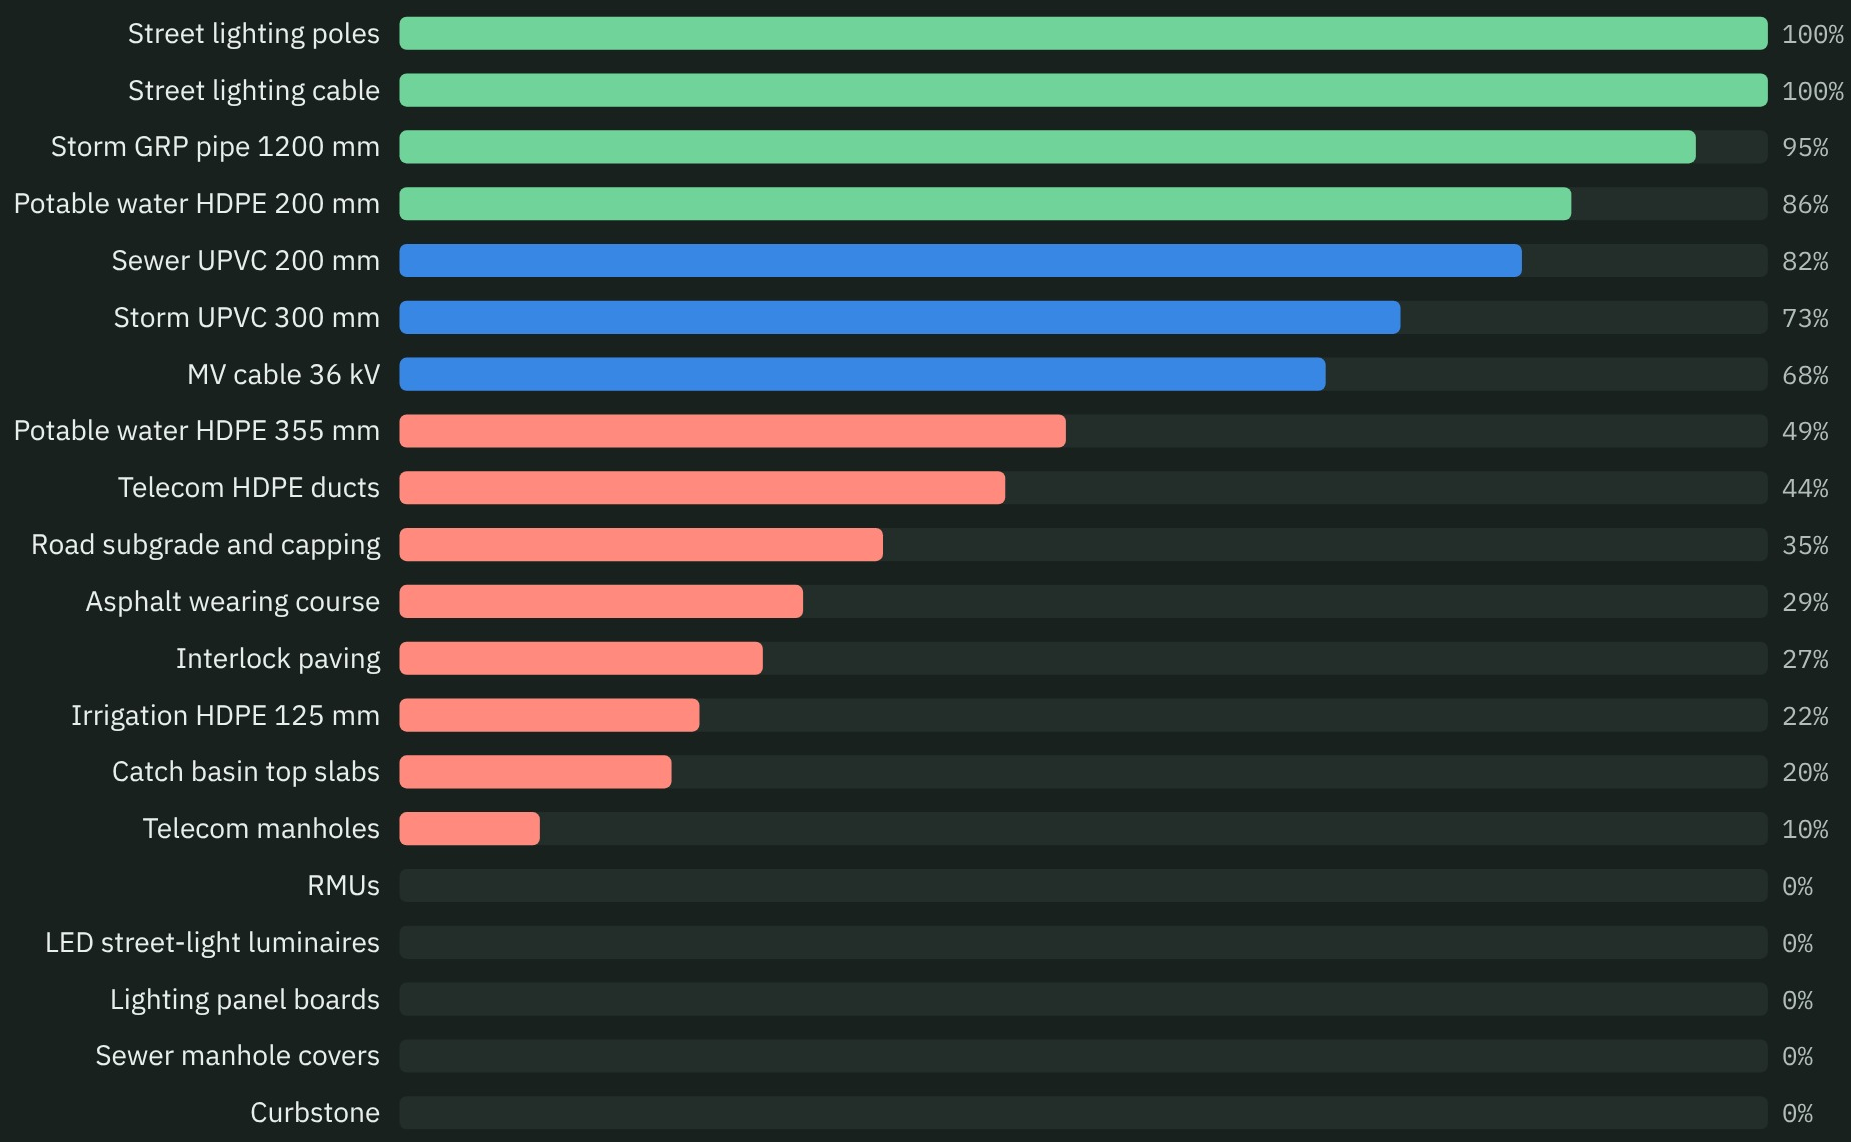

Nothing delivered yet for several items on the critical networks


RMUs (0 of 9), LED street-light luminaires (0 of 363), lighting panel boards (0 of 6), curbstone (0 of 42,552 pieces), sewer manhole covers (0 of 129) and storm covers and gratings. The register rates delay in long-lead materials as a high risk.

Telecom, irrigation and road layers lag

Telecom ducts are 44% delivered and telecom manholes 8 of 78. Irrigation 125 mm pipe is 22% delivered, catch-basin top slabs 20%, and road-layer materials (capping, subgrade, base course, asphalt, interlock) 17–35%. MV cable is at 8,378 of 12,378 m.

Manpower

Head count on site this month by trade, planned vs actual. Source: Manpower sheet. The report has no monthly history.

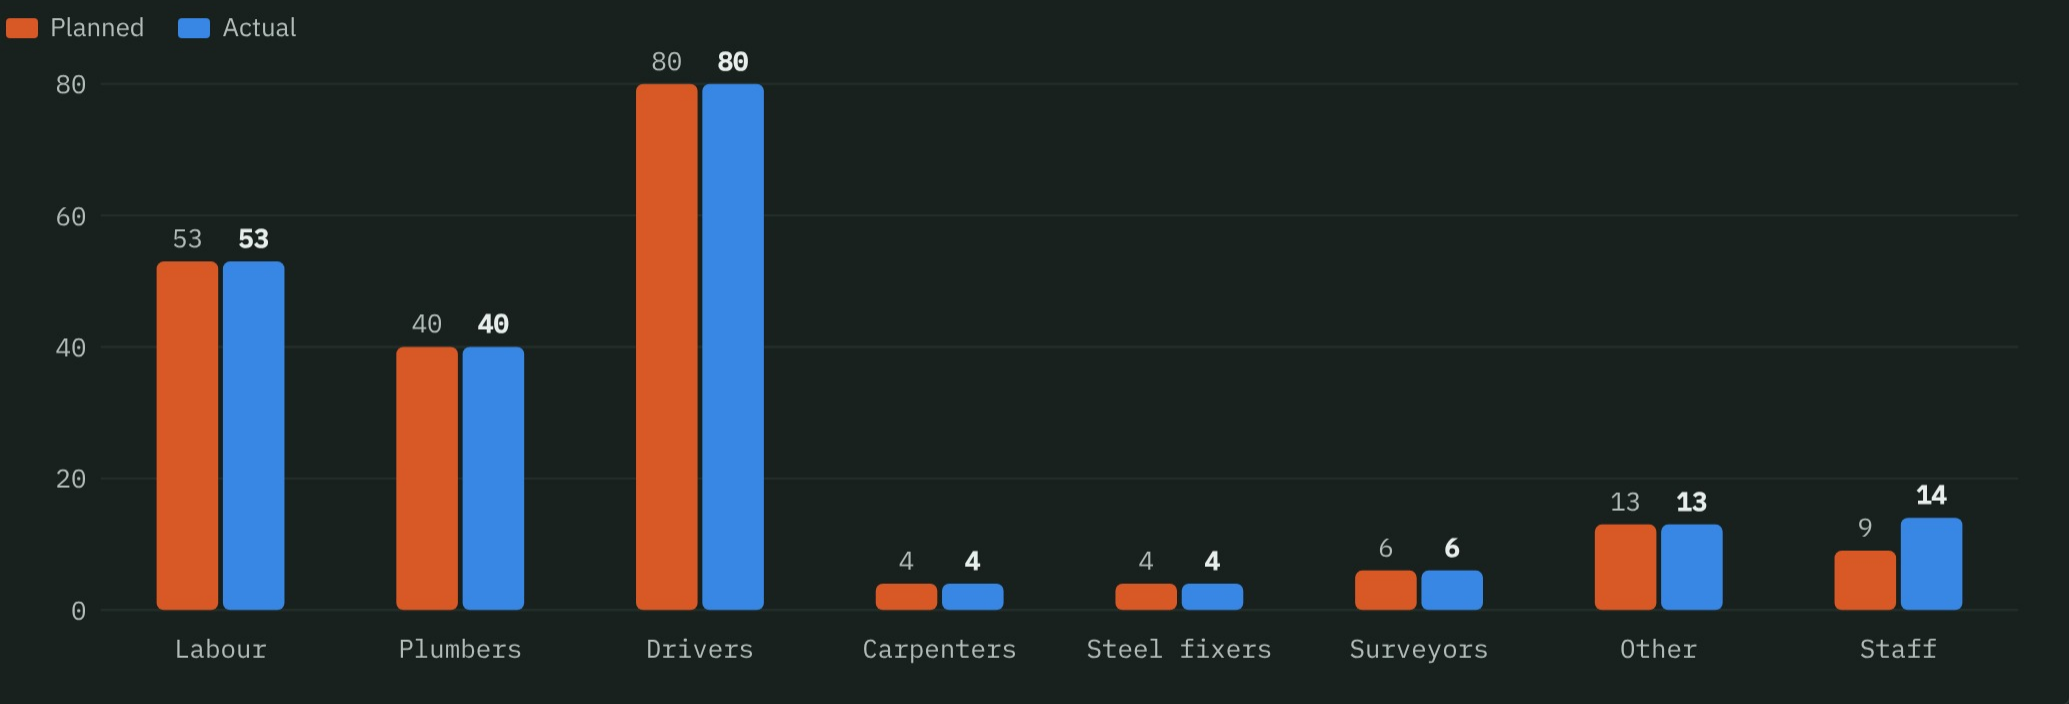

Total head count is 214 against 209 planned: 200 manual workers against 200 and 14 staff against 9. In the updated workbook every trade's plan equals its actual (for example carpenters and steel fixers 4 each, drivers and operators 80), so the trade plan no longer shows any shortfall. Equipment on site is 100 units against 78 planned.

Cost and invoicing

Contract value

Roads and paving	31,308,119
Storm water drainage	33,717,595
Sewerage and lift stations	24,177,287
Potable water	10,220,942
Irrigation	6,738,491
Street lighting and telecom	6,440,353
Medium voltage	4,788,987
BOQ total (excl. VAT)	**117,391,774**
Contract value incl. 15% VAT	135,000,540
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. The change order log is empty; the report lists one potential change.

Invoices

Advance payment (10%)	11,739,177
Progress invoices submitted	20
Gross value	50,649,221
Advance payment recovered	5,064,922
Retention / penalties	0 / 0
Approved by MODON PM	50,649,221
Paid (19 invoices)	43,414,468

Invoicing is 43.1% of the contract value against 78.5% physical progress. Invoice 19 is now recorded as paid. Invoice 20 (01-Sep to 30-Sep-2026, 7,234,753 SAR gross) is approved and awaiting payment.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	398,698
Man-hours this week	9,600
Lost-time injuries	0
Fatalities	0
First-aid cases	5
Near misses	1
Property damage	0
Inductions / toolbox talks	96 / 320
Consultant safety inspection, 27-Oct-2026	0.84

Cumulative figures. This week: 2 inductions and 6 toolbox talks.

Quality Score 0.90

FIRs issued (cumulative)	1,881
FIRs closed	1,791
FIRs pending (0–10 days)	90
NCRs issued / closed	21 / 21
Site instructions issued / closed	13 / 12
MIRs issued	0
Shop drawings submitted (all code B)	23
Material submittals (A / B / C / D)	1 / 72 / 2 / 1

NCRs close in 7 days on average. 7 material submittals are still to be approved.

Open issues and risks

ISSUE	OWNER	DETAIL
Schedule delay	Contractor	P6 forecasts completion on 07-Sep-2027, 239 days late; the updated weekly report says 18-Jan-2027 without a matching schedule file. Physical progress is 8.1% behind plan. The schedule statistics in the workbook (406 failed starts, 281 critical-path activities) repeat report 92's values. No recovery schedule approval is recorded.
Long-lead materials	Contractor	Risk 05, rated high and open: delays in long-lead materials could stop work. Mitigation: chase suppliers and get MODON approval for alternative sources. Target 20-Nov-2026.
Tie-in to existing networks	Contractor / MODON	Risk 01, rated low and open: existing infrastructure may not be ready for the tie-ins, delaying commissioning and handover. P6 tie-in milestone 24-Aug-2027, –192.5 days of float.
Testing and commissioning	Contractor	Testing was planned to start on 12-Oct-2026 (telecom), 18-Oct-2026 (irrigation) and 26-Oct-2026 (street lighting and medium voltage). None has started; the forecast starts run from 12-Nov-2026 to 04-Jan-2027.
MV network NOC	Contractor	The Employer's NOC for the medium-voltage network is still outstanding (P6: 22-Dec-2026, –46 days).

Closed in the registers: groundwater and dewatering (high), delayed or failed testing, and the two logged issues (irrigation connection point, pump-station force main). The BOQ re-measurement saving is recorded as a realised opportunity.

Data notes

Built from the updated report 94 workbook (W05 folder); the previous week's folder (report 92) was used only for this-week quantity changes.

- The updated workbook changed the progress measure from 43,571 budgeted man-hours (construction networks only) to 65,420 budgeted man-days, now including mobilisation, engineering, procurement and testing. Physical progress moved from 54.98% to 78.47% and the plan from 89.38% to 86.60% by this change of basis, not by work done.
- The updated weekly report forecasts completion on 18-Jan-2027 (7 days late; it was 07-Sep-2027, 239 days late, in the first version), and its network milestones moved four to six months earlier. The P6 file in the same folder is unchanged and still finishes on 07-Sep-2027.
- In the Physical-Chart Data sheet the earned effort up to September equals the revised plan month by month, and the cover's plan at the data date (86.60%) is higher than the revised plan for the end of October (83.11%).
- The weekly planned effort is 9,253 man-days in the Progress sheet and 9,189 on the cover (about 14% of the total in one week), which looks wrong. Earned this week is 604.9 man-days (0.92%).
- Testing and commissioning shows 4,173 man-days earned (70.3%) against no planned value, although the testing sheet shows no test started.

- The schedule statistics now repeat report 92's values (406 failed starts against 411 last week; 245 ahead, 123 on time, 367 behind), and critical-path activities changed from 674 to 281, while the P6 file is unchanged.
- Manpower: every trade's plan now equals its actual, the manual plan is 200 (130 in the first version) and the equipment plan 78 (11). The cover's trade total is 120 against 200 manual workers, and the next-month forecast is still 1,148.
- On the report cover the progress by WBS is still shifted by one row; the figures were taken from the Progress sheet. The Arabic summary sheet still labels cost-based figures as planned and actual "progress"; this report uses physical progress only.
- Report 93 was not uploaded, so the quantity changes against the previous week's folder (report 92) cover 14 days. The weekly activities sheet still repeats report 92's list with an empty quantity table, and the Major Quantities sheet and procurement log are unchanged since report 92.
- Week 93 is the contract week stated in the report's milestone sheet ("93 of 104"), matching 12-Jan-2025 to 27-Oct-2026 = 653 days; the workbook is numbered report 94.
- The summary sheet gives site handover as 12-Feb-2025 (12-Jan-2025 in the weekly report); storm drainage is 33,717,565 SAR there and 33,717,595 SAR in the invoice; the earthworks milestone baseline (24-May-2026) is later than its actual finish (31-May-2025).
- The procurement log still has deliveries above the required quantity (sewer GRP 400 mm SN5000 1,060 of 261 m) and unit typos ("m132", "m133"). The HSE inspection sheet still covers 26-Aug to 01-Sep-2026.
- The P6 file's project ID is MOD3-J-1 (MOD3-J-2 in the 20-Oct-2026 update), and the failed-start list is still named 20-10-2026.
- Several cover fields show #REF ! (EAC, top issues), and the invoice log still has stray values of 21,100,000 and 20,900,000.
- Photos: the six photos uploaded with report 94 are unchanged; they have no visible date stamp.

Compiled 02-Nov-2026 from the updated weekly report 94 workbook and the P6 update, both with data date 27-Oct-2026.
