Infrastructure Networks for the 1 km² Logistics Zone, 2nd Industrial City, Dammam

شبكات البنية التحتية للمنطقة اللوجستية لمساحة 1 كم مربع بالمدينة الصناعية الثانية بالدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Shibh Aljazira Contracting Company	Egis	Muhammad H Al-Essa	30-Jul-2025	29-Jan-2027

Scope: phase 1 of the logistics area. Wet networks (sewerage, storm, potable water, fire fighting and TSE, including the force main), dry networks (medium voltage, low voltage, street lighting and telecom), the potable water pump station, the sewage lift station, guard rooms, all road layers up to the asphalt wearing course, and landscape.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 27-Oct-2026 data date the project is 60.7% complete against 76.0% planned, 15.3% behind the plan (SPI 0.80). It gained 2.8% this week against 4.9% planned, so the gap widened from 13.2% to 15.3%.

PHYSICAL % COMPLETE

60.7% / 76.0% plan

▼ SPI 0.80 −15.3%

PROGRESS THIS WEEK

+2.8% / +4.9% plan

▼ 2.1% below the weekly plan

CONTRACT TIME ELAPSED

82.8% · day 454 of 548

▼ Forecast handover 08-Mar-2027

INVOICED TO DATE (GROSS)

31.6% · 62.9M SAR

7 invoices, last period ends 15-Sep-2026

With 82.8% of the contract time gone, 39.3% of the work remains.

Finishing by the contract completion date of 29-Jan-2027 needs about 3.0% a week over the 13 whole weeks left, against 2.8% achieved this week. The weekly report's milestone sheet and the P6 update now forecast project handover on 08-Mar-2027, 38 days late, a week later than last week's forecast. Construction is the weak phase: 50.0% done against 78.2% planned.

Site photos this week

Six site photos uploaded with the 27-Oct-2026 weekly report, camera-stamped 22 to 25 Oct 2026 where the stamp is visible. Road layers, pipe laying, waterproofing and the structures are shown. Select a photo to view it larger, then use the arrows to move between photos.




Prime coat spraying

Bitumen distributor on the road base. Camera-stamped 24-Oct-2026, 16:32, Dammam.



Asphalt core testing

Core drilling on the new asphalt layer. Camera-stamped 22-Oct-2026, 09:19, Dammam.

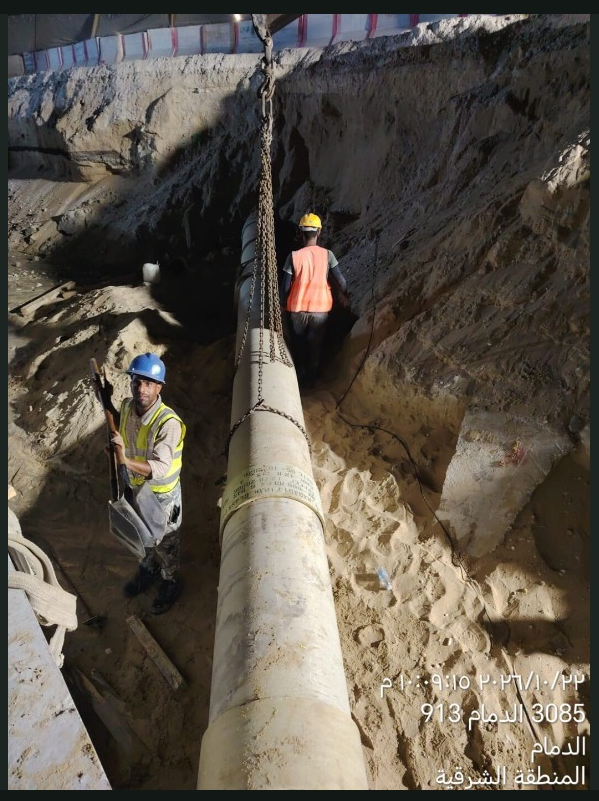

Pipe laying in deep trench

A large pipe being lowered and aligned. Camera-stamped 22-Oct-2026, 21:15, Dammam.



Waterproofing

Bitumen coating on a buried concrete structure. Camera-stamped 25-Oct-2026, 07:44, Dammam.



Station slab reinforcement

Steel mesh fixed inside the concrete walls. No date stamp.




Blockwork wall

Block wall built between columns in formwork. No date stamp.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values. Source: Physical-Chart Data sheet. The October actual is the 27-Oct value.

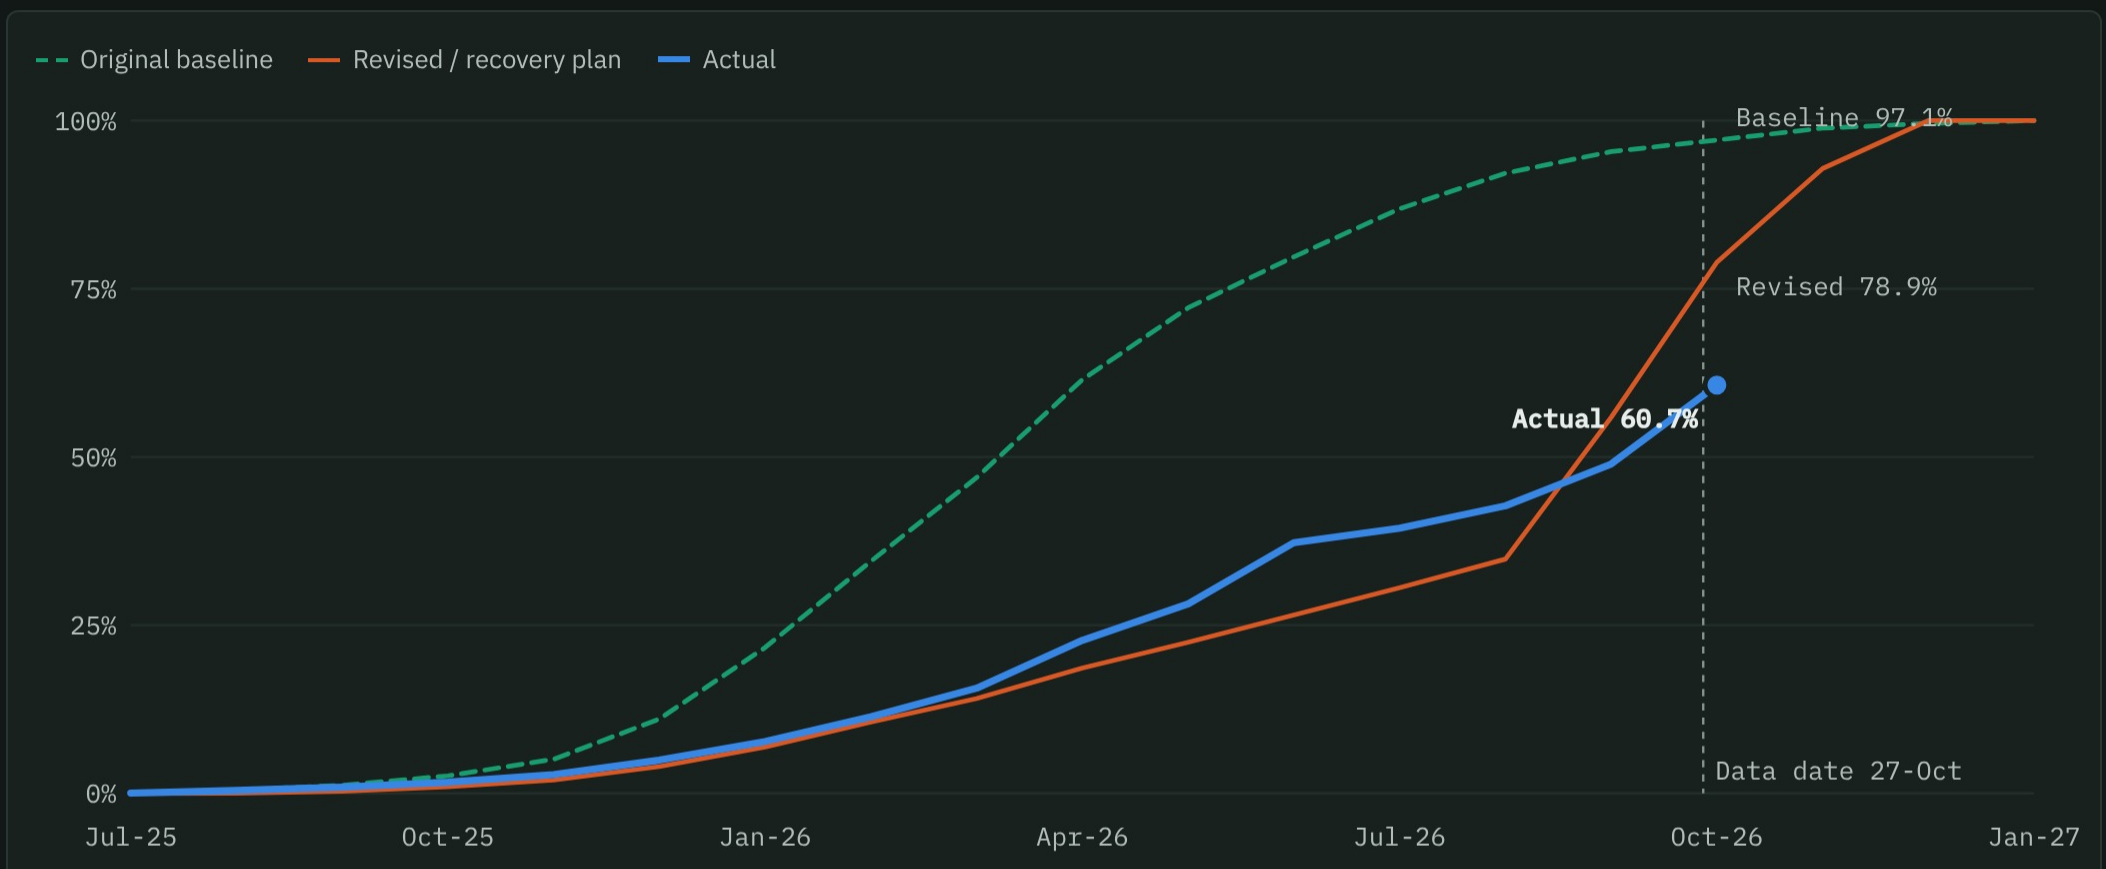

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026*	65.6	55.8	−9.7	—	0.85
20-Oct-2026	71.1	57.9	−13.2	+2.1	0.81
27-Oct-2026	**76.0**	**60.7**	**−15.3**	**+2.8**	**0.80**

Weekly values from the 20-Oct and 27-Oct weekly reports. * The 13-Oct row is derived from the 20-Oct report: to-date values minus that week's values. This week's report restates some monthly actuals (September 2026: 48.9%, previously 49.7%). The contractor's forecast reaches 81.8% by the end of November and 100% in January 2027.

Progress by phase

Physical progress to date by phase, weighted by budgeted man-hours, summed over all networks from the Progress sheet.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & earthworks	2.9%	100.0%	96.7%	-3.3	0.97	▼ Slightly behind
Engineering	3.0%	100.0%	97.3%	-2.7	0.97	▼ Slightly behind
Procurement	27.0%	94.3%	92.7%	-1.6	0.98	▼ Slightly behind
Construction	57.1%	78.2%	50.0%	-28.2	0.64	▼ Behind
Testing & commissioning	10.0%	0.0%	14.1%	+14.1	–	▲ Started early
Total	100%	**76.0%**	**60.7%**	**-15.3**	**0.80**	▼ Behind

NETWORK / WORK PACKAGE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & site clearing	0.4%	100.0%	100.0%	0.0	1.00	✓ Complete
Earthworks & site grading	2.5%	100.0%	96.2%	-3.8	0.96	▼ Slightly behind
Sewerage network	8.1%	86.4%	85.9%	-0.4	1.00	▲ On track
Storm water network	15.6%	89.7%	84.4%	-5.4	0.94	▼ Slightly behind
Potable water network	6.3%	81.0%	62.4%	-18.6	0.77	▼ Behind
Fire fighting network	6.9%	76.0%	58.6%	-17.4	0.77	▼ Behind
TSE network	5.2%	67.2%	45.2%	-22.0	0.67	▼ Behind
Potable water pump station	7.8%	81.3%	68.0%	-13.2	0.84	▼ Behind
Sewage lift station	7.7%	86.5%	70.1%	-16.4	0.81	▼ Behind
Medium-voltage network	3.7%	75.3%	46.9%	-28.5	0.62	▼ Behind
Low-voltage network	3.4%	68.9%	35.5%	-33.4	0.51	▼ Behind
Street lighting network	8.3%	54.1%	38.1%	-16.0	0.70	▼ Behind
Telecom network	6.8%	67.6%	48.1%	-19.6	0.71	▼ Behind
Road works	8.7%	70.0%	34.4%	-35.7	0.49	▼ Behind
Landscape	4.9%	31.4%	31.6%	+0.1	1.00	▲ On track
Guard rooms	3.7%	92.2%	76.9%	-15.3	0.83	▼ Behind
Total	100%	**76.0%**	**60.7%**	**-15.3**	**0.80**	▼ Behind

Weights are budgeted man-hours. This week no man-hours were earned on the TSE, MV and LV networks, road works, the pump station or landscape. The P6 update (data date 27-Oct-2026) has 4,851 activities: 2,667 completed, 400 in progress and 1,784 not started. Failed-start activities rose from 1,047 to 1,092.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 27-Oct-2026 weekly report. The sheet gives whole-site totals only, with no zones and no backfill figures. "This week" is the change since the 20-Oct-2026 report.

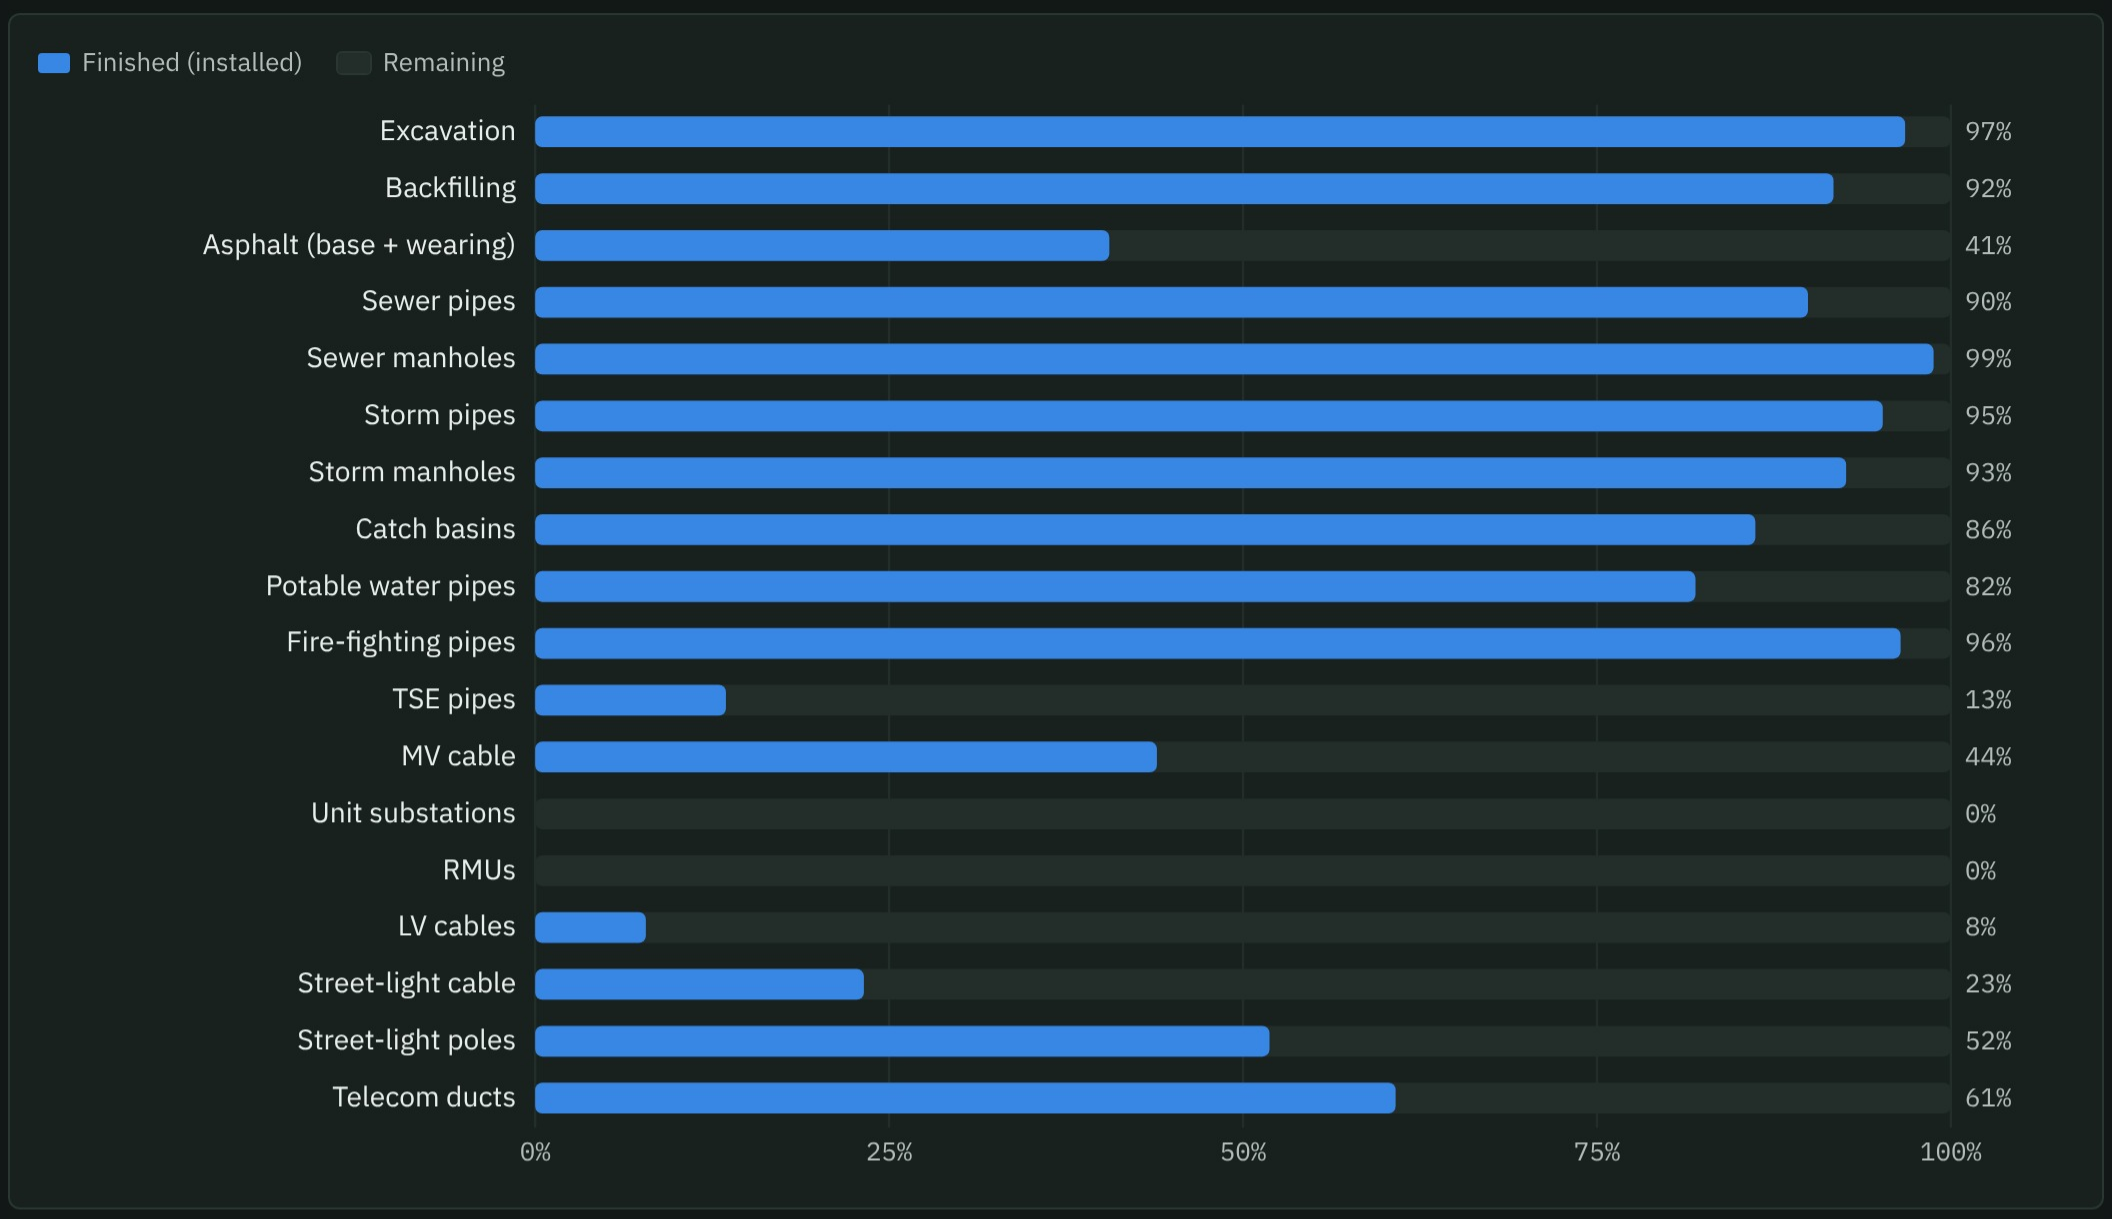

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All	m³	853,395	825,821	0	27,574	96.8%	–
Backfilling	All	m³	1,481,028	1,358,225	+2,184	122,803	91.7%	–
Asphalt (base + wearing)	All	m³	64,334	26,091	+235.3	38,243	40.6%	–
Sewer pipes	All	LM	7,567	6,803	+29.4	763.9	89.9%	–
Sewer manholes	All	EA	136	134.3	+3.1	1.7	98.8%	–
Storm pipes	All	LM	14,821	14,108	+194.2	713	95.2%	–
Storm manholes	All	EA	160	148.2	+2.1	11.8	92.6%	–
Catch basins	All	EA	338	291.3	+10.9	46.7	86.2%	–
Potable water pipes	All	LM	7,214	5,913	+235.2	1,301	82.0%	–
Fire-fighting pipes	All	LM	6,355	6,129	+378.3	225.7	96.4%	–
TSE pipes	All	LM	57,419	7,737	0	49,682	13.5%	–
MV cable	All	LM	12,559	5,516	+390.8	7,043	43.9%	–
Unit substations	All	EA	3	0	0	3	0.0%	–
RMUs	All	EA	3	0	0	3	0.0%	–
LV cables	All	LM	14,370	1,124	+440.1	13,246	7.8%	–
Street-light cable	All	LM	21,525	4,998	+1,791	16,527	23.2%	–
Street-light poles	All	EA	565	293.1	+45.8	271.9	51.9%	–
Telecom ducts	All	LM	11,057	6,720	+4,362	4,337	60.8%	–

Telecom ducts and wet networks moved most

Telecom ducts rose by 4,362 LM to 60.8%, street-light cable by 1,791 LM to 23.2%, and fire-fighting pipes by 378 LM to 96.4%. Storm pipes are 95.2% installed, sewer pipes 89.9% and potable water pipes 82.0%.

TSE, LV and asphalt are far behind

Asphalt is 26,091 m³ against 57,014 m³ planned to date (40.6% of the total), with only 235 m³ added this week. TSE pipes are unchanged at 13.5% and LV cables are at 7.8%. None of the 3 unit substations or 3 RMUs is installed.

Milestones

Baseline and forecast from the weekly report's Milestones sheet; P6 dates and total float from the P6 update with data date 27-Oct-2026.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	30-Jul-2025	30-Jul-2025	30-Jul-2025 (actual)	–	✓ Done
Complete mobilisation	30-Aug-2025	30-Aug-2025	25-Nov-2025 (actual)	–	✓ Done
Complete earthworks	15-Sep-2026	01-Sep-2026 (−14 d)	–	–	? Forecast date passed
Submittals and long-lead orders complete	24-Sep-2026	31-Oct-2026 (+37 d)	–	–	▼ Late
All equipment and materials delivered	03-Dec-2026	31-Oct-2026 (−33 d)	–	–	? Conflicts with procurement
All wet networks	22-Nov-2026	24-Dec-2026 (+32 d)	24-Dec-2026	63	▼ Late
Electrical works	24-Nov-2026	14-Dec-2026 (+20 d)	06-Jan-2027	53	▼ Late
Potable water pump station	–	–	09-Dec-2026	26	● Scheduled
Sewage lift station	–	–	22-Dec-2026	40	● Scheduled
Road works and asphalt wearing course	–	–	29-Dec-2026	5	▼ At risk
Construction finish	–	–	14-Jan-2027	11	▼ At risk
All works complete, ready for initial handover	14-Jan-2027	21-Feb-2027 (+38 d)	–	–	▼ Late
Complete demobilisation	25-Jan-2027	03-Mar-2027 (+37 d)	–	–	▼ Late
Project handover	29-Jan-2027	08-Mar-2027 (+38 d)	08-Mar-2027	0	▼ Late

The P6 update finishes the project on 08-Mar-2027, 38 days after the contract completion date.

Every P6 milestone except telecom moved 7 days later, the same as the data date, so the update shows no recovery. The schedule has no finish constraint at the contract date, so its float is measured against its own late finish. The asphalt wearing course has only 5 days of float and construction finish 11 days. Other forecasts in this week's files: 21-Feb-2027 (General Information sheet), 20-Dec-2026 (recovery schedule in the progress presentation) and 30-Nov-2026 (look-ahead sheet).

Procurement of key materials

Share of each long-lead item delivered to site. Source: weekly procurement update 27-Oct-2026. By discipline (Quality-Stat sheet), 114 of 155 materials are on site: civil and roads 61 of 77, electrical 22 of 30, mechanical 31 of 48.

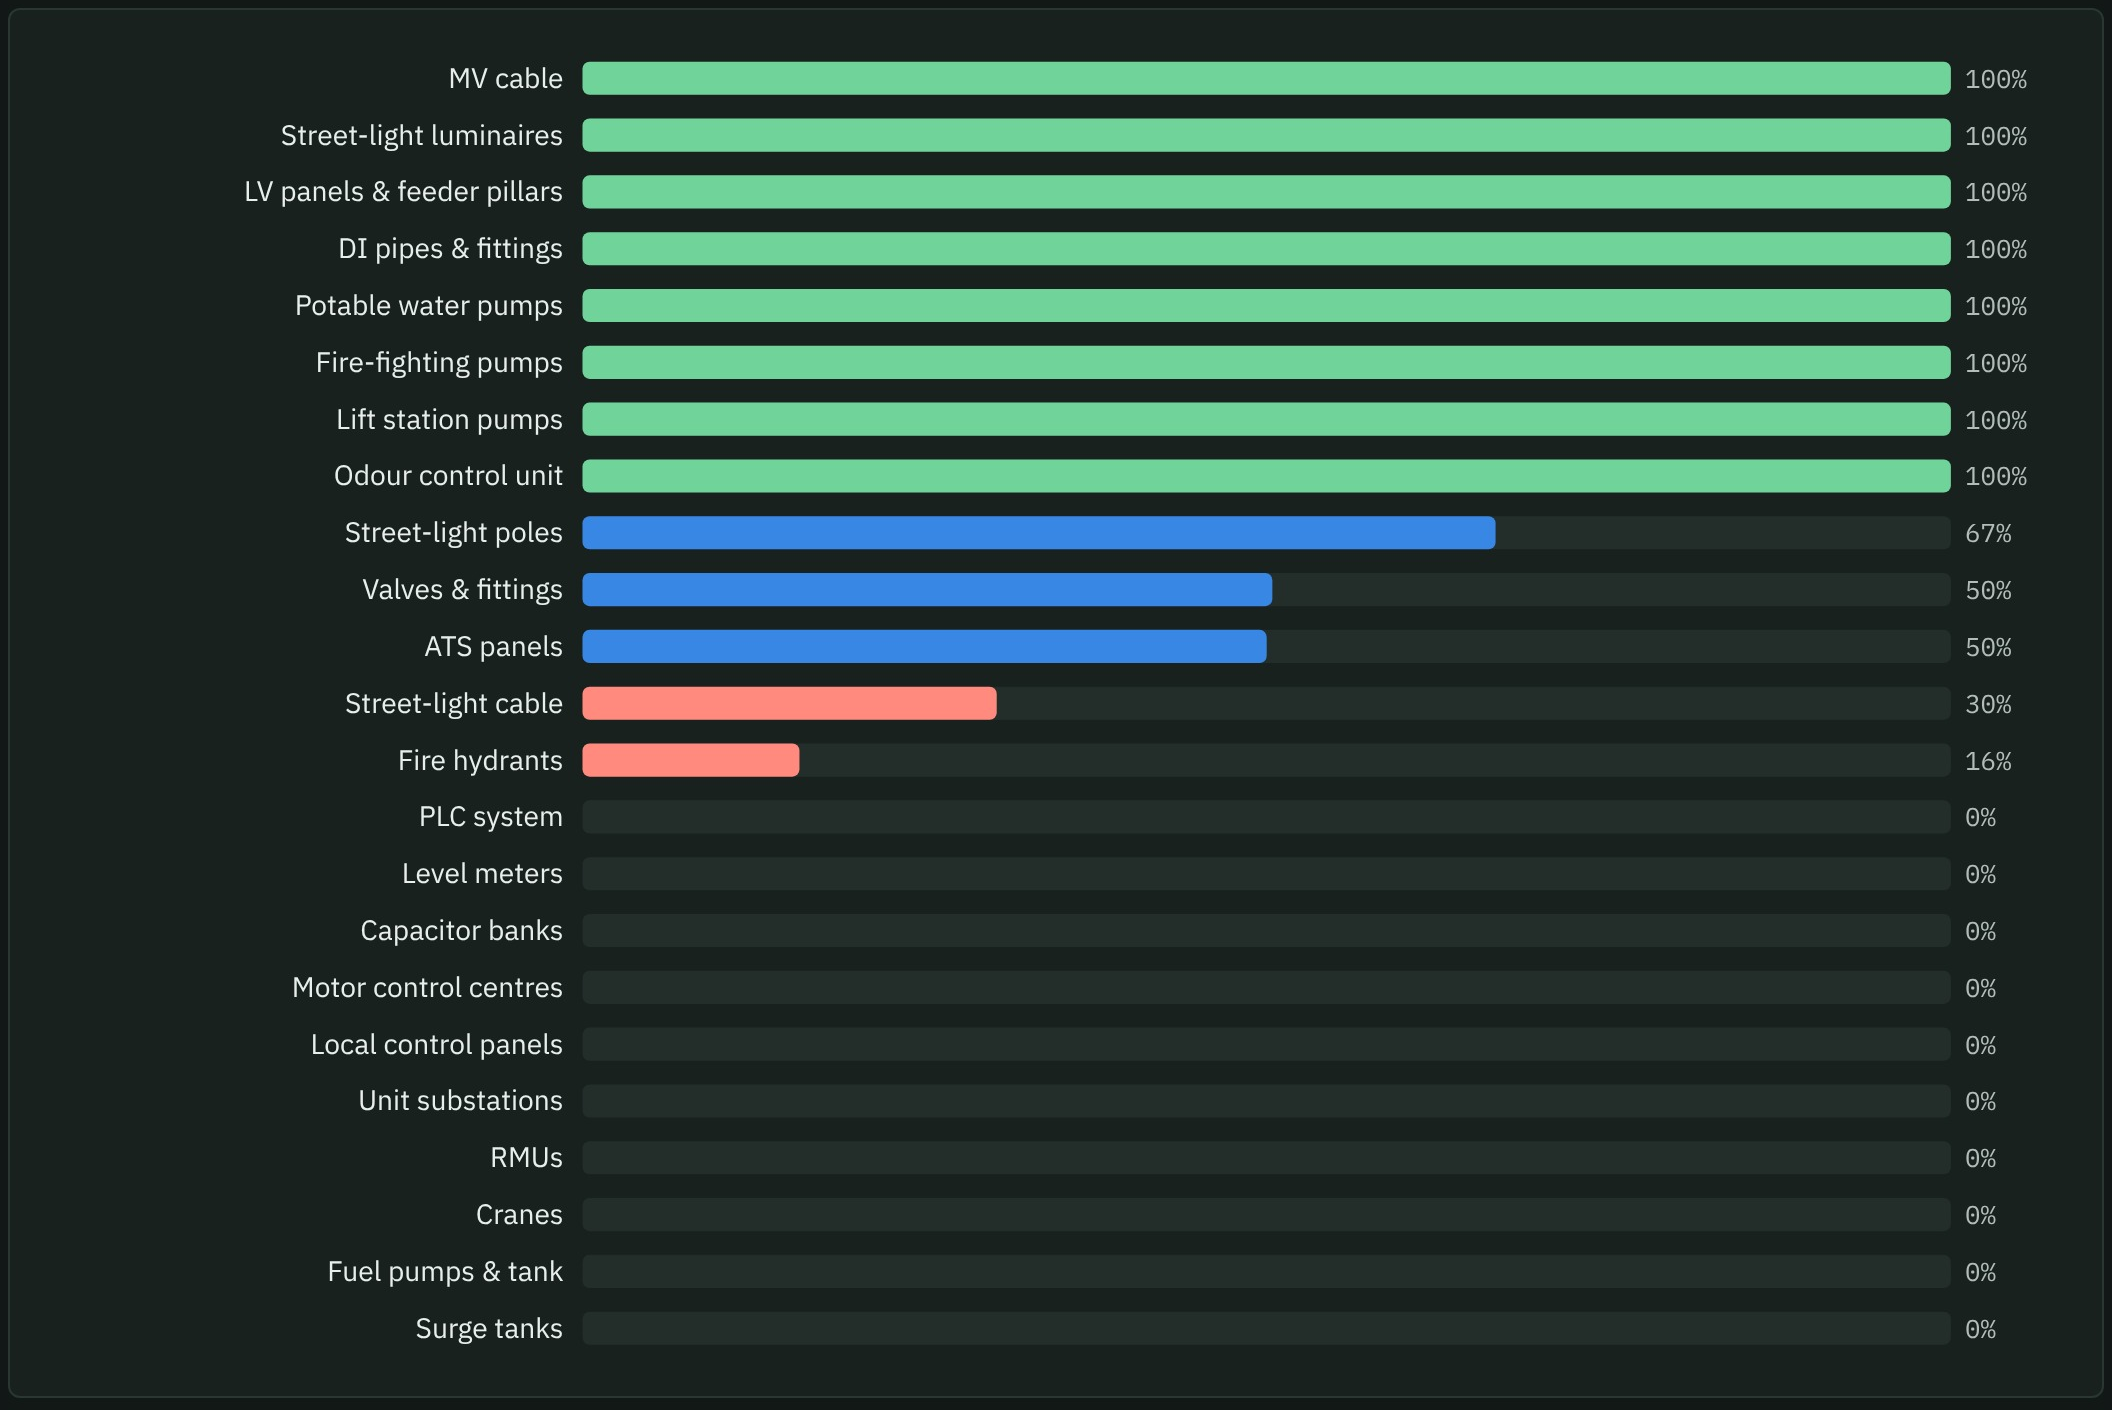

Substations, RMUs and station panels not delivered


None of the 3 unit substations or 5 RMUs is on site; both were due by 30-Oct-2026, "within 2 weeks of payment". The capacitor banks, MCCs and local control panels are due by 11-Nov-2026, and the PLC system and level meters by 19-Nov-2026. Planned delivery completion for electrical and mechanical materials was 27 and 28 Sep 2026.

Fire hydrants, valves and street-light cable

Only 13 of 82 fire hydrants are delivered, although the delivery date was 07-Jul-2026. Valves are at 61 of 121 and street-light cable at 6,054 of 20,000 LM, both due by 15-Nov-2026. The 3 surge tanks and the 2 cranes are due by 15 and 20 Nov 2026.

Manpower

Monthly head count on site (staff plus labour), planned vs actual. Source: Manpower sheet.

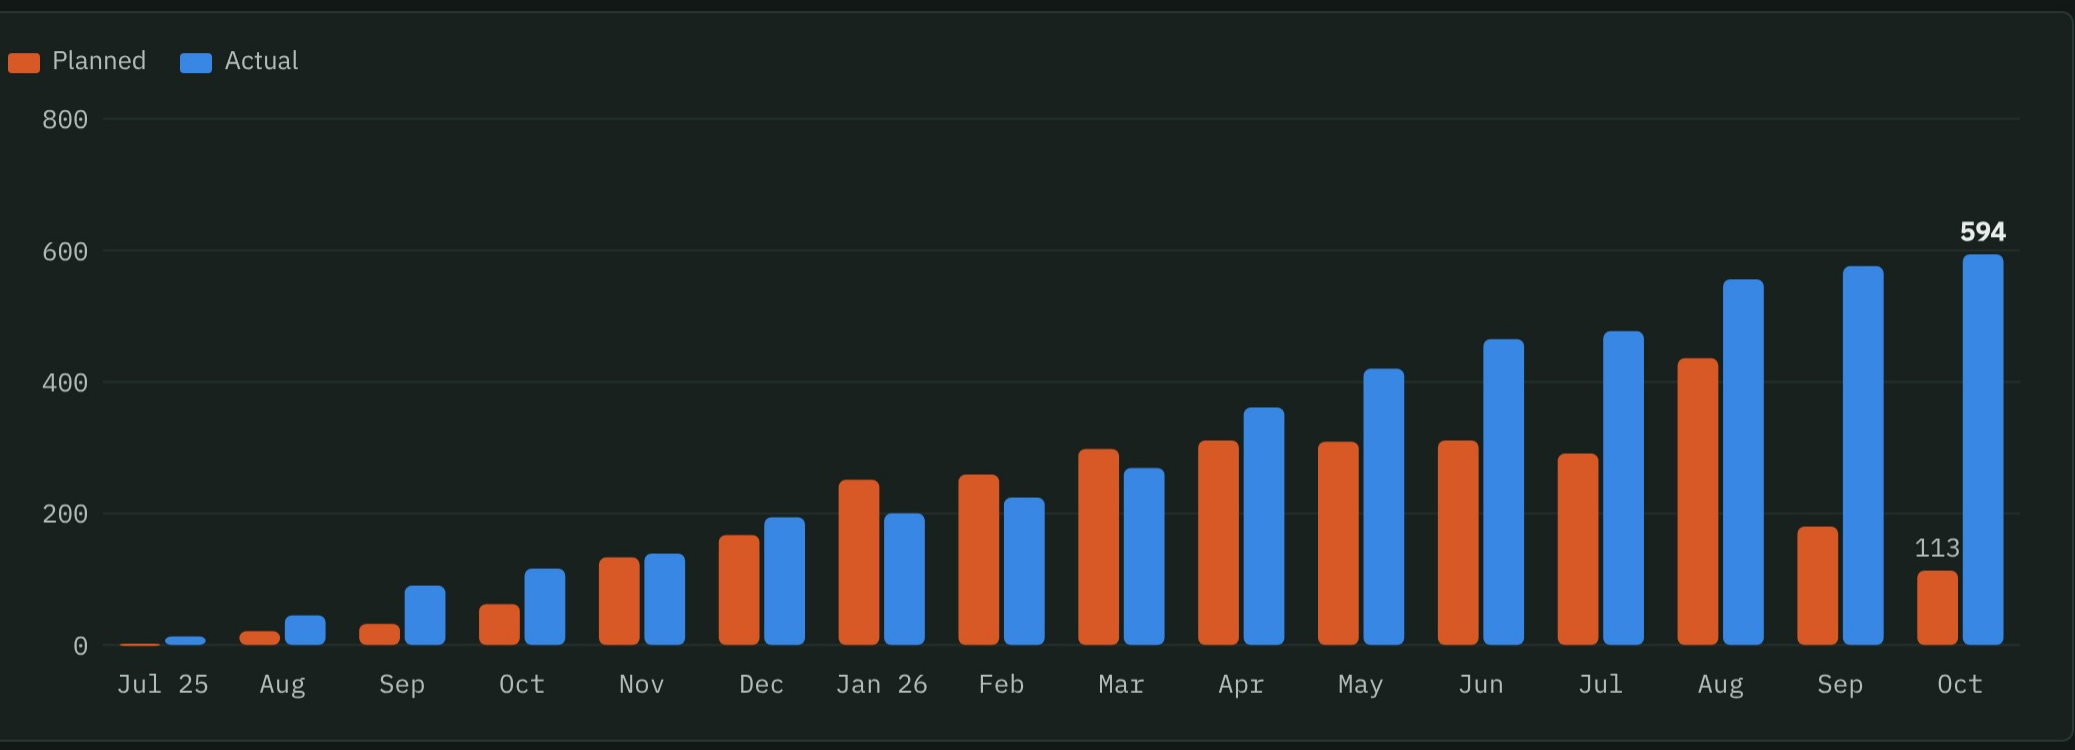

October head count is 594 (57 staff and 537 labour) against 113 planned, unchanged from last week. The manpower plan peaked at 436 in August 2026 and is falling while the work is behind, so it no longer reflects the work left. The contractor forecasts 675 for November. Equipment on site is 328 against 166 planned.

Cost and invoicing

Contract value

Original contract value	198,906,162.61
Revised contract value	198,906,162.61
Change orders	0

All values in SAR. The change order log is empty and potential changes are 0.

Invoices

Invoices submitted	7
Gross value	62,889,673.53
Deductions and penalties	−104,500
Net incl. VAT	72,218,624.56
Approved by consultant (CM)	7
Approved by MODON PM / paid	0 / 0

Invoicing is 31.6% of the contract value against 60.7% physical progress. No new invoice was submitted this week. All seven invoices are approved by the consultant, but none is recorded as approved by the MODON PM or paid. The payment status needs confirming.

Health, safety and quality

Safety Score 0.93

Safe man-hours (cumulative)	909,462
Man-hours this week	34,740
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions (cumulative)	148 (895)
Toolbox talks (cumulative)	57 (9,091)

Consultant HSE inspection of 27-Oct-2026. Bracketed figures are as given in the report.

Quality Score 0.93

FIRs issued / closed / pending	4,914 / 4,687 / 227
MIRs issued / closed / pending	120 / 117 / 3
Site instructions issued / closed	52 / 42
NCRs issued / closed	51 / 50
Shop drawings approved	1,774 of 1,774
Materials approved	140 of 155

Consultant quality inspection of 27-Oct-2026. This week 215 FIRs and 4 MIRs were added. The front page of the report shows 4 NCRs issued and 3 closed; see Data notes.

Open issues and risks

ISSUE	OWNER	DETAIL
Shortage of labour and equipment; subcontractor stopped work	Contractor	Part of the project was assigned to another contractor and the company is providing its own labour; the progress presentation gives 537 workers, 304 items of equipment and 24 dewatering pumps on site. Labour and equipment must keep increasing to meet MODON's targets. Open since 01-Apr-2026 (209 days).
Culvert on the arterial road delayed	Contractor	The roof slabs of 32 joints are cast and the last joint is excavated. The work now waits for SEC to approve the proposal for protecting the existing cable. Open since 01-Jun-2026 (148 days).
Networks must be finished before road works	Other	The subcontractor Unasco was removed and its approval withdrawn for not meeting MODON's targets. The contractor is working on the networks directly; its target to finish them by 19-Sep-2026 has passed. Open since 01-Jun-2026 (148 days).

The risk register lists the same three items, all open and rated high likelihood and high impact after treatment.

Data notes

- Report week: the weekly report states "Current Contract Weeks: 65 of 78" (Milestones sheet). The report serial number (WPR 047) and the consultant's inspection number (47) are not the week number.
- This-week values compare this report with the 20-Oct-2026 report (previous week folder). The 13-Oct S-curve row is derived from the 20-Oct report.
- Four different completion forecasts: 21-Feb-2027 (General Information sheet, −23 days), 08-Mar-2027 (Milestones sheet and P6 update, −38 days), 20-Dec-2026 (recovery schedule in the progress presentation) and 30-Nov-2026 (look-ahead sheet and the presentation's "target" date).
- The P6 update has no finish constraint, so no activity shows negative float although it finishes after the contract date. All milestones except telecom moved 7 days, the same as the data date. 215 in-progress activities have finish dates before the data date.
- This week's Physical-Chart Data sheet lowers earlier monthly actuals (May 28.9% to 28.2%, July 40.1% to 39.4%, September 49.7% to 48.9%).
- Quantities and man-hours disagree this week: Major Quantities adds 391 LM of MV cable, 440 LM of LV cable and 235 m³ of asphalt, but the MV, LV and road works packages earned no man-hours.
- Mobilisation: the weekly report gives 30-Aug-2025 as actual, the P6 milestone "Mobilization - Finish" gives 25-Nov-2025.
- The "Complete earthworks" forecast of 01-Sep-2026 has passed but is still marked as a forecast, with earthworks at 96.2%. The "all materials delivered" forecast of 31-Oct-2026 conflicts with 41 of 155 materials not yet on site.
- The procurement log in the workbook is still unusable (delivered figures above quantities, #DIV/0! and #VALUE! cells, project ID DAM2-01-029), and the front-page procurement total still repeats the mechanical row. The procurement presentation lists 5 RMUs while the quantities and the MV slide give 3; it gives 377 street-light poles delivered against 380 on the lighting slide, and 13 fire hydrants against 12. It also has malformed dates (15/111/26, 31/09/2026).
- NCRs: the front page shows 4 issued and 3 closed; the Quality-Stat sheet shows 51 issued and 50 closed.
- Labour: the front page shows 360 planned and 483 actual; the Manpower sheet shows 78 planned and 537 actual for October.
- Sewer quantities differ across the files: Major Quantities 6,803 of 7,567 LM (89.9%), the Conclusion sheet 6,803 of 6,146 LM (110.7%), and the presentation 6,135 of 6,257 LM (98.1%). Shop drawings: 1,774 approved in the workbook, 1,818 in the presentation.
- Contract value is 198,906,162.61 on the front page and 198,906,162.312 "incl. VAT" in the Conclusion sheet. The invoice log has stray values (21,100,000, 20,900,000, 200,000) and EAC shows #REF!.

- Key submittal dates are in Feb–Mar 2024, before the contract award of 30-Jun-2025. The look-ahead sheet contains P6 data from the Hail Industrial City Phase II project, and the risk register uses project ID DAM2-01-029 and names the 3rd and 6th Industrial Cities.
- The workbook's issue 1 text still quotes 304 workers and 184 items of equipment; the presentation gives 537 workers and 304 items of equipment.
- The workbook's front page and the presentation's acceleration plan also report cost-based progress; this report uses physical progress only.

Compiled 01-Nov-2026 from the weekly report with data date 27-Oct-2026, its P6 update, the progress and procurement presentations of 27-Oct-2026, and the 20-Oct-2026 report for this-week values.
