
Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS Summry

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Development of the Technology City in Dhahran Project Recovery -R		3680	06-Jan-26 A	15-Jul-27	93,388,700	35,616,581	23,396,765	22,760,264	38.14%	25.05%
Key Milestones		3680	06-Jan-26 A	15-Jul-27	0	0	0	0	0%	0%
Preliminaries and Mobilization Works		632	06-Jan-26 A	11-Apr-26 A	0	0	0	0	0%	0%
Engineering Works		2128	06-Jan-26 A	22-Nov-26	0	0	0	0	0%	0%
Procurement Cycle		2744	02-May-26 A	20-Jun-27	0	0	0	0	0%	0%
Construction Works		3102	10-Mar-26 A	23-Jun-27	93,388,700	35,616,581	23,396,765	22,760,264	38.14%	25.05%
Infrastructure Networks		3086	10-Mar-26 A	21-Jun-27	57,696,530	32,596,024	13,726,670	13,448,654	56.5%	23.79%
Internal		3086	10-Mar-26 A	21-Jun-27	32,508,953	16,942,289	3,102,401	3,102,629	52.12%	9.54%
Alignment-RD-01		2950	10-Mar-26 A	01-Jun-27	15,199,337	8,358,281	3,102,401	3,102,629	54.99%	20.41%
Alignment-RD-02		1392	22-Nov-26	21-Jun-27	7,655,882	3,978,072	0	0	51.96%	0%
Alignment-RD-03-1		1368	26-Oct-26	22-May-27	3,448,486	1,279,090	0	0	37.09%	0%
Alignment-RD-03-2		1536	28-Oct-26	17-Jun-27	3,959,670	2,215,741	0	0	55.96%	0%
Alignment-RD-03-3		1320	09-Nov-26	29-May-27	2,245,578	1,111,105	0	0	49.48%	0%
External		2720	01-Apr-26 A	11-May-27	25,187,577	15,653,735	10,624,269	10,346,026	62.15%	42.18%
External Road - 1 - 1		2712	01-Apr-26 A	10-May-27	5,221,714	3,247,135	2,608,226	2,608,226	62.19%	49.95%
External Road - 1 - 2		2608	18-Apr-26 A	11-May-27	7,651,591	4,767,067	1,790,191	1,214,285	62.3%	23.4%
External Road - 2		2464	09-May-26 A	11-May-27	3,781,297	2,348,995	1,330,763	1,330,763	62.12%	35.19%
External Road - 3		2464	09-May-26 A	11-May-27	8,532,974	5,290,538	4,895,089	5,192,752	62%	57.37%
Superstructure Work		1808	01-Aug-26 A	23-Jun-27	35,692,170	3,020,557	9,670,095	9,311,610	8.46%	27.09%
Utility Buildings		1808	29-Aug-26 A	23-Jun-27	8,083,982	1,059,788	1,082,796	1,061,039	13.11%	13.39%
Water Pump Station		1808	15-Sep-26 A	23-Jun-27	3,313,461	580,935	346,091	346,091	17.53%	10.45%
Sewage Lift Station		480	29-Aug-26 A	28-Jan-27	564,483	0	372,559	350,805	0%	66%
Potable Water Tank		616	02-Jan-27	04-Apr-27	314,972	29,027	0	0	9.22%	0%
IrrigationTank		512	16-Jan-27	03-Apr-27	314,972	0	0	0	0%	0%
Control Room		1024	03-Oct-26 A	13-May-27	3,576,093	449,827	364,146	364,142	12.58%	10.18%
Softscape and Planting Works		280	01-May-27	15-Jun-27	3,915,193	0	0	0	0%	0%
Storm Drainage Ponds		488	01-Oct-26 A	05-May-27	8,820,044	0	3,969,020	3,969,053	0%	45%
Boundary Fence and Gaurd Room		1536	01-Aug-26 A	13-Jun-27	14,872,951	1,960,769	4,618,279	4,281,518	13.18%	31.05%
Testing and Comissioning		200	14-Jun-27	12-Jul-27	0	0	0	0	0%	0%
Handing over and close out		192	19-Jun-27	15-Jul-27	0	0	0	0	0%	0%

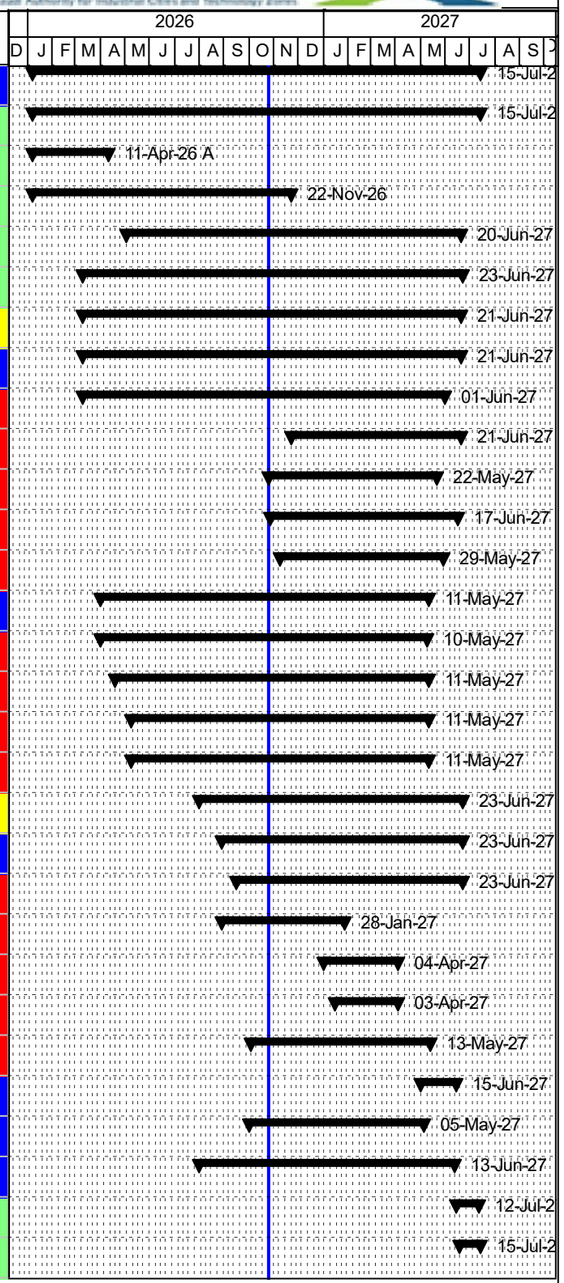

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		
