# MODON - Weekly Progress Report - Construction Projects

**Data Date** 19-Oct-26

## Contract General Information

| | | | |
|---|---|---|---|
| Project Name | Construction of Passenger Station for SAR Railway Sudair Industrial City | | |
| Project ID | SUD1-05-018 | Stage | Construction |
| Contractor | Technical Development Co. "TDC" | Status | Active |
| Consultant | Saudi Arabia Consulting Engineering Company "EGIS" | Modon PM | Engr.Zyad Al Shabat |

## Key Dates

| | | | | | |
|---|---|---|---|---|---|
| Contract Award | 31-Mar-26 | Contract Award (Hijri) | 10/12/1447 | Revised Completion | 07-Apr-26 |
| Contract Sign | 31-Mar-26 | Contract Sign (Hijri) | 10/12/1447 | Committed Completion | 06-Aug-27 |
| Site Handover | 07-Apr-26 | Site Handover (Hijri) | 11/19/1447 | Forecast Completion | 06-Aug-27 |
| Original Completion | 06-Aug-27 | Original Completion (Hijri) | 03/03/1449 | Variance | 0 |

## Cost Summary (SR)

| | | | |
|---|---|---|---|
| Original Contract Value | 33,090,825 | O&M Value | 0 |
| Revised Contract Value | 0 | Revised O&M Value | 0 |
| Estimate At Completion Value | 33,090,825 | Submitted Invoices (Gross Value) | 3,048,399 |
| Potential Changes | 0 | Total Deduction | (2,000) |

## Performance Summary

| | | | | | |
|---|---|---|---|---|---|
| Plan Value | 19.04% | Phys. Plan Value | 38.06% | Quality Score | 88.7% |
| Earn Value | 21.44% | Phys. Earn Value | 26.08% | | |
| Variance | 2.40% | Variance | (11.98%) | Safety Score | 83.3% |
| SPI | 1.13 | SPI | 0.69 | | |

## Project Scope

Civil Work , Storm Water Drainage , Sewer , Portable , Electrical , CCTV

## Progress Overview


### Earned Value Progress (SAR)

| WBS | BOQ Value (SAR) | % Wt. | Weekly (SAR) Planned | Weekly (SAR) Earned | To Date (SAR) Original Plan | To Date (SAR) Cum. Planned | To Date (SAR) Cum.Earned | Original Plan % | Cum. Planned % | Cum.Earned % | Variance | SPI |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | - | 0.0% | - | - | - | 22,585 | - | 0.0% | 0.0% | 0.0% | 0.0% | |
| Milestones | - | 0.0% | - | - | - | - | - | 0.0% | 0.0% | 0.0% | 0.0% | |
| Mobilization | - | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | |
| Engineering | - | 0.0% | - | - | - | - | - | 0.0% | 0.0% | 0.0% | 0.0% | |
| Procurement | - | 0.0% | - | - | - | - | - | 0.0% | 0.0% | 0.0% | 0.0% | |
| Construction | 33,090,852 | 100.0% | 710,697 | 214,091 | - | 6,301,807 | 7,095,542 | 0.0% | 19.0% | 21.4% | 2.4% | 1.13 |
| Package-1 | 22,502,032 | 68.0% | 613,732 | 214,091 | - | 5,886,632 | 7,095,542 | 0.0% | 26.2% | 31.5% | 5.4% | 1.21 |
| ROAD WORKS 1 | 17,704,263 | 53.5% | 514,154 | 111,823 | - | 5,366,361 | 6,500,574 | 0.0% | 30.3% | 36.7% | 6.4% | 1.21 |
| ROAD - 01 | 10,400,905 | 31.4% | 275,855 | 111,823 | - | 3,150,987 | 4,140,066 | 0.0% | 39.8% | 39.8% | 0.0% | 1.00 |
| ROAD - 02 | 7,303,358 | 22.1% | 238,299 | - | - | 2,215,374 | 2,360,507 | | | | | |
| ELECTRICAL WORKS | 3,415,753 | 10.3% | 62,395 | 43,660 | | 246,972 | 62,629 | | | | | |
| MV Network | 1,577,890 | 4.8% | 17,205 | - | | 35,479 | - | | | | | |
| Earthing System | 4,795 | 0.0% | - | - | | - | - | | | | | |
| Street Lighting Network | 1,454,545 | 4.4% | | | | 146,450 | 6,383 | | | | | |
| TELECOMMUNICATIONS WORKS | 378,522 | 1.1% | | 43,660 | | 65,043 | 56,247 | | | | | |
| LOW VOLTAGE | 86,942 | 0.3% | | - | | - | 4,927 | | | | | |
| ROAD - 01 | 28,981 | 0.1% | - | - | - | 371,500 | 2,029 | 0.0% | 7.0% | 7.0% | 0.0% | 1.00 |
| ROAD - 02 | 57,961 | 0.2% | | 869 | | | | | | | | |
| PORTABLE WATER | 379,700 | 1.1% | | 210,420 | | | | | | | | |
| ROAD - 01 | 189,850 | 0.6% | | (87,613) | | | | | | | | |
| ROAD - 02 | 189,850 | 0.6% | | 3,809 | | | | | | | | |
| SEWARAGE NETWORK | 621,335 | 1.9% | | 20,653 | | | | | | | | |
| ROAD - 01 | 372,801 | 1.1% | | | | | | | | | | |
| ROAD - 02 | 248,534 | 0.8% | | | | | | | | | | |
| STORM WATER | 294,040 | 0.9% | | | | | | | | | | |
| ROAD N... | 294,040 | 0.9% | | | | | | | | | | |
| Package-3 | 10,588,820 | 32.0% | | | | | | | | | | |
| Site Works | 21,090 | 0.1% | | | | | | | | | | |
| Earthworks | 21,090 | 0.1% | | | | | | | | | | |
| Platform Works | 6,003,782 | 18.1% | | | | | | | | | | |
| Platform Substructure | 5,037,344 | 15.2% | - | - | - | 371,500 | - | 0.0% | 0.0% | 0.0% | 0.0% | 0.00 |
| Finishes & Architectural Works | 966,437 | 2.9% | - | - | - | - | - | 0.0% | 0.0% | 0.0% | 0.0% | |
| **Total** | **33,090,825** | **100.0%** | **795,260** | **214,091** | **-** | **6,301,807** | **7,095,542** | **0.00%** | **19.04%** | **21.44%** | **2.40%** | **1.13** |


### Physical Progress (Effort)

| WBS | Budgeted (Manhours) | % Wt. | Weekly Physical Progress Planned | Weekly Physical Progress Earned | Plan % | Earned % | To Date Physical Progress Planned | To Date Physical Progress Earned | Plan % | Earned % | Variance | SPI |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | - | 0.0% | - | - | 0.0% | 0.0% | | - | 0.0% | 0.0% | 0.0% | |
| Milestones | - | 0.0% | - | - | 0.0% | 0.0% | 19,793 | 19,793 | 0.0% | 0.0% | 0.0% | |
| Mobilization | 19154.00 | 3.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | 0.0% | |
| Engineering | 31923.40 | 5.0% | - | - | 0.0% | 0.0% | 32,988 | 31,339 | 103.3% | 98.2% | -5.2% | 0.95 |
| Procurement | 89,386 | 14.0% | 3,134 | 4,642 | 3.5% | 5.2% | 68,347 | 17,130 | 76.5% | 19.2% | -57.3% | 0.25 |
| Construction | 478,851 | 75.0% | 8,552 | 3,430 | 1.8% | 0.7% | 121,851 | 98,246 | 25.4% | 20.5% | -4.9% | 0.81 |
| Package-1 | 345,776 | 54.2% | 8,143 | 3,430 | 2.4% | 1.0% | 109,662 | 98,246 | 31.7% | 28.4% | -3.3% | 0.90 |
| ROAD WORKS 1 | 168,660 | 26.4% | 15,867 | 557 | 9.4% | 0.3% | 73,549 | 78,905 | 43.6% | 46.8% | 3.2% | 1.07 |
| ROAD - 01 | 96,630 | 15.1% | 1,058 | 557 | 1.1% | 0.6% | 58,740 | 62,660 | 60.8% | 64.8% | 4.1% | 1.07 |
| ROAD - 02 | 72,030 | 11.3% | 1,164 | - | 1.6% | 0.0% | 14,810 | 16,245 | 20.6% | 22.6% | 2.0% | 1.10 |
| ELECTRICAL WORKS | 103,222 | 16.2% | - | - | 0.0% | 0.0% | 18,369 | 3,751 | 17.8% | 3.6% | -14.2% | 0.20 |
| MV Network | 37,659 | 5.9% | 1,036 | - | 2.8% | 0.0% | 1,036 | - | 2.8% | 0.0% | -2.8% | 0.00 |
| Earthing System | 173 | 0.0% | - | - | 0.0% | 0.0% | - | - | 0.0% | 0.0% | 0.0% | |
| Street Lighting Network | 51,051 | 8.0% | 9,986 | - | 19.6% | 0.0% | 13,326 | 515 | 26.1% | 1.0% | -25.1% | 0.04 |
| TELECOMMUNICATIONS WORKS | 14,340 | 2.2% | 4,008 | 2,429 | 28.0% | 16.9% | 4,008 | 3,237 | 28.0% | 22.6% | -5.4% | 0.81 |
| LOW VOLTAGE | 6,638 | 1.0% | - | 329 | 0.0% | 5.0% | - | 651 | 0.0% | 9.8% | 9.8% | |
| ROAD - 01 | 2,072 | 0.3% | - | - | 0.0% | 0.0% | 2,336 | 322 | 112.7% | 15.5% | -97.2% | 0.14 |
| ROAD - 02 | 4,566 | 0.7% | | | | | | 328 | | | | |
| PORTABLE WATER | 46,755 | 7.3% | | | | | | | | | | |
| ROAD - 01 | 20,132 | 3.2% | | | | | | | | | | |
| ROAD - 02 | 26,623 | 4.2% | | | | | | | | | | |
| SEWARAGE NETWORK | 19,752 | 3.1% | | | | | | | | | | |
| ROAD - 01 | 12,695 | 2.0% | | | | | | | | | | |
| ROAD - 02 | 7,057 | 1.1% | | | | | | | | | | |
| STORM WATER | 749 | 0.1% | | | | | | | | | | |
| ROAD N... | 749 | 0.1% | | | | | | | | | | |
| Package-3 | 133,075 | 20.8% | | | | | | | | | | |
| Site Works | 1,836 | 0.3% | | | | | | | | | | |
| Earthworks | 1,836 | 0.3% | | | | | | | | | | |
| Platform Works | 68,965 | 10.8% | | | | | | | | | | |
| Platform Substructure | 47,411 | 7.4% | - | - | 0.0% | 0.0% | 2,336 | - | 4.9% | 0.0% | -4.9% | 0.00 |
| Finishes & Architectural Works | 21,152 | 3.3% | - | - | 0.0% | 0.0% | - | - | 0.0% | 0.0% | 0.0% | |
| **Total** | **638,468** | **100.0%** | **11,686** | **8,072** | **1.83%** | **1.26%** | **242,979** | **166,508** | **38.06%** | **26.08%** | **-11.98%** | **0.69** |


### Earned Value Progress (%)

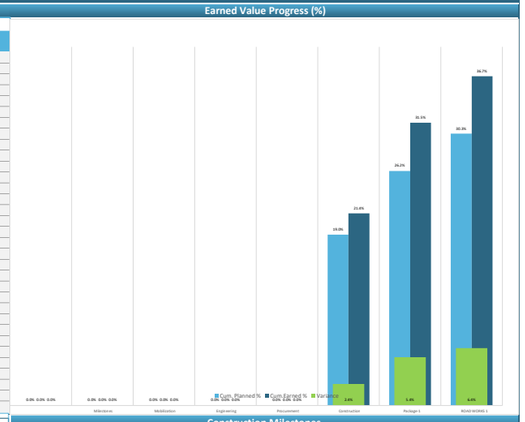


### Earned Value - Cost

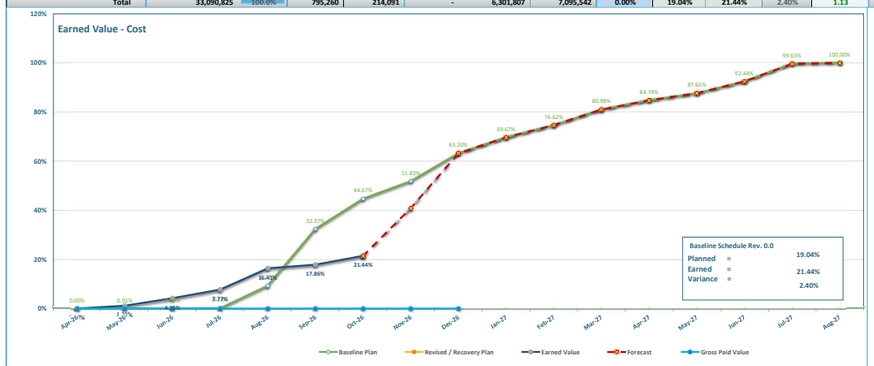


### Physical Progress - Effort

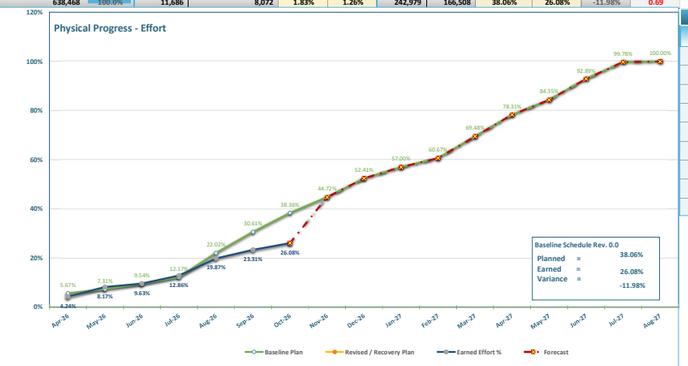



### Construction Milestones

| Item No. | Milestones | Original (Baseline) | Latest Plan | Forecast | Status | Days Change |
|---|---|---|---|---|---|---|
| 1 | Project Start Milstone | 07-Apr-26 | 07-Apr-26 | 07-Apr-26 | Finish | 0 |
| 2 | Mobilization Finish Milestone | 06-May-26 | 06-May-26 | 06-May-26 | Finish | 0 |
| 3 | Work Plan and Timeline Milestone | 06-May-26 | 16-Aug-26 | 16-Aug-26 | UP | (102) |
| 4 | Completion of MV Work | 22-May-27 | 05-May-27 | 05-May-27 | UP | 17 |
| 5 | Completion of road and paving works Milestone | 06-Dec-26 | 31-Dec-26 | 31-Dec-26 | UP | (25) |
| 6 | Completion of site and platform work Milestone | 20-Jul-27 | 05-Aug-27 | 05-Aug-27 | UP | (16) |
| 7 | Completion of finishing works and general site works | 20-Jul-27 | 06-Aug-27 | 06-Aug-27 | UP | (17) |
| 8 | Engineering Phase Finish Milestone | 06-May-26 | 21-Sep-26 | 21-Sep-26 | UP | (138) |
| 9 | Procurment Phase Finish Milestone | 15-Apr-27 | 09-Jun-27 | 09-Jun-27 | UP | (55) |

### Project Status Score



### Actual Invoices




## Performance overview

### Submittals Status

#### Shop Drawings

| Item Per WBS | Total | Total Submitted Drawings A | B | C | D | Processed | Remaining | Pending | Total Submittals |
|---|---|---|---|---|---|---|---|---|---|
| Roadwork | 90 | 80 | 10 | 0 | 0 | 90 | 0 | 0 | 90 |
| wet network(sewer,,potable) | 47 | 13 | 34 | 0 | 0 | 47 | 0 | 0 | 47 |
| Telecom | 15 | 8 | 7 | 0 | 0 | 15 | 0 | 0 | 15 |
| Lighting | 28 | 8 | 20 | 0 | 0 | 28 | 0 | 0 | 28 |
| Electrical | 24 | 5 | 19 | 0 | 0 | 24 | 0 | 0 | 24 |
| TOTAL | 204 | 114 | 90 | 0 | 0 | 204 | 0 | 0 | 204 |

#### Material Approval

| Item Per WBS | Total | Total Submitted Material A | B | C | D | Processed | Remaining to approve | Pending | Total Submittals |
|---|---|---|---|---|---|---|---|---|---|
| Civil /Structural /Architectural | 20 | 0 | 18 | 1 | 0 | 19 | 0 | 1 | 20 |
| Electrical | 16 | 1 | 13 | 2 | 0 | 16 | 0 | 0 | 16 |
| Mechanical | 7 | 0 | 7 | 0 | 0 | 7 | 0 | 0 | 7 |
| | | | | | | | | | |
| | | | | | | | | | |
| TOTAL | 43 | 1 | 38 | 3 | 0 | 42 | 0 | 1 | 43 |

#### Procurement Summary

| Item Per WBS | Total Materials | Total Number of P.O. | Actual P.O. To Date | Remaining P.O | Material on Site | Remaining Materials | Material Delivery Completion (Date) |
|---|---|---|---|---|---|---|---|
| Civil /Structural /Architectural | 3 | 2 | 2 | 1 | 0 | 3 | - |
| Electrical | 18 | 15 | 15 | 3 | 6 | 6 | - |
| Mechanical | 6 | 5 | 5 | 1 | 3 | 3 | - |
| | | | | | | | |
| | | | | | | | |
| TOTAL | 27 | 22 | 22 | 5 | 9 | 12 | 00-Jan-00 |

#### Primavera P6 Schedule Status

**Project Activities Overview**

| Schedule Statistics: Total Act. | Not Started | In Progress | Completed | % | Active Schedule Activities: Active | Ahead | On | Behind | Flag | 0 |
|---|---|---|---|---|---|---|---|---|---|---|
| 855 | 586 | 46 | 223 | 26.08% | 10 | 15 | 0 | 22 | | |

| Critical Path Activities: Last Week | This Week | Diff | Free Float Management (Total): Greater Than 14 Days Last Week | This Week | Less Than 14 Days Last Week | This Week | Failed Start Activities Last Week | This Week | Flag | 0 |
|---|---|---|---|---|---|---|---|---|---|---|
| 0 | 0 | 0 | 53 | 172 | 598 | 570 | 0 | 2 | | |

### Quality

#### Quality Reports

| Quality Reports | Issued | Closed | Pending | Avg. Closing (Days) | Pending 0-10 Days | 11-20 Days | 21-30 Days | 31-60 Days | > 60 Days |
|---|---|---|---|---|---|---|---|---|---|
| Non Conformance (NCR) | 4 | 4 | 0 | 0 | 0 | - | - | - | - |
| Site Instruction (SIR) | 0 | 0 | 0 | 0 | - | 0 | 0 | 0 | 0 |
| Material Inspection (MIR) | 15 | 15 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Field Inspection (FIR) | 152 | 143 | 9 | 0 | 9 | 0 | 0 | 0 | 0 |

#### Key Submittals Approval Status

| | | | |
|---|---|---|---|
| 1 Quality Plan Approval | 11-May-26 | 6 Baseline Approval | 02-Aug-26 |
| 2 Quality Plan Last Up | 11-May-26 | 7 No of Approved Version of Schedule | - |
| 3 Safety Plan Approval | 06-May-26 | 8 Last Approved Schedule | - |
| 4 Safety Plan Last Up | 30-Apr-26 | 9 BOQ Approval Date | - |
| 5 Construction Plan Approval | - | 10 No of Approved Version of BOQ | - |

#### Invoices Summary

| | | | |
|---|---|---|---|
| Total Submitted Invoices | 2 | Submitted Invoices (SAR) | 3,048,399 |
| PM Approved Invoices | 0 | PM Approved Invoices (SAR) | 0 |
| No of Paid Invoices | 0 | Paid Invoices (SAR) | 0 |
| No of Pending Invoices | 2 | Last Submitted Period | 00-Jan-00 |
| Advance Payment % | 0% | Advance Payment (SAR) | 0 |
| Retention % | 0% | Retention (SAR) | 0 |
| Deduction / Penalties % | 0% | Deduction / Penalties (SAR) | (2,000) |




#### Resources at Site

| Head Count - Manual: Planned | Actual | Next Month Forecast | Saudi Staff | Head Count - Non Manual: Planned | Actual | Next Month Forecast | Saudi Staff | Total Head Count: Total Plan | Total Actual | Variance |
|---|---|---|---|---|---|---|---|---|---|---|
| 40 | 65 | 0 | 0 | 20 | 22 | 0 | 3 | 60 | 87 | 27 |

**Manpower Breakdown by Trade**

| Key Trade | Planned | Actual |
|---|---|---|
| Engineer | 2 | 10 |
| Doc. Controller | 1 | 1 |
| Proc. Team | 1 | 1 |
| Foreman | 2 | 3 |
| Draftman | 1 | 1 |
| Driver | 5 | 31 |
| Unskilled Labor | 15 | 20 |
| Total | 40 | 87 |




**Major Equipment**

| Type | Planned | Actual | Idle |
|---|---|---|---|
| Pick Up/Car | 1 | 2 | 0 |
| Bus | 1 | 2 | 0 |
| Dump Truck | 10 | 12 | 0 |
| Boom Truck | 0 | 2 | 0 |
| Generator | 1 | 1 | 0 |
| CRANE | 0 | 1 | 0 |
| Shovel | 0 | 1 | 0 |
| Total | 13 | 21 | 0 |

### Safety


#### Safety Statistics

| Category | Item | This Week | This Month | Year to Date | Cumulative |
|---|---|---|---|---|---|
| General | Total Hours Worked | 4,280 | 9,540 | 77,050 | 77,050 |
| | Safe Hours Worked | 4,280 | 9,540 | 77,050 | 77,050 |
| Reactive | 0 | 0 | 0 | 22 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 20 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| | 0 | 0 | 0 | 0 | 0 |
| Proactive | 0 | 0 | 0 | 0 | 0 |
| | No.of Internal Training | 1 | 3 | 22 | 22 |
| | No.of Internal Audit | 0 | 0 | 0 | 0 |
| | No. of Toolbox Talks | 1 | 3 | 20 | 20 |
| | Safety Awards/Incentives | 0 | 0 | 0 | 0 |

#### Proactive Vs Reactive Actions Taken




#### Total Hours Worked Vs Safe Hours Worked




### Latest Contract Change Order Log

| CCO No. | Date Added | Description of Change | Status | Cost | Sch Impact (Months) | Date Approved | Duration |
|---|---|---|---|---|---|---|---|
| - | - | - | - | - | - | - | - |

### Major Quantity Trackers

| BOQ NO. | Item Description | Total Qty | Measu Unit | Plan to Date | Act to Date | Remaining | Variance |
|---|---|---|---|---|---|---|---|
| B1.32 11 13.01 | Subgrade | 20530 | m3 | 0.00 | 15000.00 | 5530.00 | 0.00 |
| B1.32 11 23.01 | Aggregate base course | 16375.94 | m3 | 0.00 | 9875.94 | 6500.00 | 0.00 |
| B1.32 12 16.01 | Asphalt | 13360 | m3 | 0.00 | 573.00 | 12787.00 | 0.00 |
| B1.32 14 13.13.0 | Interlock | 27900 | m2 | 0.00 | 0.00 | 27900.00 | 0.00 |
| B1.32 16 13.23.0 | Curbstone | 20555 | m2 | 0.00 | 0.00 | 20555.00 | 0.00 |

## Testing And Commissioning

| Item | Planned Start Date | Planned Finish Date | Forecast Start Date | Forecast Finish Date | Actual Start Date | Actual Finish Date | % Completed | Open Comments | Closed Comments |
|---|---|---|---|---|---|---|---|---|---|
| Civil Works | 09-May-27 | 31-May-27 | 06-Jun-27 | 23-Jun-27 | | | 0% | 0 | 0 |
| Storm Water Drainaee Network | 19-Jan-27 | 06-Feb-27 | 18-Mar-27 | 05-Apr-27 | | | 0% | 0 | 0 |
| Sewerage Network | 14-Mar-27 | 31-Mar-27 | 25-Jan-27 | 13-Feb-27 | | | 0% | 0 | 0 |
| Portable Water | 22-Mar-27 | 08-Apr-27 | 28-Mar-27 | 14-Apr-27 | | | 0% | 0 | 0 |
| Electrical Works | 18-Jul-27 | 03-Aug-27 | 08-Jul-27 | 26-Jul-27 | | | 0% | 0 | 0 |
| CCTV Works | 22-Jul-27 | 06-Aug-27 | 12-Jul-27 | 27-Jul-27 | | | 0% | 0 | 0 |

## Top Issues and Risks

**Top 5 Issues**

| Issue No | Date Identified | Issue Description | Responsible | Action Taken | Mitigation | Current Status | Expected/Actual Closure | Duration Elapsed |
|---|---|---|---|---|---|---|---|---|
| 3120-11 | 03/Oct/26 | Equipment operator found working zone with Non-compalince to site mandatory PPE. | Contractor/HSE Team | It was ensure to wear the mandatory PPE all the time when present on site | | Close | 2 | 1 |
| 3120-12 | 10/Oct/26 | Observe Hot Work activity without proper control measure Fire safety | Contractor/HSE Team | Provide Fire Extinguisher and other requirements as per Hot work requirements. | | Close | 2 | 1 |
| 3120-13 | 11/Oct/26 | Observe site without mandatory PPE complaince | Contractor/HSE Team | Wear the mandatory PPE all the time when present on site | | Close | 2 | 1 |
| 3120-14 | 18/Oct/26 | Observe dust created at temporary vehicles roads due insuffient dust control measures. | Contractor/HSE Team | Ensure dust control by regular spraying of water on vehicles routes | | Close | 2 | 1 |
| 3120-15 | 17/Oct/26 | Observe non complaince of mandatory PPE by equipment operators | Contractor/HSE Team | Wear the mandatory PPE all the time by equipment operators when present on site | | Close | 2 | 1 |

Data sensitivity - Internal

# Weekly Progress Report - Construction Projects

| Data Date | 19-Oct-26 |
|---|---|

## Contract General Information

| | |
|---|---|
| Project Name | Construction of Passenger Station for SAR Railway Sudair Industrial City |
| Project ID | SUD1-05-018 |
| Contractor | Technical Dvelopment Co. "TDC" |
| Consultant | Saudi Arabia Consulting Engineering Company "EGIS" |
| Stage | Construction |
| Status | Active |
| Modon PM | Engr.Zyad Al Shabat |

## Key Dates

| | |
|---|---|
| Contract Award Date | 31-Mar-26 |
| Contract Sign Date | 31-Mar-26 |
| Site Handover Date | 07-Apr-26 |
| Original Completion | 06-Aug-27 |
| Contract Award Date (Hijri) | 10/12/1447 |
| Contract Sign Date (Hijri) | 10/12/1447 |
| Site Handover Date (Hijri) | 11/19/1447 |
| Original Completion (Hijri) | 03/03/1449 |
| Revised Completion Date | 07-Apr-26 |
| Committed Completion Date | 06-Aug-27 |
| Forecast Completion | 06-Aug-27 |
| Variance | 0 |

| Key Project Submittals | Submission Date | Days taken to approve orginal plan from site handover date |
|---|---|---|
| Quality Plan submission | 30-Apr-26 | 23 |
| Quality Plan approval | 11-May-26 | |
| Quality Plan Last Update | 11-May-26 | |
| Safety Plan submission | 30-Apr-26 | 23 |
| Safety Plan approval | 6-May-26 | |
| Safety Plan Last Update | 30-Apr-26 | |
| Risk Management Plan submission | 20-Apr-26 | 13 |
| Risk Management Plan approval | 30-Apr-26 | |
| Risk Management Plan Last Update | 30-Apr-26 | |
| Baseline Schedule submission | 7-May-26 | 30 |
| Baseline Schedule approval | 2-Aug-26 | |
| No of Schedule Versions | - | |
| Last Revised Schedule Approval Date | - | |
| BOQ submission | - | - |
| BOQ approval | - | |
| No of Approved Version of BOQ | - | |
| Execution Plan submission | 30-Apr-26 | 23 |
| Execution Plan Approval | - | |

Data sensitivity - Internal

| Project Scope Statement | Construction of Passenger Station for SAR Railway Sudair Industrial City |
|---|---|

| Earned Value Progress (SAR) | | | | | | | | Physical Progress (Effort) | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| WBS | BOQ Value (SAR) | % Wt. | Weekly (SAR) | | | To Date (SAR) | | Budgeted | % Wt. | Weekly Physical Progress | | To Date Physical Progress | |
| | | | Planned | Earned | Original Plan | Planned | Earned | (Manhours) | | Planned | Earned | Planned | Earned |
| **Milestones** | | | | | | - | - | - | 0.0% | | | - | - |
| **Mobilization** | - | | | | | - | - | 19,154 | 3.0% | - | - | 19793 | 19793 |
| **Engineering** | **-** | **0.00%** | **-** | **-** | **-** | **-** | **-** | **31923.4** | **5.0%** | **-** | **-** | 32988 | 31339 |
| **Procurement** | **-** | **0.00%** | **-** | **-** | **-** | **-** | **-** | **89385.5** | **14.0%** | **3,134** | **4,642** | 68347 | 17130 |
| **Construction** | **33,090,852.00** | **100.00%** | **710,697** | **214,091** | **-** | 6,301,807.46 | 7,095,542.04 | **478850.8** | **75.0%** | **8,552** | **3,430** | 121851 | 98246 |
| Package-1 | 22,502,032.00 | 68.00% | 613,732 | 214,091 | - | 5,886,632.12 | 7,095,542.04 | 345775.5 | 54.2% | 8,143 | 3,430 | 109662 | 98246 |
| ROAD WORKS 1 | 17,704,263.00 | 53.50% | 514,154 | 111,823 | - | 5,366,361.18 | 6,500,573.51 | 168659.6 | 26.4% | 15,867 | 557 | 73549 | 78905 |
| ROAD - 01 | 10,400,905.00 | 31.43% | 275,855 | 111,823 | - | 3,150,987.44 | 4,140,066.18 | 96629.6 | 15.1% | 1,058 | 557 | 58740 | 62660 |
| ROAD - 02 | 7,303,358.00 | 22.07% | 238,299 | - | | 2,215,373.74 | 2,360,507.33 | 72030.1 | 11.3% | 1,164 | - | 14810 | 16245 |
| ELECTRICAL WORKS | 3,415,753.00 | 10.32% | 62,395 | 43,660 | | 246,971.83 | 62,629.37 | 103222.1 | 16.2% | | - | 18369 | 3751 |
| MV Network | 1,577,890.00 | 4.77% | 17,205 | - | | 35,478.52 | 0 | 37659 | 5.9% | 1,036 | - | 1036 | 0 |
| Earthing System | 4,795.00 | 0.01% | - | - | | 0 | 0 | 172.8 | 0.0% | - | - | 0 | 0 |
| Street Lighting Network | 1,454,545.00 | 4.40% | 30,727 | - | | 146,450.34 | 6,382.50 | 51050.8 | 8.0% | 9,986 | - | 13326 | 515 |
| TELECOMMUNICATIONS WORKS | 378,522.00 | 1.14% | 14,462 | 43,660 | | 65,042.96 | 56,246.87 | 14339.6 | 2.2% | 4,008 | 2,429 | 4008 | 3237 |
| LOW VOLTAGE | 86,942.00 | 0.26% | - | - | | 0 | 4,926.72 | 6638.4 | 1.0% | - | 329 | 0 | 651 |
| ROAD - 01 | 28,981.00 | 0.09% | - | - | | 0 | 2,028.65 | 2072.2 | 0.3% | - | - | 0 | 322 |
| ROAD - 02 | 57,961.00 | 0.18% | - | 869 | | 0 | 2,898.07 | 4566.2 | 0.7% | (9,146) | - | 0 | 328 |
| PORTABLE WATER | 379,700.00 | 1.15% | 11,905 | 210,420 | | 66,242.45 | 213,318.11 | 46755 | 7.3% | 7,499 | 4,879 | 11285 | 12074 |
| ROAD - 01 | 189,850.00 | 0.57% | 5,695 | (87,613) | | 30,835.92 | 121,896.06 | 20132.1 | 3.2% | (614) | 2,412 | 4746 | 7195 |
| ROAD - 02 | 189,850.00 | 0.57% | 6,209 | 3,809 | | 35,406.53 | 91,422.05 | 26622.9 | 4.2% | 1,179 | 96 | 6539 | 4879 |
| SEWARAGE NETWORK | 621,335.00 | 1.88% | 98,048 | 20,653 | | 127,245.74 | 108,266.16 | 19751.7 | 3.1% | 2,570 | 312 | 6304 | 2638 |
| ROAD - 01 | 372,801.00 | 1.13% | (32,404) | - | | 79,365.26 | 90,221.80 | 12694.5 | 2.0% | 2,872 | 1,863 | 4447 | 2226 |
| ROAD - 02 | 248,534.00 | 0.75% | (23,285) | 2,123 | | 47,880.48 | 18,044.36 | 7057.2 | 1.1% | 1,723 | 49 | 1857 | 412 |
| STORM WATER | 294,040.00 | 0.89% | 39,207 | 189,907 | | 79,810.92 | 205,828.17 | 748.6 | 0.1% | 22 | 38 | 156 | 228 |
| ROAD N... | 294,040.00 | 0.89% | 9,801 | 36,755 | | 79,810.92 | 205,828.17 | 748.6 | 0.1% | 22 | 228 | 156 | 228 |
| Package-3 | 10,588,820.00 | 32.00% | 96,966 | - | | 415,175.34 | 0 | 133075.3 | 20.8% | 410 | - | 12190 | 0 |
| Site Works | 21,090.00 | 0.06% | (297,120) | - | | 21,090.02 | 0 | 1835.5 | 0.3% | - | - | 9506 | 0 |
| Earthworks | 21,090.00 | 0.06% | - | - | | 21,090.02 | 0 | 1835.5 | 0.3% | - | - | 9506 | 0 |
| Platform Works | 6,003,782.00 | 18.14% | 84,563 | - | - | 371,500.30 | 0 | 68964.6 | 10.8% | 238 | - | 2336 | 0 |
| Platform Substructure | 5,037,344.00 | 15.22% | 84,563 | - | - | 371,500.30 | 0 | 47410.5 | 7.4% | 2,336 | - | 2336 | 0 |
| Finishes & Architectural Works | 966,437.00 | 2.92% | - | - | | 0 | 0 | 21151.7 | 3.3% | - | - | 0 | 0 |
| Platform Electrical Works | - | 0.00% | | | | 0 | 0 | 402 | 0.1% | | | 0 | 0 |
| Canopy works | 3,863,605.00 | 11.68% | | | | 22,585.02 | 0 | 33,381 | 5.2% | | | 348 | 0 |
| Civil and Architectural Works | 166,440.00 | 0.50% | | | | 11,200.01 | 0 | 1,831 | 0.3% | | | 228 | 0 |
| Metals | 3,697,165.00 | 11.17% | | | | 11,385.01 | 0 | 31,550 | 4.9% | | | 120 | 0 |
| Electrical Works | 700,343.00 | 2.12% | | | | 0 | 0 | 28,894 | 4.5% | | | 0 | 0 |
| Low-Voltage Electrical Power Conductors and Cables | 36,000.00 | 0.11% | | | | 0 | 0 | 676 | 0.1% | | | 0 | 0 |
| Ondoor Lighting Points | 62,010.00 | 0.19% | | | | 0 | 0 | 390 | 0.1% | | | 0 | 0 |
| Outdoor Lighting Fixtures | 152,490.00 | 0.46% | | | | 0 | 0 | 16,411 | 2.6% | | | 0 | 0 |
| CCTV | 327,218.00 | 0.99% | | | | 0 | 0 | 4,076 | 0.6% | | | 0 | 0 |
| Voice Evacuation System | 122,624.00 | 0.37% | | | | 0 | 0 | 7,342 | 1.1% | | | 0 | 0 |
| **Testing and Comissioning** | **0** | **0%** | | | | 0 | 0 | **12737.5** | 2.0% | | | 0 | 0 |
| **Close Out** | **0** | **0%** | | | | 0 | 0 | **6416.6** | 1.0% | | | 0 | 0 |
| **Total** | 33,090,825.00 | **100.0%** | **795,260** | **214,091** | **-** | **6,301,807** | **7,095,542** | **638,468** | **100.0%** | **11,686** | **8,072** | **242,979** | **166,508** |
| | | | | | | 19.04% | 21.44% | | | | | 38.06% | 26.08% |

Data sensitivity - Internal

| Data Date | 19-Oct-26 |
|---|---|

# WEEKLY PROGRESS PHOTOS

Asphalt base course first layer 8 cm at Road 1



Asphalt base course first layer 8 cm at Road 1



Aggregate Base course layer at Road 1



Aggregate Base course layer at Road 1



Grading for second layer of subgrade at Road no.1 From st 00+650 to 00+950



Grading for second layer of subgrade at Road no.1 From st 00+650 to 00+950



Data sensitivity - Internal

# Quality -Stat

## Quality Reports

| Item | Issued | Closed | Pending | Avg. Closing (Days) | Pending | | | | |
|---|---|---|---|---|---|---|---|---|---|
| | | | | | 0-10 Days | 11-20 Days | 21-30 Days | 31-60 Days | > 60 Days |
| Non Conforomance Report (NCR) | 4 | 4 | 0 | | | - | - | - | - |
| Site Instruction (SI) | 0 | 0 | 0 | | - | - | - | - | - |
| Material Inspection Report (MIR) | 15 | 15 | 0 | | - | - | - | - | - |
| Field Inspection Request (FIR) | 152 | 143 | 9 | | 9 | - | - | - | - |

## Shop Drawings

| Item Per WBS | Total | Total Drawings Submitted | | | | | Remaining Drawings | Pending Submittals With Consultant | Total Submittals |
|---|---|---|---|---|---|---|---|---|---|
| | | A | B | C | D | Processed(A+B+C+D) | | | |
| Road work | 90 | 80 | 10 | 0 | 0 | 90 | - | 0 | 90 |
| wet network(sewer,potable,Storm) | 47 | 13 | 34 | 0 | 0 | 47 | - | 0 | 47 |
| Telecom | 15 | 8 | 7 | 0 | 0 | 15 | - | 0 | 15 |
| Lighting | 28 | 8 | 20 | 0 | 0 | 28 | - | 0 | 28 |
| Electrical | 24 | 5 | 19 | 0 | 0 | 24 | - | 0 | 24 |
| TOTAL | **204** | **114** | **90** | **-** | **-** | **204** | **-** | **-** | **204** |

## Material Approval

| Item Per WBS | Total | Total Materials Submitted | | | | | Remaining to approve | Pending Submittals With Consultant | Total Submittals |
|---|---|---|---|---|---|---|---|---|---|
| | | A | B | C | D | Processed(A+B+C+D) | | | |
| Civil /Structural /Architectural | 20 | - | 18 | 1 | - | 19 | - | 1 | 20 |
| Electrical | 16 | 1 | 13 | 2 | - | 16 | - | 0 | 16 |
| Mechanical/STR | 7 | - | 7 | 0 | - | 7 | - | 0 | 7 |
| TOTAL | **43** | **1** | **38** | **3** | **-** | **42** | **-** | **1** | **43** |

## Procurement Summary

| Item Per WBS | Total Materials | Total Number of P.O. | Actual P.O. To Date | Remaining P.O | Actual Material on Site | Remaining Materials | Material Delivery Completion (Date) |
|---|---|---|---|---|---|---|---|
| Civil /Structural /Architectural | 3 | 2 | 2 | 1 | - | 3 | - |
| Electrical | 18 | 15 | 15 | 3 | 6 | 6 | - |
| Mechanical | 6 | 5 | 5 | 1 | 3 | 3 | - |
| TOTAL | **27** | **22** | **22** | **5** | **9** | **12** | |

Data sensitivity - Internal

# QC OBSERVATIONS CHECKLIST

| | | | | | |
|---|---|---|---|---|---|
| **Project No.** | **SUD1-05-018** | **OBS No.** | | **Inspection Day:** | **October 19, 2026** |
| **Project** | **Construction of Passenger Station for SAR Railway Sudair Industrial City** | **Contractor: Consultant:** | **Technical Development Company** **Egis Engineering cunsultancy** | | |

| | | | | | |
|---|---|---|---|---|---|
| **4** | Excellent | Quality Management System is being practiced and applies to MODON System | **90 - 100** | **QC Overall Score** | **88.7%** |
| **3** | **Good** | Evidence of compliance with plans and procedures. | **80 - 89** | | |
| **2** | Average | Indication level of compliance with standards but there is room for improvement | **70 - 79** | | |
| **1** | Improve | Quality and Control is NOT being managed effectively. Needs Improvement | **≤ 69** | | |
| **0** | N/A | Item was not applicable or this item was not reviewed during the inspection. | **Zero** | | |

| No. | Topic | E (4) | G (3) | A (2) | I (1) | N/A (0) |
|---|---|---|---|---|---|---|
| 1 | Control of Access to Site/Office | | G | | | |
| 2 | Document Control Administration | | G | | | |
| 3 | Project Documents and Progress | | G | | | |
| 4 | Contractor's Quality Plan/CM (Updated and Reviewed) | | G | | | |
| 5 | MS Log and Paperwork | | G | | | |
| 6 | RFI, FIR, & MIR Procedure | | G | | | |
| 7 | RFI, FIR, & MIR Inventory system | | G | | | |
| 8 | NCRs Control & Procedure | | G | | | |
| 9 | NCR Log | | G | | | |
| 10 | MODON Standard* | | | G | | |
| 11 | Project Risk Plan/Management* | | | | G | |
| 12 | Monthly Quality Reports* | | | | G | |
| 13 | ITP | | | G | | |
| 14 | MODON Weekly Report | | | | G | |
| 15 | Design Change Official Paperwork* | | | | | G |
| 16 | Design Change was Applied* | | | | | G |
| 17 | Material List | | G | | | |
| 18 | Pending Material Status | | G | | | |
| 19 | Lifting Plan* | | | | G | |
| 20 | DWG Log | | | | G | |
| 21 | Invoice Status | | | | G | |
| 22 | Site Handover Letter | G | | | | |
| 23 | Material Testing Results & Certification | | | | G | |
| 24 | As Build Drawings Status* | | | | | G |
| 25 | Calibrated Lab Tools & Equipment | | G | | | |
| 26 | Storage Inventory System | | G | | | |
| 27 | Logistics Plan | | G | | | |
| 28 | Project Progress Planview | | | G | | |
| 29 | Sufficient Number of QC Inspectors | | | G | | |

| No. | Topic | E (4) | G (3) | A (2) | I (1) | N/A (0) |
|---|---|---|---|---|---|---|
| 30 | QC of Excavation | | G | | | |
| 31 | QC of Roads/Round about | | G | | | |
| 32 | QC of Interlock & Curbstone | | G | | | |
| 33 | Layers/Backfilling Sampling | | G | | | |
| 34 | Pump Stations Units | | | | | G |
| 35 | Quality of Form Work | | | | | |
| 36 | Design Change List | | | | | G |
| 37 | Quality of Concrete Placing | | | | | G |
| 38 | Concrete Surface Finishing | | | | | G |
| 39 | Pedestals/Columns/Beams Alignment | | | | | G |
| 40 | Siporex Lifting & Unloading | | | | | G |
| 41 | Siporex Quality Pre-installation | | | | | G |
| 42 | Siporex Finishing Quality | | | | | G |
| 43 | Roads / Parking Markings | | G | | | |
| 44 | QC of Finishing Outdoors | | | | | G |
| 45 | Quality of Finishing Indoors | | | | | G |
| 46 | Stairs Quality | | | | | G |
| 47 | Tanks Method Statement Work | | | | | G |
| 48 | Electric Rooms | | | | | G |
| 49 | QC of MCC/ATS Plant Units | | | | | G |
| 50 | Qualified Subcontractor | | G | | | |
| 51 | Scaffold/Ladders/Slope/Bridge Compliance | | | | | G |
| 52 | Protection Applied to Completed Work | | | | | G |
| 53 | Storage Management in/out Control | | | | | G |
| 54 | Material Control | | G | | | |
| 55 | Manholes Storing and Quality | | | | | G |
| 56 | Reinforced Steel Quality | | | | | G |
| 57 | Safety Overview | | G | | | |
| 58 | Waste Management Control | | G | | | |

| | |
|---|---|
| **Prepared by:** | **Sarvar Ahmad** |

| | |
|---|---|
| **Issued to PM:** | **Engr.Zyad Al Shabat** |

*QC Observations refer only to the practices and documentation observed at time of inspection. The responsibility of the CM and Contractor is to ensure that aspects of Quality are suitably managed.
*Scores are a reflection of the general site conditions based upon the findings at the time of the walk through
*If Applicable

Data sensitivity - Internal

| Safety Statistics | | | | | |
|---|---|---|---|---|---|
| Category | Item | This Week | This Month | Year to Date | Cumulative |
| Category | Total Hours Worked | 4,280 | 9,540 | 77,050 | 77,050 |
| | Safe Hours Worked | 4,280 | 9,540 | 77,050 | 77,050 |
| | No.of Internal Training | 1 | 3 | 22 | 22 |
| | No.of Internal Audit | | | | |
| | No. of Toolbox Talks | 1 | 3 | 20 | 20 |
| | Safety Awards/Incentives | | | | |

| Category | Item | This Week | This Month | Year to Dat | Cumulative |
|---|---|---|---|---|---|
| Overall Average | 83.33% | | | | |
| This Week Score | 83% | | | | |

| Consultant Safety Inspection (Weekly Basis) | | | | | | |
|---|---|---|---|---|---|---|
| Week Number | Date of Audit | Date Issued | Numbers Of Comments | Overall Score | Date Closed | Closure Duration |
| Week-1 | | | 0 | 76% | | 0 |
| Week-2 | | | 0 | 76% | | 0 |
| Week-3 | | | 0 | 83% | | 0 |
| Week-4 | | | 0 | 77% | | 0 |
| Week-5 | | | 0 | 83% | | 0 |
| Week-6 | | | 0 | 83% | | 0 |
| Week-7 | | | 0 | 83% | | 0 |
| Week-8 | | | 0 | 83% | | 0 |
| Week-9 | | | 0 | 83% | | 0 |
| Week-10 | 17-Aug-26 | 17-Aug-26 | 0 | 83% | 17-Aug-26 | 0 |
| Week-11 | 24-Aug-26 | 24-Aug-26 | 0 | 83% | 24-Aug-26 | 0 |
| Week-12 | 31-Aug-26 | 31-Aug-26 | 0 | 83% | 31-Aug-26 | 0 |
| Week-13 | 7-Sep-26 | 7-Sep-26 | 0 | 83% | 7-Sep-26 | 0 |
| Week-14 | 14-Sep-26 | 14-Sep-26 | 0 | 83% | 14-Sep-26 | 0 |
| Week-15 | 21-Sep-26 | 21-Sep-26 | 0 | 83% | 21-Sep-26 | 0 |
| Week-16 | 28-Sep-26 | 28-Sep-26 | 0 | 83% | 28-Sep-26 | 0 |
| Week-17 | 5-Oct-26 | 5-Oct-26 | 0 | 83% | 5-Oct-26 | 0 |
| Week-18 | 12-Oct-26 | 12-Oct-26 | 0 | 83% | 12-Oct-26 | 0 |
| Week-19 | 19-Oct-26 | 19-Oct-26 | 0 | 83% | 19-Oct-26 | 0 |
| Week-20 | | | 0 | 0% | | 0 |
| Week-21 | | | 0 | 0% | | 0 |
| Week-22 | | | 0 | 0% | | 0 |
| Week-23 | | | 0 | 0% | | 0 |
| Week-24 | | | 0 | 0% | | 0 |
| Week-25 | | | 0 | 0% | | 0 |
| Week-26 | | | 0 | 0% | | 0 |
| Week-27 | | | 0 | 0% | | 0 |
| Week-28 | | | 0 | 0% | | 0 |
| Week-29 | | | 0 | 0% | | 0 |

Data sensitivity - Internal

# MODON HSE Site Inspection Report

| | | | | | |
|---|---|---|---|---|---|
| Date | 19-Oct-26 | Inspected By: | Engr Ayman Sabry | | |
| Project ID. | SUD1-02-011 | Report No. | | MODON PM Name | Engr.Ziyad Al Shabbat |
| Project Name: | Construction of Passenger Station for SAR Railway Sudair Industrial City | Contractor: | TECHNICAL DEVELOPMENT CONTRACTING CO. | Safety Performance | 83.33% |

**Inspections are a snapshot in time and refer only to the practices and documentation observed at the time of the Inspection. It remains the responsibility of the Consultant and Contractor to ensure that all aspects of Health & Safety are suitably managed.**

| | | | | | | | |
|---|---|---|---|---|---|---|---|
| | Good Practice | | Need Improvement | | Fail (Life Threatening Activity) / Comliance with Plan & Procedures | N/A | Atcitty Not Applicable for this Site Inspection Report |

| No. | Topic | HSE Compliance |
|---|---|---|
| 1 | Access and Egress - (General access to site, segregated from vehicles, / Overhead protection, while entering into the building /Adequate lighting provided when dark or overnight work) | |
| 2 | Traffic Management - (Loading/unloading/sheeting/temp. routes/speed/parking/competence) | |
| 3 | Site Signage - (Project Notice Board & General Signage) | |
| 4 | PPE Compliance - (Use, storage, stock, handling & checks - Head, Foot, Eye, Hearing) | |
| 5 | Housekeeping - (Material correctly stored/Rubbish cleaned & removed daily/slips & trips hazards) | |
| 6 | Storage of Materials - (Transporting, storage, training and use - Combustible / Flammable / Hazardous substances (COSHH) | |
| 7 | Site Waste Management - (Hazardous waste /Combustible waste / Human waste / Construction waste - asphalt, cable, timber, paving roof sheeting tiles, plastic & bricks) | |
| 8 | Health Surveillance - (Expose to excessive noise/vibration/dust/silica/CO/cement/radiation/extreme weather condition) | |
| 9 | Electrical Safety - (Electrical qualified /RCD/GFCI/Industrial Cocket/LOTO/Cable-overhung or buried/Cords in good condition/current inspection tag) | |
| 10 | Tools & Equipment - (Includes, powered, hydraulic & pneumatic/Guards in place/Properly stored/RCD Protection/Earthed/Good condition & tagged) | |
| 11 | Manual Handling - (Lifting/loading/pulling/pushing/twisting/awkward posture/repetitive task/frequent and prolong physical effort/Reasonable practicable use of mechanical aid) | |
| 12 | Vehicle and mobile equipment / Plant - (dumpers; excavators, cranes, piling rigs, grader, roller, loaders/condition/KSA License/certification) | |
| 13 | Lifting Operations & Rigging - (Lifting Plan/Lifting devices & gears/PTW/Condition/3rd party certification/bank-man/rigger/slingers/man-basket/inspection record/tagged) | N/A |
| 14 | Work at Height - (PPE/Fall Protection(Same level, above and blow) / Training / Fall restraint / competency /Safe access & egress to and from work at height / Ladders / Openings (floor/shafts/Provision of emergency rescue) | N/A |
| 15 | Scaffolding - (Temp. Scaffolding Work-platform (All types) - qualified scaffolder / Inspection / Tagged / Safe Access/egress / PTW/Falsework & Formwork) | N/A |
| 16 | Mobile Elevated Work platform (MEWP) - (PTW/competence requirements/conditions/inspections/tagged/training/Full-body harness) | N/A |
| 17 | Excavation & Trenches - (PTW/Edge protection/buffer zone/Slope/Benching/Shoring/Geo-tech report/Atmospheric hazards/Acess&egress/Emergency management / MS&RA/H.E) | |
| 18 | Confined Space - (PTW/Training/competence/Emergency Management/MS & RA/Safe access/egress) | N/A |
| 19 | Fire Protection - (Flammable/Oxy. LPG /Combustible separated/FE's/Flashback arrestor/Sparks & slags/Smoking area/PTW/Generators/MS & RA/Emergency Management) | |
| 20 | Health & Welfare - (Adequate drinking water/shaded - eating & rest area/washing & sanitary facilities/Certified FA/FA Box & Stock/adequate toilets/Ambulance) | |
| 21 | Environmental Incident Measures - (Spill/ Leakage / Concrete wash / vehicle & eqpts. wash / waste disposal/Sewers and drains/emissions/Emergency Management/Training/site run-off water) | |
| 22 | HSE Communications & Meetings - (Schedule HSE Meetings/Safety Committee meetings/Alerts / Lesson learned/Safety Bulletin contains latest HSE KPI) | |
| 23 | HSE Plan & Associated Procedures - (Approved updated HSE Plan/ CEMP/HAZComm/Procedures/Standards/Project Safety Risk Register) | |
| 24 | Health, Safety & Environment Incident reporting - (Review of HSE Statistics, Reporting of Unsafe Act & Conditions/ Reporting of Near Miss incident/Reporting of FA cases/Record MT cases) | |
| 25 | HSE Awareness, Training & Competence - (Policy /Objective & targets/Information, training/Climatic condition awareness/Reponses in emergency situation/ Safety Behavior Observation) | |
| 26 | Project Leadership Site Tours - (Provide evidence of proactive safety performance/Deficient discovered discussed/Positive feedback/Workers resolving safety issues) | |

| | | | |
|---|---|---|---|
| **Prepared by:** | **Abdul kalim** | **Sent to MODON PM:** | **Engr.Ziyad Al Shabbat** |

| Safety Results | | | | | |
|---|---|---|---|---|---|
| | **7** | | **14** | | **0** |

Data sensitivity - Internal

## MAJOR QUANTITIES

| BOQ Number | Description of Item | Total Quantity | Unit of Measurement | Actual To Date | Excecuted on site | Remaining Total |
|---|---|---|---|---|---|---|
| B1.32 11 13.01 | Subgrade | 20530 | m3 | 15,000 | 15,000.00 | 5,530 |
| B1.32 11 23.01 | Aggregate base course | 16375.94 | m3 | 9,876 | 4,625.00 | 6,500 |
| B4.33 31 23.01 | HDPE pipe | 5,808 | m | 5,808 | | 0 |
| B1.32 12 16.01 | Asphalt | 13,360 | m3 | 573 | 573.00 | 12,787 |
| B1.32 14 13.13.01 | Interlock | 27,900 | m2 | 0 | | 27,900 |
| B1.32 16 13.23.01 | Curbstone | 20,555 | m2 | 0 | | 20,555 |
| B2.31 23 00.01 | Medium Voltage cables | 7,120 | m | 0 | | 7,120 |
| B2.33 71 00 02.01 | Low Voltage Cables, Copper & Aluminum, | 7,500 | m | 7,500 | | 0 |
| 31 00 00 | Canopy | 4,000 | m | 0 | | 4,000 |
| 03 00 00 | Platform | 4,000 | m2 | 0 | | 4,000 |
| B4.05 52 00.01 | Metal Handrail | 440 | m | 0 | | 440 |
| B2.26 56 19.01 | Lighting Luminaire | 116 | Unit | 0 | | 116 |

Data sensitivity - Internal

# Weekly Progress Report - Invoice Log

## Project Value

| | | | |
|---|---|---|---|
| Original Contract Value | 33,090,825.00 | O&M Value | 0 |
| Revised Contract Value | 0.00 | Revised O&M Value | 0 |
| Estimate At Completion Value | 33,090,825.00 | Submitted Invoices (Gross Value) | 3,048,399 |
| Potential Changes | 0.00 | Total Deduction | (2,000) |

## Payment Status

| | | | |
|---|---|---|---|
| Advance Payment % | 0% | Advance Payment (SAR) | 0 |
| Retention % | 0% | Retention (SAR) | 0 |
| Penalties and deduction % | -0.006% | AP Recovery (SAR) | 0 |
| Penalties and deduction (SAR) | (2,000) | Retention Cumulative (SAR) | 0 |

## Invoices Summary

| | | | |
|---|---|---|---|
| No of Submitted Invoices | 2 | Submitted Invoices (SAR) | 3,048,399.33 |
| No of Approved Invoices (CM) | 0 | Approved Invoices (CM) (SAR) | 0 |
| No of Approved Invoices (PM) | 0 | Approved Invoices (PM) (SAR) | 0 |
| No of Paid Invoices | 0 | Paid Invoices (SAR) | 0 |

Submitted Invoice Peroid

Invoice Submitted Compared to Contract Value

| Invoice Reference | | | | Invoice Value | | | | | | Period Covered | | CM / PgM Approval Timeline | | | | Modon PM & Accounts Approval | | | | | | | Payment Status | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| # | Invoice No. | Doc Control reference | Submittal Rev. # | Gross Value | AP Recovery | Retention | VAT 5%/15% | Deduction / Penalties | Amount (net) | Start Date | End Date | Date to CM / PgM | CM / PgM Approval (Yes/No) | CM / PgM Reply Date | Days Elapsed | Date to PM | PM Approval (Yes/No) | PM Reply Date | Date to Accounts | Accounts Approval (Yes/No) | Accounts Approval Date | Days Elapsed | Date Paid | Amount Paid | Paid % | Payment Period (d) |
| 1 | 1 | SUD1-05-018-TDC-TS9-1-IPC-0001-00 | 0 | 2,573,925.60 | 0.00 | | 386,088.84 | (2,000.00) | 2,958,014.44 | 07-Apr-26 | 18-Jul-26 | | | | | | | | | | | | | | | |
| 9 | 2 | SUD1-05-018-TDC-TS9-1-IPC-0002-00 | | 474,473.73 | | | 71,171.06 | 0.00 | 545,644.79 | 19-Jul-26 | 30-Aug-26 | | | | | | | | | | | | | | | |
| 10 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 14 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 15 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 16 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 17 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 18 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 19 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 20 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 21 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 22 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 23 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 24 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 25 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 26 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 27 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 28 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 29 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 30 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 31 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 32 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 33 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 34 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 35 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 36 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 37 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 38 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 39 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 40 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 41 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 42 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 43 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 44 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 45 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 46 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 47 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 48 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 49 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 50 | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | **TOTAL** | 3,048,399.33 | 0.00 | 0.00 | | (2,000.00) | 3,503,659.23 | | | | | | | | | | | | | | | 0.00 | | |

Data sensitivity - Internal

| Project Name | Construction of Passenger Station for SAR Railway Sudair Industrial City | | | | |
|---|---|---|---|---|---|
| Project ID | SUD1-02-011 | Project Budget | 33,090,825 | | |
| Date Period | Start Date 07/Apr/26 | To | Data Date 19/Oct/26 | | |

| SL NO | BOQ Item # | BOQ Description | Date | FIR # | FIR Description | Unit Rate | Current Period Quantity | % Claim | Unite rate as per claim | Total (SR) |
|---|---|---|---|---|---|---|---|---|---|---|
| | Description | | | | | | | | | 3,646,338.73 |
| 1 | B1 .31 23 23.01 | Earth works & Embankment | 15-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0014-01 | Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 1+350 to STA: 1+700 | 24.00 | 5,835.38 | 100% | 24.00 | 140,049.12 |
| 2 | B1 .31 23 23.01 | Earth works & Embankment | 11-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0015-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+850 to STA: 1+000 (Bottom subgrade) | 24.00 | 1,733.54 | 100% | 24.00 | 41,604.96 |
| 3 | B1 .31 23 23.01 | Earth works & Embankment | 16-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0016-01 | Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 0+120 to STA: 0+500 | 24.00 | 5,229.11 | 100% | 24.00 | 125,498.64 |
| 4 | B1 .31 23 23.01 | Earth works & Embankment | 15-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0018-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st Layer for Station Road RD-01 , STA: 0+500 to STA: 1+000 | 24.00 | 6,588.40 | 100% | 24.00 | 158,121.60 |
| 5 | B1 .31 23 23.01 | Earth works & Embankment | 15-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0021-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 1+000 to STA:1+239.64 | 24.00 | 3,557.97 | 100% | 24.00 | 85,391.28 |
| 6 | B1 .31 23 23.01 | Earth works & Embankment | 15-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0022-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-01, STA: 1+000 to STA:1+350 | 24.00 | 6,159.64 | 100% | 24.00 | 147,831.36 |
| 7 | B1.312323.01 | Earth works & Embankment | 16-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0023-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+350 to STA:1+530 | 24.00 | 2,536.83 | 100% | 24.00 | 60,883.92 |
| 8 | B1 .31 23 23.01 | Earth works & Embankment | 17-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0026-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+120 to STA:0+300 | 24.00 | 3,205.93 | 100% | 24.00 | 76,942.32 |
| 9 | B1 .31 23 23.01 | Earth works & Embankment | 20-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0027-01 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 0+840 to STA:1+000 | 24.00 | 2,713.88 | 100% | 24.00 | 65,133.12 |
| 10 | B1 .31 23 23.01 | Earth works & Embankment | 20-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0028-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+200 to STA:1+350 | 24.00 | 2,471.63 | 100% | 24.00 | 59,319.12 |
| 11 | B1.31 23.23.01 | Earth works & Embankment | 21-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0029-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd Layer for Station Road RD-01, STA: 0+300 to STA:0+500 | 24.00 | 3,412.82 | 100% | 24.00 | 81,907.68 |
| 12 | B1 .31 23 23.01 | Earth works & Embankment | 21-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0030-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd Layer for Station Road RD-01, STA: 0+500 to STA:0+700 | 24.00 | 3,411.28 | 100% | 24.00 | 81,870.72 |
| 13 | B1 .31 23 23.01 | Earth works & Embankment | 21-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0031-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+000 to STA:1+200 | 24.00 | 3,279.64 | 100% | 24.00 | 78,711.36 |
| 14 | B1 .31 23 23.01 | Earth works & Embankment | 21-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0032-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+600 to STA:0+700 | 24.00 | 1,118.04 | 100% | 24.00 | 26,832.96 |
| 15 | B1 .31 23 23.01 | Earth works & Embankment | 23-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0033-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+860 to STA:1+000 | 24.00 | 1,963.02 | 100% | 24.00 | 47,112.48 |
| 16 | B1 .31 23 23.01 | Earth works & Embankment | 22-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0034-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+700 to STA:0+850 | 24.00 | 2,675.56 | 100% | 24.00 | 64,213.44 |
| 17 | B1 .31 23 23.01 | Earth works & Embankment | 22-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0035-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 0+850 to STA:1+000 | 24.00 | 2,465.69 | 100% | 24.00 | 59,176.56 |
| 18 | B1 .31 23 23.01 | Earth works & Embankment | 22-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0036-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 1+000 to STA:1+239.64 | 24.00 | 3,622.31 | 100% | 24.00 | 86,935.44 |
| 19 | B1 .31 23 23.01 | Earth works & Embankment | 23-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0037-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+120 to STA:0+300 | 24.00 | 3,301.84 | 100% | 24.00 | 79,244.16 |
| 20 | B1 .31 23 23.01 | Earth works & Embankment | 23-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0038-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road RD-02, STA: 0+550 to STA:0+700 | 24.00 | 2,146.37 | 100% | 24.00 | 51,512.88 |
| 21 | B1 .31 23 23.01 | Earth works & Embankment | 24-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0039-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+300 to STA:0+500 | 24.00 | 3,181.05 | 100% | 24.00 | 76,345.20 |
| 22 | B1 .31 23 23.01 | Earth works & Embankment | 24-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0040-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+850 to STA:1+000 | 24.00 | 2,363.84 | 100% | 24.00 | 56,732.16 |
| 23 | B1 .31 23 23.01 | Earth works & Embankment | 25-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0041-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+120 to STA:0+300 | 24.00 | 3,035.56 | 100% | 24.00 | 72,853.44 |
| 24 | B1 .31 23 23.01 | Earth works & Embankment | 25-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0042-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+200 to STA:1+350 | 24.00 | 1,819.60 | 100% | 24.00 | 43,670.40 |
| 25 | B1 .31 23 23.01 | Earth works & Embankment | 27-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0043-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+380 to STA:1+530 | 24.00 | 1,600.68 | 100% | 24.00 | 38,416.32 |
| 26 | B1 .31 23 23.01 | Earth works & Embankment | 20-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0044-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+570 to STA:0+600 | 24.00 | 422.84 | 100% | 24.00 | 10,148.16 |
| 27 | B1 .31 23 23.01 | Earth works & Embankment | 14-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0045-01 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+350 to STA:1+380 | 24.00 | 459.23 | 100% | 24.00 | 11,021.52 |
| 28 | B1 .31 23 23.01 | Earth works & Embankment | 27-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0046-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 1+000 to STA:1+200 | 24.00 | 3,121.83 | 100% | 24.00 | 74,923.92 |
| 29 | B1 .31 23 23.01 | Earth works & Embankment | 28-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0047-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+300 to STA:0+500 | 24.00 | 2,984.00 | 100% | 24.00 | 71,616.00 |
| 30 | B1 .31 23 23.01 | Earth works & Embankment | 28-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0048-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-01, STA: 1+530 to STA:1+700 (Bottom Subgrade) | 24.00 | 2,264.12 | 100% | 24.00 | 54,338.88 |
| 31 | B1 .31 23 23.01 | Earth works & Embankment | 29-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0049-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+500 to STA:0+700 | 24.00 | 3,745.61 | 100% | 24.00 | 89,894.64 |
| 32 | B1 .31 23 23.01 | Earth works & Embankment | 30-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0050-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-01, STA: 0+700 to STA:0+850 | 24.00 | 2,120.15 | 100% | 24.00 | 50,883.60 |
| 33 | B1 .31 23 23.01 | Earth works & Embankment | 30-Jun-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0051-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 1+000 to STA:1+239.64 | 24.00 | 2,901.29 | 100% | 24.00 | 69,630.96 |
| 34 | B1.31 23 16.01 | Excavation (all types of soil) | 8-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0052-02 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgarde of road at Station Road RD-02, STA: 0+340 to STA:0+500 | 24.00 | 118.65 | 25% | 6.00 | 711.90 |
| 35 | B1 .31 23 23.01 | Earth works & Embankment | 1-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0053-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+850 to STA: 1+000 | 24.00 | 2,143.65 | 100% | 24.00 | 51,447.60 |
| 36 | B1 .31 23 23.01 | Earth works & Embankment | 4-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0055-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 1+000 to STA:1+200 | 24.00 | 2,569.79 | 100% | 24.00 | 61,674.96 |

Data sensitivity - Internal

| SL NO | BOQ Item # | BOQ Description | Date | FIR # | FIR Description | Unit Rate | Current Period Quantity | % Claim | Unite rate as per claim | Total (SR) |
|---|---|---|---|---|---|---|---|---|---|---|
| 37 | B1 .31 23 23.01 | Earth works & Embankment | 4-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0056-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 1+200 to STA:1+350 | 24.00 | 1,024.89 | 100% | 24.00 | 24,597.36 |
| 38 | B1 .31 23 23.01 | Earth works & Embankment | 22-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0057-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer for Station Road \ Carriage-way RD-02, STA: 0+730 to STA:0+840 (Bottom subgrade) | 24.00 | 234.51 | 100% | 24.00 | 5,628.24 |
| 39 | B1 .31 23 23.01 | Earth works & Embankment | 4-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0058-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer for Station Road RD-02, STA: 0+600 to STA:0+700 | 24.00 | 1,290.07 | 100% | 24.00 | 30,961.68 |
| 40 | B1 .31 23 23.01 | Earth works & Embankment | 4-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0059-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+120 to STA: 0+300 (Bottom Subgrade) | 24.00 | 2,301.88 | 100% | 24.00 | 55,245.12 |
| 41 | B1 .31 23 23.01 | Earth works & Embankment | 5-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0060-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+880 to STA:1+000 | 24.00 | 938.22 | 100% | 24.00 | 22,517.28 |
| 42 | B1 .31 23 23.01 | Earth works & Embankment | 6-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0061-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 0+300 to STA: 0+500 (Bottom Subgrade) | 24.00 | 2,334.35 | 100% | 24.00 | 56,024.40 |
| 43 | B1 .31 23 23.01 | Earth works & Embankment | 6-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0062-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+500 to STA:0+700 (Bottom Subgrade) | 24.00 | 3,250.21 | 100% | 24.00 | 78,005.04 |
| 44 | B1 .31 23 16.01 | Earth works & Excavation / Cutting | 6-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0063-00 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgarde for Station Road RD-02, STA: 0+000 to STA:0+160 | 24.00 | 1,335.84 | 100% | 24.00 | 32,060.16 |
| 45 | B1 .31 23 23.01 | Earth works & Embankment | 7-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0064-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-01, STA: 0+700 to STA:0+850 (Bottom Subgrade) | 24.00 | 2,062.86 | 100% | 24.00 | 49,508.64 |
| 46 | B1 .31 23 16.01 | Earth works & Excavation/cutting (all types of soil) | 22-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0065-00 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade for Station Road\ Carriage-way RD-02, STA: 0+730 to STA:0+840 | 24.00 | 515.37 | 25% | 6.00 | 3,092.22 |
| 47 | B1 .31 23 23.01 | Earth works & Embankment | 7-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0066-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 1+000 to STA: 1+200 (Bottom Subgrade) | 24.00 | 2,348.09 | 100% | 24.00 | 56,354.16 |
| 48 | B1 .31 23 23.01 | Earth works & Embankment | 8-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0067-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-01, STA: 1+200 to STA: 1+350 (Bottom Subgrade) | 24.00 | 1,209.65 | 100% | 24.00 | 29,031.60 |
| 49 | B1 .31 23 23.01 | Earth works & Embankment | 13-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0068-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 1+110 to STA:1+239.64 (Bottom sub grade) | 24.00 | 1,033.00 | 100% | 24.00 | 24,792.00 |
| 50 | B1 .31 23 23.01 | Earth works & Embankment | 13-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0069-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 1+000 to STA:1+110 | 24.00 | 1,219.05 | 100% | 24.00 | 29,257.20 |
| 51 | B1 .31 23 23.01 | Earth works & Embankment | 13-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0070-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 0+880 to STA:1+000 | 24.00 | 1,443.25 | 100% | 24.00 | 34,638.00 |
| 52 | B1 .31 23 16.01 | Earthwork & Excavation / Cutting | 23-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0072-00 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade for shoulders (left and right side) at Station Road RD-02, STA: 0+730 to STA:0+840 | 24.00 | 276.36 | 100% | 24.00 | 6,632.64 |
| 53 | B1 .31 23 16.01 | Earth works & Embankment | 23-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0073-00 | Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of shoulders (left and right side) at Road # RD-02 STA: 0+730 to STA: 0+840 | 24.00 | 1,024.52 | 100% | 24.00 | 24,588.48 |
| 54 | B1 .31 23 23.01 | Earth works & Embankment | 27-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0074-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer for Station Road RD-02, STA: 1+030 to STA:1+110 (Bottom Sub grade) | 24.00 | 739.52 | 100% | 24.00 | 17,748.48 |
| 55 | B1 .31 23 23.01 | Earth works & Embankment | 28-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0075-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer (Road and shoulders) for Station Road RD-02, STA: 0+880 to STA:1+030 | 24.00 | 1,687.63 | 100% | 24.00 | 40,503.12 |
| 56 | B1 .31 23 16.01 | Earth works & Embankment | 29-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0076-00 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade of road at Station Road RD-02, STA: 0+160 to STA:0+340 | 24.00 | 183.94 | 100% | 24.00 | 4,414.56 |
| 57 | B1 .31 23 23.01 | Earth works & Embankment | 29-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0077-00 | Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of Road/Carriageway at Road # RD-02 STA: 0+160 to STA: 0+340 | 24.00 | 420.30 | 100% | 24.00 | 10,087.20 |
| 58 | B1 .31 23 16.01 | Earth works & Embankment | 29-Jul-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0078-00 | Check Coordinates level and Compaction F.D.T for Cutting Bottom Subgrade of road at Station Road RD-01, STA: 1+850 to STA:1+914.20 | 24.00 | 327.47 | 100% | 24.00 | 7,859.28 |
| 59 | B1 .31 23 23.01 | Earth works & Embankment | 1-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0080-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer for Station Road RD-02, STA: 0+840 to STA:0+880 | 24.00 | 475.30 | 100% | 24.00 | 11,407.20 |
| 60 | B1 .31 23 23.01 | Earth works & Embankment | 5-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0081-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer for Station Road RD-02, STA: 0+600 to STA:0+700 | 24.00 | 1,191.58 | 100% | 24.00 | 28,597.92 |
| 61 | B1 .31 23 23.01 | Earth works & Embankment | 5-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0083-00 | Check Coordinates level and Compaction F.D.T for Embankment Bottom Subgrade layer for Station Road RD-01, STA: 1+700 to STA:1+850 | 24.00 | 3,527.28 | 100% | 24.00 | 84,654.72 |
| 62 | B1 .31 23 23.01 | Earth works & Embankment | 5-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0084-00 | Check Coordinates level and Compaction F.D.T for Embankment3rd layer for Station Road RD-02, STA: 0+510 to STA:0+600 | 24.00 | 1,181.28 | 100% | 24.00 | 28,350.72 |
| 63 | B1 .31 23 23.01 | Earth works & Embankment | 10-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0090-00 | Check Coordinates level and Compaction F.D.T for Embankment 6th layer (Road and shoulders) for Station Road RD-02, STA: 0+840 to STA:1+030 (Bottom Sub grade) | 24.00 | 1,632.57 | 100% | 24.00 | 39,181.68 |
| 64 | B1 .31 23 23.01 | Earth works & Embankment | 15-Aug-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0096-00 | Check Coordinates level and Compaction F.D.T for Embankment Bottom Subgrade layer for Station Road RD-02, STA: 0+500 to STA:0+730 | 24.00 | 2,707.85 | 100% | 24.00 | 64,988.40 |
| 65 | B1 .31 23 23.01 | Earth works & Embankment/Fill | 3-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0099-02 | Check Coordinates and bottom level Road Filling and compaction test of bottom Sub-Grade of Road/Carriageway at Road # RD-02 STA: 0+340 to STA: 0+500 | 18.00 | 761.53 | 10% | 1.80 | 1,370.75 |
| 66 | B1 33 71 00 02 01 | Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm) | 22-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0100-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 05 To Manhole 06 for Street Lighting Duct Bank in Roundabout Road RD-01 & RD-02 | 1,617.00 | 57.90 | 25% | 404.25 | 23,406.08 |
| 67 | B1 33 71 00 02 01 | Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm) | 22-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0101-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 03 To Manhole 04 for Street Lighting Duct Bank in Road RD-02 | 1,617.00 | 13.00 | 25% | 404.25 | 5,255.25 |
| 68 | B1 33 71 00 02 01 | Road Crossing Duct for Street Lighting cables UPVC (2xØ110mm) | 22-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0102-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 07 To Manhole 08 for Street Lighting Duct Bank in Road RD-02 | 1,617.00 | 13.00 | 25% | 404.25 | 5,255.25 |
| 69 | B2.33 71 00 02.02 | Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm) | 23-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0105-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (4X110mm) from Manhole 01 To Manhole 02 for Street Lighting Duct Bank in Road RD-01 | 525.00 | 9.05 | 25% | 131.25 | 1,187.81 |
| 70 | B2.33 71 00 02.02 | Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm) | 23-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0106-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (4X110mm) from Manhole 09 To Manhole 10 for Street Lighting Duct Bank in Road RD-02 | 525.00 | 9.05 | 25% | 131.25 | 1,187.81 |
| 71 | B2.33 71 00 02.01 | Road Crossing Duct for Street Lighting cables UPVC (4xØ110mm) | 23-Aug-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0107-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for UPVC Pipe (2X110mm) from Manhole 11 To Manhole 12 for Street Lighting Duct Bank in Road RD-02 | 327.00 | 15.90 | 45% | 147.15 | 2,339.69 |
| 72 | B2.1.33 81 26.06 | Road crossing ducts, (6*50mm) HDPE | 23-Aug-26 | SUD1-05-018-TDC-TS9-1-TEL-FIR-0108-00 | Check levels, Laying polyethylene sheet, Form work and concrete pouring for TELECOMMUNICATIONS Works Duct Bank for HDPE Pipe 3(2X50mm) From Manhole 05 To 06 in Road RD-02 | 124.00 | 40.61 | 25% | 31.00 | 1,258.91 |
| 73 | B3.33 14 13.01 | Potable Water Network: 75mm Diameter (Depth: 0.0m - 1.5m) | 31-Aug-26 | SUD1-05-018-TDC-TS9-1-PW-FIR-0109-00 | Check Coordinates level and Excavation width Bottom level and compaction for potable water pipeline from Station ST: 0+250 to ST: 1+900 #RD-02 | 106.00 | 1,650.00 | 5% | 5.30 | 8,745.00 |

Data sensitivity - Internal

| SL NO | BOQ Item # | BOQ Description | Date | FIR # | FIR Description | Unit Rate | Current Period Quantity | % Claim | Unite rate as per claim | Total (SR) |
|---|---|---|---|---|---|---|---|---|---|---|
| 74 | B4.33 31 23.01 | Sewarage Network: HDPE force main110 mm diameter (Depth: 0- 1.5m) | 27-Aug-26 | SUD1-05-018-TDC-TS9-1-SEW-FIR-0110-00 | Check Coordinates level and Excavation width Bottom level and compaction for Sewerage pipeline trench from Station ST: 1+060 to ST: 2+625 #RD-01 | 143.00 | 1,565.00 | 10% | 14.30 | 22,379.50 |
| 75 | B5.33.42.13.01 | Storm Water Network: Concrete pipe culverts (900mm) Diameter | 6-Sep-26 | SUD1-05-018-TDC-TS9-1-STR-FIR-0111-00 | Check Coordinates level and Excavation width Bottom level and compaction for Precast concrete pipe culvert (900mm) diameter at #RD-01 | 1,018.00 | 195.00 | 10% | 101.80 | 19,851.00 |
| 76 | B1.31 23 23.01 | Earth works & Embankment/Fill | 14-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0114-00 | Check Coordinates and bottom level Road Filling and compaction test of Median Island 1st layer at Road # RD-01 STA: 1+500 to STA: 1+850 | 24.00 | 285.60 | 10% | 2.40 | 685.44 |
| 77 | B1.31 23 23.01 | Earth works & Embankment | 14-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0115-00 | Check Coordinates level and Compaction F.D.T for Embankment 1st layer from St:0+000 to 0+062.93 Parking Station Road | 24.00 | 4,750.08 | 100% | 24.00 | 114,001.92 |
| 78 | B1.31 23 23.01 | Earth works & Embankment | 19-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0116-00 | Check Coordinates level and Compaction F.D.T for Embankment 2nd layer from St:0+000 to 0+062.93 Parking Station Road | 24.00 | 1,105.46 | 100% | 24.00 | 26,531.04 |
| 79 | B5.33 42 13.01 | Storm Water Network: Concrete pipe culverts (900mm) Diameter | 24-Sep-26 | SUD1-05-018-TDC-TS9-1-STR-FIR-0117-00 | Check Pipe installation of Precast concrete pipe culvert (900mm) diameter at #RD-01 | 1,018.00 | 195.00 | 30% | 305.40 | 59,553.00 |
| 80 | B1 31 23 23 01 | Check Installation Manhole MH-18 for TELECOMMUNICATIONS Works in Road COL-MC10 | 29-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0123-00 | Check Coordinates level and Compaction F.D.T for Embankment 3rd layer from St:0+000 to 0+062.93 Parking Station Road | 5,939.00 | 1,185.51 | 0% | - | - |
| 81 | B2.1.33 81 26.04 | Earth works & Embankment | 7-Oct-26 | SUD1-05-018-TDC-TS9-1-TEL-FIR-0124-01 | Check Installation Manhole MH-18 for TELECOMMUNICATIONS Works in Road COL-MC10 | 24.00 | 1.00 | 100% | 24.00 | 24.00 |
| 82 | B2.1.33 81 26.03 | Check Installation Manhole MH-11 & MH-12 & MH-15 & MH-16 & MH-17 for TELECOMMUNICATIONS Works in Road COL-MC10 | 30-Sep-26 | SUD1-05-018-TDC-TS9-1-TEL-FIR-0125-00 | Check Installation Manhole MH-11 & MH-12 & MH-15 & MH-16 & MH-17 for TELECOMMUNICATIONS Works in Road COL-MC10 & RD-01 | 5,811.00 | 5.00 | 30% | 1,743.30 | 8,716.50 |
| 83 | B1 32 11 13 01 | Subgrade | 30-Sep-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0127-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+150 to STA: 0+650(Left side) | 36.00 | 1,312.50 | 10% | 3.60 | 4,725.00 |
| 84 | B2.26 05 19.01 | 4Cx 6mm2 + 1Cx6mm2 Cu/XLPE/SWA/PVC | 30-Sep-26 | SUD1-05-018-TDC-TS9-1-LIT-FIR-0128-00 | Check Sand Bedding and Laying of U/G LV Cables (4Cx6+6E) for Bollard Lighting Network in landscape Area near Modon Office | 24.00 | 2,200.00 | 45% | 10.80 | 23,760.00 |
| 85 | B5.33 42 13.05 | Storm Water Network: Concrete pipe culverts | 4-Oct-26 | SUD1-05-018-TDC-TS9-1-STR-FIR-0131-00 | Check Steel Reinforcement and concrete pouring for Base slab | 29,950.00 | 2.00 | 25% | 7,487.50 | 14,975.00 |
| 86 | B1.31 23 23.01 | Earth works & Embankment | 5-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0134-00 | Check Coordinates level and Compaction F.D.T for Embankment 4th layer from St:0+000 to 0+062.93 Parking Station Road | 24.00 | 1,236.30 | 100% | 24.00 | 29,671.20 |
| 87 | B1.32 11 13.01 | Subgrade | 6-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0135-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+650 to STA: 0+900 (left side) | 36.00 | 656.25 | 10% | 3.60 | 2,362.50 |
| 88 | B1.32 11 13.01 | Subgrade | 6-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0137-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+900 to STA: 1+200 (left side) | 36.00 | 787.50 | 10% | 3.60 | 2,835.00 |
| 89 | B2.1.33 81 26.03 | Manhole Type 1 | 7-Oct-26 | SUD1-05-018-TDC-TS9-1-TEL-FIR-0138-00 | Check Installation Manhole MH-03 & MH-04 & MH-07 & MH-08 & MH-09 & MH-10 for TELECOMMUNICATIONS Works in Road RD-01& RD-02 | 5,811.00 | 6.00 | 25% | 1,452.75 | 8,716.50 |
| 90 | B2.1.33 81 26.04 | Manhole Type 2 | 8-Oct-26 | SUD1-05-018-TDC-TS9-1-TEL-FIR-0139-00 | Check Installation Manhole MH-02 & MH-05 & MH-06 & MH-14 for TELECOMMUNICATIONS Works in Road COL-MC10 & RD-02 | 5,939.00 | 4.00 | 25% | 1,484.75 | 5,939.00 |
| 91 | B1.32 11 13.01 | Subgrade | 10-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0140-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 1+200 to STA: 1+500 (Left side) | 36.00 | 787.50 | 10% | 3.60 | 2,835.00 |
| 92 | B1.32 11 13.01 | Subgrade | 10-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0141-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 1+500 to STA: 1+850 (Left side) | 36.00 | 918.75 | 10% | 3.60 | 3,307.50 |
| 93 | B1.32 11 23.01 | Aggregate Base Courses | 11-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0142-01 | Check Coordinates level and compaction F.D.T for (Aggregate base course) at Road /Carriageway# RD-01 STA: 0+170 to STA: 0+650(Left Side) | 66.00 | 840.00 | 10% | 6.60 | 5,544.00 |
| 94 | B1.31 23 23.01 | Earth works & Embankment | 12-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0143-00 | Check Coordinates level and Compaction F.D.T for Embankment 5th layer from St:0+000 to 0+062.93 Parking Station Road | 24.00 | 1,515.03 | 100% | 24.00 | 36,360.72 |
| 95 | B5.33 42 13.01 | Storm Water Network: Concrete pipe culverts (900mm) Diameter | 14-Oct-26 | SUD1-05-018-TDC-TS9-1-STR-FIR-0144-00 | Check Concrete pouring on top of Precast concrete pipe culvert (900mm) diameter at #RD-01 | 1,018.00 | 195.00 | 25% | 254.50 | 49,627.50 |
| 96 | B5.33 42 13.05 | Storm Water Network: Concrete pipe culverts | 14-Oct-26 | SUD1-05-018-TDC-TS9-1-STR-FIR-0145-00 | Check Steel Reinforcement and concrete pouring for wing walls, and headwall of Outlet and inlet structures | 29,950.00 | 2.00 | 25% | 7,487.50 | 14,975.00 |
| 97 | B1.32 11 23.01 | Aggregate Base Courses | 14-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0148-00 | Check Coordinates level and compaction F.D.T for (Aggregate base course) at Road /Carriageway# RD-01 STA: 0+650 to STA: 1+200(Left Side) | 66.00 | 962.50 | 10% | 6.60 | 6,352.50 |
| 98 | B1.32 11 13.01 | Subgrade | 14-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0149-00 | Check Coordinates level and Compaction F.D.T for (Subgrade) 2nd layer at Road /Carriageway # RD-01 STA: 0+160 to STA: 0+650 (Right side) | 36.00 | 1,312.50 | 10% | 3.60 | 4,725.00 |
| 99 | B3.33 14 13.01 | Potable Water Network: 75mm Diameter (Depth: 0.0m - 1.5m) | 17-Oct-26 | SUD1-05-018-TDC-TS9-1-PW-FIR-0150-00 | Check Coordinates level and Excavation width Bottom level and compaction for potable water pipeline from Station ST: 2+350 to ST: 2+725 #RD-02 | 106.00 | 375.00 | 5% | 5.30 | 1,987.50 |
| 100 | B1.32 11 26.01 | BITUMINOUS BASE COURSE | 17-Oct-26 | SUD1-05-018-TDC-TS9-1-ROD-FIR-0151-00 | Check Coordinates, level, thickness, Compaction and Testing for Bituminous base course 1st layer (80mm) on Road /Carriageway from STA:0+170 to STA: 0+550 at Road #RD-01 | 533.00 | 266.00 | 10% | 53.30 | 14,177.80 |
| | | | | | | | | | | **3,887,955.95** |

Data sensitivity - Internal

## PROCUREMENT

| Sr. NO. | Project ID | ACT#inP6 | Item Description | Discipline | (Long \Short) Lead Items | BOQ. No. | Unit | Quantity | Proc. Qty | Required P.O Date | Method of Shipping | Required on Job | E.D.A. to Site | A.D.A. to Site | Lead Time | Approval Status | The Impact (BOQ Cost) | Completion Rate | Remarks |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 1 | SUD1-05-018 | SDR-ST-PRO-S-1010 | Waterproofing (Thermal & moisture Protection) | Civil | Short Lead Items | 07 00 00 | m2 | 910 | 910 | 10-Aug-26 | Local trancport | Civil | 4-Sep-26 | 4-Nov-26 | 25 | Approved | - | - | |
| 2 | SUD1-05-018 | SDR-ST-PRO-S-1030 | Interlock | Civil | Short Lead Items | 33 42 16 | m2 | 27900 | 27900 | 2-Sep-26 | Local trancport | Civil | 28-Sep-26 | 19-Nov-26 | 26 | Approved | - | - | on going |
| 3 | SUD1-05-018 | SDR-ST-PRO-S-1060 | Kerbstone | Civil | Short Lead Items | 32 11 26 | m | 20555 | 20555 | 3-Sep-26 | Local trancport | Civil | 17-Sep-26 | 17-Nov-26 | 14 | Approved | - | - | on going |
| 4 | SUD1-05-018 | SDR-ST-PRO-S-1260 | Steel Bars | Civil | Short Lead Items | 05 12 00 | Unit | 1 | 1 | 1-Jun-26 | Local trancport | Civil | 22-Jul-26 | 20-Sep-26 | 51 | Approved | - | 90% | on going |
| 5 | SUD1-05-018 | SDR-ST-PRO-S-1270 | Asphalt | Civil | Short Lead Items | 32 12 16 | m3 | 3420 | 3420 | 27-Oct-26 | Local trancport | Civil | 10-Nov-26 | 9-Feb-27 | 14 | Approved | - | 4.30% | on going |
| 6 | SUD1-05-018 | SDR-ST-PRO-S-1140 | LOW VOLTAGE CABLES | Electrical | Short Lead Items | 33 71 00 02 | m | 695 | 695 | 31-Aug-26 | Local trancport | Civil | 11-Sep-26 | 11-Oct-26 | 11 | Approved | - | 100% | Delivered |
| 7 | SUD1-05-018 | SDR-ST-PRO-S-1150 | LOW VOLTAGE DISTRIBUTION Panel | Electrical | Short Lead Items | 33 71 26 | Unit | 1 | 1 | 28-Aug-26 | Local trancport | Civil | 18-Sep-26 | 18-Nov-26 | 32 | Approved | - | - | on going |
| 8 | SUD1-05-018 | SDR-ST-PRO-S-1160 | STREET LIGHTING FEEDER Panel | Electrical | Short Lead Items | 33 71 26 03 | Unit | 2 | 2 | 7-Sep-26 | Local trancport | Civil | 21-Sep-26 | 1-Nov-26 | 14 | Approved | - | - | on going |
| 9 | SUD1-05-018 | SDR-ST-PRO-S-1170 | STREET LIGHTING CABLES | Electrical | Short Lead Items | 33 71 00 01 | Unit | 6800 | 6800 | 31-Aug-26 | Local trancport | Civil | 14-Sep-26 | 14-Nov-26 | 14 | Approved | - | 100% | Delivered |
| 10 | SUD1-05-018 | SDR-ST-PRO-S-1200 | ROAD CROSSING DUCTS Ø110mm | Electrical | Short Lead Items | 33 81 26 | Unit | 104 | 104 | 18-Aug-26 | Local trancport | Civil | 28-Sep-26 | 2-Nov-26 | 19 | Approved | - | 100% | Delivered |
| 12 | SUD1-05-018 | SDR-ST-PRO-S-1230 | CCTV :5MP IP PoE Bullet Camera | Electrical | Short Lead Items | B2.28.20.00.01 | unit | 16 | 16 | 1-Sep-26 | Local trancport | Electrical | 17-Sep-26 | 28-Oct-26 | 16 | Approved | - | - | on going |
| 13 | SUD1-05-018 | SDR-ST-PRO-S-1240 | CCTV :Pole mounted Filed Equipment cabinet (FE | Electrical | Short Lead Items | B2.28.20.00.02 | unit | 4 | 4 | 26-Oct-26 | Local trancport | Electrical | 6-Nov-26 | 5-Jan-27 | 11 | Approved | - | - | on going |
| 14 | SUD1-05-018 | SDR-ST-PRO-S-1250 | VOICE EVACUATION SYSTEM | Electrical | Short Lead Items | 27 40 00 | Unit | 32 | 32 | 29-Oct-26 | Local trancport | Electrical | 11-Nov-26 | 10-Jan-27 | 13 | Approved | - | - | on going |
| 15 | SUD1-05-018 | SDR-ST-PRO-S-1040 | HDPE PIPES & FITTINGS | Mechanical | Short Lead Items | 33 31 23 | m | 2946 | 2946 | 24-Aug-26 | Local trancport | Electrical | 18-Sep-26 | 18-Nov-26 | 25 | Approved | - | 100% | Delivered |
| 16 | SUD1-05-018 | SDR-ST-PRO-S-1050 | CONCRETE PIPES AND FITTINGS | Mechanical | Short Lead Items | 33 42 13 | m | 230 | 230 | 7-Sep-26 | Local trancport | Electrical | 18-Sep-26 | 7-Dec-26 | 11 | Approved | - | 100% | Delivered |
| 19 | SUD1-05-018 | SDR-ST-PRO-S-1090 | MANHOLE, CATCH BASIN & VALVE BOX COVER | Mechanical | Short Lead Items | 33 81 26 | Unit | 16 | 16 | 14-Sep-26 | Local trancport | Electrical | 28-Sep-26 | 7-Dec-26 | 14 | Approved | - | - | |
| 20 | SUD1-05-018 | SDR-ST-PRO-S-1000 | Metal railing for platform | Civil | Long Lead Items | 05 52 00 | m | 440 | 440 | 25-Aug-26 | Local trancport | Electrical | 28-Oct-26 | 2-Feb-27 | 64 | Not submitted | - | - | |
| 21 | SUD1-05-018 | SDR-ST-PRO-S-1020 | Canopy | Civil | Long Lead Items | 03 30 00/03 53 00 | 560 | m2 | m2 | 19-Nov-26 | Local trancport | Mechanical | 22-Dec-26 | 8-Apr-27 | 33 | Not submitted | - | - | |
| 22 | SUD1-05-018 | SDR-ST-PRO-S-1110 | MEDIUM VOLTAGE CABLES DUCT BANKS | Electrical | Long Lead Items | 33 71 00 | m | 105 | 105 | 12-Oct-26 | Local trancport | Mechanical | 29-Oct-26 | 14-Feb-27 | 17 | Not submitted | - | - | |
| 23 | SUD1-05-018 | SDR-ST-PRO-S-1120 | MEDIUM VOLTAGE CABLES | Electrical | Long Lead Items | 33 71 49.23 | Unit | 7120 | 7120 | 12-Oct-26 | Local trancport | Mechanical | 30-Oct-26 | 15-Feb-27 | 18 | Not submitted | - | - | |
| 24 | SUD1-05-018 | SDR-ST-PRO-S-1130 | SUB-STATION | Electrical | Long Lead Items | 33 73 00 | unit | 2 | 2 | 19-Oct-26 | Local trancport | Mechanical | 3-Dec-26 | 4-Mar-27 | 45 | Not submitted | - | - | |
| 25 | SUD1-05-018 | SDR-ST-PRO-S-1180 | LIGHTING POLES | Electrical | Long Lead Items | 33 71 16 | m | 143 | 143 | 19-Oct-26 | Local trancport | Mechanical | 5-Nov-26 | 27-Feb-27 | 17 | Not submitted | - | - | |
| 26 | SUD1-05-018 | SDR-ST-PRO-S-1190 | STREET LIGHTING LUMINAIRE | Electrical | Long Lead Items | 26 56 19 | Unit | 276 | 276 | 10-Nov-26 | Local trancport | Civil | 18-Dec-26 | 25-Mar-27 | 38 | Not submitted | - | - | |
| 27 | SUD1-05-018 | SDR-ST-PRO-S-1220 | Outdoor Lighting Fixtures | Electrical | Long Lead Items | 26 56 00 | Unit | 390 | 390 | 23-Nov-26 | Local trancport | Civil | 10-Dec-26 | 11-Apr-27 | 17 | Not submitted | - | - | |
| 28 | SUD1-05-018 | SDR-ST-PRO-S-1100 | WASHOUT & AIR VALVE, GATE VALVE, BUTTERFLY VALVE | Mechanical | Long Lead Items | 33 14 19 | Unit | 5 | 5 | 26-Oct-26 | Local trancport | Electrical | 8-Dec-26 | 25-Mar-27 | 43 | Approved | - | - | on going |


Data sensitivity - Internal

## Head-Count ( Non Manual)

| MONTHS | Apr-26 | May-26 | Jun-26 | Jul-26 | Aug-26 | Sep-26 | Oct-26 | Nov-26 | Dec-26 | Jan-27 | Feb-27 | Mar-27 | Apr-27 | May-27 | Jun-27 | Jul-27 | Aug-27 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Plan - Monthly | 12 | 16 | 20 | 29 | 30 | 30 | 32 | 32 | 32 | 30 | 28 | 24 | 21 | 20 | 19 | 21 | 15 |
| Planned - Cumulative | 12 | 24 | 40 | 60 | 89 | 119 | 149 | 181 | 213 | 245 | 275 | 303 | 327 | 348 | 368 | 387 | 408 |
| Actual - Monthly | 12 | 16 | 16 | 16 | 22 | 16 | 22 | | | | | | | | | | |
| Actual Cumulative | 12 | 28 | 44 | 60 | 82 | 98 | 120 | | | | | | | | | | |
| Forecast - Monthly | | | | | | | | | | | | | | | | | |
| Saudi Monthly - Actual | | | | | | | | | | | | | | | | | |

## Head-Count (Manual)

| MONTHS | Apr-26 | May-26 | Jun-26 | Jul-26 | Aug-26 | Sep-26 | Oct-26 | Nov-26 | Dec-26 | Jan-27 | Feb-27 | Mar-27 | Apr-27 | May-27 | Jun-27 | Jul-27 | Aug-27 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Plan - Monthly | 18 | 30 | 36 | 41 | 47 | 123 | 185 | 200 | 231 | 226 | 219 | 204 | 203 | 136 | 137 | 106 | 7 |
| Planned - Cumulative | 18 | 48 | 84 | 125 | 172 | 295 | 480 | 680 | 911 | 1137 | 1356 | 1560 | 1762 | 1898 | 2036 | 2141 | 2148 |
| Actual - Monthly | 41 | 48 | 62 | 65 | 31 | 31 | 65 | | | | | | | | | | |
| Actual Cumulative | 41 | 89 | 151 | 216 | 247 | 278 | 343 | | | | | | | | | | |
| Forecast - Monthly | | | | | | | | | | | | | | | | | |
| Saudi - Actual | | | | | | | | | | | | | | | | | |

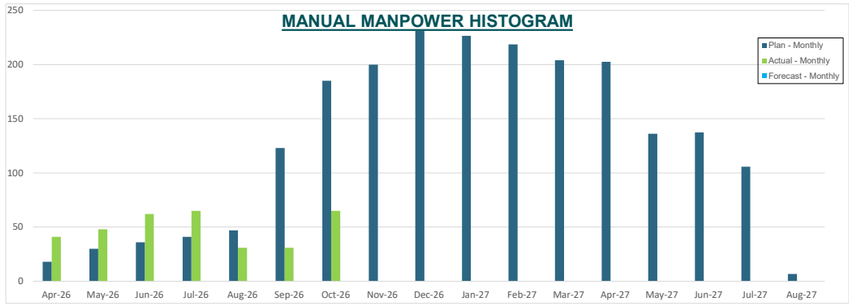


0

| Head-Count (Non-Manual) | | | | |
|---|---|---|---|---|
| Planned | Actual | Variance | Forecast Next Month | Saudi Staff |
| 20 | 22 | 2 | 0 | 3 |

| Head-Count (Manual) | | | | |
|---|---|---|---|---|
| Planned | Actual | Variance | Forecast Next Month | Saudi Staff |
| 40 | 65 | 25 | 0 | 0 |


| Month | Oct-26 | Nov-26 |
|---|---|---|

| Man Power by Trade | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|
| Key Trade | Engineer | Doc. Controller | Proc. Team | Foreman | Draftman | Driver | UnSkilled Labor | Skiled labour | Others | **Total** |
| **Plan** | 2 | 1 | 1 | 2 | 1 | 5 | 15 | 8 | 5 | 40 |
| **Actual** | 10 | 1 | 1 | 3 | 1 | 31 | 20 | 10 | 10 | 87 |

## Equipment

| MONTHS | Apr-26 | May-26 | Jun-26 | Jul-26 | Aug-26 | Sep-26 | Oct-26 | Nov-26 | Dec-26 | Jan-27 | Feb-27 | Mar-27 | Apr-27 | May-27 | Jun-27 | Jul-27 | Aug-27 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Plan - Monthly | 0 | 6 | 6 | 22 | 29 | 48 | 57 | 62 | 46 | 31 | 15 | 14 | 10 | 9 | 8 | 0 | 0 |
| Planned - Cumulative | 0 | 6 | 13 | 19 | 41 | 70 | 118 | 174 | 236 | 282 | 314 | 329 | 342 | 352 | 361 | 369 | 369 |
| Actual - Monthly | 0 | 6 | 14 | 17 | 32 | 18 | 32 | | | | | | | | | | |
| Actual Cumulative | 0 | 6 | 20 | 37 | 69 | 87 | 119 | | | | | | | | | | |
| Forecast - Monthly | | | | | | | | | | | | | | | | | |

| Equipment Count | | | | |
|---|---|---|---|---|
| Planned | Actual | Idle | Variance | Forecast Next Month |
| 29 | 32 | 0 | 3 | 0 |

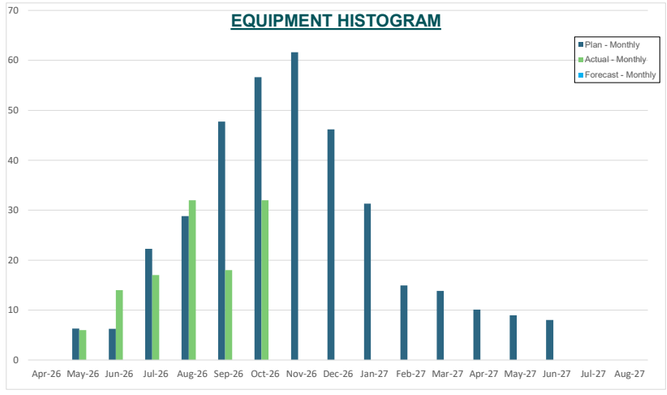


| Type | Pick Up/Car | Bus | Dump Truck | Boom Truck | Generator | CRANE | Showel | Grader | Truck | Water Tank | Finisher | Bobcat | Forklift | JCB | Loader | Boom Truck | Road Marker | Total |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Plan | 1 | 1 | 10 | 0 | 1 | 0 | 0 | 6 | 0 | 0 | 0 | 0 | 0 | 0 | 1 | 2 | 0 | 22 |
| Actual | 2 | 1 | 10 | 0 | 1 | 1 | 1 | 5 | 0 | 2 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 23 |
| Idle | | | | | | | | | | | | | | | | | | 0 |

Data sensitivity - Internal

## Issue Log

| Issue ID | Parent Project ID | Contract / Project ID | Project Name | City | Region | Fund Source | Phase | PM / Owner | Contractor / Designer | Current Status | Description | Priority | Action Required | Date Raised | Status | Duration Elapsed | Expected/Actual Closure | Target Date |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 3120-1 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Access & Permits | Egis / MODON | Technical Development Company for | Close | Noticed a signboard that is fallen and improperly positioned on the ground | Contractor | Assess the damage: Evaluate whether the sign can be repaired and | 2-Sep-26 | Closed | 1 | 2 | 2-Sep-26 |
| 3120-2 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Design / Engineering | Egis / MODON | Technical Development Company for | Close | Waste plastic bottles were scattered on-site, resulting in poor housekeeping. | Contractor | Informed the workgroup about the concern to clean up the area immediately, | 4-Sep-26 | Closed | 1 | 2 | 4-Sep-26 |
| 3120-3 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | A new water filter was installed to ensure clean drinking water. | Contractor | GOOD PRACTICE | 6-Sep-26 | Closed | 1 | 2 | 6-Sep-26 |
| 3120-4 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | It was observed that the subcontractor was carrying out pipe-shifting activities using a wheel loader. | Contractor | Stop Work: Issue an immediate Stop Work Order to halt the pipe- | 8-Sep-26 | Closed | 1 | 2 | 8-Sep-26 |
| 3120-5 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Concrete barriers were misplaced in the area | Contractor/HSE Team | Use appropriate heavy lifting equipment (such as a Boomtruck) to move the | 9-Sep-26 | Closed | 1 | 2 | 9-Sep-26 |
| 3120-6 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Dust created by vehicles moving on project routes | Contractor | Water spraying on vehiceles routes on regular basis | 20-Sep-26 | Closed | 1 | 2 | 20-Sep-26 |
| 3120-7 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Unavaiilibilty of shaded cold water station | Contractor/HSE Team | Provision of shaded cold water station to the site workers. | 20-Sep-26 | Closed | 1 | 2 | 20-Sep-26 |
| 3120-8 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Shallow excavation found without safety and warning signages | Contractor/HSE Team | posting warning and safety signages to increase the visibility and awareness | 24-Sep-26 | Closed | 1 | 2 | 24-Sep-26 |
| 3120-9 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Workers found in equipment working zone | Contractor/HSE Team | Stop movement in man machine/ equioment interface and segrete | 24-Sep-26 | Closed | 1 | 2 | 24-Sep-26 |
| 3120-10 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Directional signages along with concrete jersey barriers and warning signages and tape were found missing | Contractor HSE team | Directional signages along with concrete jersey barriers and warning tape | 3-Oct-26 | Closed | 1 | 2 | 3-Oct-26 |
| 3120-11 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Equipment operator found working zone with Non-compalince to site mandatory PPE. | Contractor consruction /HSE Team | it was ensure to wear the mandatory PPE all the time when present on site | 3-Oct-26 | Closed | 1 | 2 | 3-Oct-26 |
| 3120-12 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Observe Hot Work activity without proper control measure Fire safety | Contractor HSE team | Provide Fire Extinguisher and other requirements as per Hot work requirements. | 10-Oct-26 | Closed | 1 | 2 | 10-Oct-26 |
| 3120-13 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for | Close | Observe site without mandatory PPE complaince | Contractor consruction /HSE Team | Wear the mandatory PPE all the time when present on site | 11-Oct-26 | Closed | 1 | 2 | 11-Oct-26 |
| 3120-14 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Observe dust created at temporary vehicles roads due insuffient dust control measures. | Contractor HSE team | Ensure dust control by regular spraying of water on vehicles routes | 18-Oct-26 | Closed | 1 | 2 | 18-Oct-26 |
| 3120-15 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Observe non complaince of mandatory PPE by equipment operators | Contractor consruction /HSE Team | Wear the mandatory PPE all the time by equipment operators when present on site | 17-Oct-26 | Closed | 1 | 2 | 17-Oct-26 |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |

Data sensitivity - Internal

## Risk Log

| Risk ID | Parent Project ID | Contract / Project ID | Project Name | City | Region | Fund Source | Phase | PM / Owner | Contractor / Designer | Current Status | Category | Risk Title | Description | Evidence / Data | Probability (1-5) | Impact (1-5) | Score | Rating | Mitigation Plan | Date Identified | Status | Target Date | Notes / Updates | Source |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 3120-1 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Access & Permits | Egis / MODON | Technical Development Company for Contracting | Open | Permits/Stakeholder | Pending SAR Fence Permission Affecting Platform and Canopy Works | The required SAR/fence permission to commence the works inside the designated platform area is still pending. | Canopy and platform design/details not received from Client; related shop drawings cannot be finalized; associated procurement and construction activities are dependent on the required | 5 | 5 | 25 | Very High | Expedite the SAR/fence permission through the Client and relevant authorities. Escalate the matter to project | 16/9/2026 | Open | | SAR/fence permission remains outstanding. Platform and canopy works cannot commence until the required permission | SAR/Fence Permission Correspondence, Client Instructions, RFI/Approval Register, Site Records, Project |
| 3120-2 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Design / Engineering | Egis / MODON | Technical Development Company for Contracting | Open | Design/Technical | Outstanding Canopy and Platform Design Affecting Shop Drawing, | The required design/details for the canopy and platform have not | Canopy and platform design/details not received from Client; related shop drawings cannot be finalized; | 5 | 5 | 25 | Very High | Immediately escalate the outstanding design requirement to the | 16/9/2026 | Open | | Project is currently ahead of schedule; however, the Client's outstanding | Client/Consultant Correspondence, RFI, Design/Submittal |
| 3120-3 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Open | Interface/Utilities | Delay in Client Approval for MV Duct Crossings Affecting MV Cable | Client approval is required for the proposed MV duct | MV duct crossing proposal/submission pending Client approval; MV cable | 4 | 4 | 16 | High | Expedite Client review and approval of the MV duct | 16/9/2026 | Open | | Project is currently ahead of schedule. However, pending | MV Duct Crossing Proposal / Client Correspondence / |
| 3120-4 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Open | Authorities / Permits | Delay is receiveing SAR Permit | Affecting Geo technical Report ,Shop Drawing and | Delay in completion date | 4 | 4 | 16 | High | | 2026-05-05 | Close | 2026-06-05 | | |
| 3120-5 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Open | Authorities / Permits | Delay is receiveing Tender drawing for platform | Structure Drawing for Platform | Delay in completion date | 3 | 3 | 12 | M12 | | 2026-05-05 | Close | 2026-06-05 | | |
| 3120-6 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Visibility is low due to strong winds and dust. | Vehicle and machinery collisions, falls from high places, and breathing problems. | Severe site hazards, including vehicle and machinery collisions, respiratory damage from inhaled particles, and structural instability from high | 3 | 3 | 12 | M12 | | 2026-08-04 | Close | 2026-08-04 | Suspending high-risk tasks, controlling vehicle movement, and protecting workers. | |
| 3120-7 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Found a damaged fire extinguisher in the site office area. | May fail during a fire, can leak harmful chemicals or gas, and it can burst or fly apart. | Complete equipment failure during a fire, sudden rupture or explosion of the pressurized metal container, and delayed evacuation or severe personal injury | 2 | 2 | 10 | L4 | | 2026-08-05 | Close | 2026-08-05 | Finding a damaged fire extinguisher requires immediate removal, clear tagging, and professional servicing | |
| 3120-8 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | It was observed that diesel is being stored in plastic containers. | Chemical Breakdown and Leaks, Fuel Contamination, Environmental Spills and Exposure. Fire | Health Risks, Equipment Failure | 2 | 2 | 10 | L4 | | 2026-09-08 | Close | 2026-09-08 | Immediate transfer of the diesel into approved containers and the systematic neutralization of microbial risks | |
| 3120-9 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Due to sand storm dust accumulated and poor visibility on site | Visibility & Safety Hazards, Acute Health Risks, Equipment & Asset Damage | Immediate On-Site Consequences (Due to Poor Visibility), Physical Consequences (Due to Accumulated Dust, Health Hazards for Site Personnel, | 2 | 2 | 10 | L4 | | 2026-09-09 | Close | 2026-09-09 | Halt All Mobile Operations: Order an immediate stop to all heavy equipment operation, crane lifting, and vehicle | |
| 3120-10 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Dust created by vehicles moving on project routes | Visibility & Safety Hazards, Acute Health Risks, Equipment & Asset Damage | Health Issues (repiratory), Equipment collision due low visibility | 3 | 3 | 12 | M8 | | 2026-09-20 | Close | 2026-09-20 | Regular water spraying on vehicle routes | |
| 3120-11 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Shade not available for drinking water | Heat Stress to workers on site due improper arrangement of cold water stations. | Heat stress and heat stroke to workers as workers | 3 | 3 | 12 | M8 | | 2026-09-20 | Close | 2026-09-20 | Shaded water station so that water remains cold for long duration for site workers. | |
| 3120-12 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Shallow excavation found without safety and warning signages | Visibility & Safety Hazards which could lead in workers and equipment fall in to excavation. | Peronsal injuries and equipment damages | 4 | 4 | 25 | Very High | | 2026-09-24 | Close | 2026-09-24 | posting warning and safety signages to increase the visibility and awareness about riks. | |
| 3120-13 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Workers found in equipment working zone | Workers working in machine /equipment working zone are exposed to hit/ struck by the moving machine/ equiomnt. | Peronal injuries from minor to critical injuries and fatalities | 5 | 5 | 25 | Very High | | 2026-09-24 | Close | 2026-09-24 | Stop movement in man machine/ equiomnt interface and segrete equipment and man workino areas. | |
| 3120-14 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | directional signages along with concrete jersey barriers and warning signages and tape were missing | Information signages inncrease Visibility & absence expose workers and equipment to Safety Hazards which | Information signages increase Visibility & absence expose workers and equipment to Safety Hazards which could lead in workers and equipment collsion and | 5 | 5 | 25 | Very High | | 2026-10-03 | Close | 2026-10-03 | Directional signages along with concrete jersey barriers and warning tape with rope have been provided – New | |
| 3120-15 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Found equipment operators without PPE complaince | Mandatory PPE non complaince could to several injuries from minor to major. | Mandatory PPE non complaince could to several injuries from minor to major. | 3 | 3 | 12 | M12 | | 2026-10-03 | Close | 2026-10-03 | Wear the mandatory PPE all the time when present on site | |
| 3120-16 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Observe Hot Work activity without proper control measure Fire safety | High risk of uncontrolled fire resulted from unavialability of fire extinguisher | Peronsal injuries and equipment damages | 5 | 5 | 25 | Very High | | 2026-10-10 | Close | 2026-10-10 | Peronsal injuries and equipment damages | |
| 3120-17 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Observe site without mandatory PPE complaince | Mandatory PPE non complaince could to several injuries from minor to major. | minor and major injuries | 3 | 3 | 12 | M12 | | 2026-10-11 | Close | 2026-10-11 | minor and major injuries | |
| 3120-18 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Observe dust created at temporary vehicles roads due insuffient dust control measures. | Risk of low visibility and respiratory diseases to workers working around | Peronsal injuries and equipment damages | 5 | 5 | 25 | Very High | | 2026-10-18 | Close | 2026-10-18 | Peronsal injuries and equipment damages | |
| 3120-19 | 3120 | 3196 | Construction of Passenger Station for SAR Railway Sudair Industrial City | Sudair | Riyadh Region | Government Funded | Construction / Civil Works | Egis / MODON | Technical Development Company for Contracting | Close | Safety / Quality | Observe site without mandatory PPE complaince by equipment operator | Mandatory PPE non complaince could to several injuries from minor to major. | minor and major injuries | 5 | 5 | 25 | Very High | | 2026-10-17 | Close | 2026-10-17 | minor and major injuries | |

Post Treatment

Data sensitivity - Internal

| Project Name | | | | | | |
|---|---|---|---|---|---|---|
| Item No. | Milestones | Original (Baseline) | Latest | Forecast | | Days Change |
| | **Contract Duration**<br>**Current Contract Weeks : 28 of 69** | | **69** | **69** | | **0** |
| **1** | Project Start Milstone | 07-Apr-26 | 07-Apr-26 | 07-Apr-26 | Finish | **0** |
| **2** | Mobilization Finish Milestone | 06-May-26 | 06-May-26 | 06-May-26 | Finish | **0** |
| **3** | Work Plan and Timeline Milestone | 06-May-26 | 06-May-26 | 16-Aug-26 | UP | **(102)** |
| **4** | Completion of MV Work | 12-May-27 | 22-May-27 | 05-May-27 | UP | **17** |
| **5** | Completion of road and paving works Milestone | 06-Dec-26 | 06-Dec-26 | 31-Dec-26 | UP | **(25)** |
| **6** | Completion of site and platform work Milestone | 20-Jul-27 | 20-Jul-27 | 05-Aug-27 | UP | **(16)** |
| **7** | Completion of finishing works and general site works | 20-Jul-27 | 20-Jul-27 | 06-Aug-27 | UP | **(17)** |
| **8** | Engineering Phase Finish Milestone | 06-May-26 | 06-May-26 | 21-Sep-26 | UP | **(138)** |
| **9** | Procurment Phase Finish Milestone | 15-Apr-27 | 15-Apr-27 | 09-Jun-27 | UP | **(55)** |
| **10** | Project Finish Milstone | 06-Aug-27 | 06-Aug-27 | 06-Aug-27 | - | **0** |

Data sensitivity - Internal

| Primavera P6 Schedule Status | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|
| Project Activities Overview | | | | | | | | | |
| Schedule Statistics | | | | | Active Schedule Activities | | | | |
| Total Act. | Not Started | In Progress | Completed | % | Active | Ahead | On | Behind | Flag |
| 855 | 586 | 46 | 223 | 26.08% | 10 | 15 | 0 | 22 | (7) |
| Critical Path Activities | | | Free Float Management (Total) | | | | Failed Start Activities | | |
| | | | Greater Than 14 Days | | Less Than 14 Days | | | | |
| Last Week | This Week | Diff | Last Week | This Week | Last Week | This Week | Last Week | This Week | Flag |
| 0 | 0 | 0 | 53 | 172 | 598 | 570 | 0 | 2 | -2 |

Data Date 19-Oct-26

Data sensitivity - Internal

| | Baseline Plan | | | Revised / Recovery Plan | | | Earned Value | | | Gross Paid Value | | | Forecast | | | Actual/Fcst vs Plan | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Month | Monthly | Cum | % | Monthly | Cum | % | Monthly | Cum | % | Monthly | Cum | % | Monthly | C um | | Month | Cum |
| Apr-26 | | 0.00 | 0.00% | | | | 0.00 | 0.0 | 0.00% | - | 0.00 | 0.00% | 0.00 | 0.00 | | | 0.00 |
| May-26 | 2034 | 2,034.00 | 0.01% | | | | 397,090.00 | 397,090.00 | 1.20% | - | 0.00 | 0.00% | 397,090.00 | 397,090.00 | | 395,056.00 | 395,056.00 |
| Jun-26 | 4,767.00 | 6,801.00 | 0.02% | | | | 980,202.00 | 1,377,292.0 | 4.16% | - | 0.00 | 0.00% | 980,202.00 | 1,377,292.0 | | 975,435.00 | 975,435.00 |
| Jul-26 | 36,612.00 | 43,413.00 | 0.13% | | | | 1,192,785.00 | 2,570,077.00 | 7.77% | - | 0.00 | 0.00% | 1,192,785.00 | 2,570,077.00 | | 1,156,173.00 | 1,156,173.00 |
| Aug-26 | 3,025,382.00 | 3,068,795.00 | 9.27% | | | | 2,859,151.79 | 5,429,228.79 | 16.41% | - | 0.00 | 0.00% | 2,859,151.79 | 5,429,228.79 | | (166,230.21) | (166,230.21) |
| Sep-26 | 7,642,106.00 | 10,710,901.00 | 32.37% | | | | 482,348.68 | 5,911,577.47 | 17.86% | - | 0.00 | 0.00% | 482,348.68 | 5,911,577.47 | | (7,159,757.32) | (7,159,757.32) |
| Oct-26 | 4,071,913.00 | 14,782,814.00 | 44.67% | | | | 1,183,964.57 | 7,095,542.04 | 21.44% | - | 0.00 | 0.00% | 1,183,964.57 | 7,095,542.04 | 21.44% | (2,887,948.43) | (2,887,948.43) |
| Nov-26 | 2,368,425.00 | 17,151,239.00 | 51.83% | | | | 0.00 | | | - | 0.00 | 0.00% | 6,427,021.61 | 13,522,563.65 | 40.86% | 4,058,596.61 | 4,058,596.61 |
| Dec-26 | 3,761,619.00 | 20,912,858.00 | 63.20% | | | | 0.00 | | | - | 0.00 | 0.00% | 7,390,294.35 | 20,912,858.00 | 63.20% | 3,628,675.35 | 3,628,675.35 |
| Jan-27 | 2,141,463.00 | 23,054,321.00 | 69.67% | | | | 0.00 | | | | | | 2,141,463.00 | 23,054,321.00 | 69.67% | 0.00 | 0.00 |
| Feb-27 | 1,637,344.00 | 24,691,665.00 | 74.62% | | | | 0.00 | | | | | | 1,637,344.00 | 24,691,665.00 | 74.62% | 0.00 | 0.00 |
| Mar-27 | 2,104,692.00 | 26,796,357.00 | 80.98% | | | | 0.00 | | | | | | 2,104,692.00 | 26,796,357.00 | 80.98% | 0.00 | 0.00 |
| Apr-27 | 1,246,419.00 | 28,042,776.00 | 84.74% | | | | 0.00 | | | | | | 1,246,419.00 | 28,042,776.00 | 84.74% | 0.00 | 0.00 |
| May-27 | 955,808.00 | 28,998,584.00 | 87.63% | | | | 0.00 | | | | | | 955,808.00 | 28,998,584.00 | 87.63% | 0.00 | 0.00 |
| Jun-27 | 1,588,983.00 | 30,587,567.00 | 92.44% | | | | 0.00 | | | | | | 1,588,983.00 | 30,587,567.00 | 92.44% | 0.00 | 0.00 |
| Jul-27 | 2,381,575.00 | 32,969,142.00 | 99.63% | | | | 0.00 | | | | | | 2,381,575.00 | 32,969,142.00 | 99.63% | 0.00 | 0.00 |
| Aug-27 | 121,711.00 | 33,090,853.00 | 100.00% | | | | 0.00 | | | | | | 121,711.00 | 33,090,853.00 | 100.00% | 0.00 | 0.00 |

***Actuals thru previous month***

***Forecast current and future months***

**UPDATE ONLY YELLOW PORTION FROM PRIMAVERA EXPORT, IF NEEDED, EXTEND YELLOW PORTION BASED ON SCHEDULE.**

Data sensitivity - Internal

| | Baseline Plan | | | Revised / Recovery Plan | | | Earned Effort % | | | Forecast | | | Achieved/Fcst vs Plan | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Week | Monthly Effort | Cum Effort | Plan Wt.% | MonthlyEffort | Cum Effort | Plan Wt.% | Monthly Wt. | Cum Wt. | Achieved Wt.% | Monthly Wt. | Cum Wt. | Wt.% | Monthly Wt. | Cum Wt. |
| Apr-26 | 36,221 | 36,221 | 5.67% | | | | 22,574 | 22,574.00 | 4.24% | 22,574 | 22,574.00 | | (13,647.30) | (13,647.30) |
| May-26 | 10,471 | 46,693 | 7.31% | | | | 11,000 | 33,574.00 | 8.17% | 11,000 | 33,574.00 | | 528.70 | (13,118.60) |
| Jun-26 | 14,208 | 60,900 | 9.54% | | | | 27,880 | 61,454.00 | 9.63% | 27,880 | 61,454.00 | | 13,672.40 | 553.80 |
| Jul-26 | 16,821 | 77,721 | 12.17% | | | | 20,650 | 82,104.00 | 12.86% | 20,650 | 82,104.00 | | 3,829.20 | 4,383.00 |
| Aug-26 | 62,842 | 140,563 | 22.02% | | | | 44,752 | 126,856.00 | 19.87% | 44,752 | 126,856.00 | | (18,090.30) | (13,707.30) |
| Sep-26 | 54,899 | 195,462 | 30.61% | | | | 21,939 | 148,795.00 | 23.31% | 21,939 | 148,795.00 | | (32,959.50) | (46,666.80) |
| Oct-26 | 49,442 | 244,904 | 38.36% | | | | 17,713 | 166,508.00 | 26.08% | 17,713 | 166,508.00 | 26.08% | (31,729.20) | (78,396.00) |
| Nov-26 | 40,628 | 285,532 | 44.72% | | | | - | | | 119,024 | 285,531.80 | 44.72% | 78,396.00 | 0.00 |
| Dec-26 | 49,100 | 334,632 | 52.41% | | | | - | | | 49,100 | 334,632.20 | 52.41% | 0.00 | 0.00 |
| Jan-27 | 29,292 | 363,925 | 57.00% | | | | - | | | 29,292 | 363,924.50 | 57.00% | 0.00 | 0.00 |
| Feb-27 | 23,424 | 387,349 | 60.67% | | | | | | | 23,424 | 387,348.90 | 60.67% | 0.00 | 0.00 |
| Mar-27 | 56,271 | 443,620 | 69.48% | | | | | | | 56,271 | 443,620.00 | 69.48% | 0.00 | 0.00 |
| Apr-27 | 56,367 | 499,987 | 78.31% | | | | | | | 56,367 | 499,987.40 | 78.31% | 0.00 | 0.00 |
| May-27 | 38,590 | 538,578 | 84.35% | | | | | | | 38,590 | 538,577.50 | 84.35% | 0.00 | 0.00 |
| Jun-27 | 54,479 | 593,056 | 92.89% | | | | | | | 54,479 | 593,056.20 | 92.89% | 0.00 | 0.00 |
| Jul-27 | 44,014 | 637,070 | 99.78% | | | | | | | 44,014 | 637,069.80 | 99.78% | 0.00 | 0.00 |
| Aug-27 | 1,398 | 638,468 | 100.00% | | | | | | | 1,398 | 638,468 | 100.00% | (0.00) | (0.00) |

***Actuals thru previous month***

***Forecast current and future months***

**UPDATE ONLY YELLOW PORTION FROM PRIMAVERA EXPORT, IF NEEDED, EXTEND YELLOW PORTION BASED ON SCHEDULE.**

Data sensitivity - Internal

# Testing and Commissioning

| Item | Planned Start Date | Planned Finish Date | Forecast Start Date | Forecast Finish Date | Actual Start Date | Actual Finish Date | % Completed | Open Comments | Closed Comments |
|---|---|---|---|---|---|---|---|---|---|
| Package 1 | 19-Jan-27 | 06-Aug-27 | 25-Jan-27 | 27-Jul-27 | | | 0% | 0 | 0 |
| Testing and Comissioning | 19-Jan-27 | 06-Aug-27 | 25-Jan-27 | 27-Jul-27 | | | 0% | 0 | 0 |
| Civil Works | 9-May-27 | 31-May-27 | 6-Jun-27 | 23-Jun-27 | | | 0% | 0.00 | 0.00 |
| Storm Water Drainage Network | 19-Jan-27 | 6-Feb-27 | 18-Mar-27 | 5-Apr-27 | | | 0% | 0.00 | 0.00 |
| Sewerage Network | 14-Mar-27 | 31-Mar-27 | 25-Jan-27 | 13-Feb-27 | | | 0% | 0.00 | 0.00 |
| Portable Water | 22-Mar-27 | 8-Apr-27 | 28-Mar-27 | 14-Apr-27 | | | 0% | 0.00 | 0.00 |
| Electrical Works | 18-Jul-27 | 3-Aug-27 | 8-Jul-27 | 26-Jul-27 | | | 0% | 0.00 | 0.00 |
| CCTV Works | 22-Jul-27 | 6-Aug-27 | 12-Jul-27 | 27-Jul-27 | | | 0% | 0.00 | 0.00 |
| Package 3 | 19-Jan-27 | 06-Aug-27 | 25-Jan-27 | 27-Jul-27 | | | 0% | 0 | 0 |
| Testing and Comissioning | 19-Jan-27 | 06-Aug-27 | 25-Jan-27 | 27-Jul-27 | | | 0% | 0 | 0 |
| Civil Works | 9-May-27 | 31-May-27 | 6-Jun-27 | 23-Jun-27 | | | 0% | 0.00 | 0.00 |
| Storm Water Drainage Network | 19-Jan-27 | 6-Feb-27 | 18-Mar-27 | 5-Apr-27 | | | 0% | 0.00 | 0.00 |
| Sewerage Network | 14-Mar-27 | 31-Mar-27 | 25-Jan-27 | 13-Feb-27 | | | 0% | 0.00 | 0.00 |
| Portable Water | 22-Mar-27 | 8-Apr-27 | 28-Mar-27 | 14-Apr-27 | | | 0% | 0.00 | 0.00 |
| Electrical Works | 18-Jul-27 | 3-Aug-27 | 8-Jul-27 | 26-Jul-27 | | | 0% | 0.00 | 0.00 |
| CCTV Works | 22-Jul-27 | 6-Aug-27 | 12-Jul-27 | 27-Jul-27 | | | 0% | 0.00 | 0.00 |
| Total | | | | | | | 0 | 0 | 0 |

Data sensitivity - Internal
