
Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
MLTX-02-004 - Playground Initiative for Western Region (Asir - Jazan - Jeddah) - Update 12-10-2026		182.00	17.98%	12.01%	05-Jul-26	25-Jan-27	11-Aug-26A	02-May-27	$4,525,179.03	$3,023,248.92	$25,173,432.47	-47.00
KEY MILESTONES		169.00	0%	0%	22-Jul-26	25-Jan-27	13-Oct-26	02-May-27	$0.00	$0.00	$0.00	-10.00
GENERAL MILESTONES		0.00	0%	0%	25-Jan-27	25-Jan-27	02-May-27	02-May-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1030	Project Completion	0.00	0%	0%		25-Jan-27		02-May-27	$0.00	$0.00	$0.00	0.00
CONTRACTUAL MILESTONE		169.00	0%	0%	22-Jul-26	25-Jan-27	13-Oct-26	02-May-27	$0.00	$0.00	$0.00	-10.00
MLTX-02-004-MS-1160	Completion of Asir Works	0.00	0%	0%		19-Jan-27		24-Mar-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1170	Completion of Jazan Works	0.00	0%	0%		25-Jan-27		02-May-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1180	Completion of Jeddah Works	0.00	0%	0%		25-Jan-27		06-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1100	Completion of Engineering	0.00	100%	0%		22-Jul-26		29-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1120	Completion of Levelling Works	0.00	100%	0%		09-Aug-26		13-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1070	Completion of Testing & Commissioning	0.00	0%	0%		19-Jan-27		07-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1130	Completion of Toilet Building	0.00	0%	0%		30-Nov-26		09-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1140	Completion of Playground Area	0.00	0%	0%		16-Jan-27		22-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-MS-1150	Completion of Natural Landscape Works	0.00	0%	0%		13-Dec-26		03-Mar-27	$0.00	$0.00	$0.00	0.00
JEDDAH		147.00	29.25%	12.97%	05-Jul-26	25-Jan-27	11-Aug-26A	06-Apr-27	$2,496,544.06	$1,106,672.12	$8,534,963.44	-25.00
MOBILIZATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOPOGRAPHIC SURVEY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SITE FACILITIES & OFFICES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRELIMINARY SUBMITTALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PREPARATIONS & SUBMITTAL BY CONTRACTORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
APPROVALS BY EMPLOYERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ENGINEERING		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMISSION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVALFOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVALFOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALFOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALFOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENTS		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
METHOD STATEMENT SUBMITTAL		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-12330	Preparation & Submission of Method Statement for Fence Works	5.00	100%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENT APPROVAL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRE-QUALIFICATION & MATERIAL		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
PRE-QUALIFICATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER PROOFING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00




© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MATERIAL SUBMITTAL		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-14150	Material Approval for Steel Tension Cables	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-14160	Material Approval for Emergency Doors	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-14170	Material Approval for Pressure Units	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

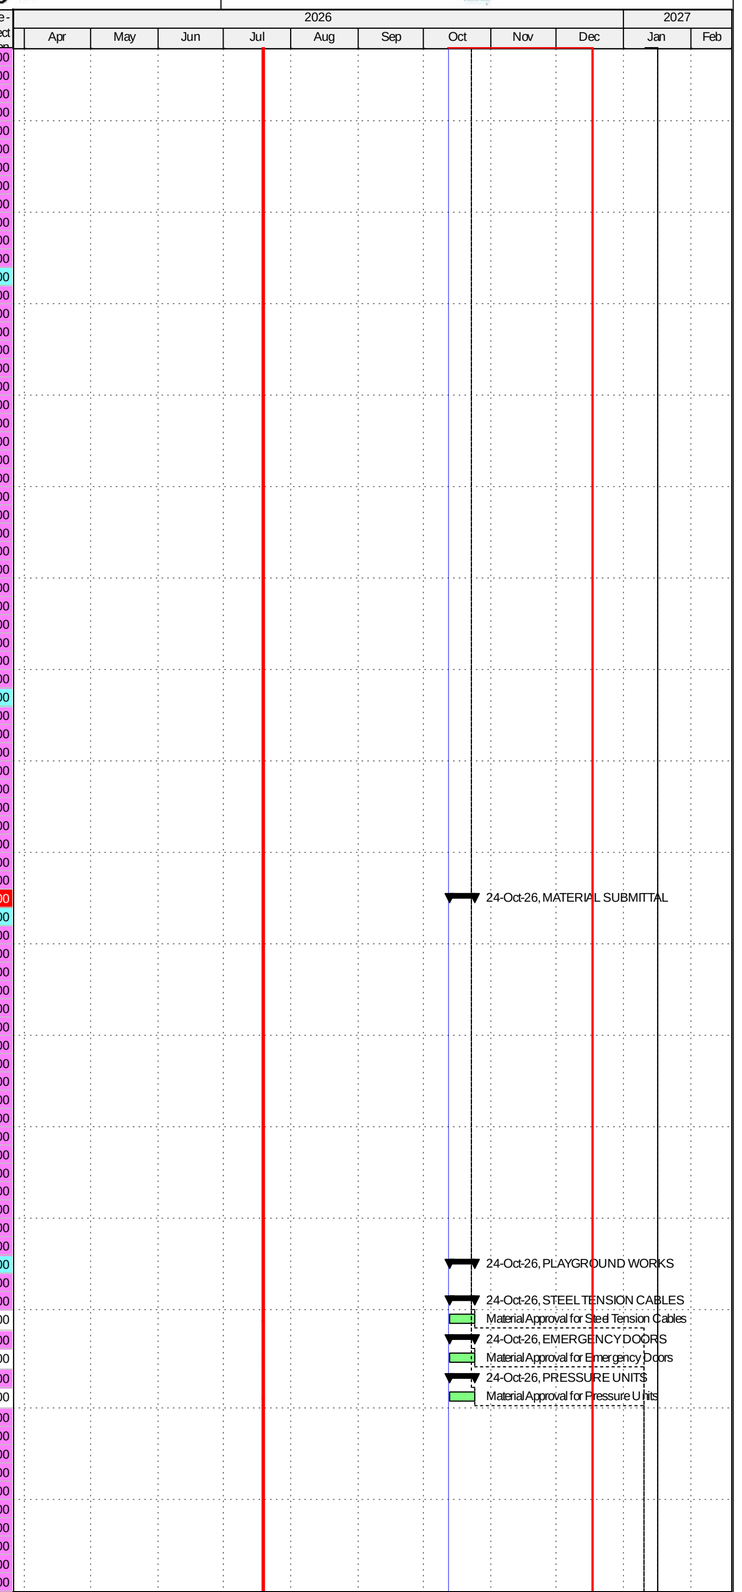


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PROCUREMENT		45.00	0%	0%	05-Jul-26	25-Aug-26	13-Oct-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
SHORT LEAD ITEM		38.00	0%	0%	05-Jul-26	17-Aug-26	13-Oct-26	25-Nov-26	$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11380	Material Delivery for Lighting Fixtures	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11210	PO for Distribution Panels	5.00	100%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		38.00	0%	0%	05-Jul-26	17-Aug-26	13-Oct-26	25-Nov-26	$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		12.00	0%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11860	Material Delivery for Artificial TURF	12.00	100%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		12.00	0%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11880	Material Delivery for Rubber Granules	12.00	100%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		8.00	0%	0%	05-Jul-26	13-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11110	Material Delivery for Interlocking Block Pavers	8.00	100%	0%	05-Jul-26	13-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
MARKING PAINT		17.00	0%	0%	29-Jul-26	17-Aug-26	07-Nov-26	25-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11440	Material Delivery for Marking Paint	17.00	100%	0%	29-Jul-26	17-Aug-26	07-Nov-26	25-Nov-26	$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11740	Material Delivery for Power Cables	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11770	PO for CCTV	6.00	100%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		18.00	0%	0%	05-Jul-26	28-Jul-26	13-Oct-26	02-Nov-26	$0.00	$0.00	$0.00	3.00
MLTX-02-004-PR-11790	PO for Power Outlets/Switches	6.00	100%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11800	Material Delivery for Power Outlets/Switches	6.00	100%	0%	22-Jul-26	28-Jul-26	27-Oct-26	02-Nov-26	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		27.00	0%	0%	05-Jul-26	10-Aug-26	13-Oct-26	12-Nov-26	$0.00	$0.00	$0.00	5.00
INTERLOCKING PAVING		12.00	0%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11840	Material Delivery for Interlocking Block Pavers	12.00	100%	0%	05-Jul-26	18-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		10.00	0%	0%	11-Jul-26	21-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11130	Material Delivery for Pavement Markings	10.00	100%	0%	11-Jul-26	21-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		10.00	0%	0%	11-Jul-26	21-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11160	Material Delivery for Traffic Signs	10.00	100%	0%	11-Jul-26	21-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		8.00	0%	0%	11-Jul-26	19-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11180	Material Delivery for Irrigation Pipes/Sprinkles	8.00	100%	0%	11-Jul-26	19-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		12.00	0%	0%	11-Jul-26	23-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11940	Material Delivery for Agriculture Soil	12.00	100%	0%	11-Jul-26	23-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
TRACK SURFACE		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11960	Material Delivery for Track Surface	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00

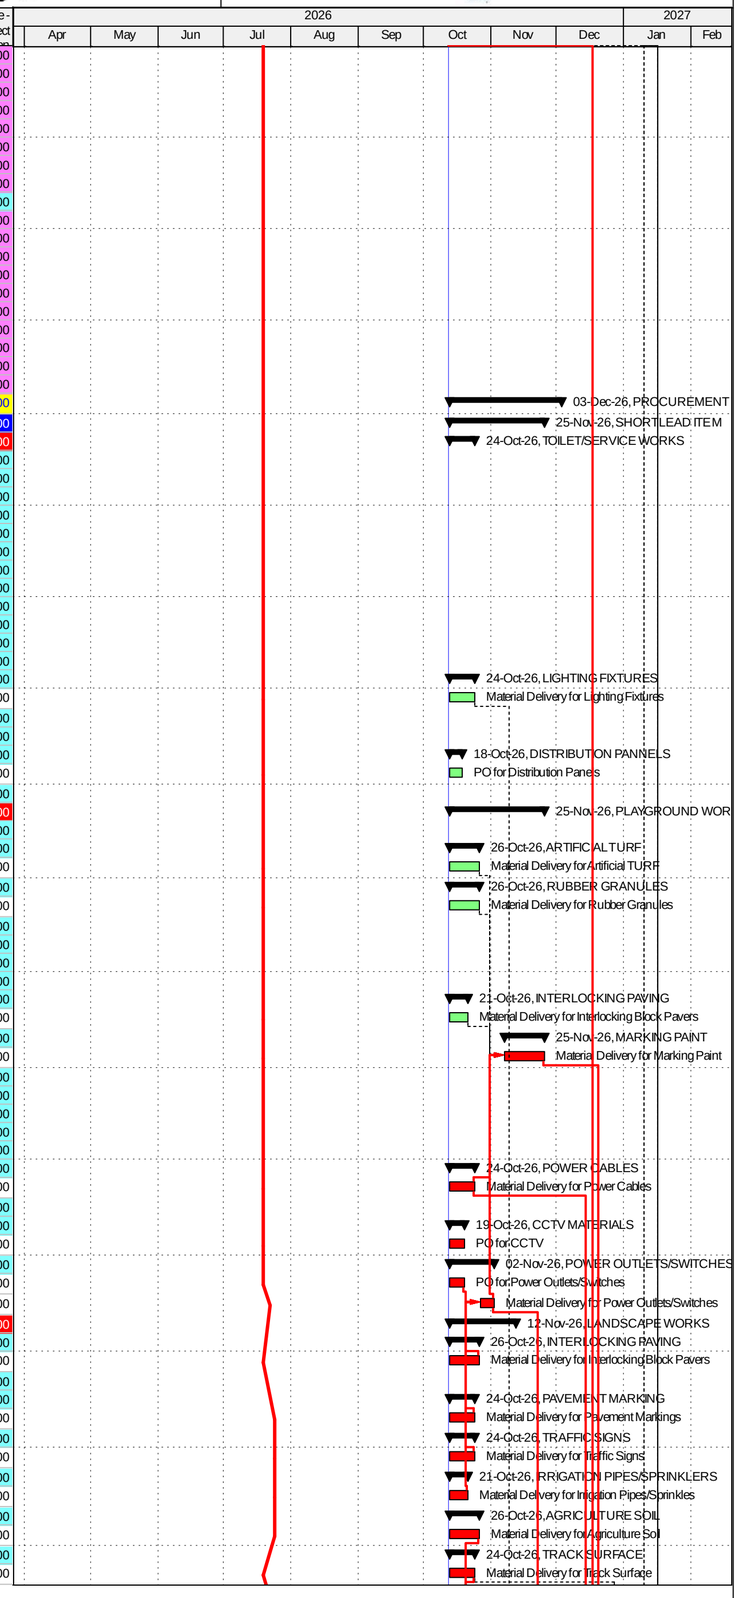

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
GRASS/TREES		15.00	0%	0%	25-Jul-26	10-Aug-26	27-Oct-26	12-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-12000	Material Delivery for Grass/Trees	15.00	100%	0%	25-Jul-26	10-Aug-26	27-Oct-26	12-Nov-26	$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LONG LEAD ITEM		45.00	0%	0%	05-Jul-26	25-Aug-26	13-Oct-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		45.00	0%	0%	05-Jul-26	25-Aug-26	13-Oct-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		34.00	0%	0%	05-Jul-26	18-Aug-26	13-Oct-26	21-Nov-26	$0.00	$0.00	$0.00	5.00
MLTX-02-004-PR-12050	Staging time	7.00	100%	0%	11-Aug-26	18-Aug-26	14-Nov-26	21-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-12010	Material Fabrication for Steel Tension Cables	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		25.00	0%	0%	22-Jul-26	19-Aug-26	31-Oct-26	28-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-12060	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	23-Nov-26	28-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11660	Material Delivery for Emergency Doors	20.00	100%	0%	22-Jul-26	13-Aug-26	31-Oct-26	22-Nov-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		30.00	0%	0%	22-Jul-26	25-Aug-26	31-Oct-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-12070	Staging time	5.00	100%	0%	20-Aug-26	25-Aug-26	29-Nov-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11680	Material Delivery for Pressure Units	20.00	100%	0%	22-Jul-26	13-Aug-26	31-Oct-26	22-Nov-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		25.00	0%	0%	22-Jul-26	19-Aug-26	31-Oct-26	28-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-12080	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	23-Nov-26	28-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11700	Material Delivery for Lock Doors	20.00	100%	0%	22-Jul-26	13-Aug-26	31-Oct-26	22-Nov-26	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONSTRUCTION PHASE		147.00	29.25%	12.97%	12-Sep-26	25-Jan-27	11-Aug-26A	06-Apr-27	$2,496,544.06	$1,106,672.12	$8,534,963.44	-84.00
SITE WORKS		147.00	27.96%	13.85%	12-Sep-26	25-Jan-27	11-Aug-26A	06-Apr-27	$2,223,250.58	$1,101,433.12	$7,951,594.72	-84.00
EARTH WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		147.00	28.31%	13.67%	12-Sep-26	25-Jan-27	16-Aug-26A	06-Apr-27	$2,223,250.58	$1,073,645.62	$7,854,095.70	-80.00
PLAYGROUND AREA		104.00	43.71%	0%	21-Sep-26	05-Jan-27	13-Oct-26	10-Feb-27	$275,438.08	$0.00	$630,093.75	-13.00
FOOTBALL PLAYGROUND		58.00	62.5%	0%	21-Sep-26	21-Nov-26	22-Nov-26	27-Jan-27	$143,812.50	$0.00	$230,100.00	-6.00
MLTX-02-004-CN-13530	Finishing and Surface Finish Works (Football Playground)	15.00	100%	0%	21-Sep-26	08-Oct-26	22-Nov-26	08-Dec-26	$143,812.50	$0.00	$143,812.50	0.00
MLTX-02-004-CN-13540	Install Sport Equipments - Goal / Nets - (Football Playground)	10.00	0%	0%	10-Nov-26	21-Nov-26	17-Jan-27	27-Jan-27	$0.00	$0.00	$71,906.25	0.00
MLTX-02-004-CN-13550	Surface Marking and Painting (Football Playground)	10.00	0%	0%	27-Oct-26	07-Nov-26	27-Dec-26	06-Jan-27	$0.00	$0.00	$14,381.25	0.00
PADEL PLAYGROUND		58.00	55.56%	0%	21-Sep-26	21-Nov-26	22-Nov-26	27-Jan-27	$53,625.00	$0.00	$96,525.00	-6.00
MLTX-02-004-CN-13580	Finishing and Surface Finish Works (Padel Playground)	15.00	100%	0%	21-Sep-26	08-Oct-26	22-Nov-26	08-Dec-26	$53,625.00	$0.00	$53,625.00	0.00
MLTX-02-004-CN-13590	Install Sport Equipments - Goal / Nets - (Padel Playground)	10.00	0%	0%	10-Nov-26	21-Nov-26	17-Jan-27	27-Jan-27	$0.00	$0.00	$32,175.00	0.00
MLTX-02-004-CN-13600	Surface Marking and Painting (Padel Playground)	10.00	0%	0%	10-Nov-26	21-Nov-26	17-Jan-27	27-Jan-27	$0.00	$0.00	$10,725.00	0.00
BASKETBALL PLAYGROUND		55.00	31.25%	0%	10-Oct-26	05-Dec-26	09-Dec-26	10-Feb-27	$78,000.58	$0.00	$249,600.00	-6.00
MLTX-02-004-CN-13630	Finishing and Surface Finish Works (Basketball Playground)	15.00	20%	0%	10-Oct-26	26-Oct-26	09-Dec-26	26-Dec-26	$78,000.58	$0.00	$156,000.00	0.00
MLTX-02-004-CN-13640	Install Sport Equipments - Goal / Nets - (Basketball Playground)	10.00	0%	0%	22-Nov-26	02-Dec-26	28-Jan-27	08-Feb-27	$0.00	$0.00	$78,000.00	0.00
MLTX-02-004-CN-13650	Surface Marking and Painting (Basketball Playground)	12.00	0%	0%	22-Nov-26	05-Dec-26	28-Jan-27	10-Feb-27	$0.00	$0.00	$15,600.00	0.00
PADEL FENCE		26.00	0%	0%	13-Dec-26	05-Jan-27	13-Oct-26	11-Nov-26	$0.00	$0.00	$53,868.75	-5.00
MLTX-02-004-CN-13680	Tempered Glass Fenc Installation and Fixation	10.00	0%	0%	13-Dec-26	23-Dec-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$33,150.00	0.00
MLTX-02-004-CN-13690	Chain Link Fence Installation and Fixation	10.00	0%	0%	13-Dec-26	23-Dec-26	31-Oct-26	10-Nov-26	$0.00	$0.00	$16,575.00	0.00
MLTX-02-004-CN-13700	Install of Fence Gates	11.00	0%	0%	24-Dec-26	05-Jan-27	31-Oct-26	11-Nov-26	$0.00	$0.00	$4,143.75	0.00
CURBSTOEN/INTERLOCK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME		106.00	39.48%	9.66%	12-Sep-26	04-Jan-27	24-Sep-26A	08-Mar-27	$1,947,812.50	$476,531.25	$4,933,500.00	-43.00
CIVIL WORKS		27.00	100%	28.33%	12-Sep-26	05-Oct-26	24-Sep-26A	05-Dec-26	$1,681,875.00	$476,531.25	$1,681,875.00	-42.00
MLTX-02-004-CN-13740	Install of Membrane Covering System (Air Dome)	12.00	100%	0%	21-Sep-26	05-Oct-26	22-Nov-26	05-Dec-26	$560,625.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-13750	Thermal Insulation Works (Air Dome)	6.00	100%	0%	21-Sep-26	28-Sep-26	29-Nov-26	05-Dec-26	$560,625.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-13730	Cable System Installation (Air Dome)	8.00	100%	85%	12-Sep-26	20-Sep-26	24-Sep-26A	21-Nov-26	$560,625.00	$476,531.25	$560,625.00	-42.00
MECHANICAL WORKS		36.00	23.72%	0%	29-Sep-26	09-Nov-26	06-Dec-26	16-Jan-27	$265,937.50	$0.00	$1,121,250.00	0.00
MLTX-02-004-CN-13780	Air Ducts and Grills Installation (Air Dome)	13.00	92.31%	0%	29-Sep-26	13-Oct-26	06-Dec-26	20-Dec-26	$265,937.50	$0.00	$280,312.50	0.00
MLTX-02-004-CN-13790	Air Units Installation (Air Dome)	13.00	0%	0%	14-Oct-26	28-Oct-26	21-Dec-26	04-Jan-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-13800	Exhaust Fans and Ducts Installation (Air Dome)	10.00	0%	0%	29-Oct-26	09-Nov-26	05-Jan-27	16-Jan-27	$0.00	$0.00	$392,437.50	0.00
ELECTRICAL WORKS		66.00	0%	0%	14-Oct-26	04-Jan-27	21-Dec-26	08-Mar-27	$0.00	$0.00	$1,681,875.00	5.00
MLTX-02-004-CN-13810	Light Fixture Works (Air Dome)	15.00	0%	0%	14-Oct-26	31-Oct-26	21-Dec-26	06-Jan-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-13820	Distribution Board and Electrical Works (Air Dome)	15.00	0%	0%	07-Nov-26	23-Nov-26	07-Jan-27	24-Jan-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-13830	External Electrical Connection Works (Air Dome)	15.00	0%	0%	24-Nov-26	10-Dec-26	25-Jan-27	10-Feb-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-13840	Emergency Generator Installation (Air Dome)	11.00	0%	0%	12-Dec-26	23-Dec-26	11-Feb-27	24-Feb-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-13850	Control System Installation (Air Dome)	10.00	0%	0%	24-Dec-26	04-Jan-27	25-Feb-27	08-Mar-27	$0.00	$0.00	$280,312.50	0.00
FINISHES WORKS		28.00	0%	0%	24-Nov-26	26-Dec-26	25-Jan-27	27-Feb-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-13760	Doors Installation Including Emergency, Entrance doors (Air Dome)	15.00	0%	0%	24-Nov-26	10-Dec-26	25-Jan-27	10-Feb-27	$0.00	$0.00	$224,250.00	0.00
MLTX-02-004-CN-13770	Logo and Signs Installation (Air Dome)	13.00	0%	0%	12-Dec-26	26-Dec-26	11-Feb-27	27-Feb-27	$0.00	$0.00	$224,250.00	0.00
IRRIGATION NETWORK		13.00	0%	40.14%	09-Nov-26	21-Nov-26	15-Sep-26A	29-Nov-26	$0.00	$37,180.00	$92,625.00	-53.00
MLTX-02-004-CN-14650	Installing of Bubblers and Spreyers	3.00	0%	0%	18-Nov-26	21-Nov-26	26-Nov-26	29-Nov-26	$0.00	$0.00	$46,150.00	0.00
MLTX-02-004-CN-14640	Installing of Valves and fittings for Irrigation Network	3.00	0%	80%	09-Nov-26	11-Nov-26	15-Sep-26A	19-Nov-26	$0.00	$37,180.00	$46,475.00	-53.00
NATURAL GROUND		5.00	0%	0%	12-Nov-26	17-Nov-26	21-Nov-26	25-Nov-26	$0.00	$0.00	$117,000.00	0.00
MLTX-02-004-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	5.00	0%	0%	12-Nov-26	17-Nov-26	21-Nov-26	25-Nov-26	$0.00	$0.00	$117,000.00	0.00
PLANTING		18.00	0%	0%	22-Nov-26	12-Dec-26	30-Nov-26	20-Dec-26	$0.00	$0.00	$884,633.75	0.00
MLTX-02-004-CN-13480	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	5.00	0%	0%	22-Nov-26	26-Nov-26	30-Nov-26	05-Dec-26	$0.00	$0.00	$321,945.00	0.00
MLTX-02-004-CN-13490	Placement of Lawn Ground Cover (Rolling and Compaction)	7.00	0%	0%	05-Dec-26	12-Dec-26	13-Dec-26	20-Dec-26	$0.00	$0.00	$175,175.00	0.00
MLTX-02-004-CN-13500	Placement and Fixation of Trees	6.00	0%	0%	28-Nov-26	03-Dec-26	06-Dec-26	12-Dec-26	$0.00	$0.00	$387,513.75	0.00
WALKING/BIKE PATHS		8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	20-Dec-26	$0.00	$276,412.50	$552,825.01	-100.00
MLTX-02-004-CN-13430	Bike Path Preparation and Installation Works	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	20-Dec-26	$0.00	$142,045.32	$284,090.63	-100.00
MLTX-02-004-CN-13440	Walking Path Preparation and Installation Works	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	21-Oct-26	$0.00	$134,367.19	$268,734.38	-49.00
GENERAL/FURNITURE		88.00	0%	44.06%	22-Dec-26	25-Jan-27	04-Oct-26A	06-Apr-27	$0.00	$283,521.87	$643,418.20	-125.00
MLTX-02-004-CN-13400	Stamped Concrete Works for LandScape (Including Finishing Works)	7.00	0%	0%	22-Dec-26	29-Dec-26	04-Mar-27	15-Mar-27	$0.00	$0.00	$28,080.00	0.00
MLTX-02-004-CN-13470	Traffic Signs Posts and Poles Installation	5.00	0%	0%	13-Jan-27	18-Jan-27	25-Mar-27	30-Mar-27	$0.00	$0.00	$9,750.00	0.00
MLTX-02-004-CN-13870	Fixation and Installation of Steel Frame for Benches	10.00	0%	0%	22-Dec-26	02-Jan-27	21-Dec-26	31-Dec-26	$0.00	$0.00	$17,276.03	0.00
MLTX-02-004-CN-13880	Fixation and Installation of Benches	9.00	0%	0%	03-Jan-27	12-Jan-27	02-Jan-27	11-Jan-27	$0.00	$0.00	$40,310.73	0.00
MLTX-02-004-CN-13890	Fixation and Installation of Precast Concrete Seats (Rectangular)	9.00	0%	0%	03-Jan-27	12-Jan-27	02-Jan-27	11-Jan-27	$0.00	$0.00	$43,680.00	0.00
MLTX-02-004-CN-13900	Fixation and Installation of Precast Concrete Seats (Circular)	9.00	0%	0%	03-Jan-27	12-Jan-27	02-Jan-27	11-Jan-27	$0.00	$0.00	$17,160.00	0.00

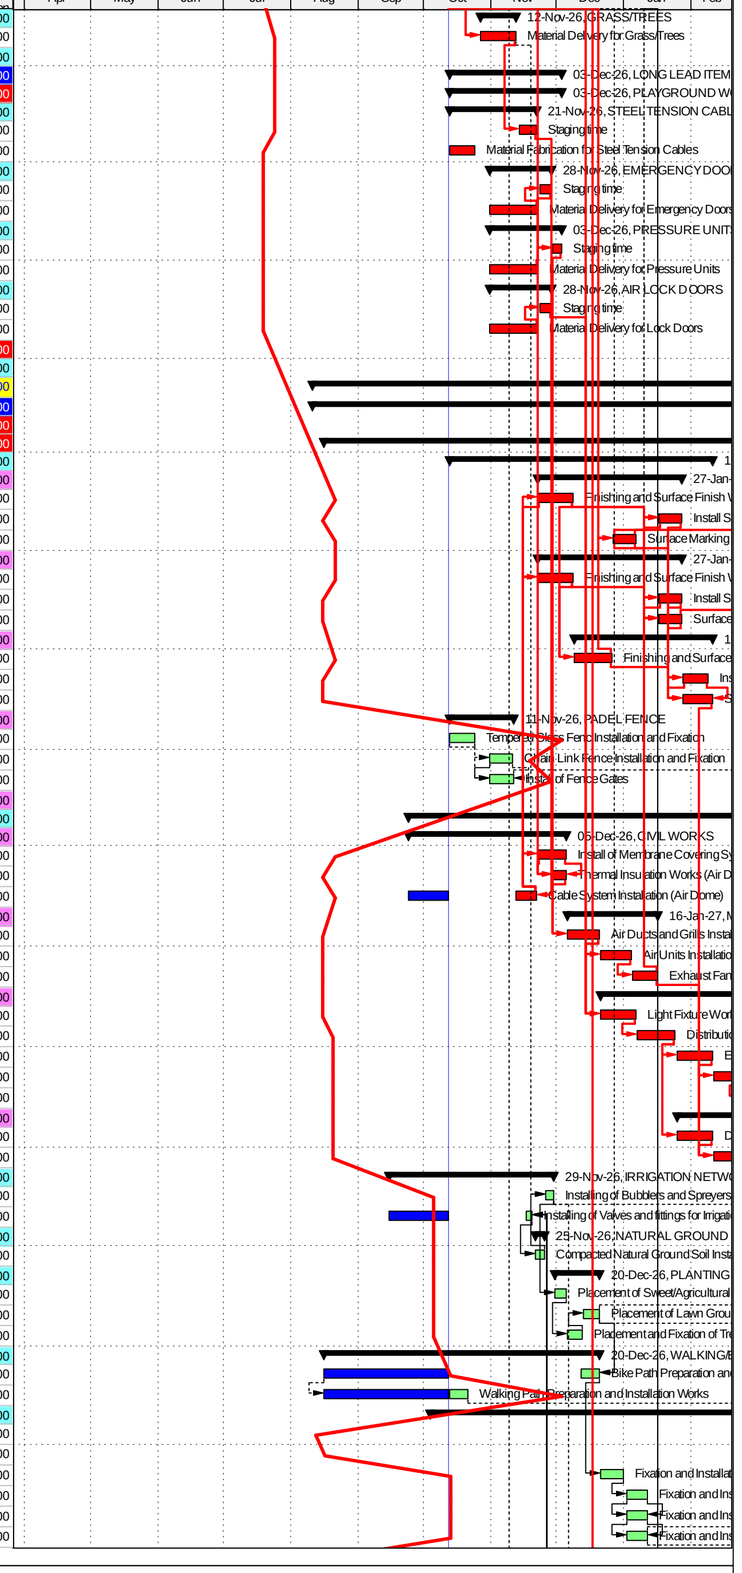


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

2 Weeks look ahead schedule
D.D 12-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
MLTX-02-004-CN-13910	Fixation and Installation of Precast Concrete Trash Bins	11.00	0%	0%	13-Jan-27	25-Jan-27	25-Mar-27	06-Apr-27	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-14360	Installing of Site Light Poles	12.00	0%	60%	30-Dec-26	12-Jan-27	04-Oct-26 A	15-Mar-27	$0.00	$283,521.87	$472,536.45	-124.00
PARKING		53.00	0%	28.5%	30-Dec-26	12-Jan-27	11-Aug-26 A	24-Mar-27	$0.00	$27,787.50	$97,499.02	-177.00
MLTX-02-004-CN-13370	Interlock Installation (8 Cm) for Parking Area (Including Finishing Works)	8.00	0%	0%	04-Jan-27	12-Jan-27	16-Mar-27	24-Mar-27	$0.00	$0.00	$68,249.02	0.00
MLTX-02-004-CN-13380	Site Preparation & Compaction Under Interlock for Parking Area	4.00	0%	95%	30-Dec-26	03-Jan-27	11-Aug-26 A	15-Mar-27	$0.00	$27,787.50	$29,250.00	-177.00
TOILET/SERVICE BUILDING		52.00	46.85%	0.9%	15-Sep-26	30-Nov-26	11-Oct-26 A	12-Dec-26	$273,293.47	$5,239.00	$583,368.72	11.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUB-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUPER-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
UNDER GROUND SEPTIC TANK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ANTI TERMIT CONTROL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POLYETHYLENE SHEET		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EPOXY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MASONARY WORK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANICAL WORK		33.00	75.96%	0%	17-Sep-26	08-Nov-26	13-Oct-26	19-Nov-26	$209,096.88	$0.00	$275,266.88	11.00
HVAC SYSTEM		6.00	0%	0%	02-Nov-26	08-Nov-26	14-Nov-26	19-Nov-26	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-14160	Install and Finish HVAC and Ventilation Works Including Split Air Units	6.00	0%	0%	02-Nov-26	08-Nov-26	14-Nov-26	19-Nov-26	$0.00	$0.00	$14,625.00	0.00
WATER SUPPLY SYSTEM		10.00	91.11%	0%	21-Sep-26	13-Oct-26	13-Oct-26	24-Oct-26	$186,550.00	$0.00	$204,750.00	9.00
MLTX-02-004-CN-14200	Installing of Booster Pump Units Including fittings and accessories	5.00	80%	0%	08-Oct-26	13-Oct-26	19-Oct-26	24-Oct-26	$72,800.00	$0.00	$91,000.00	0.00
MLTX-02-004-CN-14210	Installing of GRP Tanks	5.00	100%	0%	03-Oct-26	07-Oct-26	13-Oct-26	18-Oct-26	$104,000.00	$0.00	$104,000.00	0.00
MLTX-02-004-CN-14600	Installing of Valves and Fittings	4.00	100%	0%	21-Sep-26	26-Sep-26	13-Oct-26	17-Oct-26	$9,750.00	$0.00	$9,750.00	0.00
SEWER/DRAINAGE SYSTEM		25.00	41.8%	0%	17-Sep-26	29-Oct-26	13-Oct-26	10-Nov-26	$22,546.88	$0.00	$53,941.88	11.00
MLTX-02-004-CN-14230	Installing of Plumping Fixtures and Accessories	4.00	100%	0%	29-Sep-26	03-Oct-26	18-Oct-26	21-Oct-26	$10,359.38	$0.00	$10,359.38	0.00
MLTX-02-004-CN-14680	Installing Inspection Chamber for Sewage Network	5.00	100%	0%	17-Sep-26	22-Sep-26	13-Oct-26	18-Oct-26	$12,187.50	$0.00	$12,187.50	0.00
MLTX-02-004-CN-14700	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	3.00	0%	0%	27-Oct-26	29-Oct-26	08-Nov-26	10-Nov-26	$0.00	$0.00	$31,395.00	0.00
FIRE PROTECTION		4.00	0%	0%	04-Nov-26	08-Nov-26	16-Nov-26	19-Nov-26	$0.00	$0.00	$1,950.00	0.00
MLTX-02-004-CN-14240	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	4.00	0%	0%	04-Nov-26	08-Nov-26	16-Nov-26	19-Nov-26	$0.00	$0.00	$1,950.00	0.00
ELECTRICAL WORKS		13.00	0%	0%	02-Nov-26	16-Nov-26	14-Nov-26	28-Nov-26	$0.00	$0.00	$106,322.39	0.00
ROUGH-IN WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FIXTURE WORKS		13.00	0%	0%	02-Nov-26	16-Nov-26	14-Nov-26	28-Nov-26	$0.00	$0.00	$106,322.39	0.00
MLTX-02-004-CN-14250	Installing of Fire automation and Fire Alarm System	7.00	0%	0%	09-Nov-26	16-Nov-26	21-Nov-26	28-Nov-26	$0.00	$0.00	$34,320.00	0.00
MLTX-02-004-CN-14320	Installing and Finalize Works of Lighting Works including Light Fixtures	4.00	0%	0%	04-Nov-26	08-Nov-26	16-Nov-26	19-Nov-26	$0.00	$0.00	$16,050.06	0.00
MLTX-02-004-CN-14340	Installing Data and Telecommunication System with all Accessories	4.00	0%	0%	04-Nov-26	08-Nov-26	16-Nov-26	19-Nov-26	$0.00	$0.00	$18,427.50	0.00
MLTX-02-004-CN-14380	Installing and Finalize Works of Security and Access Control System	6.00	0%	0%	02-Nov-26	08-Nov-26	14-Nov-26	19-Nov-26	$0.00	$0.00	$22,899.83	0.00
MLTX-02-004-CN-14400	Installing and Finalize Works of Lightning Protection System	6.00	0%	0%	02-Nov-26	08-Nov-26	14-Nov-26	19-Nov-26	$0.00	$0.00	$14,625.00	0.00
DOORS/WINDOWS		52.00	36.36%	0%	15-Sep-26	30-Nov-26	13-Oct-26	12-Dec-26	$23,400.00	$0.00	$64,350.00	13.00
MLTX-02-004-CN-14100	Finalize Metal Doors for Toilets Building	12.00	0%	0%	17-Nov-26	30-Nov-26	29-Nov-26	12-Dec-26	$0.00	$0.00	$5,850.00	0.00
MLTX-02-004-CN-14470	Finalize Glazzed Curtain Wall Works	4.00	0%	0%	02-Nov-26	05-Nov-26	14-Nov-26	17-Nov-26	$0.00	$0.00	$35,100.00	0.00
MLTX-02-004-CN-14550	Preliminary Works For Windows/Curtain Wall	2.00	100%	0%	15-Sep-26	16-Sep-26	13-Oct-26	14-Oct-26	$23,400.00	$0.00	$23,400.00	0.00
METAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FINISHING WORKS		29.00	33.16%	6.64%	30-Sep-26	03-Nov-26	11-Oct-26 A	15-Nov-26	$26,171.60	$5,239.00	$78,923.00	-1.00
FLOOR FINISHES		4.00	100%	0%	05-Oct-26	08-Oct-26	13-Oct-26	17-Oct-26	$2,925.00	$0.00	$2,925.00	0.00
MLTX-02-004-CN-14480	Granite Tiles Floor Finish Works	4.00	100%	0%	05-Oct-26	08-Oct-26	13-Oct-26	17-Oct-26	$2,925.00	$0.00	$2,925.00	0.00
WALL FINISHES		29.00	28.9%	8.13%	06-Oct-26	03-Nov-26	11-Oct-26 A	15-Nov-26	$18,629.00	$5,239.00	$64,454.00	-6.00
MLTX-02-004-CN-14460	Phenolic Partitions for Toilets	5.00	0%	0%	21-Oct-26	26-Oct-26	02-Nov-26	07-Nov-26	$0.00	$0.00	$31,200.00	0.00
MLTX-02-004-CN-14570	Glass Partitions including all accessories and doors	5.00	0%	0%	27-Oct-26	01-Nov-26	08-Nov-26	12-Nov-26	$0.00	$0.00	$12,285.00	0.00
MLTX-02-004-CN-14580	Granite Capping for Parpet	2.00	100%	0%	10-Oct-26	11-Oct-26	13-Oct-26	14-Oct-26	$8,151.00	$0.00	$8,151.00	0.00
MLTX-02-004-CN-14670	Painting Finish Works for Internal Walls	2.00	0%	0%	02-Nov-26	03-Nov-26	14-Nov-26	15-Nov-26	$0.00	$0.00	$2,340.00	0.00
MLTX-02-004-CN-14440	Painting Finish Works for External Walls	3.00	100%	50%	06-Oct-26	08-Oct-26	11-Oct-26 A	15-Oct-26	$10,478.00	$5,239.00	$10,478.00	-2.00
CELLING FINISHES		10.00	40%	0%	30-Sep-26	20-Oct-26	13-Oct-26	24-Oct-26	$4,617.60	$0.00	$11,544.00	8.00
MLTX-02-004-CN-14720	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5.00	0%	0%	15-Oct-26	20-Oct-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$6,926.40	0.00
MLTX-02-004-CN-14730	Preliminary Works for Ceiling Painting Works	10.00	100%	0%	30-Sep-26	11-Oct-26	13-Oct-26	24-Oct-26	$4,617.60	$0.00	$4,617.60	0.00
SPECIALTIES WORK		26.00	25%	0%	04-Oct-26	15-Nov-26	28-Oct-26	26-Nov-26	$14,625.00	$0.00	$58,506.46	11.00
MLTX-02-004-CN-14130	Sanitary Fixtures and Accessories Works	4.00	100%	0%	04-Oct-26	07-Oct-26	28-Oct-26	01-Nov-26	$14,625.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-14140	Installation of MODON Logo on the entrance	10.00	0%	0%	04-Nov-26	15-Nov-26	16-Nov-26	26-Nov-26	$0.00	$0.00	$19,506.46	0.00
MLTX-02-004-CN-14590	Installation of Phenolic Locker	2.00	0%	0%	27-Oct-26	28-Oct-26	08-Nov-26	09-Nov-26	$0.00	$0.00	$24,375.00	0.00
TESTING & COMMISSIONING		89.00	0%	0%	01-Dec-26	18-Jan-27	13-Dec-26	30-Mar-27	$0.00	$0.00	$0.00	-47.00
MLTX-02-004-TC-11920	Testing and Commissioning for MEP Works for Playground Area	8.00	0%	0%	05-Jan-27	13-Jan-27	09-Mar-27	21-Mar-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service Building	15.00	0%	0%	01-Dec-26	17-Dec-26	13-Dec-26	29-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11940	Testing and Commissioning for MEP Works for Landscape Works	4.00	0%	0%	14-Jan-27	18-Jan-27	27-Mar-27	30-Mar-27	$0.00	$0.00	$0.00	0.00
ASIR		160.00	4.22%	14.5%	05-Jul-26	24-Jan-27	11-Aug-26 A	06-Apr-27	$331,539.03	$1,137,752.87	$7,848,477.11	-26.00
MOBILIZATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOPOGRAPHIC SURVEY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SITE FACILITIES & OFFICES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRELIMINARY SUBMITTALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PREPARATIONS & SUBMITTAL BY CONTRACTORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
APPROVALS BY EMPLOYERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ENGINEERING		51.00	0%	0%	05-Jul-26	02-Sep-26	13-Oct-26	10-Dec-26	$0.00	$0.00	$0.00	1.00
SHOP DRAWINGS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMISSION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

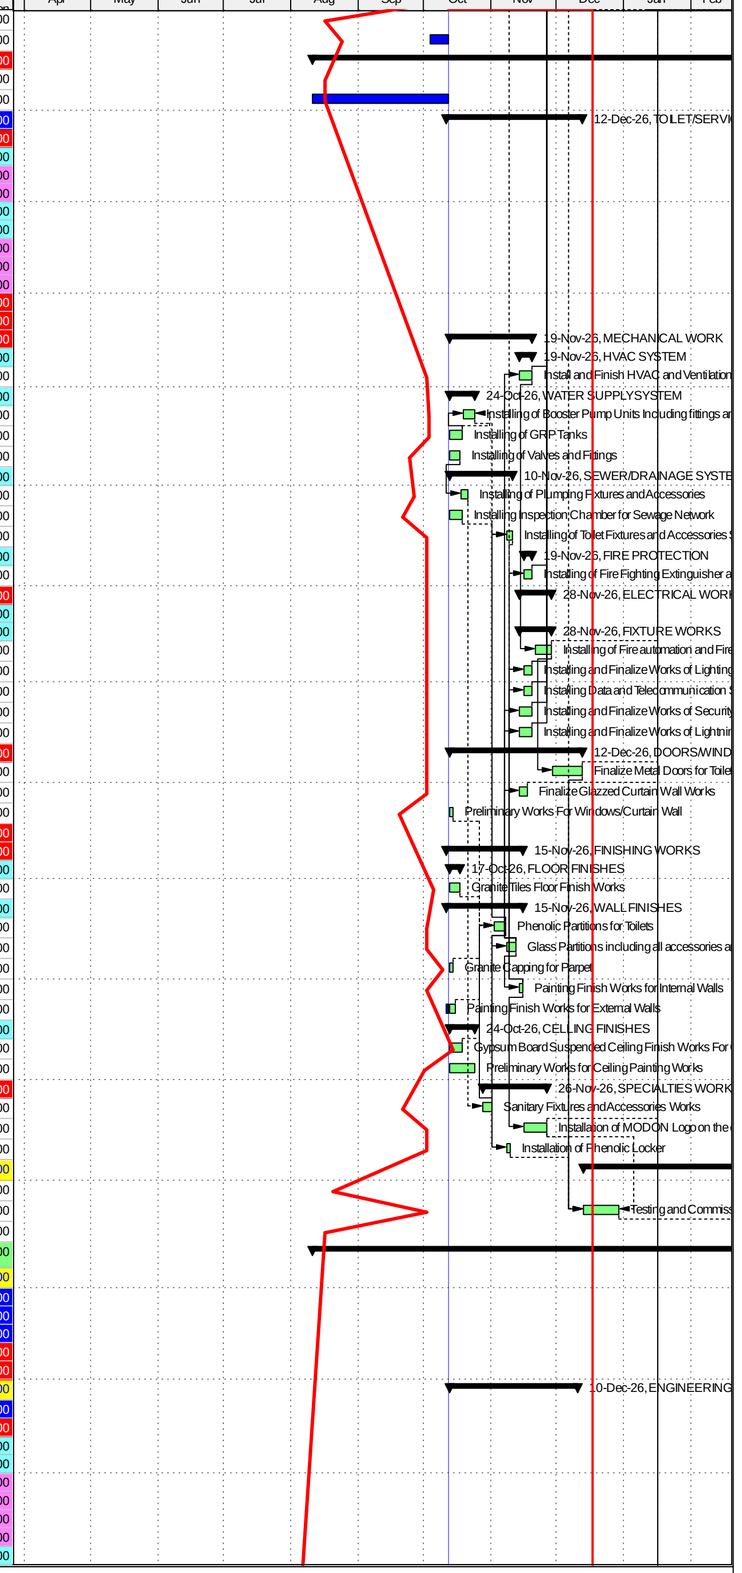


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filters: 2 Weeks Ahead, Remaining work.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVALFOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVALFOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALFOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALFOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENTS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
METHOD STATEMENT SUBMITTAL		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-4140	Preparation & Submission of Method Statement for Fence Works	6.00	100%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENT APPROVAL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRE-QUALIFICATION & MATERIAL		51.00	0%	0%	05-Jul-26	02-Sep-26	13-Oct-26	10-Dec-26	$0.00	$0.00	$0.00	1.00
PRE-QUALIFICATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER PROOFING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

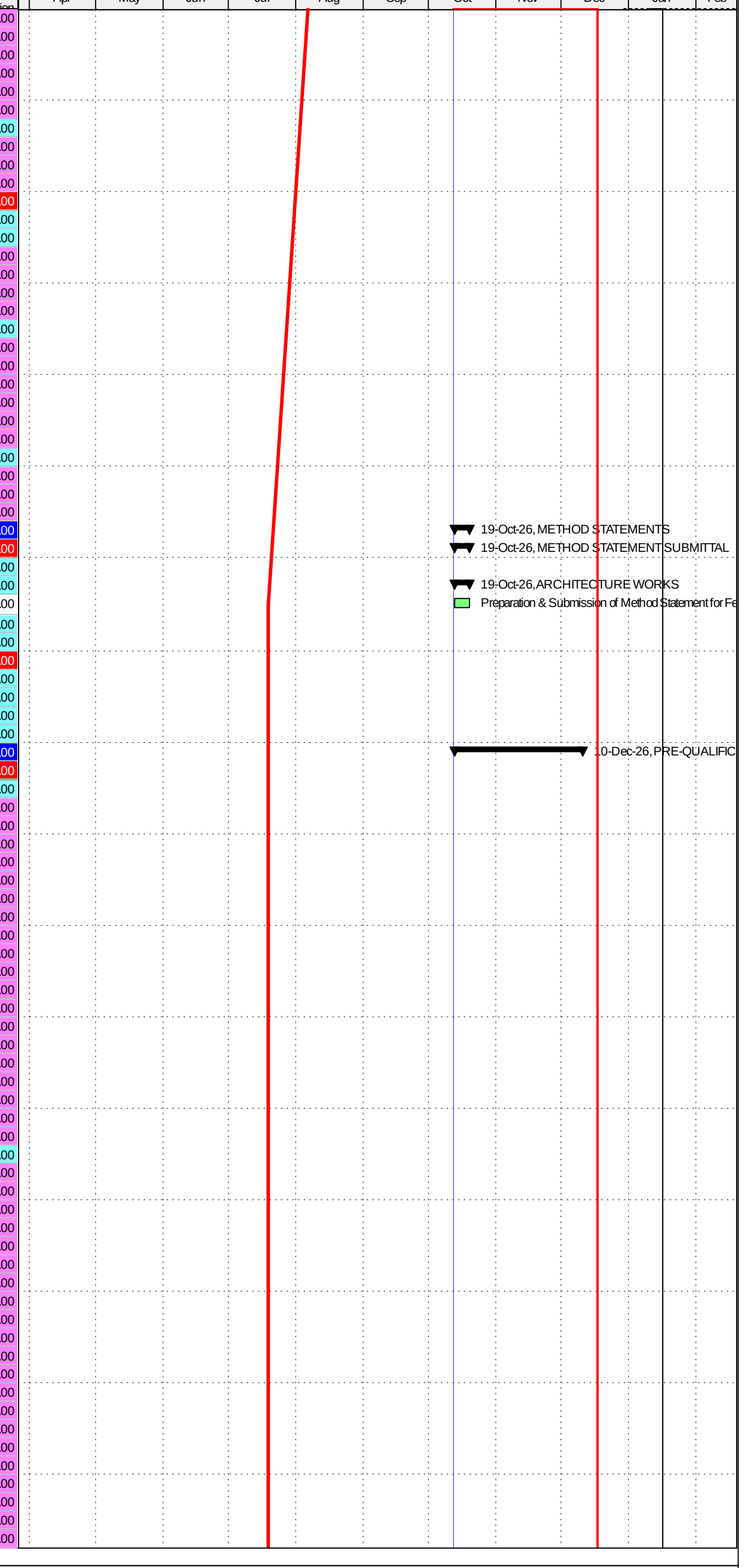


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MATERIAL SUBMITTAL & APPROVAL		51.00	0%	0%	05-Jul-26	02-Sep-26	13-Oct-26	10-Dec-26	$0.00	$0.00	$0.00	1.00
TOILET/SERVICE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		51.00	0%	0%	05-Jul-26	02-Sep-26	13-Oct-26	10-Dec-26	$0.00	$0.00	$0.00	1.00
PVC MEMBRANE		8.00	0%	0%	05-Jul-26	13-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-6880	Material Approval for PVC Membrane	8.00	100%	0%	05-Jul-26	13-Jul-26	13-Oct-26	21-Oct-26	$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		9.00	0%	0%	25-Jul-26	03-Aug-26	02-Nov-26	11-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-6940	Material Approval for Emergency Doors	9.00	100%	0%	25-Jul-26	03-Aug-26	02-Nov-26	11-Nov-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		9.00	0%	0%	04-Aug-26	13-Aug-26	12-Nov-26	22-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-6970	Material Approval for Pressure Units	9.00	100%	0%	04-Aug-26	13-Aug-26	12-Nov-26	22-Nov-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		8.00	0%	0%	16-Aug-26	24-Aug-26	23-Nov-26	01-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-7000	Material Approval for Lock Doors	8.00	100%	0%	16-Aug-26	24-Aug-26	23-Nov-26	01-Dec-26	$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		8.00	0%	0%	25-Aug-26	02-Sep-26	02-Dec-26	10-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-7120	Material Approval for Wire Mesh/Steel Sets	8.00	100%	0%	25-Aug-26	02-Sep-26	02-Dec-26	10-Dec-26	$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PROCUREMENT		89.00	0%	0%	05-Jul-26	17-Oct-26	13-Oct-26	24-Jan-27	$0.00	$0.00	$0.00	0.00
SHORT LEAD ITEM		85.00	0%	0%	05-Jul-26	12-Oct-26	13-Oct-26	19-Jan-27	$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

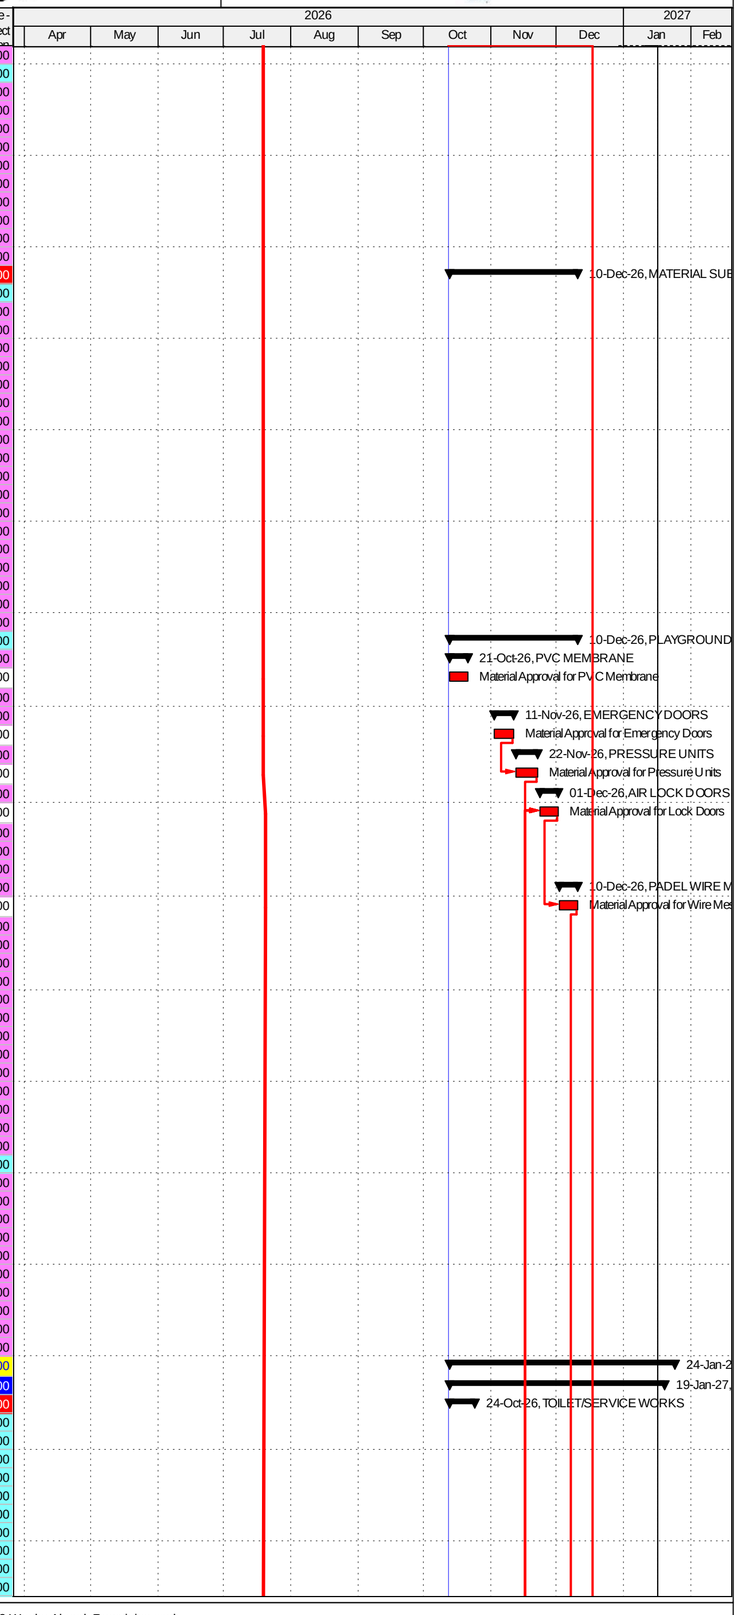


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8450	Material Delivery for Exhaust Fans	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8490	Material Delivery for Lighting Fixtures	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8530	Material Delivery for Switches/Sockets	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		30.00	0%	0%	05-Jul-26	01-Sep-26	13-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	21.00
PVC MEMBRANE		4.00	0%	0%	05-Jul-26	08-Jul-26	13-Oct-26	17-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8650	Material Delivery for PVC Membrane	4.00	100%	0%	05-Jul-26	08-Jul-26	13-Oct-26	17-Oct-26	$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9070	Material Delivery for Interlocking Block Pavers	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MARKING PAINT		7.00	0%	0%	11-Jul-26	18-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9110	Material Delivery for Marking Paint	7.00	100%	0%	11-Jul-26	18-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		10.00	0%	0%	04-Aug-26	15-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9350	Material Delivery for Power Cables	10.00	100%	0%	04-Aug-26	15-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		30.00	0%	0%	12-Jul-26	01-Sep-26	13-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	15.00
MLTX-02-004-PR-9410	PO for CCTV	5.00	100%	0%	12-Jul-26	16-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9430	Material Delivery for CCTV	15.00	100%	0%	16-Aug-26	01-Sep-26	31-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		85.00	0%	0%	12-Aug-26	12-Oct-26	13-Oct-26	19-Jan-27	$0.00	$0.00	$0.00	-33.00
INTERLOCKING PAVING		12.00	0%	0%	02-Sep-26	15-Sep-26	17-Nov-26	30-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9520	Material Delivery for Interlocking Block Pavers	12.00	100%	0%	02-Sep-26	15-Sep-26	17-Nov-26	30-Nov-26	$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		10.00	0%	0%	12-Aug-26	23-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9600	Material Delivery for Pavement Markings	10.00	100%	0%	12-Aug-26	23-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		14.00	0%	0%	16-Sep-26	03-Oct-26	26-Dec-26	10-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9620	PO for Traffic Signs	5.00	100%	0%	16-Sep-26	21-Sep-26	26-Dec-26	30-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9640	Material Delivery for Traffic Signs	9.00	100%	0%	22-Sep-26	03-Oct-26	31-Dec-26	10-Jan-27	$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		8.00	0%	0%	18-Aug-26	26-Aug-26	05-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9680	Material Delivery for Irrigation Pipes/Sprinkles	8.00	100%	0%	18-Aug-26	26-Aug-26	05-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		17.00	0%	0%	22-Sep-26	12-Oct-26	31-Dec-26	19-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9700	PO for Agriculture Soil	5.00	100%	0%	22-Sep-26	28-Sep-26	31-Dec-26	05-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9720	Material Delivery for Agriculture Soil	12.00	100%	0%	29-Sep-26	12-Oct-26	06-Jan-27	19-Jan-27	$0.00	$0.00	$0.00	0.00
TRACK SURFACE		15.00	0%	0%	05-Sep-26	21-Sep-26	14-Dec-26	30-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9740	PO for Track Surface	5.00	100%	0%	05-Sep-26	09-Sep-26	14-Dec-26	19-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9760	Material Delivery for Track Surface	10.00	100%	0%	10-Sep-26	21-Sep-26	20-Dec-26	30-Dec-26	$0.00	$0.00	$0.00	0.00
GRASS/TREES		20.00	0%	0%	10-Sep-26	04-Oct-26	20-Dec-26	11-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9780	PO for Grass/Trees	5.00	100%	0%	10-Sep-26	15-Sep-26	20-Dec-26	24-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9800	Material Delivery for Grass/Trees	15.00	100%	0%	16-Sep-26	04-Oct-26	26-Dec-26	11-Jan-27	$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LONG LEAD ITEM		69.00	0%	0%	28-Jul-26	17-Oct-26	05-Nov-26	24-Jan-27	$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		69.00	0%	0%	28-Jul-26	17-Oct-26	05-Nov-26	24-Jan-27	$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		36.00	0%	0%	05-Sep-26	17-Oct-26	14-Dec-26	24-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8690	Material Delivery for Steel Tension Cables	29.00	100%	0%	05-Sep-26	08-Oct-26	14-Dec-26	16-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9890	Staging time	7.00	42.86%	0%	10-Oct-26	17-Oct-26	17-Jan-27	24-Jan-27	$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		33.00	0%	0%	28-Jul-26	03-Sep-26	05-Nov-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8730	Material Delivery for Emergency Doors	25.00	100%	0%	28-Jul-26	25-Aug-26	05-Nov-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9900	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	05-Dec-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		33.00	0%	0%	28-Jul-26	03-Sep-26	05-Nov-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8770	Material Delivery for Pressure Units	25.00	100%	0%	28-Jul-26	25-Aug-26	05-Nov-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9910	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	05-Dec-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		33.00	0%	0%	28-Jul-26	03-Sep-26	05-Nov-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-8810	Material Delivery for Lock Doors	25.00	100%	0%	28-Jul-26	25-Aug-26	05-Nov-26	03-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9920	Staging time	8.00	100%	0%	26-Aug-26	03-Sep-26	05-Dec-26	13-Dec-26	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONSTRUCTION PHASE		158.00	4.22%	14.5%	19-Jul-26	24-Jan-27	11-Aug-26	04-Apr-27	$331,539.03	$1,137,752.87	$7,848,477.11	-36.00
SITE WORKS		129.00	0.26%	15.52%	12-Oct-26	24-Jan-27	11-Aug-26	04-Apr-27	$18,590.00	$1,122,805.54	$7,234,629.33	-108.00
EARTH WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		129.00	0.26%	15.52%	12-Oct-26	24-Jan-27	11-Aug-26	04-Apr-27	$18,590.00	$1,122,805.54	$7,234,629.33	-108.00
PLAYGROUND AREA		120.00	3.07%	0%	12-Oct-26	04-Jan-27	01-Nov-26	24-Mar-27	$18,590.00	$0.00	$606,368.75	-47.00
FOOTBALL PLAYGROUND		39.00	0%	0%	29-Oct-26	13-Dec-26	25-Jan-27	15-Mar-27	$0.00	$0.00	$230,100.00	0.00
MLTX-02-004-CN-10040	Finishing and Surface Finish Works (Football Playground)	30.00	0%	0%	29-Oct-26	02-Dec-26	25-Jan-27	01-Mar-27	$0.00	$0.00	$143,812.50	0.00
MLTX-02-004-CN-10050	Install Sport Equipments - Goal / Nets - (Football Playground)	9.00	0%	0%	03-Dec-26	13-Dec-26	02-Mar-27	15-Mar-27	$0.00	$0.00	$71,906.25	0.00
MLTX-02-004-CN-10060	Surface Marking and Painting (Football Playground)	8.00	0%	0%	03-Dec-26	12-Dec-26	02-Mar-27	14-Mar-27	$0.00	$0.00	$14,381.25	0.00

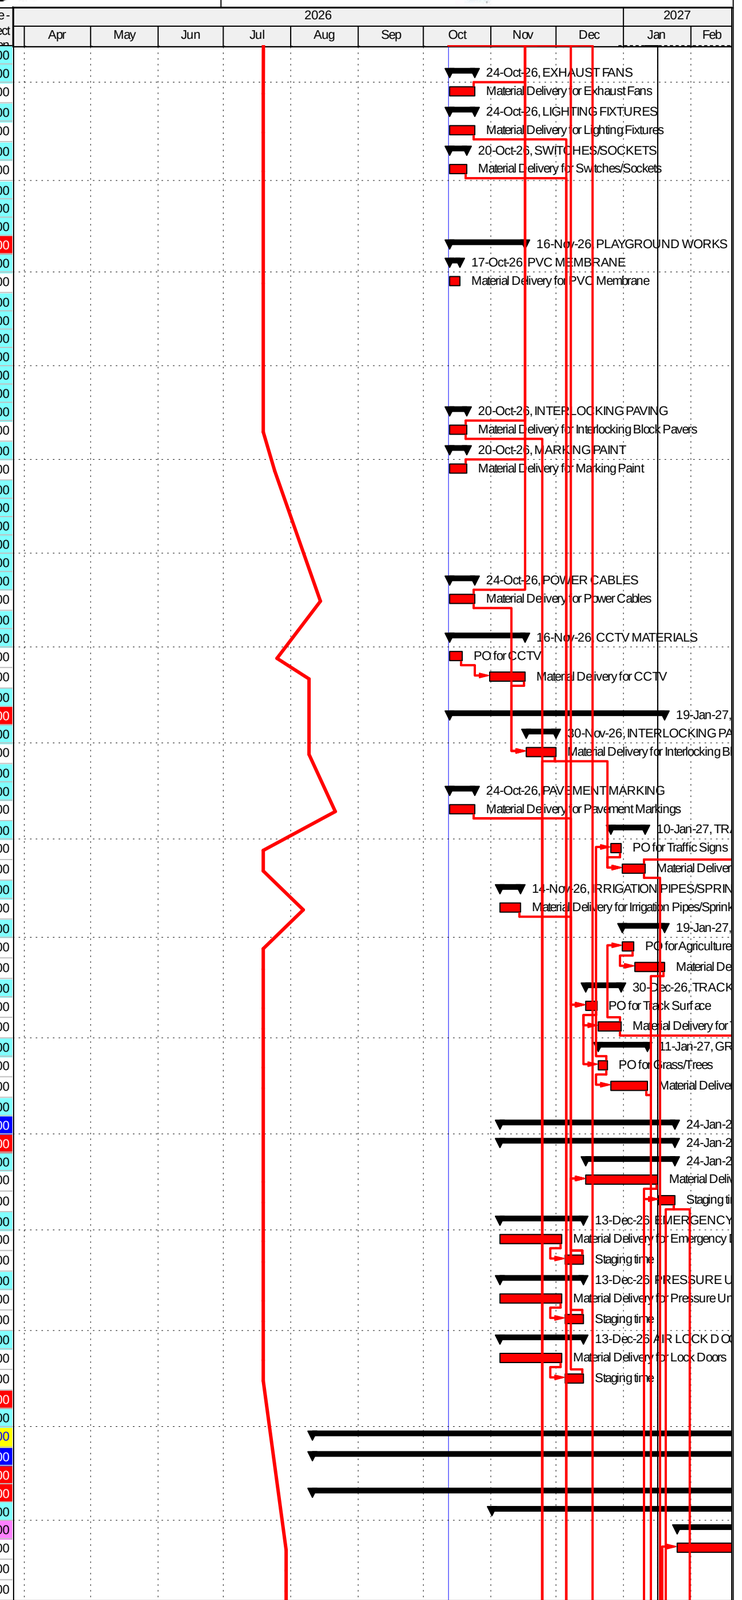

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
PADEL PLAYGROUND		10.00	0%	0%	03-Dec-26	14-Dec-26	02-Mar-27	16-Mar-27	$0.00	$0.00	$42,900.00	0.00
MLTX-02-004-CN-10110	Install Sport Equipments - Goal / Nets - (Padel Playground)	10.00	0%	0%	03-Dec-26	14-Dec-26	02-Mar-27	16-Mar-27	$0.00	$0.00	$32,175.00	0.00
MLTX-02-004-CN-10120	Surface Marking and Painting (Padel Playground)	8.00	0%	0%	03-Dec-26	12-Dec-26	04-Mar-27	16-Mar-27	$0.00	$0.00	$10,725.00	0.00
BASKETBALL PLAYGROUND		17.00	0%	0%	03-Dec-26	20-Dec-26	02-Mar-27	24-Mar-27	$0.00	$0.00	$93,600.00	-2.00
MLTX-02-004-CN-10210	Install Sport Equipments - Goal / Nets - (Basketball Playground)	15.00	0%	0%	03-Dec-26	20-Dec-26	02-Mar-27	22-Mar-27	$0.00	$0.00	$78,000.00	0.00
MLTX-02-004-CN-10220	Surface Marking and Painting (Basketball Playground)	7.00	0%	0%	13-Dec-26	20-Dec-26	17-Mar-27	24-Mar-27	$0.00	$0.00	$15,600.00	0.00
PADEL FENCE		4.00	0%	0%	31-Dec-26	04-Jan-27	01-Nov-26	04-Nov-26	$0.00	$0.00	$53,868.75	0.00
MLTX-02-004-CN-10260	Tempered Glass Fenc Installation and Fixation	2.00	0%	0%	31-Dec-26	02-Jan-27	01-Nov-26	02-Nov-26	$0.00	$0.00	$33,150.00	0.00
MLTX-02-004-CN-10270	Chain Link Fence Installation and Fixation	2.00	0%	0%	03-Jan-27	04-Jan-27	03-Nov-26	04-Nov-26	$0.00	$0.00	$16,575.00	0.00
MLTX-02-004-CN-10280	Install of Fence Gates	2.00	0%	0%	03-Jan-27	04-Jan-27	03-Nov-26	04-Nov-26	$0.00	$0.00	$4,143.75	0.00
CURBSTOEN/INTERLOCK		10.00	10%	0%	12-Oct-26	22-Oct-26	01-Dec-26	12-Dec-26	$18,590.00	$0.00	$185,900.00	0.00
MLTX-02-004-CN-10140	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	10.00	10%	0%	12-Oct-26	22-Oct-26	01-Dec-26	12-Dec-26	$18,590.00	$0.00	$185,900.00	0.00
AIR DOME		63.00	0%	12.5%	18-Oct-26	31-Dec-26	24-Sep-26 A	25-Mar-27	$0.00	$616,687.50	$4,933,500.00	-88.00
CIVIL WORKS		31.00	0%	30%	18-Oct-26	24-Nov-26	24-Sep-26 A	11-Feb-27	$0.00	$504,562.50	$1,681,875.00	-88.00
MLTX-02-004-CN-10360	Install of Membrane Covering System (Air Dome)	14.00	0%	0%	09-Nov-26	24-Nov-26	27-Jan-27	11-Feb-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-10370	Thermal Insulation Works (Air Dome)	14.00	0%	0%	09-Nov-26	24-Nov-26	27-Jan-27	11-Feb-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-10340	Cable System Installation (Air Dome)	10.00	0%	90%	18-Oct-26	28-Oct-26	24-Sep-26 A	24-Jan-27	$0.00	$504,562.50	$560,625.00	-95.00
MECHANICAL WORKS		13.00	0%	0%	25-Nov-26	09-Dec-26	13-Feb-27	28-Feb-27	$0.00	$0.00	$1,121,250.00	0.00
MLTX-02-004-CN-10410	Air Ducts and Grills Installation (Air Dome)	10.00	0%	0%	25-Nov-26	06-Dec-26	13-Feb-27	24-Feb-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-10420	Air Units Installation (Air Dome)	13.00	0%	0%	25-Nov-26	09-Dec-26	13-Feb-27	28-Feb-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-10430	Exhaust Fans and Ducts Installation (Air Dome)	7.00	0%	0%	25-Nov-26	02-Dec-26	13-Feb-27	20-Feb-27	$0.00	$0.00	$392,437.50	0.00
ELECTRICAL WORKS		22.00	0%	6.67%	10-Dec-26	31-Dec-26	07-Oct-26 A	25-Mar-27	$0.00	$112,125.00	$1,681,875.00	-123.00
MLTX-02-004-CN-10460	Distribution Board and Electrical Works (Air Dome)	3.00	0%	0%	15-Dec-26	17-Dec-26	01-Mar-27	03-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-10470	External Electrical Connection Works (Air Dome)	4.00	0%	0%	19-Dec-26	22-Dec-26	04-Mar-27	08-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-10480	Emergency Generator Installation (Air Dome)	4.00	0%	0%	23-Dec-26	27-Dec-26	09-Mar-27	16-Mar-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-10490	Control System Installation (Air Dome)	4.00	0%	0%	28-Dec-26	31-Dec-26	22-Mar-27	25-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-10450	Light Fixture Works (Air Dome)	4.00	0%	40%	10-Dec-26	14-Dec-26	07-Oct-26 A	28-Feb-27	$0.00	$112,125.00	$280,312.50	-119.00
FINISHES WORKS		15.00	0%	0%	10-Dec-26	27-Dec-26	01-Mar-27	21-Mar-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-10380	Doors Installation Including Emergency, Entrance doors (Air Dome)	6.00	0%	0%	10-Dec-26	16-Dec-26	01-Mar-27	07-Mar-27	$0.00	$0.00	$224,250.00	0.00
MLTX-02-004-CN-10390	Logo and Signs Installation (Air Dome)	9.00	0%	0%	17-Dec-26	27-Dec-26	08-Mar-27	21-Mar-27	$0.00	$0.00	$224,250.00	0.00
IRRIGATION NETWORK		43.00	0%	40.14%	21-Oct-26	04-Nov-26	24-Sep-26 A	23-Jan-27	$0.00	$37,180.00	$92,625.00	-91.00
MLTX-02-004-CN-11460	Installing of Bubblers and Spreyers	3.00	0%	0%	02-Nov-26	04-Nov-26	20-Jan-27	23-Jan-27	$0.00	$0.00	$46,150.00	0.00
MLTX-02-004-CN-11450	Installing of Valves and fittings for Irrigation Network	4.00	0%	80%	21-Oct-26	25-Oct-26	24-Sep-26 A	15-Dec-26	$0.00	$37,180.00	$46,475.00	-67.00
NATURAL GROUND		6.00	0%	0%	26-Oct-26	01-Nov-26	21-Dec-26	27-Dec-26	$0.00	$0.00	$80,291.25	0.00
MLTX-02-004-CN-10550	Compacted Natural Ground Soil Installation Works for Landscape	6.00	0%	0%	26-Oct-26	01-Nov-26	21-Dec-26	27-Dec-26	$0.00	$0.00	$80,291.25	0.00
PLANTING		33.00	0%	0%	05-Nov-26	13-Dec-26	24-Jan-27	03-Mar-27	$0.00	$0.00	$597,837.50	0.00
MLTX-02-004-CN-10570	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	3.00	0%	0%	05-Nov-26	08-Nov-26	24-Jan-27	26-Jan-27	$0.00	$0.00	$186,420.00	0.00
MLTX-02-004-CN-10580	Placement of Lawn Ground Cover (Rolling and Compaction)	3.00	0%	0%	10-Dec-26	13-Dec-26	01-Mar-27	03-Mar-27	$0.00	$0.00	$175,175.00	0.00
MLTX-02-004-CN-10590	Placement and Fixation of Trees	3.00	0%	0%	07-Dec-26	09-Dec-26	25-Feb-27	28-Feb-27	$0.00	$0.00	$236,242.50	0.00
WALKING/BIKE PATHS		12.00	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	03-Mar-27	$0.00	$138,206.39	$276,412.77	-162.00
MLTX-02-004-CN-10510	Bike Path Preparation and Installation Works	12.00	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	03-Mar-27	$0.00	$71,022.68	$142,045.36	-162.00
MLTX-02-004-CN-10520	Walking Path Preparation and Installation Works	12.00	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	26-Oct-26	$0.00	$67,183.70	$134,367.41	-53.00
GENERAL/FURNITURE		24.00	0%	51.07%	28-Dec-26	24-Jan-27	01-Oct-26 A	04-Apr-27	$0.00	$330,731.65	$647,594.06	-131.00
MLTX-02-004-CN-10610	Stamped Concrete Works for LandScape (Including Finishing Works)	9.00	0%	0%	28-Dec-26	06-Jan-27	04-Mar-27	17-Mar-27	$0.00	$0.00	$42,068.52	0.00
MLTX-02-004-CN-10630	Fixation and Installation of Steel Frame for Benches	7.00	0%	0%	28-Dec-26	04-Jan-27	04-Mar-27	15-Mar-27	$0.00	$0.00	$17,276.03	0.00
MLTX-02-004-CN-10640	Fixation and Installation of Benches	7.00	0%	0%	05-Jan-27	12-Jan-27	16-Mar-27	23-Mar-27	$0.00	$0.00	$40,310.73	0.00
MLTX-02-004-CN-10650	Fixation and Installation of Precast Concrete Seats (Rectangular)	7.00	0%	0%	05-Jan-27	12-Jan-27	16-Mar-27	23-Mar-27	$0.00	$0.00	$43,680.00	0.00
MLTX-02-004-CN-10660	Fixation and Installation of Precast Concrete Seats (Circular)	8.00	0%	0%	05-Jan-27	13-Jan-27	16-Mar-27	24-Mar-27	$0.00	$0.00	$17,160.00	0.00
MLTX-02-004-CN-10670	Fixation and Installation of Precast Concrete Trash Bins	9.00	0%	0%	14-Jan-27	24-Jan-27	25-Mar-27	04-Apr-27	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-11800	Installing of Site Light Poles	11.00	0%	70%	07-Jan-27	19-Jan-27	01-Oct-26 A	17-Mar-27	$0.00	$330,731.65	$472,473.79	-129.00
TOILET/SERVICE BUILDING		79.00	50.98%	2.44%	19-Jul-26	02-Nov-26	27-Sep-26 A	28-Dec-26	$312,949.03	$14,947.34	$613,847.78	11.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUB-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUPER-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
UNDER GROUND SEPTIC TANK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ANTI TERMIT CONTROL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POLYETHYLENE SHEET		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EPOXY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MASONARY WORK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		15.00	100%	79.87%	23-Aug-26	15-Sep-26	27-Sep-26 A	21-Oct-26	$18,714.15	$14,947.34	$18,714.15	-1.00
MLTX-02-004-CN-11050	Preparing Surface and Preliminary Works for Toilets Waterproofing	2.00	100%	0%	23-Aug-26	24-Aug-26	13-Oct-26	14-Oct-26	$2,106.00	$0.00	$2,106.00	0.00
MLTX-02-004-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8.00	100%	90%	07-Sep-26	15-Sep-26	27-Sep-26 A	21-Oct-26	$16,608.15	$14,947.34	$16,608.15	-14.00
MECHANICAL WORK		55.00	84.28%	0%	03-Sep-26	20-Oct-26	13-Oct-26	15-Dec-26	$144,981.88	$0.00	$172,021.88	-15.00
HVAC SYSTEM		6.00	0%	0%	14-Oct-26	20-Oct-26	09-Dec-26	15-Dec-26	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-11500	Install and Finish HVAC and Ventilation Works Including Split Air Units	6.00	0%	0%	14-Oct-26	20-Oct-26	09-Dec-26	15-Dec-26	$0.00	$0.00	$14,625.00	0.00
WATER SUPPLY SYSTEM		44.00	100%	0%	07-Sep-26	10-Oct-26	15-Oct-26	05-Dec-26	$101,505.00	$0.00	$101,505.00	-16.00
MLTX-02-004-CN-11530	Installing of HDPE Pipes and Valves for Water Supply Network	3.00	100%	0%	09-Sep-26	12-Sep-26	18-Oct-26	20-Oct-26	$39,000.00	$0.00	$39,000.00	0.00
MLTX-02-004-CN-11550	Installing of Booster Pump Units Including fittings and accessories	7.00	100%	0%	29-Sep-26	06-Oct-26	03-Nov-26	10-Nov-26	$51,000.00	$0.00	$51,000.00	0.00
MLTX-02-004-CN-11520	Installing of Valves and Fittings	2.00	100%	0%	07-Sep-26	08-Sep-26	15-Oct-26	17-Oct-26	$9,750.00	$0.00	$9,750.00	0.00
MLTX-02-004-CN-11860	Installing of Water Heater	4.00	100%	0%	06-Oct-26	10-Oct-26	01-Dec-26	05-Dec-26	$1,755.00	$0.00	$1,755.00	0.00
SEWER/DRAINAGE SYSTEM		51.00	80.6%	0%	03-Sep-26	15-Oct-26	13-Oct-26	10-Dec-26	$43,476.88	$0.00	$53,941.88	-15.00
MLTX-02-004-CN-11600	Installing of Plumping Fixtures and Accessories	2.00	100%	0%	19-Sep-26	20-Sep-26	15-Nov-26	16-Nov-26	$10,359.38	$0.00	$10,359.38	0.00
MLTX-02-004-CN-11850	Installing Inspection Chamber for Sewage Network	9.00	100%	0%	03-Sep-26	13-Sep-26	13-Oct-26	22-Oct-26	$12,187.50	$0.00	$12,187.50	0.00
MLTX-02-004-CN-11870	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	9.00	66.67%	0%	06-Oct-26	15-Oct-26	01-Dec-26	10-Dec-26	$20,930.00	$0.00	$31,395.00	0.00
FIRE PROTECTION		4.00	0%	0%	17-Oct-26	20-Oct-26	12-Dec-26	15-Dec-26	$0.00	$0.00	$1,950.00	0.00
MLTX-02-004-CN-11620	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	4.00	0%	0%	17-Oct-26	20-Oct-26	12-Dec-26	15-Dec-26	$0.00	$0.00	$1,950.00	0.00
ELECTRICAL WORKS		10.00	0%	0%	14-Oct-26	25-Oct-26	09-Dec-26	20-Dec-26	$0.00	$0.00	$227,643.75	0.00

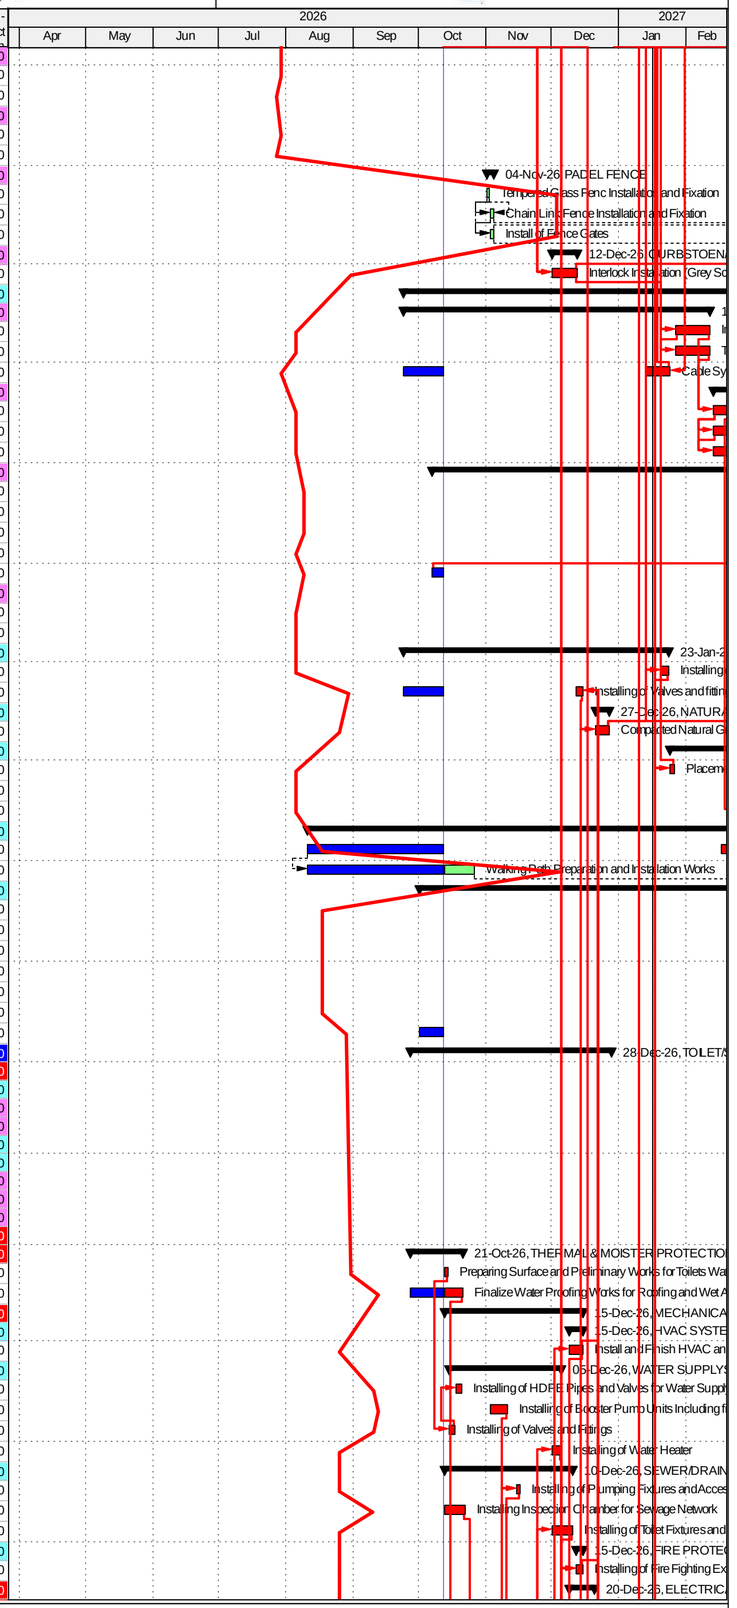


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filters: 2 Weeks Ahead, Remaining work.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
ROUGH-IN WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FIXTURE WORKS		10.00	0%	0%	14-Oct-26	25-Oct-26	09-Dec-26	20-Dec-26	$0.00	$0.00	$227,643.75	0.00
MLTX-02-004-CN-11780	Installing of Fire automation and Fire Alarm System	4.00	0%	0%	21-Oct-26	25-Oct-26	16-Dec-26	20-Dec-26	$0.00	$0.00	$34,320.00	0.00
MLTX-02-004-CN-11740	Installing and Finish Works of Panel Boards	10.00	0%	0%	14-Oct-26	25-Oct-26	09-Dec-26	20-Dec-26	$0.00	$0.00	$84,075.00	0.00
MLTX-02-004-CN-11760	Installing and Finalize Works of Sockets and Power Points	4.00	0%	0%	17-Oct-26	20-Oct-26	12-Dec-26	15-Dec-26	$0.00	$0.00	$13,846.37	0.00
MLTX-02-004-CN-11790	Installing and Finalize Works of Lighting Works including Light Fixtures	4.00	0%	0%	17-Oct-26	20-Oct-26	12-Dec-26	15-Dec-26	$0.00	$0.00	$16,050.06	0.00
MLTX-02-004-CN-11750	Installing Data and Telecommunication System with all Accessories	4.00	0%	0%	17-Oct-26	20-Oct-26	12-Dec-26	15-Dec-26	$0.00	$0.00	$18,427.50	0.00
MLTX-02-004-CN-11830	Installing and Finalize Works of Security and Access Control System	6.00	0%	0%	14-Oct-26	20-Oct-26	09-Dec-26	15-Dec-26	$0.00	$0.00	$22,899.83	0.00
MLTX-02-004-CN-11770	Installing and Finalize Works of Earthing Works	6.00	0%	0%	14-Oct-26	20-Oct-26	09-Dec-26	15-Dec-26	$0.00	$0.00	$23,400.00	0.00
MLTX-02-004-CN-11820	Installing and Finalize Works of Lightning Protection System	6.00	0%	0%	14-Oct-26	20-Oct-26	09-Dec-26	15-Dec-26	$0.00	$0.00	$14,625.00	0.00
DOORS/WINDOWS		51.00	40%	0%	19-Aug-26	02-Nov-26	31-Oct-26	28-Dec-26	$27,300.00	$0.00	$68,250.00	13.00
MLTX-02-004-CN-11110	Preliminary Works For Doors	3.00	100%	0%	19-Aug-26	22-Aug-26	31-Oct-26	02-Nov-26	$3,900.00	$0.00	$3,900.00	0.00
MLTX-02-004-CN-11120	Finalize Metal Doors for Toilets Building	7.00	0%	0%	18-Oct-26	25-Oct-26	09-Dec-26	16-Dec-26	$0.00	$0.00	$5,850.00	0.00
MLTX-02-004-CN-11130	Finalize Glazzed Curtain Wall Works	7.00	0%	0%	26-Oct-26	02-Nov-26	21-Dec-26	28-Dec-26	$0.00	$0.00	$35,100.00	0.00
MLTX-02-004-CN-11100	Preliminary Works For Windows/Curtain Wall	2.00	100%	0%	19-Aug-26	20-Aug-26	31-Oct-26	01-Nov-26	$23,400.00	$0.00	$23,400.00	0.00
METAL WORKS		10.00	100%	0%	19-Jul-26	29-Jul-26	13-Oct-26	24-Oct-26	$3,900.00	$0.00	$3,900.00	0.00
MLTX-02-004-CN-11160	Installation of DI Cover for Tank	10.00	100%	0%	19-Jul-26	29-Jul-26	13-Oct-26	24-Oct-26	$3,900.00	$0.00	$3,900.00	0.00
FINISHING WORKS		52.00	93.76%	0%	07-Sep-26	17-Oct-26	13-Oct-26	12-Dec-26	$79,053.00	$0.00	$84,318.00	-18.00
FLOOR FINISHES		34.00	93.18%	0%	07-Sep-26	17-Oct-26	03-Nov-26	12-Dec-26	$15,990.00	$0.00	$17,160.00	0.00
MLTX-02-004-CN-11200	Creamic Tiles Floor Finish Works	2.00	100%	0%	07-Sep-26	08-Sep-26	03-Nov-26	04-Nov-26	$11,895.00	$0.00	$11,895.00	0.00
MLTX-02-004-CN-11210	Granite Tiles Floor Finish Works	4.00	100%	0%	09-Sep-26	13-Sep-26	05-Nov-26	09-Nov-26	$2,925.00	$0.00	$2,925.00	0.00
MLTX-02-004-CN-11220	Epoxy Coaton Concrete Floor	3.00	0%	0%	14-Oct-26	17-Oct-26	09-Dec-26	12-Dec-26	$0.00	$0.00	$1,170.00	0.00
MLTX-02-004-CN-11230	Ceramic Skirting Tiles Finish Works	4.00	100%	0%	14-Sep-26	17-Sep-26	10-Nov-26	14-Nov-26	$1,170.00	$0.00	$1,170.00	0.00
WALL FINISHES		43.00	92.41%	0%	16-Sep-26	15-Oct-26	22-Oct-26	10-Dec-26	$49,881.00	$0.00	$53,976.00	-18.00
MLTX-02-004-CN-11320	Phenolic Partitions for Toilets	7.00	100%	0%	28-Sep-26	05-Oct-26	23-Nov-26	30-Nov-26	$31,200.00	$0.00	$31,200.00	0.00
MLTX-02-004-CN-11260	Glass Partitions including all accessories and doors	7.00	85.71%	0%	06-Oct-26	13-Oct-26	01-Dec-26	08-Dec-26	$10,530.00	$0.00	$12,285.00	0.00
MLTX-02-004-CN-11270	Granite Capping for Parpet	2.00	100%	0%	16-Sep-26	17-Sep-26	22-Oct-26	24-Oct-26	$8,151.00	$0.00	$8,151.00	0.00
MLTX-02-004-CN-11840	Painting Finish Works for Internal Walls	2.00	0%	0%	14-Oct-26	15-Oct-26	09-Dec-26	10-Dec-26	$0.00	$0.00	$2,340.00	0.00
CELLING FINISHES		19.00	100%	0%	07-Sep-26	30-Sep-26	13-Oct-26	03-Nov-26	$13,182.00	$0.00	$13,182.00	1.00
MLTX-02-004-CN-11350	Painting Finish Works for Ceiling	3.00	100%	0%	28-Sep-26	30-Sep-26	01-Nov-26	03-Nov-26	$1,638.00	$0.00	$1,638.00	0.00
MLTX-02-004-CN-11360	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7.00	100%	0%	19-Sep-26	27-Sep-26	13-Oct-26	20-Oct-26	$6,926.40	$0.00	$6,926.40	0.00
MLTX-02-004-CN-11340	Preliminary Works for Ceiling Painting Works	3.00	100%	0%	07-Sep-26	09-Sep-26	28-Oct-26	31-Oct-26	$4,617.60	$0.00	$4,617.60	0.00
SPECIALTIES WORK		15.00	100%	0%	21-Sep-26	08-Oct-26	17-Nov-26	03-Dec-26	$39,000.00	$0.00	$39,000.00	0.00
MLTX-02-004-CN-11390	Sanitary Fixtures and Accessories Works	5.00	100%	0%	21-Sep-26	27-Sep-26	17-Nov-26	22-Nov-26	$14,625.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-11380	Installation of Phenolic Locker	3.00	100%	0%	06-Oct-26	08-Oct-26	01-Dec-26	03-Dec-26	$24,375.00	$0.00	$24,375.00	0.00
TESTING & COMMISSIONING		59.00	0%	0%	05-Nov-26	12-Jan-27	24-Jan-27	06-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11860	Testing and Commissioning for MEP Works for Playground Area	10.00	0%	0%	02-Jan-27	12-Jan-27	27-Mar-27	06-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service Building	22.00	0%	0%	05-Nov-26	30-Nov-26	24-Jan-27	17-Feb-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11880	Testing and Commissioning for MEP Works for Landscape Works	22.00	0%	0%	01-Dec-26	26-Dec-26	18-Feb-27	20-Mar-27	$0.00	$0.00	$0.00	0.00
JAZAN		169.00	19.31%	8.86%	05-Jul-26	25-Jan-27	19-Aug-26	02-May-27	$1,697,095.94	$778,823.93	$8,789,991.93	-40.00
MOBILIZATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOPOGRAPHIC SURVEY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SITE FACILITIES & OFFICES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRELIMINARY SUBMITTALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PREPARATIONS & SUBMITTAL BY CONTRACTORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
APPROVALS BY EMPLOYERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ENGINEERING		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMISSION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVAL FOR EARTHING WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DOME SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SPORTS EQUIPMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

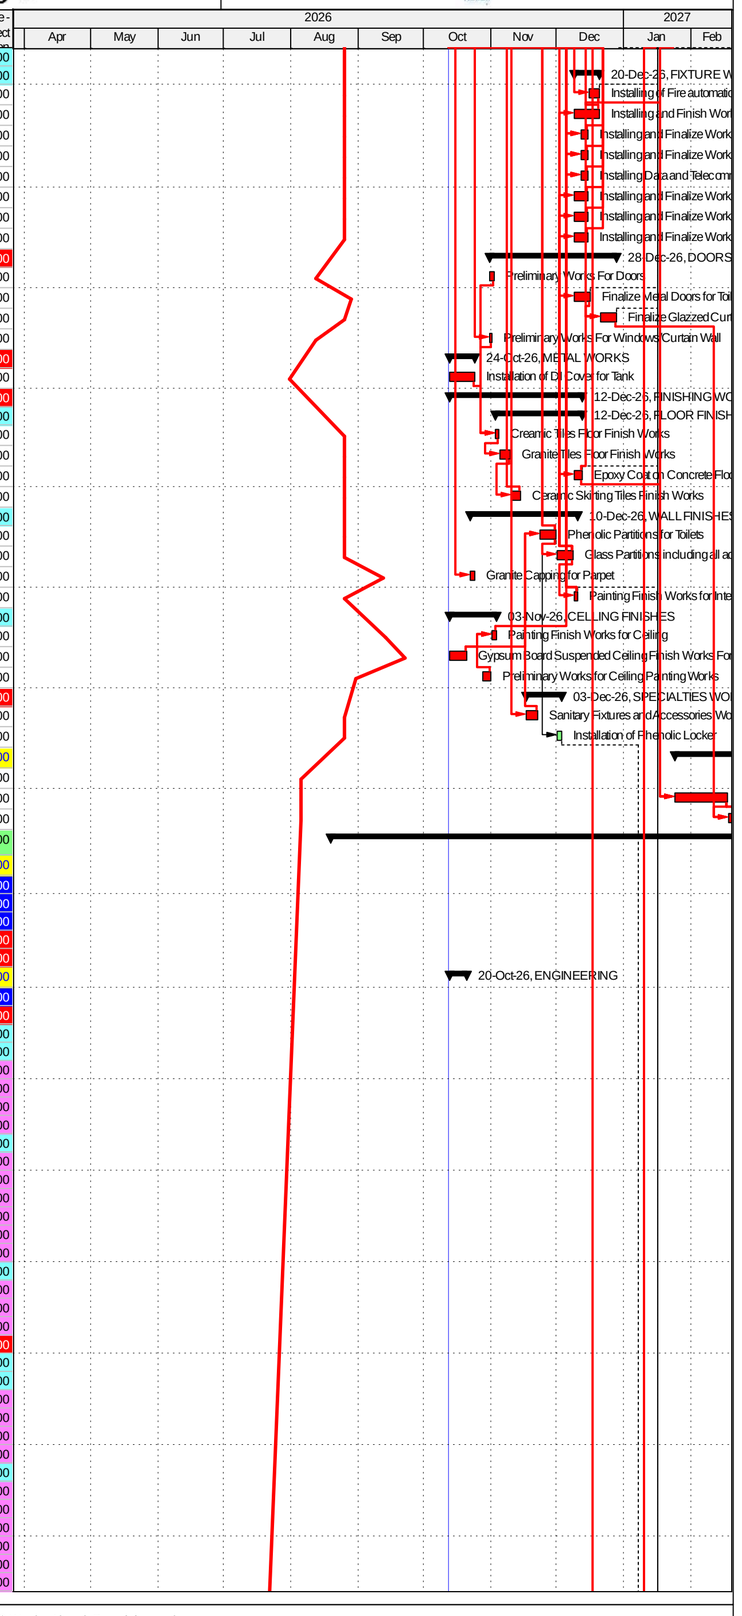


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filters: 2 Weeks Ahead, Remaining work.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
SHOP DRAWINGS APPROVALFOR LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANCAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENTS		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
METHOD STATEMENT SUBMITTAL		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-8060	Preparation & Submission of Method Statement for Fence Works	5.00	100%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
METHOD STATEMENT APPROVAL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CIVIL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARCHITECTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MECHANICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ELECTRICAL WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRE-QUALIFICATION & MATERIAL		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PRE-QUALIFICATION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER PROOFING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MATERIAL SUBMITTAL		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
TOILET/SERVICE WORKS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
READY MIX CONCRETE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

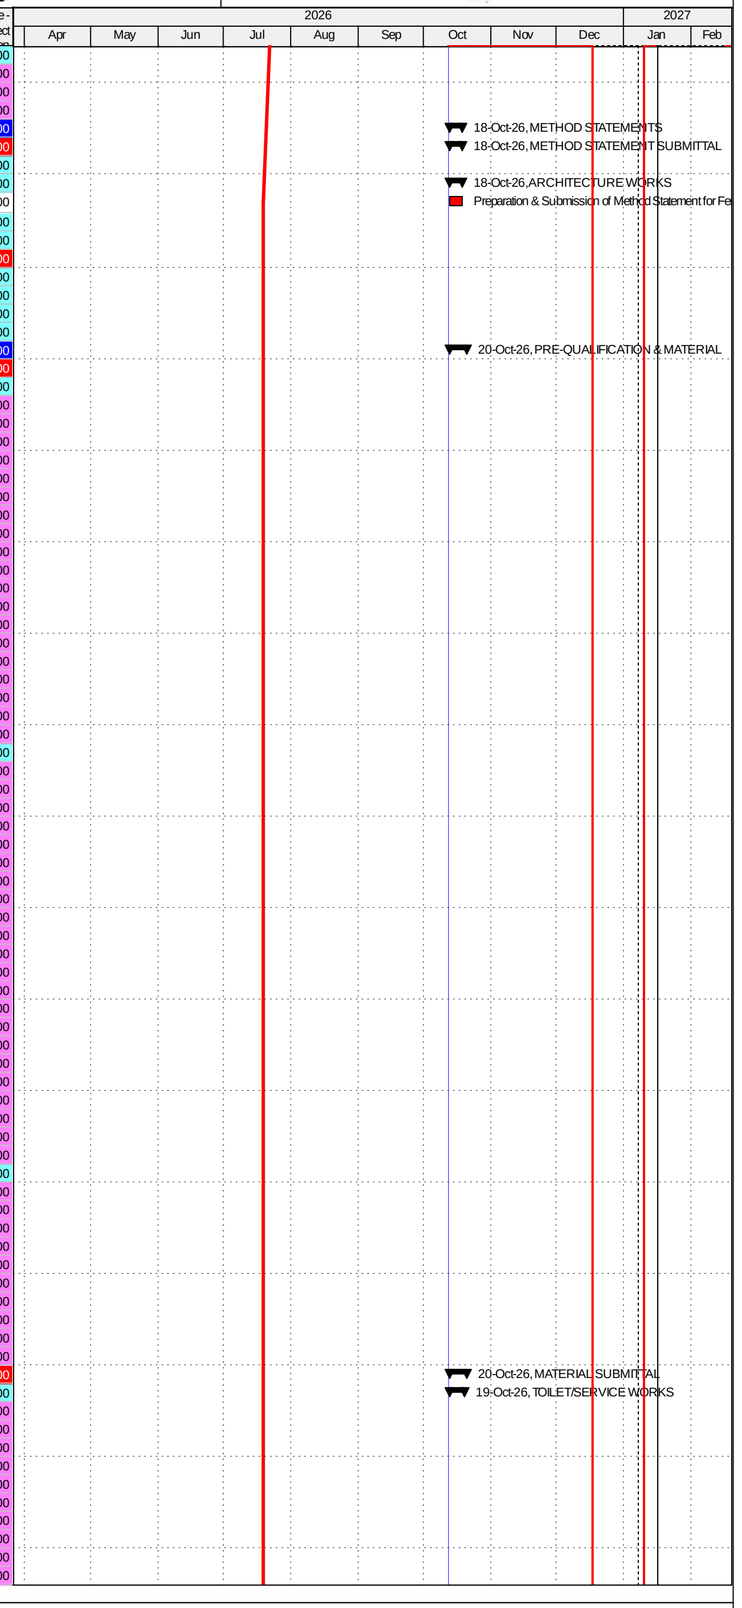


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9450	Material Approval for Galvanized Ducts	6.00	100%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PVC MEMBRANE		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9570	Material Approval for PVC Membrane	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
STEEL TENSION CABLES		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9880	Material Approval for Steel Tension Cables	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9890	Material Approval for Emergency Doors	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9900	Material Approval for Pressure Units	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9910	Material Approval for Lock Doors	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
RUBBER GRANULES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL GLASS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		7.00	0%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9950	Material Approval for Wire Mesh/Steel Sets	7.00	100%	0%	05-Jul-26	12-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MARKING PAINT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		6.00	0%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-EN-9530	Material Approval for Galvanized Duct	6.00	100%	0%	05-Jul-26	11-Jul-26	13-Oct-26	19-Oct-26	$0.00	$0.00	$0.00	0.00
EXHAUST FANS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CURBSTONE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
TRACK SURFACE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LIGHT POLES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PROCUREMENT		107.00	0%	0%	05-Jul-26	07-Nov-26	13-Oct-26	14-Feb-27	$0.00	$0.00	$0.00	0.00
SHORT LEAD ITEM		87.00	0%	0%	05-Jul-26	21-Oct-26	13-Oct-26	21-Jan-27	$0.00	$0.00	$0.00	6.00
TOILET/SERVICE WORKS		43.00	0%	0%	05-Jul-26	23-Aug-26	13-Oct-26	01-Dec-26	$0.00	$0.00	$0.00	0.00
STEEL REINFORCEMENT		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE BLOCKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FLOOR/WALL TILES		28.00	0%	0%	19-Jul-26	08-Aug-26	13-Oct-26	14-Nov-26	$0.00	$0.00	$0.00	-10.00
MLTX-02-004-PR-10170	PO for Tilling Materials	5.00	100%	0%	19-Jul-26	23-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10180	Material Delivery of Talling Material	13.00	100%	0%	25-Jul-26	08-Aug-26	31-Oct-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
SUSPENDED CEILING		5.00	0%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10190	PO for Suspend Ceiling	5.00	100%	0%	05-Jul-26	09-Jul-26	13-Oct-26	18-Oct-26	$0.00	$0.00	$0.00	0.00
DOORS/WINDOWS		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10220	Material Delivery for Doors/Windows	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
WATER SUPPLY PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SEWAGE/DRAINAGE PIPES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SANITARY FIXTURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		10.00	0%	0%	30-Jul-26	10-Aug-26	08-Nov-26	18-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10380	Material Delivery for PackageAC Units	10.00	100%	0%	30-Jul-26	10-Aug-26	08-Nov-26	18-Nov-26	$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		10.00	0%	0%	11-Aug-26	22-Aug-26	19-Nov-26	30-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10400	Material Delivery for Air Diffusers/Grills	10.00	100%	0%	11-Aug-26	22-Aug-26	19-Nov-26	30-Nov-26	$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EXHAUST FANS		15.00	0%	0%	20-Jul-26	05-Aug-26	28-Oct-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10440	Material Delivery for Exhaust Fans	15.00	100%	0%	20-Jul-26	05-Aug-26	28-Oct-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
LIGHTING FIXTURES		15.00	0%	0%	06-Aug-26	23-Aug-26	15-Nov-26	01-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10300	Material Delivery for Lighting Fixtures	15.00	100%	0%	06-Aug-26	23-Aug-26	15-Nov-26	01-Dec-26	$0.00	$0.00	$0.00	0.00
SWITCHES/SOCKETS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
EARTHING SYSTEM		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
DISTRIBUTION PANNELS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FURNITURES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
PLAYGROUND WORKS		87.00	0%	0%	05-Jul-26	21-Oct-26	13-Oct-26	21-Jan-27	$0.00	$0.00	$0.00	6.00
PVC MEMBRANE		4.00	0%	0%	05-Jul-26	08-Jul-26	13-Oct-26	17-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10540	Material Delivery for PVC Membrane	4.00	100%	0%	05-Jul-26	08-Jul-26	13-Oct-26	17-Oct-26	$0.00	$0.00	$0.00	0.00
ARTIFICIAL TURF		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

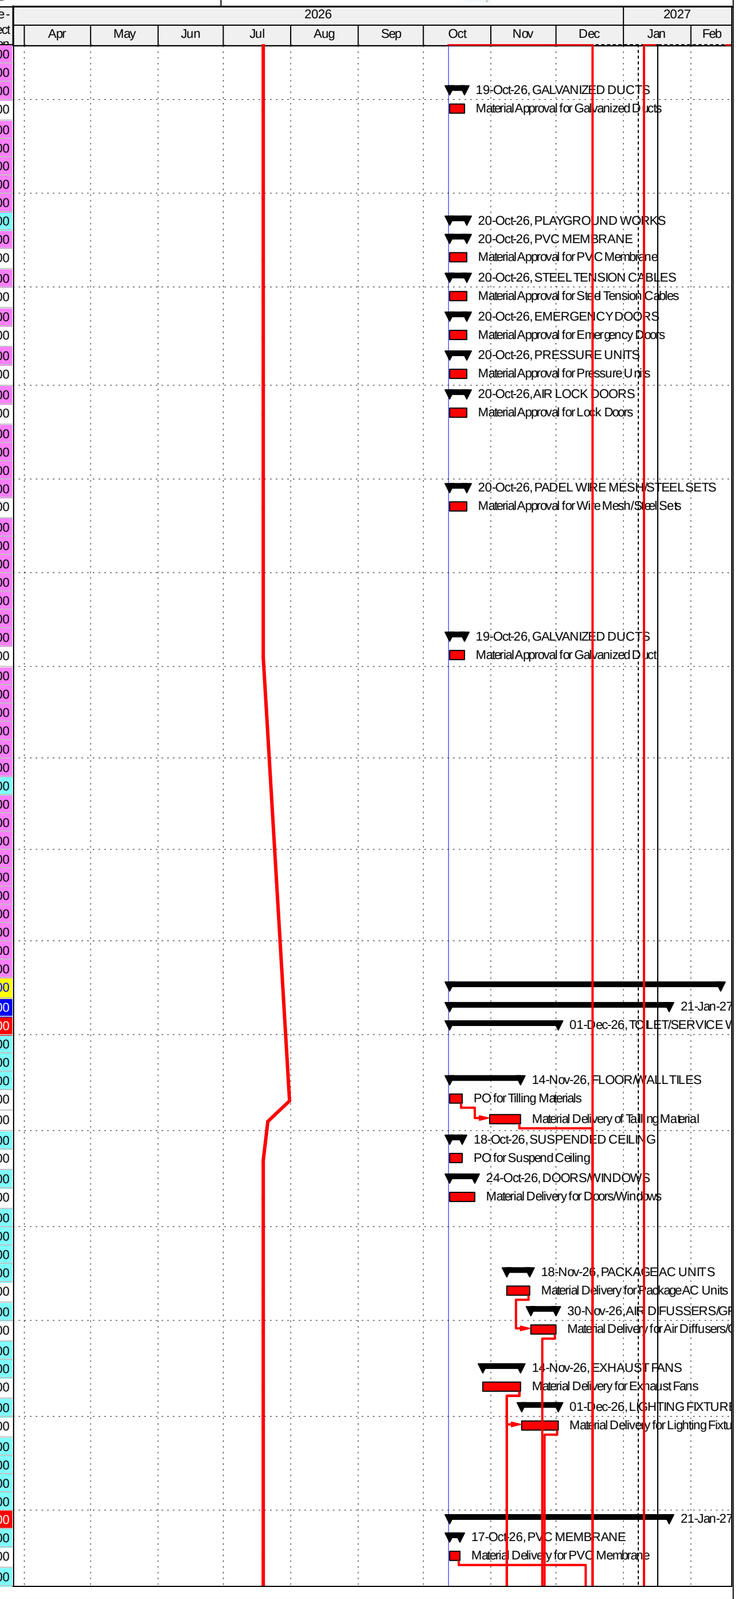


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
RUBBER GRANULES		12.00	0%	0%	23-Jul-26	05-Aug-26	01-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10800	Material Delivery for Rubber Granules	12.00	100%	0%	23-Jul-26	05-Aug-26	01-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
PADEL GLASS		18.00	0%	0%	06-Aug-26	26-Aug-26	15-Nov-26	05-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10820	Material Delivery for Padel Glass	18.00	100%	0%	06-Aug-26	26-Aug-26	15-Nov-26	05-Dec-26	$0.00	$0.00	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		15.00	0%	0%	27-Aug-26	13-Sep-26	06-Dec-26	22-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15.00	100%	0%	27-Aug-26	13-Sep-26	06-Dec-26	22-Dec-26	$0.00	$0.00	$0.00	0.00
AGGREGATE BASE COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
INTERLOCKING PAVING		7.00	0%	0%	14-Sep-26	21-Sep-26	23-Dec-26	30-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10030	Material Delivery for Interlocking Block Pavers	7.00	100%	0%	14-Sep-26	21-Sep-26	23-Dec-26	30-Dec-26	$0.00	$0.00	$0.00	0.00
MARKING PAINT		7.00	0%	0%	12-Jul-26	19-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10360	Material Delivery for Marking Paint	7.00	100%	0%	12-Jul-26	19-Jul-26	13-Oct-26	20-Oct-26	$0.00	$0.00	$0.00	0.00
PACKAGE AC UNITS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
AIR DIFUSSERS/GRILLS		15.00	0%	0%	06-Aug-26	23-Aug-26	08-Nov-26	24-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10480	Material Delivery for Air Difussers/Grills	15.00	100%	0%	06-Aug-26	23-Aug-26	08-Nov-26	24-Nov-26	$0.00	$0.00	$0.00	0.00
GALVANIZED DUCTS		15.00	0%	0%	24-Aug-26	09-Sep-26	25-Nov-26	12-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10500	Material Delivery for Galvanized Duct	15.00	100%	0%	24-Aug-26	09-Sep-26	25-Nov-26	12-Dec-26	$0.00	$0.00	$0.00	0.00
EXHAUST FANS		15.00	0%	0%	10-Sep-26	28-Sep-26	13-Dec-26	29-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10520	Material Delivery for Exhaust Fans	15.00	100%	0%	10-Sep-26	28-Sep-26	13-Dec-26	29-Dec-26	$0.00	$0.00	$0.00	0.00
DISTRIBUTION BOARDS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POWER CABLES		10.00	0%	0%	03-Aug-26	13-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10660	Material Delivery for Power Cables	10.00	100%	0%	03-Aug-26	13-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
LIGHT FIXTURES		21.00	0%	0%	15-Aug-26	07-Sep-26	15-Nov-26	08-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10670	PO for Light Fixtures	5.00	100%	0%	15-Aug-26	19-Aug-26	15-Nov-26	19-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10680	Material Delivery for Light Fixtures	16.00	100%	0%	20-Aug-26	07-Sep-26	21-Nov-26	08-Dec-26	$0.00	$0.00	$0.00	0.00
CCTV MATERIALS		38.00	0%	0%	08-Sep-26	21-Oct-26	09-Dec-26	21-Jan-27	$0.00	$0.00	$0.00	-1.00
MLTX-02-004-PR-10690	PO for CCTV	10.00	100%	0%	08-Sep-26	19-Sep-26	09-Dec-26	20-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10700	Material Delivery for CCTV	20.00	60%	0%	29-Sep-26	21-Oct-26	30-Dec-26	21-Jan-27	$0.00	$0.00	$0.00	0.00
POWER OUTLETS/SWITCHES		21.00	0%	0%	20-Sep-26	14-Oct-26	21-Dec-26	13-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10710	PO for Power Outlets/Switches	6.00	100%	0%	20-Sep-26	27-Sep-26	21-Dec-26	27-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10720	Material Delivery for Power Outlets/Switches	15.00	86.67%	0%	28-Sep-26	14-Oct-26	28-Dec-26	13-Jan-27	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		30.00	0%	0%	05-Jul-26	04-Oct-26	13-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	48.00
INTERLOCKING PAVING		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10760	Material Delivery for Interlocking Block Pavers	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
CURBSTONE		10.00	0%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10900	Material Delivery for Curbstone	10.00	100%	0%	05-Jul-26	15-Jul-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
PAVEMENT MARKING		10.00	0%	0%	22-Jul-26	02-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10050	Material Delivery for Pavement Markings	10.00	100%	0%	22-Jul-26	02-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
TRAFFIC SIGNS		9.00	0%	0%	09-Aug-26	18-Aug-26	13-Oct-26	22-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10080	Material Delivery for Traffic Signs	9.00	100%	0%	09-Aug-26	18-Aug-26	13-Oct-26	22-Oct-26	$0.00	$0.00	$0.00	0.00
IRRIGATION PIPES/SPRINKLERS		8.00	0%	0%	26-Sep-26	04-Oct-26	05-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10100	Material Delivery for Irrigation Pipes/Sprinkles	8.00	100%	0%	26-Sep-26	04-Oct-26	05-Nov-26	14-Nov-26	$0.00	$0.00	$0.00	0.00
AGRICULTURE SOIL		12.00	0%	0%	11-Jul-26	23-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10860	Material Delivery for Agriculture Soil	12.00	100%	0%	11-Jul-26	23-Jul-26	13-Oct-26	26-Oct-26	$0.00	$0.00	$0.00	0.00
TRACK SURFACE		10.00	0%	0%	25-Jul-26	04-Aug-26	27-Oct-26	07-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10880	Material Delivery for Track Surface	10.00	100%	0%	25-Jul-26	04-Aug-26	27-Oct-26	07-Nov-26	$0.00	$0.00	$0.00	0.00
GRASS/TREES		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CABLES		15.00	0%	0%	29-Aug-26	14-Sep-26	31-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10740	Material Delivery for Cables	15.00	100%	0%	29-Aug-26	14-Sep-26	31-Oct-26	16-Nov-26	$0.00	$0.00	$0.00	0.00
LONG LEAD ITEM		107.00	0%	0%	25-Jul-26	07-Nov-26	13-Oct-26	14-Feb-27	$0.00	$0.00	$0.00	-17.00
PLAYGROUND WORKS		77.00	0%	0%	25-Jul-26	06-Oct-26	13-Oct-26	10-Jan-27	$0.00	$0.00	$0.00	-14.00
STEEL TENSION CABLES		37.00	0%	0%	25-Jul-26	05-Sep-26	02-Nov-26	14-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10560	Material Delivery for Steel Tension Cables	30.00	100%	0%	25-Jul-26	27-Aug-26	02-Nov-26	06-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10970	Staging time	7.00	100%	0%	29-Aug-26	05-Sep-26	07-Dec-26	14-Dec-26	$0.00	$0.00	$0.00	0.00
EMERGENCY DOORS		59.00	0%	0%	03-Aug-26	10-Sep-26	13-Oct-26	20-Dec-26	$0.00	$0.00	$0.00	-25.00
MLTX-02-004-PR-10940	Material Fabrication for Emergency Doors	10.00	100%	0%	03-Aug-26	13-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10980	Staging time	5.00	100%	0%	06-Sep-26	10-Sep-26	15-Dec-26	20-Dec-26	$0.00	$0.00	$0.00	0.00
PRESSURE UNITS		60.00	0%	0%	28-Jul-26	06-Oct-26	13-Oct-26	21-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10590	PO for Pressure Units	10.00	100%	0%	28-Jul-26	08-Aug-26	13-Oct-26	24-Oct-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10600	Material Delivery for Pressure Units	25.00	100%	0%	01-Sep-26	30-Sep-26	17-Nov-26	15-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10990	Staging time	5.00	100%	0%	01-Oct-26	06-Oct-26	16-Dec-26	21-Dec-26	$0.00	$0.00	$0.00	0.00
AIR LOCK DOORS		60.00	0%	0%	25-Jul-26	03-Oct-26	02-Nov-26	10-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10610	PO for Lock Doors	10.00	100%	0%	25-Jul-26	04-Aug-26	02-Nov-26	12-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10620	Material Delivery for Lock Doors	25.00	100%	0%	29-Aug-26	27-Sep-26	07-Dec-26	04-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-10960	Material Fabrication for Lock Doors	20.00	100%	0%	05-Aug-26	27-Aug-26	14-Nov-26	06-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11000	Staging time	5.00	100%	0%	28-Sep-26	03-Oct-26	05-Jan-27	10-Jan-27	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		60.00	0%	0%	29-Aug-26	07-Nov-26	07-Dec-26	14-Feb-27	$0.00	$0.00	$0.00	0.00
LIGHT POLES		60.00	0%	0%	29-Aug-26	07-Nov-26	07-Dec-26	14-Feb-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9950	Material Fabrication for Lighting poles	30.00	100%	0%	29-Aug-26	03-Oct-26	07-Dec-26	10-Jan-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-9960	Material Delivery for Lighting poles	25.00	32%	0%	04-Oct-26	01-Nov-26	11-Jan-27	08-Feb-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-PR-11010	Staging time	5.00	0%	0%	02-Nov-26	07-Nov-26	09-Feb-27	14-Feb-27	$0.00	$0.00	$0.00	0.00
CONSTRUCTION PHASE		169.00	19.31%	8.86%	25-Jul-26	25-Jan-27	19-Aug-26	02-May-27	$1,697,095.94	$778,823.93	$8,789,991.93	-57.00
SITE WORKS		169.00	14.41%	8.6%	25-Jul-26	25-Jan-27	19-Aug-26	02-May-27	$1,169,369.35	$697,661.22	$8,113,148.52	-57.00
EARTH WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		169.00	14.59%	8.7%	25-Jul-26	25-Jan-27	19-Aug-26	02-May-27	$1,169,369.35	$697,661.22	$8,015,648.03	-57.00
PLAYGROUND AREA		161.00	42.28%	0%	25-Jul-26	16-Jan-27	13-Oct-26	22-Apr-27	$487,521.67	$0.00	$1,153,197.50	-11.00
FOOTBALL PLAYGROUND		94.00	63.33%	0%	25-Jul-26	07-Dec-26	02-Nov-26	18-Feb-27	$182,162.50	$0.00	$287,625.00	22.00
MLTX-02-004-CN-12090	Backfilling and Compaction of Base Layers (Football Playground)	25.00	100%	0%	25-Jul-26	22-Aug-26	02-Nov-26	30-Nov-26	$57,525.00	$0.00	$57,525.00	0.00
MLTX-02-004-CN-12100	Finishing and Surface Finish Works (Football Playground)	30.00	86.67%	0%	12-Sep-26	17-Oct-26	21-Dec-26	24-Jan-27	$124,637.50	$0.00	$143,812.50	0.00

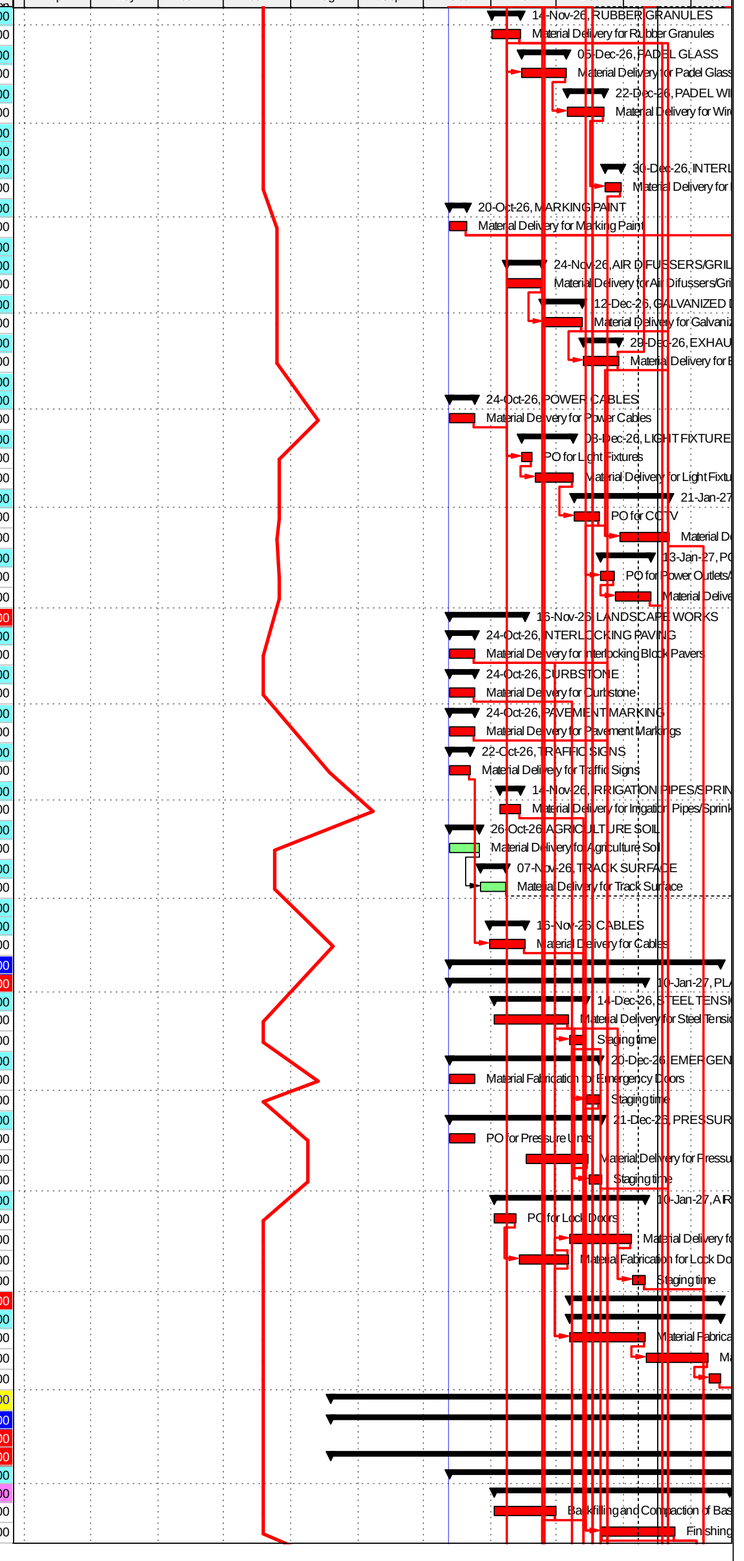

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
MLTX-02-004-CN-12110	Install Sport Equipments - Goal / Nets - (Football Playground)	8.00	0%	0%	29-Nov-26	07-Dec-26	10-Feb-27	18-Feb-27	$0.00	$0.00	$71,906.25	0.00
MLTX-02-004-CN-12120	Surface Marking and Painting (Football Playground)	8.00	0%	0%	29-Nov-26	07-Dec-26	10-Feb-27	18-Feb-27	$0.00	$0.00	$14,381.25	0.00
PADEL PLAYGROUND		123.00	55%	0%	25-Jul-26	22-Dec-26	02-Nov-26	29-Mar-27	$117,975.00	$0.00	$214,500.00	6.00
MLTX-02-004-CN-12130	Preparation and Proofing for Subgrade (Padel Playground)	25.00	100%	0%	25-Jul-26	22-Aug-26	02-Nov-26	30-Nov-26	$75,075.00	$0.00	$75,075.00	0.00
MLTX-02-004-CN-12140	Backfilling and Compaction of Base Layers (Padel Playground)	20.00	100%	0%	23-Aug-26	14-Sep-26	01-Dec-26	23-Dec-26	$42,900.00	$0.00	$42,900.00	0.00
MLTX-02-004-CN-12150	Finishing and Surface Finish Works (Padel Playground)	30.00	0%	0%	18-Oct-26	21-Nov-26	25-Jan-27	01-Mar-27	$0.00	$0.00	$53,625.00	0.00
MLTX-02-004-CN-12160	Install Sport Equipments - Goal / Nets - (Padel Playground)	13.00	0%	0%	29-Nov-26	13-Dec-26	02-Mar-27	20-Mar-27	$0.00	$0.00	$32,175.00	0.00
MLTX-02-004-CN-12170	Surface Marking and Painting (Padel Playground)	8.00	0%	0%	14-Dec-26	22-Dec-26	21-Mar-27	29-Mar-27	$0.00	$0.00	$10,725.00	0.00
BASKETBALL PLAYGROUND		98.00	17.67%	0%	23-Aug-26	22-Dec-26	01-Dec-26	29-Mar-27	$55,120.00	$0.00	$312,000.00	6.00
MLTX-02-004-CN-12180	Preparation and Proofing for Subgrade (Padel Playground)	20.00	100%	0%	23-Aug-26	14-Sep-26	01-Dec-26	23-Dec-26	$31,200.00	$0.00	$31,200.00	0.00
MLTX-02-004-CN-12190	Backfilling and Compaction of Base Layers (Basketball Playground)	30.00	76.67%	0%	15-Sep-26	20-Oct-26	24-Dec-26	27-Jan-27	$23,920.00	$0.00	$31,200.00	0.00
MLTX-02-004-CN-12200	Finishing and Surface Finish Works (Basketball Playground)	30.00	0%	0%	21-Oct-26	24-Nov-26	28-Jan-27	04-Mar-27	$0.00	$0.00	$156,000.00	0.00
MLTX-02-004-CN-12210	Install Sport Equipments - Goal / Nets - (Basketball Playground)	10.00	0%	0%	08-Dec-26	19-Dec-26	06-Mar-27	20-Mar-27	$0.00	$0.00	$78,000.00	0.00
MLTX-02-004-CN-12220	Surface Marking and Painting (Basketball Playground)	8.00	0%	0%	14-Dec-26	22-Dec-26	21-Mar-27	29-Mar-27	$0.00	$0.00	$15,600.00	0.00
PADEL FENCE		21.00	0%	0%	23-Dec-26	16-Jan-27	30-Mar-27	22-Apr-27	$0.00	$0.00	$82,875.00	0.00
MLTX-02-004-CN-12230	Excavation for Fence	3.00	0%	0%	23-Dec-26	26-Dec-26	30-Mar-27	01-Apr-27	$0.00	$0.00	$8,287.50	0.00
MLTX-02-004-CN-12240	Concrete Foundation for Fence including Posts Fixation	4.00	0%	0%	27-Dec-26	30-Dec-26	03-Apr-27	06-Apr-27	$0.00	$0.00	$16,575.00	0.00
MLTX-02-004-CN-12250	Tempered Glass Fenc Installation and Fixation	5.00	0%	0%	05-Jan-27	10-Jan-27	12-Apr-27	17-Apr-27	$0.00	$0.00	$33,150.00	0.00
MLTX-02-004-CN-12260	Chain Link Fence Installation and Fixation	5.00	0%	0%	05-Jan-27	10-Jan-27	12-Apr-27	17-Apr-27	$0.00	$0.00	$16,575.00	0.00
MLTX-02-004-CN-12270	Install of Fence Gates	5.00	0%	0%	11-Jan-27	16-Jan-27	18-Apr-27	22-Apr-27	$0.00	$0.00	$4,143.75	0.00
MLTX-02-004-CN-12241	Backfilling and Reinstatement for Concrete Foundation	4.00	0%	0%	31-Dec-26	04-Jan-27	07-Apr-27	11-Apr-27	$0.00	$0.00	$4,143.75	0.00
CURBSTOEN/INTERLOCK		83.00	51.63%	0%	27-Sep-26	24-Oct-26	13-Oct-26	17-Jan-27	$132,264.17	$0.00	$256,197.50	-59.00
MLTX-02-004-CN-11960	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	15.00	33.33%	0%	07-Oct-26	24-Oct-26	31-Dec-26	17-Jan-27	$61,966.67	$0.00	$185,900.00	0.00
MLTX-02-004-CN-12020	Concrete Works Under Curbstone	5.00	100%	0%	27-Sep-26	01-Oct-26	13-Oct-26	18-Oct-26	$15,990.00	$0.00	$15,990.00	0.00
MLTX-02-004-CN-12030	Curbstone Installation	4.00	100%	0%	03-Oct-26	06-Oct-26	15-Dec-26	19-Dec-26	$54,307.50	$0.00	$54,307.50	0.00
AIR DOME		88.00	11.36%	9.66%	27-Sep-26	26-Dec-26	24-Sep-26 A	14-Mar-27	$560,625.00	$476,531.25	$4,933,500.00	-65.00
CIVIL WORKS		53.00	33.33%	28.33%	27-Sep-26	15-Nov-26	24-Sep-26 A	27-Jan-27	$560,625.00	$476,531.25	$1,681,875.00	-65.00
MLTX-02-004-CN-12310	Install of Membrane Covering System (Air Dome)	4.00	0%	0%	08-Nov-26	11-Nov-26	20-Jan-27	24-Jan-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-12320	Thermal Insulation Works (Air Dome)	3.00	0%	0%	12-Nov-26	15-Nov-26	25-Jan-27	27-Jan-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-12300	Cable System Installation (Air Dome)	3.00	100%	85%	27-Sep-26	29-Sep-26	24-Sep-26 A	14-Dec-26	$560,625.00	$476,531.25	$560,625.00	-67.00
MECHANICAL WORKS		13.00	0%	0%	16-Nov-26	30-Nov-26	28-Jan-27	11-Feb-27	$0.00	$0.00	$1,121,250.00	0.00
MLTX-02-004-CN-12350	Air Ducts and Grills Installation (Air Dome)	10.00	0%	0%	16-Nov-26	26-Nov-26	28-Jan-27	08-Feb-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-12360	Air Units Installation (Air Dome)	13.00	0%	0%	16-Nov-26	30-Nov-26	28-Jan-27	11-Feb-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-12370	Exhaust Fans and Ducts Installation (Air Dome)	11.00	0%	0%	16-Nov-26	28-Nov-26	28-Jan-27	09-Feb-27	$0.00	$0.00	$392,437.50	0.00
ELECTRICAL WORKS		22.00	0%	0%	01-Dec-26	26-Dec-26	13-Feb-27	14-Mar-27	$0.00	$0.00	$1,681,875.00	0.00
MLTX-02-004-CN-12380	Light Fixture Works (Air Dome)	20.00	0%	0%	01-Dec-26	23-Dec-26	13-Feb-27	08-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-12390	Distribution Board and Electrical Works (Air Dome)	18.00	0%	0%	01-Dec-26	21-Dec-26	13-Feb-27	06-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-12400	External Electrical Connection Works (Air Dome)	20.00	0%	0%	01-Dec-26	23-Dec-26	13-Feb-27	08-Mar-27	$0.00	$0.00	$280,312.50	0.00
MLTX-02-004-CN-12410	Emergency Generator Installation (Air Dome)	20.00	0%	0%	01-Dec-26	23-Dec-26	13-Feb-27	08-Mar-27	$0.00	$0.00	$560,625.00	0.00
MLTX-02-004-CN-12420	Control System Installation (Air Dome)	22.00	0%	0%	01-Dec-26	26-Dec-26	13-Feb-27	14-Mar-27	$0.00	$0.00	$280,312.50	0.00
FINISHES WORKS		25.00	0%	0%	19-Nov-26	17-Dec-26	01-Feb-27	02-Mar-27	$0.00	$0.00	$448,500.00	0.00
MLTX-02-004-CN-12330	Doors Installation Including Emergency, Entrance doors (Air Dome)	10.00	0%	0%	19-Nov-26	30-Nov-26	01-Feb-27	11-Feb-27	$0.00	$0.00	$224,250.00	0.00
MLTX-02-004-CN-12340	Logo and Signs Installation (Air Dome)	15.00	0%	0%	01-Dec-26	17-Dec-26	13-Feb-27	02-Mar-27	$0.00	$0.00	$224,250.00	0.00
IRRIGATION NETWORK		22.00	30.18%	0%	07-Oct-26	01-Nov-26	20-Dec-26	13-Jan-27	$80,795.00	$0.00	$267,670.00	0.00
MLTX-02-004-CN-13190	Installing of HDPE Pipes for Irrigation Network (Main Line)	5.00	100%	0%	07-Oct-26	12-Oct-26	20-Dec-26	24-Dec-26	$80,795.00	$0.00	$80,795.00	0.00
MLTX-02-004-CN-13200	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	5.00	0%	0%	13-Oct-26	18-Oct-26	26-Dec-26	30-Dec-26	$0.00	$0.00	$94,250.00	0.00
MLTX-02-004-CN-13210	Installing of Valves and fittings for Irrigation Network	4.00	0%	0%	19-Oct-26	22-Oct-26	31-Dec-26	04-Jan-27	$0.00	$0.00	$46,475.00	0.00
MLTX-02-004-CN-13220	Installing of Bubblers and Spreyers	3.00	0%	0%	29-Oct-26	01-Nov-26	11-Jan-27	13-Jan-27	$0.00	$0.00	$46,150.00	0.00
NATURAL GROUND		5.00	0%	0%	24-Oct-26	28-Oct-26	05-Jan-27	10-Jan-27	$0.00	$0.00	$80,291.25	0.00
MLTX-02-004-CN-11990	Compacted Natural Ground Soil Installation Works for Landscape	5.00	0%	0%	24-Oct-26	28-Oct-26	05-Jan-27	10-Jan-27	$0.00	$0.00	$80,291.25	0.00
PLANTING		28.00	0%	0%	02-Nov-26	03-Dec-26	14-Jan-27	15-Feb-27	$0.00	$0.00	$573,462.50	0.00
MLTX-02-004-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	5.00	0%	0%	02-Nov-26	07-Nov-26	14-Jan-27	19-Jan-27	$0.00	$0.00	$186,420.00	0.00
MLTX-02-004-CN-12060	Placement of Lawn Ground Cover (Rolling and Compaction)	3.00	0%	0%	01-Dec-26	03-Dec-26	13-Feb-27	15-Feb-27	$0.00	$0.00	$175,175.00	0.00
MLTX-02-004-CN-12070	Placement and Fixation of Trees	3.00	0%	0%	28-Nov-26	30-Nov-26	09-Feb-27	11-Feb-27	$0.00	$0.00	$211,867.50	0.00
WALKING/BIKE PATHS		8.00	0%	80%	05-Dec-26	13-Dec-26	19-Aug-26 A	15-Feb-27	$0.00	$221,129.97	$276,412.47	-146.00
MLTX-02-004-CN-12000	Bike Path Preparation and Installation Works	8.00	0%	80%	05-Dec-26	13-Dec-26	19-Aug-26 A	15-Feb-27	$0.00	$113,636.22	$142,045.28	-146.00
MLTX-02-004-CN-12010	Walking Path Preparation and Installation Works	8.00	0%	80%	05-Dec-26	13-Dec-26	19-Aug-26 A	21-Oct-26	$0.00	$107,493.75	$134,367.19	-46.00
GENERAL/FURNITURE		111.00	5.53%	0%	07-Oct-26	25-Jan-27	20-Dec-26	02-May-27	$40,427.68	$0.00	$731,114.31	-16.00
MLTX-02-004-CN-12040	Traffic Signs Posts and Poles Installation	7.00	0%	0%	06-Jan-27	13-Jan-27	25-Mar-27	01-Apr-27	$0.00	$0.00	$9,750.00	0.00
MLTX-02-004-CN-12440	Fixation and Installation of Steel Frame for Benches	12.00	0%	0%	14-Dec-26	27-Dec-26	16-Feb-27	02-Mar-27	$0.00	$0.00	$17,276.03	0.00
MLTX-02-004-CN-12450	Fixation and Installation of Benches	8.00	0%	0%	28-Dec-26	05-Jan-27	03-Mar-27	15-Mar-27	$0.00	$0.00	$40,310.73	0.00
MLTX-02-004-CN-12460	Fixation and Installation of Precast Concrete Seats (Rectangular)	8.00	0%	0%	28-Dec-26	05-Jan-27	03-Mar-27	15-Mar-27	$0.00	$0.00	$43,680.00	0.00
MLTX-02-004-CN-12470	Fixation and Installation of Precast Concrete Seats (Circular)	8.00	0%	0%	28-Dec-26	05-Jan-27	03-Mar-27	15-Mar-27	$0.00	$0.00	$17,160.00	0.00
MLTX-02-004-CN-12480	Fixation and Installation of Precast Concrete Trash Bins	8.00	0%	0%	17-Jan-27	25-Jan-27	24-Apr-27	02-May-27	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-12920	Preleminary Works for Site Light Poles Including Cable and Bases Works	14.00	35.71%	0%	07-Oct-26	22-Oct-26	20-Dec-26	04-Jan-27	$40,427.68	$0.00	$113,197.50	0.00
MLTX-02-004-CN-12930	Installing of Site Light Poles	11.00	0%	0%	24-Dec-26	05-Jan-27	09-Mar-27	24-Mar-27	$0.00	$0.00	$475,115.06	0.00
PARKING		12.00	0%	0%	23-Dec-26	05-Jan-27	01-Nov-26	14-Nov-26	$0.00	$0.00	$97,500.48	0.00
MLTX-02-004-CN-11940	Interlock Installation (8 Cm) for Parking Area (Including Finishing Works)	7.00	0%	0%	29-Dec-26	05-Jan-27	07-Nov-26	14-Nov-26	$0.00	$0.00	$68,249.02	0.00
MLTX-02-004-CN-11950	Site Preparation & Compaction Under Interlock for Parking Area	5.00	0%	0%	23-Dec-26	28-Dec-26	01-Nov-26	05-Nov-26	$0.00	$0.00	$29,251.46	0.00
TOILET/SERVICE BUILDING		76.00	77.97%	11.99%	20-Aug-26	16-Nov-26	15-Sep-26 A	09-Jan-27	$527,726.60	$81,162.71	$676,843.41	-24.00
STRUCTURE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
CONCRETE WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUB-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
SUPER-STRUCTURE		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
UNDER GROUND SEPTIC TANK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
ANTI TERMIT CONTROL		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
POLYETHYLENE SHEET		0.00	0%	0%					$0.00	$0.00	$0.00	0.00

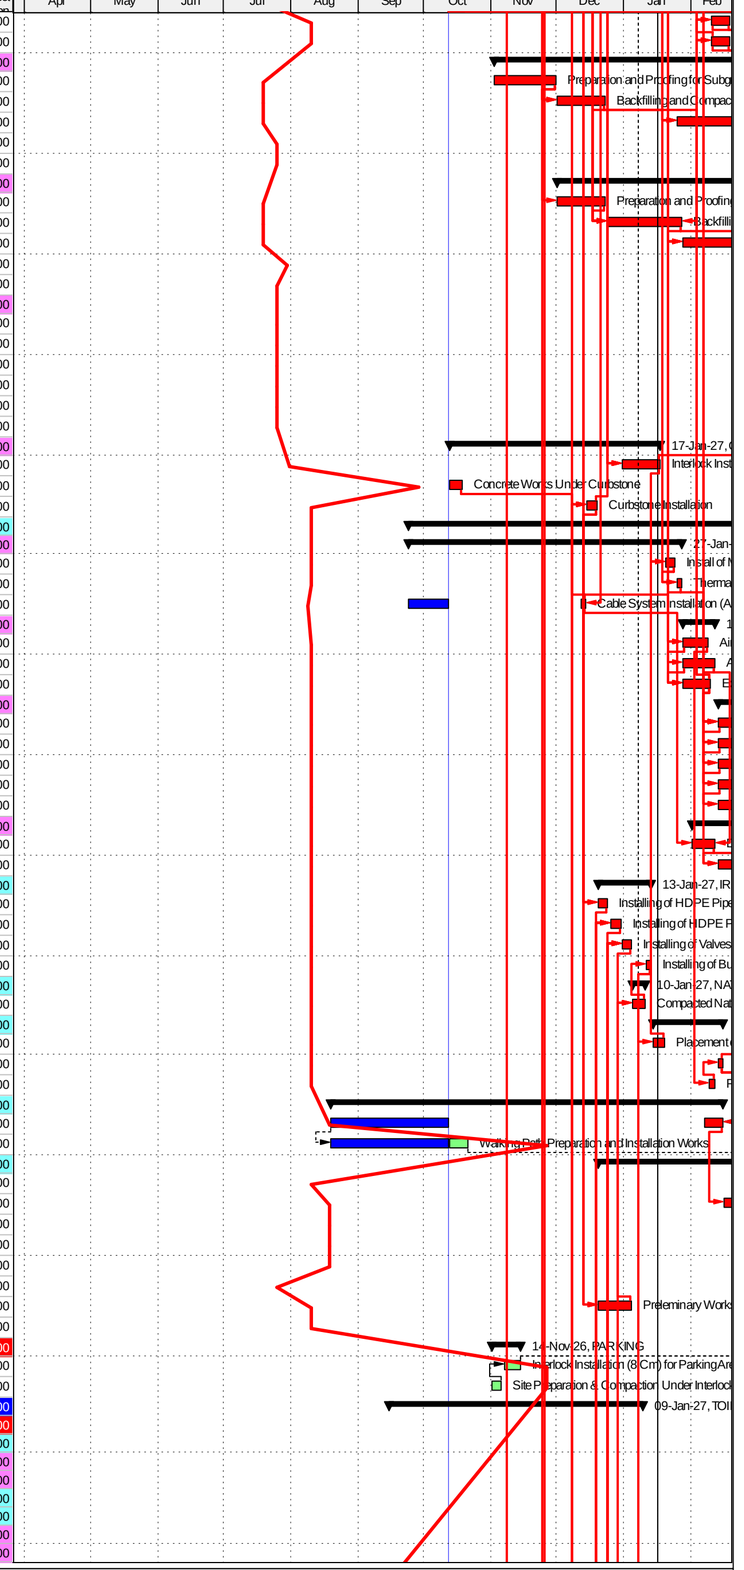

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filters: 2 Weeks Ahead, Remaining work.

© Oracle Corporation


MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

2 Weeks look ahead schedule
D.D 12-10-2026

PROFAST

egis

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project Duration
EPOXY		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
MASONARY WORK		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
THERMAL & MOISTER PROTECTION		10.00	100%	49.2%	20-Aug-26	13-Sep-26	29-Sep-26 A	21-Oct-26	$23,628.15	$11,625.71	$23,628.15	1.00
MLTX-02-004-CN-12620	Preparing Surface and Preliminary Works for Toilets Waterproofing	2.00	100%	0%	20-Aug-26	22-Aug-26	13-Oct-26	14-Oct-26	$2,106.00	$0.00	$2,106.00	0.00
MLTX-02-004-CN-12630	Finalize Water Proofing Works for Toilets	5.00	100%	0%	23-Aug-26	27-Aug-26	15-Oct-26	20-Oct-26	$4,914.00	$0.00	$4,914.00	0.00
MLTX-02-004-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	8.00	100%	70%	05-Sep-26	13-Sep-26	29-Sep-26 A	21-Oct-26	$16,608.15	$11,625.71	$16,608.15	-12.00
MECHANICAL WORK		51.00	96.49%	23.01%	31-Aug-26	18-Oct-26	15-Sep-26 A	10-Dec-26	$261,654.02	$62,400.00	$271,171.88	-33.00
HVAC SYSTEM		23.00	56.14%	0%	16-Sep-26	18-Oct-26	15-Nov-26	10-Dec-26	$10,400.00	$0.00	$18,525.00	4.00
MLTX-02-004-CN-12730	Install and Finish HVAC and Ventilation Works Including Split Air Units	9.00	44.44%	0%	08-Oct-26	18-Oct-26	01-Dec-26	10-Dec-26	$6,500.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-12740	Exhaust,Air Ducts Installation with all Accessories	8.00	100%	0%	16-Sep-26	26-Sep-26	15-Nov-26	23-Nov-26	$3,900.00	$0.00	$3,900.00	0.00
WATER SUPPLY SYSTEM		40.00	100%	31.71%	16-Sep-26	10-Oct-26	15-Sep-26 A	29-Nov-26	$196,755.00	$62,400.00	$196,755.00	-44.00
MLTX-02-004-CN-12770	Installing of Booster Pump Units Including fittings and accessories	5.00	100%	0%	27-Sep-26	01-Oct-26	24-Nov-26	29-Nov-26	$91,000.00	$0.00	$91,000.00	0.00
MLTX-02-004-CN-13260	Installing of Water Heater	7.00	100%	0%	03-Oct-26	10-Oct-26	19-Nov-26	26-Nov-26	$1,755.00	$0.00	$1,755.00	0.00
MLTX-02-004-CN-12780	Installing of GRP Tanks	8.00	100%	60%	16-Sep-26	26-Sep-26	15-Sep-26 A	24-Oct-26	$104,000.00	$62,400.00	$104,000.00	-25.00
SEWER/DRAINAGE SYSTEM		41.00	100%	0%	31-Aug-26	12-Oct-26	13-Oct-26	29-Nov-26	$53,941.88	$0.00	$53,941.88	-5.00
MLTX-02-004-CN-12800	Installing of Plumping Fixtures and Accessories	2.00	100%	0%	17-Sep-26	19-Sep-26	31-Oct-26	01-Nov-26	$10,359.38	$0.00	$10,359.38	0.00
MLTX-02-004-CN-13250	Installing Inspection Chamber for Sewage Network	8.00	100%	0%	31-Aug-26	08-Sep-26	13-Oct-26	21-Oct-26	$12,187.50	$0.00	$12,187.50	0.00
MLTX-02-004-CN-13270	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	9.00	100%	0%	03-Oct-26	12-Oct-26	19-Nov-26	29-Nov-26	$31,395.00	$0.00	$31,395.00	0.00
FIRE PROTECTION		7.00	28.57%	0%	11-Oct-26	18-Oct-26	01-Dec-26	08-Dec-26	$557.14	$0.00	$1,950.00	0.00
MLTX-02-004-CN-12810	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	7.00	28.57%	0%	11-Oct-26	18-Oct-26	01-Dec-26	08-Dec-26	$557.14	$0.00	$1,950.00	0.00
ELECTRICAL WORKS		19.00	31.6%	0%	08-Oct-26	24-Oct-26	25-Nov-26	16-Dec-26	$60,158.43	$0.00	$190,397.39	-5.00
ROUGH-IN WORKS		0.00	0%	0%					$0.00	$0.00	$0.00	0.00
FIXTURE WORKS		19.00	31.6%	0%	08-Oct-26	24-Oct-26	25-Nov-26	16-Dec-26	$60,158.43	$0.00	$190,397.39	-5.00
MLTX-02-004-CN-12820	Installing of Fire automation and Fire Alarm System	5.00	0%	0%	19-Oct-26	24-Oct-26	12-Dec-26	16-Dec-26	$0.00	$0.00	$34,320.00	0.00
MLTX-02-004-CN-12840	Installing and Finish Works of Panel Boards	10.00	40%	0%	08-Oct-26	19-Oct-26	25-Nov-26	06-Dec-26	$33,630.00	$0.00	$84,075.00	0.00
MLTX-02-004-CN-12890	Installing and Finalize Works of Lighting Works including Light Fixtures	7.00	28.57%	0%	11-Oct-26	18-Oct-26	02-Dec-26	09-Dec-26	$4,585.73	$0.00	$16,050.06	0.00
MLTX-02-004-CN-12910	Installing Data and Telecommunication System with all Accessories	7.00	28.57%	0%	11-Oct-26	18-Oct-26	28-Nov-26	05-Dec-26	$5,265.00	$0.00	$18,427.50	0.00
MLTX-02-004-CN-12950	Installing and Finalize Works of Security and Access Control System	9.00	44.44%	0%	08-Oct-26	18-Oct-26	25-Nov-26	05-Dec-26	$10,177.70	$0.00	$22,899.83	0.00
MLTX-02-004-CN-12970	Installing and Finalize Works of Lightning Protection System	9.00	44.44%	0%	08-Oct-26	18-Oct-26	25-Nov-26	05-Dec-26	$6,500.00	$0.00	$14,625.00	0.00
DOORS/WINDOWS		5.00	80%	0%	08-Oct-26	13-Oct-26	25-Nov-26	30-Nov-26	$32,760.00	$0.00	$40,950.00	0.00
MLTX-02-004-CN-12670	Finalize Metal Doors for Toilets Building	5.00	80%	0%	08-Oct-26	13-Oct-26	25-Nov-26	30-Nov-26	$4,680.00	$0.00	$5,850.00	0.00
MLTX-02-004-CN-13040	Finalize Glazzed Curtain Wall Works	5.00	80%	0%	08-Oct-26	13-Oct-26	25-Nov-26	30-Nov-26	$28,080.00	$0.00	$35,100.00	0.00
METAL WORKS		25.00	100%	0%	20-Aug-26	04-Oct-26	13-Oct-26	10-Nov-26	$7,800.00	$0.00	$7,800.00	13.00
MLTX-02-004-CN-12980	Installation of DI Cover for Tank	4.00	100%	0%	20-Aug-26	24-Aug-26	13-Oct-26	17-Oct-26	$3,900.00	$0.00	$3,900.00	0.00
MLTX-02-004-CN-12990	Installation of Galvanized Steel Roof Scupper	10.00	100%	0%	22-Sep-26	04-Oct-26	31-Oct-26	10-Nov-26	$3,900.00	$0.00	$3,900.00	0.00
FINISHING WORKS		76.00	98.87%	6.87%	03-Sep-26	16-Nov-26	08-Oct-26 A	09-Jan-27	$102,726.00	$7,137.00	$103,896.00	-17.00
FLOOR FINISHES		74.00	93.18%	41.59%	03-Sep-26	16-Nov-26	08-Oct-26 A	09-Jan-27	$15,990.00	$7,137.00	$17,160.00	-17.00
MLTX-02-004-CN-13050	Granite Tiles Floor Finish Works	6.00	100%	0%	06-Sep-26	12-Sep-26	15-Oct-26	21-Oct-26	$2,925.00	$0.00	$2,925.00	0.00
MLTX-02-004-CN-13060	Epoxy Coat on Concrete Floor	20.00	0%	0%	25-Oct-26	16-Nov-26	17-Dec-26	09-Jan-27	$0.00	$0.00	$1,170.00	0.00
MLTX-02-004-CN-13070	Ceramic Skirting Tiles Finish Works	4.00	100%	0%	13-Sep-26	16-Sep-26	22-Oct-26	26-Oct-26	$1,170.00	$0.00	$1,170.00	0.00
MLTX-02-004-CN-12680	Creamic Tiles Floor Finish Works	2.00	100%	60%	03-Sep-26	05-Sep-26	08-Oct-26 A	14-Oct-26	$11,895.00	$7,137.00	$11,895.00	-4.00
WALL FINISHES		39.00	100%	0%	14-Sep-26	10-Oct-26	13-Oct-26	26-Nov-26	$73,554.00	$0.00	$73,554.00	-17.00
MLTX-02-004-CN-13010	Painting Finish Works for External Walls	3.00	100%	0%	14-Sep-26	16-Sep-26	13-Oct-26	15-Oct-26	$10,478.00	$0.00	$10,478.00	0.00
MLTX-02-004-CN-13030	Phenolic Partitions for Toilets	7.00	100%	0%	24-Sep-26	01-Oct-26	11-Nov-26	18-Nov-26	$31,200.00	$0.00	$31,200.00	0.00
MLTX-02-004-CN-13130	Stone Cladding Finish Works for External Walls	5.00	100%	0%	17-Sep-26	22-Sep-26	17-Oct-26	21-Oct-26	$9,100.00	$0.00	$9,100.00	0.00
MLTX-02-004-CN-13140	Glass Partitions including all accessories and doors	5.00	100%	0%	03-Oct-26	07-Oct-26	19-Nov-26	24-Nov-26	$12,285.00	$0.00	$12,285.00	0.00
MLTX-02-004-CN-13150	Granite Capping for Parpet	2.00	100%	0%	14-Sep-26	15-Sep-26	22-Oct-26	24-Oct-26	$8,151.00	$0.00	$8,151.00	0.00
MLTX-02-004-CN-13240	Painting Finish Works for Internal Walls	2.00	100%	0%	08-Oct-26	10-Oct-26	25-Nov-26	26-Nov-26	$2,340.00	$0.00	$2,340.00	0.00
CELLING FINISHES		42.00	100%	0%	03-Sep-26	01-Oct-26	13-Oct-26	30-Nov-26	$13,182.00	$0.00	$13,182.00	-18.00
MLTX-02-004-CN-13280	Painting Finish Works for Ceiling	9.00	100%	0%	21-Sep-26	01-Oct-26	21-Nov-26	30-Nov-26	$1,638.00	$0.00	$1,638.00	0.00
MLTX-02-004-CN-13290	Gypsum Board Suspended Ceiling Finish Works For Ceiling	4.00	100%	0%	16-Sep-26	20-Sep-26	13-Oct-26	17-Oct-26	$6,926.40	$0.00	$6,926.40	0.00
MLTX-02-004-CN-13300	Preliminary Works for Ceiling Painting Works	15.00	100%	0%	03-Sep-26	20-Sep-26	03-Nov-26	19-Nov-26	$4,617.60	$0.00	$4,617.60	0.00
SPECIALTIES WORK		12.00	100%	0%	20-Sep-26	04-Oct-26	08-Nov-26	21-Nov-26	$39,000.00	$0.00	$39,000.00	0.00
MLTX-02-004-CN-12700	Sanitary Fixtures and Accessories Works	3.00	100%	0%	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	$14,625.00	$0.00	$14,625.00	0.00
MLTX-02-004-CN-13160	Installation of Phenolic Locker	2.00	100%	0%	03-Oct-26	04-Oct-26	19-Nov-26	21-Nov-26	$24,375.00	$0.00	$24,375.00	0.00
TESTING & COMMISSIONING		68.00	0%	0%	17-Nov-26	19-Jan-27	14-Jan-27	07-Apr-27	$0.00	$0.00	$0.00	-13.00
MLTX-02-004-TC-11890	Testing and Commissioning for MEP Works for Playground Area	16.00	0%	0%	27-Dec-26	13-Jan-27	21-Mar-27	07-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service Building	25.00	0%	0%	17-Nov-26	15-Dec-26	14-Jan-27	11-Feb-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-TC-11910	Testing and Commissioning for MEP Works for Landscape Works	5.00	0%	0%	14-Jan-27	19-Jan-27	03-Apr-27	07-Apr-27	$0.00	$0.00	$0.00	0.00
PROJECT CLOSEOUT & DEMOBILIZATION		21.00	0%	0%	14-Jan-27	25-Jan-27	27-Mar-27	19-Apr-27	$0.00	$0.00	$0.00	-11.00
As-Built DWGs		19.00	0%	0%	14-Jan-27	23-Jan-27	27-Mar-27	17-Apr-27	$0.00	$0.00	$0.00	-11.00
As-Built DWGs Submittals		15.00	0%	0%	14-Jan-27	18-Jan-27	27-Mar-27	12-Apr-27	$0.00	$0.00	$0.00	-11.00
MLTX-02-004-CO-12000	As-Built DWGs Submittal for Playground Area Works	4.00	0%	0%	14-Jan-27	18-Jan-27	08-Apr-27	12-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12010	As-Built DWGs Submittal for Toilet/Service Building Works	4.00	0%	0%	14-Jan-27	18-Jan-27	27-Mar-27	30-Mar-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12020	As-Built DWGs Submittal for Landscape Works	4.00	0%	0%	14-Jan-27	18-Jan-27	03-Apr-27	06-Apr-27	$0.00	$0.00	$0.00	0.00
As-Built DWGs Approvals		15.00	0%	0%	19-Jan-27	23-Jan-27	31-Mar-27	17-Apr-27	$0.00	$0.00	$0.00	-11.00
MLTX-02-004-CO-12040	As-Built DWGs Approval for Playground Area Works	4.00	0%	0%	19-Jan-27	23-Jan-27	13-Apr-27	17-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12050	As-Built DWGs Approval for Toilet/Service Building Works	4.00	0%	0%	19-Jan-27	23-Jan-27	31-Mar-27	04-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12060	As-Built DWGs Approval for Landscape Works	4.00	0%	0%	19-Jan-27	23-Jan-27	07-Apr-27	11-Apr-27	$0.00	$0.00	$0.00	0.00
Demobilization		6.00	0%	0%	19-Jan-27	25-Jan-27	13-Apr-27	19-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12080	Demobilization of Manpower	2.00	0%	0%	19-Jan-27	20-Jan-27	13-Apr-27	14-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12090	Removal of Equipment from Site	2.00	0%	0%	19-Jan-27	20-Jan-27	13-Apr-27	14-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12100	Site Clean Up	2.00	0%	0%	21-Jan-27	23-Jan-27	15-Apr-27	17-Apr-27	$0.00	$0.00	$0.00	0.00
MLTX-02-004-CO-12110	Restoration of Ground Surfaces	2.00	0%	0%	24-Jan-27	25-Jan-27	18-Apr-27	19-Apr-27	$0.00	$0.00	$0.00	0.00

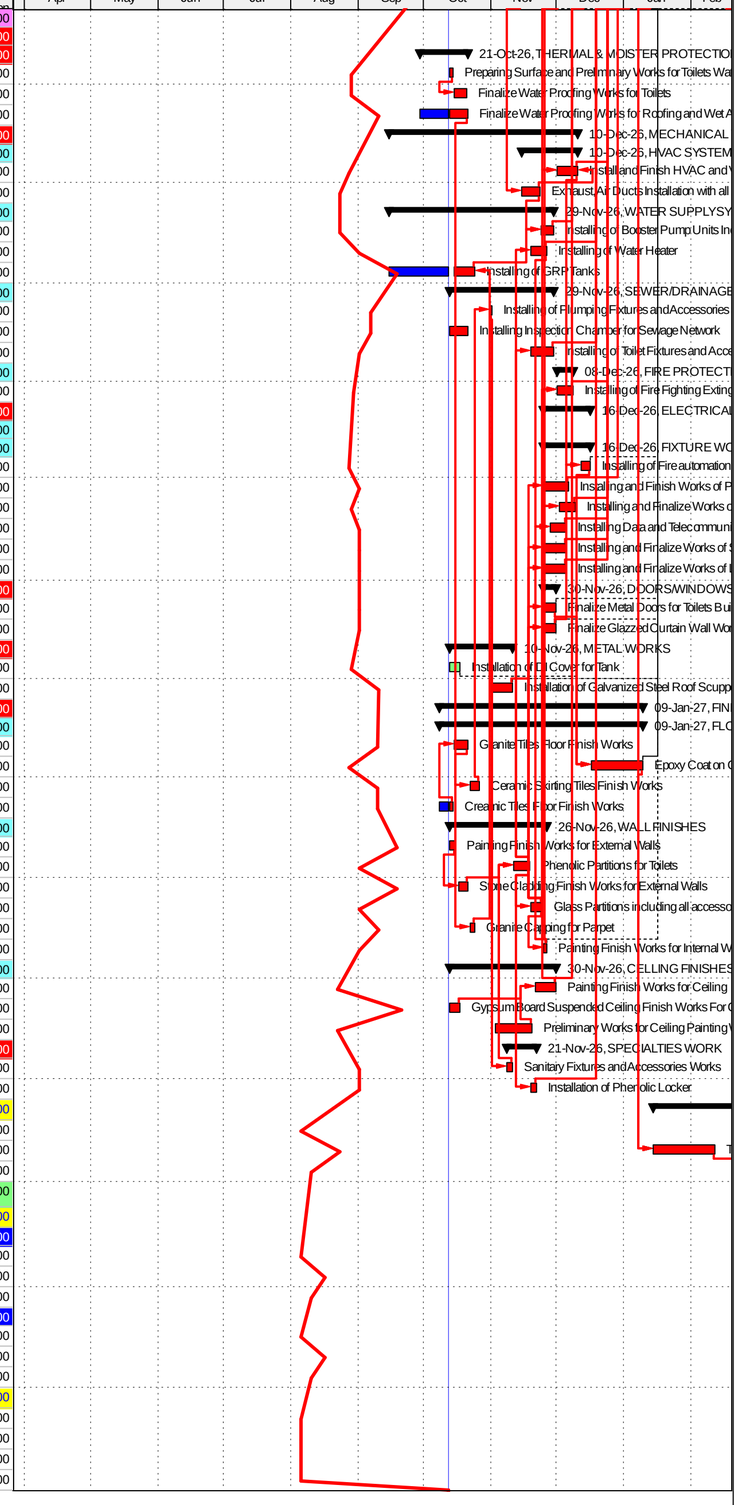

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filters: 2 Weeks Ahead, Remaining work.

© Oracle Corporation
