
Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Development of the Technology City in Dammam-Project UPDATE 06-10-2(		211	02-Aug-26 A	16-Mar-27	23-Jun-26	19-Jan-27	18,978,096.12
Key Milestones		0	14-Oct-26	14-Oct-26	13-Jul-26	13-Jul-26	0.00
Contractual Milestones		0	14-Oct-26	14-Oct-26	13-Jul-26	13-Jul-26	0.00
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		14-Oct-26		13-Jul-26	0.00
Engineering Works		8	06-Oct-26	14-Oct-26	23-Jun-26	02-Jul-26	0.00
Material Submittals and Approvals		8	06-Oct-26	14-Oct-26	23-Jun-26	02-Jul-26	0.00
Short Lead Time Items		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
Superstructure Works		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
Storage Tank (TSE)		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
ENG-MT-TSE-CV-S-	Material Submittal for Civil Works for Storage Tank (TSE)	7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
Long Lead Time Items		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Superstructure Works		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Pump Stations		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0.00
ENG-MT-SPS-MC-S-	Material Submittal for Electromechanical Works for Pump Stations	7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0.00
Approval of Material		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
ENG-MT-SPS-MC-A-	Material Approval for Electromechanical Works for Pump Stations	8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Storage Tank (TSE)		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0.00
ENG-MT-TSE-MC-S-	Material Submittal for Electromechanical Works for Storage Tank (TSE)	7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0.00
Approval of Material		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
ENG-MT-TSE-MC-A-	Material Approval for Electromechanical Works for Storage Tank (TSE)	8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0.00
Procurement Cycle		198	02-Aug-26 A	16-Mar-27	23-Jun-26	12-Dec-26	0.00
Short Lead Time Items		198	02-Aug-26 A	16-Mar-27	23-Jun-26	12-Dec-26	0.00
Infrastructure Networks		198	02-Aug-26 A	16-Mar-27	23-Jun-26	12-Dec-26	0.00
Road Works		23	02-Aug-26 A	06-Oct-26	02-Nov-26	05-Dec-26	0.00
Material Delivery & Site Inspection		23	02-Aug-26 A	06-Oct-26	02-Nov-26	05-Dec-26	0.00
Pre-Bituminous Construction		23	02-Aug-26 A	06-Oct-26	02-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-10	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	06-Oct-26	02-Nov-26	02-Nov-26	0.00
PRO-R25-RD-DL-11	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0.00
Bituminous Construction		0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-16	Material Delivery & Site Inspection for Prime Coat of Road Works	0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-17	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0.00
Pavement Works		0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-12	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-13	Material Delivery & Site Inspection of Curbstones for Landscaping	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0.00
Traffic Signs Boards and Roads Marking		0	06-Oct-26	06-Oct-26	08-Nov-26	25-Nov-26	0.00
PRO-R25-RD-DL-14	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	06-Oct-26	06-Oct-26	08-Nov-26	08-Nov-26	0.00
PRO-R25-RD-DL-15	Material Delivery & Site Inspection of Road Markings For Road Works	0	06-Oct-26	06-Oct-26	25-Nov-26	25-Nov-26	0.00
Softscape and Planting Works		83	06-Oct-26	10-Jan-27	11-Jul-26	17-Oct-26	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	11-Jul-26	19-Jul-26	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	11-Jul-26	19-Jul-26	0.00
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	06-Oct-26	12-Oct-26	12-Jul-26	19-Jul-26	0.00
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	06-Oct-26	12-Oct-26	11-Jul-26	18-Jul-26	0.00

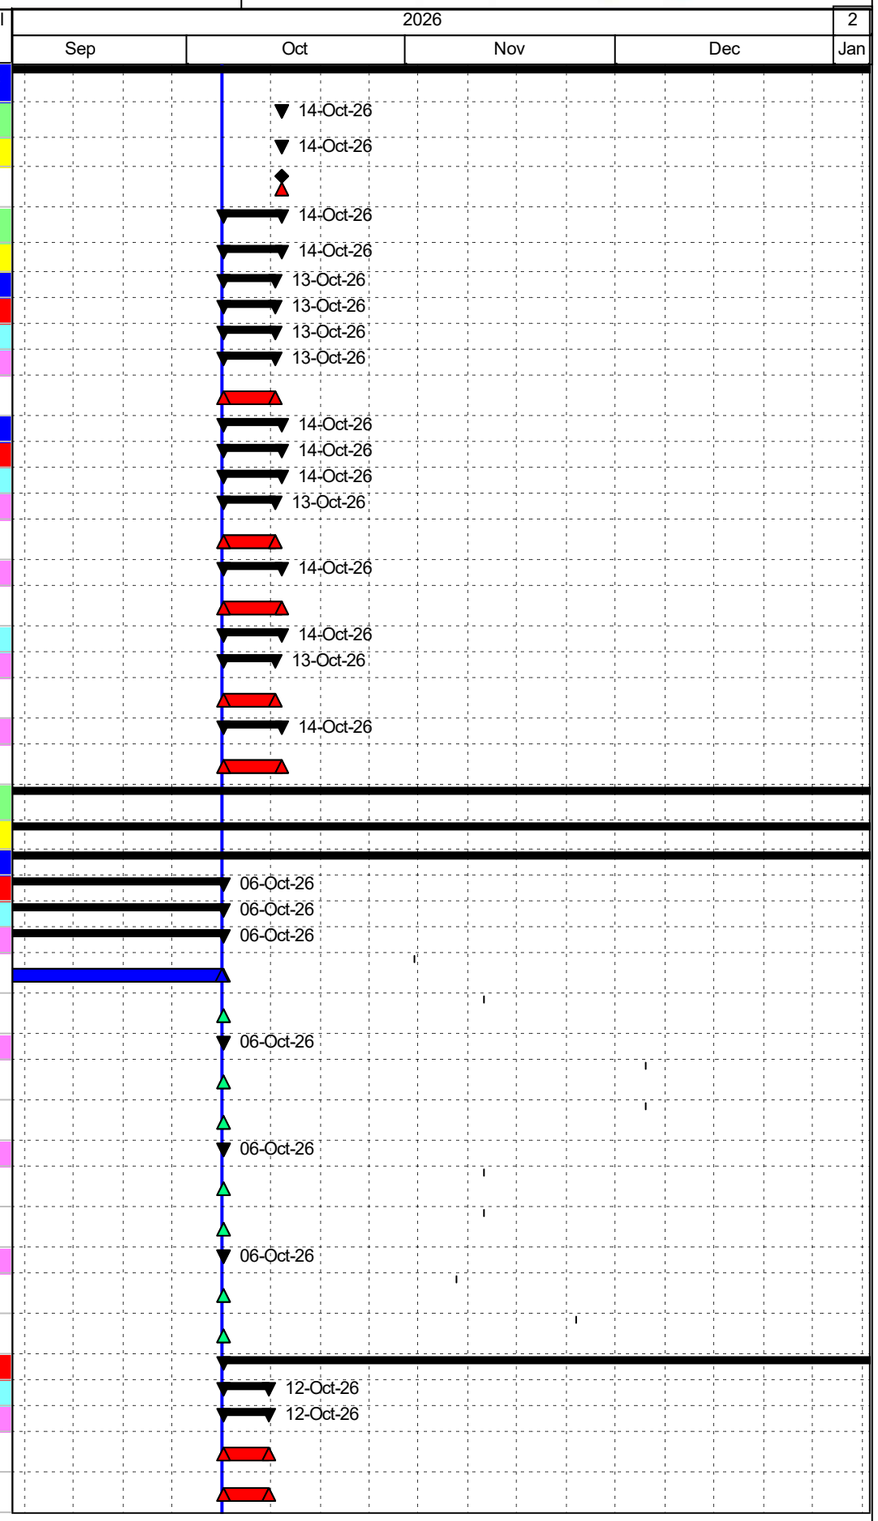

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Manufacturing of Material		90	13-Oct-26	10-Jan-27	18-Jul-26	17-Oct-26	0.00
Main Line Pipes		90	13-Oct-26	10-Jan-27	18-Jul-26	17-Oct-26	0.00
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	13-Oct-26	10-Jan-27	19-Jul-26	17-Oct-26	0.00
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	90	13-Oct-26	10-Jan-27	18-Jul-26	16-Oct-26	0.00
Sewage Network		115	06-Oct-26	19-Feb-27	08-Jul-26	21-Nov-26	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
PRO-SW-PO-120	Issuance of Purchase Order for Manhole Covers of Sewage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
Manufacturing of Material		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
Testing and Finishes		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0.00
Material Delivery & Site Inspection		0	06-Oct-26	06-Oct-26	09-Aug-26	09-Aug-26	0.00
Main Line Sections		0	06-Oct-26	06-Oct-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SW-DL-11	Material Delivery & Site Inspection of Manholes for Sewage Network	0	06-Oct-26	06-Oct-26	09-Aug-26	09-Aug-26	0.00
Storm Drainage Network		161	02-Aug-26 A	20-Jan-27	23-Jun-26	22-Oct-26	0.00
Issuance of Purchase Orders		6	06-Oct-26	13-Oct-26	23-Jun-26	14-Jul-26	0.00
Main Line Sections		6	06-Oct-26	13-Oct-26	23-Jun-26	01-Jul-26	0.00
PRO-SD-PO-100	Issuance of Purchase Order for Manholes of Storm Drainage Network	6	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0.00
PRO-SD-PO-110	Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network	3	06-Oct-26	08-Oct-26	28-Jun-26	01-Jul-26	0.00
Catch Basin Sections		6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
PRO-SD-PO-130	Issuance of Purchase Order for Catch Basins of Storm Drainage Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
PRO-SD-PO-150	Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
PRO-SD-PO-120	Issuance of Purchase Order for Manhole Covers of Storm Drainage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
PRO-SD-PO-140	Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
Manufacturing of Material		104	09-Oct-26	20-Jan-27	30-Jun-26	22-Oct-26	0.00
Main Line Sections		44	09-Oct-26	22-Nov-26	30-Jun-26	08-Aug-26	0.00
PRO-SD-MF-110	Manufacturing of Materials for Main Line Pipes of Storm Drainage Network	8	09-Oct-26	16-Oct-26	01-Jul-26	09-Jul-26	0.00
PRO-SD-MF-100	Manufacturing of Materials for Manholes of Storm Drainage Network	40	13-Oct-26	22-Nov-26	30-Jun-26	08-Aug-26	0.00
Catch Basin Sections		20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0.00
PRO-SD-MF-130	Manufacturing of Materials for Catch Basins of Storm Drainage Network	20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0.00
PRO-SD-MF-150	Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network	20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0.00
Testing and Finishes		100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0.00
1st Material Delivery & Site Inspection		6	17-Oct-26	22-Oct-26	09-Jul-26	16-Jul-26	0.00
Main Line Sections		6	17-Oct-26	22-Oct-26	09-Jul-26	16-Jul-26	0.00
PRO-SD-1DL-110	1ST Material Delivery for Main Line Pipes of Storm Drainage Network	6	17-Oct-26	22-Oct-26	09-Jul-26	16-Jul-26	0.00
Material Delivery & Site Inspection		20	02-Aug-26 A	22-Nov-26	16-Jul-26	09-Aug-26	0.00
Main Line Sections		20	02-Aug-26 A	22-Nov-26	16-Jul-26	09-Aug-26	0.00
PRO-R25-SD-DL-10	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	22-Nov-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SD-DL-12	Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network	0	02-Aug-26 A	24-Oct-26	16-Jul-26	16-Jul-26	0.00
Catch Basin Sections		0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	0.00
PRO-R25-SD-DL-13	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	0.00




Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R25-SD-DL-11	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	0.00
Potable Water Network		111	02-Aug-26 A	04-Feb-27	01-Jul-26	06-Nov-26	0.00
Issuance of Purchase Orders		10	06-Oct-26	17-Oct-26	01-Jul-26	19-Jul-26	0.00
Main Line Sections		8	06-Oct-26	14-Oct-26	01-Jul-26	14-Jul-26	0.00
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0.00
PRO-PW-PO-100_R	Issuance of Purchase Order for Main Line Pipes of Potable Water Network(Remaining)	5	10-Oct-26	14-Oct-26	01-Jul-26	07-Jul-26	0.00
Fire Hydrant		10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0.00
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0.00
Testing and Finishes		10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0.00
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0.00
Manufacturing of Material		115	13-Oct-26	04-Feb-27	07-Jul-26	06-Nov-26	0.00
Main Line Sections		99	13-Oct-26	19-Jan-27	07-Jul-26	12-Oct-26	0.00
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	13-Oct-26	10-Jan-27	15-Jul-26	12-Oct-26	0.00
PRO-PW-MF-100_R	Manufacturing of Main Line Pipes for Potable Water Network(Remaining)	97	15-Oct-26	19-Jan-27	07-Jul-26	11-Oct-26	0.00
Fire Hydrant		60	18-Oct-26	16-Dec-26	20-Jul-26	17-Sep-26	0.00
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	18-Oct-26	16-Dec-26	20-Jul-26	17-Sep-26	0.00
Testing and Finishes		110	18-Oct-26	04-Feb-27	20-Jul-26	06-Nov-26	0.00
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	18-Oct-26	04-Feb-27	20-Jul-26	06-Nov-26	0.00
1st Material Delivery & Site Inspection		71	15-Oct-26	05-Jan-27	07-Jul-26	28-Sep-26	0.00
Main Line Sections		71	15-Oct-26	05-Jan-27	07-Jul-26	28-Sep-26	0.00
PRO-PW-1DL-100_F	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	15-Oct-26	05-Jan-27	07-Jul-26	28-Sep-26	0.00
Material Delivery & Site Inspection		0	02-Aug-26 A	05-Jan-27	29-Sep-26	29-Sep-26	0.00
Main Line Sections		0	02-Aug-26 A	05-Jan-27	29-Sep-26	29-Sep-26	0.00
PRO-R25-PW-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Remaining)	0	02-Aug-26 A	05-Jan-27	29-Sep-26	29-Sep-26	0.00
Irrigation Network		83	13-Oct-26	17-Jan-27	07-Jul-26	19-Oct-26	0.00
Issuance of Purchase Orders		6	13-Oct-26	19-Oct-26	07-Jul-26	21-Jul-26	0.00
Main Line Pipes		6	13-Oct-26	19-Oct-26	07-Jul-26	21-Jul-26	0.00
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	13-Oct-26	19-Oct-26	15-Jul-26	21-Jul-26	0.00
PRO-IR-PO-100_R	Issuance of Purchase Order for Main Line Pipes of Irrigation Network(Remaining)	3	15-Oct-26	19-Oct-26	07-Jul-26	11-Jul-26	0.00
Manufacturing of Material		91	19-Oct-26	17-Jan-27	11-Jul-26	19-Oct-26	0.00
Main Line Pipes		91	19-Oct-26	17-Jan-27	11-Jul-26	19-Oct-26	0.00
PRO-IR-MF-100	Manufacturing of Main Line Pipes for Irrigation Network	86	19-Oct-26	13-Jan-27	11-Jul-26	05-Oct-26	0.00
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0.00
Treated Sewage Effluent (Tse)		83	02-Aug-26 A	18-Jan-27	27-Jun-26	10-Oct-26	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0.00
PRO-TSE-PO-120	Issuance of Purchase Order for Main Line Pipes of Treated Sewage Effluent (Tse)	6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0.00
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0.00
Main Line Pipes		90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0.00
PRO-TSE-MF-120	Manufacturing of Main Line Pipes for Treated Sewage Effluent (Tse)	90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0.00
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0.00
Material Delivery & Site Inspection		0	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	0.00
Main Line Pipes		0	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	0.00
PRO-R25-TSE-DL-1	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (Tse)(Remaining)	0	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	0.00

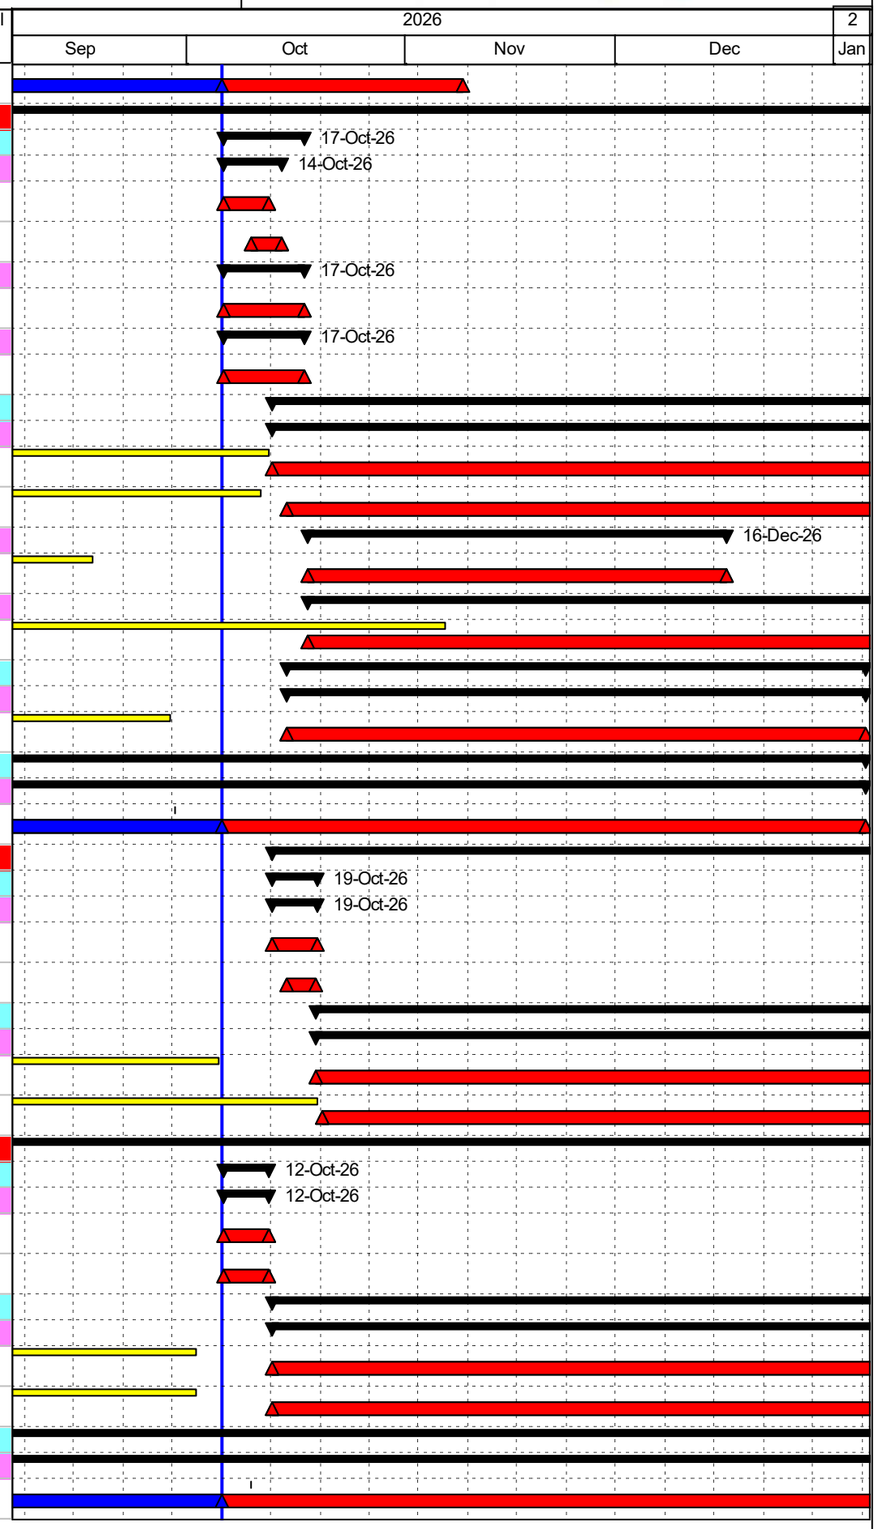

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Medium Voltage Network		89	06-Oct-26	17-Jan-27	23-Jun-26	19-Oct-26	0.00
Issuance of Purchase Orders		12	06-Oct-26	19-Oct-26	23-Jun-26	21-Jul-26	0.00
Cabling Works		12	06-Oct-26	19-Oct-26	23-Jun-26	06-Jul-26	0.00
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	06-Oct-26	19-Oct-26	23-Jun-26	06-Jul-26	0.00
Termination and Testing Works		12	06-Oct-26	19-Oct-26	08-Jul-26	21-Jul-26	0.00
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Network	12	06-Oct-26	19-Oct-26	08-Jul-26	21-Jul-26	0.00
Manufacturing of Material		90	20-Oct-26	17-Jan-27	07-Jul-26	19-Oct-26	0.00
Cabling Works		60	20-Oct-26	18-Dec-26	07-Jul-26	04-Sep-26	0.00
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	20-Oct-26	18-Dec-26	07-Jul-26	04-Sep-26	0.00
Termination and Testing Works		90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0.00
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0.00
Low Voltage and Street Lighting Network		130	06-Oct-26	16-Mar-27	23-Jun-26	12-Dec-26	0.00
Issuance of Purchase Orders		10	06-Oct-26	17-Oct-26	23-Jun-26	06-Aug-26	0.00
Cabling Works		6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
PRO-SL-PO-100	Issuance of Purchase Order for Lighting Cables of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
Lighting Poles Works		6	06-Oct-26	12-Oct-26	23-Jun-26	06-Aug-26	0.00
PRO-SL-PO-110	Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
PRO-SL-PO-120	Issuance of Purchase Order for Lighting Poles of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0.00
PRO-SL-PO-140	Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network	6	06-Oct-26	12-Oct-26	01-Aug-26	06-Aug-26	0.00
Distribution Panel Board		10	06-Oct-26	17-Oct-26	23-Jun-26	04-Jul-26	0.00
PRO-SL-PO-160	Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network	10	06-Oct-26	17-Oct-26	23-Jun-26	04-Jul-26	0.00
Termination and Testing Works		8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0.00
PRO-SL-PO-130	Issuance of Purchase Order for Fuse Boxes of Street Lighting Network	8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0.00
PRO-SL-PO-170	Issuance of Purchase Order for Cable Lugs of Street Lighting Network	8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0.00
Earthing System Works		8	06-Oct-26	14-Oct-26	07-Jul-26	15-Jul-26	0.00
PRO-SL-PO-150	Issuance of Purchase Order for Lighting Earthing of Street Lighting Network	8	06-Oct-26	14-Oct-26	07-Jul-26	15-Jul-26	0.00
Manufacturing of Material		151	13-Oct-26	16-Mar-27	30-Jun-26	12-Dec-26	0.00
Cabling Works		90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0.00
PRO-SL-MF-100	Manufacturing of Lighting Cables for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0.00
Lighting Poles Works		128	13-Oct-26	17-Feb-27	30-Jun-26	12-Dec-26	0.00
PRO-SL-MF-110	Manufacturing of Lighting Poles Foundations for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0.00
PRO-SL-MF-120	Manufacturing of Lighting Poles for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0.00
PRO-SL-MF-140	Manufacturing of Lighting Fixtures for Street Lighting Network	128	13-Oct-26	17-Feb-27	07-Aug-26	12-Dec-26	0.00
Distribution Panel Board		110	18-Oct-26	04-Feb-27	05-Jul-26	22-Oct-26	0.00
PRO-SL-MF-160	Manufacturing of Distrubution Panel Boards for Street Lighting Network	110	18-Oct-26	04-Feb-27	05-Jul-26	22-Oct-26	0.00
Termination and Testing Works		149	15-Oct-26	16-Mar-27	17-Jul-26	12-Dec-26	0.00
PRO-SL-MF-130	Manufacturing of Fuse Boxes for Street Lighting Network	149	15-Oct-26	16-Mar-27	17-Jul-26	12-Dec-26	0.00
PRO-SL-MF-170	Manufacturing of Cable Lugs for Street Lighting Network	110	15-Oct-26	01-Feb-27	17-Jul-26	03-Nov-26	0.00
Earthing System Works		140	15-Oct-26	03-Mar-27	16-Jul-26	02-Dec-26	0.00
PRO-SL-MF-150	Manufacturing of Lighting Earthing for Street Lighting Network	140	15-Oct-26	03-Mar-27	16-Jul-26	02-Dec-26	0.00
Telecom Network		83	06-Oct-26	10-Jan-27	07-Jul-26	11-Oct-26	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
Ducts Works		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
Manholes Works		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00



Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
CCTV System Wroks		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0.00
Ducts Works		60	13-Oct-26	11-Dec-26	14-Jul-26	11-Sep-26	0.00
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	13-Oct-26	11-Dec-26	14-Jul-26	11-Sep-26	0.00
Manholes Works		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0.00
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0.00
CCTV System Wroks		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0.00
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0.00
Superstructure Works		139	02-Aug-26 A	03-Jan-27	23-Jun-26	11-Oct-26	0.00
Issuance of Purchase Orders		18	06-Oct-26	26-Oct-26	23-Jun-26	13-Jul-26	0.00
Storage Tank (TSE)		11	14-Oct-26	26-Oct-26	01-Jul-26	13-Jul-26	0.00
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	14-Oct-26	26-Oct-26	01-Jul-26	13-Jul-26	0.00
Gaurd Room		11	06-Oct-26	18-Oct-26	23-Jun-26	05-Jul-26	0.00
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	06-Oct-26	18-Oct-26	23-Jun-26	05-Jul-26	0.00
Manufacturing of Material		90	06-Oct-26	03-Jan-27	23-Jun-26	11-Oct-26	0.00
Pump Stations		40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0.00
PRO-SPS-CV-MF-10	Manufacturing of Civil Works for Pump Stations	40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0.00
Lift Station		40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0.00
PRO-LS-CV-MF-30	Manufacturing of Civil Works for Civil Works for Lift Stations	40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0.00
Gaurd Room		40	18-Oct-26	27-Nov-26	05-Jul-26	14-Aug-26	0.00
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	18-Oct-26	27-Nov-26	05-Jul-26	14-Aug-26	0.00
Softscape and Planting Works		90	06-Oct-26	03-Jan-27	13-Jul-26	11-Oct-26	0.00
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	06-Oct-26	03-Jan-27	13-Jul-26	11-Oct-26	0.00
Material Delivery & Site Inspection		9	02-Aug-26 A	25-Nov-26	25-Jul-26	04-Aug-26	0.00
Pump Stations		0	02-Aug-26 A	25-Nov-26	04-Aug-26	04-Aug-26	0.00
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Pump Stations	0	02-Aug-26 A	25-Nov-26	04-Aug-26	04-Aug-26	0.00
Fence		0	02-Aug-26 A	06-Oct-26	25-Jul-26	25-Jul-26	0.00
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	06-Oct-26	25-Jul-26	25-Jul-26	0.00
Long Lead Time Items		38	06-Oct-26	18-Nov-26	23-Jun-26	06-Aug-26	0.00
Infrastructure Networks		20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0.00
CCTV System Wroks of Telecom Network		20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0.00
Issuance of Purchase Orders		20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0.00
PRO-CTV-LL-PO-10	Issuance of Purchase Order for Low Current Works of CCTV Complete System with All Accessories	20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0.00
Superstructure Works		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Pump Stations		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
PRO-SPS-LL-PO-10	Issuance of Purchase Order for Electromechanical Works for Pump Stations	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Lift Stations		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
PRO-LS-LL-PO-20	Issuance of Purchase Order for Electromechanical Works for Lift Stations	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Storage Tank (TSE)		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0.00
Construction Works		154	02-Aug-26 A	01-Dec-26	01-Jul-26	28-Nov-26	18,978,096.12

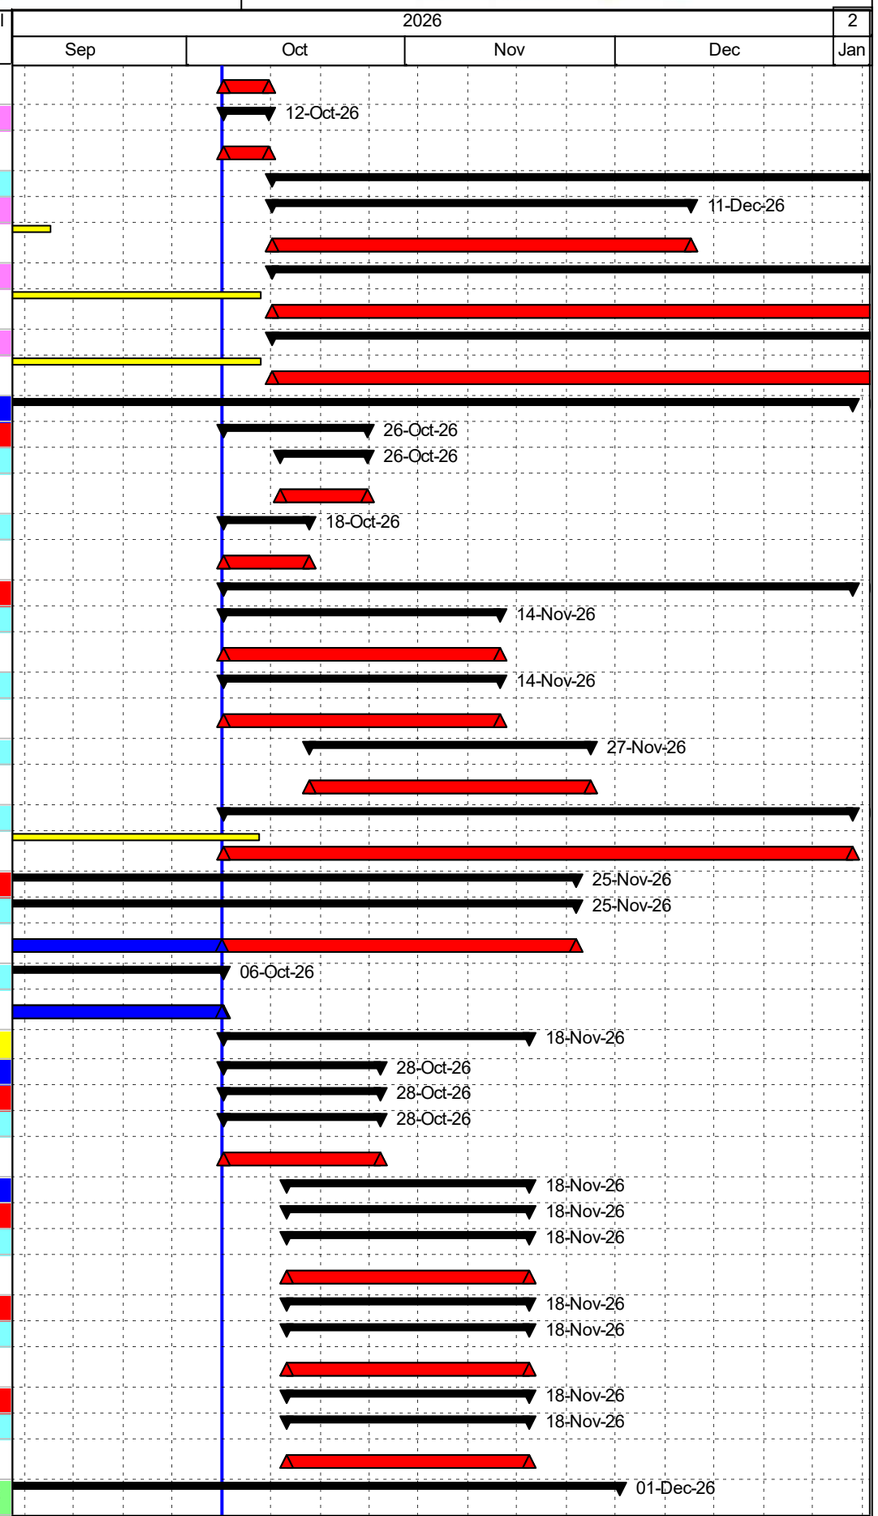


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Infrastructure Networks		112	02-Aug-26 A	09-Nov-26	01-Jul-26	17-Aug-26	6,053,466.65
Earthworks		26	02-Aug-26 A	24-Oct-26	01-Jul-26	01-Aug-26	3,797,028.96
Earthworks		26	02-Aug-26 A	24-Oct-26	01-Jul-26	01-Aug-26	3,797,028.96
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	17-Oct-26	01-Jul-26	13-Jul-26	522,497.42
CO-EW-110_R	Embankments Works Upto Design Level for Earthworks(Remaining)	16	02-Aug-26 A	24-Oct-26	13-Jul-26	01-Aug-26	2,419,920.17
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	17-Oct-26	01-Jul-26	13-Jul-26	275,826.95
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	19-Oct-26	01-Jul-26	15-Jul-26	578,784.42
Storm Drainage Network		101	02-Aug-26 A	09-Nov-26	13-Jul-26	17-Aug-26	2,194,330.10
FROM MH-25:MH-12		18	02-Aug-26 A	03-Nov-26	13-Jul-26	03-Aug-26	1,787,972.67
Main Line Sections		18	02-Aug-26 A	03-Nov-26	13-Jul-26	03-Aug-26	1,787,972.67
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	22-Oct-26	13-Jul-26	16-Jul-26	496,659.08
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	28-Oct-26	16-Jul-26	22-Jul-26	893,986.33
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	03-Nov-26	22-Jul-26	03-Aug-26	397,327.26
FROM MH-12:MH-01		14	25-Oct-26	09-Nov-26	01-Aug-26	17-Aug-26	406,357.43
Main Line Sections		14	25-Oct-26	09-Nov-26	01-Aug-26	17-Aug-26	406,357.43
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	25-Oct-26	09-Nov-26	01-Aug-26	17-Aug-26	406,357.43
Sewage Network		12	25-Oct-26	07-Nov-26	01-Aug-26	15-Aug-26	62,107.60
FROM MH-18:MH-10		12	25-Oct-26	07-Nov-26	01-Aug-26	15-Aug-26	62,107.60
Main Line Sections		12	25-Oct-26	07-Nov-26	01-Aug-26	15-Aug-26	62,107.60
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	25-Oct-26	07-Nov-26	01-Aug-26	15-Aug-26	62,107.60
Superstructure Work		127	02-Aug-26 A	01-Dec-26	02-Aug-26	28-Nov-26	12,924,629.47
Utility Buildings		27	23-Sep-26 A	01-Dec-26	13-Oct-26	28-Nov-26	290,678.88
Pump Station		6	26-Sep-26 A	01-Dec-26	21-Nov-26	28-Nov-26	72,069.14
Civil work		6	26-Sep-26 A	01-Dec-26	21-Nov-26	28-Nov-26	72,069.14
Super structure		6	26-Sep-26 A	01-Dec-26	21-Nov-26	28-Nov-26	72,069.14
CO-UB-PS-230	Steel fixing for pump roof	6	26-Sep-26 A	01-Dec-26	21-Nov-26	28-Nov-26	72,069.14
Lift Station		22	23-Sep-26 A	26-Nov-26	13-Oct-26	02-Nov-26	218,609.74
Civil work		22	23-Sep-26 A	26-Nov-26	13-Oct-26	02-Nov-26	218,609.74
Super structure		22	23-Sep-26 A	26-Nov-26	13-Oct-26	02-Nov-26	218,609.74
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	25-Nov-26	13-Oct-26	21-Oct-26	84,080.67
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	26-Nov-26	21-Oct-26	01-Nov-26	84,080.67
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	26-Nov-26	01-Nov-26	02-Nov-26	50,448.40
Fence and Gaurd Room		112	02-Aug-26 A	01-Dec-26	02-Aug-26	19-Nov-26	12,633,950.58
Fence Work		112	02-Aug-26 A	01-Dec-26	02-Aug-26	19-Nov-26	12,633,950.58
Northern Fence N01:N03		74	02-Aug-26 A	27-Oct-26	02-Aug-26	06-Sep-26	2,422,327.27
Civil Work		70	02-Aug-26 A	22-Oct-26	02-Aug-26	01-Sep-26	2,237,792.73
CO-SU-FE-N-CI-110	Pouring for Plain Concrete Northern Fence	4	02-Aug-26 A	10-Oct-26	02-Aug-26	05-Aug-26	53,454.55
CO-SU-FE-N-CI-120	Pouring R.C Footing For Northern Fence	6	02-Aug-26 A	12-Oct-26	05-Aug-26	12-Aug-26	1,494,000.00
CO-SU-FE-N-CI-130	Pouring R.C Columns For Northern Fence	5	13-Oct-26	18-Oct-26	12-Aug-26	18-Aug-26	649,407.27
CO-SU-FE-N-CI-140	Pouring Beams For Northern Fence	4	19-Oct-26	22-Oct-26	29-Aug-26	01-Sep-26	40,930.91
Finishing Work		14	29-Sep-26 A	27-Oct-26	18-Aug-26	06-Sep-26	184,534.55
Electrical Work		8	19-Oct-26	27-Oct-26	29-Aug-26	06-Sep-26	26,025.45
CO-SU-FE-N-EL-10	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	19-Oct-26	27-Oct-26	29-Aug-26	06-Sep-26	17,843.64
CO-SU-FE-N-EL-11	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	19-Oct-26	27-Oct-26	29-Aug-26	06-Sep-26	8,181.82
Architictural work		9	29-Sep-26 A	18-Oct-26	18-Aug-26	27-Aug-26	158,509.09

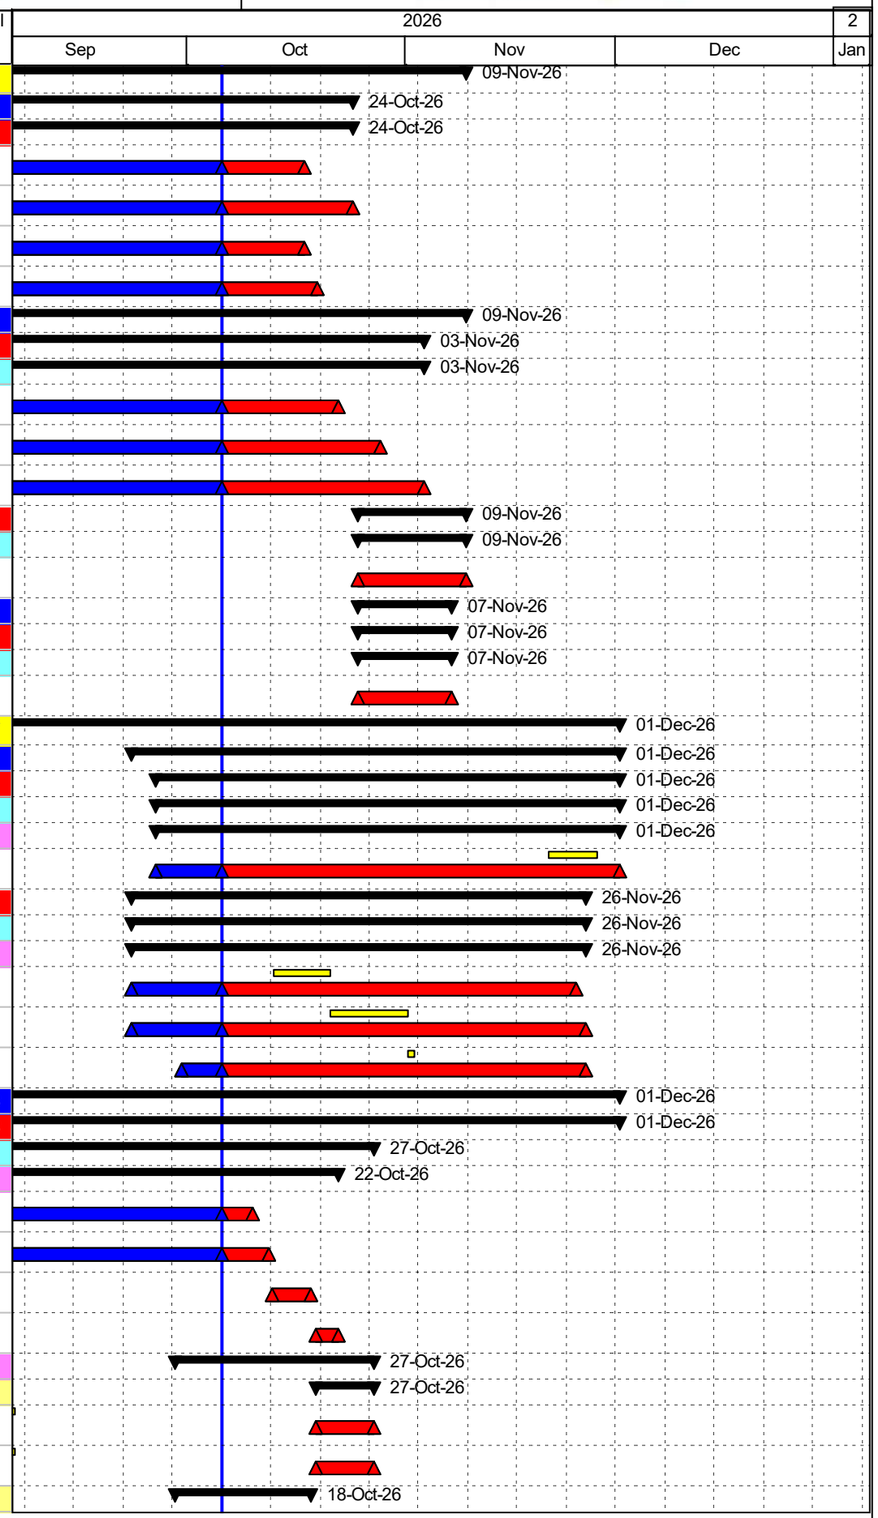

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-SU-FE-N-AR-1(	Install Brick Work For Northern Fence	9	29-Sep-26 A	18-Oct-26	18-Aug-26	27-Aug-26	158,509.09
Western Fence P1 (W01:W06)		75	02-Aug-26 A	01-Nov-26	27-Aug-26	12-Oct-26	2,287,309.09
Civil Work		61	02-Aug-26 A	01-Nov-26	27-Aug-26	01-Oct-26	1,970,290.91
CO-SU-FE-WP1-CI-1	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	11-Oct-26	27-Aug-26	02-Sep-26	106,909.09
CO-SU-FE-WP1-CI-1	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	22-Oct-26	02-Sep-26	12-Sep-26	1,188,000.00
CO-SU-FE-WP1-CI-1	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	01-Nov-26	12-Sep-26	01-Oct-26	675,381.82
Finishing Work		9	29-Sep-26 A	01-Nov-26	01-Oct-26	12-Oct-26	317,018.18
Architictural work		9	29-Sep-26 A	01-Nov-26	01-Oct-26	12-Oct-26	317,018.18
CO-SU-FE-WP1-AR	Install Brick Work For Northern Fence	9	29-Sep-26 A	01-Nov-26	01-Oct-26	12-Oct-26	317,018.18
Western Fence P2 (W07:W12)		44	02-Aug-26 A	31-Oct-26	22-Sep-26	03-Nov-26	2,231,153.01
Civil Work		31	02-Aug-26 A	24-Oct-26	22-Sep-26	18-Oct-26	1,862,083.92
CO-SU-FE-WP2-CI-2	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	19-Oct-26	22-Sep-26	29-Sep-26	106,909.09
CO-SU-FE-WP2-CI-2	Pouring R.C Footing For Northern Fence	7	02-Aug-26 A	21-Oct-26	29-Sep-26	07-Oct-26	1,188,000.00
CO-SU-FE-WP2-CI-2	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	24-Oct-26	07-Oct-26	18-Oct-26	567,174.83
Finishing Work		18	29-Sep-26 A	31-Oct-26	18-Oct-26	03-Nov-26	369,069.09
Electrical Work		6	25-Oct-26	31-Oct-26	27-Oct-26	03-Nov-26	52,050.91
CO-SU-FE-WP2-EL	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	25-Oct-26	28-Oct-26	27-Oct-26	01-Nov-26	35,687.27
CO-SU-FE-WP2-EL	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	25-Oct-26	31-Oct-26	27-Oct-26	03-Nov-26	16,363.64
Architictural work		8	29-Sep-26 A	24-Oct-26	18-Oct-26	27-Oct-26	317,018.18
CO-SU-FE-WP2-AR	Install Brick Work For Northern Fence	8	29-Sep-26 A	24-Oct-26	18-Oct-26	27-Oct-26	317,018.18
Southern Fence S01:S05		76	02-Aug-26 A	05-Nov-26	09-Aug-26	20-Sep-26	2,105,513.94
Civil Work		67	02-Aug-26 A	26-Oct-26	09-Aug-26	02-Sep-26	1,797,956.36
CO-SU-FE-S-CI-260	Pouring for Plain Concrete Northern Fence	3	02-Aug-26 A	08-Oct-26	09-Aug-26	12-Aug-26	89,090.91
CO-SU-FE-S-CI-270	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	14-Oct-26	12-Aug-26	22-Aug-26	990,000.00
CO-SU-FE-S-CI-280	Pouring R.C Columns For Northern Fence	10	15-Oct-26	26-Oct-26	22-Aug-26	02-Sep-26	718,865.45
Finishing Work		15	29-Sep-26 A	05-Nov-26	02-Sep-26	20-Sep-26	307,557.58
Electrical Work		15	20-Oct-26	05-Nov-26	02-Sep-26	20-Sep-26	43,375.76
CO-SU-FE-S-EL-56	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	20-Oct-26	05-Nov-26	02-Sep-26	20-Sep-26	29,739.39
CO-SU-FE-S-EL-62	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	20-Oct-26	05-Nov-26	02-Sep-26	20-Sep-26	13,636.36
Architictural work		6	29-Sep-26 A	26-Oct-26	02-Sep-26	09-Sep-26	264,181.82
CO-SU-FE-S-AR-28	Install Brick Work For Northern Fence	6	29-Sep-26 A	26-Oct-26	02-Sep-26	09-Sep-26	264,181.82
Eastern Fence P1 (E01:E06)		63	02-Aug-26 A	05-Nov-26	26-Aug-26	17-Oct-26	2,130,741.82
Civil Work		61	02-Aug-26 A	05-Nov-26	26-Aug-26	07-Oct-26	1,813,723.64
CO-SU-FE-EP1-CI-3	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	14-Oct-26	26-Aug-26	05-Sep-26	106,909.09
CO-SU-FE-EP1-CI-3	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	19-Oct-26	05-Sep-26	19-Sep-26	1,188,000.00
CO-SU-FE-EP1-CI-3	Pouring R.C Columns For Northern Fence	15	20-Oct-26	05-Nov-26	19-Sep-26	07-Oct-26	518,814.55
Finishing Work		8	29-Sep-26 A	05-Nov-26	07-Oct-26	17-Oct-26	317,018.18
Architictural work		8	29-Sep-26 A	05-Nov-26	07-Oct-26	17-Oct-26	317,018.18
CO-SU-FE-EP1-AR	Install Brick Work For Northern Fence	8	29-Sep-26 A	05-Nov-26	07-Oct-26	17-Oct-26	317,018.18
Eastern Fence P2 (E07:E13)		59	02-Aug-26 A	01-Dec-26	04-Oct-26	19-Nov-26	1,456,905.45
Civil Work		28	02-Aug-26 A	05-Nov-26	04-Oct-26	12-Nov-26	1,087,050.91
CO-SU-FE-EP2-CI-3	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	05-Nov-26	04-Oct-26	18-Oct-26	124,727.27
CO-SU-FE-EP2-CI-3	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	05-Nov-26	18-Oct-26	01-Nov-26	486,000.00

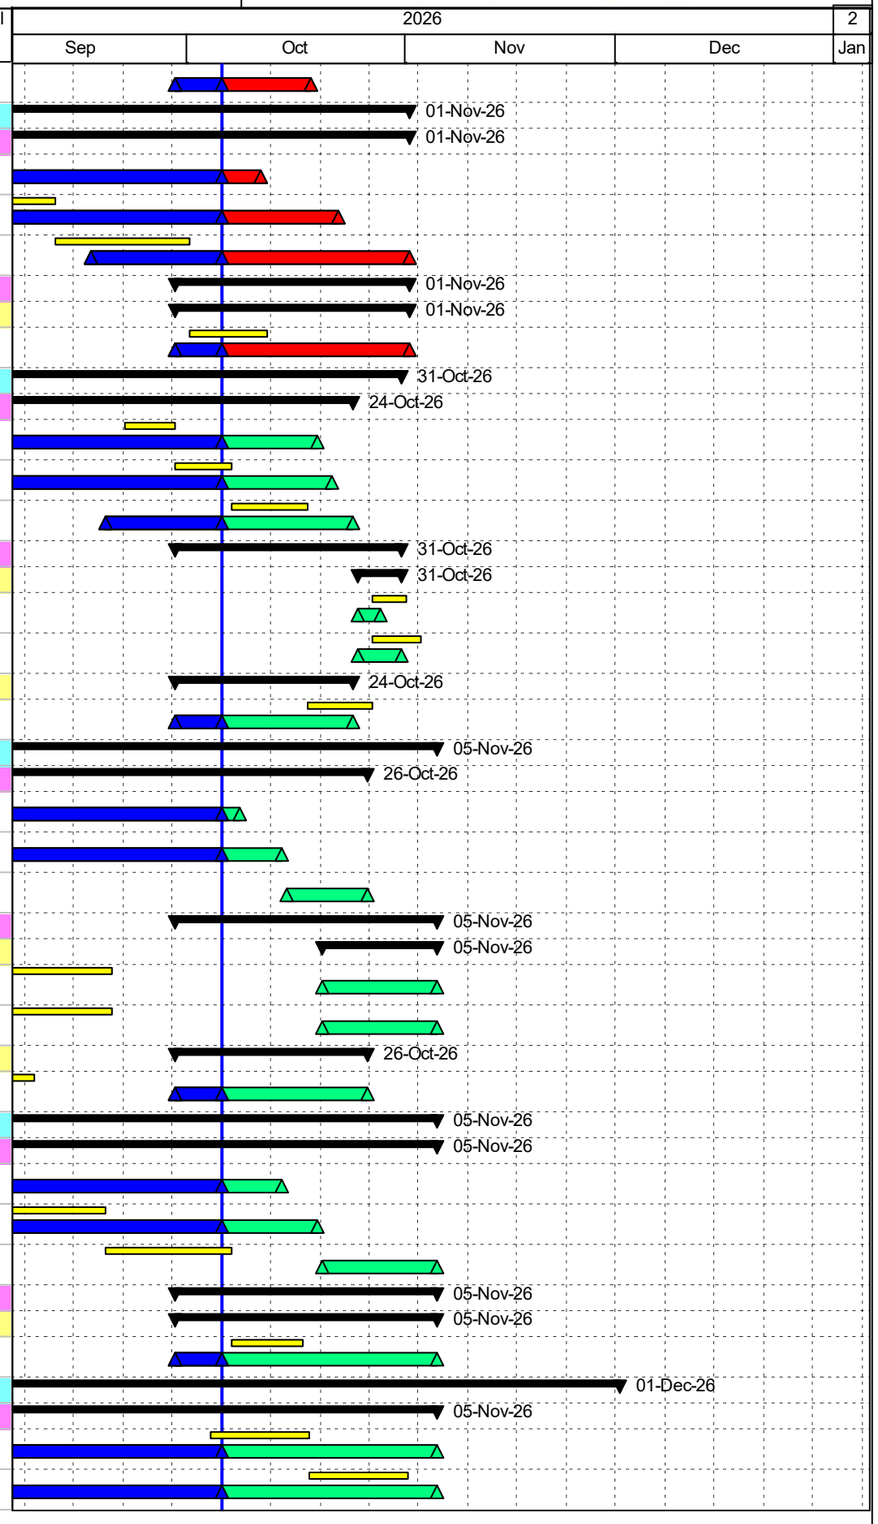


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-SU-FE-EP2-CI-3	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	05-Nov-26	01-Nov-26	12-Nov-26	476,323.64
Finishing Work		6	29-Sep-26 A	01-Dec-26	12-Nov-26	19-Nov-26	369,854.55
Architictural work		6	29-Sep-26 A	01-Dec-26	12-Nov-26	19-Nov-26	369,854.55
CO-SU-FE-EP2-AR	Install Brick Work For Northern Fence	6	29-Sep-26 A	01-Dec-26	12-Nov-26	19-Nov-26	369,854.55
Testing and Comissioning		0	24-Oct-26	24-Oct-26	04-Jan-27	04-Jan-27	0.00
Utility Buildings		0	24-Oct-26	24-Oct-26	04-Jan-27	04-Jan-27	0.00
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	24-Oct-26	24-Oct-26	04-Jan-27	04-Jan-27	0.00
Handing over and close out		14	24-Oct-26	08-Nov-26	04-Jan-27	19-Jan-27	0.00
As-Built		14	24-Oct-26	08-Nov-26	04-Jan-27	19-Jan-27	0.00
HO-130	Submission As-Built Drawing For Pond	14	24-Oct-26	08-Nov-26	04-Jan-27	19-Jan-27	0.00

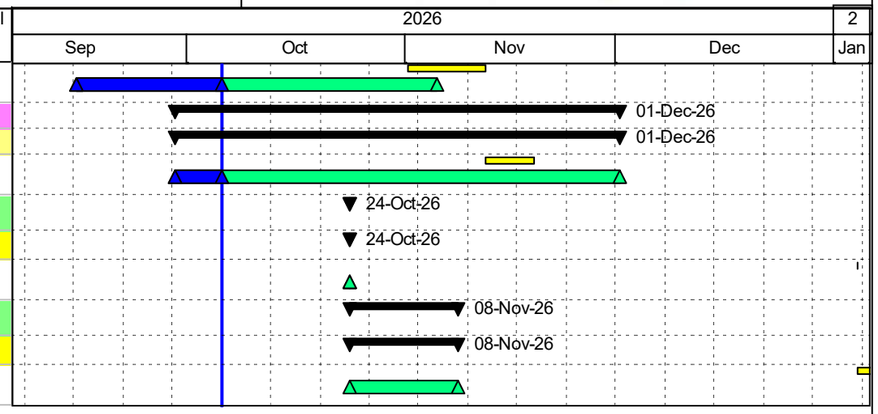

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
