

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Development of the Technology City in Dammam-Project UPDATE 06-1(		288	02-Aug-26 A	20-Jun-27	23-Jun-26	23-Feb-27	16.03%	64,363,673.52	64,363,673.52
Key Milestones		198	14-Oct-26	20-Jun-27	13-Jul-26	23-Feb-27	0%	0.00	0.00
Contractual Milestones		198	14-Oct-26	20-Jun-27	13-Jul-26	23-Feb-27	0%	0.00	0.00
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		14-Oct-26		13-Jul-26	0%	0.00	0.00
MS-CF-SW	Completion of Construction Works for Sewage Network	0		21-Apr-27		13-Jan-27	0%	0.00	0.00
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		21-Apr-27		02-Jan-27	0%	0.00	0.00
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		24-Apr-27		03-Jan-27	0%	0.00	0.00
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		29-Apr-27		10-Jan-27	0%	0.00	0.00
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0		04-May-27		14-Jan-27	0%	0.00	0.00
MS-CF-TE	Completion of Construction Works for Telecom Network	0		09-May-27		19-Jan-27	0%	0.00	0.00
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		22-May-27		26-Jan-27	0%	0.00	0.00
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		22-May-27		26-Jan-27	0%	0.00	0.00
MS-CF-RD	Completion of Construction Works for Road Works	0		07-Jun-27		14-Feb-27	0%	0.00	0.00
MS-CF-PF	Project Completion Date	0		20-Jun-27		23-Feb-27	0%	0.00	0.00
Engineering Works		8	06-Oct-26	14-Oct-26	23-Jun-26	02-Jul-26	0%	0.00	0.00
Material Submittals and Approvals		8	06-Oct-26	14-Oct-26	23-Jun-26	02-Jul-26	0%	0.00	0.00
Short Lead Time Items		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
Superstructure Works		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
Storage Tank (TSE)		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
ENG-MT-TSE-CV-S	Material Submittal for Civil Works for Storage Tank (TSE)	7	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
Long Lead Time Items		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Superstructure Works		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Pump Stations		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0%	0.00	0.00
ENG-MT-SPS-MC-S	Material Submittal for Electromechanical Works for Pump Stations	7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0%	0.00	0.00
Approval of Material		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
ENG-MT-SPS-MC-A	Material Approval for Electromechanical Works for Pump Stations	8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Storage Tank (TSE)		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Submission of Material		7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0%	0.00	0.00
ENG-MT-TSE-MC-S	Material Submittal for Electromechanical Works for Storage Tank (TSE)	7	06-Oct-26	13-Oct-26	24-Jun-26	01-Jul-26	0%	0.00	0.00
Approval of Material		8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
ENG-MT-TSE-MC-A	Material Approval for Electromechanical Works for Storage Tank (TSE)	8	06-Oct-26	14-Oct-26	24-Jun-26	02-Jul-26	0%	0.00	0.00
Procurement Cycle		239	02-Aug-26 A	03-May-27	23-Jun-26	28-Jan-27	0%	0.00	0.00
Short Lead Time Items		239	02-Aug-26 A	03-May-27	23-Jun-26	28-Jan-27	0%	0.00	0.00
Infrastructure Networks		239	02-Aug-26 A	03-May-27	23-Jun-26	28-Jan-27	0%	0.00	0.00
Road Works		23	02-Aug-26 A	06-Oct-26	02-Nov-26	05-Dec-26	0%	0.00	0.00
Material Delivery & Site Inspection		23	02-Aug-26 A	06-Oct-26	02-Nov-26	05-Dec-26	0%	0.00	0.00
Pre-Bituminous Construction		23	02-Aug-26 A	06-Oct-26	02-Nov-26	12-Nov-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	06-Oct-26	02-Nov-26	02-Nov-26	30%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0%	0.00	0.00
Bituminous Construction		0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Prime Coat of Road Works	0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0%	0.00	0.00
PRO-R25-RD-DL-17(	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	0	06-Oct-26	06-Oct-26	05-Dec-26	05-Dec-26	0%	0.00	0.00
Pavement Works		0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Curbstones for Landscaping	0	06-Oct-26	06-Oct-26	12-Nov-26	12-Nov-26	0%	0.00	0.00
Traffic Signs Boards and Roads Marking		0	06-Oct-26	06-Oct-26	08-Nov-26	25-Nov-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	06-Oct-26	06-Oct-26	08-Nov-26	08-Nov-26	0%	0.00	0.00
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Road Markings For Road Works	0	06-Oct-26	06-Oct-26	25-Nov-26	25-Nov-26	0%	0.00	0.00
Softscape and Planting Works		105	06-Oct-26	04-Feb-27	11-Jul-26	10-Nov-26	0%	0.00	0.00

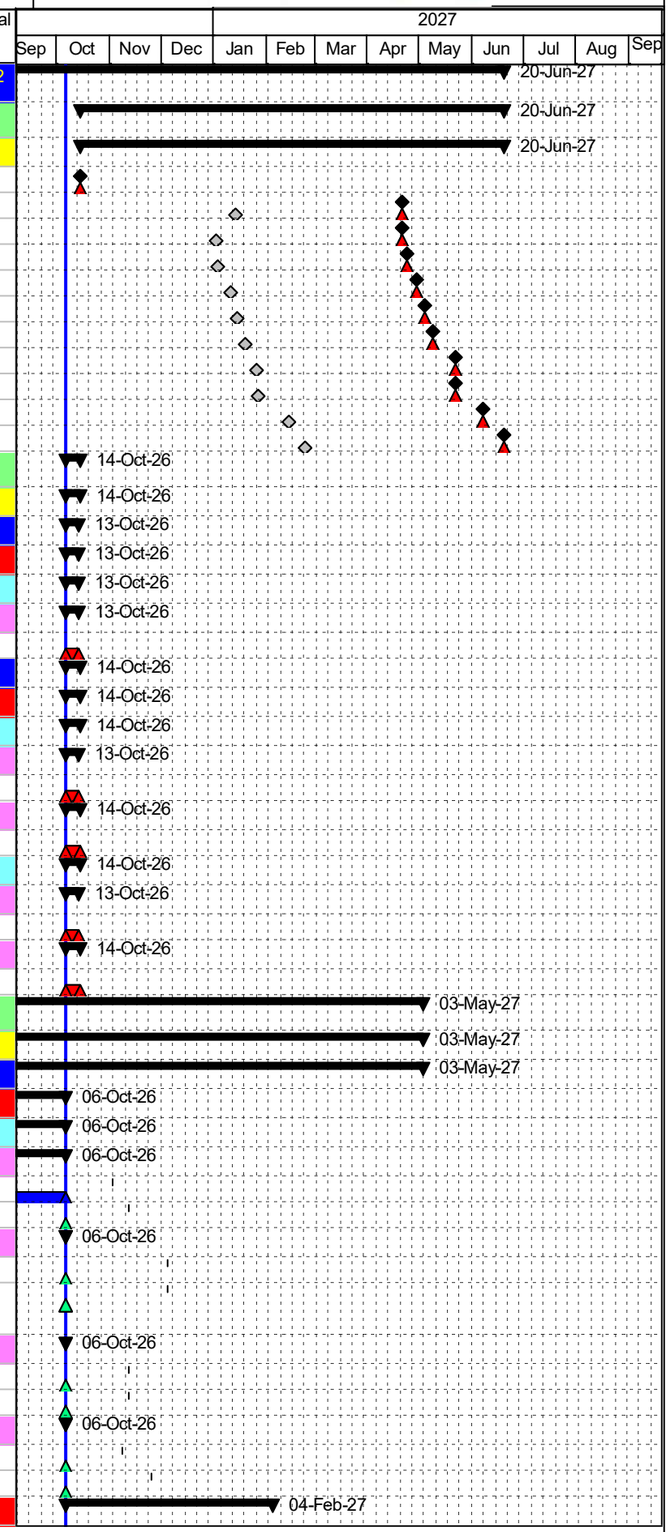

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	11-Jul-26	19-Jul-26	0%	0.00	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	11-Jul-26	19-Jul-26	0%	0.00	0.00
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	06-Oct-26	12-Oct-26	12-Jul-26	19-Jul-26	0%	0.00	0.00
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	06-Oct-26	12-Oct-26	11-Jul-26	18-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	18-Jul-26	17-Oct-26	0%	0.00	0.00
Main Line Pipes		90	13-Oct-26	10-Jan-27	18-Jul-26	17-Oct-26	0%	0.00	0.00
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	13-Oct-26	10-Jan-27	19-Jul-26	17-Oct-26	0%	0.00	0.00
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	90	13-Oct-26	10-Jan-27	18-Jul-26	16-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		6	11-Jan-27	17-Jan-27	17-Oct-26	24-Oct-26	0%	0.00	0.00
Main Line Pipes		6	11-Jan-27	17-Jan-27	17-Oct-26	24-Oct-26	0%	0.00	0.00
PRO-IR-1DL-140	1ST Material Delivery for Softscape and Planting Works	6	11-Jan-27	17-Jan-27	17-Oct-26	24-Oct-26	0%	0.00	0.00
PRO-IR-1DL-150	1ST Material Delivery for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	11-Jan-27	17-Jan-27	17-Oct-26	22-Oct-26	0%	0.00	0.00
Material Delivery & Site Inspection		16	18-Jan-27	04-Feb-27	24-Oct-26	10-Nov-26	0%	0.00	0.00
Main Line Pipes		16	18-Jan-27	04-Feb-27	24-Oct-26	10-Nov-26	0%	0.00	0.00
PRO-R25-IR-DL-14	Material Delivery & Site Inspection of Softscape and Planting Works	12	18-Jan-27	31-Jan-27	24-Oct-26	07-Nov-26	0%	0.00	0.00
PRO-R25-IR-DL-150	Material Delivery & Site Inspection of Site Furnishings (Seating Bench,Stone Boulders and Gravel)	16	18-Jan-27	04-Feb-27	24-Oct-26	10-Nov-26	0%	0.00	0.00
Sewage Network		147	06-Oct-26	05-Apr-27	08-Jul-26	28-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
PRO-SW-PO-120	Issuance of Purchase Order for Manhole Covers of Sewage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
Manufacturing of Material		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0%	0.00	0.00
Testing and Finishes		130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0%	0.00	0.00
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	13-Oct-26	19-Feb-27	15-Jul-26	21-Nov-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		6	20-Feb-27	28-Feb-27	22-Nov-26	28-Nov-26	0%	0.00	0.00
Testing and Finishes		6	20-Feb-27	28-Feb-27	22-Nov-26	28-Nov-26	0%	0.00	0.00
PRO-SW-1DL-120	1ST Material Delivery for Manholes Covers of Sewage Network	6	20-Feb-27	28-Feb-27	22-Nov-26	28-Nov-26	0%	0.00	0.00
Material Delivery & Site Inspection		147	06-Oct-26	05-Apr-27	09-Aug-26	28-Dec-26	0%	0.00	0.00
Main Line Sections		0	06-Oct-26	06-Oct-26	09-Aug-26	09-Aug-26	0%	0.00	0.00
PRO-R25-SW-DL-1	Material Delivery & Site Inspection of Manholes for Sewage Network	0	06-Oct-26	06-Oct-26	09-Aug-26	09-Aug-26	0%	0.00	0.00
Testing and Finishes		26	28-Feb-27	05-Apr-27	29-Nov-26	28-Dec-26	0%	0.00	0.00
PRO-R25-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	28-Feb-27	05-Apr-27	29-Nov-26	28-Dec-26	0%	0.00	0.00
Storm Drainage Network		200	02-Aug-26 A	17-Mar-27	23-Jun-26	10-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		6	06-Oct-26	13-Oct-26	23-Jun-26	14-Jul-26	0%	0.00	0.00
Main Line Sections		6	06-Oct-26	13-Oct-26	23-Jun-26	01-Jul-26	0%	0.00	0.00
PRO-SD-PO-100	Issuance of Purchase Order for Manholes of Storm Drainage Network	6	06-Oct-26	13-Oct-26	23-Jun-26	30-Jun-26	0%	0.00	0.00
PRO-SD-PO-110	Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network	3	06-Oct-26	08-Oct-26	28-Jun-26	01-Jul-26	0%	0.00	0.00
Catch Basin Sections		6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
PRO-SD-PO-130	Issuance of Purchase Order for Catch Basins of Storm Drainage Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
PRO-SD-PO-150	Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
PRO-SD-PO-120	Issuance of Purchase Order for Manhole Covers of Storm Drainage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
PRO-SD-PO-140	Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
Manufacturing of Material		104	09-Oct-26	20-Jan-27	30-Jun-26	22-Oct-26	0%	0.00	0.00
Main Line Sections		44	09-Oct-26	22-Nov-26	30-Jun-26	08-Aug-26	0%	0.00	0.00
PRO-SD-MF-110	Manufacturing of Materials for Main Line Pipes of Storm Drainage Network	8	09-Oct-26	16-Oct-26	01-Jul-26	09-Jul-26	0%	0.00	0.00
PRO-SD-MF-100	Manufacturing of Materials for Manholes of Storm Drainage Network	40	13-Oct-26	22-Nov-26	30-Jun-26	08-Aug-26	0%	0.00	0.00
Catch Basin Sections		20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0%	0.00	0.00

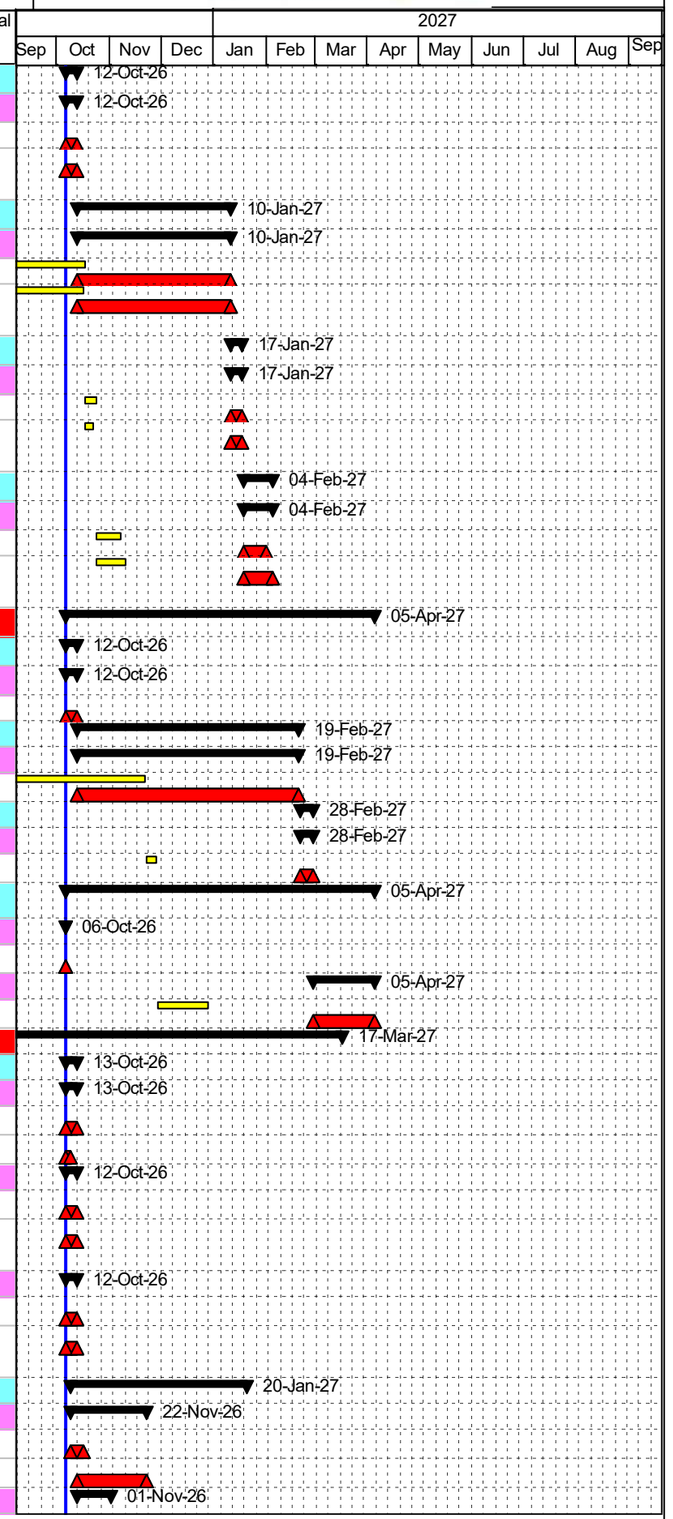

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-SD-MF-130	Manufacturing of Materials for Catch Basins of Storm Drainage Network	20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0%	0.00	0.00
PRO-SD-MF-150	Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network	20	13-Oct-26	01-Nov-26	30-Jun-26	19-Jul-26	0%	0.00	0.00
Testing and Finishes		100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0%	0.00	0.00
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0%	0.00	0.00
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	13-Oct-26	20-Jan-27	15-Jul-26	22-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		89	17-Oct-26	27-Jan-27	09-Jul-26	29-Oct-26	0%	0.00	0.00
Main Line Sections		6	17-Oct-26	22-Oct-26	09-Jul-26	16-Jul-26	0%	0.00	0.00
PRO-SD-1DL-110	1ST Material Delivery for Main Line Pipes of Storm Drainage Network	6	17-Oct-26	22-Oct-26	09-Jul-26	16-Jul-26	0%	0.00	0.00
Catch Basin Sections		6	02-Nov-26	08-Nov-26	20-Jul-26	26-Jul-26	0%	0.00	0.00
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	6	02-Nov-26	08-Nov-26	20-Jul-26	26-Jul-26	0%	0.00	0.00
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	6	02-Nov-26	08-Nov-26	20-Jul-26	26-Jul-26	0%	0.00	0.00
Testing and Finishes		6	21-Jan-27	27-Jan-27	24-Oct-26	29-Oct-26	0%	0.00	0.00
PRO-SD-1DL-140	1ST Material Delivery for Manholes Covers of Storm Drainage Network	6	21-Jan-27	27-Jan-27	24-Oct-26	29-Oct-26	0%	0.00	0.00
PRO-SD-1DL-150	1ST Material Delivery for Catch Basin Covers of Storm Drainage Network	6	21-Jan-27	27-Jan-27	24-Oct-26	29-Oct-26	0%	0.00	0.00
Material Delivery & Site Inspection		200	02-Aug-26 A	17-Mar-27	16-Jul-26	10-Dec-26	0%	0.00	0.00
Main Line Sections		20	02-Aug-26 A	22-Nov-26	16-Jul-26	09-Aug-26	0%	0.00	0.00
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	22-Nov-26	09-Aug-26	09-Aug-26	40%	0.00	0.00
PRO-R25-SD-DL-12(	Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network	0	02-Aug-26 A	24-Oct-26	16-Jul-26	16-Jul-26	82%	0.00	0.00
Catch Basin Sections		0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	0%	0.00	0.00
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Networl	0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	40%	0.00	0.00
PRO-R25-SD-DL-11(	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	09-Nov-26	27-Jul-26	27-Jul-26	40%	0.00	0.00
Testing and Finishes		33	28-Jan-27	17-Mar-27	31-Oct-26	10-Dec-26	0%	0.00	0.00
PRO-R25-SD-DL-15(	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	20	28-Jan-27	24-Feb-27	31-Oct-26	22-Nov-26	0%	0.00	0.00
PRO-R25-SD-DL-14(	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	06-Feb-27	17-Mar-27	11-Nov-26	10-Dec-26	0%	0.00	0.00
Potable Water Network		143	02-Aug-26 A	24-Mar-27	01-Jul-26	13-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		10	06-Oct-26	17-Oct-26	01-Jul-26	19-Jul-26	0%	0.00	0.00
Main Line Sections		8	06-Oct-26	14-Oct-26	01-Jul-26	14-Jul-26	0%	0.00	0.00
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	06-Oct-26	12-Oct-26	08-Jul-26	14-Jul-26	0%	0.00	0.00
PRO-PW-PO-100_R	Issuance of Purchase Order for Main Line Pipes of Potable Water Network(Remaining)	5	10-Oct-26	14-Oct-26	01-Jul-26	07-Jul-26	0%	0.00	0.00
Fire Hydrant		10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0%	0.00	0.00
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0%	0.00	0.00
Testing and Finishes		10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0%	0.00	0.00
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	06-Oct-26	17-Oct-26	08-Jul-26	19-Jul-26	0%	0.00	0.00
Manufacturing of Material		115	13-Oct-26	04-Feb-27	07-Jul-26	06-Nov-26	0%	0.00	0.00
Main Line Sections		99	13-Oct-26	19-Jan-27	07-Jul-26	12-Oct-26	0%	0.00	0.00
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	13-Oct-26	10-Jan-27	15-Jul-26	12-Oct-26	0%	0.00	0.00
PRO-PW-MF-100_I	Manufacturing of Main Line Pipes for Potable Water Network(Remaining)	97	15-Oct-26	19-Jan-27	07-Jul-26	11-Oct-26	0%	0.00	0.00
Fire Hydrant		60	18-Oct-26	16-Dec-26	20-Jul-26	17-Sep-26	0%	0.00	0.00
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	18-Oct-26	16-Dec-26	20-Jul-26	17-Sep-26	0%	0.00	0.00
Testing and Finishes		110	18-Oct-26	04-Feb-27	20-Jul-26	06-Nov-26	0%	0.00	0.00
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	18-Oct-26	04-Feb-27	20-Jul-26	06-Nov-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		103	15-Oct-26	14-Feb-27	07-Jul-26	12-Nov-26	0%	0.00	0.00
Main Line Sections		81	15-Oct-26	17-Jan-27	07-Jul-26	19-Oct-26	0%	0.00	0.00
PRO-PW-1DL-100_R	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	15-Oct-26	05-Jan-27	07-Jul-26	28-Sep-26	0%	0.00	0.00
PRO-PW-1DL-110	1ST Material Delivery for Valves of Potable Water Network	6	11-Jan-27	17-Jan-27	13-Oct-26	19-Oct-26	0%	0.00	0.00
Fire Hydrant		6	17-Dec-26	23-Dec-26	19-Sep-26	26-Sep-26	0%	0.00	0.00
PRO-PW-1DL-120	1ST Material Delivery for Fire Hydrants of Potable Water Network	6	17-Dec-26	23-Dec-26	19-Sep-26	26-Sep-26	0%	0.00	0.00

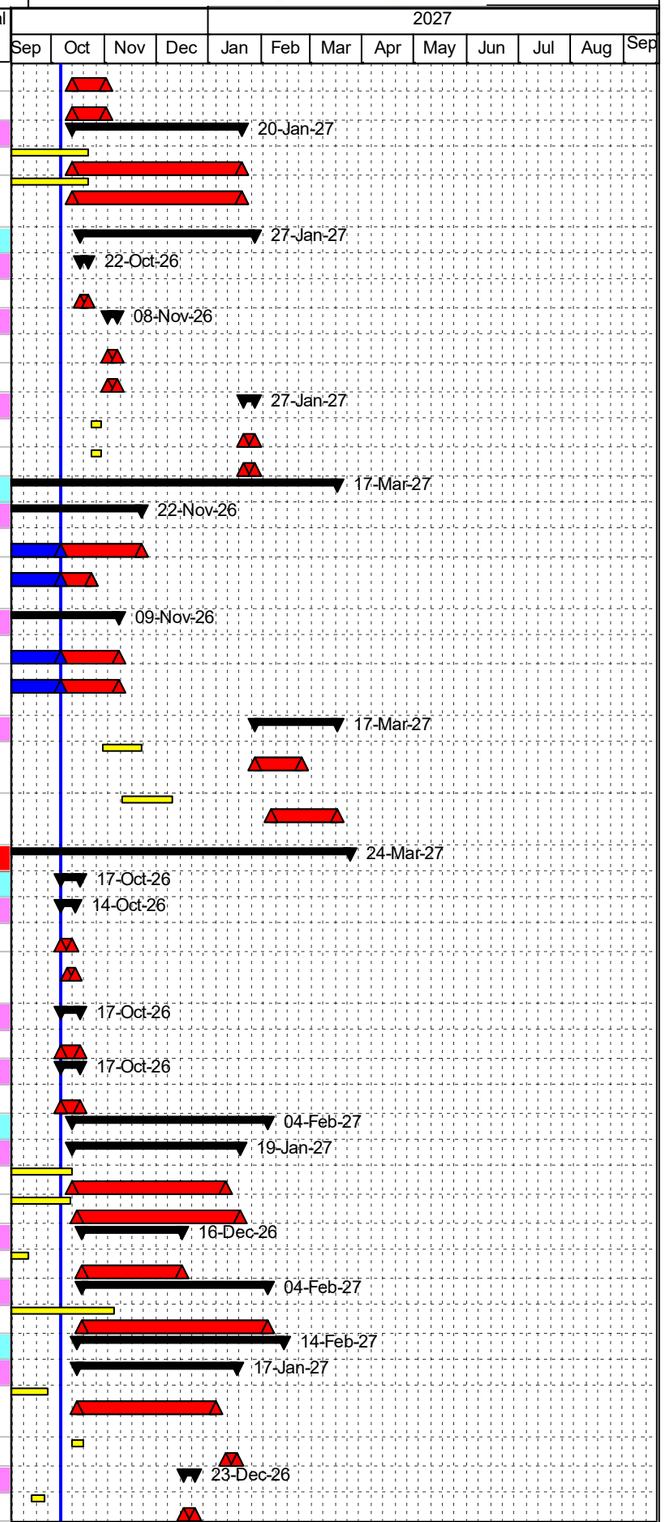

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Testing and Finishes		6	06-Feb-27	14-Feb-27	07-Nov-26	12-Nov-26	0%	0.00	0.00
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	06-Feb-27	14-Feb-27	07-Nov-26	12-Nov-26	0%	0.00	0.00
Material Delivery & Site Inspection		143	02-Aug-26 A	24-Mar-27	27-Sep-26	13-Dec-26	0%	0.00	0.00
Main Line Sections		95	02-Aug-26 A	18-Jan-27	29-Sep-26	20-Oct-26	0%	0.00	0.00
PRO-R25-PW-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Remaining)	0	02-Aug-26 A	05-Jan-27	29-Sep-26	29-Sep-26	90%	0.00	0.00
PRO-R25-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	0	18-Jan-27	18-Jan-27	20-Oct-26	20-Oct-26	0%	0.00	0.00
Fire Hydrant		0	24-Dec-26	24-Dec-26	27-Sep-26	27-Sep-26	0%	0.00	0.00
PRO-R25-PW-DL-1	Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network	0	24-Dec-26	24-Dec-26	27-Sep-26	27-Sep-26	0%	0.00	0.00
Testing and Finishes		26	14-Feb-27	24-Mar-27	14-Nov-26	13-Dec-26	0%	0.00	0.00
PRO-R25-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	14-Feb-27	24-Mar-27	14-Nov-26	13-Dec-26	0%	0.00	0.00
Irrigation Network		89	13-Oct-26	25-Jan-27	07-Jul-26	27-Oct-26	0%	0.00	0.00
Issuance of Purchase Orders		6	13-Oct-26	19-Oct-26	07-Jul-26	21-Jul-26	0%	0.00	0.00
Main Line Pipes		6	13-Oct-26	19-Oct-26	07-Jul-26	21-Jul-26	0%	0.00	0.00
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	13-Oct-26	19-Oct-26	15-Jul-26	21-Jul-26	0%	0.00	0.00
PRO-IR-PO-100_R	Issuance of Purchase Order for Main Line Pipes of Irrigation Network(Remaining)	3	15-Oct-26	19-Oct-26	07-Jul-26	11-Jul-26	0%	0.00	0.00
Manufacturing of Material		91	19-Oct-26	17-Jan-27	11-Jul-26	19-Oct-26	0%	0.00	0.00
Main Line Pipes		91	19-Oct-26	17-Jan-27	11-Jul-26	19-Oct-26	0%	0.00	0.00
PRO-IR-MF-100	Manufacturing of Main Line Pipes for Irrigation Network	86	19-Oct-26	13-Jan-27	11-Jul-26	05-Oct-26	0%	0.00	0.00
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		10	13-Jan-27	24-Jan-27	05-Oct-26	26-Oct-26	0%	0.00	0.00
Main Line Pipes		10	13-Jan-27	24-Jan-27	05-Oct-26	26-Oct-26	0%	0.00	0.00
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	13-Jan-27	19-Jan-27	05-Oct-26	11-Oct-26	0%	0.00	0.00
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	18-Jan-27	24-Jan-27	20-Oct-26	26-Oct-26	0%	0.00	0.00
Material Delivery & Site Inspection		5	19-Jan-27	25-Jan-27	11-Oct-26	27-Oct-26	0%	0.00	0.00
Main Line Pipes		5	19-Jan-27	25-Jan-27	11-Oct-26	27-Oct-26	0%	0.00	0.00
PRO-R25-IR-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	19-Jan-27	19-Jan-27	11-Oct-26	11-Oct-26	0%	0.00	0.00
PRO-R25-IR-DL-11	Material Delivery & Site Inspection of Valves for Irrigation Network	0	25-Jan-27	25-Jan-27	27-Oct-26	27-Oct-26	0%	0.00	0.00
Treated Sewage Effluent (Tse)		89	02-Aug-26 A	18-Jan-27	27-Jun-26	10-Oct-26	0%	0.00	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0%	0.00	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0%	0.00	0.00
PRO-TSE-PO-120	Issuance of Purchase Order for Main Line Pipes of Treated Sewage Effluent (Tse)	6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0%	0.00	0.00
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	06-Oct-26	12-Oct-26	27-Jun-26	04-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0%	0.00	0.00
Main Line Pipes		90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0%	0.00	0.00
PRO-TSE-MF-120	Manufacturing of Main Line Pipes for Treated Sewage Effluent (Tse)	90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0%	0.00	0.00
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	13-Oct-26	10-Jan-27	04-Jul-26	02-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		6	11-Jan-27	17-Jan-27	03-Oct-26	08-Oct-26	0%	0.00	0.00
Main Line Pipes		6	11-Jan-27	17-Jan-27	03-Oct-26	08-Oct-26	0%	0.00	0.00
PRO-TSE-1DL-120	1ST Material Delivery for Main Line Pipes of Treated Sewage Effluent (Tse)	6	11-Jan-27	17-Jan-27	03-Oct-26	08-Oct-26	0%	0.00	0.00
PRO-TSE-1DL-130	1ST Material Delivery for Valves of Treated Sewage Effluent (Tse)	6	11-Jan-27	17-Jan-27	03-Oct-26	08-Oct-26	0%	0.00	0.00
Material Delivery & Site Inspection		86	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	0%	0.00	0.00
Main Line Pipes		86	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	0%	0.00	0.00
PRO-R25-TSE-DL-12	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (Tse)(Remaining)	0	02-Aug-26 A	18-Jan-27	10-Oct-26	10-Oct-26	50%	0.00	0.00
PRO-R25-TSE-DL-	Material Delivery & Site Inspection of Valves for Treated Sewage Effluent (Tse)	0	18-Jan-27	18-Jan-27	10-Oct-26	10-Oct-26	0%	0.00	0.00
Medium Voltage Network		129	06-Oct-26	15-Mar-27	23-Jun-26	05-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		12	06-Oct-26	19-Oct-26	23-Jun-26	21-Jul-26	0%	0.00	0.00
Cabling Works		12	06-Oct-26	19-Oct-26	23-Jun-26	06-Jul-26	0%	0.00	0.00
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	06-Oct-26	19-Oct-26	23-Jun-26	06-Jul-26	0%	0.00	0.00
Termination and Testing Works		12	06-Oct-26	19-Oct-26	08-Jul-26	21-Jul-26	0%	0.00	0.00

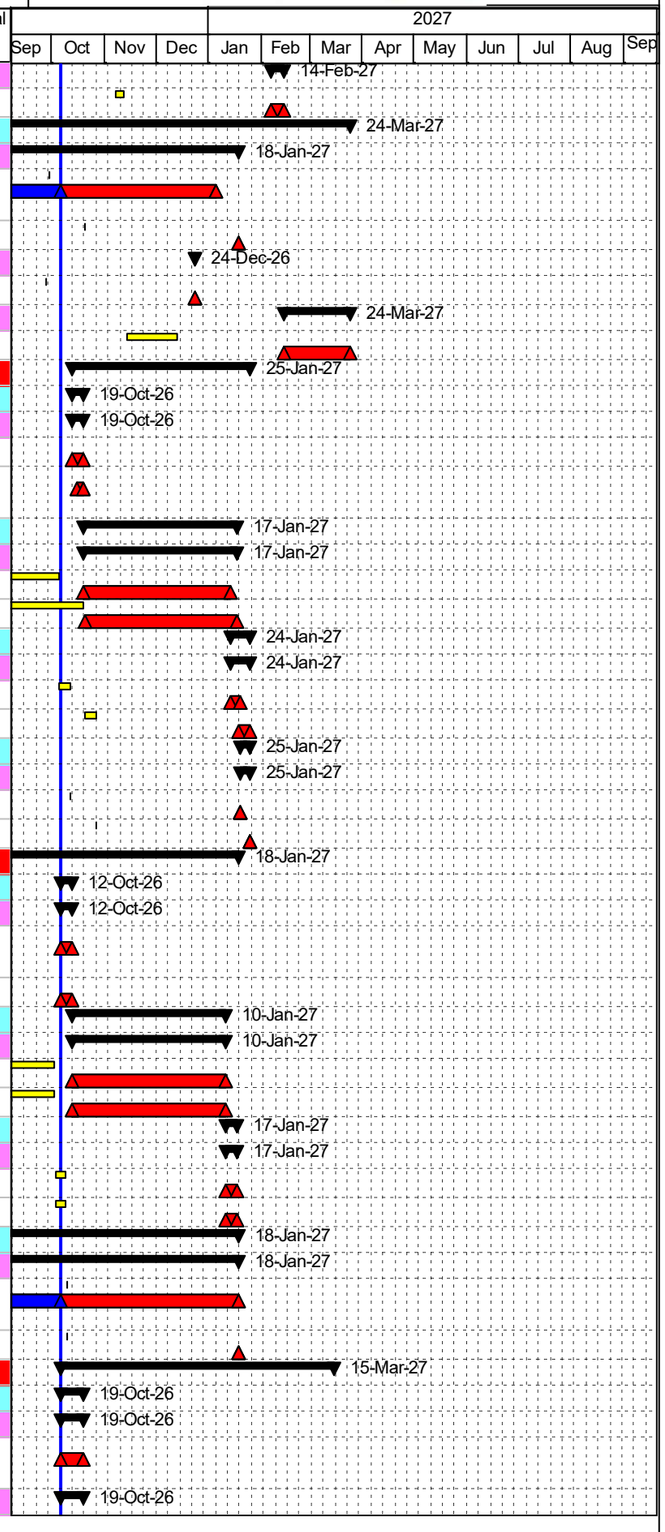

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Network	12	06-Oct-26	19-Oct-26	08-Jul-26	21-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	20-Oct-26	17-Jan-27	07-Jul-26	19-Oct-26	0%	0.00	0.00
Cabling Works		60	20-Oct-26	18-Dec-26	07-Jul-26	04-Sep-26	0%	0.00	0.00
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	20-Oct-26	18-Dec-26	07-Jul-26	04-Sep-26	0%	0.00	0.00
Termination and Testing Works		90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0%	0.00	0.00
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	20-Oct-26	17-Jan-27	22-Jul-26	19-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		40	19-Dec-26	02-Feb-27	05-Sep-26	04-Nov-26	0%	0.00	0.00
Cabling Works		12	19-Dec-26	31-Dec-26	05-Sep-26	17-Sep-26	0%	0.00	0.00
PRO-MV-1DL-100	1ST Material Delivery for Medium Voltage Cables of Medium Voltage Network	12	19-Dec-26	31-Dec-26	05-Sep-26	17-Sep-26	0%	0.00	0.00
Termination and Testing Works		14	18-Jan-27	02-Feb-27	20-Oct-26	04-Nov-26	0%	0.00	0.00
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	14	18-Jan-27	02-Feb-27	20-Oct-26	04-Nov-26	0%	0.00	0.00
Material Delivery & Site Inspection		54	02-Jan-27	15-Mar-27	19-Sep-26	05-Dec-26	0%	0.00	0.00
Cabling Works		0	02-Jan-27	02-Jan-27	19-Sep-26	19-Sep-26	0%	0.00	0.00
PRO-MV-DL-100	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage Network	0	02-Jan-27	02-Jan-27	19-Sep-26	19-Sep-26	0%	0.00	0.00
Termination and Testing Works		26	03-Feb-27	15-Mar-27	05-Nov-26	05-Dec-26	0%	0.00	0.00
PRO-MV-DL-110	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	03-Feb-27	15-Mar-27	05-Nov-26	05-Dec-26	0%	0.00	0.00
Low Voltage and Street Lighting Network		171	06-Oct-26	03-May-27	23-Jun-26	28-Jan-27	0%	0.00	0.00
Issuance of Purchase Orders		10	06-Oct-26	17-Oct-26	23-Jun-26	06-Aug-26	0%	0.00	0.00
Cabling Works		6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
PRO-SL-PO-100	Issuance of Purchase Order for Lighting Cables of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
Lighting Poles Works		6	06-Oct-26	12-Oct-26	23-Jun-26	06-Aug-26	0%	0.00	0.00
PRO-SL-PO-110	Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
PRO-SL-PO-120	Issuance of Purchase Order for Lighting Poles of Street Lighting Network	6	06-Oct-26	12-Oct-26	23-Jun-26	29-Jun-26	0%	0.00	0.00
PRO-SL-PO-140	Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network	6	06-Oct-26	12-Oct-26	01-Aug-26	06-Aug-26	0%	0.00	0.00
Distribution Panel Board		10	06-Oct-26	17-Oct-26	23-Jun-26	04-Jul-26	0%	0.00	0.00
PRO-SL-PO-160	Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network	10	06-Oct-26	17-Oct-26	23-Jun-26	04-Jul-26	0%	0.00	0.00
Termination and Testing Works		8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0%	0.00	0.00
PRO-SL-PO-130	Issuance of Purchase Order for Fuse Boxes of Street Lighting Network	8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0%	0.00	0.00
PRO-SL-PO-170	Issuance of Purchase Order for Cable Lugs of Street Lighting Network	8	06-Oct-26	14-Oct-26	08-Jul-26	16-Jul-26	0%	0.00	0.00
Earthing System Works		8	06-Oct-26	14-Oct-26	07-Jul-26	15-Jul-26	0%	0.00	0.00
PRO-SL-PO-150	Issuance of Purchase Order for Lighting Earthing of Street Lighting Network	8	06-Oct-26	14-Oct-26	07-Jul-26	15-Jul-26	0%	0.00	0.00
Manufacturing of Material		151	13-Oct-26	16-Mar-27	30-Jun-26	12-Dec-26	0%	0.00	0.00
Cabling Works		90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0%	0.00	0.00
PRO-SL-MF-100	Manufacturing of Lighting Cables for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0%	0.00	0.00
Lighting Poles Works		128	13-Oct-26	17-Feb-27	30-Jun-26	12-Dec-26	0%	0.00	0.00
PRO-SL-MF-110	Manufacturing of Lighting Poles Foundations for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0%	0.00	0.00
PRO-SL-MF-120	Manufacturing of Lighting Poles for Street Lighting Network	90	13-Oct-26	10-Jan-27	30-Jun-26	27-Sep-26	0%	0.00	0.00
PRO-SL-MF-140	Manufacturing of Lighting Fixtures for Street Lighting Network	128	13-Oct-26	17-Feb-27	07-Aug-26	12-Dec-26	0%	0.00	0.00
Distribution Panel Board		110	18-Oct-26	04-Feb-27	05-Jul-26	22-Oct-26	0%	0.00	0.00
PRO-SL-MF-160	Manufacturing of Distrubution Panel Boards for Street Lighting Network	110	18-Oct-26	04-Feb-27	05-Jul-26	22-Oct-26	0%	0.00	0.00
Termination and Testing Works		149	15-Oct-26	16-Mar-27	17-Jul-26	12-Dec-26	0%	0.00	0.00
PRO-SL-MF-130	Manufacturing of Fuse Boxes for Street Lighting Network	149	15-Oct-26	16-Mar-27	17-Jul-26	12-Dec-26	0%	0.00	0.00
PRO-SL-MF-170	Manufacturing of Cable Lugs for Street Lighting Network	110	15-Oct-26	01-Feb-27	17-Jul-26	03-Nov-26	0%	0.00	0.00
Earthing System Works		140	15-Oct-26	03-Mar-27	16-Jul-26	02-Dec-26	0%	0.00	0.00
PRO-SL-MF-150	Manufacturing of Lighting Earthing for Street Lighting Network	140	15-Oct-26	03-Mar-27	16-Jul-26	02-Dec-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		62	11-Jan-27	03-Apr-27	28-Sep-26	29-Dec-26	0%	0.00	0.00
Cabling Works		6	11-Jan-27	17-Jan-27	28-Sep-26	04-Oct-26	0%	0.00	0.00
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	11-Jan-27	17-Jan-27	28-Sep-26	04-Oct-26	0%	0.00	0.00

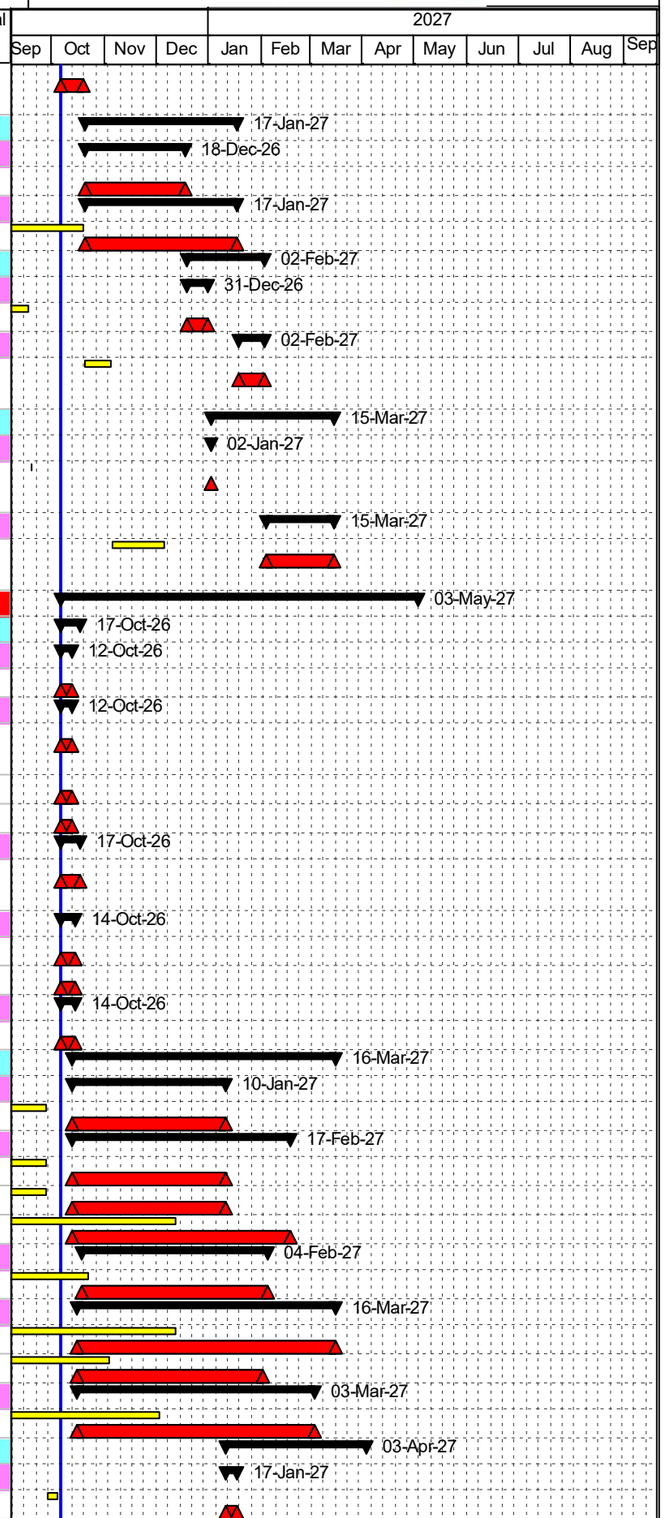


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Lighting Poles Works		37	11-Jan-27	27-Feb-27	28-Sep-26	19-Dec-26	0%	0.00	0.00
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	11-Jan-27	17-Jan-27	28-Sep-26	04-Oct-26	0%	0.00	0.00
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	11-Jan-27	17-Jan-27	28-Sep-26	04-Oct-26	0%	0.00	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	18-Feb-27	27-Feb-27	13-Dec-26	19-Dec-26	0%	0.00	0.00
Distribution Panel Board		6	06-Feb-27	14-Feb-27	24-Oct-26	29-Oct-26	0%	0.00	0.00
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	06-Feb-27	14-Feb-27	24-Oct-26	29-Oct-26	0%	0.00	0.00
Termination and Testing Works		43	02-Feb-27	03-Apr-27	03-Nov-26	29-Dec-26	0%	0.00	0.00
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	02-Feb-27	22-Feb-27	03-Nov-26	21-Nov-26	0%	0.00	0.00
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	16-Mar-27	03-Apr-27	13-Dec-26	29-Dec-26	0%	0.00	0.00
Earthing System Works		6	04-Mar-27	15-Mar-27	03-Dec-26	09-Dec-26	0%	0.00	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	04-Mar-27	15-Mar-27	03-Dec-26	09-Dec-26	0%	0.00	0.00
Material Delivery & Site Inspection		82	18-Jan-27	03-May-27	05-Oct-26	28-Jan-27	0%	0.00	0.00
Cabling Works		0	18-Jan-27	18-Jan-27	05-Oct-26	05-Oct-26	0%	0.00	0.00
PRO-R25-SL-DL-100	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	18-Jan-27	18-Jan-27	05-Oct-26	05-Oct-26	0%	0.00	0.00
Lighting Poles Works		31	18-Jan-27	27-Feb-27	05-Oct-26	20-Dec-26	0%	0.00	0.00
PRO-R25-SL-DL-110	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network	18	18-Jan-27	07-Feb-27	05-Oct-26	25-Oct-26	0%	0.00	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	18-Jan-27	18-Jan-27	05-Oct-26	05-Oct-26	0%	0.00	0.00
PRO-R25-SL-DL-140	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	27-Feb-27	27-Feb-27	20-Dec-26	20-Dec-26	0%	0.00	0.00
Distribution Panel Board		0	14-Feb-27	14-Feb-27	31-Oct-26	31-Oct-26	0%	0.00	0.00
PRO-R25-SL-DL-160	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	0	14-Feb-27	14-Feb-27	31-Oct-26	31-Oct-26	0%	0.00	0.00
Termination and Testing Works		54	23-Feb-27	03-May-27	21-Nov-26	28-Jan-27	0%	0.00	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	23-Feb-27	31-Mar-27	21-Nov-26	21-Dec-26	0%	0.00	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	03-Apr-27	03-May-27	30-Dec-26	28-Jan-27	0%	0.00	0.00
Earthing System Works		0	16-Mar-27	16-Mar-27	10-Dec-26	10-Dec-26	0%	0.00	0.00
PRO-R25-SL-DL-150	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	16-Mar-27	16-Mar-27	10-Dec-26	10-Dec-26	0%	0.00	0.00
Telecom Network		93	06-Oct-26	23-Jan-27	07-Jul-26	24-Oct-26	0%	0.00	0.00
Issuance of Purchase Orders		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
Ducts Works		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
Manholes Works		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
CCTV System Wroks		6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	06-Oct-26	12-Oct-26	07-Jul-26	13-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0%	0.00	0.00
Ducts Works		60	13-Oct-26	11-Dec-26	14-Jul-26	11-Sep-26	0%	0.00	0.00
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	13-Oct-26	11-Dec-26	14-Jul-26	11-Sep-26	0%	0.00	0.00
Manholes Works		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0%	0.00	0.00
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0%	0.00	0.00
CCTV System Wroks		90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0%	0.00	0.00
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	13-Oct-26	10-Jan-27	14-Jul-26	11-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		36	12-Dec-26	21-Jan-27	12-Sep-26	22-Oct-26	0%	0.00	0.00
Ducts Works		6	12-Dec-26	17-Dec-26	12-Sep-26	17-Sep-26	0%	0.00	0.00
PRO-TE-1DL-100	1ST Material Delivery for Ducts of Telecom Network	6	12-Dec-26	17-Dec-26	12-Sep-26	17-Sep-26	0%	0.00	0.00
Manholes Works		6	11-Jan-27	17-Jan-27	12-Oct-26	18-Oct-26	0%	0.00	0.00
PRO-TE-1DL-110	1ST Material Delivery for Manholes of Telecom Network	6	11-Jan-27	17-Jan-27	12-Oct-26	18-Oct-26	0%	0.00	0.00
CCTV System Wroks		10	11-Jan-27	21-Jan-27	12-Oct-26	22-Oct-26	0%	0.00	0.00
PRO-CTV-1DL-100	1ST Material Delivery for Civil and Finishes Works of CCTV Complete System	10	11-Jan-27	21-Jan-27	12-Oct-26	22-Oct-26	0%	0.00	0.00

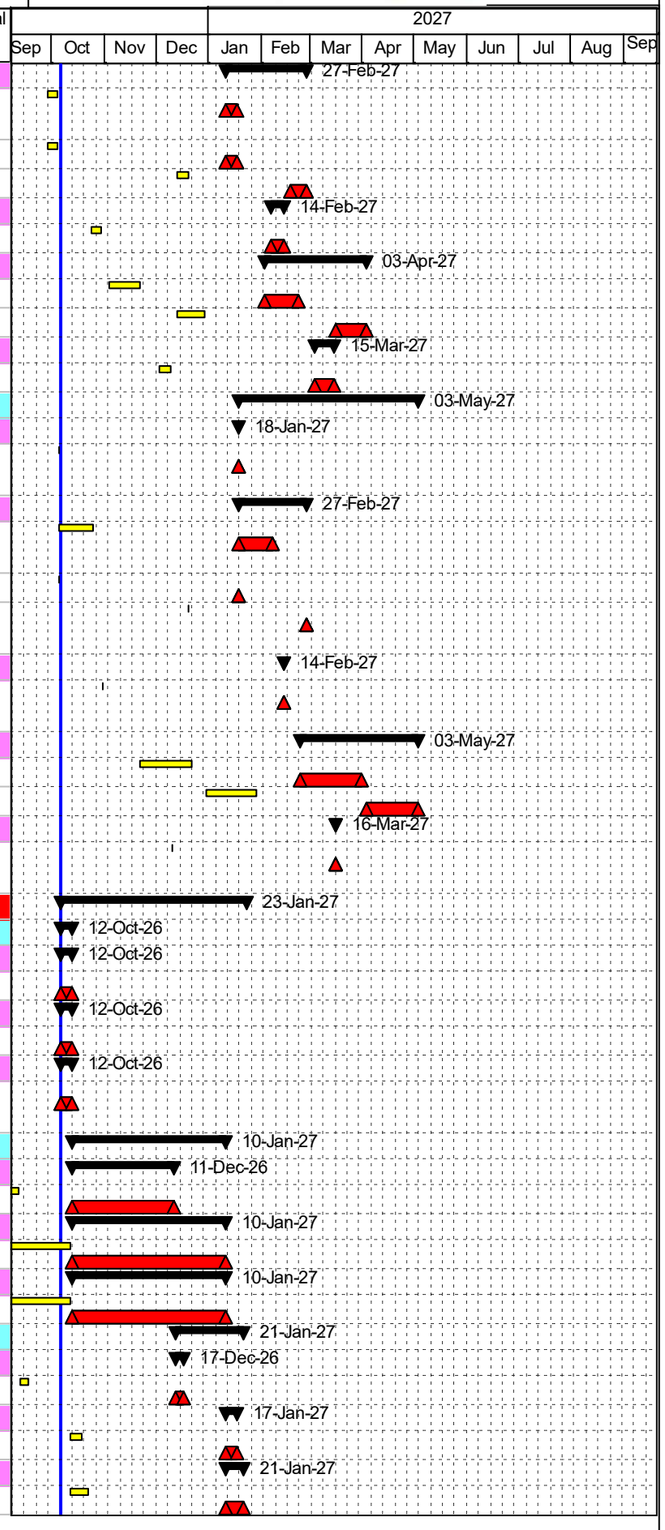

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Material Delivery & Site Inspection		30	19-Dec-26	23-Jan-27	19-Sep-26	24-Oct-26	0%	0.00	0.00
Ducts Works		0	19-Dec-26	19-Dec-26	19-Sep-26	19-Sep-26	0%	0.00	0.00
PRO-R25-TE-DL-1(	Material Delivery & Site Inspection for Ducts of Telecom Network	0	19-Dec-26	19-Dec-26	19-Sep-26	19-Sep-26	0%	0.00	0.00
Manholes Works		0	18-Jan-27	18-Jan-27	19-Oct-26	19-Oct-26	0%	0.00	0.00
PRO-R25-TE-DL-1'	Material Delivery & Site Inspection of Manholes for Telecom Network	0	18-Jan-27	18-Jan-27	19-Oct-26	19-Oct-26	0%	0.00	0.00
CCTV System Wroks		0	23-Jan-27	23-Jan-27	24-Oct-26	24-Oct-26	0%	0.00	0.00
PRO-R25-CTV-DL-1(	Material Delivery & Site Inspection of for Civil and Finishes Works of CCTV Complete System	0	23-Jan-27	23-Jan-27	24-Oct-26	24-Oct-26	0%	0.00	0.00
Superstructure Works		139	02-Aug-26 A	04-Jan-27	23-Jun-26	11-Oct-26	0%	0.00	0.00
Issuance of Purchase Orders		18	06-Oct-26	26-Oct-26	23-Jun-26	13-Jul-26	0%	0.00	0.00
Storage Tank (TSE)		11	14-Oct-26	26-Oct-26	01-Jul-26	13-Jul-26	0%	0.00	0.00
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	14-Oct-26	26-Oct-26	01-Jul-26	13-Jul-26	0%	0.00	0.00
Gaurd Room		11	06-Oct-26	18-Oct-26	23-Jun-26	05-Jul-26	0%	0.00	0.00
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	06-Oct-26	18-Oct-26	23-Jun-26	05-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	06-Oct-26	03-Jan-27	23-Jun-26	11-Oct-26	0%	0.00	0.00
Pump Stations		40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0%	0.00	0.00
PRO-SPS-CV-MF-1(	Manufacturing of Civil Works for Pump Stations	40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0%	0.00	0.00
Lift Station		40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0%	0.00	0.00
PRO-LS-CV-MF-30	Manufacturing of Civil Works for Civil Works for Lift Stations	40	06-Oct-26	14-Nov-26	23-Jun-26	01-Aug-26	0%	0.00	0.00
Storage Tank (TSE)		40	27-Oct-26	05-Dec-26	14-Jul-26	22-Aug-26	0%	0.00	0.00
PRO-TSE-CV-MF-40	Manufacturing of Civil Works for Civil Works for Storage Tank (TSE)	40	27-Oct-26	05-Dec-26	14-Jul-26	22-Aug-26	0%	0.00	0.00
Gaurd Room		40	18-Oct-26	27-Nov-26	05-Jul-26	14-Aug-26	0%	0.00	0.00
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	18-Oct-26	27-Nov-26	05-Jul-26	14-Aug-26	0%	0.00	0.00
Softscape and Planting Works		90	06-Oct-26	03-Jan-27	13-Jul-26	11-Oct-26	0%	0.00	0.00
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	06-Oct-26	03-Jan-27	13-Jul-26	11-Oct-26	0%	0.00	0.00
1st Material Delivery & Site Inspection		16	23-Nov-26	10-Dec-26	02-Aug-26	27-Aug-26	0%	0.00	0.00
Pump Stations		2	23-Nov-26	24-Nov-26	02-Aug-26	03-Aug-26	0%	0.00	0.00
PRO-SPS-CV-1DL-1	1ST Material Delivery for Civil Works for Pump Stations	2	23-Nov-26	24-Nov-26	02-Aug-26	03-Aug-26	0%	0.00	0.00
Lift Station		1	25-Nov-26	25-Nov-26	02-Aug-26	02-Aug-26	0%	0.00	0.00
PRO-LS-CV-1DL-40	1ST Material Delivery for Civil Works for Civil Works for Lift Stations	1	25-Nov-26	25-Nov-26	02-Aug-26	02-Aug-26	0%	0.00	0.00
Storage Tank (TSE)		1	06-Dec-26	06-Dec-26	23-Aug-26	23-Aug-26	0%	0.00	0.00
PRO-TSE-CV-1DL-5	1ST Material Delivery for Civil Works for Civil Works for Storage Tank (TSE)	1	06-Dec-26	06-Dec-26	23-Aug-26	23-Aug-26	0%	0.00	0.00
Gaurd Room		12	28-Nov-26	10-Dec-26	15-Aug-26	27-Aug-26	0%	0.00	0.00
PRO-GR-CV-1DL-60	1ST Material Delivery for Civil Works for Civil Works for Gaurd Room	12	28-Nov-26	10-Dec-26	15-Aug-26	27-Aug-26	0%	0.00	0.00
Material Delivery & Site Inspection		139	02-Aug-26 A	04-Jan-27	25-Jul-26	11-Oct-26	0%	0.00	0.00
Pump Stations		0	02-Aug-26 A	25-Nov-26	04-Aug-26	04-Aug-26	0%	0.00	0.00
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Pump Stations	0	02-Aug-26 A	25-Nov-26	04-Aug-26	04-Aug-26	20%	0.00	0.00
Lift Station		0	26-Nov-26	26-Nov-26	03-Aug-26	03-Aug-26	0%	0.00	0.00
PRO-LS-CV-DL-50	Material Delivery & Site Inspection for Civil Works for Lift Stations	0	26-Nov-26	26-Nov-26	03-Aug-26	03-Aug-26	0%	0.00	0.00
Storage Tank (TSE)		0	06-Dec-26	06-Dec-26	23-Aug-26	23-Aug-26	0%	0.00	0.00
PRO-TSE-CV-DL-60	Material Delivery & Site Inspection for Civil Works for Storage Tank (TSE)	0	06-Dec-26	06-Dec-26	23-Aug-26	23-Aug-26	0%	0.00	0.00
Gaurd Room		0	12-Dec-26	12-Dec-26	29-Aug-26	29-Aug-26	0%	0.00	0.00
PRO-GR-CV-DL-70	Material Delivery & Site Inspection for Civil Works for Gaurd Room	0	12-Dec-26	12-Dec-26	29-Aug-26	29-Aug-26	0%	0.00	0.00
Fence		0	02-Aug-26 A	06-Oct-26	25-Jul-26	25-Jul-26	0%	0.00	0.00
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	06-Oct-26	25-Jul-26	25-Jul-26	80%	0.00	0.00
Softscape and Planting Works		0	04-Jan-27	04-Jan-27	11-Oct-26	11-Oct-26	0%	0.00	0.00
PRO-FE-CV-DL-90	Material Delivery & Site Inspection for Softscape and Planting Works	0	04-Jan-27	04-Jan-27	11-Oct-26	11-Oct-26	0%	0.00	0.00
Long Lead Time Items		157	06-Oct-26	17-Apr-27	23-Jun-26	23-Dec-26	0%	0.00	0.00
Infrastructure Networks		112	06-Oct-26	15-Feb-27	23-Jun-26	31-Oct-26	0%	0.00	0.00
CCTV System Wroks of Telecom Network		112	06-Oct-26	15-Feb-27	23-Jun-26	31-Oct-26	0%	0.00	0.00
Issuance of Purchase Orders		20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0%	0.00	0.00
PRO-CTV-LL-PO-10	Issuance of Purchase Order for Low Current Works of CCTV Complete System with All Accessories	20	06-Oct-26	28-Oct-26	23-Jun-26	15-Jul-26	0%	0.00	0.00
Manufacturing of Material		90	29-Oct-26	26-Jan-27	16-Jul-26	13-Oct-26	0%	0.00	0.00

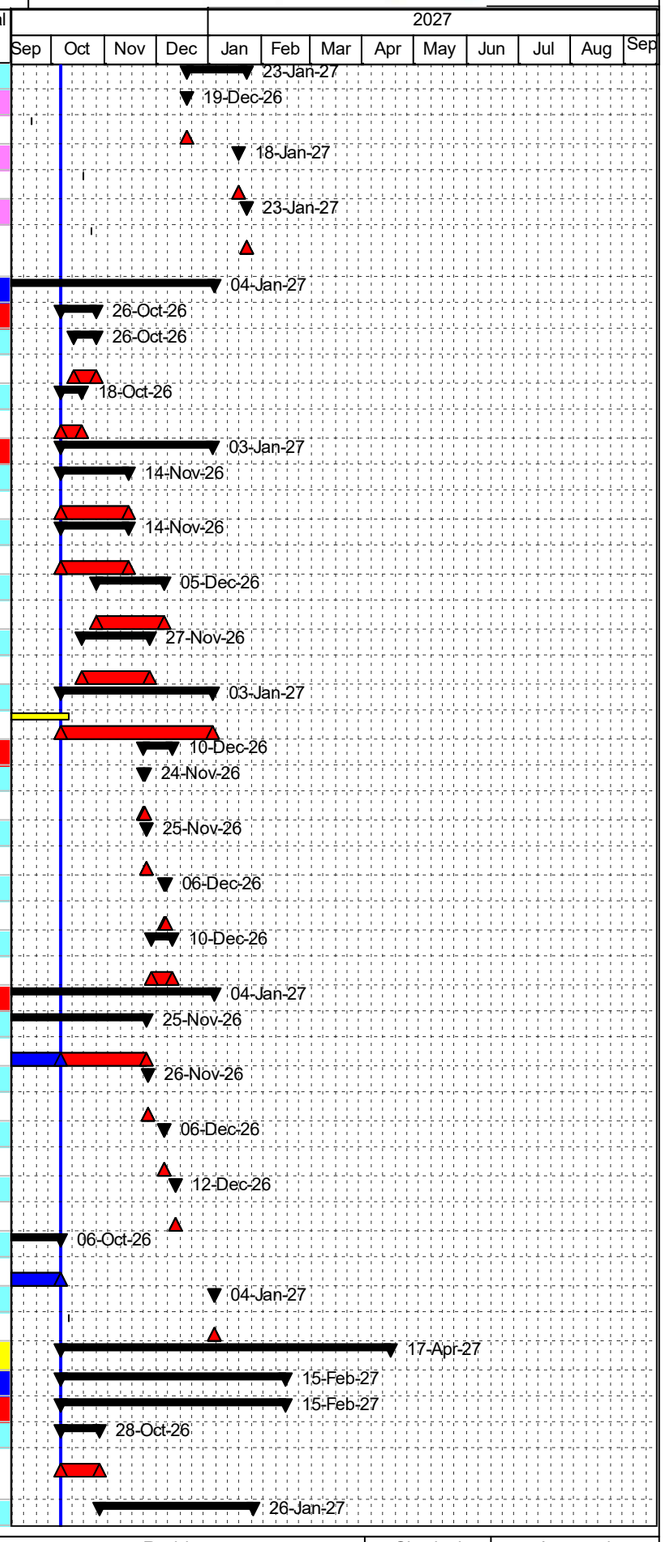

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-CTV-LL-MF-10	Manufacturing of Low Current Works for CCTV Complete System with All Accessories	90	29-Oct-26	26-Jan-27	16-Jul-26	13-Oct-26	0%	0.00	0.00
Material Shipping/Custom Clearance/Delivery		15	27-Jan-27	15-Feb-27	13-Oct-26	31-Oct-26	0%	0.00	0.00
PRO-CTV-LL-SH/DL-1	Material Delivery for Low Current Works of CCTV Complete System with All Accessories	15	27-Jan-27	15-Feb-27	13-Oct-26	31-Oct-26	0%	0.00	0.00
Material Site Inspection		0	15-Feb-27	15-Feb-27	31-Oct-26	31-Oct-26	0%	0.00	0.00
PRO-CTV-LL-MSI-10	Material Site Inspection for Low Current Works of CCTV Complete System with All Accessories	0	15-Feb-27	15-Feb-27	31-Oct-26	31-Oct-26	0%	0.00	0.00
Superstructure Works		149	15-Oct-26	17-Apr-27	04-Jul-26	23-Dec-26	0%	0.00	0.00
Pump Stations		146	15-Oct-26	13-Apr-27	04-Jul-26	20-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
PRO-SPS-LL-PO-10	Issuance of Purchase Order for Electromechanical Works for Pump Stations	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
Manufacturing of Material		60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
Material Shipping/Custom Clearance/Delivery		30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
PRO-SPS-LL-SH/DL	Material Delivery for Electromechanical Works for Pump Stations	30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
Material Site Inspection		35	25-Feb-27	13-Apr-27	10-Nov-26	20-Dec-26	0%	0.00	0.00
PRO-SPS-LL-MSI-1(	Material Site Inspection for Electromechanical Works for Pump Stations	35	25-Feb-27	13-Apr-27	10-Nov-26	20-Dec-26	0%	0.00	0.00
Lift Stations		149	15-Oct-26	17-Apr-27	04-Jul-26	23-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
PRO-LS-LL-PO-20	Issuance of Purchase Order for Electromechanical Works for Lift Stations	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
Manufacturing of Material		60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
Material Shipping/Custom Clearance/Delivery		30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
PRO-LS-LL-SH/DL-2	Material Delivery for Electromechanical Works for Lift Stations	30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
Material Site Inspection		38	25-Feb-27	17-Apr-27	10-Nov-26	23-Dec-26	0%	0.00	0.00
PRO-LS-LL-MSI-20	Material Site Inspection for Electromechanical Works for Lift Stations	38	25-Feb-27	17-Apr-27	10-Nov-26	23-Dec-26	0%	0.00	0.00
Storage Tank (TSE)		149	15-Oct-26	17-Apr-27	04-Jul-26	23-Dec-26	0%	0.00	0.00
Issuance of Purchase Orders		30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	15-Oct-26	18-Nov-26	04-Jul-26	06-Aug-26	0%	0.00	0.00
Manufacturing of Material		60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
PRO-TSE-LL-MF-30	Manufacturing of Electromechanical Works for Storage Tank (TSE)	60	19-Nov-26	17-Jan-27	07-Aug-26	05-Oct-26	0%	0.00	0.00
Material Shipping/Custom Clearance/Delivery		30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
PRO-TSE-LL-SH/DL	Material Delivery for Electromechanical Works for Storage Tank (TSE)	30	18-Jan-27	25-Feb-27	06-Oct-26	09-Nov-26	0%	0.00	0.00
Material Site Inspection		38	25-Feb-27	17-Apr-27	10-Nov-26	23-Dec-26	0%	0.00	0.00
PRO-TSE-LL-MSI-3(	Material Site Inspection for Electromechanical Works for Storage Tank (TSE)	38	25-Feb-27	17-Apr-27	10-Nov-26	23-Dec-26	0%	0.00	0.00
Construction Works		278	02-Aug-26 A	07-Jun-27	01-Jul-26	23-Feb-27	16.03%	64,363,673.52	64,363,673.52
Infrastructure Networks		278	02-Aug-26 A	07-Jun-27	01-Jul-26	14-Feb-27	11.69%	26,355,596.32	26,355,596.32
Earthworks		26	02-Aug-26 A	24-Oct-26	01-Jul-26	01-Aug-26	79.73%	3,797,028.96	3,797,028.96
Earthworks		26	02-Aug-26 A	24-Oct-26	01-Jul-26	01-Aug-26	79.73%	3,797,028.96	3,797,028.96
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	17-Oct-26	01-Jul-26	13-Jul-26	77.5%	522,497.42	522,497.42
CO-EW-110_R	Embankments Works Upto Design Level for Earthworks(Remaining)	16	02-Aug-26 A	24-Oct-26	13-Jul-26	01-Aug-26	81%	2,419,920.17	2,419,920.17
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	17-Oct-26	01-Jul-26	13-Jul-26	77.5%	275,826.95	275,826.95
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	19-Oct-26	01-Jul-26	15-Jul-26	77.5%	578,784.42	578,784.42
Storm Drainage Network		183	02-Aug-26 A	15-Feb-27	13-Jul-26	01-Nov-26	1.08%	4,958,378.40	4,958,378.40
FROM MH-25:MH-12		156	02-Aug-26 A	13-Jan-27	13-Jul-26	30-Sep-26	1.97%	2,725,882.92	2,725,882.92
Main Line Sections		18	02-Aug-26 A	03-Nov-26	13-Jul-26	03-Aug-26	3%	1,787,972.67	1,787,972.67
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	22-Oct-26	13-Jul-26	16-Jul-26	3%	496,659.08	496,659.08
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	28-Oct-26	16-Jul-26	22-Jul-26	3%	893,986.33	893,986.33
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	03-Nov-26	22-Jul-26	03-Aug-26	3%	397,327.26	397,327.26
Manholes		25	22-Nov-26	21-Dec-26	09-Aug-26	06-Sep-26	0%	247,670.25	247,670.25

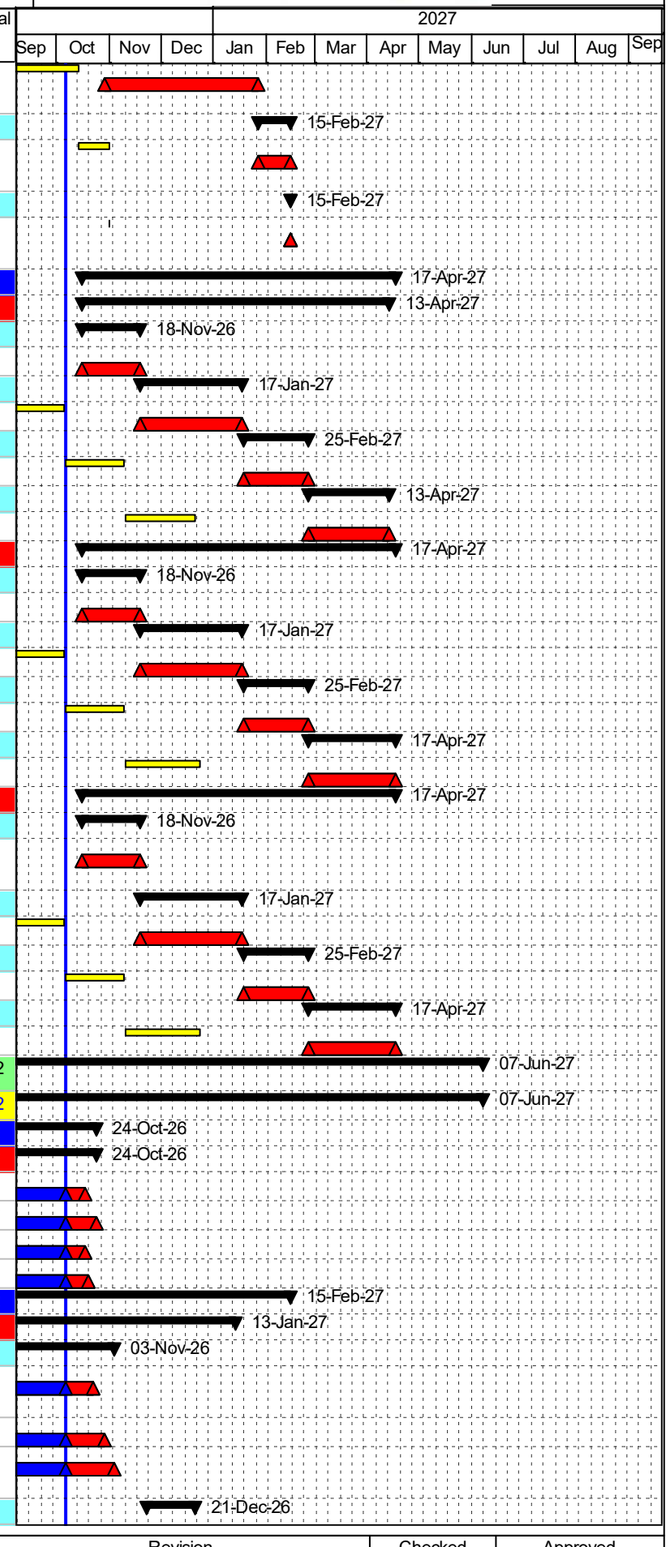

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	22-Nov-26	30-Nov-26	09-Aug-26	16-Aug-26	0%	49,534.05	49,534.05
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network	7	30-Nov-26	08-Dec-26	17-Aug-26	24-Aug-26	0%	82,556.75	82,556.75
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	4	08-Dec-26	13-Dec-26	25-Aug-26	29-Aug-26	0%	49,534.05	49,534.05
CO-SD-MH-220	Backfilling Works for Manholes of Storm Drainage Network	7	13-Dec-26	21-Dec-26	30-Aug-26	06-Sep-26	0%	66,045.40	66,045.40
Catch Basin Sections		38	30-Nov-26	13-Jan-27	17-Aug-26	30-Sep-26	0%	690,240.00	690,240.00
CO-SD-CB-140	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	10	30-Nov-26	12-Dec-26	17-Aug-26	27-Aug-26	0%	129,420.00	129,420.00
CO-SD-CB-150	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network	10	21-Dec-26	02-Jan-27	07-Sep-26	17-Sep-26	0%	388,260.00	388,260.00
CO-SD-CB-170	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network	10	02-Jan-27	13-Jan-27	19-Sep-26	30-Sep-26	0%	172,560.00	172,560.00
FROM MH-12:MH-01		96	25-Oct-26	15-Feb-27	01-Aug-26	01-Nov-26	0%	2,232,495.48	2,232,495.48
Main Line Sections		48	25-Oct-26	19-Dec-26	01-Aug-26	27-Sep-26	0%	1,462,886.73	1,462,886.73
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	25-Oct-26	09-Nov-26	01-Aug-26	17-Aug-26	0%	406,357.43	406,357.43
CO-SD-ML-150	Pipes Laying Works for Main Lines of Storm Drainage Network	14	10-Nov-26	25-Nov-26	17-Aug-26	02-Sep-26	0%	731,443.37	731,443.37
CO-SD-ML-160	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	20	26-Nov-26	19-Dec-26	02-Sep-26	27-Sep-26	0%	325,085.94	325,085.94
Manholes		32	30-Nov-26	06-Jan-27	02-Sep-26	11-Oct-26	0%	197,928.75	197,928.75
CO-SD-MH-230	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	9	30-Nov-26	10-Dec-26	02-Sep-26	13-Sep-26	0%	39,585.75	39,585.75
CO-SD-MH-240	Install RC Footing Works for Manholes of Storm Drainage Network	7	10-Dec-26	19-Dec-26	13-Sep-26	21-Sep-26	0%	65,976.25	65,976.25
CO-SD-MH-250	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	7	19-Dec-26	27-Dec-26	21-Sep-26	30-Sep-26	0%	39,585.75	39,585.75
CO-SD-MH-260	Backfilling Works for Manholes of Storm Drainage Network	9	27-Dec-26	06-Jan-27	30-Sep-26	11-Oct-26	0%	52,781.00	52,781.00
Catch Basin Sections		27	13-Jan-27	15-Feb-27	01-Oct-26	01-Nov-26	0%	571,680.00	571,680.00
CO-SD-CB-180	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	9	13-Jan-27	24-Jan-27	01-Oct-26	11-Oct-26	0%	107,190.00	107,190.00
CO-SD-CB-190	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network	9	24-Jan-27	03-Feb-27	12-Oct-26	21-Oct-26	0%	321,570.00	321,570.00
CO-SD-CB-200	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network	9	03-Feb-27	15-Feb-27	22-Oct-26	01-Nov-26	0%	142,920.00	142,920.00
Sewage Network		61	25-Oct-26	03-Jan-27	01-Aug-26	12-Oct-26	0%	651,749.20	651,749.20
FROM MH-18:MH-10		53	25-Oct-26	24-Dec-26	01-Aug-26	03-Oct-26	0%	258,640.96	258,640.96
Main Line Sections		44	25-Oct-26	14-Dec-26	01-Aug-26	21-Sep-26	0%	223,587.36	223,587.36
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	25-Oct-26	07-Nov-26	01-Aug-26	15-Aug-26	0%	62,107.60	62,107.60
CO-SW-ML-120	Pipes Laying Works for Main Lines of Sewage Network	12	08-Nov-26	21-Nov-26	15-Aug-26	29-Aug-26	0%	111,793.68	111,793.68
CO-SW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Sewage Network	20	22-Nov-26	14-Dec-26	29-Aug-26	21-Sep-26	0%	49,686.08	49,686.08
Manholes		29	22-Nov-26	24-Dec-26	29-Aug-26	03-Oct-26	0%	35,053.60	35,053.60
CO-SW-MH-160	Excavation Works for Main Line Manholes of Sewage Network	7	22-Nov-26	29-Nov-26	29-Aug-26	06-Sep-26	0%	6,572.55	6,572.55
CO-SW-MH-170	Installation RC Footing Works for Main Line Manholes of Sewage Network	7	30-Nov-26	07-Dec-26	06-Sep-26	14-Sep-26	0%	8,763.40	8,763.40
CO-SW-MH-180	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network	7	08-Dec-26	15-Dec-26	14-Sep-26	22-Sep-26	0%	8,763.40	8,763.40
CO-SW-MH-190	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network	4	16-Dec-26	20-Dec-26	22-Sep-26	28-Sep-26	0%	2,190.85	2,190.85
CO-SW-MH-200	Backfilling Works for Main Line Manholes of Sewage Network	4	21-Dec-26	24-Dec-26	28-Sep-26	03-Oct-26	0%	8,763.40	8,763.40
FROM MH-10:MH-01		49	08-Nov-26	03-Jan-27	15-Aug-26	12-Oct-26	0%	393,108.24	393,108.24
Main Line Sections		27	08-Nov-26	08-Dec-26	15-Aug-26	13-Sep-26	0%	335,381.04	335,381.04
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network	6	08-Nov-26	14-Nov-26	15-Aug-26	22-Aug-26	0%	93,161.40	93,161.40
CO-SW-ML-150	Pipes Laying Works for Main Lines of Sewage Network	7	15-Nov-26	22-Nov-26	22-Aug-26	30-Aug-26	0%	167,690.52	167,690.52
CO-SW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Sewage Network	12	25-Nov-26	08-Dec-26	30-Aug-26	13-Sep-26	0%	74,529.12	74,529.12
Manholes		30	30-Nov-26	03-Jan-27	06-Sep-26	12-Oct-26	0%	57,727.20	57,727.20
CO-SW-MH-210	Excavation Works for Main Line Manholes of Sewage Network	8	30-Nov-26	08-Dec-26	06-Sep-26	15-Sep-26	0%	10,823.85	10,823.85
CO-SW-MH-220	Installation RC Footing Works for Main Line Manholes of Sewage Network	7	09-Dec-26	16-Dec-26	15-Sep-26	24-Sep-26	0%	14,431.80	14,431.80
CO-SW-MH-230	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network	7	17-Dec-26	24-Dec-26	24-Sep-26	03-Oct-26	0%	14,431.80	14,431.80
CO-SW-MH-240	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network	4	26-Dec-26	29-Dec-26	03-Oct-26	07-Oct-26	0%	3,607.95	3,607.95

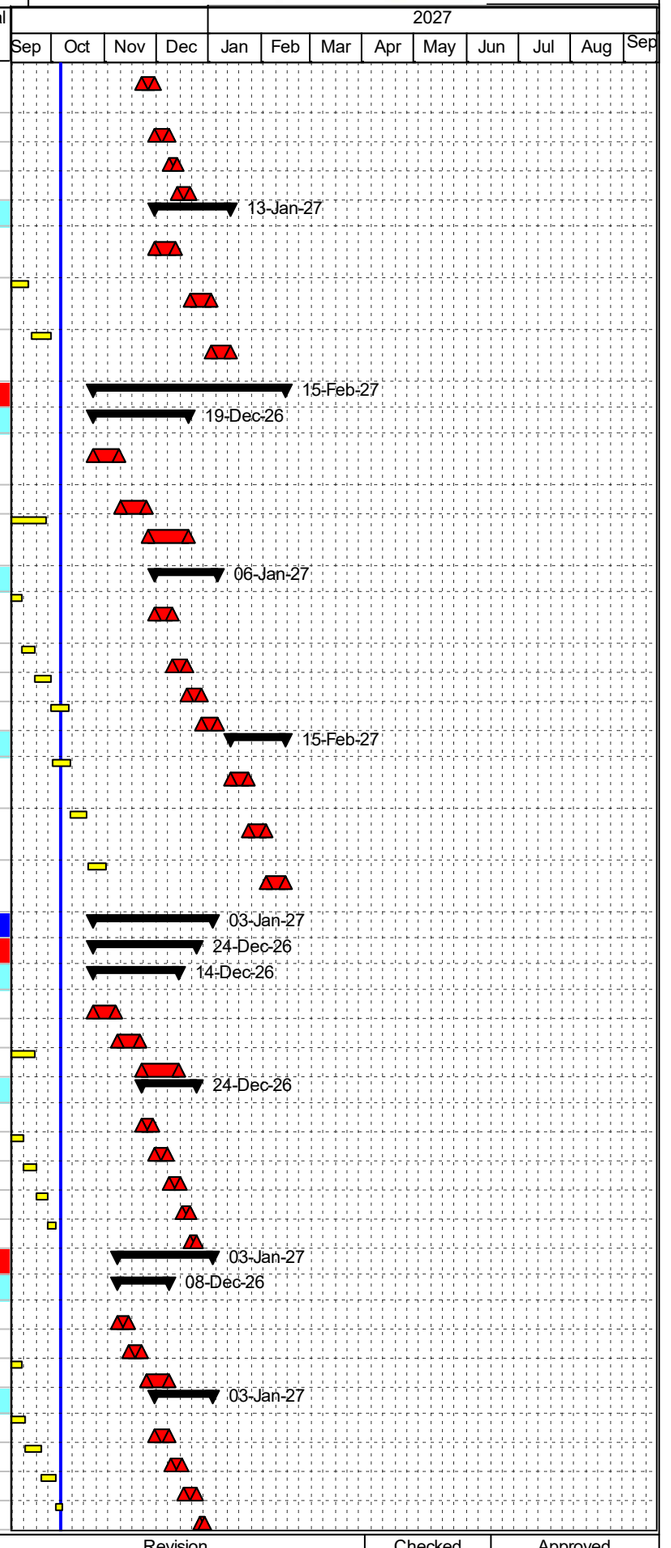

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SW-MH-250	Backfilling Works for Main Line Manholes of Sewage Network	4	30-Dec-26	03-Jan-27	07-Oct-26	12-Oct-26	0%	14,431.80	14,431.80
Potable Water Network		61	19-Jan-27	11-Apr-27	12-Oct-26	22-Dec-26	0%	956,108.40	956,108.40
Main Line Sections		24	19-Jan-27	18-Feb-27	12-Oct-26	09-Nov-26	0%	522,248.40	522,248.40
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network	8	19-Jan-27	28-Jan-27	12-Oct-26	21-Oct-26	0%	145,069.00	145,069.00
CO-PW-ML-110	Pipes Laying and accessories for Main Lines of Potable Water Network	8	28-Jan-27	07-Feb-27	21-Oct-26	31-Oct-26	0%	261,124.20	261,124.20
CO-PW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network	8	07-Feb-27	18-Feb-27	31-Oct-26	09-Nov-26	0%	116,055.20	116,055.20
Valve Chamber		16	20-Feb-27	17-Mar-27	09-Nov-26	28-Nov-26	0%	259,440.00	259,440.00
CO-PW-VC-170	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network	2	20-Feb-27	22-Feb-27	09-Nov-26	11-Nov-26	0%	15,000.00	15,000.00
CO-PW-VC180	Installation Works for Valve Chambers of Potable Water Network	4	22-Feb-27	28-Feb-27	11-Nov-26	16-Nov-26	0%	27,000.00	27,000.00
CO-PW-VC-190	Installation Works for Valves of Potable Water Network	7	28-Feb-27	14-Mar-27	16-Nov-26	24-Nov-26	0%	205,440.00	205,440.00
CO-PW-VC-220	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network	3	14-Mar-27	17-Mar-27	24-Nov-26	28-Nov-26	0%	12,000.00	12,000.00
Fire Hydrant		21	17-Mar-27	11-Apr-27	28-Nov-26	22-Dec-26	0%	174,420.00	174,420.00
CO-PW-FH-140	Excavation Works for Fire Hydrants of Potable Water Network	7	17-Mar-27	25-Mar-27	28-Nov-26	06-Dec-26	0%	48,450.00	48,450.00
CO-PW-FH-150	Installation Works for Fire Hydrant of Potable Water Network	7	25-Mar-27	03-Apr-27	06-Dec-26	14-Dec-26	0%	87,210.00	87,210.00
CO-PW-FH-160	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network	7	03-Apr-27	11-Apr-27	14-Dec-26	22-Dec-26	0%	38,760.00	38,760.00
Irrigation Network		50	28-Jan-27	07-Apr-27	21-Oct-26	19-Dec-26	0%	760,970.00	760,970.00
Main Line Pipes		50	28-Jan-27	07-Apr-27	21-Oct-26	19-Dec-26	0%	760,970.00	760,970.00
CO-IR-ML-100	Trench Excavation and Bedding Works for Main Lines of Irrigation Network	10	28-Jan-27	09-Feb-27	21-Oct-26	02-Nov-26	0%	48,300.00	48,300.00
CO-IR-ML-110	Pipes Laying Works for Main Lines of Irrigation Network	10	10-Feb-27	24-Feb-27	02-Nov-26	12-Nov-26	0%	86,940.00	86,940.00
CO-IR-ML-120	Installation Works for Main Line Valves of Irrigation Network	9	24-Feb-27	13-Mar-27	14-Nov-26	23-Nov-26	0%	572,640.00	572,640.00
CO-IR-ML-130	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network	9	17-Mar-27	28-Mar-27	28-Nov-26	08-Dec-26	0%	38,640.00	38,640.00
CO-IR-ML-140	Installation Works for Bulbblers And Sprinklers of Irrigation Network	9	28-Mar-27	07-Apr-27	08-Dec-26	19-Dec-26	0%	14,450.00	14,450.00
Treated Sewage Effluent (Tse)		50	28-Jan-27	07-Apr-27	21-Oct-26	19-Dec-26	0%	530,262.40	530,262.40
Main Line Pipes		50	28-Jan-27	07-Apr-27	21-Oct-26	19-Dec-26	0%	530,262.40	530,262.40
CO-TSE-ML-150	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	9	28-Jan-27	08-Feb-27	21-Oct-26	01-Nov-26	0%	76,734.00	76,734.00
CO-TSE-ML-160	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse)	9	10-Feb-27	23-Feb-27	02-Nov-26	12-Nov-26	0%	138,121.20	138,121.20
CO-TSE-ML-170	Installation Works for Main Line Valves of Treated Sewage Effluent (Tse)	8	24-Feb-27	08-Mar-27	14-Nov-26	22-Nov-26	0%	127,320.00	127,320.00
CO-TSE-ML-180	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse)	9	17-Mar-27	28-Mar-27	28-Nov-26	08-Dec-26	0%	61,387.20	61,387.20
CO-TSE-ML-190	Installation Works for Valve and Washout Chambers of Treated Sewage Effluent (Tse)	9	28-Mar-27	07-Apr-27	08-Dec-26	19-Dec-26	0%	126,700.00	126,700.00
Medium Voltage Network		43	07-Feb-27	08-Apr-27	31-Oct-26	20-Dec-26	0%	639,985.36	639,985.36
Cabling Works		43	07-Feb-27	08-Apr-27	31-Oct-26	20-Dec-26	0%	639,985.36	639,985.36
CO-MV-ML-250	Trench Excavation and Bedding Works for Medium Voltage Network	11	07-Feb-27	23-Feb-27	31-Oct-26	12-Nov-26	0%	41,649.44	41,649.44
CO-MV-ML-260	Cable Laying Works for Medium Voltage Network	16	23-Feb-27	21-Mar-27	12-Nov-26	01-Dec-26	0%	465,372.38	465,372.38
CO-MV-ML-270	Trench Backfilling and Compaction Works for Medium Voltage Network	16	21-Mar-27	08-Apr-27	01-Dec-26	20-Dec-26	0%	132,963.54	132,963.54
Street Lighting Network		67	08-Feb-27	06-May-27	31-Oct-26	17-Jan-27	0%	824,676.69	824,676.69
Lighting Poles Works		35	08-Feb-27	30-Mar-27	31-Oct-26	10-Dec-26	0%	239,640.00	239,640.00
CO-SL-LP-300	Foundation Excavation Works for Lighting Poles of Street Lighting Network	8	08-Feb-27	20-Feb-27	31-Oct-26	09-Nov-26	0%	29,955.00	29,955.00
CO-SL-LP-310	Installation Works for Lighting Poles Foundation of Street Lighting Network	8	20-Feb-27	03-Mar-27	09-Nov-26	18-Nov-26	0%	59,910.00	59,910.00
CO-SL-LP-320	Installation Works for Lighting Poles of Street Lighting Network	9	04-Mar-27	18-Mar-27	18-Nov-26	29-Nov-26	0%	119,820.00	119,820.00
CO-SL-LP-210	Backfilling Works for Lighting Poles of Street Lighting Network	10	20-Mar-27	30-Mar-27	29-Nov-26	10-Dec-26	0%	29,955.00	29,955.00
Cabling Works		25	20-Feb-27	28-Mar-27	09-Nov-26	08-Dec-26	0%	554,959.89	554,959.89
CO-SL-CL-250	Trench Excavation and Bedding Works for Street Lighting Network	7	20-Feb-27	02-Mar-27	09-Nov-26	17-Nov-26	0%	76,889.89	76,889.89
CO-SL-CL-260	Cable Laying Works for Street Lighting Network	7	02-Mar-27	15-Mar-27	17-Nov-26	25-Nov-26	0%	382,456.00	382,456.00
CO-SL-CL-270	Trench Backfilling and Compaction Works for Street Lighting Network	8	20-Mar-27	28-Mar-27	29-Nov-26	08-Dec-26	0%	95,614.00	95,614.00
Distrubution Panel Boards		24	08-Apr-27	06-May-27	20-Dec-26	17-Jan-27	0%	30,076.80	30,076.80
CO-SL-DB-250	Foundation Excavation Works For Panel Boards of Street Lighting Network	6	08-Apr-27	15-Apr-27	20-Dec-26	27-Dec-26	0%	4,792.20	4,792.20

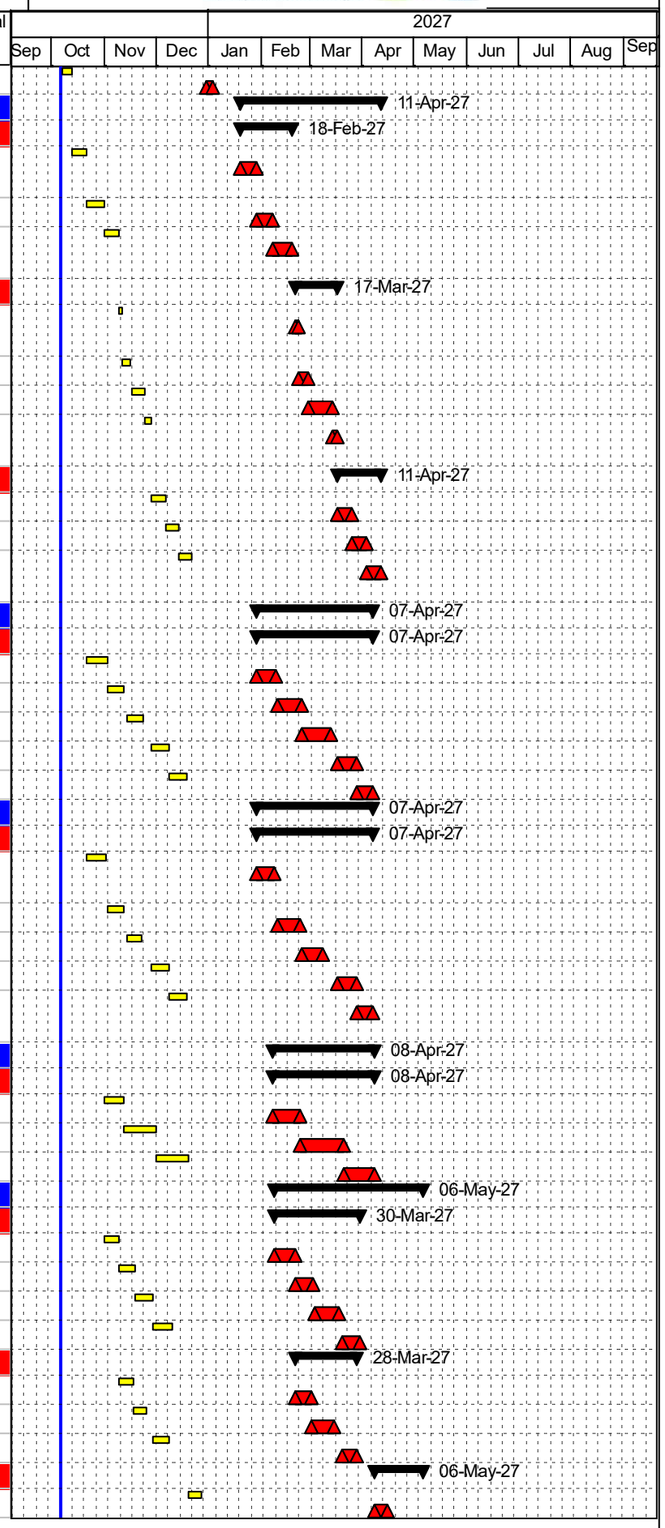

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SL-DB-260	Installation Works for Panel Board Concrete Foundations of Street Lighting Network	6	15-Apr-27	22-Apr-27	27-Dec-26	03-Jan-27	0%	4,792.20	4,792.20
CO-SL-DB-270	Installation Works for Lighting Panel Boards of Street Lighting Network	6	22-Apr-27	29-Apr-27	03-Jan-27	10-Jan-27	0%	9,584.40	9,584.40
CO-SL-DB-220	A wall of concrete blocks to install the KWH meter of Street Lighting Network	6	29-Apr-27	06-May-27	10-Jan-27	17-Jan-27	0%	10,908.00	10,908.00
Telecom Network		42	23-Feb-27	20-Apr-27	12-Nov-26	31-Dec-26	0%	4,775,135.00	4,775,135.00
Ducts Works		26	23-Feb-27	01-Apr-27	12-Nov-26	13-Dec-26	0%	1,277,742.00	1,277,742.00
CO-TE-DW-100	Trench Excavation and Bedding Works for Ducts of Telecom Network	4	23-Feb-27	01-Mar-27	12-Nov-26	17-Nov-26	0%	274,681.50	274,681.50
CO-TE-DW-110	Pipes Laying Works for Ducts of Telecom Network	4	02-Mar-27	08-Mar-27	17-Nov-26	22-Nov-26	0%	604,299.30	604,299.30
CO-TE-DW-130	Trench Backfilling and Compaction Works for Ducts of Telecom Network	8	08-Mar-27	21-Mar-27	22-Nov-26	01-Dec-26	0%	219,745.20	219,745.20
CO-TE-DW-120	Pouring Road Crossing Concrete Encasement	10	21-Mar-27	01-Apr-27	01-Dec-26	13-Dec-26	0%	179,016.00	179,016.00
Manholes Works		19	08-Mar-27	03-Apr-27	22-Nov-26	14-Dec-26	0%	266,796.00	266,796.00
CO-TE-MH-140	Excavation Works for Manholes of Telecom Network	5	08-Mar-27	17-Mar-27	22-Nov-26	28-Nov-26	0%	66,699.00	66,699.00
CO-TE-MH-150	Installation Works for Manholes of Telecom Network	7	17-Mar-27	25-Mar-27	28-Nov-26	06-Dec-26	0%	146,737.80	146,737.80
CO-TE-MH-160	Backfilling Works for Manholes of Telecom Network	7	25-Mar-27	03-Apr-27	06-Dec-26	14-Dec-26	0%	53,359.20	53,359.20
CCTV System Wroks		15	03-Apr-27	20-Apr-27	14-Dec-26	31-Dec-26	0%	3,230,597.00	3,230,597.00
CO-TE-CTV-100	Digging and Pulling Trenches PVC ducts , Backfilling, Excavations, of Power Cable	5	03-Apr-27	08-Apr-27	14-Dec-26	20-Dec-26	0%	44,838.00	44,838.00
CO-TE-CTV-110	Installation of Network Cable Cat.6A from Network switch to CCTV Camera and ACS Device	5	08-Apr-27	14-Apr-27	20-Dec-26	26-Dec-26	0%	3,142,189.00	3,142,189.00
CO-TE-CTV-130	Installation of Access Control System	5	14-Apr-27	20-Apr-27	26-Dec-26	31-Dec-26	0%	43,570.00	43,570.00
Road Works		51	23-Mar-27	26-May-27	03-Dec-26	31-Jan-27	0%	294,864.10	294,864.10
ST+1000:ST+1531		28	23-Mar-27	24-Apr-27	03-Dec-26	04-Jan-27	0%	127,701.70	127,701.70
Pre-Bituminous Construction		28	23-Mar-27	24-Apr-27	03-Dec-26	04-Jan-27	0%	127,701.70	127,701.70
CO-RD-PB-140	Subgrade Layer for Road Works	14	23-Mar-27	07-Apr-27	03-Dec-26	19-Dec-26	0%	75,313.00	75,313.00
CO-RD-PB-150	Aggregate Base Course Layer for Road Works	14	08-Apr-27	24-Apr-27	20-Dec-26	04-Jan-27	0%	52,388.70	52,388.70
ST+500:ST+1000		25	08-Apr-27	06-May-27	20-Dec-26	17-Jan-27	0%	78,701.70	78,701.70
Pre-Bituminous Construction		25	08-Apr-27	06-May-27	20-Dec-26	17-Jan-27	0%	78,701.70	78,701.70
CO-RD-PB-120	Subgrade Layer for Road Works	11	08-Apr-27	21-Apr-27	20-Dec-26	02-Jan-27	0%	26,313.00	26,313.00
CO-RD-PB-130	Aggregate Base Course Layer for Road Works	11	25-Apr-27	06-May-27	05-Jan-27	17-Jan-27	0%	52,388.70	52,388.70
ST+01:ST+500		26	21-Apr-27	26-May-27	02-Jan-27	31-Jan-27	0%	88,460.70	88,460.70
Pre-Bituminous Construction		26	21-Apr-27	26-May-27	02-Jan-27	31-Jan-27	0%	88,460.70	88,460.70
CO-RD-PB-100	Subgrade Layer for Road Works	12	21-Apr-27	05-May-27	02-Jan-27	16-Jan-27	0%	43,556.10	43,556.10
CO-RD-PB-110	Aggregate Base Course Layer for Road Works	12	08-May-27	26-May-27	18-Jan-27	31-Jan-27	0%	44,904.60	44,904.60
Finishes for Infrastructure Networks		119	04-Jan-27	07-Jun-27	12-Oct-26	14-Feb-27	0%	8,166,437.82	8,166,437.82
Storm Drainage Network		56	15-Feb-27	01-May-27	02-Nov-26	05-Jan-27	0%	825,219.60	825,219.60
Testing and Finishes		56	15-Feb-27	01-May-27	02-Nov-26	05-Jan-27	0%	825,219.60	825,219.60
CO-SD-ML-TF-100	Testing Work for Pipes of Storm Drainage Network	10	15-Feb-27	02-Mar-27	02-Nov-26	12-Nov-26	0%	361,206.60	361,206.60
CO-SD-CB-TF-130	Catch Basin Internal Finishes (Benching) for Storm Drainage Network	10	02-Mar-27	20-Mar-27	14-Nov-26	24-Nov-26	0%	78,870.00	78,870.00
CO-SD-CB-TF-160	Testing Works for Catch Basins of Storm Drainage Network	10	20-Mar-27	31-Mar-27	25-Nov-26	06-Dec-26	0%	157,740.00	157,740.00
CO-SD-CB-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network	10	31-Mar-27	12-Apr-27	07-Dec-26	17-Dec-26	0%	78,870.00	78,870.00
CO-SD-MH-TF-120	Main Manhole Internal Finishes (Benching) for Storm Drainage Network	10	12-Apr-27	24-Apr-27	19-Dec-26	29-Dec-26	0%	89,119.80	89,119.80
CO-SD-MH-TF-210	Testing Works for Manholes of Storm Drainage Network	6	24-Apr-27	01-May-27	30-Dec-26	05-Jan-27	0%	59,413.20	59,413.20
Sewage Network		84	04-Jan-27	21-Apr-27	12-Oct-26	13-Jan-27	0%	85,302.80	85,302.80
Testing and Finishes		84	04-Jan-27	21-Apr-27	12-Oct-26	13-Jan-27	0%	85,302.80	85,302.80
CO-SW-TF-100	Final Testing For Main Line of Sewage Network	9	04-Jan-27	13-Jan-27	12-Oct-26	22-Oct-26	0%	62,107.60	62,107.60
CO-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network	21	14-Jan-27	07-Feb-27	22-Oct-26	16-Nov-26	0%	5,798.80	5,798.80
CO-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network	10	05-Apr-27	17-Apr-27	29-Dec-26	09-Jan-27	0%	5,798.80	5,798.80
CO-SW-TF-210	Testing Works for Main Line Manholes of Sewage Network	4	17-Apr-27	21-Apr-27	10-Jan-27	13-Jan-27	0%	11,597.60	11,597.60
Potable Water Network		31	11-Apr-27	22-May-27	22-Dec-26	26-Jan-27	0%	83,407.60	83,407.60
Testing and Finishes		31	11-Apr-27	22-May-27	22-Dec-26	26-Jan-27	0%	83,407.60	83,407.60
CO-PW-TF-110	Testing Work for Main Line of Potable Water Network	11	11-Apr-27	22-Apr-27	22-Dec-26	03-Jan-27	0%	58,027.60	58,027.60

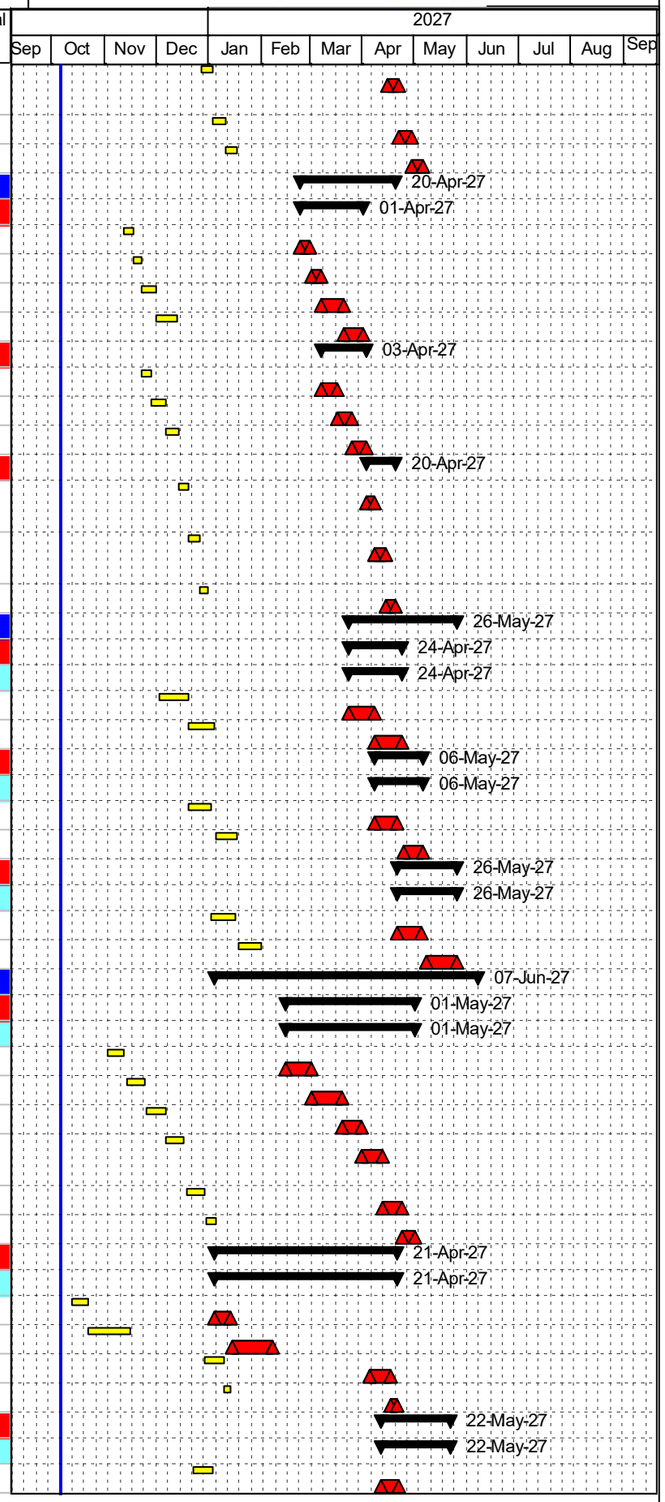

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network	10	24-Apr-27	04-May-27	04-Jan-27	14-Jan-27	0%	19,380.00	19,380.00
CO-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network	10	05-May-27	22-May-27	16-Jan-27	26-Jan-27	0%	6,000.00	6,000.00
Irrigation Network		12	07-Apr-27	21-Apr-27	19-Dec-26	02-Jan-27	0%	19,320.00	19,320.00
Testing and Finishes		12	07-Apr-27	21-Apr-27	19-Dec-26	02-Jan-27	0%	19,320.00	19,320.00
CO-IR-TF-160	Final Testing (pressure tests) of Irrigation Network	12	07-Apr-27	21-Apr-27	19-Dec-26	02-Jan-27	0%	19,320.00	19,320.00
Treated Sewage Effluent (Tse)		12	21-Apr-27	04-May-27	02-Jan-27	14-Jan-27	0%	30,693.60	30,693.60
Testing and Finishes		12	21-Apr-27	04-May-27	02-Jan-27	14-Jan-27	0%	30,693.60	30,693.60
CO-TSE-TF-170	Final Testing (pressure tests) of Treated Sewage Effluent (Tse)	12	21-Apr-27	04-May-27	02-Jan-27	14-Jan-27	0%	30,693.60	30,693.60
Medium Voltage Network		18	08-Apr-27	29-Apr-27	20-Dec-26	10-Jan-27	0%	66,481.77	66,481.77
Termination and Testing Works		18	08-Apr-27	29-Apr-27	20-Dec-26	10-Jan-27	0%	66,481.77	66,481.77
CO-MV-TF-220	Termination Works of Medium Voltage Network	18	08-Apr-27	29-Apr-27	20-Dec-26	10-Jan-27	0%	66,481.77	66,481.77
Street Lighting Network		14	29-Apr-27	22-May-27	10-Jan-27	03-Feb-27	0%	143,686.20	143,686.20
Termination and Testing Works		14	29-Apr-27	22-May-27	10-Jan-27	03-Feb-27	0%	130,636.20	130,636.20
CO-SL-LP-330	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network	7	29-Apr-27	08-May-27	10-Jan-27	18-Jan-27	0%	65,934.00	65,934.00
CO-SL-TF-220	Termination Works For Lighting Poles Cables of Street Lighting Network	7	08-May-27	22-May-27	18-Jan-27	26-Jan-27	0%	29,955.00	29,955.00
CO-SL-TF-230	Termination Works For Panel Board Cables of Street Lighting Network	7	08-May-27	22-May-27	18-Jan-27	26-Jan-27	0%	2,396.10	2,396.10
CO-SL-TF-200	Testing Works for Lighting Poles of Street Lighting Network	5	08-May-27	13-May-27	30-Jan-27	03-Feb-27	0%	29,955.00	29,955.00
CO-SL-TF-380	Testing Works For Panel Board Cables of Street Lighting Network	2	08-May-27	10-May-27	18-Jan-27	20-Jan-27	0%	2,396.10	2,396.10
Earthing System Works		7	29-Apr-27	08-May-27	10-Jan-27	18-Jan-27	0%	13,050.00	13,050.00
CO-SL-ES-220	Install Earthing System Works for Lighting Poles of Street Lighting Network	7	29-Apr-27	08-May-27	10-Jan-27	18-Jan-27	0%	9,135.00	9,135.00
CO-SL-ES-230	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network	7	29-Apr-27	08-May-27	10-Jan-27	18-Jan-27	0%	3,915.00	3,915.00
Telecom Network		16	20-Apr-27	09-May-27	31-Dec-26	19-Jan-27	0%	82,794.00	82,794.00
Testing and Finishes		16	20-Apr-27	09-May-27	31-Dec-26	19-Jan-27	0%	82,794.00	82,794.00
CO-TE-CTV-TF-110	Smart Card Printer	4	20-Apr-27	25-Apr-27	31-Dec-26	05-Jan-27	0%	9,324.00	9,324.00
CO-TE-CTV-TF-120	Card Issue Work Station	4	25-Apr-27	29-Apr-27	05-Jan-27	10-Jan-27	0%	14,918.00	14,918.00
CO-TE-CTV-TF-130	Photographic Camera with stand	4	29-Apr-27	04-May-27	10-Jan-27	14-Jan-27	0%	11,189.00	11,189.00
CO-TE-CTV-TF-140	Interface modules with CCTV, Fire and other systems	4	04-May-27	09-May-27	14-Jan-27	19-Jan-27	0%	47,363.00	47,363.00
Road Works		47	08-Apr-27	07-Jun-27	20-Dec-26	14-Feb-27	0%	6,829,532.25	6,829,532.25
ST+1000:ST+1531		42	08-Apr-27	01-Jun-27	20-Dec-26	06-Feb-27	0%	2,390,336.29	2,390,336.29
Bituminous Construction		14	25-Apr-27	10-May-27	05-Jan-27	20-Jan-27	0%	212,667.00	212,667.00
CO-RD-B-150	Application of Prime Coat Layer for Road Works	7	25-Apr-27	02-May-27	05-Jan-27	12-Jan-27	0%	105,814.80	105,814.80
CO-RD-B-160	Bituminous Base Courses Layers for Road Works-	7	03-May-27	10-May-27	13-Jan-27	20-Jan-27	0%	106,852.20	106,852.20
Pavement Works		23	08-Apr-27	05-May-27	20-Dec-26	16-Jan-27	0%	2,104,946.29	2,104,946.29
CO-RD-PV-160	Fixing of Curbstone for Sidewalks Pavement	12	08-Apr-27	22-Apr-27	20-Dec-26	03-Jan-27	0%	258,753.60	258,753.60
CO-RD-PV-170	Fixing of Interlock Tiles for Sidewalks Pavement	11	22-Apr-27	05-May-27	03-Jan-27	16-Jan-27	0%	1,846,192.69	1,846,192.69
Traffic Signs Boards and Roads Marking		14	11-May-27	01-Jun-27	21-Jan-27	06-Feb-27	0%	72,723.00	72,723.00
CO-RD-F-RM-180	Application of Road Marking Works For Road Works	7	11-May-27	24-May-27	21-Jan-27	28-Jan-27	0%	35,427.00	35,427.00
CO-RD-F-TS-120	Installation Works of Traffic Signs Boards For Road Works	7	25-May-27	01-Jun-27	30-Jan-27	06-Feb-27	0%	37,296.00	37,296.00
ST+500:ST+1000		34	22-Apr-27	06-Jun-27	03-Jan-27	11-Feb-27	0%	2,390,336.29	2,390,336.29
Bituminous Construction		8	11-May-27	25-May-27	21-Jan-27	30-Jan-27	0%	212,667.00	212,667.00
CO-RD-B-130	Application of Prime Coat Layer for Road Works	4	11-May-27	20-May-27	21-Jan-27	25-Jan-27	0%	105,814.80	105,814.80
CO-RD-B-140	Bituminous Base Courses Layers for Road Works-	4	22-May-27	25-May-27	26-Jan-27	30-Jan-27	0%	106,852.20	106,852.20
Pavement Works		22	22-Apr-27	24-May-27	03-Jan-27	28-Jan-27	0%	2,104,946.29	2,104,946.29
CO-RD-PV-140	Fixing of Curbstone for Sidewalks Pavement	11	22-Apr-27	05-May-27	03-Jan-27	16-Jan-27	0%	258,753.60	258,753.60
CO-RD-PV-150	Fixing of Interlock Tiles for Sidewalks Pavement	11	05-May-27	24-May-27	16-Jan-27	28-Jan-27	0%	1,846,192.69	1,846,192.69
Traffic Signs Boards and Roads Marking		9	27-May-27	06-Jun-27	01-Feb-27	11-Feb-27	0%	72,723.00	72,723.00
CO-RD-F-RM-170	Application of Road Marking Works For Road Works	5	27-May-27	01-Jun-27	01-Feb-27	06-Feb-27	0%	35,427.00	35,427.00
CO-RD-F-TS-110	Installation Works of Traffic Signs Boards For Road Works	4	02-Jun-27	06-Jun-27	07-Feb-27	11-Feb-27	0%	37,296.00	37,296.00
ST+01:ST+500		24	05-May-27	07-Jun-27	16-Jan-27	14-Feb-27	0%	2,048,859.67	2,048,859.67

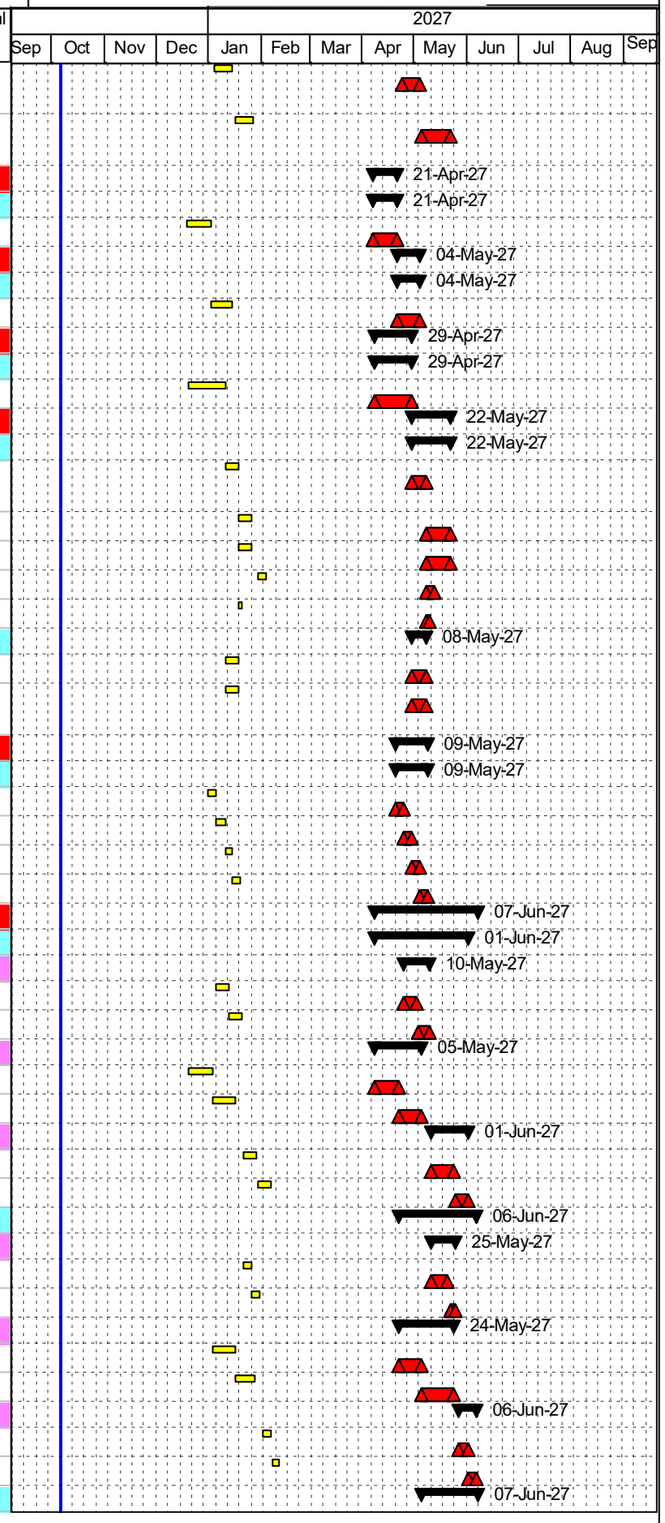

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Bituminous Construction		9	27-May-27	06-Jun-27	01-Feb-27	11-Feb-27	0%	182,286.00	182,286.00
CO-RD-B-110	Application of Prime Coat Layer for Road Works	5	27-May-27	01-Jun-27	01-Feb-27	06-Feb-27	0%	90,698.40	90,698.40
CO-RD-B-120	Bituminous Base Courses Layers for Road Works-	4	02-Jun-27	06-Jun-27	07-Feb-27	11-Feb-27	0%	91,587.60	91,587.60
Pavement Works		22	05-May-27	06-Jun-27	16-Jan-27	11-Feb-27	0%	1,804,239.67	1,804,239.67
CO-RD-PV-120	Fixing of Curbstone for Sidewalks Pavement	11	05-May-27	24-May-27	16-Jan-27	28-Jan-27	0%	221,788.80	221,788.80
CO-RD-PV-130	Fixing of Interlock Tiles for Sidewalks Pavement	11	24-May-27	06-Jun-27	28-Jan-27	11-Feb-27	0%	1,582,450.87	1,582,450.87
Traffic Signs Boards and Roads Marking		1	07-Jun-27	07-Jun-27	13-Feb-27	14-Feb-27	0%	62,334.00	62,334.00
CO-RD-F-RM-160	Application of Road Marking Works For Road Works	1	07-Jun-27	07-Jun-27	13-Feb-27	14-Feb-27	0%	30,366.00	30,366.00
CO-RD-F-TS-100	Installation Works of Traffic Signs Boards For Road Works	1	07-Jun-27	07-Jun-27	13-Feb-27	14-Feb-27	0%	31,968.00	31,968.00
Superstructure Work		236	02-Aug-26 A	20-May-27	02-Aug-26	23-Feb-27	19.04%	38,008,077.20	38,008,077.20
Utility Buildings		138	23-Sep-26 A	20-May-27	24-Aug-26	27-Jan-27	1.6%	13,013,990.60	13,013,990.60
Pump Station		136	26-Sep-26 A	20-May-27	21-Nov-26	27-Jan-27	2%	3,248,719.51	3,248,719.51
Civil work		7	26-Sep-26 A	05-Dec-26	21-Nov-26	01-Dec-26	30%	216,207.42	216,207.42
Super structure		7	26-Sep-26 A	05-Dec-26	21-Nov-26	01-Dec-26	30%	216,207.42	216,207.42
CO-UB-PS-230	Steel fixing for pump roof	6	26-Sep-26 A	01-Dec-26	21-Nov-26	28-Nov-26	90%	72,069.14	72,069.14
CO-UB-PS-240	pouring for pump roof	1	02-Dec-26	02-Dec-26	28-Nov-26	29-Nov-26	0%	72,069.14	72,069.14
CO-UB-PS-250	curing and deshuttering formwork for pump roof	2	03-Dec-26	05-Dec-26	29-Nov-26	01-Dec-26	0%	72,069.14	72,069.14
Architectural work		35	06-Dec-26	14-Jan-27	01-Dec-26	11-Jan-27	0%	870,437.72	870,437.72
CO-UB-PS-260	Executing Masonry Works for Pump station building	5	06-Dec-26	10-Dec-26	01-Dec-26	07-Dec-26	0%	183,776.32	183,776.32
CO-UB-PS-270	Executing Plastering Works for Pump station building	5	12-Dec-26	16-Dec-26	07-Dec-26	13-Dec-26	0%	229,720.40	229,720.40
CO-UB-PS-280	Executing Painting Works for Pump station building	5	17-Dec-26	22-Dec-26	13-Dec-26	19-Dec-26	0%	227,220.60	227,220.60
CO-UB-PS-320	Doors and windows Fixing &Stair Tiles	7	07-Jan-27	14-Jan-27	03-Jan-27	11-Jan-27	0%	229,720.40	229,720.40
Electrical work		109	23-Dec-26	09-May-27	19-Dec-26	21-Jan-27	0%	540,518.60	540,518.60
CO-UB-PS-290	Lighting system for pump house	5	23-Dec-26	28-Dec-26	19-Dec-26	24-Dec-26	0%	135,129.65	135,129.65
CO-UB-PS-300	Wiring connection for pump house	5	29-Dec-26	03-Jan-27	24-Dec-26	30-Dec-26	0%	54,051.87	54,051.87
CO-UB-PS-310	Sockets and switches for pump house	3	04-Jan-27	06-Jan-27	30-Dec-26	03-Jan-27	0%	81,077.78	81,077.78
CO-UB-PS-330	Installation for Distribution boards for pump house	8	07-Jan-27	16-Jan-27	03-Jan-27	12-Jan-27	0%	135,129.65	135,129.65
CO-UB-PS-370	Executing Earthing and bonding for the entire system	8	29-Apr-27	09-May-27	12-Jan-27	21-Jan-27	0%	135,129.65	135,129.65
Mechanical work		101	07-Jan-27	20-May-27	03-Jan-27	27-Jan-27	0%	1,621,555.78	1,621,555.78
CO-UB-PS-340	Executing HVAC System for Pump station building	14	07-Jan-27	23-Jan-27	03-Jan-27	19-Jan-27	0%	162,155.58	162,155.58
CO-UB-PS-350	Executing Fire Alarm System for Pump station building	5	07-Jan-27	12-Jan-27	03-Jan-27	09-Jan-27	0%	324,311.15	324,311.15
CO-UB-PS-360	Executing Fire fighting institution works(piping and wire installation) for Pump station building	5	13-Jan-27	18-Jan-27	09-Jan-27	14-Jan-27	0%	405,388.95	405,388.95
CO-UB-PS-380	Executing Fire fighting finishing works for Pump station building	5	19-Jan-27	24-Jan-27	14-Jan-27	20-Jan-27	0%	162,155.58	162,155.58
CO-UB-PS-390	Installation of pumps	5	09-May-27	20-May-27	21-Jan-27	27-Jan-27	0%	567,544.52	567,544.52
Lift Station		68	23-Sep-26 A	16-Feb-27	13-Oct-26	20-Jan-27	5.65%	2,530,828.20	2,530,828.20
Civil work		27	23-Sep-26 A	21-Dec-26	13-Oct-26	26-Nov-26	25.76%	554,932.43	554,932.43
Super structure		27	23-Sep-26 A	21-Dec-26	13-Oct-26	26-Nov-26	25.76%	554,932.43	554,932.43
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	25-Nov-26	13-Oct-26	21-Oct-26	70%	84,080.67	84,080.67
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	26-Nov-26	21-Oct-26	01-Nov-26	70%	84,080.67	84,080.67
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	26-Nov-26	01-Nov-26	02-Nov-26	50%	50,448.40	50,448.40
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	2	28-Nov-26	29-Nov-26	02-Nov-26	04-Nov-26	0%	8,408.07	8,408.07
CO-UB-LS-330	Waterproofing for Walls columns	4	30-Nov-26	03-Dec-26	04-Nov-26	09-Nov-26	0%	84,080.67	84,080.67
CO-UB-LS-340	Formwork for pump roof	5	05-Dec-26	09-Dec-26	09-Nov-26	15-Nov-26	0%	84,080.67	84,080.67
CO-UB-LS-350	Steel fixing for pump roof	6	10-Dec-26	16-Dec-26	15-Nov-26	22-Nov-26	0%	84,080.67	84,080.67
CO-UB-LS-360	pouring for pump roof	1	17-Dec-26	17-Dec-26	22-Nov-26	23-Nov-26	0%	67,264.53	67,264.53
CO-UB-LS-370	curing and deshuttering formwork for pump roof	3	19-Dec-26	21-Dec-26	23-Nov-26	26-Nov-26	0%	8,408.07	8,408.07
Architectural work		15	22-Dec-26	07-Jan-27	26-Nov-26	14-Dec-26	0%	714,685.71	714,685.71
CO-UB-LS-380	Executing Masonry Works for Pump station building	7	22-Dec-26	29-Dec-26	26-Nov-26	05-Dec-26	0%	357,342.85	357,342.85
CO-UB-LS-390	Executing Plastering Works for Pump station building	8	30-Dec-26	07-Jan-27	05-Dec-26	14-Dec-26	0%	357,342.85	357,342.85
Electrical work		32	09-Jan-27	16-Feb-27	14-Dec-26	20-Jan-27	0%	420,403.36	420,403.36
CO-UB-LS-400	Lighting system for pump house	8	09-Jan-27	17-Jan-27	14-Dec-26	23-Dec-26	0%	147,141.18	147,141.18

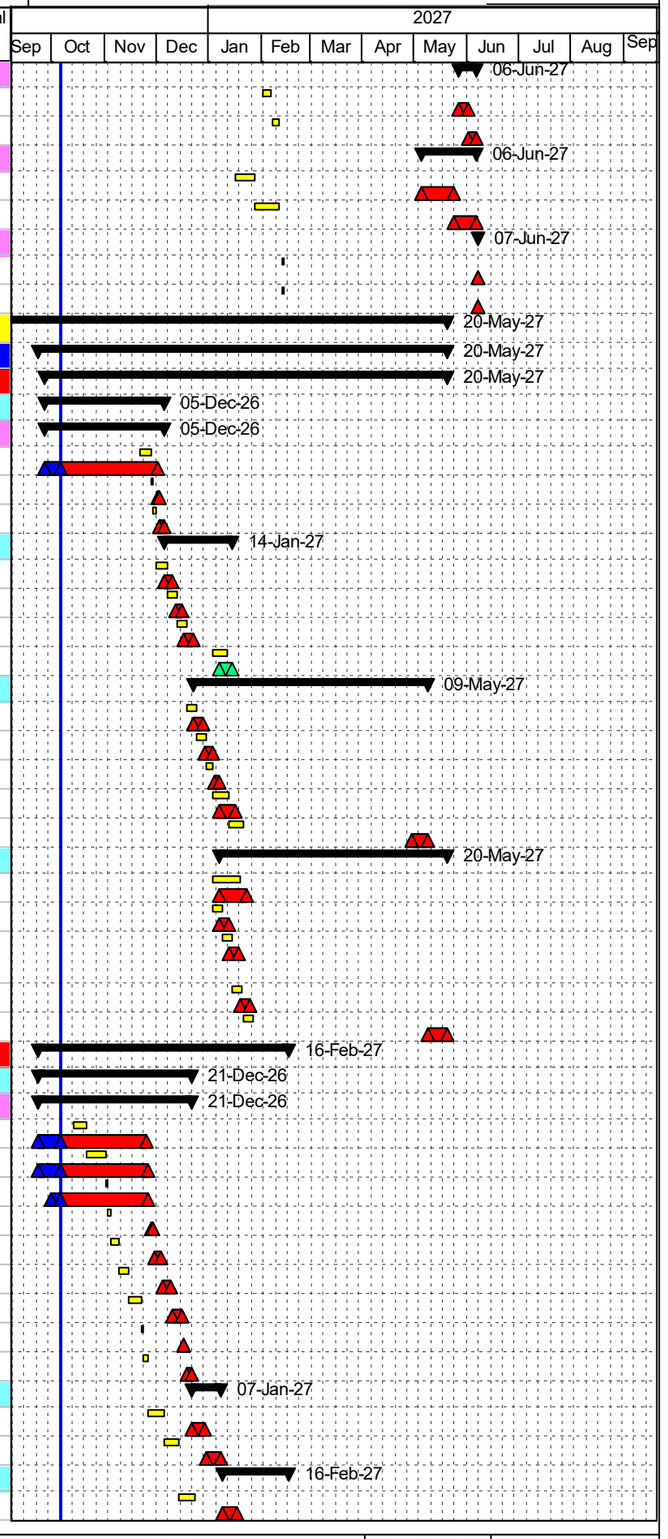

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-UB-LS-420	Wiring connection for pump house	6	18-Jan-27	24-Jan-27	23-Dec-26	30-Dec-26	0%	84,080.67	84,080.67
CO-UB-LS-440	Sockets and switches for pump house	6	25-Jan-27	31-Jan-27	30-Dec-26	06-Jan-27	0%	42,040.34	42,040.34
CO-UB-LS-460	Installation for Distribution boards for pump house	6	01-Feb-27	07-Feb-27	06-Jan-27	13-Jan-27	0%	105,100.84	105,100.84
CO-UB-LS-480	Executing Earthing and bonding for the entire system	6	08-Feb-27	16-Feb-27	13-Jan-27	20-Jan-27	0%	42,040.34	42,040.34
Mechanical work		30	09-Jan-27	14-Feb-27	14-Dec-26	18-Jan-27	0%	840,806.70	840,806.70
CO-UB-LS-410	Internal pipe installation	8	09-Jan-27	17-Jan-27	14-Dec-26	23-Dec-26	0%	210,201.68	210,201.68
CO-UB-LS-430	Guide rails & lifting chains installation	7	18-Jan-27	25-Jan-27	23-Dec-26	31-Dec-26	0%	168,161.34	168,161.34
CO-UB-LS-450	ExeValve installation	7	26-Jan-27	02-Feb-27	31-Dec-26	09-Jan-27	0%	210,201.68	210,201.68
CO-UB-LS-470	Installation of pumps	8	03-Feb-27	14-Feb-27	09-Jan-27	18-Jan-27	0%	252,242.01	252,242.01
Potable Water Tank		66	07-Dec-26	25-Feb-27	24-Aug-26	09-Nov-26	0%	615,094.02	615,094.02
Eearth Work		12	07-Dec-26	20-Dec-26	24-Aug-26	06-Sep-26	0%	7,353.58	7,353.58
CO-UB-PWT-100	Excavation work for tank foundation tank formation level	7	07-Dec-26	14-Dec-26	24-Aug-26	31-Aug-26	0%	0.00	0.00
CO-UB-PWT-110	Soil replacement Up to tank formation level	5	15-Dec-26	20-Dec-26	01-Sep-26	06-Sep-26	0%	7,353.58	7,353.58
Structural Work		15	21-Dec-26	06-Jan-27	07-Sep-26	24-Sep-26	0%	118,428.55	118,428.55
CO-UB-PWT-120	Plain Concrete works	3	21-Dec-26	23-Dec-26	07-Sep-26	09-Sep-26	0%	24,787.37	24,787.37
CO-UB-PWT-130	Form work for Tank Foundation	5	24-Dec-26	29-Dec-26	10-Sep-26	15-Sep-26	0%	41,312.28	41,312.28
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation	6	30-Dec-26	05-Jan-27	16-Sep-26	22-Sep-26	0%	38,558.13	38,558.13
CO-UB-PWT-150	Casting concrete for Tank Foundation	1	06-Jan-27	06-Jan-27	24-Sep-26	24-Sep-26	0%	13,770.76	13,770.76
Tank Shell Erection&Roof Installation		22	07-Jan-27	01-Feb-27	26-Sep-26	20-Oct-26	0%	330,498.27	330,498.27
CO-UB-PWT-160	Bottom ring installation	6	07-Jan-27	13-Jan-27	26-Sep-26	01-Oct-26	0%	82,624.57	82,624.57
CO-UB-PWT-170	shell erection	8	14-Jan-27	23-Jan-27	03-Oct-26	11-Oct-26	0%	110,166.09	110,166.09
CO-UB-PWT-180	Aluminum dome / steel roof installation	8	24-Jan-27	01-Feb-27	12-Oct-26	20-Oct-26	0%	137,707.61	137,707.61
Mechanical Work&Accessories		17	02-Feb-27	25-Feb-27	21-Oct-26	09-Nov-26	0%	158,813.62	158,813.62
CO-UB-PWT-190	Inlet / outlet piping connections	6	02-Feb-27	09-Feb-27	21-Oct-26	27-Oct-26	0%	81,697.34	81,697.34
CO-UB-PWT-200	installation Valves	6	09-Feb-27	18-Feb-27	28-Oct-26	03-Nov-26	0%	55,083.05	55,083.05
CO-UB-PWT-210	Ladders, platforms & handrails	5	18-Feb-27	25-Feb-27	04-Nov-26	09-Nov-26	0%	22,033.23	22,033.23
IrrigationTank		54	25-Feb-27	05-May-27	10-Nov-26	11-Jan-27	0%	615,094.02	615,094.02
Eearth Work		11	25-Feb-27	16-Mar-27	10-Nov-26	22-Nov-26	0%	7,353.58	7,353.58
CO-UB-IRT-140	Excavation work for tank foundation tank formation level	6	25-Feb-27	07-Mar-27	10-Nov-26	16-Nov-26	0%	0.00	0.00
CO-UB-IRT-150	Soil replacement Up to tank formation level	5	07-Mar-27	16-Mar-27	17-Nov-26	22-Nov-26	0%	7,353.58	7,353.58
Structural Work		15	17-Mar-27	03-Apr-27	23-Nov-26	09-Dec-26	0%	118,428.55	118,428.55
CO-UB-IRT-160	Plain Concrete works	3	17-Mar-27	20-Mar-27	23-Nov-26	25-Nov-26	0%	24,787.37	24,787.37
CO-UB-IRT-170	Form work for Tank Foundation	6	21-Mar-27	27-Mar-27	26-Nov-26	02-Dec-26	0%	41,312.28	41,312.28
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation	5	28-Mar-27	01-Apr-27	03-Dec-26	08-Dec-26	0%	38,558.13	38,558.13
CO-UB-IRT-190	Casting concrete for Tank Foundation	1	03-Apr-27	03-Apr-27	09-Dec-26	09-Dec-26	0%	13,770.76	13,770.76
Tank Shell Erection&Roof Installation		18	04-Apr-27	24-Apr-27	10-Dec-26	30-Dec-26	0%	330,498.27	330,498.27
CO-UB-IRT-200	Bottom ring installation	6	04-Apr-27	10-Apr-27	10-Dec-26	16-Dec-26	0%	82,624.57	82,624.57
CO-UB-IRT-210	shell erection	6	11-Apr-27	17-Apr-27	17-Dec-26	23-Dec-26	0%	110,166.09	110,166.09
CO-UB-IRT-220	Aluminum dome / steel roof installation	6	18-Apr-27	24-Apr-27	24-Dec-26	30-Dec-26	0%	137,707.61	137,707.61
Mechanical Work&Accessories		10	25-Apr-27	05-May-27	31-Dec-26	11-Jan-27	0%	158,813.62	158,813.62
CO-UB-IRT-230	Inlet / outlet piping connections	4	25-Apr-27	28-Apr-27	31-Dec-26	04-Jan-27	0%	81,697.34	81,697.34
CO-UB-IRT-240	installation Valves	4	29-Apr-27	03-May-27	05-Jan-27	09-Jan-27	0%	55,083.05	55,083.05
CO-UB-IRT-250	Ladders, platforms & handrails	2	04-May-27	05-May-27	10-Jan-27	11-Jan-27	0%	22,033.23	22,033.23
Control Room		82	25-Nov-26	07-Mar-27	17-Oct-26	20-Jan-27	0%	2,078,714.40	2,078,714.40
Civil Work		16	25-Nov-26	13-Dec-26	17-Oct-26	04-Nov-26	0%	397,100.98	397,100.98
CO-UB-CR-130	Pouring R.C Columns For Control Room	8	25-Nov-26	03-Dec-26	17-Oct-26	26-Oct-26	0%	144,858.97	144,858.97
CO-UB-CR-140	Pouring Beams and Slab For Control Room	8	05-Dec-26	13-Dec-26	26-Oct-26	04-Nov-26	0%	252,242.01	252,242.01
Finishing Work		66	14-Dec-26	07-Mar-27	04-Nov-26	20-Jan-27	0%	1,681,613.42	1,681,613.42
Architictural work		40	14-Dec-26	28-Jan-27	04-Nov-26	21-Dec-26	0%	480,461.00	480,461.00
CO-UB-CR-150	Brick Work For Control Room	9	14-Dec-26	23-Dec-26	04-Nov-26	15-Nov-26	0%	96,092.20	96,092.20
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	7	24-Dec-26	31-Dec-26	15-Nov-26	23-Nov-26	0%	96,092.20	96,092.20
CO-UB-CR-200	Install For Curtian Wall and Windows and Doors	8	02-Jan-27	10-Jan-27	23-Nov-26	02-Dec-26	0%	96,092.20	96,092.20

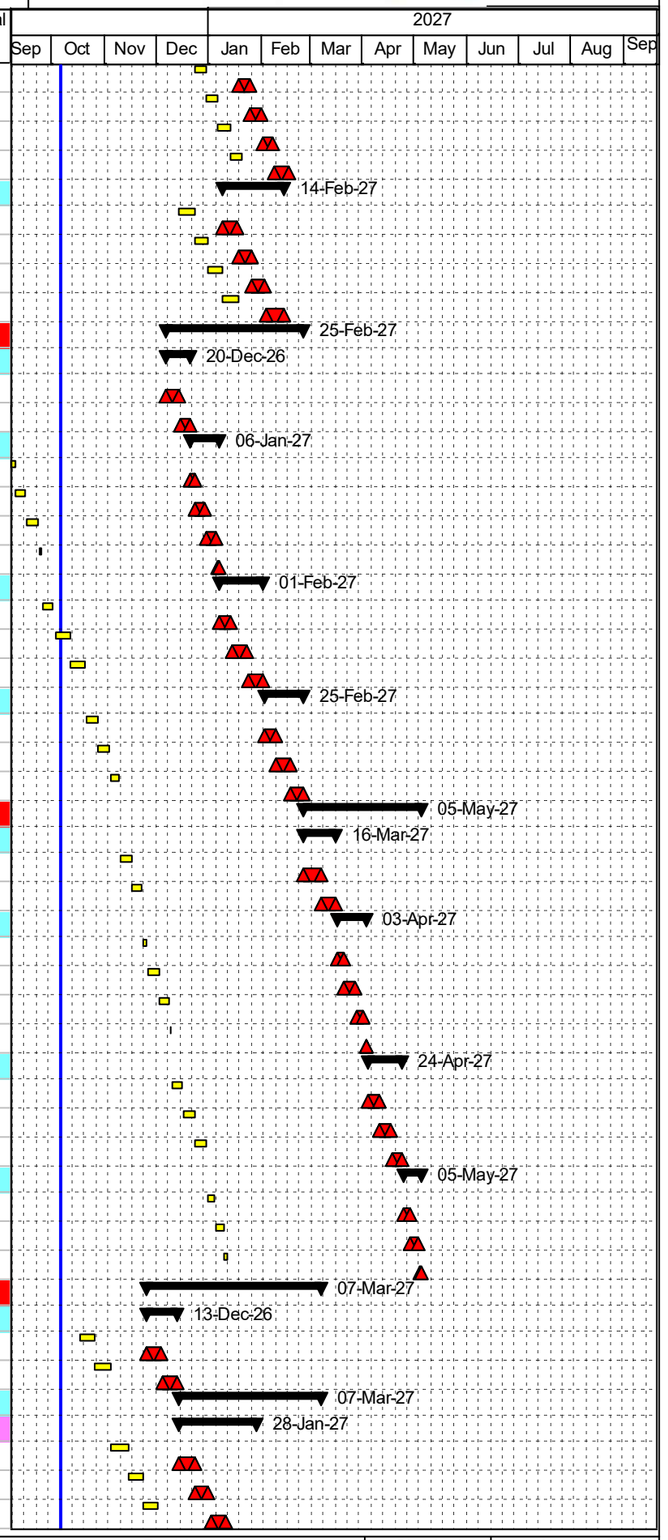

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-UB-CR-240	External Finshing Work (Walls and Floor)	8	11-Jan-27	19-Jan-27	02-Dec-26	12-Dec-26	0%	96,092.20	96,092.20
CO-UB-CR-250	Internal Finshing Work (Walls,Floor and Ceiling)	8	20-Jan-27	28-Jan-27	12-Dec-26	21-Dec-26	0%	96,092.20	96,092.20
Mechanical Work		41	24-Dec-26	10-Feb-27	15-Nov-26	02-Jan-27	0%	480,461.00	480,461.00
HVAC System		41	24-Dec-26	10-Feb-27	15-Nov-26	02-Jan-27	0%	288,276.60	288,276.60
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports, vanes, dampers)	4	24-Dec-26	28-Dec-26	15-Nov-26	19-Nov-26	0%	96,092.20	96,092.20
CO-UB-CR-260	Install of Mini split actual capacity 2 Ton and Ducted split actual capacity 4 Ton	7	30-Jan-27	06-Feb-27	21-Dec-26	29-Dec-26	0%	96,092.20	96,092.20
CO-UB-CR-310	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	3	07-Feb-27	10-Feb-27	29-Dec-26	02-Jan-27	0%	96,092.20	96,092.20
Fire Fitting System		30	29-Dec-26	01-Feb-27	19-Nov-26	24-Dec-26	0%	192,184.40	192,184.40
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between rooms with help of Rock wool	4	29-Dec-26	02-Jan-27	19-Nov-26	24-Nov-26	0%	96,092.20	96,092.20
CO-UB-CR-270	Install Fire Extinguishers	3	30-Jan-27	01-Feb-27	21-Dec-26	24-Dec-26	0%	96,092.20	96,092.20
Electrical Work		44	03-Jan-27	27-Feb-27	24-Nov-26	14-Jan-27	0%	480,460.93	480,460.93
LV Power		15	30-Jan-27	18-Feb-27	21-Dec-26	07-Jan-27	0%	131,034.80	131,034.80
CO-UB-CR-190	Install of Distribution board For Control Room	5	30-Jan-27	03-Feb-27	21-Dec-26	27-Dec-26	0%	43,678.27	43,678.27
CO-UB-CR-220	Install of Earting Cable for Control Room	5	04-Feb-27	10-Feb-27	27-Dec-26	02-Jan-27	0%	43,678.27	43,678.27
CO-UB-CR-280	Install of Socket outlet and LED Lighting	5	10-Feb-27	18-Feb-27	02-Jan-27	07-Jan-27	0%	43,678.27	43,678.27
Fire Detection And Alarm System		44	03-Jan-27	27-Feb-27	24-Nov-26	14-Jan-27	0%	349,426.13	349,426.13
CO-UB-CR-210	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	5	03-Jan-27	07-Jan-27	24-Nov-26	30-Nov-26	0%	43,678.27	43,678.27
CO-UB-CR-230	Install of Transmission Communication cable - Fiber Optics 12Core	5	09-Jan-27	13-Jan-27	30-Nov-26	06-Dec-26	0%	43,678.27	43,678.27
CO-UB-CR-290	Install of power supply system for fire alarm control panel	5	30-Jan-27	03-Feb-27	21-Dec-26	27-Dec-26	0%	43,678.27	43,678.27
CO-UB-CR-300	Install of Fire Alarm Control panel	6	04-Feb-27	11-Feb-27	27-Dec-26	03-Jan-27	0%	43,678.27	43,678.27
CO-UB-CR-320	Installation of the addressable manual call point with operation safety glass breaking	3	13-Feb-27	16-Feb-27	03-Jan-27	06-Jan-27	0%	43,678.27	43,678.27
CO-UB-CR-330	Install of the photoelectric heat & smoke detector	3	17-Feb-27	21-Feb-27	06-Jan-27	10-Jan-27	0%	43,678.27	43,678.27
CO-UB-CR-340	Install of Sounder With Beacon	3	17-Feb-27	21-Feb-27	06-Jan-27	10-Jan-27	0%	43,678.27	43,678.27
CO-UB-CR-350	Install of Addressable Control module	4	22-Feb-27	27-Feb-27	10-Jan-27	14-Jan-27	0%	43,678.27	43,678.27
Furnitures work		5	28-Feb-27	07-Mar-27	14-Jan-27	20-Jan-27	0%	240,230.48	240,230.48
CO-UB-CR-360	Office Chairs,Tables and Stand	5	28-Feb-27	07-Mar-27	14-Jan-27	20-Jan-27	0%	240,230.48	240,230.48
Softscape and Planting Works		39	01-Feb-27	28-Mar-27	07-Nov-26	22-Dec-26	0%	3,925,540.44	3,925,540.44
Planting Beds Preparation		21	01-Feb-27	02-Mar-27	07-Nov-26	01-Dec-26	0%	1,011,244.10	1,011,244.10
CO-LS-PL-100	Excavation of planting beds	7	01-Feb-27	09-Feb-27	07-Nov-26	15-Nov-26	0%	144,463.44	144,463.44
CO-LS-PL-110	Supply & placement of suitable topsoil	7	09-Feb-27	20-Feb-27	15-Nov-26	23-Nov-26	0%	433,390.33	433,390.33
CO-LS-PL-120	Soil improvement (fertilizer, compost, additives)	7	20-Feb-27	02-Mar-27	23-Nov-26	01-Dec-26	0%	433,390.33	433,390.33
Supports & Protection		6	02-Mar-27	14-Mar-27	01-Dec-26	08-Dec-26	0%	1,011,244.09	1,011,244.09
CO-LS-PL-130	installation of plant supports / stakes	3	02-Mar-27	07-Mar-27	01-Dec-26	05-Dec-26	0%	433,390.33	433,390.33
CO-LS-PL-140	Ties and protection materials	3	07-Mar-27	14-Mar-27	05-Dec-26	08-Dec-26	0%	577,853.76	577,853.76
Plant Supply		3	15-Mar-27	17-Mar-27	08-Dec-26	12-Dec-26	0%	866,780.63	866,780.63
CO-LS-PL-150	installation of trees	3	15-Mar-27	17-Mar-27	08-Dec-26	12-Dec-26	0%	866,780.63	866,780.63
Site Furnishings		9	18-Mar-27	28-Mar-27	12-Dec-26	22-Dec-26	0%	1,036,271.63	1,036,271.63
CO-LS-PL-160	installation of Seating benches	3	18-Mar-27	21-Mar-27	12-Dec-26	15-Dec-26	0%	345,423.85	345,423.85
CO-LS-PL-170	tone boulders ï¿½ placement & fixing Works	3	22-Mar-27	24-Mar-27	15-Dec-26	19-Dec-26	0%	345,423.89	345,423.89
CO-LS-PL-180	Gravel Works	3	25-Mar-27	28-Mar-27	19-Dec-26	22-Dec-26	0%	345,423.89	345,423.89
Fence and Gaurd Room		236	02-Aug-26 A	20-May-27	02-Aug-26	23-Feb-27	28.12%	24,994,086.60	24,994,086.60
Gaurd Room Work		124	12-Dec-26	20-May-27	29-Aug-26	20-Jan-27	0%	2,138,080.85	2,138,080.85
Civil Work		41	12-Dec-26	27-Jan-27	29-Aug-26	15-Oct-26	0%	198,090.00	198,090.00
A1000	Excavation Work For Gaurd Room Foundation	7	12-Dec-26	19-Dec-26	29-Aug-26	05-Sep-26	0%	0.00	0.00
A1010	Pouring for Plain Concrete	4	20-Dec-26	23-Dec-26	06-Sep-26	09-Sep-26	0%	42,000.00	42,000.00
A1020	Pouring R.C Footing For Gaurd Room	11	24-Dec-26	05-Jan-27	10-Sep-26	22-Sep-26	0%	60,600.00	60,600.00
A1030	Pouring R.C Columns For Gaurd Room	10	06-Jan-27	17-Jan-27	24-Sep-26	05-Oct-26	0%	12,600.00	12,600.00
A1040	Pouring Beams and Slab For Gaurd Room	9	18-Jan-27	27-Jan-27	06-Oct-26	15-Oct-26	0%	82,890.00	82,890.00
Finishing Work		83	28-Jan-27	20-May-27	17-Oct-26	20-Jan-27	0%	1,939,990.85	1,939,990.85

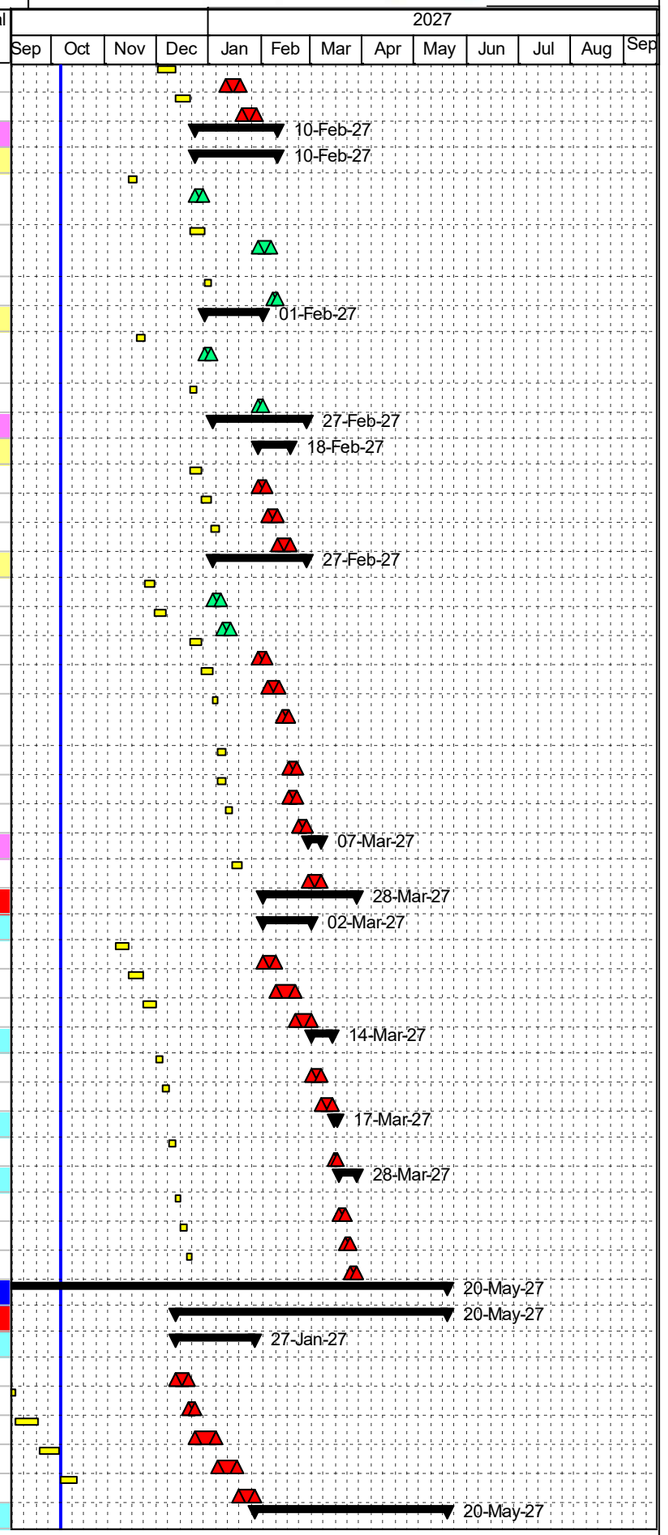


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Architictural work		46	28-Jan-27	01-Apr-27	17-Oct-26	08-Dec-26	0%	287,137.00	287,137.00
A1050	Brick Work For Gaurd Room	9	28-Jan-27	07-Feb-27	17-Oct-26	26-Oct-26	0%	32,904.00	32,904.00
A1060	Thermal & Moisture Protection Work for Gaurd Room	7	08-Feb-27	18-Feb-27	27-Oct-26	03-Nov-26	0%	40,920.00	40,920.00
A1070	Install For Curtian Wall and Windows and Doors	8	28-Feb-27	14-Mar-27	11-Nov-26	19-Nov-26	0%	170,473.00	170,473.00
A1080	External Finshing Work (Walls and Floor)	8	15-Mar-27	23-Mar-27	21-Nov-26	29-Nov-26	0%	11,172.00	11,172.00
A1090	Internal Finshing Work (Walls,Floor and Ceiling)	8	24-Mar-27	01-Apr-27	30-Nov-26	08-Dec-26	0%	31,668.00	31,668.00
Mechanical Work		47	08-Feb-27	13-Apr-27	27-Oct-26	20-Dec-26	0%	190,986.00	190,986.00
Sanitary Drainage & Plumbing System		13	08-Feb-27	27-Feb-27	27-Oct-26	10-Nov-26	0%	33,408.00	33,408.00
A1110	Install Sanitary Piping System (UPVC)	4	08-Feb-27	14-Feb-27	27-Oct-26	31-Oct-26	0%	22,224.00	22,224.00
A1120	Install Base mounted flush tank water Western water closet system	6	14-Feb-27	22-Feb-27	01-Nov-26	07-Nov-26	0%	7,680.00	7,680.00
A1130	Install 1 meter length 10mm diameter Flexible Hose and Gate Valves and Slow Closing Valve	3	23-Feb-27	27-Feb-27	08-Nov-26	10-Nov-26	0%	3,504.00	3,504.00
Water Supply System		39	08-Feb-27	04-Apr-27	27-Oct-26	10-Dec-26	0%	69,498.00	69,498.00
A1240	Install GRP water tanks capacity of each 1000 liter	3	08-Feb-27	11-Feb-27	27-Oct-26	29-Oct-26	0%	25,200.00	25,200.00
A1140	Install for Cold Water Pipe complete with joints, angles, reducer etc.	5	13-Feb-27	20-Feb-27	31-Oct-26	04-Nov-26	0%	4,044.00	4,044.00
A1150	Install for Hot Water Pipe complete with joints, angles, reducer etc.	4	20-Feb-27	25-Feb-27	05-Nov-26	09-Nov-26	0%	714.00	714.00
A1160	Install for Isolation Valve,Spray Head,Roof Drain,Floor Drain,Gully teap,Vend on Roof to exhaust air	3	25-Feb-27	02-Mar-27	10-Nov-26	12-Nov-26	0%	16,140.00	16,140.00
A1170	Install of Inspection chamber, size 800x900x1000	2	02-Mar-27	06-Mar-27	14-Nov-26	15-Nov-26	0%	10,800.00	10,800.00
A1180	Install OF Electric Water Heater set with connection and Water meter complete with accessories	2	03-Apr-27	04-Apr-27	09-Dec-26	10-Dec-26	0%	12,600.00	12,600.00
HVAC System		43	14-Feb-27	13-Apr-27	01-Nov-26	20-Dec-26	0%	29,280.00	29,280.00
A1200	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports, vanes, dampers)	4	14-Feb-27	20-Feb-27	01-Nov-26	04-Nov-26	0%	7,560.00	7,560.00
A1190	Install of Mini split actual capacity 2 Ton and Ducted split actual capacity 4 Ton	7	03-Apr-27	10-Apr-27	09-Dec-26	16-Dec-26	0%	18,600.00	18,600.00
A1210	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	3	11-Apr-27	13-Apr-27	17-Dec-26	20-Dec-26	0%	3,120.00	3,120.00
Fire Fitting System		35	20-Feb-27	08-Apr-27	05-Nov-26	15-Dec-26	0%	58,800.00	58,800.00
A1220	Installation & Testing of 2 hours Fire rated system for closing the openings between rooms with help of Rock wool	6	20-Feb-27	01-Mar-27	05-Nov-26	11-Nov-26	0%	30,000.00	30,000.00
A1230	Install Fire Extinguishers	6	03-Apr-27	08-Apr-27	09-Dec-26	15-Dec-26	0%	28,800.00	28,800.00
Electrical Work		61	20-Feb-27	09-May-27	05-Nov-26	14-Jan-27	0%	1,440,267.85	1,440,267.85
LV Power		34	20-Feb-27	07-Apr-27	05-Nov-26	14-Dec-26	0%	67,800.00	67,800.00
A1250	Install of Distribution board For Gaurd Room	5	20-Feb-27	27-Feb-27	05-Nov-26	10-Nov-26	0%	11,904.00	11,904.00
A1270	Install of Earting Cable for Gaurd Room	5	28-Feb-27	07-Mar-27	11-Nov-26	16-Nov-26	0%	7,920.00	7,920.00
A1260	Install of Socket outlet and LED Lighting	5	03-Apr-27	07-Apr-27	09-Dec-26	14-Dec-26	0%	47,976.00	47,976.00
Fire Detection And Alarm System		44	01-Mar-27	26-Apr-27	12-Nov-26	02-Jan-27	0%	232,960.00	232,960.00
A1340	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	5	01-Mar-27	08-Mar-27	12-Nov-26	17-Nov-26	0%	27,000.00	27,000.00
A1350	Install of Transmission Communication cable - Fiber Optics 12Core	5	13-Mar-27	17-Mar-27	18-Nov-26	23-Nov-26	0%	129,735.00	129,735.00
A1360	Install of power supply system for fire alarm control panel	5	03-Apr-27	07-Apr-27	09-Dec-26	14-Dec-26	0%	4,617.00	4,617.00
A1280	Install of Fire Alarm Control panel	6	08-Apr-27	14-Apr-27	15-Dec-26	21-Dec-26	0%	40,620.00	40,620.00
A1290	Installation of the addressable manual call point with operation safety glass breaking	3	15-Apr-27	18-Apr-27	22-Dec-26	24-Dec-26	0%	4,182.00	4,182.00
A1300	Install of the photoelectric heat & smoke detector	3	19-Apr-27	21-Apr-27	26-Dec-26	28-Dec-26	0%	14,760.00	14,760.00
A1310	Install of Sounder With Beacon	3	19-Apr-27	21-Apr-27	26-Dec-26	28-Dec-26	0%	4,920.00	4,920.00
A1320	Install of Addressable Control module	4	22-Apr-27	26-Apr-27	29-Dec-26	02-Jan-27	0%	7,126.00	7,126.00
Security System		30	05-Apr-27	09-May-27	12-Dec-26	14-Jan-27	0%	1,139,507.85	1,139,507.85
A1580	Install 8 Port Industrial PoE Switch 10/100BaseT (0 deg to +70 deg. Celsius)	5	05-Apr-27	10-Apr-27	12-Dec-26	16-Dec-26	0%	337,590.00	337,590.00
A1590	Optical Fiber,48 Core Splice Closure	3	11-Apr-27	13-Apr-27	17-Dec-26	20-Dec-26	0%	277,542.00	277,542.00
A1650	Pole/Bollard mounted IP(PoE) and 12U rack dimension	4	11-Apr-27	14-Apr-27	17-Dec-26	21-Dec-26	0%	114,735.00	114,735.00
A1600	Boom Barrier at Security Guard Room	5	15-Apr-27	20-Apr-27	22-Dec-26	27-Dec-26	0%	239,100.00	239,100.00
A1610	Pedestrian turnstile at Security Guard Room	5	21-Apr-27	26-Apr-27	28-Dec-26	02-Jan-27	0%	149,917.85	149,917.85
A1620	Access Control Unit and Access Card Reader	4	27-Apr-27	01-May-27	03-Jan-27	06-Jan-27	0%	14,268.00	14,268.00

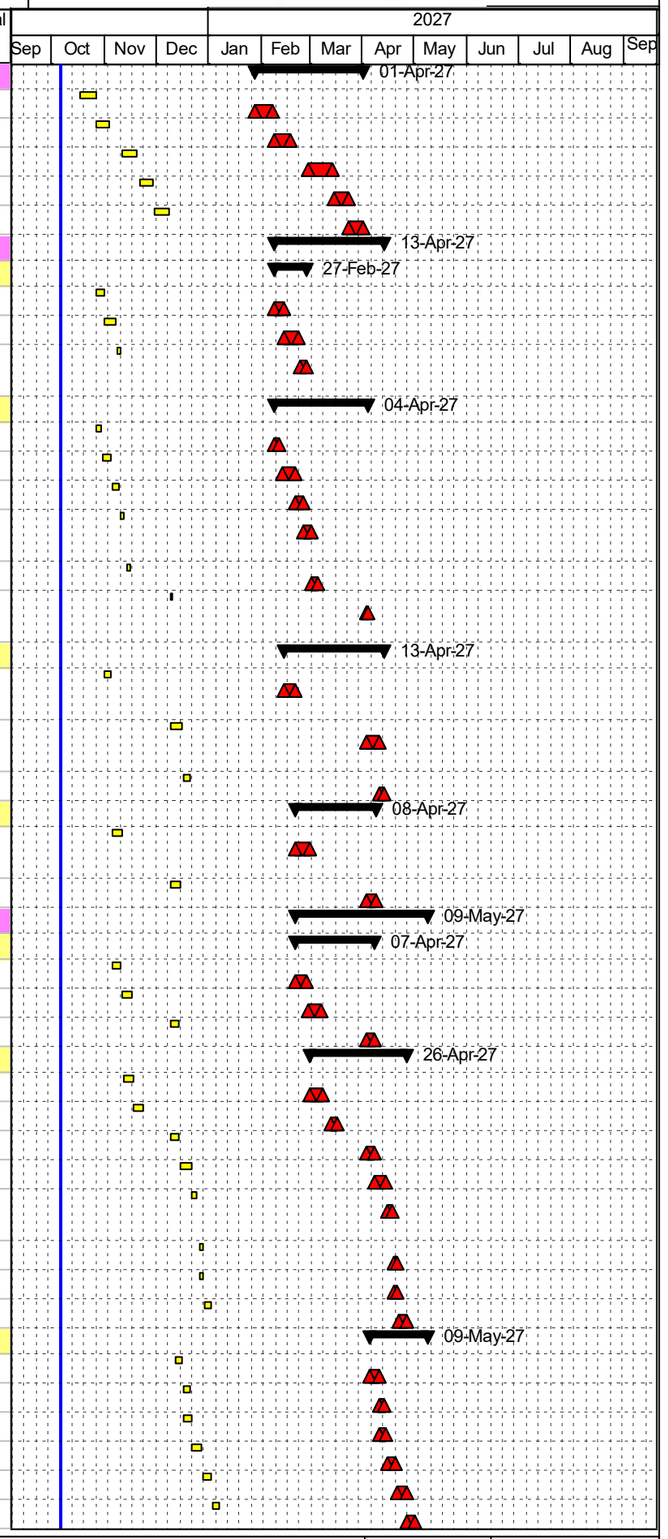

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
A1630	Magnetic Lock and Break Glass and Exit Push button	4	02-May-27	05-May-27	07-Jan-27	11-Jan-27	0%	4,485.00	4,485.00
A1640	Door Sensor and Biometrics Reader	3	06-May-27	09-May-27	12-Jan-27	14-Jan-27	0%	1,870.00	1,870.00
Furnitures work		5	10-May-27	20-May-27	16-Jan-27	20-Jan-27	0%	21,600.00	21,600.00
A1100	Office Chairs,Tables and Stand	5	10-May-27	20-May-27	16-Jan-27	20-Jan-27	0%	21,600.00	21,600.00
Fence Work		226	02-Aug-26 A	03-May-27	02-Aug-26	23-Feb-27	30.75%	22,856,005.75	22,856,005.75
Northern Fence N01:N03		148	02-Aug-26 A	21-Jan-27	02-Aug-26	17-Jan-27	28.21%	4,811,563.47	4,811,563.47
Civil Work		70	02-Aug-26 A	22-Oct-26	02-Aug-26	01-Sep-26	59.02%	2,237,792.73	2,237,792.73
CO-SU-FE-N-CI-11	Pouring for Plain Concrete Northern Fence	4	02-Aug-26 A	10-Oct-26	02-Aug-26	05-Aug-26	95%	53,454.55	53,454.55
CO-SU-FE-N-CI-12	Pouring R.C Footing For Northern Fence	6	02-Aug-26 A	12-Oct-26	05-Aug-26	12-Aug-26	85%	1,494,000.00	1,494,000.00
CO-SU-FE-N-CI-13	Pouring R.C Columns For Northern Fence	5	13-Oct-26	18-Oct-26	12-Aug-26	18-Aug-26	0%	649,407.27	649,407.27
CO-SU-FE-N-CI-14	Pouring Beams For Northern Fence	4	19-Oct-26	22-Oct-26	29-Aug-26	01-Sep-26	0%	40,930.91	40,930.91
Finishing Work		88	29-Sep-26 A	21-Jan-27	18-Aug-26	17-Jan-27	1.42%	2,573,770.75	2,573,770.75
Electrical Work		82	19-Oct-26	21-Jan-27	29-Aug-26	08-Dec-26	0%	165,946.09	165,946.09
CO-SU-FE-N-EL-1	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	19-Oct-26	27-Oct-26	29-Aug-26	06-Sep-26	0%	17,843.64	17,843.64
CO-SU-FE-N-EL-1	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	19-Oct-26	27-Oct-26	29-Aug-26	06-Sep-26	0%	8,181.82	8,181.82
CO-SU-FE-N-EL-1	Fixing of Control cable,CAT6A cable	9	28-Oct-26	07-Nov-26	07-Sep-26	16-Sep-26	0%	4,240.91	4,240.91
CO-SU-FE-N-EL-1	Install 800mm x 800mm x 800mm height concrete handhole	9	28-Oct-26	07-Nov-26	07-Sep-26	16-Sep-26	0%	4,435.64	4,435.64
CO-SU-FE-N-EL-14	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	8	28-Oct-26	05-Nov-26	07-Sep-26	15-Sep-26	0%	5,767.36	5,767.36
CO-SU-FE-N-EL-1	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	8	08-Nov-26	16-Nov-26	17-Sep-26	27-Sep-26	0%	2,608.82	2,608.82
CO-SU-FE-N-EL-16	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	8	17-Nov-26	25-Nov-26	28-Sep-26	06-Oct-26	0%	15,946.18	15,946.18
CO-SU-FE-N-EL-1	Fence Lightining 400V, 3PH, 60Hz lighting control panelï¿½ (LCP-02)	8	17-Nov-26	25-Nov-26	28-Sep-26	06-Oct-26	0%	0.00	0.00
CO-SU-FE-N-EL-1	Install of direct buried armored cable 4C-16mm2 ,10mm2	9	26-Nov-26	06-Dec-26	07-Oct-26	17-Oct-26	0%	11,145.45	11,145.45
CO-SU-FE-N-EL-1	Install 16mm2,10mm2 CU/PVC wire	9	26-Nov-26	06-Dec-26	07-Oct-26	17-Oct-26	0%	1,995.45	1,995.45
CO-SU-FE-N-EL-20	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	8	26-Nov-26	05-Dec-26	07-Oct-26	15-Oct-26	0%	25,963.64	25,963.64
CO-SU-FE-N-EL-2	Junction Box for lighting fixture	8	07-Dec-26	15-Dec-26	18-Oct-26	26-Oct-26	0%	1,520.73	1,520.73
CO-SU-FE-N-EL-2	IR Intrusion Detection System Quad Beams	8	04-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	0%	57,469.09	57,469.09
CO-SU-FE-N-EL-2	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	9	04-Jan-27	13-Jan-27	19-Nov-26	30-Nov-26	0%	8,456.73	8,456.73
CO-SU-FE-N-EL-2	Install, fixings, testing and commissioning 80W LED	7	14-Jan-27	21-Jan-27	30-Nov-26	08-Dec-26	0%	370.64	370.64
Architictural work		81	29-Sep-26 A	13-Jan-27	18-Aug-26	17-Jan-27	1.51%	2,407,824.65	2,407,824.65
CO-SU-FE-N-AR-	Install Brick Work For Northern Fence	9	29-Sep-26 A	18-Oct-26	18-Aug-26	27-Aug-26	23%	158,509.09	158,509.09
CO-SU-FE-N-AR-	External plastering to walls and columns	7	07-Dec-26	14-Dec-26	18-Oct-26	25-Oct-26	0%	0.00	0.00
CO-SU-FE-N-AR-	Install 50mm thick random cut stone cladding	7	15-Dec-26	22-Dec-26	26-Oct-26	02-Nov-26	0%	2,046,910.47	2,046,910.47
CO-SU-FE-N-AR-	Install 2 coats of weatherproof paint at walls	6	23-Dec-26	29-Dec-26	03-Nov-26	09-Nov-26	0%	64,011.82	64,011.82
CO-SU-FE-N-AR-	Install Stone coping 500mm,525mm	4	30-Dec-26	03-Jan-27	10-Nov-26	14-Nov-26	0%	74,029.64	74,029.64
CO-SU-FE-N-AR-	Install MODON Signage	7	06-Jan-27	13-Jan-27	09-Jan-27	17-Jan-27	0%	64,363.64	64,363.64
Western Fence P1 (W01:W06)		168	02-Aug-26 A	22-Mar-27	27-Aug-26	26-Jan-27	39.59%	3,503,358.22	3,503,358.22
Civil Work		73	02-Aug-26 A	21-Nov-26	27-Aug-26	01-Nov-26	64.03%	2,052,152.73	2,052,152.73
CO-SU-FE-WP1-CI	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	11-Oct-26	27-Aug-26	02-Sep-26	95%	106,909.09	106,909.09
CO-SU-FE-WP1-CI	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	22-Oct-26	02-Sep-26	12-Sep-26	85%	1,188,000.00	1,188,000.00
CO-SU-FE-WP1-CI	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	01-Nov-26	12-Sep-26	01-Oct-26	30%	675,381.82	675,381.82
CO-SU-FE-WP1-CI	Pouring Beams For Northern Fence	17	02-Nov-26	21-Nov-26	12-Oct-26	01-Nov-26	0%	81,861.82	81,861.82
Finishing Work		112	29-Sep-26 A	22-Mar-27	01-Oct-26	26-Jan-27	5.02%	1,451,205.49	1,451,205.49
Electrical Work		112	02-Nov-26	22-Mar-27	12-Oct-26	20-Jan-27	0%	331,892.18	331,892.18
CO-SU-FE-WP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	14	02-Nov-26	17-Nov-26	12-Oct-26	28-Oct-26	0%	35,687.27	35,687.27
CO-SU-FE-WP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	14	02-Nov-26	17-Nov-26	12-Oct-26	28-Oct-26	0%	16,363.64	16,363.64
CO-SU-FE-WP1-E	Fixing of Control cable,CAT6A cable	14	18-Nov-26	03-Dec-26	28-Oct-26	14-Nov-26	0%	8,481.82	8,481.82
CO-SU-FE-WP1-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	14	18-Nov-26	03-Dec-26	28-Oct-26	14-Nov-26	0%	11,534.73	11,534.73
CO-SU-FE-WP1-E	Install 800mm x 800mm x 800mm height concrete handhole	14	16-Dec-26	31-Dec-26	28-Oct-26	14-Nov-26	0%	8,871.27	8,871.27

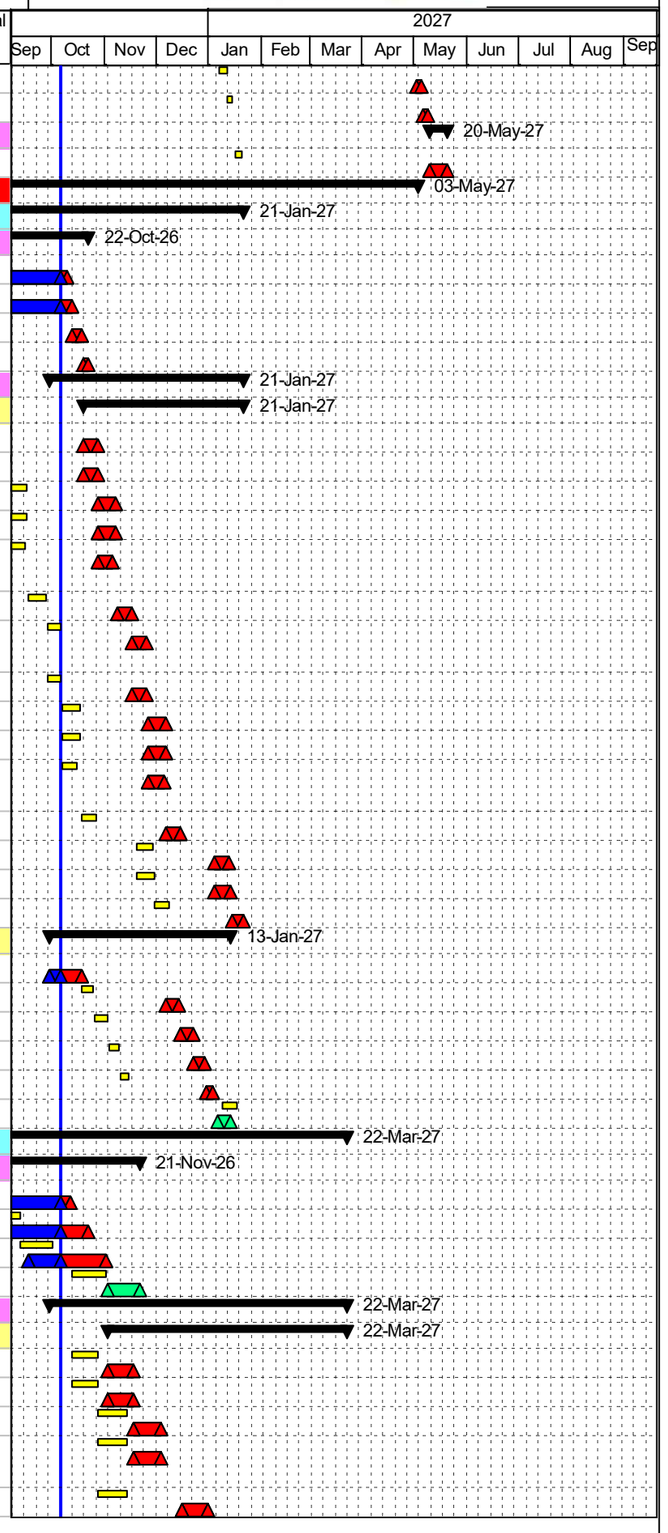


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SU-FE-WP1-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	11	04-Jan-27	16-Jan-27	15-Nov-26	26-Nov-26	0%	5,217.64	5,217.64
CO-SU-FE-WP1-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	9	17-Jan-27	26-Jan-27	28-Nov-26	07-Dec-26	0%	31,892.36	31,892.36
CO-SU-FE-WP1-E	Fence Lightining 400V, 3PH, 60Hz lighting control panelï¿½ (LCP-02)	9	17-Jan-27	26-Jan-27	28-Nov-26	07-Dec-26	0%	0.00	0.00
CO-SU-FE-WP1-E	Install of direct buried armored cable 4C-16mm2 ,10mm2	8	27-Jan-27	04-Feb-27	08-Dec-26	16-Dec-26	0%	22,290.91	22,290.91
CO-SU-FE-WP1-E	Install 16mm2,10mm2 CU/PVC wire	8	27-Jan-27	04-Feb-27	08-Dec-26	16-Dec-26	0%	3,990.91	3,990.91
CO-SU-FE-WP1-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	9	27-Jan-27	06-Feb-27	08-Dec-26	17-Dec-26	0%	51,927.27	51,927.27
CO-SU-FE-WP1-E	Junction Box for lighting fixture	11	06-Feb-27	21-Feb-27	17-Dec-26	29-Dec-26	0%	3,041.45	3,041.45
CO-SU-FE-WP1-E	IR Intrusion Detection System Quad Beams	4	14-Mar-27	17-Mar-27	12-Jan-27	16-Jan-27	0%	114,938.18	114,938.18
CO-SU-FE-WP1-E	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	4	14-Mar-27	17-Mar-27	12-Jan-27	16-Jan-27	0%	16,913.45	16,913.45
CO-SU-FE-WP1-E	Install, fixings, testing and commissioning 80W LED	4	18-Mar-27	22-Mar-27	17-Jan-27	20-Jan-27	0%	741.27	741.27
Architictural work		102	29-Sep-26 A	22-Mar-27	01-Oct-26	26-Jan-27	6.51%	1,119,313.31	1,119,313.31
CO-SU-FE-WP1-A	Install Brick Work For Northern Fence	9	29-Sep-26 A	01-Nov-26	01-Oct-26	12-Oct-26	23%	317,018.18	317,018.18
CO-SU-FE-WP1-A	External plastering to walls and columns	6	07-Feb-27	15-Feb-27	19-Dec-26	24-Dec-26	0%	0.00	0.00
CO-SU-FE-WP1-A	Install 50mm thick random cut stone cladding	5	15-Feb-27	22-Feb-27	26-Dec-26	30-Dec-26	0%	397,484.95	397,484.95
CO-SU-FE-WP1-A	Install 2 coats of weatherproof paint at walls	6	23-Feb-27	03-Mar-27	31-Dec-26	06-Jan-27	0%	128,023.64	128,023.64
CO-SU-FE-WP1-A	Install Stone coping 500mm,525mm	4	04-Mar-27	13-Mar-27	07-Jan-27	11-Jan-27	0%	148,059.27	148,059.27
CO-SU-FE-WP1-A	Install MODON Signage	8	14-Mar-27	22-Mar-27	17-Jan-27	26-Jan-27	0%	128,727.27	128,727.27
Western Fence P2 (W07:W12)		156	02-Aug-26 A	03-Apr-27	22-Sep-26	04-Feb-27	30.76%	4,403,151.23	4,403,151.23
Civil Work		58	02-Aug-26 A	29-Nov-26	22-Sep-26	09-Nov-26	65.92%	1,943,945.73	1,943,945.73
CO-SU-FE-WP2-CI	Pouring for Plain Concrete Northern Fence	5	02-Aug-26 A	19-Oct-26	22-Sep-26	29-Sep-26	95%	106,909.09	106,909.09
CO-SU-FE-WP2-CI	Pouring R.C Footing For Northern Fence	7	02-Aug-26 A	21-Oct-26	29-Sep-26	07-Oct-26	85%	1,188,000.00	1,188,000.00
CO-SU-FE-WP2-CI	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	24-Oct-26	07-Oct-26	18-Oct-26	30%	567,174.83	567,174.83
CO-SU-FE-WP2-CI	Pouring Beams For Northern Fence	7	22-Nov-26	29-Nov-26	01-Nov-26	09-Nov-26	0%	81,861.82	81,861.82
Finishing Work		129	29-Sep-26 A	03-Apr-27	18-Oct-26	04-Feb-27	2.96%	2,459,205.49	2,459,205.49
Electrical Work		129	25-Oct-26	03-Apr-27	27-Oct-26	01-Feb-27	0%	331,892.18	331,892.18
CO-SU-FE-WP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	25-Oct-26	28-Oct-26	27-Oct-26	01-Nov-26	0%	35,687.27	35,687.27
CO-SU-FE-WP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	25-Oct-26	31-Oct-26	27-Oct-26	03-Nov-26	0%	16,363.64	16,363.64
CO-SU-FE-WP2-E	Fixing of Control cable,CAT6A cable	7	01-Nov-26	08-Nov-26	03-Nov-26	11-Nov-26	0%	8,481.82	8,481.82
CO-SU-FE-WP2-E	Install 800mm x 800mm x 800mm height concrete handhole	7	01-Nov-26	08-Nov-26	03-Nov-26	10-Nov-26	0%	8,871.27	8,871.27
CO-SU-FE-WP2-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	6	01-Nov-26	07-Nov-26	03-Nov-26	10-Nov-26	0%	11,534.73	11,534.73
CO-SU-FE-WP2-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	09-Nov-26	15-Nov-26	11-Nov-26	18-Nov-26	0%	5,217.64	5,217.64
CO-SU-FE-WP2-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	16-Nov-26	19-Nov-26	18-Nov-26	23-Nov-26	0%	31,892.36	31,892.36
CO-SU-FE-WP2-E	Install of direct buried armored cable 4C-16mm2 ,10mm2	8	21-Nov-26	29-Nov-26	23-Nov-26	01-Dec-26	0%	22,290.91	22,290.91
CO-SU-FE-WP2-E	Install 16mm2,10mm2 CU/PVC wire	8	21-Nov-26	29-Nov-26	23-Nov-26	01-Dec-26	0%	3,990.91	3,990.91
CO-SU-FE-WP2-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	8	21-Nov-26	29-Nov-26	23-Nov-26	02-Dec-26	0%	51,927.27	51,927.27
CO-SU-FE-WP2-E	Junction Box for lighting fixture	3	29-Nov-26	02-Dec-26	01-Dec-26	05-Dec-26	0%	3,041.45	3,041.45
CO-SU-FE-WP2-E	IR Intrusion Detection System Quad Beams	7	18-Mar-27	25-Mar-27	17-Jan-27	24-Jan-27	0%	114,938.18	114,938.18
CO-SU-FE-WP2-E	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	7	18-Mar-27	25-Mar-27	17-Jan-27	24-Jan-27	0%	16,913.45	16,913.45
CO-SU-FE-WP2-E	Install, fixings, testing and commissioning 80W LED	7	27-Mar-27	03-Apr-27	25-Jan-27	01-Feb-27	0%	741.27	741.27
Architictural work		118	29-Sep-26 A	31-Mar-27	18-Oct-26	04-Feb-27	3.43%	2,127,313.31	2,127,313.31
CO-SU-FE-WP2-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	24-Oct-26	18-Oct-26	27-Oct-26	23%	317,018.18	317,018.18
CO-SU-FE-WP2-A	External plastering to walls and columns	8	30-Nov-26	08-Dec-26	02-Dec-26	12-Dec-26	0%	0.00	0.00
CO-SU-FE-WP2-A	Install 50mm thick random cut stone cladding	8	09-Dec-26	17-Dec-26	12-Dec-26	21-Dec-26	0%	1,405,484.95	1,405,484.95
CO-SU-FE-WP2-A	Install 2 coats of weatherproof paint at walls	8	19-Dec-26	27-Dec-26	21-Dec-26	30-Dec-26	0%	128,023.64	128,023.64
CO-SU-FE-WP2-A	Install Stone coping 500mm,525mm	8	28-Dec-26	05-Jan-27	30-Dec-26	09-Jan-27	0%	148,059.27	148,059.27
CO-SU-FE-WP2-A	Install MODON Signage	8	23-Mar-27	31-Mar-27	26-Jan-27	04-Feb-27	0%	128,727.27	128,727.27
Southern Fence S01:S05		201	02-Aug-26 A	11-Apr-27	09-Aug-26	15-Feb-27	27.15%	3,635,456.45	3,635,456.45

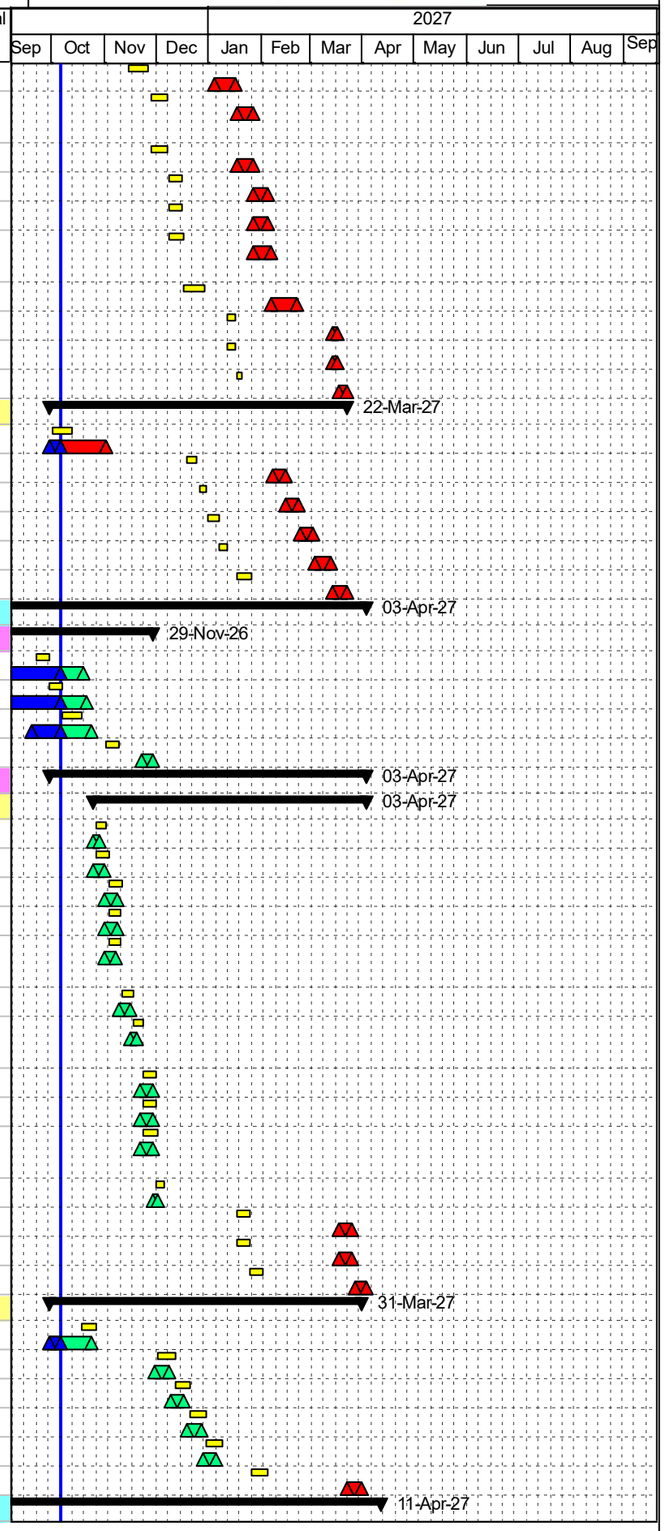

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Civil Work		76	02-Aug-26 A	05-Nov-26	09-Aug-26	13-Sep-26	49.63%	1,866,174.55	1,866,174.55
CO-SU-FE-S-CI-26	Pouring for Plain Concrete Northern Fence	3	02-Aug-26 A	08-Oct-26	09-Aug-26	12-Aug-26	95%	89,090.91	89,090.91
CO-SU-FE-S-CI-27	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	14-Oct-26	12-Aug-26	22-Aug-26	85%	990,000.00	990,000.00
CO-SU-FE-S-CI-28	Pouring R.C Columns For Northern Fence	10	15-Oct-26	26-Oct-26	22-Aug-26	02-Sep-26	0%	718,865.45	718,865.45
CO-SU-FE-S-CI-29	Pouring Beams For Northern Fence	9	27-Oct-26	05-Nov-26	02-Sep-26	13-Sep-26	0%	68,218.18	68,218.18
Finishing Work		140	29-Sep-26 A	11-Apr-27	02-Sep-26	15-Feb-27	3.43%	1,769,281.91	1,769,281.91
Electrical Work		140	20-Oct-26	11-Apr-27	02-Sep-26	10-Feb-27	0%	276,576.82	276,576.82
CO-SU-FE-S-EL-5	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	20-Oct-26	05-Nov-26	02-Sep-26	20-Sep-26	0%	29,739.39	29,739.39
CO-SU-FE-S-EL-6	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	20-Oct-26	05-Nov-26	02-Sep-26	20-Sep-26	0%	13,636.36	13,636.36
CO-SU-FE-S-EL-6	Fixing of Control cable,CAT6A cable	15	07-Nov-26	23-Nov-26	20-Sep-26	08-Oct-26	0%	7,068.18	7,068.18
CO-SU-FE-S-EL-6	Install 800mm x 800mm x 800mm height concrete handhole	15	07-Nov-26	23-Nov-26	20-Sep-26	08-Oct-26	0%	7,392.73	7,392.73
CO-SU-FE-S-EL-63	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	15	07-Nov-26	23-Nov-26	20-Sep-26	08-Oct-26	0%	9,612.27	9,612.27
CO-SU-FE-S-EL-5	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	24-Nov-26	30-Nov-26	08-Oct-26	15-Oct-26	0%	4,348.03	4,348.03
CO-SU-FE-S-EL-64	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	26-Nov-26	30-Nov-26	08-Oct-26	13-Oct-26	0%	26,576.97	26,576.97
CO-SU-FE-S-EL-6	Fence Lightining 400V, 3PH, 60Hz lighting control panelï¿½ (LCP-02)	4	26-Nov-26	30-Nov-26	08-Oct-26	13-Oct-26	0%	0.00	0.00
CO-SU-FE-S-EL-6	Install of direct buried armored cable 4C-16mm2 ,10mm2	10	26-Nov-26	07-Dec-26	08-Oct-26	20-Oct-26	0%	18,575.76	18,575.76
CO-SU-FE-S-EL-6	Install 16mm2,10mm2 CU/PVC wire	6	01-Dec-26	07-Dec-26	13-Oct-26	20-Oct-26	0%	3,325.76	3,325.76
CO-SU-FE-S-EL-69	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	7	01-Dec-26	08-Dec-26	13-Oct-26	21-Oct-26	0%	43,272.73	43,272.73
CO-SU-FE-S-EL-5	Junction Box for lighting fixture	7	08-Dec-26	15-Dec-26	05-Dec-26	13-Dec-26	0%	2,534.55	2,534.55
CO-SU-FE-S-EL-5	IR Intrusion Detection System Quad Beams	7	06-Mar-27	17-Mar-27	09-Jan-27	16-Jan-27	0%	95,781.82	95,781.82
CO-SU-FE-S-EL-6	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	7	27-Mar-27	03-Apr-27	25-Jan-27	01-Feb-27	0%	14,094.55	14,094.55
CO-SU-FE-S-EL-5	Install, fixings, testing and commissioning 80W LED	7	04-Apr-27	11-Apr-27	02-Feb-27	10-Feb-27	0%	617.73	617.73
Architictural work		139	29-Sep-26 A	10-Apr-27	02-Sep-26	15-Feb-27	4.07%	1,492,705.09	1,492,705.09
CO-SU-FE-S-AR-2	Install Brick Work For Northern Fence	6	29-Sep-26 A	26-Oct-26	02-Sep-26	09-Sep-26	23%	264,181.82	264,181.82
CO-SU-FE-S-AR-2	External plastering to walls and columns	6	09-Dec-26	15-Dec-26	21-Oct-26	28-Oct-26	0%	0.00	0.00
CO-SU-FE-S-AR-3	Install 50mm thick random cut stone cladding	6	16-Dec-26	22-Dec-26	28-Oct-26	04-Nov-26	0%	891,181.45	891,181.45
CO-SU-FE-S-AR-3	Install 2 coats of weatherproof paint at walls	8	22-Feb-27	06-Mar-27	30-Dec-26	07-Jan-27	0%	106,686.36	106,686.36
CO-SU-FE-S-AR-3	Install Stone coping 500mm,525mm	10	06-Mar-27	21-Mar-27	09-Jan-27	19-Jan-27	0%	123,382.73	123,382.73
CO-SU-FE-S-AR-3	Install MODON Signage	8	01-Apr-27	10-Apr-27	04-Feb-27	15-Feb-27	0%	107,272.73	107,272.73
Eastern Fence P1 (E01:E06)		190	02-Aug-26 A	15-Apr-27	26-Aug-26	20-Feb-27	33.69%	3,514,790.95	3,514,790.95
Civil Work		68	02-Aug-26 A	14-Nov-26	26-Aug-26	25-Oct-26	58.63%	1,895,585.45	1,895,585.45
CO-SU-FE-EP1-CI-	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	14-Oct-26	26-Aug-26	05-Sep-26	95%	106,909.09	106,909.09
CO-SU-FE-EP1-CI-	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	19-Oct-26	05-Sep-26	19-Sep-26	85%	1,188,000.00	1,188,000.00
CO-SU-FE-EP1-CI-	Pouring R.C Columns For Northern Fence	15	20-Oct-26	05-Nov-26	19-Sep-26	07-Oct-26	0%	518,814.55	518,814.55
CO-SU-FE-EP1-CI-	Pouring Beams For Northern Fence	7	07-Nov-26	14-Nov-26	17-Oct-26	25-Oct-26	0%	81,861.82	81,861.82
Finishing Work		135	29-Sep-26 A	15-Apr-27	07-Oct-26	20-Feb-27	4.5%	1,619,205.49	1,619,205.49
Electrical Work		129	07-Nov-26	15-Apr-27	17-Oct-26	16-Feb-27	0%	331,892.18	331,892.18
CO-SU-FE-EP1-EI	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	17-Oct-26	21-Oct-26	0%	35,687.27	35,687.27
CO-SU-FE-EP1-EI	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	17-Oct-26	21-Oct-26	0%	16,363.64	16,363.64
CO-SU-FE-EP1-EI	Fixing of Control cable,CAT6A cable	4	11-Nov-26	15-Nov-26	21-Oct-26	26-Oct-26	0%	8,481.82	8,481.82
CO-SU-FE-EP1-EI	Install 800mm x 800mm x 800mm height concrete handhole	4	11-Nov-26	15-Nov-26	21-Oct-26	26-Oct-26	0%	8,871.27	8,871.27
CO-SU-FE-EP1-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	4	11-Nov-26	15-Nov-26	21-Oct-26	26-Oct-26	0%	11,534.73	11,534.73
CO-SU-FE-EP1-EI	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	16-Nov-26	22-Nov-26	26-Oct-26	02-Nov-26	0%	5,217.64	5,217.64
CO-SU-FE-EP1-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	23-Nov-26	26-Nov-26	02-Nov-26	07-Nov-26	0%	31,892.36	31,892.36
CO-SU-FE-EP1-EI	Fence Lightining 400V, 3PH, 60Hz lighting control panelï¿½ (LCP-02)	4	23-Nov-26	26-Nov-26	02-Nov-26	07-Nov-26	0%	0.00	0.00
CO-SU-FE-EP1-EI	Install of direct buried armored cable 4C-16mm2 ,10mm2	4	28-Nov-26	01-Dec-26	07-Nov-26	11-Nov-26	0%	22,290.91	22,290.91
CO-SU-FE-EP1-EI	Install 16mm2,10mm2 CU/PVC wire	4	28-Nov-26	01-Dec-26	07-Nov-26	11-Nov-26	0%	3,990.91	3,990.91

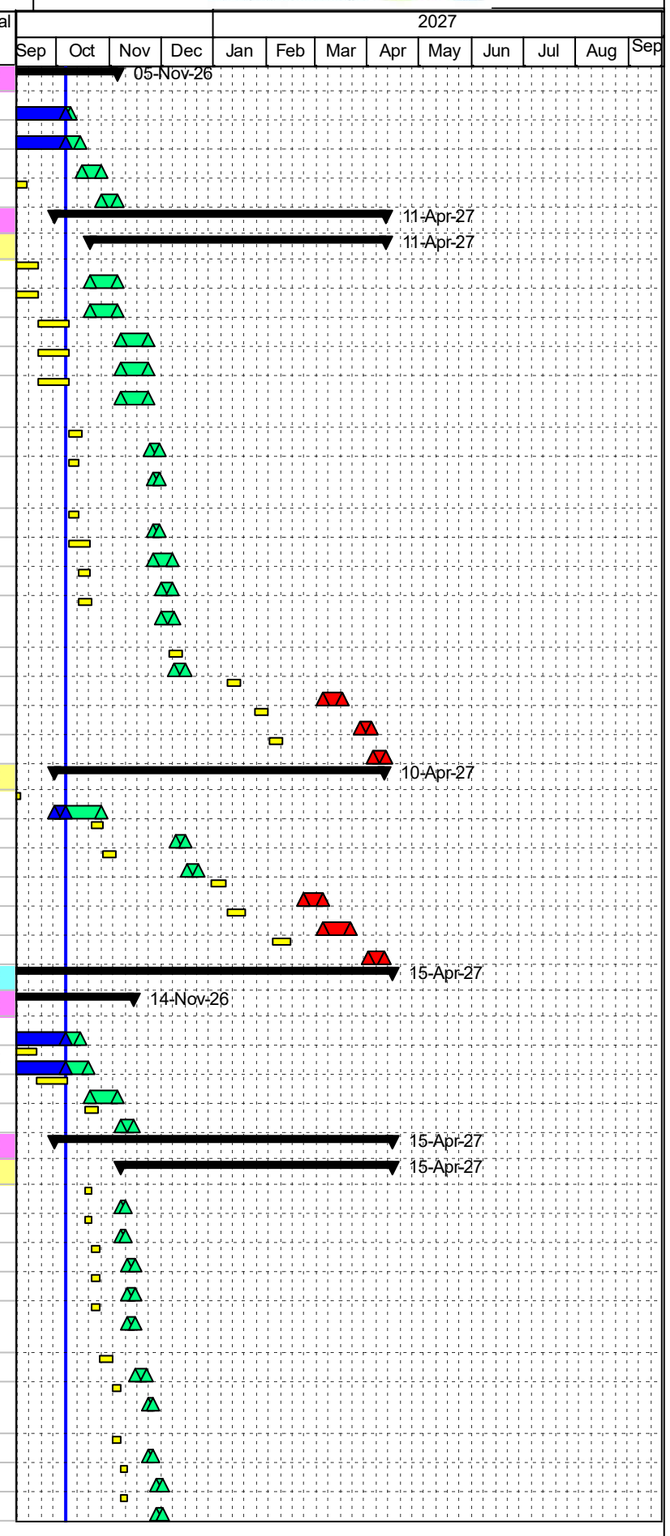

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SU-FE-EP1-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	4	28-Nov-26	01-Dec-26	07-Nov-26	11-Nov-26	0%	51,927.27	51,927.27
CO-SU-FE-EP1-EI	Junction Box for lighting fixture	3	16-Dec-26	19-Dec-26	13-Dec-26	16-Dec-26	0%	3,041.45	3,041.45
CO-SU-FE-EP1-EI	IR Intrusion Detection System Quad Beams	4	18-Mar-27	22-Mar-27	17-Jan-27	20-Jan-27	0%	114,938.18	114,938.18
CO-SU-FE-EP1-EI	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	4	18-Mar-27	22-Mar-27	17-Jan-27	20-Jan-27	0%	16,913.45	16,913.45
CO-SU-FE-EP1-EI	Install, fixings, testing and commissioning 80W LED	4	12-Apr-27	15-Apr-27	10-Feb-27	16-Feb-27	0%	741.27	741.27
Architictural work		133	29-Sep-26 A	13-Apr-27	07-Oct-26	20-Feb-27	5.66%	1,287,313.31	1,287,313.31
CO-SU-FE-EP1-AI	Install Brick Work For Northern Fence	8	29-Sep-26 A	05-Nov-26	07-Oct-26	17-Oct-26	23%	317,018.18	317,018.18
CO-SU-FE-EP1-AI	External plastering to walls and columns	8	02-Dec-26	10-Dec-26	11-Nov-26	21-Nov-26	0%	0.00	0.00
CO-SU-FE-EP1-AI	Install 50mm thick random cut stone cladding	10	12-Dec-26	22-Dec-26	21-Nov-26	02-Dec-26	0%	565,484.95	565,484.95
CO-SU-FE-EP1-AI	Install 2 coats of weatherproof paint at walls	10	23-Dec-26	03-Jan-27	02-Dec-26	14-Dec-26	0%	128,023.64	128,023.64
CO-SU-FE-EP1-AI	Install Stone coping 500mm,525mm	10	04-Jan-27	14-Jan-27	14-Dec-26	26-Dec-26	0%	148,059.27	148,059.27
CO-SU-FE-EP1-AI	Install MODON Signage	3	11-Apr-27	13-Apr-27	15-Feb-27	20-Feb-27	0%	128,727.27	128,727.27
Eastern Fence P2 (E07:E13)		172	02-Aug-26 A	03-May-27	04-Oct-26	23-Feb-27	25.42%	2,987,685.44	2,987,685.44
Civil Work		61	02-Aug-26 A	13-Dec-26	04-Oct-26	01-Dec-26	57.04%	1,182,556.36	1,182,556.36
CO-SU-FE-EP2-CI-	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	05-Nov-26	04-Oct-26	18-Oct-26	95%	124,727.27	124,727.27
CO-SU-FE-EP2-CI-	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	05-Nov-26	18-Oct-26	01-Nov-26	85%	486,000.00	486,000.00
CO-SU-FE-EP2-CI-	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	05-Nov-26	01-Nov-26	12-Nov-26	30%	476,323.64	476,323.64
CO-SU-FE-EP2-CI-	Pouring Beams For Northern Fence	10	02-Dec-26	13-Dec-26	19-Nov-26	01-Dec-26	0%	95,505.45	95,505.45
Finishing Work		122	29-Sep-26 A	03-May-27	12-Nov-26	23-Feb-27	4.71%	1,805,129.07	1,805,129.07
Electrical Work		122	02-Dec-26	03-May-27	19-Nov-26	21-Feb-27	0%	387,207.55	387,207.55
CO-SU-FE-EP2-EI	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	02-Dec-26	06-Dec-26	19-Nov-26	24-Nov-26	0%	41,635.15	41,635.15
CO-SU-FE-EP2-EI	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	02-Dec-26	06-Dec-26	19-Nov-26	24-Nov-26	0%	19,090.91	19,090.91
CO-SU-FE-EP2-EI	Install 800mm x 800mm x 800mm height concrete handhole	3	07-Dec-26	09-Dec-26	24-Nov-26	28-Nov-26	0%	10,349.82	10,349.82
CO-SU-FE-EP2-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	3	07-Dec-26	09-Dec-26	24-Nov-26	28-Nov-26	0%	13,457.18	13,457.18
CO-SU-FE-EP2-EI	Fixing of Control cable,CAT6A cable	3	20-Dec-26	22-Dec-26	16-Dec-26	20-Dec-26	0%	9,895.45	9,895.45
CO-SU-FE-EP2-EI	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	3	23-Dec-26	26-Dec-26	20-Dec-26	23-Dec-26	0%	6,087.24	6,087.24
CO-SU-FE-EP2-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	27-Dec-26	30-Dec-26	23-Dec-26	28-Dec-26	0%	37,207.76	37,207.76
CO-SU-FE-EP2-EI	Fence Lightining 400V, 3PH, 60Hz lighting control panelï¿½ (LCP-02)	4	27-Dec-26	30-Dec-26	23-Dec-26	28-Dec-26	0%	0.00	0.00
CO-SU-FE-EP2-EI	Install of direct buried armored cable 4C-16mm2 ,10mm2	3	31-Dec-26	03-Jan-27	28-Dec-26	31-Dec-26	0%	26,006.06	26,006.06
CO-SU-FE-EP2-EI	Install 16mm2,10mm2 CU/PVC wire	3	31-Dec-26	03-Jan-27	28-Dec-26	31-Dec-26	0%	4,656.06	4,656.06
CO-SU-FE-EP2-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	6	31-Dec-26	06-Jan-27	28-Dec-26	04-Jan-27	0%	60,581.82	60,581.82
CO-SU-FE-EP2-EI	Junction Box for lighting fixture	3	04-Jan-27	06-Jan-27	31-Dec-26	04-Jan-27	0%	3,548.36	3,548.36
CO-SU-FE-EP2-EI	IR Intrusion Detection System Quad Beams	3	26-Apr-27	29-Apr-27	26-Jan-27	30-Jan-27	0%	134,094.55	134,094.55
CO-SU-FE-EP2-EI	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	3	26-Apr-27	29-Apr-27	26-Jan-27	30-Jan-27	0%	19,732.36	19,732.36
CO-SU-FE-EP2-EI	Install, fixings, testing and commissioning 80W LED	3	29-Apr-27	03-May-27	17-Feb-27	21-Feb-27	0%	864.82	864.82
Architictural work		116	29-Sep-26 A	28-Apr-27	12-Nov-26	23-Feb-27	6%	1,417,921.53	1,417,921.53
CO-SU-FE-EP2-AI	Install Brick Work For Northern Fence	6	29-Sep-26 A	01-Dec-26	12-Nov-26	19-Nov-26	23%	369,854.55	369,854.55
CO-SU-FE-EP2-AI	External plastering to walls and columns	5	07-Jan-27	12-Jan-27	04-Jan-27	10-Jan-27	0%	0.00	0.00
CO-SU-FE-EP2-AI	Install 50mm thick random cut stone cladding	5	13-Jan-27	18-Jan-27	10-Jan-27	16-Jan-27	0%	575,788.44	575,788.44
CO-SU-FE-EP2-AI	Install 2 coats of weatherproof paint at walls	5	19-Jan-27	24-Jan-27	16-Jan-27	21-Jan-27	0%	149,360.91	149,360.91
CO-SU-FE-EP2-AI	Install Stone coping 500mm,525mm	4	21-Apr-27	26-Apr-27	21-Jan-27	26-Jan-27	0%	172,735.82	172,735.82
CO-SU-FE-EP2-AI	Install MODON Signage	2	26-Apr-27	28-Apr-27	20-Feb-27	23-Feb-27	0%	150,181.82	150,181.82
Testing and Comissioning		184	24-Oct-26	10-Jun-27	04-Jan-27	18-Feb-27	0%	0.00	0.00
Infrastructure Networks		31	01-May-27	10-Jun-27	06-Jan-27	18-Feb-27	0%	0.00	0.00
Irrigation Network		5	23-May-27	27-May-27	27-Jan-27	02-Feb-27	0%	0.00	0.00
T/C-IR	Testing and Commissioning of Irrigation Network	5	23-May-27	27-May-27	27-Jan-27	02-Feb-27	0%	0.00	0.00
TSE Network		15	11-May-27	03-Jun-27	17-Jan-27	02-Feb-27	0%	0.00	0.00
T/C-TSE-10	Testing and Commissioning of TSE Network	15	11-May-27	03-Jun-27	17-Jan-27	02-Feb-27	0%	0.00	0.00

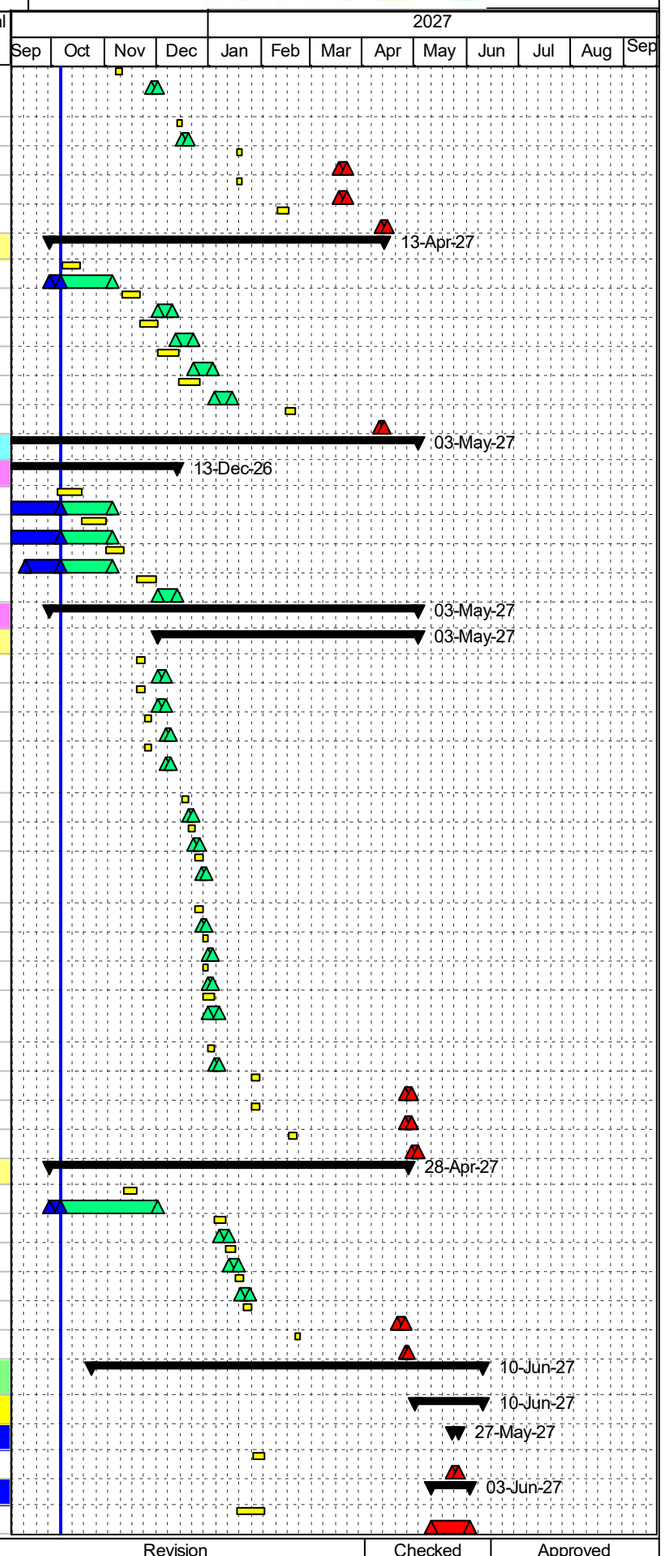


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-Projec
UPDATE 06-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Potable Water Network		6	23-May-27	29-May-27	27-Jan-27	03-Feb-27	0%	0.00	0.00
T/C-PW	Testing and Commissioning of Potable Water Network	6	23-May-27	29-May-27	27-Jan-27	03-Feb-27	0%	0.00	0.00
Sewage Network		3	11-May-27	20-May-27	17-Jan-27	19-Jan-27	0%	0.00	0.00
T/C-SW	Testing and Commissioning of Sewage Network	3	11-May-27	20-May-27	17-Jan-27	19-Jan-27	0%	0.00	0.00
Storm Drainage Network		9	01-May-27	11-May-27	06-Jan-27	16-Jan-27	0%	0.00	0.00
T/C-SD	Testing and Commissioning of Storm Drainage Network	9	01-May-27	11-May-27	06-Jan-27	16-Jan-27	0%	0.00	0.00
Street Lighting Network		6	29-May-27	03-Jun-27	04-Feb-27	11-Feb-27	0%	0.00	0.00
T/C-SL	Testing and Commissioning of Street Lighting Network	6	29-May-27	03-Jun-27	04-Feb-27	11-Feb-27	0%	0.00	0.00
Telecom Network		3	20-May-27	24-May-27	20-Jan-27	23-Jan-27	0%	0.00	0.00
T/C-TE	Testing and Commissioning of Telecom Network	3	20-May-27	24-May-27	20-Jan-27	23-Jan-27	0%	0.00	0.00
Medium Voltage Network		14	20-May-27	06-Jun-27	20-Jan-27	04-Feb-27	0%	0.00	0.00
T/C-MV	Testing and Commissioning of Medium Voltage Network	14	20-May-27	06-Jun-27	20-Jan-27	04-Feb-27	0%	0.00	0.00
Road Works		4	07-Jun-27	10-Jun-27	13-Feb-27	18-Feb-27	0%	0.00	0.00
T/C-RD	Testing and Commissioning of Road Works	4	07-Jun-27	10-Jun-27	13-Feb-27	18-Feb-27	0%	0.00	0.00
Utility Buildings		177	24-Oct-26	03-Jun-27	04-Jan-27	03-Feb-27	0%	0.00	0.00
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	24-Oct-26	24-Oct-26	04-Jan-27	04-Jan-27	0%	0.00	0.00
T/C-CTV	Testing and Commissioning of Guard Room and Fence	0	22-May-27	22-May-27	21-Jan-27	21-Jan-27	0%	0.00	0.00
T/C-SPS	Testing and Commissioning of Sewage Pump Stations& soft scape and planting work	0	03-Jun-27	03-Jun-27	03-Feb-27	03-Feb-27	0%	0.00	0.00
Handing over and close out		191	24-Oct-26	20-Jun-27	04-Jan-27	22-Feb-27	0%	0.00	0.00
As-Built		191	24-Oct-26	20-Jun-27	04-Jan-27	22-Feb-27	0%	0.00	0.00
HO-130	Submission As-Built Drawing For Pond	14	24-Oct-26	08-Nov-26	04-Jan-27	19-Jan-27	0%	0.00	0.00
HO-100	Submission As-Built Drawing For Sewage Network	14	20-May-27	06-Jun-27	20-Jan-27	04-Feb-27	0%	0.00	0.00
HO-160	Submission As-Built Drawing For Telecom Network	12	24-May-27	07-Jun-27	24-Jan-27	06-Feb-27	0%	0.00	0.00
HO-180	Submission As-Built Drawing For Irrigation Network	12	29-May-27	10-Jun-27	02-Feb-27	18-Feb-27	0%	0.00	0.00
HO-190	As-Built Drawing For Potable Water Network	12	30-May-27	12-Jun-27	03-Feb-27	21-Feb-27	0%	0.00	0.00
HO-210	Submission As-Built Drawing For Pump station	1	03-Jun-27	05-Jun-27	03-Feb-27	03-Feb-27	0%	0.00	0.00
HO-150	Submission As-Built Drawing For Street Lighting Network	7	05-Jun-27	12-Jun-27	13-Feb-27	22-Feb-27	0%	0.00	0.00
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	06-Jun-27	20-Jun-27	06-Feb-27	22-Feb-27	0%	0.00	0.00
HO-140	Submission As-Built Drawing For Roads Network	3	12-Jun-27	14-Jun-27	18-Feb-27	22-Feb-27	0%	0.00	0.00
De-Mobilization Works		5	07-Jun-27	12-Jun-27	13-Feb-27	20-Feb-27	0%	0.00	0.00
HO-230	Remove Temporary Car Shades	5	07-Jun-27	12-Jun-27	13-Feb-27	20-Feb-27	0%	0.00	0.00
Handing Over		3	12-Jun-27	14-Jun-27	18-Feb-27	22-Feb-27	0%	0.00	0.00
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	3	12-Jun-27	14-Jun-27	18-Feb-27	22-Feb-27	0%	0.00	0.00

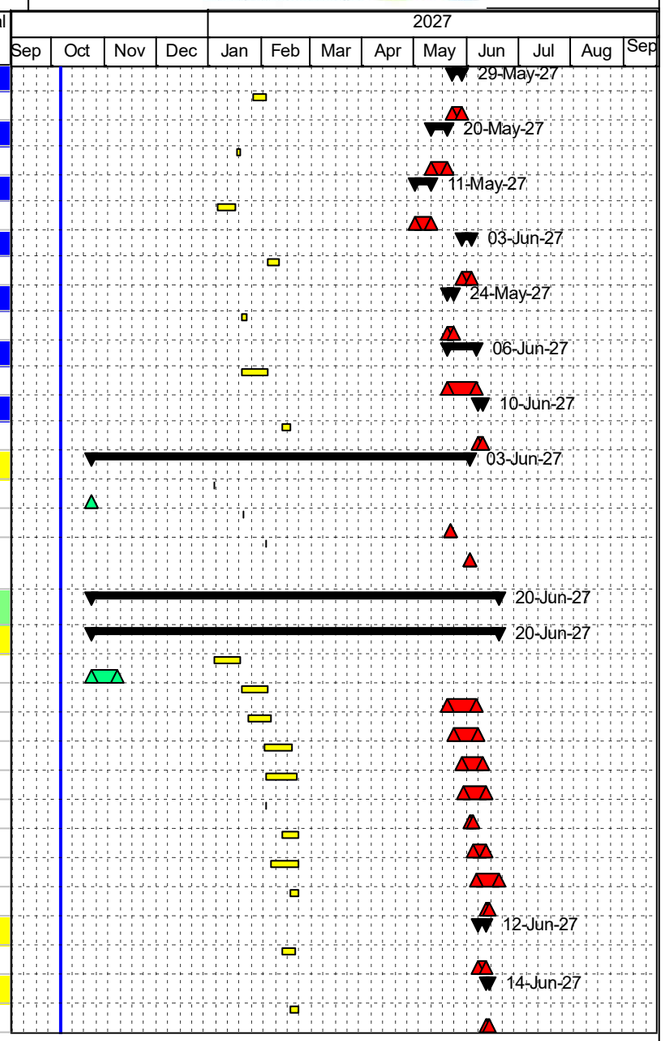

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
