Playgrounds Initiative: Qassim Oasis, Hail and Tabuk Industrial City

مبادرة الملاعب بالمنطقة الوسطى (حائل, واحة القصيم, تبوك)

CLIENT	CONTRACTOR	CONSULTANT	COMMENCEMENT	CONTRACT COMPLETION	P6 FORECAST FINISH
MODON	ADV	Egis	17-Feb-2026	16-Dec-2026	10-Feb-2027

Scope: football, basketball and padel playgrounds, air domes (Qassim and Tabuk), toilet buildings, landscaping, tanks and site services at three sites: Qassim Oasis, Hail and Tabuk Industrial City.

Status at a glance

Progress is measured as % complete in the cost-loaded P6 update (Performance % complete, weighted by budgeted cost); this week's files contain no man-hour-weighted progress. At 11-Oct-2026 the project is 65.36% complete against 76.88% planned, behind by 11.52% (SPI 0.85). Tabuk is furthest behind, at 55.38% against 70.53%, mainly in air dome construction and procurement.

PHYSICAL % COMPLETE
65.36% / 76.88% plan
▼ SPI 0.85 11.52% behind plan

PROGRESS THIS WEEK
— not stated
This week's files give no weekly increment.

CONTRACT TIME ELAPSED
78.1% · day 236 of 302
▼ P6 finish 10-Feb-2027

FORECAST DELAY TO COMPLETION
56 days
Contract 16-Dec-2026, P6 forecast 10-Feb-2027, float −47.4 days

The P6 update forecasts completion on 10-Feb-2027, 56 days after the contract date.

Substantial completion of all works moves from 16-Dec-2026 to 10-Feb-2027, with −47.4 days of total float. 205 of the 338 open activities have negative float, and the failed-start list of 11-Oct-2026 names 77 activities that did not start on time (Qassim 28, Hail 31, Tabuk 18). The air domes are the largest gap: Qassim is at 34.97% against 73.61% planned and Tabuk at 28.98% against 61.6%.

Progress by phase

Planned (Schedule % complete) and actual (Performance % complete) by site and phase, from the WBS summary of the P6 update, 11-Oct-2026. Weight is the share of budgeted cost.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Qassim Oasis	**49.1%**	**79.15%**	**67.2%**	**−11.95%**	**0.85**	▼ Behind
Engineering	1.5%	100%	100%	0.00%	1.00	✓ Complete
Procurement	13.3%	100%	82.29%	−17.71%	0.82	▼ Behind
Construction	29.5%	81.46%	66.88%	−14.58%	0.82	▼ Behind
Project closeout	4.9%	3%	18.5%	+15.50%	6.17	▲ Ahead
Hail	**19.1%**	**81.68%**	**77.3%**	**−4.38%**	**0.95**	▼ Behind
Engineering	0.6%	100%	100%	0.00%	1.00	✓ Complete
Procurement	5.2%	100%	97.17%	−2.83%	0.97	▼ Behind
Construction	11.4%	85.63%	78.26%	−7.37%	0.91	▼ Behind

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Project closeout	1.9%	3%	11.1%	+8.10%	3.70	▲ Ahead
Tabuk	**31.8%**	**70.53%**	**55.38%**	**-15.15%**	**0.79**	▼ Behind
Engineering	1.0%	100%	100%	0.00%	1.00	✓ Complete
Procurement	8.6%	100%	74.52%	-25.48%	0.75	▼ Behind
Construction	19.1%	67.06%	50.68%	-16.38%	0.76	▼ Behind
Project closeout	3.2%	3%	18.5%	+15.50%	6.17	▲ Ahead
Total	100%	**76.88%**	**65.36%**	**-11.52%**	**0.85**	▼ Behind

The P6 update (project PG-Reco-4, data date 09-Oct-2026) has 1,929 activities: 1,591 completed, 205 in progress and 133 not started. Its scheduled finish is 10-Feb-2027, against a must-finish date of 16-Dec-2026. Closeout runs ahead of plan because as-built drawings started early.

Scope of work: sites and work packages

The schedule holds no quantities, so the scope is shown as the construction work packages at each site: budgeted cost, earned value to date and planned value to date in SAR, from the WBS summary of 11-Oct-2026. This week's files give no previous figures, so “This week” shows –.

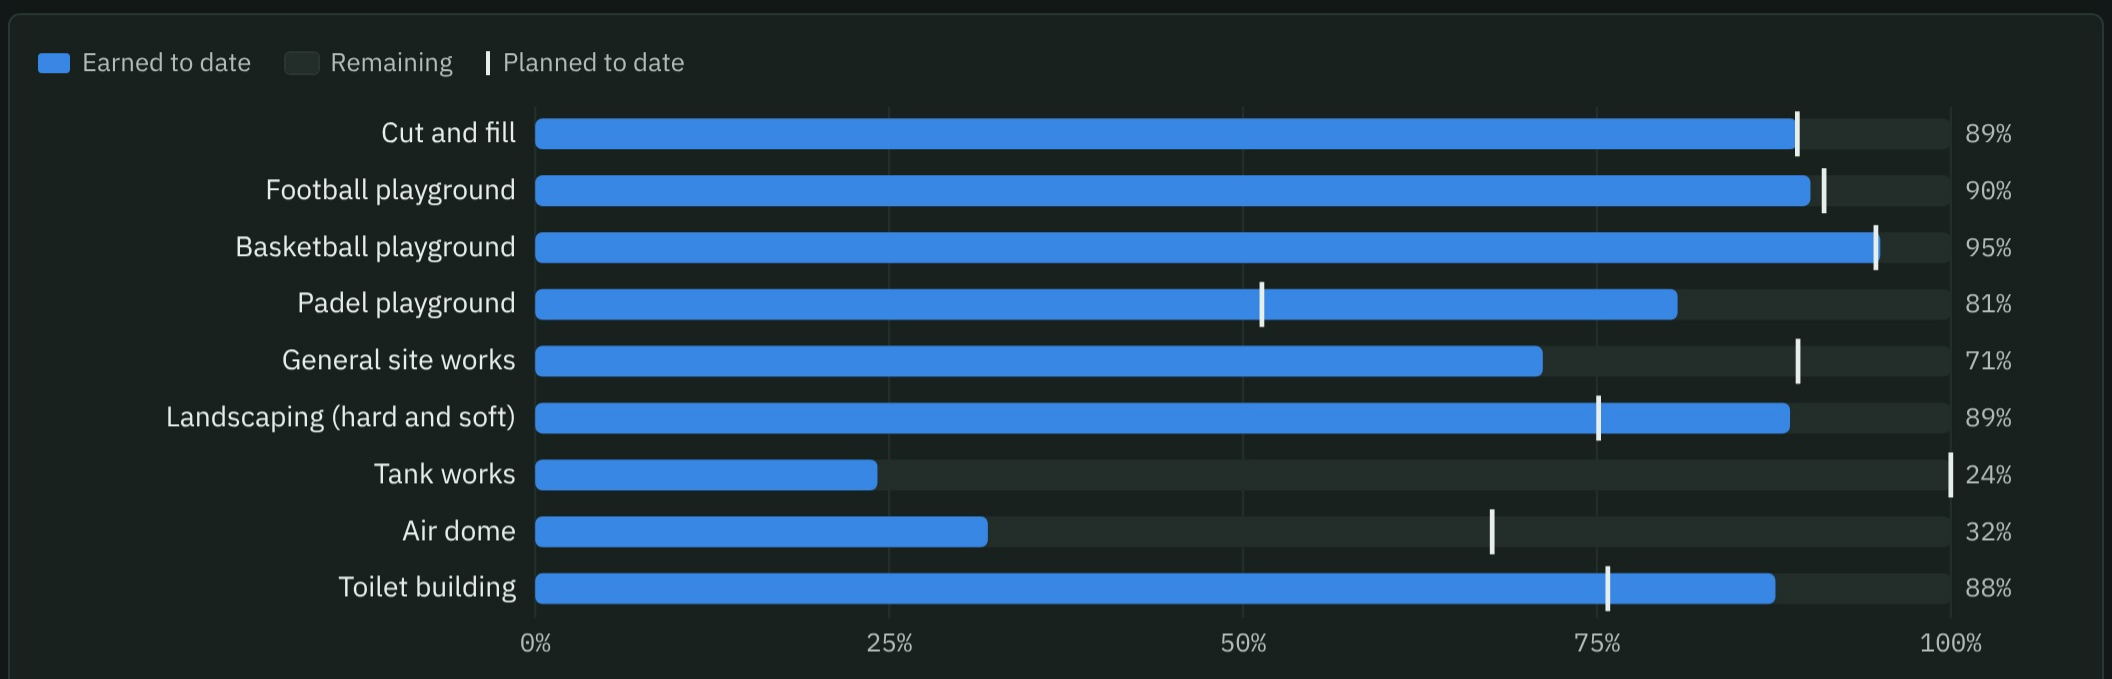

WORK PACKAGE	SITE	UNIT	BUDGET	EARNED	THIS WEEK	REMAINING	% COMPLETE	PLANNED %
Cut and fill	Qassim	SAR	900,600	729,000	–	171,600	80.9%	80.9%
	Hail	SAR	453,900	453,900	–	0	100.0%	100.0%
	Tabuk	SAR	228,240	228,240	–	0	100.0%	100.0%
	Total	SAR	**1,582,740**	**1,411,140**	–	**171,600**	**89.2%**	89.2%
Football playground	Qassim	SAR	611,282	571,304	–	39,979	93.5%	92.3%
	Hail	SAR	781,940	687,924	–	94,016	88.0%	93.2%
	Tabuk	SAR	333,290	296,090	–	37,200	88.8%	83.8%
	Total	SAR	**1,726,513**	**1,555,318**	–	**171,195**	**90.1%**	91.0%
Basketball playground	Qassim	SAR	381,705	372,447	–	9,258	97.6%	96.4%
	Tabuk	SAR	173,211	154,829	–	18,382	89.4%	91.1%
	Total	SAR	**554,916**	**527,276**	–	**27,640**	**95.0%**	94.7%
Padel playground	Qassim	SAR	325,484	276,386	–	49,098	84.9%	51.0%

WORK PACKAGE	SITE	UNIT	BUDGET	EARNED	THIS WEEK	REMAINING	% COMPLETE	PLANNED %
	Tabuk	SAR	116,990	80,691	–	36,299	69.0%	52.3%
	Total	SAR	**442,474**	**357,077**	**–**	**85,397**	**80.7%**	51.3%
General site works	Qassim	SAR	1,617,942	1,303,725	–	314,217	80.6%	92.4%
	Hail	SAR	1,224,114	716,076	–	508,038	58.5%	86.7%
	Tabuk	SAR	656,604	470,510	–	186,094	71.7%	86.1%
	Total	SAR	**3,498,661**	**2,490,311**	**–**	**1,008,350**	**71.2%**	89.2%
Landscaping (hard and soft)	Qassim	SAR	2,134,335	1,896,826	–	237,509	88.9%	81.5%
	Hail	SAR	1,252,052	1,069,354	–	182,699	85.4%	71.1%
	Tabuk	SAR	755,169	704,954	–	50,215	93.4%	63.9%
	Total	SAR	**4,141,556**	**3,671,133**	**–**	**470,423**	**88.6%**	75.1%
Tank works	Qassim	SAR	48,290	13,577	–	34,713	28.1%	100.0%
	Hail	SAR	48,290	11,826	–	36,465	24.5%	100.0%
	Tabuk	SAR	48,290	9,623	–	38,668	19.9%	100.0%
	Total	SAR	**144,871**	**35,026**	**–**	**109,845**	**24.2%**	100.0%
Air dome	Qassim	SAR	4,178,041	1,461,182	–	2,716,860	35.0%	73.6%
	Tabuk	SAR	4,178,041	1,210,693	–	2,967,348	29.0%	61.6%
	Total	SAR	**8,356,082**	**2,671,875**	**–**	**5,684,207**	**32.0%**	67.6%
Toilet building	Qassim	SAR	324,844	297,907	–	26,938	91.7%	76.4%
	Hail	SAR	328,494	260,954	–	67,539	79.4%	97.0%
	Tabuk	SAR	324,844	298,150	–	26,694	91.8%	53.7%
	Total	SAR	**978,182**	**857,011**	**–**	**121,171**	**87.6%**	75.8%

Reported this week

Stamped concrete, curbstone, steel posts for the fence, backfilling of the irrigation network, asphalt, waterproofing of the raft foundation for the glass facade and toilet area, and compaction and levelling (weekly executive summary). Next week: compaction and levelling, asphalt, curbstone, fence installation and stamped concrete.

Air domes and tanks lag most

Air dome: Qassim 34.97% against 73.61% planned, Tabuk 28.98% against 61.6%. Air dome mechanical works are at 0% at both sites, although planned at 100% (Qassim) and 84.38% (Tabuk). Water storage tanks are at 14.95% at every site against 100% planned. Padel playgrounds, softscape and parking are ahead of plan.

Milestones

Baseline from the recovery baseline schedule (Recovery Schedule.01). Forecasts from the Level 5 schedule (PDF, 11-Oct-2026) and the P6 update (XER, data date 09-Oct-2026), which agree on every milestone. Float is the P6 total float.

MILESTONE	BASELINE	LEVEL 5 SCHEDULE FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	17-Feb-2026	17-Feb-2026	17-Feb-2026 (actual)	–	✓ Done
Completion of earthworks (cut and fill)	05-May-2026	05-May-2026	05-May-2026 (actual)	–	✓ Done
Site preparation, work plans, schedule and drawing submittals	04-Aug-2026	16-Sep-2026 (+43 d)	16-Sep-2026 (actual)	–	✓ Done late
Completion of toilet building	28-Oct-2026	28-Nov-2026 (+31 d)	28-Nov-2026	−5.5	▼ Late

MILESTONE	BASELINE	LEVEL 5 SCHEDULE FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Completion of playground works	07-Dec-2026	14-Dec-2026 (+7 d)	14-Dec-2026	+2.6	▼ At risk
Completion of landscape works	16-Dec-2026	25-Jan-2027 (+40 d)	25-Jan-2027	−33.0	▼ Late
Substantial completion: all works	16-Dec-2026	10-Feb-2027 (+56 d)	10-Feb-2027	−47.4	▼ Late
Project completion date	16-Dec-2026	10-Feb-2027 (+56 d)	10-Feb-2027	−47.4	▼ Late

Every open contractual milestone is now forecast after its baseline date.

Toilet building completion moves by 31 days, landscape works by 40 days and substantial completion by 56 days. Playground works keeps +2.6 days of float but is forecast 7 days after its baseline. The site preparation and submittals milestone was achieved on 16-Sep-2026, 43 days late.

Procurement of key materials

P6 % complete of the open “delivery to site” activities for key materials (P6 update, data date 09-Oct-2026). Overall procurement is 82.29% complete at Qassim, 97.17% at Hail and 74.52% at Tabuk, against 100% planned.



Air dome materials: 60% delivered

At both Qassim and Tabuk, with −38.8 and −47.4 days of float. Tabuk's air dome materials carry the same −47.4 days of float as project completion.

Curtain wall (remaining)

Qassim delivery has not started: fabrication was due to start on 25-Jun-2026 and is now forecast to start on 10-Oct-2026, with delivery from 08-Nov-2026 to 24-Nov-2026. Hail is at 80% and Tabuk at 60%. Fire extinguishers at Hail are at 20%.

Health, safety and quality

This week's upload has no safety statistics or site inspection records (MIR, IR, NCR). The technical submittals register is the only quality record provided. Source: Technical Document Submittals Tracker, % Summary sheet.

Technical submittals

Submitted to date	819
Approved (codes A and B)	677 (82.7%)
Revise and resubmit (code C)	50
Under review	57
Delayed review (5 days or more)	35

Approved / submitted by type

Shop drawings	309 / 375
Document submittals (technical and general)	148 / 183
Material submittals	120 / 137
Pre-qualification	47 / 55
RFIs	30 / 34
Method statements	22 / 22
Material source approvals	1 / 13

9 of the 13 material source approvals are in delayed review.

Open issues and risks

From the failed-start list (11-Oct-2026), the P6 update and the submittals tracker. The files do not assign owners.

ISSUE	SITE	DETAIL
Air dome works	Qassim, Tabuk	At 34.97% (Qassim) and 28.98% (Tabuk) against 73.61% and 61.6% planned. Steel cable structure, membrane, air package units, HVAC and lighting installation are on the failed-start list (15 activities).
Site electrical, ELV and fire alarm	All sites	29 of the 77 failed starts: MDB and power panels, wiring, lighting fixtures, fibre optic, telecom, CCTV and fire alarm installation.
Storm water and utility works	All sites	Concrete encasement, backfilling and compaction, and surface reinstatement have not started on time (14 mechanical failed starts, including fire extinguishers and irrigation bubblers).
Water storage tanks	All sites	GRP water tank installation is on the failed-start list at all three sites. Tank works are at 28.12% (Qassim), 24.49% (Hail) and 19.93% (Tabuk) against 100% planned.
Curtain wall	Qassim, Hail	Fabrication of the remaining curtain wall is on the failed-start list at Qassim and Hail (baseline start 25-Jun-2026, now 10-Oct-2026).
Delayed submittal reviews	All sites	35 submittals are in delayed review, 12 of them shop drawings and 12 document submittals.

Data notes

- This report uses only the W2 upload (data date 11-Oct-2026). It has no physical progress sheet, no man-hour weights, no S-curve data, no site photos, no manpower, no cost or invoice data and no HSE statistics, so those sections are left out. Progress shown is the cost-weighted % complete from the P6 update.
- No previous-week or “this week” figures are stated in these files, so progress this week and the this-week column show –.
- The P6 XER has a data date of 09-Oct-2026, while the PDF schedules and the failed-start list are dated 11-Oct-2026.
- Three PDFs (Level 5 schedule, 3-week look-ahead, remaining works) are named MLTX-05-047 although they contain this project (MLTX-02-003).
- At project level, P6 reports 76.88% planned and 65.36% actual, but planned value ÷ budget gives 76.51% and earned value ÷ budget gives 65.04%. The report uses the P6 percentages.
- Qassim cut and fill is shown 100% complete, but its earned value is 729,000 of a 900,600 SAR budget (80.9%).

- 108 in-progress activities in the P6 update have a finish date before its data date (for example Air dome materials, Qassim: 60%, finish 06-Oct-2026). Their remaining durations need updating.
- Hail curtain wall fabrication is on the failed-start list (not started), but the P6 update shows Hail curtain wall delivery 80% complete.
- The submittals tracker has no planned submissions or deadlines (N/A) and its Design Drawings rows show #DIV/0!.

Compiled 28-Oct-2026 from the W2 weekly upload only (data date 11-Oct-2026).
