

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		366	07-Jan-26	06-Mar-27	07-Jan-26 A	03-Mar-27	95,996,525.00	72,199,080.25	72,486,079.99	75.21%	75.51%
PROJECT MILESTONES		351	07-Jan-26	06-Mar-27	07-Jan-26 A	03-Mar-27	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		351	07-Jan-26	06-Mar-27	07-Jan-26 A	03-Mar-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0010	Project Start Date	0	07-Jan-26		07-Jan-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0020	Completion of Mobilization Works	0		07-Feb-26		18-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0040	Completion of Time Schedule submission	0		28-Jan-26		11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0030	Completion of Site Suvey Works	0		09-Feb-26		12-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0050	Completion of Plans (PEP,PQP,HSE, Procurement Plan)	0		04-Feb-26		04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0060	Completion of Engineering and Materials	0		07-May-26		05-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0080	Network start	0	07-Sep-26		01-Aug-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0070	Completion of Site levelling, local roads & parkings	0		12-Feb-26		27-Oct-26	0.00	0.00	0.00	100%	0%
DAM3-PMS-MMS-0110	Competion of Testing and Commissioning	0		06-Feb-27		24-Dec-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0090	Completion of Construction	0		21-Feb-27		23-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0100	Project Completion Date	0		06-Mar-27		03-Mar-27	0.00	0.00	0.00	0%	0%
DISCIPLINE MILESTONES		292	27-Jan-26	21-Feb-27	15-Feb-26 A	23-Feb-27	0.00	0.00	0.00	0%	0%
900 SQM FACTORIES		292	27-Jan-26	21-Feb-27	15-Feb-26 A	23-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2360	Construction Start	0	27-Jan-26		15-Feb-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-DMS-2310	Completion of Civil works	0		01-Oct-26		21-Nov-26	0.00	0.00	0.00	100%	0%
DAM3-PMS-DMS-2330	Completion of Mechanical works	0		14-Dec-26		21-Dec-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2320	Completion of Electrical works	0		21-Dec-26		02-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2340	Completion of Architectural works	0		21-Dec-26		02-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2370	Construction Finish	0		21-Feb-27		23-Feb-27	0.00	0.00	0.00	0%	0%
SITE INFRASTRUCTURE		22	22-Dec-26	21-Feb-27	27-Jan-27	23-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2460	Completion of Environmentall works	0		22-Dec-26		27-Jan-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2450	Completion of External works	0		21-Feb-27		23-Feb-27	0.00	0.00	0.00	0%	0%
MOBILIZATION		35	07-Jan-26	16-Feb-26	07-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
SITE FACILITIES AND OFFICES		27	07-Jan-26	07-Feb-26	07-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	0%	0%
DAM3-MOB-SO.0019	Mobilization of Manpower	2	05-Feb-26	07-Feb-26	07-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0014	Clear and Grub for Offices and Access Roads	2	15-Jan-26	17-Jan-26	11-Jan-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0015	Construct Site Offices	4	18-Jan-26	21-Jan-26	19-Jan-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0020	Mobilization of Equipment	2	05-Feb-26	07-Feb-26	25-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0018	Install Project Signs	4	01-Feb-26	04-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0011	Site Layout Plan Prep	2	10-Jan-26	11-Jan-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0012	Site Layout Plan Submittal	2	12-Jan-26	13-Jan-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0013	Site Layout Plan Owner Approval	2	14-Jan-26	15-Jan-26	04-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0016	Electrical Works and Connections	4	22-Jan-26	26-Jan-26	09-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0017	Site Utilities	4	27-Jan-26	31-Jan-26	11-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0010	Site Survey	2	07-Jan-26	08-Jan-26	12-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%
PRELIMINARY SUBMITTALS		31	22-Jan-26	16-Feb-26	14-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTALS		21	22-Jan-26	04-Feb-26	14-Jan-26 A	21-Feb-26 A	0.00	0.00	0.00	0%	0%
DAM3-PRE-SUB-0012	Baseline Schedule	2	27-Jan-26	28-Jan-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0011	Health & Safety Plan	2	25-Jan-26	26-Jan-26	26-Jan-26 A	26-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0015	Quality Control Plan	2	03-Feb-26	04-Feb-26	28-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0013	Risk Management plan	2	29-Jan-26	31-Jan-26	28-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0014	Communication Plan	2	01-Feb-26	02-Feb-26	21-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0010	Project Execution Plan	2	22-Jan-26	24-Jan-26	21-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVALS		29	25-Jan-26	16-Feb-26	14-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
DAM3-PRE-SUB-1015	Baseline Schedule	10	05-Feb-26	16-Feb-26	14-Jan-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-PRE-SUB-1011	Health & Safety Plan	10	27-Jan-26	07-Feb-26	26-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1014	Quality Control Plan	10	05-Feb-26	16-Feb-26	28-Jan-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1012	Risk Management plan	10	01-Feb-26	11-Feb-26	28-Jan-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1013	Communication Plan	10	03-Feb-26	14-Feb-26	21-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1010	Project Execution Plan	10	25-Jan-26	04-Feb-26	21-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
ENGINEERING (3%)		159	22-Jan-26	17-May-26	15-Jan-26 A	05-Jul-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
SHOP DRAWINGS		138	27-Jan-26	17-May-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTAL		136	27-Jan-26	07-May-26	20-Jan-26 A	01-Jul-26 A	0.00	0.00	0.00	0%	0%
STRUCTURAL		87	10-Feb-26	22-Mar-26	03-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-C-830	SECTIONS	2	03-Mar-26	04-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-840	EXTERNAL WALL SECTION DETAILS	2	05-Mar-26	07-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-850	BASE PLATE DETAILS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-770	BASE PLATE LAYOUT	2	15-Feb-26	16-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-790	ROOF FRAMING LAYOUT	2	19-Feb-26	23-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-800	PURLINS FRAMING LAYOUT	2	23-Feb-26	25-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-810	ROOF SHEETING LAYOUT	2	25-Feb-26	28-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-820	COLUMNS AND AXIS LAYOUT	2	01-Mar-26	02-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-750	FOUNDATION LAYOUT	2	10-Feb-26	11-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-780	TIE BEAM @ 4500mm EL.	2	17-Feb-26	19-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	15-Mar-26	16-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	21-Mar-26	22-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	12-Feb-26	14-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	10-Mar-26	11-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-870	STRUCTURAL SCHEDULE	2	12-Mar-26	14-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		75	25-Feb-26	04-Apr-26	03-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-A-830	GROUND FLOOR LAYOUT PLAN	2	25-Feb-26	28-Feb-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	01-Mar-26	02-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-860	ELEVATIONS (SHEET 01 0F 02)	2	05-Mar-26	07-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-870	BUILDING SECTIONS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-880	WALL SECTIONS	2	11-Mar-26	12-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-1170	ELEVATIONS (SHEET 01 0F 02)	5	05-Mar-26	10-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-890	CEILING LAYOUT PLAN	2	14-Mar-26	15-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-900	FINISHING LAYOUT PLAN	2	16-Mar-26	21-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-910	TOILET DETAILS	2	22-Mar-26	23-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-920	DOORS & WINDOWS SCHEDULE	2	24-Mar-26	25-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-930	MISCELLANEOUS DETAILS - 01	2	26-Mar-26	28-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-940	MISCELLANEOUS DETAILS - 02	2	29-Mar-26	30-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-950	SIGNAGE LOCATION PLAN	2	31-Mar-26	01-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-960	SIGNAGE DESIGN DETAILS	2	02-Apr-26	04-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	03-Mar-26	04-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		47	03-Mar-26	23-Apr-26	04-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	15-Mar-26	16-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	21-Mar-26	22-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	23-Mar-26	24-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	25-Mar-26	26-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	11-Apr-26	12-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	18-Apr-26	19-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	20-Apr-26	21-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-800	MISCELLANEOUS DETAILS	2	22-Apr-26	23-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%

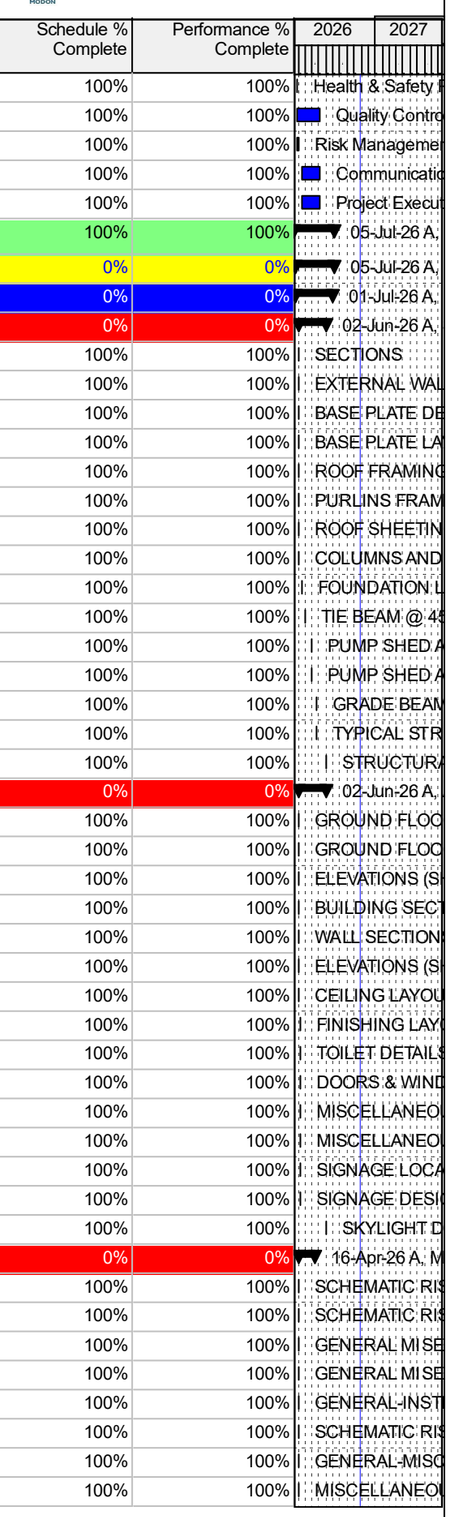

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SS-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	13-Apr-26	14-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	GENERAL MISC
DAM3-E-SS-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	05-Mar-26	07-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	TOILETS DETA
DAM3-E-SS-M-640	TOILET DETAILS PLUMBING-WATER	2	12-Mar-26	14-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	TOILET DETAIL
DAM3-E-SS-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	15-Apr-26	16-Apr-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GROU
DAM3-E-SS-M-620	TYPICAL ROOF PLUMBING PLAN	2	08-Mar-26	09-Mar-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL ROOF
DAM3-E-SS-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	03-Mar-26	04-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GROU
DAM3-E-SS-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	10-Mar-26	11-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-M-690	SCHEDULE- PLUMBING	2	28-Mar-26	29-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE- P
DAM3-E-SS-M-720	SCHEDULES	2	04-Apr-26	05-Apr-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SS-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	06-Apr-26	07-Apr-26	26-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-M-740	TYPICAL ROOF HVAC PLAN	2	08-Apr-26	09-Apr-26	26-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL ROO
DAM3-E-SS-M-700	PUMP ROOM LAYOUT	2	30-Mar-26	31-Mar-26	16-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SS-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	01-Apr-26	02-Apr-26	16-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
ELECTRICAL		133	05-Mar-26	05-May-26	09-Feb-26 A	25-Jun-26 A	0.00	0.00	0.00	0%	0%	25-Jun-26 A
DAM3-E-SS-E-940	GROUND FLOOR POWER PLAN	2	05-Mar-26	07-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	08-Mar-26	09-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	10-Mar-26	11-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR P
DAM3-E-SS-E-990	GROUND FLOOR LIGHTING PLAN	2	21-Mar-26	22-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1000	ROOF FLOOR LIGHTING PLAN	2	23-Mar-26	24-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SS-E-1060	ROOF FLOOR LIGHTENING PLAN	2	06-Apr-26	07-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SS-E-1140	POWER FOR MECHANICAL	2	25-Apr-26	26-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	POWER FOR M
DAM3-E-SS-E-1150	GROUND FLOOR LIGHTING PLAN	2	27-Apr-26	28-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1130	GROUND FLOOR POWER PLAN	1	22-Apr-26	23-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1030	GROUND FLOOR CCTV PLAN	2	30-Mar-26	31-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	01-Apr-26	02-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1050	GROUND FLOOR GROUNDING PLAN	2	04-Apr-26	05-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1120	ELECTRICAL DETAILS	2	20-Apr-26	21-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SS-E-1160	GROUND FLOOR GROUNDING PLAN	2	29-Apr-26	30-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1180	ELECTRICAL DETAILS	2	04-May-26	05-May-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SS-E-1010	GOUND FLOOR ACCESS CONTROL	2	25-Mar-26	26-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	GOUND FLOO
DAM3-E-SS-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	28-Mar-26	29-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-E-1070	POWER RISER DIAGRAM	2	08-Apr-26	09-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	POWER RISER
DAM3-E-SS-E-1080	FIRE ALARM RISER DIAGRAM	2	11-Apr-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	FIRE ALARM R
DAM3-E-SS-E-1090	DATA & TELECOME RISER DIAGRAM	2	13-Apr-26	14-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	DATA & TELEC
DAM3-E-SS-E-1100	ACCESS CONTROL RISER DIAGRAM	2	15-Apr-26	16-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	ACCESS CON
DAM3-E-SS-E-1110	SCHEDULES	2	18-Apr-26	19-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SS-E-970	ROOF FLOOR POWER	2	12-Mar-26	14-Mar-26	08-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SS-E-1170	RISER DIAGRAM	2	02-May-26	03-May-26	27-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	RISER DIAGR
DAM3-E-SS-E-980	PV SYSTEM CALCULATION	2	15-Mar-26	16-Mar-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	100%	100%	PV SYSTEM
ROAD DRAWINGS		117	27-Jan-26	29-Mar-26	20-Jan-26 A	01-Jul-26 A	0.00	0.00	0.00	0%	0%	01-Jul-26 A
DAM3-E-SS-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	08-Feb-26	09-Feb-26	20-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%	TOPOGRAPHIC
DAM3-E-SS-R-730	GRADING LAYOUT PLAN	2	27-Jan-26	28-Jan-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	GRADING LAYO
DAM3-E-SS-R-880	GENERAL SITE PLAN - OVERALL	2	05-Mar-26	07-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL SITE
DAM3-E-SS-R-890	SITE SETTING-OUT PLAN - OVERALL	2	08-Mar-26	09-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	SITE SETTING-
DAM3-E-SS-R-900	GENERAL LANDSCAPE LAYOUT	2	10-Mar-26	11-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL LAN
DAM3-E-SS-R-910	GENERAL HARDSCAPE LAYOUT	2	12-Mar-26	14-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL HAR
DAM3-E-SS-R-920	GENERAL SOFTSCAPE LAYOUT	2	15-Mar-26	16-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL SOF
DAM3-E-SS-R-960	LANDSCAPE SCHEDULES	2	28-Mar-26	29-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	LANDSCAPE S
DAM3-E-SS-R-930	PUMP ROOM DETAILS	1	21-Mar-26	22-Mar-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM D

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SS-R-740	ROAD LAYOUT PLAN	2	29-Jan-26	31-Jan-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	ROAD LAYOUT
DAM3-E-SS-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	01-Feb-26	02-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CROS
DAM3-E-SS-R-760	TYPICAL CROSS SECTIONS	2	03-Feb-26	04-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CROS
DAM3-E-SS-R-770	ROAD PROFILES	2	05-Feb-26	07-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	ROAD PROFIL
DAM3-E-SS-R-940	GENERAL DETAILS	1	23-Mar-26	24-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL DET
DAM3-E-SS-R-830	SIGNING & MARKING LAYOUT PLAN	2	19-Feb-26	23-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SIGNING & M
DAM3-E-SS-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	23-Feb-26	25-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SS-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	25-Feb-26	28-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SS-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	01-Mar-26	02-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SS-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	03-Mar-26	04-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SS-R-790	ALIGNMENT & CURB SETTING OUT	2	10-Feb-26	11-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SS-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	12-Feb-26	14-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SS-R-810	ALIGNMNET GEOMETRIC DATA	2	15-Feb-26	16-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMNET
DAM3-E-SS-R-820	SWEPT PATH LAYOUT PLAN	2	17-Feb-26	19-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	SWEPT PAT
DAM3-E-SS-R-950	LANDSCAPE DETAILS	1	25-Mar-26	26-Mar-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	100%	100%	LANDSCAP
EXTERNAL		74	01-Mar-26	07-May-26	10-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%	02-Jun-26 A,
DAM3-E-SS-EX-730	PIPE TRENCH DETAILS	2	10-Mar-26	11-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SS-EX-740	BURIED GATE VALVE DETAILS	2	12-Mar-26	14-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BURIED GATE V
DAM3-E-SS-EX-770	WASHOUT CHAMBER DETAILS	2	23-Mar-26	24-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	WASHOUT CHA
DAM3-E-SS-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	25-Mar-26	26-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	AIR RELEASE V
DAM3-E-SS-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-870	GENERAL NOTES	2	08-Apr-26	09-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	GENERAL NOTE
DAM3-E-SS-EX-880	PIPE TRENCHES DETAILS (1)	2	11-Apr-26	12-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCHE
DAM3-E-SS-EX-890	PIPE TRENCHES DETAILS (2)	2	13-Apr-26	14-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCHE
DAM3-E-SS-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLACE
DAM3-E-SS-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BACKDROP DE
DAM3-E-SS-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM TO	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BACKDROP DE
DAM3-E-SS-EX-960	PIPE TRENCH DETAILS	2	22-Apr-26	23-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SS-EX-970	BURIED GATE VALVE DETAILS	2	25-Apr-26	26-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BURIED GATE V
DAM3-E-SS-EX-1000	WASHOUT CHAMBER DETAILS	2	02-May-26	03-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	WASHOUT CHA
DAM3-E-SS-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	04-May-26	05-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	AIR RELEASE V
DAM3-E-SS-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK
DAM3-E-SS-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	15-Apr-26	16-Apr-26	12-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLACE
DAM3-E-SS-EX-940	PRECAST MANHOLE DETAILS	2	18-Apr-26	19-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	PRECAST MA
DAM3-E-SS-EX-750	SINGLE VALVE CHAMBER DETAILS	2	15-Mar-26	16-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SS-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	21-Mar-26	22-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VALV
DAM3-E-SS-EX-980	SINGLE VALVE CHAMBER DETAILS	2	27-Apr-26	28-Apr-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SS-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	29-Apr-26	30-Apr-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VALV
DAM3-E-SS-EX-690	POTABLE WATER NETWORK	2	01-Mar-26	02-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE WA
DAM3-E-SS-EX-700	FIRE FIGHTING WATER NETWORK	2	03-Mar-26	04-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SS-EX-710	POTABLE WATER NETWORK PROFILES	2	05-Mar-26	07-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE WA
DAM3-E-SS-EX-720	FIRE FIGHTING NETWORK PROFILE	2	08-Mar-26	09-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SS-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	20-Apr-26	21-Apr-26	12-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	IRRIGATION

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-SS-EX-850	SEWAGE NETWORK	2	04-Apr-26	05-Apr-26	14-May-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE	
DAM3-E-SS-EX-860	SEWAGE NETWORK PROFILES	2	06-Apr-26	07-Apr-26	14-May-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE	
DAM3-E-SS-EX-790	FLOW METER DETAILS	2	28-Mar-26	29-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE	
DAM3-E-SS-EX-800	FLOW METER REINFORCEMENT DETAILS	2	30-Mar-26	31-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE	
REVIEW AND APPROVAL		117	29-Jan-26	17-May-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%	05-Jul-26 A,	
STRUCTURAL		87	12-Feb-26	24-Mar-26	03-Feb-26 A	03-Jun-26 A	0.00	0.00	0.00	0%	0%	03-Jun-26 A,	
DAM3-E-SA-C-830	SECTIONS	2	05-Mar-26	07-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	SECTIONS	
DAM3-E-SA-C-840	EXTERNAL WALL SECTION DETAILS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	EXTERNAL WAL	
DAM3-E-SA-C-850	BASE PLATE DETAILS	2	10-Mar-26	11-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	BASE PLATE DE	
DAM3-E-SA-C-770	BASE PLATE LAYOUT	2	17-Feb-26	19-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	BASE PLATE L	
DAM3-E-SA-C-790	ROOF FRAMING LAYOUT	2	23-Feb-26	25-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	ROOF FRAMIN	
DAM3-E-SA-C-800	PURLINS FRAMING LAYOUT	2	25-Feb-26	28-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	PURLINS FRA	
DAM3-E-SA-C-810	ROOF SHEETING LAYOUT	2	01-Mar-26	02-Mar-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	ROOF SHEETI	
DAM3-E-SA-C-820	COLUMNS AND AXIS LAYOUT	2	03-Mar-26	04-Mar-26	07-Feb-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	COLUMNS AND	
DAM3-E-SA-C-750	FOUNDATION LAYOUT	2	12-Feb-26	14-Feb-26	18-Feb-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	FOUNDATION L	
DAM3-E-SA-C-780	TIE BEAM @ 4500mm EL.	2	19-Feb-26	23-Feb-26	01-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	TIE BEAM @	
DAM3-E-SA-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	21-Mar-26	22-Mar-26	29-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP SHED	
DAM3-E-SA-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	23-Mar-26	24-Mar-26	29-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP SHED	
DAM3-E-SA-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	15-Feb-26	16-Feb-26	21-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	GRADE BEAM	
DAM3-E-SA-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	12-Mar-26	14-Mar-26	21-Apr-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL STR	
DAM3-E-SA-C-870	STRUCTURAL SCHEDULE	2	15-Mar-26	16-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	STRUCTURA	
ARCHITECTURAL		75	01-Mar-26	06-Apr-26	03-Feb-26 A	03-Jun-26 A	0.00	0.00	0.00	0%	0%	03-Jun-26 A,	
DAM3-E-SA-A-830	GROUND FLOOR LAYOUT PLAN	2	01-Mar-26	02-Mar-26	03-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO	
DAM3-E-SA-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	03-Mar-26	04-Mar-26	03-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO	
DAM3-E-SA-A-860	ELEVATIONS (SHEET 01 0F 02)	2	08-Mar-26	09-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	ELEVATIONS (S	
DAM3-E-SA-A-870	ELEVATIONS (SHEET 01 0F 02)	2	10-Mar-26	11-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	ELEVATIONS (S	
DAM3-E-SA-A-880	WALL SECTIONS	2	14-Mar-26	15-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	WALL SECTION	
DAM3-E-SA-A-1170	BUILDING SECTIONS	5	12-Mar-26	21-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	BUILDING SECT	
DAM3-E-SA-A-890	CEILING LAYOUT PLAN	2	16-Mar-26	21-Mar-26	05-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	CEILING LAYOU	
DAM3-E-SA-A-900	FINISHING LAYOUT PLAN	2	22-Mar-26	23-Mar-26	09-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	FINISHING LAY	
DAM3-E-SA-A-910	TOILET DETAILS	2	24-Mar-26	25-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	TOILET DETAIL	
DAM3-E-SA-A-920	DOORS & WINDOWS SCHEDULE	2	26-Mar-26	28-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	DOORS & WINI	
DAM3-E-SA-A-930	MISCELLANEOUS DETAILS - 01	2	29-Mar-26	30-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-A-940	MISCELLANEOUS DETAILS - 02	2	31-Mar-26	01-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-A-950	SIGNAGE LOCATION PLAN	2	02-Apr-26	04-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	SIGNAGE LOC	
DAM3-E-SA-A-960	SIGNAGE DESIGN DETAILS	2	05-Apr-26	06-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	SIGNAGE DESI	
DAM3-E-SA-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	05-Mar-26	07-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	SKYLIGHT D	
MECHANICAL		51	05-Mar-26	26-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	0%	0%	09-Jun-26 A,	
DAM3-E-SA-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	21-Mar-26	22-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC R	
DAM3-E-SA-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	23-Mar-26	24-Mar-26	04-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC R	
DAM3-E-SA-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	25-Mar-26	26-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	28-Mar-26	29-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	13-Apr-26	14-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	GENERAL-IN	
DAM3-E-SA-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	20-Apr-26	21-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC	
DAM3-E-SA-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	22-Apr-26	23-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	GENERAL-M	
DAM3-E-SA-M-800	MISCELLANEOUS DETAILS	2	25-Apr-26	26-Apr-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	15-Apr-26	16-Apr-26	05-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	08-Mar-26	09-Mar-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	TOILETS DET	
DAM3-E-SA-M-640	TOILET DETAILS PLUMBING-WATER	2	15-Mar-26	16-Mar-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	TOILET DETA	

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SA-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	18-Apr-26	19-Apr-26	14-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GR
DAM3-E-SA-M-620	TYPICAL ROOF PLUMBING PLAN	2	10-Mar-26	11-Mar-26	16-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL RO
DAM3-E-SA-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	05-Mar-26	07-Mar-26	17-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GR
DAM3-E-SA-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	12-Mar-26	14-Mar-26	17-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	GROUND FL
DAM3-E-SA-M-690	SCHEDULE- PLUMBING	2	30-Mar-26	31-Mar-26	17-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE-
DAM3-E-SA-M-720	SCHEDULES	2	06-Apr-26	07-Apr-26	17-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SA-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	08-Apr-26	09-Apr-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	GROUND FL
DAM3-E-SA-M-740	TYPICAL ROOF HVAC PLAN	2	11-Apr-26	12-Apr-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL RO
DAM3-E-SA-M-700	PUMP ROOM LAYOUT	2	01-Apr-26	02-Apr-26	16-Apr-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SA-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	04-Apr-26	05-Apr-26	21-Apr-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
ELECTRICAL		99	08-Mar-26	07-May-26	09-Feb-26 A	28-Jun-26 A	0.00	0.00	0.00	0%	0%	28-Jun-26 A
DAM3-E-SA-E-940	GROUND FLOOR POWER PLAN	2	08-Mar-26	09-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	10-Mar-26	11-Mar-26	09-Feb-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SA-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	12-Mar-26	14-Mar-26	09-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SA-E-990	GROUND FLOOR LIGHTING PLAN	2	23-Mar-26	24-Mar-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1000	ROOF FLOOR LIGHTING PLAN	2	25-Mar-26	26-Mar-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SA-E-1060	ROOF FLOOR LIGHTENING PLAN	2	08-Apr-26	09-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SA-E-1130	GROUND FLOOR POWER PLAN	2	25-Apr-26	26-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1140	POWER FOR MECHANICAL	2	27-Apr-26	28-Apr-26	09-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	POWER FOR M
DAM3-E-SA-E-1150	GROUND FLOOR LIGHTING PLAN	2	29-Apr-26	30-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1030	GROUND FLOOR CCTV PLAN	2	01-Apr-26	02-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	04-Apr-26	05-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1050	GROUND FLOOR GROUNDING PLAN	2	06-Apr-26	07-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1120	ELECTRICAL DETAILS	2	22-Apr-26	23-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SA-E-1160	GROUND FLOOR GROUNDING PLAN	2	02-May-26	03-May-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1180	ELECTRICAL DETAILS	2	06-May-26	07-May-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SA-E-1010	GOUND FLOOR ACCESS CONTROL	2	28-Mar-26	29-Mar-26	29-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	GOUND FLOO
DAM3-E-SA-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	30-Mar-26	31-Mar-26	29-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SA-E-1070	POWER RISER DIAGRAM	2	11-Apr-26	12-Apr-26	29-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	POWER RIS
DAM3-E-SA-E-1080	FIRE ALARM RISER DIAGRAM	2	13-Apr-26	14-Apr-26	29-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE ALARM
DAM3-E-SA-E-1090	DATA & TELECOME RISER DIAGRAM	2	15-Apr-26	16-Apr-26	29-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	DATA & TELEC
DAM3-E-SA-E-1100	ACCESS CONTROL RISER DIAGRAM	2	18-Apr-26	19-Apr-26	29-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	ACCESS CON
DAM3-E-SA-E-1110	SCHEDULES	2	20-Apr-26	21-Apr-26	29-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE
DAM3-E-SA-E-970	ROOF FLOOR POWER	2	15-Mar-26	16-Mar-26	08-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SA-E-1170	RISER DIAGRAM	2	04-May-26	05-May-26	27-Apr-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	RISER DIAG
DAM3-E-SA-E-980	PV SYSTEM CALCULATION	2	21-Mar-26	22-Mar-26	25-Jun-26 A	28-Jun-26 A	0.00	0.00	0.00	100%	100%	PV SYSTEM
ROAD DRAWINGS		117	29-Jan-26	31-Mar-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%	05-Jul-26 A,
DAM3-E-SA-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	10-Feb-26	11-Feb-26	20-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	TOPOGRAPHIC
DAM3-E-SA-R-730	GRADING LAYOUT PLAN	2	29-Jan-26	31-Jan-26	03-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	GRADING LA
DAM3-E-SA-R-880	GENERAL SITE PLAN - OVERALL	2	08-Mar-26	09-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL SI
DAM3-E-SA-R-890	SITE SETTING-OUT PLAN - OVERALL	2	10-Mar-26	11-Mar-26	08-Mar-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	SITE SETTIN
DAM3-E-SA-R-900	GENERAL LANDSCAPE LAYOUT	2	12-Mar-26	14-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL LA
DAM3-E-SA-R-910	GENERAL HARDSCAPE LAYOUT	2	15-Mar-26	16-Mar-26	08-Mar-26 A	07-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL HA
DAM3-E-SA-R-920	GENERAL SOFTSCAPE LAYOUT	2	21-Mar-26	22-Mar-26	08-Mar-26 A	09-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL SC
DAM3-E-SA-R-960	LANDSCAPE SCHEDULES	2	30-Mar-26	31-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	LANDSCAPE
DAM3-E-SA-R-930	PUMP ROOM DETAILS	2	23-Mar-26	24-Mar-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SA-R-740	ROAD LAYOUT PLAN	2	01-Feb-26	02-Feb-26	16-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD LAYOU
DAM3-E-SA-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	03-Feb-26	04-Feb-26	16-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CRO
DAM3-E-SA-R-760	TYPICAL CROSS SECTIONS	2	05-Feb-26	07-Feb-26	16-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CRO

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SA-R-770	ROAD PROFILES	2	08-Feb-26	09-Feb-26	16-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD PROFI
DAM3-E-SA-R-940	GENERAL DETAILS	2	25-Mar-26	26-Mar-26	18-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL DE
DAM3-E-SA-R-830	SIGNING & MARKING LAYOUT PLAN	2	23-Feb-26	25-Feb-26	21-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	SIGNING & M
DAM3-E-SA-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	25-Feb-26	28-Feb-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	01-Mar-26	02-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	03-Mar-26	04-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	05-Mar-26	07-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-790	ALIGNMENT & CURB SETTING OUT	2	12-Feb-26	14-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SA-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	15-Feb-26	16-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SA-R-810	ALIGNMNET GEOMETRIC DATA	2	17-Feb-26	19-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMNET
DAM3-E-SA-R-820	SWEPT PATH LAYOUT PLAN	2	19-Feb-26	23-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	SWEPT PAT
DAM3-E-SA-R-950	LANDSCAPE DETAILS	2	28-Mar-26	29-Mar-26	01-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%	LANDSCAP
EXTERNAL		78	03-Mar-26	17-May-26	10-Feb-26 A	08-Jun-26 A	0.00	0.00	0.00	0%	0%	08-Jun-26 A,
DAM3-E-SA-EX-730	PIPE TRENCH DETAILS	2	12-Mar-26	14-Mar-26	10-Feb-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENC
DAM3-E-SA-EX-740	BURIED GATE VALVE DETAILS	2	15-Mar-26	16-Mar-26	10-Feb-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	BURIED GAT
DAM3-E-SA-EX-770	WASHOUT CHAMBER DETAILS	2	25-Mar-26	26-Mar-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	WASHOUT C
DAM3-E-SA-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	28-Mar-26	29-Mar-26	10-Feb-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	AIR RELEAS
DAM3-E-SA-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-870	GENERAL NOTES	2	11-Apr-26	12-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL NOT
DAM3-E-SA-EX-880	PIPE TRENCHES DETAILS (1)	2	13-Apr-26	14-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-890	PIPE TRENCHES DETAILS (2)	2	15-Apr-26	16-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	18-Apr-26	19-Apr-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLA
DAM3-E-SA-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM TO	2	18-Apr-26	19-Apr-26	10-Feb-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	BACKDROP
DAM3-E-SA-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	18-Apr-26	19-Apr-26	10-Feb-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	BACKDROP
DAM3-E-SA-EX-960	PIPE TRENCH DETAILS	2	25-Apr-26	26-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-970	BURIED GATE VALVE DETAILS	2	27-Apr-26	28-Apr-26	10-Feb-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	BURIED GAT
DAM3-E-SA-EX-1000	WASHOUT CHAMBER DETAILS	2	04-May-26	05-May-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	WASHOUT C
DAM3-E-SA-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	06-May-26	07-May-26	10-Feb-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	AIR RELEAS
DAM3-E-SA-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	09-May-26	10-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	11-May-26	12-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	13-May-26	14-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	16-May-26	17-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	06-Apr-26	07-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	18-Apr-26	19-Apr-26	12-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLA
DAM3-E-SA-EX-940	PRECAST MANHOLE DETAILS	2	20-Apr-26	21-Apr-26	15-Apr-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	PRECAST M
DAM3-E-SA-EX-750	SINGLE VALVE CHAMBER DETAILS	2	21-Mar-26	22-Mar-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SA-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	23-Mar-26	24-Mar-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VAL
DAM3-E-SA-EX-980	SINGLE VALVE CHAMBER DETAILS	2	29-Apr-26	30-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SA-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	02-May-26	03-May-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VAL
DAM3-E-SA-EX-690	POTABLE WATER NETWORK	2	03-Mar-26	04-Mar-26	11-May-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	POTABLE W
DAM3-E-SA-EX-700	FIRE FIGHTING WATER NETWORK	2	05-Mar-26	07-Mar-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SA-EX-710	POTABLE WATER NETWORK PROFILES	2	08-Mar-26	09-Mar-26	11-May-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE W
DAM3-E-SA-EX-720	FIRE FIGHTING NETWORK PROFILE	2	10-Mar-26	11-Mar-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SA-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	22-Apr-26	23-Apr-26	12-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	IRRIGATION
DAM3-E-SA-EX-850	SEWAGE NETWORK	2	06-Apr-26	07-Apr-26	14-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE
DAM3-E-SA-EX-860	SEWAGE NETWORK PROFILES	2	08-Apr-26	09-Apr-26	14-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE
DAM3-E-SA-EX-790	FLOW METER DETAILS	2	30-Mar-26	31-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-SA-EX-800	FLOW METER REINFORCEMENT DETAILS	2	01-Apr-26	02-Apr-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE	
PRE QUALIFACTION FOR MATERIALS		138	22-Jan-26	12-Apr-26	15-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%	11-Jun-26 A,	
PREPARATION AND SUBMITTAL		108	22-Jan-26	09-Apr-26	15-Jan-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,	
STRUCTURAL		10	22-Jan-26	02-Feb-26	15-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	0%	0%	19-Jan-26 A, STR	
DAM3-E-PS-C-0010	Anti termite	2	22-Jan-26	24-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Anti termite	
DAM3-E-PS-C-0020	Concrete mix	2	25-Jan-26	26-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Concrete mix	
DAM3-E-PS-C-0040	Bitumen paint	2	29-Jan-26	31-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Bitumen paint	
DAM3-E-PS-C-0050	Rebar	2	01-Feb-26	02-Feb-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Rebar	
DAM3-E-PS-C-0030	Polyethylene sheet	2	27-Jan-26	28-Jan-26	19-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	100%	100%	Polyethylene she	
ARCHITECTURAL		100	25-Jan-26	02-Mar-26	08-Feb-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,	
DAM3-E-PS-A-0040	Concrete masonry unit (CMU)	2	27-Jan-26	28-Jan-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Concrete mason	
DAM3-E-PS-A-0130	Windows	2	08-Feb-26	09-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Windows	
DAM3-E-PS-A-0200	Aluminum Composite Panel	2	23-Feb-26	25-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Aluminum Comp	
DAM3-E-PS-A-0120	Doors	2	05-Feb-26	07-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Doors	
DAM3-E-PS-A-0020	PES -Steel Structure	2	25-Jan-26	26-Jan-26	19-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	PES -Steel Struc	
DAM3-E-PS-A-0190	Gypsum board	2	19-Feb-26	23-Feb-26	24-Feb-26 A	24-Feb-26 A	0.00	0.00	0.00	100%	100%	Gypsum board	
DAM3-E-PS-A-0050	Steel ladder	2	29-Jan-26	31-Jan-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	Steel ladder	
DAM3-E-PS-A-0140	Ceramic tiles	2	10-Feb-26	11-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	Ceramic tiles	
DAM3-E-PS-A-0180	Interni paint	2	17-Feb-26	19-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	Interni paint	
DAM3-E-PS-A-0170	Epoxy paint	2	15-Feb-26	16-Feb-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	Epoxy paint	
DAM3-E-PS-A-0150	Granite strip	2	12-Feb-26	14-Feb-26	03-May-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	Granite strip	
DAM3-E-PS-A-0060	Steel gratings	2	01-Feb-26	02-Feb-26	19-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	Steel gratings	
DAM3-E-PS-A-0230	Steel fence and gates	2	25-Feb-26	28-Feb-26	20-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	Steel fence a	
DAM3-E-PS-A-0070	Steel rails	2	03-Feb-26	04-Feb-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Steel rails	
DAM3-E-PS-A-0240	Identification sign; ID01 & ID02	2	01-Mar-26	02-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Identification	
MECHANICAL		98	27-Jan-26	09-Apr-26	24-Jan-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,	
DAM3-E-PS-M-0330	GRP tank	2	04-Apr-26	05-Apr-26	24-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%	GRP tank	
DAM3-E-PS-M-0250	Inline exhaust fans	2	23-Mar-26	24-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Inline exhaust fa	
DAM3-E-PS-M-0260	Wall propeller type exhaust fans	2	25-Mar-26	26-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Wall propeller typ	
DAM3-E-PS-M-0280	Fire fighting valves	2	30-Mar-26	31-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire fighting valve	
DAM3-E-PS-M-0340	Water supply valves	2	06-Apr-26	07-Apr-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Water supply valv	
DAM3-E-PS-M-0030	PPR pipes	2	29-Jan-26	31-Jan-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	PPR pipes	
DAM3-E-PS-M-0270	Fire pumps	2	28-Mar-26	29-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire pumps	
DAM3-E-PS-M-0320	Booster pump	2	01-Apr-26	02-Apr-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	Booster pump	
DAM3-E-PS-M-0070	U/G HDPE pipes	2	08-Feb-26	09-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	U/G HDPE pipes	
DAM3-E-PS-M-0090	Fire hose cabinet	2	10-Feb-26	11-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire hose cabinet	
DAM3-E-PS-M-0160	UPVC pipes	2	25-Feb-26	28-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes	
DAM3-E-PS-M-0200	Electric water heater	2	08-Mar-26	09-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Electric water hea	
DAM3-E-PS-M-0210	Western water closet	2	10-Mar-26	11-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Western water cl	
DAM3-E-PS-M-0240	Lavatory / wash basin	2	21-Mar-26	22-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Lavatory / wash b	
DAM3-E-PS-M-0190	Gully trap	2	05-Mar-26	07-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Gully trap	
DAM3-E-PS-M-0230	Toilet Fittings	2	15-Mar-26	16-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Toilet Fittings	
DAM3-E-PS-M-0010	Seamless black steel or ERW pipes	2	27-Jan-26	28-Jan-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Seamless black s	
DAM3-E-PS-M-0100	Automatic air release valve	2	12-Feb-26	14-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Automatic air rele	
DAM3-E-PS-M-0110	OS & Y gate valve	2	15-Feb-26	16-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	OS & Y gate valv	
DAM3-E-PS-M-0120	Fire alarm check valve	2	17-Feb-26	19-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm check	
DAM3-E-PS-M-0040	HVAC duct	2	01-Feb-26	02-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	HVAC duct	
DAM3-E-PS-M-0050	Flexible duct	2	03-Feb-26	04-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Flexible duct	
DAM3-E-PS-M-0140	Ball valve	2	19-Feb-26	23-Feb-26	11-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	Ball valve	

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PS-M-0350	Water tap	2	08-Apr-26	09-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0080	Warning tapes	2	08-Feb-26	09-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0170	Roof vent caps	2	01-Mar-26	02-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0180	Floor drain	2	03-Mar-26	04-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0220	Bib tap	2	12-Mar-26	14-Mar-26	04-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0060	Exhaust diffuser	2	05-Feb-26	07-Feb-26	27-May-26 A	27-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0150	Capped connection	2	23-Feb-26	25-Feb-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		85	29-Jan-26	05-Apr-26	07-Feb-26 A	20-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-E-0010	PVC conduits	2	29-Jan-26	31-Jan-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0180	Fire alarm system	2	12-Mar-26	14-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0240	Access control system	2	28-Mar-26	29-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0170	Wall mounted, duplex, telephone and data outlet	2	10-Mar-26	11-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0230	CCTV System	2	25-Mar-26	26-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0250	Solar system	2	30-Mar-26	31-Mar-26	24-Feb-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0120	Suspended High Bay LED lights	2	25-Feb-26	28-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0130	Flood lights	2	01-Mar-26	02-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0140	Recessed mounted LED downlight	2	03-Mar-26	04-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0150	LED Emergency Lights wall mounted	2	05-Mar-26	07-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0160	LED Emergency Exit Light	2	08-Mar-26	09-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0200	Street Lighting poles	1	15-Mar-26	16-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0220	Surface mounted lights	2	23-Mar-26	24-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0050	Wiring devices	2	08-Feb-26	09-Feb-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0030	Cable Tray	2	03-Feb-26	04-Feb-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0070	Low Voltage cables	2	12-Feb-26	14-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0020	Wires	2	01-Feb-26	02-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0040	Grounding system	2	05-Feb-26	07-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0110	Disconnect switches	2	23-Feb-26	25-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0080	Main distribution board (MDB)	2	15-Feb-26	16-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0210	Distribution board for pump room	1	21-Mar-26	22-Mar-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0090	Lighting panel board	2	17-Feb-26	19-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0100	PP-AC panel	2	19-Feb-26	23-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0060	HDPE ducts	2	10-Feb-26	11-Feb-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0260	Main program system & controller	2	01-Apr-26	02-Apr-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0270	PLC controller	2	04-Apr-26	05-Apr-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
EXTERNAL		14	25-Mar-26	09-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-EX-0010	Asphalt works	2	25-Mar-26	26-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0020	Concrete parking bumper	2	28-Mar-26	29-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0030	Road markings	2	30-Mar-26	31-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0040	Road signs	2	01-Apr-26	02-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0060	Interlock tiles	2	04-Apr-26	05-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0070	Curbstones	2	06-Apr-26	07-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0080	Gravel bedding	2	08-Apr-26	09-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
ENVIRONMETAL		75	29-Jan-26	16-Feb-26	03-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-EN-0080	UPVC pipes	2	15-Feb-26	16-Feb-26	03-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0010	HDPE pipes for fire system	2	29-Jan-26	31-Jan-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0030	HDPE pipes for water supply system	2	03-Feb-26	04-Feb-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0020	Directly buried gate valve for fire system	2	01-Feb-26	02-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0040	Directly buried gate valve for water system	2	05-Feb-26	07-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0050	Air valve	2	08-Feb-26	09-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%

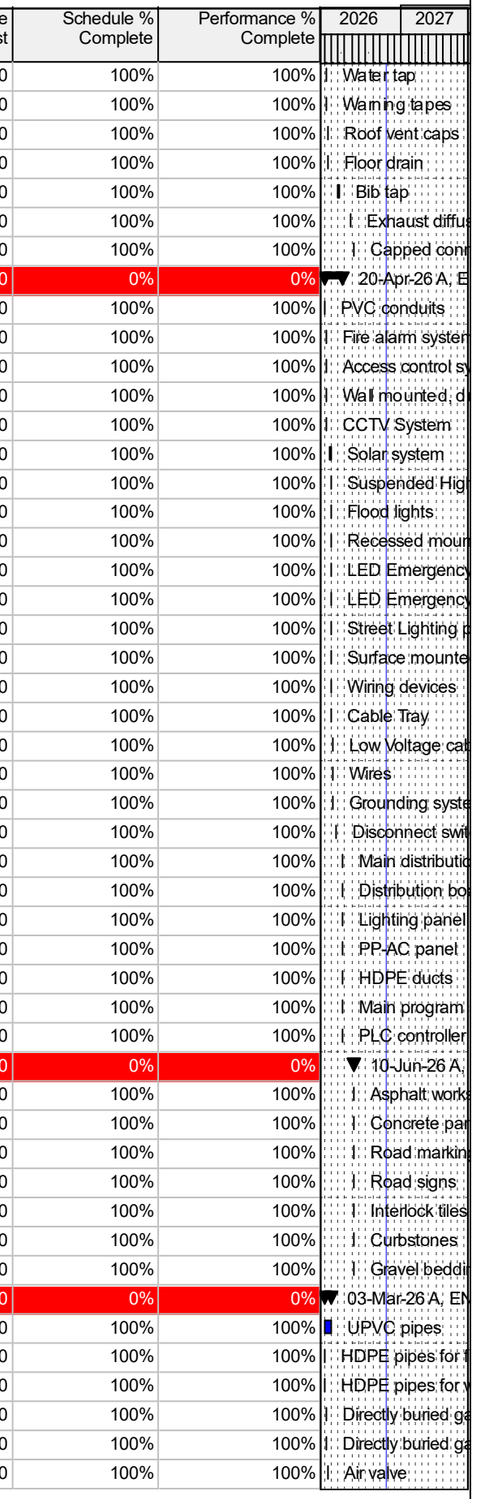

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PS-EN-0060	Washout valve	2	10-Feb-26	11-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0070	Gate valve	2	12-Feb-26	14-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		138	25-Jan-26	12-Apr-26	15-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
STRUCTURAL		34	25-Jan-26	04-Feb-26	15-Jan-26 A	21-Jan-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-C-0010	Anti termite	2	25-Jan-26	26-Jan-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0020	Concrete mix	2	27-Jan-26	28-Jan-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0040	Bitumen paint	2	01-Feb-26	02-Feb-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0050	Rebar	2	03-Feb-26	04-Feb-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0030	Polyethylene sheet	5	29-Jan-26	31-Jan-26	19-Jan-26 A	21-Jan-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		104	27-Jan-26	04-Mar-26	08-Feb-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-A-0040	Concrete masonry unit (CMU)	2	29-Jan-26	31-Jan-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0130	Windows	2	10-Feb-26	11-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0200	Aluminum Composite Panel	2	25-Feb-26	28-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0120	Doors	2	08-Feb-26	09-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0050	Steel ladder	2	01-Feb-26	02-Feb-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0020	PES -Steel Structure	2	27-Jan-26	28-Jan-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0190	Gypsum board	2	23-Feb-26	25-Feb-26	24-Feb-26 A	12-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0140	Ceramic tiles	2	12-Feb-26	14-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0180	Interni paint	2	19-Feb-26	23-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0170	Epoxy paint	2	17-Feb-26	19-Feb-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0150	Granite strip	2	15-Feb-26	16-Feb-26	03-May-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0060	Steel gratings	2	03-Feb-26	04-Feb-26	19-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0230	Steel fence and gates	2	01-Mar-26	02-Mar-26	20-May-26 A	21-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0070	Steel rails	2	05-Feb-26	07-Feb-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0240	Identification sign; ID01 & ID02	2	03-Mar-26	04-Mar-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		98	29-Jan-26	12-Apr-26	24-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-M-0340	GRP tank	2	06-Apr-26	07-Apr-26	24-Jan-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0250	Inline exhaust fans	2	25-Mar-26	26-Mar-26	02-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0260	Wall propeller type exhaust fans	2	28-Mar-26	29-Mar-26	02-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0280	Fire fighting valves	2	01-Apr-26	02-Apr-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0350	Water supply valves	2	08-Apr-26	09-Apr-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0030	PPR pipes	2	01-Feb-26	02-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0270	Fire pumps	2	30-Mar-26	31-Mar-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0330	Booster pump	2	04-Apr-26	05-Apr-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0070	U/G HDPE pipes	2	10-Feb-26	11-Feb-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0090	Fire hose cabinet	2	12-Feb-26	14-Feb-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0160	UPVC pipes	2	01-Mar-26	02-Mar-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0200	Electric water heater	2	10-Mar-26	11-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0210	Western water closet	2	12-Mar-26	14-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0240	Lavatory / wash basin	2	23-Mar-26	24-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0190	Gully trap	2	08-Mar-26	09-Mar-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0230	Toilet Fittings	2	21-Mar-26	22-Mar-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0010	Seamless black steel or ERW pipes	2	29-Jan-26	31-Jan-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0100	Automatic air release valve	2	15-Feb-26	16-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0110	OS & Y gate valve	2	17-Feb-26	19-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0120	Fire alarm check valve	2	19-Feb-26	23-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0040	HVAC duct	2	03-Feb-26	04-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0050	Flexible duct	2	05-Feb-26	07-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0140	Ball valve	2	23-Feb-26	25-Feb-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%

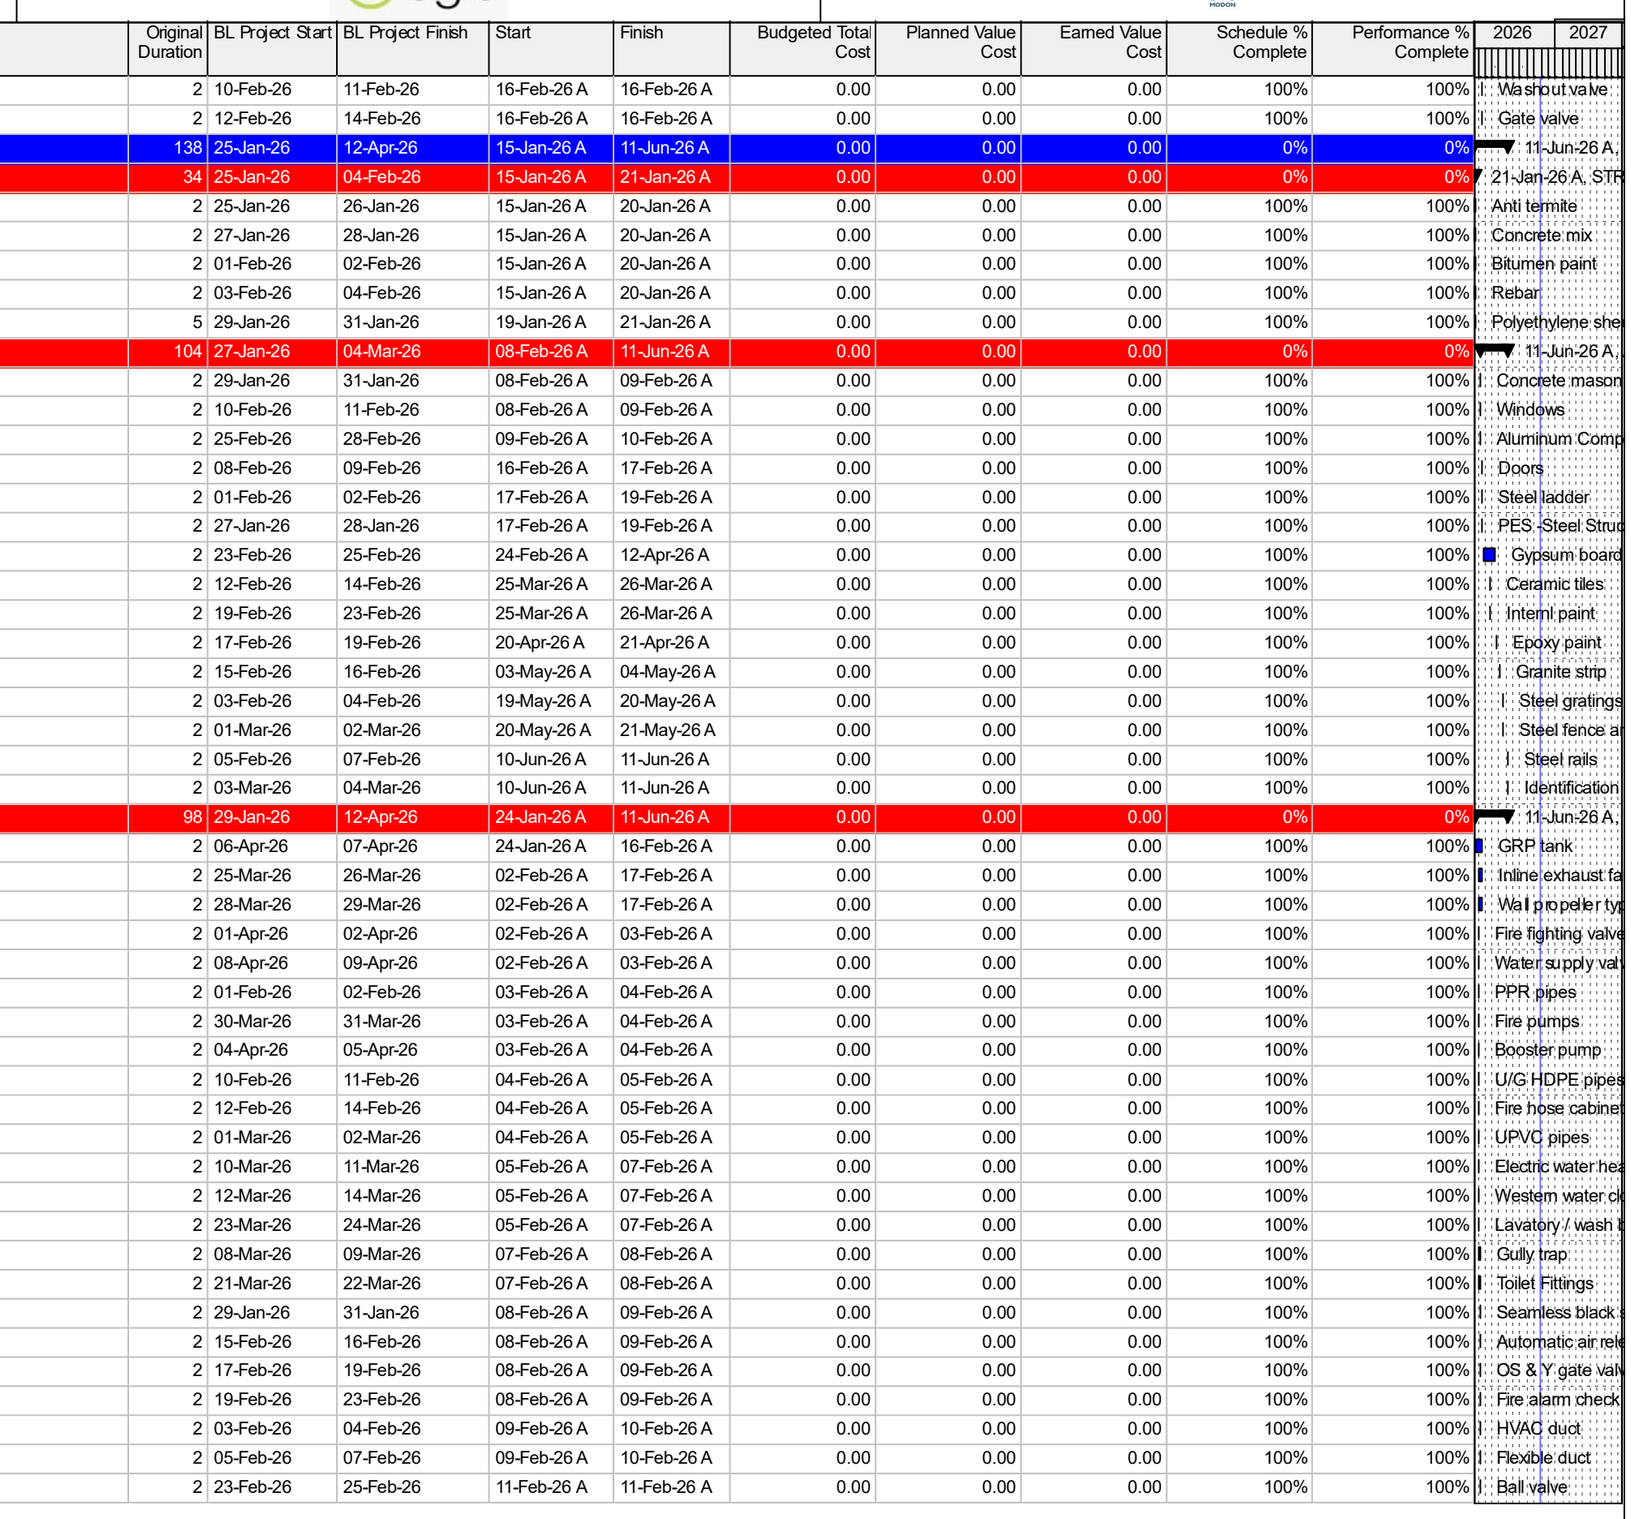

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-PA-M-0320	Water tap	2	11-Apr-26	12-Apr-26	11-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	Water tap
DAM3-E-PA-M-0080	Warning tapes	2	10-Feb-26	11-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%	Warning tapes
DAM3-E-PA-M-0170	Roof vent caps	2	03-Mar-26	04-Mar-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Roof vent caps
DAM3-E-PA-M-0180	Floor drain	2	05-Mar-26	07-Mar-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Floor drain
DAM3-E-PA-M-0220	Bib tap	2	15-Mar-26	16-Mar-26	06-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%	Bib tap
DAM3-E-PA-M-0060	Exhaust diffuser	2	08-Feb-26	09-Feb-26	27-May-26 A	28-May-26 A	0.00	0.00	0.00	100%	100%	Exhaust diffu
DAM3-E-PA-M-0150	Capped connection	2	25-Feb-26	28-Feb-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Capped conn
ELECTRICAL		85	01-Feb-26	07-Apr-26	07-Feb-26 A	21-Apr-26 A	0.00	0.00	0.00	0%	0%	21-Apr-26 A, E
DAM3-E-PA-E-0010	PVC conduits	2	01-Feb-26	02-Feb-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	PVC conduits
DAM3-E-PA-E-0180	Fire alarm system	2	15-Mar-26	16-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm syster
DAM3-E-PA-E-0240	Access control system	2	30-Mar-26	31-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Access control sy
DAM3-E-PA-E-0170	Wall mounted, duplex, telephone and data outlet	2	12-Mar-26	14-Mar-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	Wall mounted, d
DAM3-E-PA-E-0230	CCTV System	2	28-Mar-26	29-Mar-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	CCTV System
DAM3-E-PA-E-0250	Solar system	2	01-Apr-26	02-Apr-26	24-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Solar system
DAM3-E-PA-E-0120	Suspended High Bay LED lights	2	01-Mar-26	02-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Suspended Hig
DAM3-E-PA-E-0130	Flood lights	2	03-Mar-26	04-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Flood lights
DAM3-E-PA-E-0140	Recessed mounted LED downlight	2	05-Mar-26	07-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Recessed moun
DAM3-E-PA-E-0150	LED Emergency Lights wall mounted	2	08-Mar-26	09-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency
DAM3-E-PA-E-0160	LED Emergency Exit Light	2	10-Mar-26	11-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency
DAM3-E-PA-E-0200	Street Lighting poles	2	21-Mar-26	22-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Street Lighting p
DAM3-E-PA-E-0220	Surface mounted lights	2	25-Mar-26	26-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	Surface mounte
DAM3-E-PA-E-0050	Wiring devices	2	10-Feb-26	11-Feb-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Wiring devices
DAM3-E-PA-E-0030	Cable Tray	2	05-Feb-26	07-Feb-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Cable Tray
DAM3-E-PA-E-0070	Low Voltage cables	2	15-Feb-26	16-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	Low Voltage ca
DAM3-E-PA-E-0020	Wires	2	03-Feb-26	04-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	Wires
DAM3-E-PA-E-0040	Grounding system	2	08-Feb-26	09-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	Grounding syste
DAM3-E-PA-E-0110	Disconnect switches	2	25-Feb-26	28-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	Disconnect swi
DAM3-E-PA-E-0080	Main distribution board (MDB)	2	17-Feb-26	19-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	Main distributio
DAM3-E-PA-E-0210	Distribution board for pump room	2	23-Mar-26	24-Mar-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	Distribution bo
DAM3-E-PA-E-0090	Lighting panel board	2	19-Feb-26	23-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	Lighting panel
DAM3-E-PA-E-0100	PP-AC panel	2	23-Feb-26	25-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	PP-AC panel
DAM3-E-PA-E-0060	HDPE ducts	2	12-Feb-26	14-Feb-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	HDPE ducts
DAM3-E-PA-E-0260	Main program system & controller	2	04-Apr-26	05-Apr-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	Main program
DAM3-E-PA-E-0270	PLC controller	2	06-Apr-26	07-Apr-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	PLC controller
EXTERNAL		14	28-Mar-26	12-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,
DAM3-E-PA-EX-0010	Asphalt works	2	28-Mar-26	29-Mar-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Asphalt works
DAM3-E-PA-EX-0020	Concrete parking bumper	2	30-Mar-26	31-Mar-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Concrete par
DAM3-E-PA-EX-0030	Road markings	2	01-Apr-26	02-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Road markin
DAM3-E-PA-EX-0040	Road signs	2	04-Apr-26	05-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Road signs
DAM3-E-PA-EX-0060	Interlock tiles	2	06-Apr-26	07-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Interlock tiles
DAM3-E-PA-EX-0070	Curbstones	2	08-Apr-26	09-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Curbstones
DAM3-E-PA-EX-0080	Gravel bedding	2	11-Apr-26	12-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Gravel beddi
ENVIRONMETAL		73	01-Feb-26	19-Feb-26	03-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	0%	0%	17-Feb-26 A, EN
DAM3-E-PA-EN-0080	UPVC pipes	2	17-Feb-26	19-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes
DAM3-E-PA-EN-0010	HDPE pipes for fire system	2	01-Feb-26	02-Feb-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for f
DAM3-E-PA-EN-0030	HDPE pipes for water supply system	2	05-Feb-26	07-Feb-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for v
DAM3-E-PA-EN-0020	Directly buried gate valve for fire system	2	03-Feb-26	04-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga
DAM3-E-PA-EN-0040	Directly buried gate valve for water system	2	08-Feb-26	09-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga
DAM3-E-PA-EN-0050	Air valve	2	10-Feb-26	11-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Air valve

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-PA-EN-0060	Washout valve	2	12-Feb-26	14-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Washout valve
DAM3-E-PA-EN-0070	Gate valve	2	15-Feb-26	16-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Gate valve
MATERIAL SUBMITTAL		108	27-Jan-26	20-Apr-26	15-Jan-26 A	14-Jun-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%	14-Jun-26 A,
PREPARATION AND SUBMITTAL		108	27-Jan-26	14-Apr-26	15-Jan-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
STRUCTURAL		10	27-Jan-26	07-Feb-26	15-Jan-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	14-Mar-26 A, ST
DAM3-E-MS-C-0020	Concrete mix	2	29-Jan-26	31-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Concrete mix
DAM3-E-MS-C-0030	Polyethylene sheet	2	01-Feb-26	02-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Polyethylene she
DAM3-E-MS-C-0040	Bitumen paint	2	03-Feb-26	04-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Bitumen paint
DAM3-E-MS-C-0050	Rebar	2	05-Feb-26	07-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Rebar
DAM3-E-MS-C-0010	Anti termite	2	27-Jan-26	28-Jan-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	Anti termite
ARCHITECTURAL		100	29-Jan-26	07-Mar-26	07-Feb-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
DAM3-E-MS-A-0030	Steel ladder	2	03-Feb-26	04-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Steel ladder
DAM3-E-MS-A-1700	PES -Steel Structure	2	29-Jan-26	31-Jan-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	PES -Steel Struc
DAM3-E-MS-A-0100	Doors	2	10-Feb-26	11-Feb-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Doors
DAM3-E-MS-A-0110	Windows	2	12-Feb-26	14-Feb-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Windows
DAM3-E-MS-A-1720	Aluminum Composite Panel	2	01-Mar-26	02-Mar-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Aluminum Comp
DAM3-E-MS-A-0160	Interni paint	2	23-Feb-26	25-Feb-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Interni paint
DAM3-E-MS-A-0120	Ceramic tiles	2	15-Feb-26	16-Feb-26	30-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	Ceramic tiles
DAM3-E-MS-A-0170	Gypsum board	2	25-Feb-26	28-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	Gypsum board
DAM3-E-MS-A-0020	Concrete masonry unit (CMU)	2	01-Feb-26	02-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Concrete mas
DAM3-E-MS-A-0150	Epoxy paint	2	19-Feb-26	23-Feb-26	29-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	Epoxy paint
DAM3-E-MS-A-0130	Granite strip	2	17-Feb-26	19-Feb-26	09-May-26 A	09-May-26 A	0.00	0.00	0.00	100%	100%	Granite strip
DAM3-E-MS-A-0040	Steel gratings	2	05-Feb-26	07-Feb-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	100%	100%	Steel gratings
DAM3-E-MS-A-1750	Steel fence and gates	2	03-Mar-26	04-Mar-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	100%	100%	Steel fence a
DAM3-E-MS-A-0050	Steel rails	2	08-Feb-26	09-Feb-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Steel rails
DAM3-E-MS-A-1760	Identification sign; ID01 & ID02	2	05-Mar-26	07-Mar-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Identification
MECHANICAL		98	01-Feb-26	14-Apr-26	05-Feb-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
DAM3-E-MS-M-0080	PPR pipes	2	03-Feb-26	04-Feb-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	PPR pipes
DAM3-E-MS-M-0250	Fire pumps	2	01-Apr-26	02-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire pumps
DAM3-E-MS-M-0310	Booster pump	2	06-Apr-26	07-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Booster pump
DAM3-E-MS-M-0010	U/G HDPE pipes	2	12-Feb-26	14-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	U/G HDPE pipes
DAM3-E-MS-M-0030	Fire hose cabinet	2	15-Feb-26	16-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire hose cabinet
DAM3-E-MS-M-0110	UPVC pipes	2	03-Mar-26	04-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes
DAM3-E-MS-M-0150	Electric water heater	2	12-Mar-26	14-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Electric water hea
DAM3-E-MS-M-0160	Western water closet	2	15-Mar-26	16-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Western water cl
DAM3-E-MS-M-0190	Lavatory / wash basin	2	25-Mar-26	26-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Lavatory / wash
DAM3-E-MS-M-0140	Gully trap	2	10-Mar-26	11-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Gully trap
DAM3-E-MS-M-0180	Toilet Fittings	2	23-Mar-26	24-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Toilet Fittings
DAM3-E-MS-M-0020	Seamless black steel or ERW pipes	2	01-Feb-26	02-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Seamless black s
DAM3-E-MS-M-0040	Automatic air release valve	2	17-Feb-26	19-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Automatic air rele
DAM3-E-MS-M-0050	OS & Y gate valve	2	19-Feb-26	23-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	OS & Y gate valv
DAM3-E-MS-M-0060	Fire alarm check valve	2	23-Feb-26	25-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm check
DAM3-E-MS-M-0270	Fire fighting valves	2	04-Apr-26	05-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire fighting valve
DAM3-E-MS-M-0330	Water supply valves	2	11-Apr-26	12-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Water supply val
DAM3-E-MS-M-0090	Ball valve	2	25-Feb-26	28-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	Ball valve
DAM3-E-MS-M-0170	Bib tap	2	21-Mar-26	22-Mar-26	14-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	Bib tap
DAM3-E-MS-M-3410	Water tap	2	13-Apr-26	14-Apr-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	Water tap
DAM3-E-MS-M-0120	Roof vent caps	2	05-Mar-26	07-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Roof vent caps
DAM3-E-MS-M-0130	Floor drain	2	08-Mar-26	09-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Floor drain

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-MS-M-0340	Warning tapes	2	12-Feb-26	14-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Warning tapes	
DAM3-E-MS-M-0320	GRP tank	2	08-Apr-26	09-Apr-26	02-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	GRP tank	
DAM3-E-MS-M-0220	HVAC duct	2	05-Feb-26	07-Feb-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	HVAC duct	
DAM3-E-MS-M-0230	Flexible duct	2	08-Feb-26	09-Feb-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Flexible duct	
DAM3-E-MS-M-0200	Inline exhaust fans	2	28-Mar-26	29-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	Inline exhaust f	
DAM3-E-MS-M-0210	Wall propeller type exhaust fans	2	30-Mar-26	31-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	Wall propeller ty	
DAM3-E-MS-M-0240	Exhaust diffuser	2	10-Feb-26	11-Feb-26	01-Jun-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	Exhaust diffu	
DAM3-E-MS-M-0100	Capped connection	2	01-Mar-26	02-Mar-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Capped conn	
ELECTRICAL		69	03-Feb-26	09-Apr-26	09-Feb-26 A	30-Apr-26 A	0.00	0.00	0.00	0%	0%	30-Apr-26 A, E	
DAM3-E-MS-E-0040	PVC conduits	2	03-Feb-26	04-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	PVC conduits	
DAM3-E-MS-E-0130	Fire alarm system	2	21-Mar-26	22-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm syster	
DAM3-E-MS-E-0240	Access control system	2	01-Apr-26	02-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%	Access control sy	
DAM3-E-MS-E-0060	Suspended High Bay LED lights	2	03-Mar-26	04-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Suspended Hig	
DAM3-E-MS-E-0070	Flood lights	2	05-Mar-26	07-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Flood lights	
DAM3-E-MS-E-0080	Recessed mounted LED downlight	2	08-Mar-26	09-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Recessed moun	
DAM3-E-MS-E-0090	LED Emergency Lights wall mounted	2	10-Mar-26	11-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency	
DAM3-E-MS-E-0100	LED Emergency Exit Light	2	12-Mar-26	14-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency	
DAM3-E-MS-E-0190	Surface mounted lights	2	28-Mar-26	29-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Surface mounte	
DAM3-E-MS-E-0250	Solar system	2	04-Apr-26	05-Apr-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Solar system	
DAM3-E-MS-E-0170	Street Lighting poles	2	23-Mar-26	24-Mar-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Street Lighting p	
DAM3-E-MS-E-0140	Wiring devices	2	12-Feb-26	14-Feb-26	07-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	Wiring devices	
DAM3-E-MS-E-210	Cable Tray	2	08-Feb-26	09-Feb-26	07-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	Cable Tray	
DAM3-E-MS-E-0010	Low Voltage cables	2	17-Feb-26	19-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Low Voltage ca	
DAM3-E-MS-E-0050	Wires	2	05-Feb-26	07-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Wires	
DAM3-E-MS-E-0120	Grounding system	2	10-Feb-26	11-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Grounding syste	
DAM3-E-MS-E-0230	CCTV System	2	30-Mar-26	31-Mar-26	28-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	CCTV System	
DAM3-E-MS-E-0030	Disconnect switches	2	01-Mar-26	02-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Disconnect swi	
DAM3-E-MS-E-0110	Wall mounted, duplex, telephone and data outlet	1	15-Mar-26	16-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Wall mounted,	
DAM3-E-MS-E-0020	Main distribution board (MDB)	2	19-Feb-26	23-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Main distributio	
DAM3-E-MS-E-0180	Distribution board for pump room	2	25-Mar-26	26-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Distribution bo	
DAM3-E-MS-E-190	Lighting panel board	2	23-Feb-26	25-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Lighting panel	
DAM3-E-MS-E-200	PP-AC panel	2	25-Feb-26	28-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	PP-AC panel	
DAM3-E-MS-E-0160	HDPE ducts	2	15-Feb-26	16-Feb-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	HDPE ducts	
DAM3-E-MS-E-0260	Main program system & controller	2	06-Apr-26	07-Apr-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	Main program	
DAM3-E-MS-E-0270	PLC controller	2	08-Apr-26	09-Apr-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	PLC controller	
EXTERNAL		14	30-Mar-26	14-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%	11-Jun-26 A,	
DAM3-E-MS-EX-0010	Asphalt works	2	30-Mar-26	31-Mar-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Asphalt work	
DAM3-E-MS-EX-0020	Concrete parking bumper	2	01-Apr-26	02-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Concrete par	
DAM3-E-MS-EX-0030	Road markings	2	04-Apr-26	05-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Road markin	
DAM3-E-MS-EX-0040	Road signs	2	06-Apr-26	07-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Road signs	
DAM3-E-MS-EX-0060	Interlock tiles	2	08-Apr-26	09-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Interlock tiles	
DAM3-E-MS-EX-0070	Curbstones	2	11-Apr-26	12-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Curbstones	
DAM3-E-MS-EX-0080	Gravel bedding	2	13-Apr-26	14-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Gravel beddi	
ENVIRONMETAL		55	03-Feb-26	23-Feb-26	08-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	0%	0%	18-Feb-26 A, EN	
DAM3-E-MS-EN-0010	HDPE pipes for fire system	2	03-Feb-26	04-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for	
DAM3-E-MS-EN-0030	HDPE pipes for water supply system	2	08-Feb-26	09-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for	
DAM3-E-MS-EN-0080	UPVC pipes	2	19-Feb-26	23-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes	
DAM3-E-MS-EN-0020	Directly buried gate valve for fire system	2	05-Feb-26	07-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga	
DAM3-E-MS-EN-0040	Directly buried gate valve for water system	2	10-Feb-26	11-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga	

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MS-EN-0050	Air valve	2	12-Feb-26	14-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MS-EN-0060	Washout valve	2	15-Feb-26	16-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MS-EN-0070	Gate valve	2	17-Feb-26	19-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		104	29-Jan-26	20-Apr-26	20-Jan-26 A	14-Jun-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
STRUCTURAL		20	29-Jan-26	12-Feb-26	20-Jan-26 A	07-Apr-26 A	481,112.68	481,112.68	481,112.68	100%	100%
DAM3-E-MA-C-0020	Concrete mix	5	01-Feb-26	05-Feb-26	20-Jan-26 A	20-Jan-26 A	251,751.70	251,751.70	251,751.70	100%	100%
DAM3-E-MA-C-0030	Polyethylene sheet	5	03-Feb-26	08-Feb-26	22-Jan-26 A	29-Jan-26 A	13,035.98	13,035.98	13,035.98	100%	100%
DAM3-E-MA-C-0040	Bitumen paint	5	05-Feb-26	10-Feb-26	22-Jan-26 A	29-Jan-26 A	28,944.10	28,944.10	28,944.10	100%	100%
DAM3-E-MA-C-0050	Rebar	5	08-Feb-26	12-Feb-26	22-Jan-26 A	29-Jan-26 A	167,834.46	167,834.46	167,834.46	100%	100%
DAM3-E-MA-C-0010	Anti termite	5	29-Jan-26	03-Feb-26	14-Mar-26 A	07-Apr-26 A	19,546.44	19,546.44	19,546.44	100%	100%
ARCHITECTURAL		93	03-Feb-26	12-Mar-26	07-Feb-26 A	14-Jun-26 A	1,232,403.28	1,232,403.28	1,232,403.28	100%	100%
DAM3-E-MA-A-0030	Steel ladder	5	05-Feb-26	10-Feb-26	07-Feb-26 A	10-Feb-26 A	4,846.16	4,846.16	4,846.16	100%	100%
DAM3-E-MA-A-1700	PES -Steel Structure	5	12-Feb-26	17-Feb-26	07-Feb-26 A	17-Mar-26 A	799,834.94	799,834.94	799,834.94	100%	100%
DAM3-E-MA-A-0100	Doors	5	12-Feb-26	17-Feb-26	19-Feb-26 A	25-Feb-26 A	75,386.56	75,386.56	75,386.56	100%	100%
DAM3-E-MA-A-0110	Windows	5	15-Feb-26	21-Feb-26	19-Feb-26 A	25-Feb-26 A	52,525.19	52,525.19	52,525.19	100%	100%
DAM3-E-MA-A-0160	Interni paint	5	25-Feb-26	03-Mar-26	29-Mar-26 A	03-May-26 A	21,754.04	21,754.04	21,754.04	100%	100%
DAM3-E-MA-A-0120	Ceramic tiles	5	17-Feb-26	24-Feb-26	30-Mar-26 A	04-May-26 A	36,151.26	36,151.26	36,151.26	100%	100%
DAM3-E-MA-A-0170	Gypsum board	5	01-Mar-26	05-Mar-26	19-Apr-26 A	14-Jun-26 A	23,046.95	23,046.95	23,046.95	100%	100%
DAM3-E-MA-A-0150	Epoxy paint	5	23-Feb-26	01-Mar-26	21-Apr-26 A	26-Apr-26 A	56,848.54	56,848.54	56,848.54	100%	100%
DAM3-E-MA-A-1720	Aluminum Composite Panel	5	03-Mar-26	08-Mar-26	21-Apr-26 A	26-Apr-26 A	86,631.78	86,631.78	86,631.78	100%	100%
DAM3-E-MA-A-0020	Concrete masonry unit (CMU)	5	03-Feb-26	08-Feb-26	26-Apr-26 A	29-Apr-26 A	62,820.36	62,820.36	62,820.36	100%	100%
DAM3-E-MA-A-0130	Granite strip	5	19-Feb-26	26-Feb-26	09-May-26 A	17-May-26 A	330.55	330.55	330.55	100%	100%
DAM3-E-MA-A-0040	Steel gratings	5	08-Feb-26	12-Feb-26	21-May-26 A	24-May-26 A	3,179.40	3,179.40	3,179.40	100%	100%
DAM3-E-MA-A-1750	Steel fence and gates	5	05-Mar-26	10-Mar-26	23-May-26 A	25-May-26 A	3,548.60	3,548.60	3,548.60	100%	100%
DAM3-E-MA-A-1760	Identification sign; ID01 & ID02	5	08-Mar-26	12-Mar-26	08-Jun-26 A	13-Jun-26 A	4,743.41	4,743.41	4,743.41	100%	100%
DAM3-E-MA-A-0050	Steel rails	5	10-Feb-26	15-Feb-26	13-Jun-26 A	14-Jun-26 A	755.54	755.54	755.54	100%	100%
MECHANICAL		101	03-Feb-26	20-Apr-26	05-Feb-26 A	14-Jun-26 A	303,435.06	303,435.06	303,435.06	100%	100%
DAM3-E-MA-M-0080	PPR pipes	5	05-Feb-26	10-Feb-26	05-Feb-26 A	11-May-26 A	11,485.19	11,485.19	11,485.19	100%	100%
DAM3-E-MA-M-0250	Fire pumps	5	04-Apr-26	08-Apr-26	05-Feb-26 A	24-Feb-26 A	15,505.34	15,505.34	15,505.34	100%	100%
DAM3-E-MA-M-0310	Booster pump	5	08-Apr-26	13-Apr-26	05-Feb-26 A	11-Feb-26 A	1,938.67	1,938.67	1,938.67	100%	100%
DAM3-E-MA-M-0010	U/G HDPE pipes	5	15-Feb-26	21-Feb-26	07-Feb-26 A	08-Mar-26 A	7,495.73	7,495.73	7,495.73	100%	100%
DAM3-E-MA-M-0030	Fire hose cabinet	5	17-Feb-26	24-Feb-26	07-Feb-26 A	01-Mar-26 A	7,466.16	7,466.16	7,466.16	100%	100%
DAM3-E-MA-M-0110	UPVC pipes	5	05-Mar-26	10-Mar-26	07-Feb-26 A	12-Apr-26 A	19,003.97	19,003.97	19,003.97	100%	100%
DAM3-E-MA-M-0150	Electric water heater	5	15-Mar-26	23-Mar-26	08-Feb-26 A	01-Mar-26 A	896.17	896.17	896.17	100%	100%
DAM3-E-MA-M-0160	Western water closet	5	21-Mar-26	25-Mar-26	08-Feb-26 A	17-May-26 A	9,812.19	9,812.19	9,812.19	100%	100%
DAM3-E-MA-M-0190	Lavatory / wash basin	5	28-Mar-26	01-Apr-26	08-Feb-26 A	17-May-26 A	10,548.52	10,548.52	10,548.52	100%	100%
DAM3-E-MA-M-0140	Gully trap	5	12-Mar-26	21-Mar-26	09-Feb-26 A	26-Feb-26 A	2,397.38	2,397.38	2,397.38	100%	100%
DAM3-E-MA-M-0180	Toilet Fittings	5	25-Mar-26	30-Mar-26	09-Feb-26 A	01-Jun-26 A	11,319.13	11,319.13	11,319.13	100%	100%
DAM3-E-MA-M-0020	Seamless black steel or ERW pipes	5	03-Feb-26	08-Feb-26	10-Feb-26 A	26-Feb-26 A	35,657.12	35,657.12	35,657.12	100%	100%
DAM3-E-MA-M-0040	Automatic air release valve	5	19-Feb-26	26-Feb-26	10-Feb-26 A	26-Feb-26 A	265.43	265.43	265.43	100%	100%
DAM3-E-MA-M-0050	OS & Y gate valve	5	23-Feb-26	01-Mar-26	10-Feb-26 A	26-Feb-26 A	1,744.73	1,744.73	1,744.73	100%	100%
DAM3-E-MA-M-0060	Fire alarm check valve	5	25-Feb-26	03-Mar-26	10-Feb-26 A	26-Feb-26 A	3,998.51	3,998.51	3,998.51	100%	100%
DAM3-E-MA-M-0270	Fire fighting valves	5	06-Apr-26	11-Apr-26	10-Feb-26 A	26-Mar-26 A	1,332.84	1,332.84	1,332.84	100%	100%
DAM3-E-MA-M-0330	Water supply valves	5	13-Apr-26	18-Apr-26	10-Feb-26 A	26-Mar-26 A	467.18	467.18	467.18	100%	100%
DAM3-E-MA-M-0090	Ball valve	5	01-Mar-26	05-Mar-26	14-Feb-26 A	16-Apr-26 A	2,134.82	2,134.82	2,134.82	100%	100%
DAM3-E-MA-M-0170	Bib tap	5	23-Mar-26	28-Mar-26	14-Feb-26 A	16-Apr-26 A	936.14	936.14	936.14	100%	100%
DAM3-E-MA-M-3410	Water tap	5	15-Apr-26	20-Apr-26	14-Feb-26 A	16-Apr-26 A	1,415.62	1,415.62	1,415.62	100%	100%
DAM3-E-MA-M-0120	Roof vent caps	5	08-Mar-26	12-Mar-26	16-Feb-26 A	14-Jun-26 A	456.64	456.64	456.64	100%	100%
DAM3-E-MA-M-0130	Floor drain	5	10-Mar-26	15-Mar-26	16-Feb-26 A	04-Jun-26 A	11,113.99	11,113.99	11,113.99	100%	100%

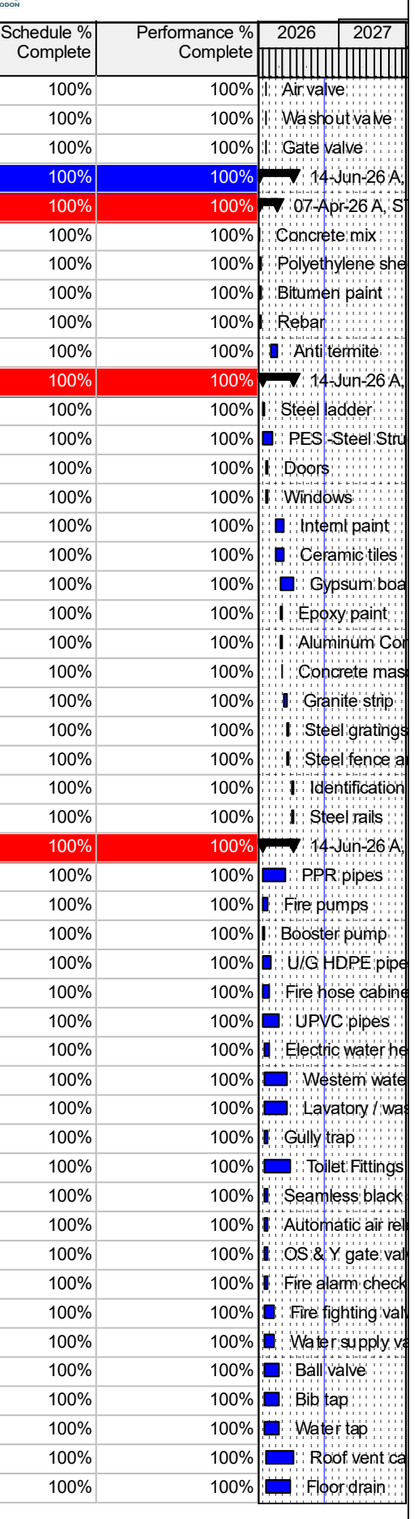

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MA-M-0340	Warning tapes	5	15-Feb-26	21-Feb-26	16-Feb-26 A	03-Mar-26 A	2,111.55	2,111.55	2,111.55	100%	100%
DAM3-E-MA-M-0320	GRP tank	5	11-Apr-26	15-Apr-26	02-Mar-26 A	07-Apr-26 A	31,477.96	31,477.96	31,477.96	100%	100%
DAM3-E-MA-M-0220	HVAC duct	5	08-Feb-26	12-Feb-26	04-Mar-26 A	12-May-26 A	73,629.07	73,629.07	73,629.07	100%	100%
DAM3-E-MA-M-0230	Flexible duct	5	10-Feb-26	15-Feb-26	04-Mar-26 A	12-May-26 A	10,444.45	10,444.45	10,444.45	100%	100%
DAM3-E-MA-M-0200	Inline exhaust fans	5	30-Mar-26	04-Apr-26	18-Mar-26 A	19-Apr-26 A	4,121.24	4,121.24	4,121.24	100%	100%
DAM3-E-MA-M-0210	Wall propeller type exhaust fans	5	01-Apr-26	06-Apr-26	18-Mar-26 A	19-Apr-26 A	23,066.33	23,066.33	23,066.33	100%	100%
DAM3-E-MA-M-0240	Exhaust diffuser	5	12-Feb-26	17-Feb-26	01-Jun-26 A	04-Jun-26 A	1,056.00	1,056.00	1,056.00	100%	100%
DAM3-E-MA-M-0100	Capped connection	5	03-Mar-26	08-Mar-26	13-Jun-26 A	14-Jun-26 A	136.99	136.99	136.99	100%	100%
ELECTRICAL		74	05-Feb-26	15-Apr-26	09-Feb-26 A	14-Jun-26 A	472,829.48	472,829.48	472,829.48	100%	100%
DAM3-E-MA-E-0040	PVC conduits	5	05-Feb-26	10-Feb-26	09-Feb-26 A	01-Mar-26 A	2,360.80	2,360.80	2,360.80	100%	100%
DAM3-E-MA-E-0130	Fire alarm system	5	23-Mar-26	28-Mar-26	11-Feb-26 A	30-Mar-26 A	41,920.11	41,920.11	41,920.11	100%	100%
DAM3-E-MA-E-0240	Access control system	5	04-Apr-26	08-Apr-26	11-Feb-26 A	07-Mar-26 A	13,602.34	13,602.34	13,602.34	100%	100%
DAM3-E-MA-E-0060	Suspended High Bay LED lights	5	05-Mar-26	10-Mar-26	03-Mar-26 A	07-Mar-26 A	14,938.02	14,938.02	14,938.02	100%	100%
DAM3-E-MA-E-0070	Flood lights	5	08-Mar-26	12-Mar-26	03-Mar-26 A	07-Mar-26 A	2,268.18	2,268.18	2,268.18	100%	100%
DAM3-E-MA-E-0080	Recessed mounted LED downlight	5	10-Mar-26	15-Mar-26	03-Mar-26 A	07-Mar-26 A	20,081.13	20,081.13	20,081.13	100%	100%
DAM3-E-MA-E-0090	LED Emergency Lights wall mounted	5	12-Mar-26	21-Mar-26	03-Mar-26 A	07-Mar-26 A	4,144.06	4,144.06	4,144.06	100%	100%
DAM3-E-MA-E-0100	LED Emergency Exit Light	5	15-Mar-26	23-Mar-26	03-Mar-26 A	07-Mar-26 A	1,145.13	1,145.13	1,145.13	100%	100%
DAM3-E-MA-E-0190	Surface mounted lights	5	30-Mar-26	04-Apr-26	03-Mar-26 A	07-Mar-26 A	11,068.82	11,068.82	11,068.82	100%	100%
DAM3-E-MA-E-0250	Solar system	4	06-Apr-26	11-Apr-26	03-Mar-26 A	25-Apr-26 A	124,744.29	124,744.29	124,744.29	100%	100%
DAM3-E-MA-E-0170	Street Lighting poles	4	25-Mar-26	30-Mar-26	04-Mar-26 A	20-May-26 A	10,525.31	10,525.31	10,525.31	100%	100%
DAM3-E-MA-E-0140	Wiring devices	5	15-Feb-26	21-Feb-26	07-Mar-26 A	08-Mar-26 A	9,962.15	9,962.15	9,962.15	100%	100%
DAM3-E-MA-E-210	Cable Tray	5	10-Feb-26	15-Feb-26	07-Mar-26 A	08-Mar-26 A	159.57	159.57	159.57	100%	100%
DAM3-E-MA-E-0010	Low Voltage cables	5	19-Feb-26	26-Feb-26	16-Mar-26 A	29-Mar-26 A	44,855.17	44,855.17	44,855.17	100%	100%
DAM3-E-MA-E-0050	Wires	5	08-Feb-26	12-Feb-26	16-Mar-26 A	29-Mar-26 A	1,106.91	1,106.91	1,106.91	100%	100%
DAM3-E-MA-E-0120	Grounding system	5	12-Feb-26	17-Feb-26	16-Mar-26 A	29-Mar-26 A	9,771.19	9,771.19	9,771.19	100%	100%
DAM3-E-MA-E-0230	CCTV System	4	01-Apr-26	06-Apr-26	28-Mar-26 A	13-Apr-26 A	37,604.85	37,604.85	37,604.85	100%	100%
DAM3-E-MA-E-0030	Disconnect switches	5	03-Mar-26	08-Mar-26	29-Mar-26 A	14-Jun-26 A	15,086.41	15,086.41	15,086.41	100%	100%
DAM3-E-MA-E-0110	Wall mounted, duplex, telephone and data outlet	4	21-Mar-26	25-Mar-26	29-Mar-26 A	13-Apr-26 A	13,294.12	13,294.12	13,294.12	100%	100%
DAM3-E-MA-E-0020	Main distribution board (MDB)	5	23-Feb-26	01-Mar-26	26-Apr-26 A	12-May-26 A	15,994.03	15,994.03	15,994.03	100%	100%
DAM3-E-MA-E-0180	Distribution board for pump room	4	28-Mar-26	01-Apr-26	26-Apr-26 A	12-May-26 A	11,002.71	11,002.71	11,002.71	100%	100%
DAM3-E-MA-E-190	Lighting panel board	5	25-Feb-26	03-Mar-26	26-Apr-26 A	12-May-26 A	9,064.43	9,064.43	9,064.43	100%	100%
DAM3-E-MA-E-200	PP-AC panel	5	01-Mar-26	05-Mar-26	26-Apr-26 A	12-May-26 A	10,662.68	10,662.68	10,662.68	100%	100%
DAM3-E-MA-E-0160	HDPE ducts	5	17-Feb-26	24-Feb-26	30-Apr-26 A	03-May-26 A	26,402.96	26,402.96	26,402.96	100%	100%
DAM3-E-MA-E-0260	Main program system & controller	5	08-Apr-26	13-Apr-26	30-Apr-26 A	12-May-26 A	12,578.11	12,578.11	12,578.11	100%	100%
DAM3-E-MA-E-0270	PLC controller	5	11-Apr-26	15-Apr-26	30-Apr-26 A	12-May-26 A	8,486.00	8,486.00	8,486.00	100%	100%
EXTERNAL		29	01-Apr-26	20-Apr-26	11-Jun-26 A	13-Jun-26 A	332,383.67	332,383.67	332,383.67	100%	100%
DAM3-E-MA-EX-0010	Asphalt works	5	01-Apr-26	06-Apr-26	11-Jun-26 A	13-Jun-26 A	280,347.76	280,347.76	280,347.76	100%	100%
DAM3-E-MA-EX-0020	Concrete parking bumper	5	04-Apr-26	08-Apr-26	11-Jun-26 A	13-Jun-26 A	1,433.72	1,433.72	1,433.72	100%	100%
DAM3-E-MA-EX-0030	Road markings	5	06-Apr-26	11-Apr-26	11-Jun-26 A	13-Jun-26 A	1,696.34	1,696.34	1,696.34	100%	100%
DAM3-E-MA-EX-0040	Road signs	5	08-Apr-26	13-Apr-26	11-Jun-26 A	13-Jun-26 A	4,654.29	4,654.29	4,654.29	100%	100%
DAM3-E-MA-EX-0060	Interlock tiles	5	11-Apr-26	15-Apr-26	11-Jun-26 A	13-Jun-26 A	21,297.02	21,297.02	21,297.02	100%	100%
DAM3-E-MA-EX-0070	Curbstones	5	13-Apr-26	18-Apr-26	11-Jun-26 A	13-Jun-26 A	13,036.86	13,036.86	13,036.86	100%	100%
DAM3-E-MA-EX-0080	Gravel bedding	5	15-Apr-26	20-Apr-26	11-Jun-26 A	13-Jun-26 A	9,917.68	9,917.68	9,917.68	100%	100%
ENVIRONMETAL		59	05-Feb-26	01-Mar-26	08-Feb-26 A	14-Jun-26 A	57,731.58	57,731.58	57,731.58	100%	100%
DAM3-E-MA-EN-0010	HDPE pipes for fire system	5	05-Feb-26	10-Feb-26	08-Feb-26 A	26-Feb-26 A	21,745.93	21,745.93	21,745.93	100%	100%
DAM3-E-MA-EN-0030	HDPE pipes for water supply system	5	10-Feb-26	15-Feb-26	08-Feb-26 A	26-Feb-26 A	1,598.26	1,598.26	1,598.26	100%	100%
DAM3-E-MA-EN-0080	UPVC pipes	5	23-Feb-26	01-Mar-26	08-Feb-26 A	26-Feb-26 A	20,218.26	20,218.26	20,218.26	100%	100%
DAM3-E-MA-EN-0020	Directly buried gate valve for fire system	5	08-Feb-26	12-Feb-26	16-Feb-26 A	25-May-26 A	1,090.50	1,090.50	1,090.50	100%	100%
DAM3-E-MA-EN-0040	Directly buried gate valve for water system	5	12-Feb-26	17-Feb-26	16-Feb-26 A	25-May-26 A	2,414.78	2,414.78	2,414.78	100%	100%

2026 2027

Warning tapes
GRP tank
HVAC duct
Flexible duct
Inline exhaust
Wall propeller
Exhaust diffu
Capped con
14-Jun-26 A,
PVC conduits
Fire alarm syste
Access control s
Suspended Hig
Flood lights
Recessed moun
LED Emergency
LED Emergency
Surface mounte
Solar system
Street Lightin
Wiring devices
Cable Tray
Low Voltage ca
Wires
Grounding syst
CCTV System
Disconnect s
Wall mounted,
Main distributi
Distribution bo
Lighting panel
PP-AC panel
HDPE ducts
Main program
PLC controlle
13-Jun-26 A,
Asphalt work
Concrete par
Road markin
Road signs
Interlock tiles
Curbstones
Gravel beddi
14-Jun-26 A,
HDPE pipes for
HDPE pipes for
UPVC pipes
Directly buried
Directly buried

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MA-EN-0050	Air valve	5	15-Feb-26	21-Feb-26	18-Feb-26 A	26-Feb-26 A	1,963.06	1,963.06	1,963.06	100%	100%
DAM3-E-MA-EN-0060	Washout valve	5	17-Feb-26	24-Feb-26	18-Feb-26 A	14-Jun-26 A	2,302.04	2,302.04	2,302.04	100%	100%
DAM3-E-MA-EN-0070	Gate valve	5	19-Feb-26	26-Feb-26	18-Feb-26 A	14-Jun-26 A	6,398.75	6,398.75	6,398.75	100%	100%
METHOD STATEMENTS		125	29-Jan-26	23-Apr-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTAL		112	29-Jan-26	25-Mar-26	07-Feb-26 A	22-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-0010	Method Statement for Structural Works	7	29-Jan-26	05-Feb-26	07-Feb-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-0020	Method Statement for Architectural Works	7	07-Feb-26	14-Feb-26	05-Mar-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-0030	Method Statement for Mechanical Works	7	15-Feb-26	24-Feb-26	10-May-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-0040	Method Statement for Electrical Works	7	24-Feb-26	04-Mar-26	10-May-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-0050	Method Statement for External Works	7	05-Mar-26	12-Mar-26	21-Jun-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-0060	Method Statement for Environmental Works	8	14-Mar-26	25-Mar-26	21-Jun-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		51	07-Feb-26	22-Apr-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-1010	Method Statement for Structural Works	10	07-Feb-26	17-Feb-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-1020	Method Statement for Architectural Works	10	18-Feb-26	03-Mar-26	05-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-1030	Method Statement for Mechanical Works	10	04-Mar-26	15-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-1040	Method Statement for Electrical Works	10	16-Mar-26	30-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-1050	Method Statement for External Works	10	31-Mar-26	11-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-1060	Method Statement for Environmental Works	10	12-Apr-26	22-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
STAGING		42	18-Feb-26	23-Apr-26	09-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-2010	Method Statement for Structural Works	1	18-Feb-26	19-Feb-26	09-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-2030	Method Statement for Mechanical Works	1	16-Mar-26	16-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-2040	Method Statement for Electrical Works	1	31-Mar-26	31-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-2020	Method Statement for Architectural Works	4	04-Mar-26	08-Mar-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-2050	Method Statement for External Works	1	12-Apr-26	12-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-2060	Method Statement for Environmental Works	1	23-Apr-26	23-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
PROCUREMENT (20%)		258	04-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	19,199,305.00	19,106,789.83	19,199,305.00	99.52%	100%
LONG LEAD MATERIALS		245	09-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	9,350,010.31	9,257,495.14	9,350,010.31	99.01%	100%
ARCHITECTURAL		145	18-Feb-26	06-Jul-26	14-Jan-26 A	20-Aug-26 A	6,184,977.93	6,184,977.93	6,184,977.93	100%	100%
PO ISSUE		90	18-Feb-26	28-Feb-26	14-Jan-26 A	22-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PO-A-1700	PES -Steel Structure	5	18-Feb-26	25-Feb-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-180	Doors	5	18-Feb-26	25-Feb-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-190	Windows	5	21-Feb-26	28-Feb-26	22-Mar-26 A	22-Mar-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		99	25-Feb-26	20-Jun-26	14-Jan-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MF-A-1700	PES -Steel Structure	45	25-Feb-26	22-Apr-26	14-Jan-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-180	Doors	90	25-Feb-26	17-Jun-26	21-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-190	Windows	90	01-Mar-26	20-Jun-26	25-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DELIVERY TO SITE		59	23-Apr-26	04-Jul-26	31-May-26 A	20-Aug-26 A	6,184,977.93	6,184,977.93	6,184,977.93	100%	100%
DAM3-P-DL-A-1700	PES -Steel Structure -1	7	23-Apr-26	30-Apr-26	31-May-26 A	31-May-26 A	2,369,269.97	2,369,269.97	2,369,269.97	100%	100%
DAM3-P-DL-A-1770	PES -Steel Structure -2	7	02-May-26	09-May-26	10-Jun-26 A	14-Jun-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-A-1780	PES -Steel Structure -3	7	18-Jun-26	25-Jun-26	14-Jun-26 A	14-Jul-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-A-1790	PES -Steel Structure -4	7	27-Jun-26	04-Jul-26	01-Jul-26 A	01-Jul-26 A	1,481,481.48	1,481,481.48	1,481,481.48	100%	100%
DAM3-P-DL-A-180	Doors	7	18-Jun-26	25-Jun-26	18-Aug-26 A	20-Aug-26 A	502,577.07	502,577.07	502,577.07	100%	100%
DAM3-P-DL-A-190	Windows	7	21-Jun-26	28-Jun-26	19-Aug-26 A	20-Aug-26 A	350,167.93	350,167.93	350,167.93	100%	100%
STAGING TIME		38	02-May-26	06-Jul-26	21-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-ST-A-1700	PES -Steel Structure	2	02-May-26	03-May-26	21-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-180	Doors	7	27-Jun-26	04-Jul-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-190	Windows	7	29-Jun-26	06-Jul-26	19-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		187	01-Mar-26	15-Nov-26	24-Mar-26 A	27-Sep-26 A	2,332,207.26	2,239,692.09	2,332,207.26	96.03%	100%
PO ISSUE		60	01-Mar-26	14-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-P-PO-E-190	Main distribution board (MDB)	5	01-Mar-26	07-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Main distributio
DAM3-P-PO-E-200	Suspended High Bay LED lights	5	24-Mar-26	29-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Suspended Hig
DAM3-P-PO-E-210	Flood lights	5	30-Mar-26	04-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Flood lights
DAM3-P-PO-E-220	Recessed mounted LED downlight	5	05-Apr-26	09-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Recessed mou
DAM3-P-PO-E-230	LED Emergency Lights wall mounted	5	11-Apr-26	15-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergenc
DAM3-P-PO-E-240	LED Emergency Exit Light	5	16-Apr-26	21-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergenc
DAM3-P-PO-E-250	Fire alarm system	5	22-Apr-26	27-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Fire alarm syste
DAM3-P-PO-E-260	Street Lighting poles	5	28-Apr-26	03-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Street Lighting
DAM3-P-PO-E-270	Distribution board for pump room	5	04-May-26	09-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Distribution boa
DAM3-P-PO-E-280	Surface mounted lights	5	10-May-26	14-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Surface mounte
DAM3-E-PO-E-190	Lighting panel board	5	07-Mar-26	12-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Lighting panel b
DAM3-E-PO-E-200	PP-AC panel	5	12-Mar-26	22-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	PP-AC panel
DAM3-E-PO-E-0230	CCTV System	5	07-Apr-26	12-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	CCTV System
DAM3-E-PO-E-0240	Access control system	5	09-Apr-26	14-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Access control s
DAM3-E-PO-E-0250	Solar system	5	12-Apr-26	16-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Solar system
DAM3-E-PO-E-0260	Main program system & controller	5	14-Apr-26	19-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Main program s
DAM3-E-PO-E-0270	PLC controller	5	16-Apr-26	21-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	PLC controller
MANUFACTURING		187	07-Mar-26	29-Oct-26	01-Apr-26 A	27-Sep-26 A	0.00	0.00	0.00	0%	0%	27-Sep-2
DAM3-P-MF-E-190	Main distribution board (MDB)	90	07-Mar-26	27-Jun-26	01-Apr-26 A	22-Aug-26 A	0.00	0.00	0.00	100%	100%	Main distrib
DAM3-E-MF-E-190	Lighting panel board	90	12-Mar-26	02-Jul-26	07-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Lighting p
DAM3-E-MF-E-200	PP-AC panel	90	22-Mar-26	08-Jul-26	13-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	PP-AC pa
DAM3-E-MF-E-0240	Access control system	150	15-Apr-26	11-Oct-26	16-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Access co
DAM3-P-MF-E-200	Suspended High Bay LED lights	90	30-Mar-26	15-Jul-26	20-Apr-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	Suspende
DAM3-E-MF-E-0230	CCTV System	120	13-Apr-26	02-Sep-26	25-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	CCTV Sy
DAM3-E-MF-E-0250	Solar system	150	18-Apr-26	13-Oct-26	25-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Solar syst
DAM3-P-MF-E-210	Flood lights	90	05-Apr-26	21-Jul-26	28-Apr-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	Flood ligh
DAM3-E-MF-E-0260	Main program system & controller	155	20-Apr-26	21-Oct-26	29-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Main prog
DAM3-E-MF-E-0270	PLC controller	160	22-Apr-26	29-Oct-26	02-May-26 A	20-Sep-26 A	0.00	0.00	0.00	98.13%	100%	PLC cont
DAM3-P-MF-E-220	Recessed mounted LED downlight	90	11-Apr-26	27-Jul-26	04-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	Recessed
DAM3-P-MF-E-230	LED Emergency Lights wall mounted	90	16-Apr-26	02-Aug-26	10-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	LED Eme
DAM3-P-MF-E-240	LED Emergency Exit Light	90	22-Apr-26	08-Aug-26	16-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	LED Eme
DAM3-P-MF-E-250	Fire alarm system	130	28-Apr-26	30-Sep-26	21-May-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire alarm
DAM3-P-MF-E-260	Street Lighting poles	90	04-May-26	19-Aug-26	31-May-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Street Lightin
DAM3-P-MF-E-270	Distribution board for pump room	90	10-May-26	25-Aug-26	06-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Distribution b
DAM3-P-MF-E-280	Surface mounted lights	90	16-May-26	31-Aug-26	11-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Surface mou
DELIVERY TO SITE		33	27-Jun-26	07-Nov-26	24-Aug-26 A	21-Sep-26 A	2,332,207.26	2,239,692.09	2,332,207.26	96.03%	100%	21-Sep-26
DAM3-P-DL-E-190	Main distribution board (MDB)	7	27-Jun-26	05-Jul-26	24-Aug-26 A	24-Mar-26 A	106,626.87	106,626.87	106,626.87	100%	100%	Main distrit
DAM3-P-DL-E-200	Suspended High Bay LED lights	7	16-Jul-26	23-Jul-26	29-Aug-26 A	29-Aug-26 A	99,586.79	99,586.79	99,586.79	100%	100%	Suspende
DAM3-P-DL-E-210	Flood lights	7	22-Jul-26	29-Jul-26	29-Aug-26 A	29-Aug-26 A	15,121.21	15,121.21	15,121.21	100%	100%	Flood light
DAM3-P-DL-E-220	Recessed mounted LED downlight	7	28-Jul-26	04-Aug-26	29-Aug-26 A	29-Aug-26 A	133,874.22	133,874.22	133,874.22	100%	100%	Recessed
DAM3-P-DL-E-230	LED Emergency Lights wall mounted	7	03-Aug-26	10-Aug-26	29-Aug-26 A	29-Aug-26 A	27,627.07	27,627.07	27,627.07	100%	100%	LED Emer
DAM3-P-DL-E-240	LED Emergency Exit Light	7	09-Aug-26	16-Aug-26	29-Aug-26 A	29-Aug-26 A	7,634.17	7,634.17	7,634.17	100%	100%	LED Emer
DAM3-P-DL-E-280	Surface mounted lights	7	01-Sep-26	08-Sep-26	29-Aug-26 A	29-Aug-26 A	73,792.16	73,792.16	73,792.16	100%	100%	Surface m
DAM3-P-DL-E-1900	Lighting panel board	7	02-Jul-26	11-Jul-26	01-Sep-26 A	21-Sep-26 A	60,429.51	60,429.51	60,429.51	100%	100%	Lighting p
DAM3-P-DL-E-2000	PP-AC panel	7	08-Jul-26	16-Jul-26	01-Sep-26 A	21-Sep-26 A	71,084.56	71,084.56	71,084.56	100%	100%	PP-AC pa
DAM3-P-DL-E-250	Fire alarm system	7	01-Oct-26	08-Oct-26	02-Sep-26 A	21-Sep-26 A	279,467.41	279,467.41	279,467.41	100%	100%	Fire alarm
DAM3-P-DL-E-0230	CCTV System	7	03-Sep-26	10-Sep-26	06-Sep-26 A	21-Sep-26 A	250,698.98	250,698.98	250,698.98	100%	100%	CCTV Sy
DAM3-P-DL-E-0260	Main program system & controller	7	22-Oct-26	29-Oct-26	06-Sep-26 A	21-Sep-26 A	83,856.79	47,918.16	83,856.79	57.14%	100%	Main prog
DAM3-P-DL-E-0270	PLC controller	7	31-Oct-26	07-Nov-26	07-Sep-26 A	21-Sep-26 A	56,576.55	0.00	56,576.55	0%	100%	PLC cont

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-P-DL-E-0250	Solar system	7	14-Oct-26	21-Oct-26	09-Sep-26 A	21-Sep-26 A	831,628.60	831,628.60	831,628.60	100%	100%	Solar syst	
DAM3-P-DL-E-0240	Access control system	7	12-Oct-26	19-Oct-26	19-Sep-26 A	21-Sep-26 A	90,682.24	90,682.24	90,682.24	100%	100%	Access co	
DAM3-P-DL-E-260	Street Lighting poles	7	20-Aug-26	27-Aug-26	19-Sep-26 A	21-Sep-26 A	70,168.75	70,168.75	70,168.75	100%	100%	Street Lig	
DAM3-P-DL-E-270	Distribution board for pump room	7	26-Aug-26	02-Sep-26	19-Sep-26 A	20-Sep-26 A	73,351.39	73,351.39	73,351.39	100%	100%	Distributio	
STAGING TIME		38	05-Jul-26	15-Nov-26	24-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	21-Sep-26	
DAM3-P-ST-E-190	Main distribution board (MDB)	7	05-Jul-26	13-Jul-26	24-Aug-26 A	24-Aug-26 A	0.00	0.00	0.00	100%	100%	Main distrib	
DAM3-P-ST-E-200	Suspended High Bay LED lights	7	25-Jul-26	01-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	Suspended	
DAM3-P-ST-E-210	Flood lights	7	30-Jul-26	06-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	Flood lights	
DAM3-P-ST-E-220	Recessed mounted LED downlight	7	05-Aug-26	12-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	Recessed	
DAM3-P-ST-E-230	LED Emergency Lights wall mounted	7	11-Aug-26	18-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	LED Emer	
DAM3-P-ST-E-240	LED Emergency Exit Light	7	17-Aug-26	24-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	LED Emer	
DAM3-P-ST-E-280	Surface mounted lights	7	09-Sep-26	16-Sep-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%	Surface mo	
DAM3-E-ST-E-190	Lighting panel board	7	11-Jul-26	19-Jul-26	01-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	Lighting p	
DAM3-E-ST-E-200	PP-AC panel	7	16-Jul-26	25-Jul-26	01-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	PP-AC pa	
DAM3-P-ST-E-250	Fire alarm system	7	10-Oct-26	17-Oct-26	02-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire alarm	
DAM3-E-ST-E-0230	CCTV System	7	12-Sep-26	19-Sep-26	06-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	CCTV Sys	
DAM3-E-ST-E-0260	Main program system & controller	7	31-Oct-26	07-Nov-26	06-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%	Main prog	
DAM3-E-ST-E-0270	PLC controller	7	08-Nov-26	15-Nov-26	07-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%	PLC contr	
DAM3-E-ST-E-0250	Solar system	7	22-Oct-26	29-Oct-26	09-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	57.14%	100%	Solar syst	
DAM3-P-ST-E-260	Street Lighting poles	7	29-Aug-26	05-Sep-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	Street Lig	
DAM3-P-ST-E-270	Distribution board for pump room	7	03-Sep-26	10-Sep-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%	Distributio	
DAM3-E-ST-E-0240	Access control system	7	20-Oct-26	27-Oct-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	85.71%	100%	Access co	
MECHANICAL		216	09-Feb-26	13-Oct-26	01-Mar-26 A	20-Sep-26 A	832,825.12	832,825.12	832,825.12	100%	100%	20-Sep-26	
PO ISSUE		84	09-Feb-26	29-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	0%	0%	01-Mar-26 A, PO	
DAM3-P-PO-M-340	Seamless black steel or ERW pipes	5	09-Feb-26	14-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Seamless black	
DAM3-P-PO-M-350	Fire hose cabinet	5	24-Feb-26	02-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Fire hose cabine	
DAM3-P-PO-M-360	Western water closet	5	25-Mar-26	31-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Western water c	
DAM3-P-PO-M-370	Wall propeller type exhaust fans	5	06-Apr-26	12-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Wall propeller ty	
DAM3-P-PO-M-380	Fire pumps	5	12-Apr-26	18-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Fire pumps	
DAM3-P-PO-M-400	Booster pump	5	18-Apr-26	23-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	Booster pump	
DAM3-P-PO-M-410	GRP tank	5	23-Apr-26	29-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GRP tank	
MANUFACTURING		211	15-Feb-26	27-Sep-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%	19-Sep-26	
DAM3-P-MF-M-340	Seamless black steel or ERW pipes	120	15-Feb-26	13-Jul-26	02-Mar-26 A	29-Jun-26 A	0.00	0.00	0.00	100%	100%	Seamless bl	
DAM3-P-MF-M-350	Fire hose cabinet	120	03-Mar-26	27-Jul-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire hose	
DAM3-P-MF-M-360	Western water closet	150	31-Mar-26	27-Sep-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%	Western w	
DAM3-P-MF-M-370	Wall propeller type exhaust fans	100	12-Apr-26	10-Aug-26	02-Mar-26 A	09-Aug-26 A	0.00	0.00	0.00	100%	100%	Wall propel	
DAM3-P-MF-M-380	Fire pumps	120	18-Apr-26	08-Sep-26	02-Mar-26 A	17-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire pump	
DAM3-P-MF-M-400	Booster pump	110	23-Apr-26	02-Sep-26	02-Mar-26 A	06-Sep-26 A	0.00	0.00	0.00	100%	100%	Booster pu	
DAM3-P-MF-M-410	GRP tank	100	29-Apr-26	27-Aug-26	02-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	100%	100%	GRP tank	
DELIVERY TO SITE		72	14-Jul-26	05-Oct-26	01-Jul-26 A	20-Sep-26 A	832,825.12	832,825.12	832,825.12	100%	100%	20-Sep-26	
DAM3-P-DL-M-340	Seamless black steel or ERW pipes	7	14-Jul-26	21-Jul-26	01-Jul-26 A	11-Aug-26 A	237,714.11	237,714.11	237,714.11	100%	100%	Seamless b	
DAM3-P-DL-M-370	Wall propeller type exhaust fans	7	10-Aug-26	18-Aug-26	10-Aug-26 A	20-Sep-26 A	153,775.51	153,775.51	153,775.51	100%	100%	Wall prope	
DAM3-P-DL-M-410	GRP tank	7	27-Aug-26	05-Sep-26	29-Aug-26 A	31-Aug-26 A	209,853.09	209,853.09	209,853.09	100%	100%	GRP tank	
DAM3-P-DL-M-400	Booster pump	7	02-Sep-26	10-Sep-26	07-Sep-26 A	07-Sep-26 A	12,924.47	12,924.47	12,924.47	100%	100%	Booster pu	
DAM3-P-DL-M-350	Fire hose cabinet	7	28-Jul-26	04-Aug-26	19-Sep-26 A	20-Sep-26 A	49,774.39	49,774.39	49,774.39	100%	100%	Fire hose	
DAM3-P-DL-M-360	Western water closet	7	27-Sep-26	05-Oct-26	19-Sep-26 A	20-Sep-26 A	65,414.62	65,414.62	65,414.62	100%	100%	Western w	
DAM3-P-DL-M-380	Fire pumps	7	08-Sep-26	16-Sep-26	20-Sep-26 A	20-Sep-26 A	103,368.93	103,368.93	103,368.93	100%	100%	Fire pump	
STAGING TIME		86	22-Jul-26	13-Oct-26	01-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%	20-Sep-26	
DAM3-P-ST-M-340	Seamless black steel or ERW pipes	7	22-Jul-26	29-Jul-26	01-Jul-26 A	11-Aug-26 A	0.00	0.00	0.00	100%	100%	Seamless b	

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-ST-M-370	Wall propeller type exhaust fans	7	18-Aug-26	26-Aug-26	10-Aug-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-410	GRP tank	7	05-Sep-26	13-Sep-26	29-Aug-26 A	31-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-400	Booster pump	7	10-Sep-26	19-Sep-26	07-Sep-26 A	07-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-350	Fire hose cabinet	7	05-Aug-26	12-Aug-26	19-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-360	Western water closet	7	05-Oct-26	13-Oct-26	19-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-380	Fire pumps	7	16-Sep-26	26-Sep-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
SHORT LEAD MATERIALS		258	04-Feb-26	14-Oct-26	14-Jan-26 A	21-Sep-26 A	9,849,294.69	9,849,294.69	9,849,294.69	100%	100%
STRUCTURAL		74	04-Feb-26	15-Apr-26	20-Jan-26 A	29-Apr-26 A	3,207,417.90	3,207,417.90	3,207,417.90	100%	100%
PO ISSUE		28	04-Feb-26	15-Feb-26	20-Jan-26 A	25-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-C-60	Concrete mix	2	07-Feb-26	08-Feb-26	20-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-90	Rebar	2	14-Feb-26	15-Feb-26	01-Feb-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-70	Polyethylene sheet	2	09-Feb-26	10-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-80	Bitumen paint	2	11-Feb-26	12-Feb-26	09-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-50	Anti termite	2	04-Feb-26	05-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		38	07-Feb-26	02-Mar-26	21-Jan-26 A	07-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-C-60	Concrete mix	17	09-Feb-26	02-Mar-26	21-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-90	Rebar	7	16-Feb-26	25-Feb-26	02-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-70	Polyethylene sheet	10	09-Feb-26	21-Feb-26	02-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-80	Bitumen paint	10	14-Feb-26	26-Feb-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-50	Anti termite	12	07-Feb-26	21-Feb-26	26-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		59	21-Feb-26	15-Apr-26	12-Mar-26 A	29-Apr-26 A	3,207,417.90	3,207,417.90	3,207,417.90	100%	100%
DAM3-P-DL-C-50	Anti termite	2	21-Feb-26	24-Feb-26	12-Mar-26 A	29-Apr-26 A	130,309.59	130,309.59	130,309.59	100%	100%
DAM3-P-DL-C-60	Concrete mix -1	2	03-Mar-26	04-Mar-26	12-Mar-26 A	14-Apr-26 A	196,863.16	196,863.16	196,863.16	100%	100%
DAM3-P-DL-C-70	Polyethylene sheet	2	21-Feb-26	24-Feb-26	12-Mar-26 A	29-Apr-26 A	86,906.55	86,906.55	86,906.55	100%	100%
DAM3-P-DL-C-80	Bitumen paint	2	26-Feb-26	01-Mar-26	31-Mar-26 A	29-Apr-26 A	192,960.68	192,960.68	192,960.68	100%	100%
DAM3-P-DL-C-90	Rebar-1	2	25-Feb-26	28-Feb-26	31-Mar-26 A	29-Apr-26 A	218,896.43	218,896.43	218,896.43	100%	100%
DAM3-P-DL-C-100	Concrete mix -2	2	12-Apr-26	13-Apr-26	16-Apr-26 A	29-Apr-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-C-110	Concrete mix -3	2	14-Apr-26	15-Apr-26	16-Apr-26 A	29-Apr-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-C-120	Rebar-2	2	12-Apr-26	13-Apr-26	16-Apr-26 A	29-Apr-26 A	450,000.00	450,000.00	450,000.00	100%	100%
DAM3-P-DL-C-130	Rebar-3	2	14-Apr-26	15-Apr-26	16-Apr-26 A	29-Apr-26 A	450,000.00	450,000.00	450,000.00	100%	100%
STAGING TIME		16	24-Feb-26	05-Mar-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-C-50	Anti termite	1	24-Feb-26	25-Feb-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-60	Concrete mix	1	05-Mar-26	05-Mar-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-70	Polyethylene sheet	1	24-Feb-26	25-Feb-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-80	Bitumen paint	1	02-Mar-26	02-Mar-26	31-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-90	Rebar	1	01-Mar-26	01-Mar-26	31-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		107	09-Feb-26	19-Jul-26	14-Jan-26 A	20-Sep-26 A	2,031,043.96	2,031,043.96	2,031,043.96	100%	100%
PO ISSUE		86	09-Feb-26	28-Mar-26	14-Jan-26 A	24-May-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-A-210	Steel ladder	5	15-Feb-26	21-Feb-26	14-Jan-26 A	18-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-220	Steel gratings	5	21-Feb-26	28-Feb-26	02-Apr-26 A	02-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-200	Concrete masonry unit (CMU)	5	09-Feb-26	14-Feb-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-320	Interal paint	5	07-Mar-26	12-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-330	Gypsum board	5	12-Mar-26	22-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1720	Aluminum Composite Panel	5	22-Mar-26	28-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1750	Steel fence and gates	5	11-Mar-26	16-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1760	Identification sign; ID01 & ID02	5	21-Mar-26	25-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-280	Ceramic tiles	5	24-Feb-26	02-Mar-26	07-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-290	Granite strip	5	03-Mar-26	08-Mar-26	12-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-230	Steel rails	5	01-Mar-26	05-Mar-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-PO-A-310	Epoxy paint	5	01-Mar-26	07-Mar-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		100	15-Feb-26	02-Jul-26	14-Jan-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-A-210	Steel ladder	80	21-Feb-26	02-Jun-26	14-Jan-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-200	Concrete masonry unit (CMU)	50	15-Feb-26	19-Apr-26	06-Apr-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-220	Steel gratings	80	01-Mar-26	08-Jun-26	06-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-230	Steel rails	80	07-Mar-26	14-Jun-26	06-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-280	Ceramic tiles	80	03-Mar-26	10-Jun-26	06-Apr-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-290	Granite strip	80	09-Mar-26	16-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-310	Epoxy paint	80	07-Mar-26	15-Jun-26	06-Apr-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-320	Interml paint	80	12-Mar-26	21-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-330	Gypsum board	80	22-Mar-26	27-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1720	Aluminum Composite Panel	80	28-Mar-26	02-Jul-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1750	Steel fence and gates	80	21-Mar-26	24-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1760	Identification sign; ID01 & ID02	80	26-Mar-26	30-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		59	20-Apr-26	11-Jul-26	10-Jun-26 A	20-Sep-26 A	2,031,043.96	2,031,043.96	2,031,043.96	100%	100%
DAM3-P-DL-A-200	Concrete masonry unit (CMU)	7	20-Apr-26	27-Apr-26	10-Jun-26 A	14-Jun-26 A	418,802.40	418,802.40	418,802.40	100%	100%
DAM3-P-DL-A-280	Ceramic tiles	7	11-Jun-26	18-Jun-26	11-Jun-26 A	15-Jun-26 A	241,008.42	241,008.42	241,008.42	100%	100%
DAM3-P-DL-A-220	Steel gratings	7	09-Jun-26	16-Jun-26	05-Jul-26 A	05-Jul-26 A	21,196.03	21,196.03	21,196.03	100%	100%
DAM3-P-DL-A-310	Epoxy paint	7	15-Jun-26	23-Jun-26	23-Jul-26 A	25-Jul-26 A	378,990.27	378,990.27	378,990.27	100%	100%
DAM3-P-DL-A-210	Steel ladder	7	03-Jun-26	10-Jun-26	28-Jul-26 A	28-Jul-26 A	32,307.70	32,307.70	32,307.70	100%	100%
DAM3-P-DL-A-230	Steel rails	7	15-Jun-26	22-Jun-26	28-Jul-26 A	28-Jul-26 A	5,036.93	5,036.93	5,036.93	100%	100%
DAM3-P-DL-A-320	Interml paint	7	21-Jun-26	29-Jun-26	02-Sep-26 A	20-Sep-26 A	145,026.96	145,026.96	145,026.96	100%	100%
DAM3-P-DL-A-1720	Aluminum Composite Panel	7	02-Jul-26	11-Jul-26	07-Sep-26 A	20-Sep-26 A	577,545.17	577,545.17	577,545.17	100%	100%
DAM3-P-DL-A-330	Gypsum board	7	27-Jun-26	05-Jul-26	14-Sep-26 A	20-Sep-26 A	153,646.35	153,646.35	153,646.35	100%	100%
DAM3-P-DL-A-290	Granite strip	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	2,203.66	2,203.66	2,203.66	100%	100%
DAM3-P-DL-A-1750	Steel fence and gates	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	23,657.36	23,657.36	23,657.36	100%	100%
DAM3-P-DL-A-1760	Identification sign; ID01 & ID02	7	01-Jul-26	08-Jul-26	20-Sep-26 A	20-Sep-26 A	31,622.71	31,622.71	31,622.71	100%	100%
STAGING TIME		58	28-Apr-26	19-Jul-26	15-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-A-200	Concrete masonry unit (CMU)	7	28-Apr-26	05-May-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-280	Ceramic tiles	7	20-Jun-26	27-Jun-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-220	Steel gratings	7	17-Jun-26	24-Jun-26	05-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-310	Epoxy paint	7	23-Jun-26	01-Jul-26	23-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-210	Steel ladder	7	11-Jun-26	18-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-230	Steel rails	7	23-Jun-26	30-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-320	Interml paint	7	29-Jun-26	07-Jul-26	02-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1720	Aluminum Composite Panel	7	11-Jul-26	19-Jul-26	07-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-330	Gypsum board	7	05-Jul-26	13-Jul-26	14-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-290	Granite strip	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1750	Steel fence and gates	7	04-Jul-26	11-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1760	Identification sign; ID01 & ID02	7	09-Jul-26	16-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		174	11-Feb-26	14-Oct-26	05-Apr-26 A	20-Sep-26 A	1,190,075.32	1,190,075.32	1,190,075.32	100%	100%
PO ISSUE		60	11-Feb-26	12-May-26	05-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-M-600	HVAC duct	5	17-Feb-26	24-Feb-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-390	Fire fighting valves	5	07-May-26	12-May-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-420	Water supply valves	5	18-Apr-26	23-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-430	U/G HDPE pipes	5	09-Mar-26	14-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-440	Automatic air release valve	5	24-Mar-26	29-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-450	OS & Y gate valve	5	30-Mar-26	04-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-460	Fire alarm check valve	5	05-Apr-26	09-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-PO-M-480	PPR pipes	5	11-Feb-26	16-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-490	Ball valve	5	07-Mar-26	11-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-500	Capped connection	5	12-Mar-26	21-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-510	UPVC pipes	5	22-Mar-26	26-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-520	Roof vent caps	5	28-Mar-26	01-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-530	Floor drain	5	02-Apr-26	07-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-540	Gully trap	5	08-Apr-26	13-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-550	Electric water heater	5	14-Apr-26	19-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-560	Bib tap	5	20-Apr-26	25-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-580	Lavatory / wash basin	5	26-Apr-26	30-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-590	Inline exhaust fans	5	02-May-26	06-May-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-610	Flexible duct	5	24-Feb-26	02-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-620	Exhaust diffuser	5	03-Mar-26	08-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-660	Warning tapes	5	15-Mar-26	23-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-M-3410	Water tap	5	21-Apr-26	26-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-570	Toilet Fittings	5	30-Mar-26	05-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		169	17-Feb-26	28-Sep-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-M-600	HVAC duct	80	24-Feb-26	04-Jun-26	06-Apr-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-390	Fire fighting valves	80	13-May-26	17-Aug-26	27-Apr-26 A	09-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-420	Water supply valves	80	23-Apr-26	29-Jul-26	27-Apr-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-430	U/G HDPE pipes	80	15-Mar-26	22-Jun-26	27-Apr-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-440	Automatic air release valve	80	30-Mar-26	04-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-450	OS & Y gate valve	80	05-Apr-26	09-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-460	Fire alarm check valve	80	11-Apr-26	15-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-480	PPR pipes	80	17-Feb-26	30-May-26	27-Apr-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-490	Ball valve	80	12-Mar-26	20-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-500	Capped connection	80	22-Mar-26	25-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-510	UPVC pipes	80	28-Mar-26	01-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-520	Roof vent caps	80	02-Apr-26	07-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-530	Floor drain	80	08-Apr-26	13-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-540	Gully trap	80	14-Apr-26	19-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-550	Electric water heater	120	20-Apr-26	09-Sep-26	27-Apr-26 A	13-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-560	Bib tap	80	26-Apr-26	30-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-580	Lavatory / wash basin	80	02-May-26	05-Aug-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-590	Inline exhaust fans	120	07-May-26	28-Sep-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-610	Flexible duct	80	03-Mar-26	10-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-620	Exhaust diffuser	80	09-Mar-26	16-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-660	Warning tapes	80	24-Mar-26	28-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-M-3410	Water tap	80	27-Apr-26	01-Aug-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-570	Toilet Fittings	5	05-Apr-26	11-Apr-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		60	11-Apr-26	06-Oct-26	10-May-26 A	20-Sep-26 A	1,190,075.32	1,190,075.32	1,190,075.32	100%	100%
DAM3-P-DL-M-510	UPVC pipes	7	02-Jul-26	09-Jul-26	10-May-26 A	19-May-26 A	126,693.12	126,693.12	126,693.12	100%	100%
DAM3-P-DL-M-600	HVAC duct	7	06-Jun-26	13-Jun-26	04-Jun-26 A	14-Jun-26 A	490,860.48	490,860.48	490,860.48	100%	100%
DAM3-P-DL-M-420	Water supply valves	7	29-Jul-26	06-Aug-26	05-Jul-26 A	15-Sep-26 A	3,114.56	3,114.56	3,114.56	100%	100%
DAM3-P-DL-M-480	PPR pipes	7	31-May-26	07-Jun-26	05-Jul-26 A	15-Sep-26 A	76,567.93	76,567.93	76,567.93	100%	100%
DAM3-P-DL-M-500	Capped connection	7	27-Jun-26	04-Jul-26	05-Jul-26 A	14-Sep-26 A	913.27	913.27	913.27	100%	100%
DAM3-P-DL-M-660	Warning tapes	7	29-Jun-26	06-Jul-26	05-Jul-26 A	05-Jul-26 A	14,077.01	14,077.01	14,077.01	100%	100%
DAM3-P-DL-M-450	OS & Y gate valve	7	11-Jul-26	18-Jul-26	15-Jul-26 A	20-Sep-26 A	11,631.51	11,631.51	11,631.51	100%	100%
DAM3-P-DL-M-490	Ball valve	7	21-Jun-26	28-Jun-26	18-Jul-26 A	18-Jul-26 A	14,232.16	14,232.16	14,232.16	100%	100%

2026 2027

PPR pipes
Ball valve
Capped conne
UPVC pipes
Roof vent cap
Floor drain
Gully trap
Electric water h
Bib tap
Lavatory / was
Inline exhaust
Flexible duct
Exhaust diffus
Warning tapes
Water tap
Toilet Fittings
19-Sep-26
HVAC duct
Fire fighting
Water supp
U/G HDPE
Automatic
OS & Y ga
Fire alarm
PPR pipes
Ball valve
Capped c
UPVC pip
Roof vent
Floor drain
Gully trap
Electric wa
Bib tap
Lavatory /
Inline exha
Flexible du
Exhaust d
Warning ta
Water tap
Toilet Fittin
20-Sep-26
UPVC pipes
HVAC duct
Water sup
PPR pipes
Capped c
Warning tap
OS & Y ga
Ball valve

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-P-DL-M-430	U/G HDPE pipes	7	23-Jun-26	30-Jun-26	01-Aug-26 A	20-Sep-26 A	49,971.54	49,971.54	49,971.54	100%	100%	U/G HDP
DAM3-P-DL-M-390	Fire fighting valves	7	18-Aug-26	25-Aug-26	10-Aug-26 A	10-Aug-26 A	8,885.58	8,885.58	8,885.58	100%	100%	Fire fighting
DAM3-P-DL-M-590	Inline exhaust fans	7	29-Sep-26	06-Oct-26	05-Sep-26 A	20-Sep-26 A	27,474.92	27,474.92	27,474.92	100%	100%	Inline exh
DAM3-P-DL-M-540	Gully trap	7	20-Jul-26	27-Jul-26	06-Sep-26 A	20-Sep-26 A	15,982.56	15,982.56	15,982.56	100%	100%	Gully trap
DAM3-P-DL-M-570	Toilet Fittings	5	11-Apr-26	16-Apr-26	15-Sep-26 A	20-Sep-26 A	75,460.88	75,460.88	75,460.88	100%	100%	Toilet Fitti
DAM3-P-DL-M-530	Floor drain	7	14-Jul-26	21-Jul-26	16-Sep-26 A	20-Sep-26 A	74,093.27	74,093.27	74,093.27	100%	100%	Floor drai
DAM3-P-DL-M-550	Electric water heater	7	10-Sep-26	17-Sep-26	16-Sep-26 A	16-Sep-26 A	5,974.50	5,974.50	5,974.50	100%	100%	Electric wa
DAM3-P-DL-M-580	Lavatory / wash basin	7	06-Aug-26	13-Aug-26	16-Sep-26 A	20-Sep-26 A	70,323.44	70,323.44	70,323.44	100%	100%	Lavatory /
DAM3-P-DL-M-610	Flexible duct	7	11-Jun-26	18-Jun-26	16-Sep-26 A	20-Sep-26 A	69,629.67	69,629.67	69,629.67	100%	100%	Flexible d
DAM3-P-DL-M-440	Automatic air release valve	7	05-Jul-26	12-Jul-26	20-Sep-26 A	20-Sep-26 A	1,769.50	1,769.50	1,769.50	100%	100%	Automatic
DAM3-P-DL-M-460	Fire alarm check valve	7	16-Jul-26	23-Jul-26	20-Sep-26 A	20-Sep-26 A	26,656.72	26,656.72	26,656.72	100%	100%	Fire alarm
DAM3-P-DL-M-520	Roof vent caps	7	08-Jul-26	15-Jul-26	20-Sep-26 A	20-Sep-26 A	3,044.27	3,044.27	3,044.27	100%	100%	Roof vent
DAM3-P-DL-M-560	Bib tap	7	01-Aug-26	08-Aug-26	20-Sep-26 A	20-Sep-26 A	6,240.96	6,240.96	6,240.96	100%	100%	Bib tap
DAM3-P-DL-M-620	Exhaust diffuser	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	7,040.00	7,040.00	7,040.00	100%	100%	Exhaust d
DAM3-P-DL-M-3410	Water tap	7	02-Aug-26	09-Aug-26	20-Sep-26 A	20-Sep-26 A	9,437.47	9,437.47	9,437.47	100%	100%	Water tap
STAGING TIME		67	16-Apr-26	14-Oct-26	10-May-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%	20-Sep-26
DAM3-P-ST-M-510	UPVC pipes	7	11-Jul-26	18-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes
DAM3-P-ST-M-600	HVAC duct	7	14-Jun-26	21-Jun-26	04-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	HVAC duct
DAM3-P-ST-M-420	Water supply valves	7	06-Aug-26	15-Aug-26	05-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%	Water sup
DAM3-P-ST-M-480	PPR pipes	7	08-Jun-26	15-Jun-26	05-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%	PPR pipes
DAM3-P-ST-M-500	Capped connection	7	05-Jul-26	12-Jul-26	05-Jul-26 A	14-Sep-26 A	0.00	0.00	0.00	100%	100%	Capped c
DAM3-P-ST-M-660	Warning tapes	7	07-Jul-26	14-Jul-26	05-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%	Warning tap
DAM3-P-ST-M-450	OS & Y gate valve	7	19-Jul-26	26-Jul-26	15-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	OS & Y g
DAM3-P-ST-M-490	Ball valve	7	29-Jun-26	06-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	100%	100%	Ball valve
DAM3-P-ST-M-430	U/G HDPE pipes	7	01-Jul-26	08-Jul-26	01-Aug-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	U/G HDP
DAM3-P-ST-M-390	Fire fighting valves	7	26-Aug-26	02-Sep-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	100%	100%	Fire fighting
DAM3-P-ST-M-590	Inline exhaust fans	7	07-Oct-26	14-Oct-26	05-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Inline exh
DAM3-P-ST-M-540	Gully trap	7	28-Jul-26	04-Aug-26	06-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Gully trap
DAM3-P-ST-M-570	Toilet Fittings	5	16-Apr-26	22-Apr-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Toilet Fitti
DAM3-P-ST-M-530	Floor drain	7	22-Jul-26	29-Jul-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Floor drai
DAM3-P-ST-M-550	Electric water heater	7	19-Sep-26	27-Sep-26	16-Sep-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%	Electric wa
DAM3-P-ST-M-580	Lavatory / wash basin	7	15-Aug-26	22-Aug-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Lavatory /
DAM3-P-ST-M-610	Flexible duct	7	20-Jun-26	27-Jun-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Flexible d
DAM3-P-ST-M-440	Automatic air release valve	7	13-Jul-26	20-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Automatic
DAM3-P-ST-M-460	Fire alarm check valve	7	25-Jul-26	01-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire alarm
DAM3-P-ST-M-520	Roof vent caps	7	16-Jul-26	23-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Roof vent
DAM3-P-ST-M-560	Bib tap	7	09-Aug-26	16-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Bib tap
DAM3-P-ST-M-620	Exhaust diffuser	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Exhaust d
DAM3-E-ST-M-3410	Water tap	7	10-Aug-26	17-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Water tap
ELECTRICAL		147	11-Feb-26	01-Aug-26	10-Mar-26 A	20-Sep-26 A	819,995.13	819,995.13	819,995.13	100%	100%	20-Sep-26
PO ISSUE		68	11-Feb-26	09-Apr-26	10-Mar-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%	21-Jun-26 A
DAM3-P-PO-E-310	PVC conduits	5	11-Feb-26	16-Feb-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	PVC conduits
DAM3-P-PO-E-340	Grounding system	5	03-Mar-26	08-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Grounding sys
DAM3-P-PO-E-370	HDPE ducts	5	15-Mar-26	23-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	HDPE ducts
DAM3-P-PO-E-290	Low Voltage cables	5	24-Mar-26	29-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Low Voltage
DAM3-P-PO-E-300	Disconnect switches	5	30-Mar-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Disconnect s
DAM3-P-PO-E-320	Wires	5	17-Feb-26	24-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Wires
DAM3-P-PO-E-330	Wall mounted, duplex, telephone and data outlet	5	05-Apr-26	09-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Wall mounte
DAM3-P-PO-E-350	Wiring devices	5	09-Mar-26	14-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Wiring devic

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PO-E-210	Cable Tray	5	24-Feb-26	02-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		142	17-Feb-26	15-Jul-26	11-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-E-310	PVC conduits	60	17-Feb-26	03-May-26	11-Mar-26 A	02-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-340	Grounding system	80	09-Mar-26	16-Jun-26	27-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-370	HDPE ducts	80	24-Mar-26	28-Jun-26	27-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-320	Wires	80	24-Feb-26	04-Jun-26	28-Jun-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-E-210	Cable Tray	80	03-Mar-26	10-Jun-26	04-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-350	Wiring devices	80	15-Mar-26	22-Jun-26	09-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-290	Low Voltage cables	80	30-Mar-26	04-Jul-26	15-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-300	Disconnect switches	80	05-Apr-26	09-Jul-26	21-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-330	Wall mounted, duplex, telephone and data outlet	80	11-Apr-26	15-Jul-26	27-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		65	04-May-26	23-Jul-26	03-May-26 A	20-Sep-26 A	819,995.13	819,995.13	819,995.13	100%	100%
DAM3-P-DL-E-310	PVC conduits	7	04-May-26	11-May-26	03-May-26 A	20-May-26 A	15,738.66	15,738.66	15,738.66	100%	100%
DAM3-P-DL-E-340	Grounding system	7	17-Jun-26	24-Jun-26	10-May-26 A	19-May-26 A	65,141.26	65,141.26	65,141.26	100%	100%
DAM3-P-DL-E-370	HDPE ducts	7	29-Jun-26	06-Jul-26	10-May-26 A	19-May-26 A	176,019.75	176,019.75	176,019.75	100%	100%
DAM3-P-DL-E-290	Low Voltage cables	7	05-Jul-26	12-Jul-26	23-Jul-26 A	25-Jul-26 A	299,034.47	299,034.47	299,034.47	100%	100%
DAM3-P-DL-E-300	Disconnect switches	7	11-Jul-26	18-Jul-26	23-Jul-26 A	25-Jul-26 A	100,576.04	100,576.04	100,576.04	100%	100%
DAM3-P-DL-E-330	Wall mounted, duplex, telephone and data outlet	7	16-Jul-26	23-Jul-26	17-Sep-26 A	20-Sep-26 A	88,627.44	88,627.44	88,627.44	100%	100%
DAM3-P-DL-E-350	Wiring devices	7	23-Jun-26	30-Jun-26	17-Sep-26 A	20-Sep-26 A	66,414.34	66,414.34	66,414.34	100%	100%
DAM3-P-DL-E-320	Wires	7	06-Jun-26	13-Jun-26	20-Sep-26 A	20-Sep-26 A	7,379.37	7,379.37	7,379.37	100%	100%
DAM3-P-DL-E-2100	Cable Tray	7	11-Jun-26	18-Jun-26	20-Sep-26 A	20-Sep-26 A	1,063.80	1,063.80	1,063.80	100%	100%
STAGING TIME		75	12-May-26	01-Aug-26	03-May-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-E-310	PVC conduits	7	12-May-26	19-May-26	03-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-340	Grounding system	7	25-Jun-26	02-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-370	HDPE ducts	7	07-Jul-26	14-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-290	Low Voltage cables	7	13-Jul-26	20-Jul-26	25-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-300	Disconnect switches	7	19-Jul-26	26-Jul-26	25-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-330	Wall mounted, duplex, telephone and data outlet	7	25-Jul-26	01-Aug-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-350	Wiring devices	7	01-Jul-26	08-Jul-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-320	Wires	7	14-Jun-26	21-Jun-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-210	Cable Tray	7	20-Jun-26	27-Jun-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
EXTERNAL		119	07-Apr-26	03-Sep-26	02-Mar-26 A	21-Sep-26 A	2,215,885.18	2,215,885.18	2,215,885.18	100%	100%
PO ISSUE		23	07-Apr-26	28-Apr-26	02-Mar-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-EX-80	Asphalt works	5	07-Apr-26	12-Apr-26	02-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-90	Concrete parking bumper	5	08-Apr-26	14-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-100	Road markings	5	11-Apr-26	16-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-110	Road signs	5	13-Apr-26	19-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-130	Interlock tiles	5	22-Apr-26	28-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-140	Curbstones	5	18-Apr-26	23-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-150	Gravel bedding	5	21-Apr-26	26-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		111	13-Apr-26	15-Aug-26	03-Mar-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-EX-80	Asphalt works	100	13-Apr-26	10-Aug-26	03-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-90	Concrete parking bumper	90	14-Apr-26	01-Aug-26	28-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-100	Road markings	90	16-Apr-26	03-Aug-26	28-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-110	Road signs	90	19-Apr-26	05-Aug-26	28-Jun-26 A	17-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-140	Curbstones	90	23-Apr-26	10-Aug-26	28-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-150	Gravel bedding	90	27-Apr-26	12-Aug-26	28-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-130	Interlock tiles	90	28-Apr-26	15-Aug-26	21-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		27	01-Aug-26	23-Aug-26	08-Jun-26 A	21-Sep-26 A	2,215,885.18	2,215,885.18	2,215,885.18	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-DL-EX-80	Asphalt works	7	11-Aug-26	18-Aug-26	08-Jun-26 A	17-Jun-26 A	1,868,985.04	1,868,985.04	1,868,985.04	100%	100%
DAM3-P-DL-EX-130	Interlock tiles	7	15-Aug-26	23-Aug-26	17-Sep-26 A	20-Sep-26 A	141,980.16	141,980.16	141,980.16	100%	100%
DAM3-P-DL-EX-140	Curbstones	7	10-Aug-26	18-Aug-26	17-Sep-26 A	20-Sep-26 A	86,912.40	86,912.40	86,912.40	100%	100%
DAM3-P-DL-EX-150	Gravel bedding	7	13-Aug-26	20-Aug-26	17-Sep-26 A	21-Sep-26 A	66,111.93	66,111.93	66,111.93	100%	100%
DAM3-P-DL-EX-110	Road signs	7	05-Aug-26	13-Aug-26	20-Sep-26 A	20-Sep-26 A	31,028.59	31,028.59	31,028.59	100%	100%
DAM3-P-DL-EX-90	Concrete parking bumper	7	01-Aug-26	09-Aug-26	21-Sep-26 A	21-Sep-26 A	9,558.14	9,558.14	9,558.14	100%	100%
DAM3-P-DL-EX-100	Road markings	7	03-Aug-26	11-Aug-26	21-Sep-26 A	21-Sep-26 A	11,308.91	11,308.91	11,308.91	100%	100%
STAGING TIME		41	09-Aug-26	03-Sep-26	08-Jun-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-EX-80	Asphalt works	7	19-Aug-26	26-Aug-26	08-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-130	Interlock tiles	7	23-Aug-26	31-Aug-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-140	Curbstones	7	27-Aug-26	03-Sep-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-150	Gravel bedding	7	22-Aug-26	29-Aug-26	17-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-110	Road signs	7	13-Aug-26	22-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-90	Concrete parking bumper	7	09-Aug-26	17-Aug-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-100	Road markings	7	11-Aug-26	19-Aug-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
ENVIRONMENTAL		151	11-Feb-26	06-Aug-26	21-Jun-26 A	20-Sep-26 A	384,877.22	384,877.22	384,877.22	100%	100%
PO ISSUE		40	11-Feb-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-EN-100	HDPE pipes for fire system	5	11-Feb-26	16-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-110	Directly buried gate valve for fire system	5	17-Feb-26	24-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-120	HDPE pipes for water supply system	5	24-Feb-26	02-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-130	Directly buried gate valve for water system	5	03-Mar-26	08-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-140	Air valve	5	09-Mar-26	14-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-150	Washout valve	5	15-Mar-26	23-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-160	Gate valve	5	24-Mar-26	29-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-170	UPVC pipes	5	30-Mar-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		133	17-Feb-26	21-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-EN-120	HDPE pipes for water supply system	90	03-Mar-26	22-Jun-26	22-Jun-26 A	15-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-130	Directly buried gate valve for water system	90	09-Mar-26	28-Jun-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-140	Air valve	90	15-Mar-26	04-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-150	Washout valve	90	24-Mar-26	09-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-160	Gate valve	90	30-Mar-26	15-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-170	UPVC pipes	90	05-Apr-26	21-Jul-26	22-Jun-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-100	HDPE pipes for fire system	90	17-Feb-26	10-Jun-26	28-Jun-26 A	23-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-110	Directly buried gate valve for fire system	90	24-Feb-26	16-Jun-26	04-Jul-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		107	11-Jun-26	29-Jul-26	25-Jul-26 A	20-Sep-26 A	384,877.22	384,877.22	384,877.22	100%	100%
DAM3-P-DL-EN-100	HDPE pipes for fire system	7	11-Jun-26	18-Jun-26	25-Jul-26 A	26-Jul-26 A	144,972.85	144,972.85	144,972.85	100%	100%
DAM3-P-DL-EN-170	UPVC pipes	7	22-Jul-26	29-Jul-26	26-Jul-26 A	26-Jul-26 A	134,788.44	134,788.44	134,788.44	100%	100%
DAM3-P-DL-EN-120	HDPE pipes for water supply system	7	23-Jun-26	30-Jun-26	17-Aug-26 A	17-Aug-26 A	10,655.04	10,655.04	10,655.04	100%	100%
DAM3-P-DL-EN-160	Gate valve	7	16-Jul-26	23-Jul-26	05-Sep-26 A	20-Sep-26 A	42,658.36	42,658.36	42,658.36	100%	100%
DAM3-P-DL-EN-110	Directly buried gate valve for fire system	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	7,270.01	7,270.01	7,270.01	100%	100%
DAM3-P-DL-EN-130	Directly buried gate valve for water system	7	29-Jun-26	06-Jul-26	20-Sep-26 A	20-Sep-26 A	16,098.52	16,098.52	16,098.52	100%	100%
DAM3-P-DL-EN-140	Air valve	7	05-Jul-26	12-Jul-26	20-Sep-26 A	20-Sep-26 A	13,087.07	13,087.07	13,087.07	100%	100%
DAM3-P-DL-EN-150	Washout valve	7	11-Jul-26	18-Jul-26	20-Sep-26 A	20-Sep-26 A	15,346.94	15,346.94	15,346.94	100%	100%
STAGING TIME		107	20-Jun-26	06-Aug-26	25-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-EN-100	HDPE pipes for fire system	7	20-Jun-26	27-Jun-26	25-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-170	UPVC pipes	7	30-Jul-26	06-Aug-26	26-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-120	HDPE pipes for water supply system	7	01-Jul-26	08-Jul-26	17-Aug-26 A	17-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-160	Gate valve	7	25-Jul-26	01-Aug-26	05-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-110	Directly buried gate valve for fire system	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-ST-EN-130	Directly buried gate valve for water system	7	07-Jul-26	14-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-140	Air valve	7	13-Jul-26	20-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-150	Washout valve	7	19-Jul-26	26-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
CONSTRUCTION (67%)		321	27-Jan-26	21-Feb-27	14-Jan-26 A	24-Feb-27	64,317,671.75	42,950,975.87	43,084,570.98	66.78%	66.99%
RBF 900 SQM FACTORIES		321	27-Jan-26	16-Feb-27	14-Jan-26 A	13-Feb-27	55,841,646.40	40,731,897.99	40,180,130.43	72.94%	71.95%
SITE WORKS		16	27-Jan-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
DAM3-C-GEN-88	Demolition of the existing pavement	12	10-Feb-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
DAM3-C-GEN-10	Initial Site Survey and Setting out	12	27-Jan-26	09-Feb-26	19-Jan-26 A	24-Jan-26 A	0.00	0.00	0.00	100%	100%
BLOCK B6		262	10-Feb-26	23-Nov-26	15-Feb-26 A	07-Jan-27	5,075,523.09	4,369,689.33	3,719,785.18	86.09%	73.29%
STRUCTURAL		207	10-Feb-26	07-Jul-26	15-Feb-26 A	11-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		74	10-Feb-26	25-Mar-26	15-Feb-26 A	10-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B6-S-160	Excavation for footings	8	10-Feb-26	19-Feb-26	15-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B6-S-6143	Soil replacement - rock fill	6	19-Feb-26	28-Feb-26	02-Apr-26 A	04-Apr-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B6-S-6153	Engineering fill	6	01-Mar-26	07-Mar-26	12-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B6-S-537	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	22-Apr-26 A	22-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B6-S-687	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	22-Apr-26 A	22-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B6-S-777	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	22-Apr-26 A	22-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B6-S-587	Rebar for Footings	4	12-Mar-26	16-Mar-26	02-May-26 A	05-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B6-S-597	Formwork for Footings	4	21-Mar-26	24-Mar-26	04-May-26 A	09-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B6-S-547	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	10-May-26 A	10-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		12	26-Mar-26	11-Apr-26	05-May-26 A	01-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B6-S-637	Rebar for column neck	2	26-Mar-26	28-Mar-26	05-May-26 A	09-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B6-S-647	Formwork for column neck	2	29-Mar-26	30-Mar-26	12-May-26 A	16-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B6-S-627	Pouring Concrete for column neck	1	31-Mar-26	31-Mar-26	17-May-26 A	17-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B6-S-677	Damp proof /Bitumin paint on Footings & column neck	2	01-Apr-26	02-Apr-26	18-May-26 A	19-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B6-S-737	Backfilling / Compaction up to Bottom of Grade Beams	7	04-Apr-26	11-Apr-26	24-May-26 A	01-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		17	12-Apr-26	28-Apr-26	04-Jun-26 A	22-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B6-S-557	Lean Concrete Below Grade Beams	2	15-Apr-26	16-Apr-26	04-Jun-26 A	04-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B6-S-707	Vapour barrier for Grade Beams	2	13-Apr-26	14-Apr-26	04-Jun-26 A	04-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B6-S-787	Anti Termite Below Grade Beams	1	12-Apr-26	12-Apr-26	04-Jun-26 A	04-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B6-S-607	Rebar for Grade Beams	5	18-Apr-26	22-Apr-26	08-Jun-26 A	09-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B6-S-617	Formwork for Grade Beams	2	23-Apr-26	25-Apr-26	10-Jun-26 A	14-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B6-S-767	Anchor bolts installation	2	23-Apr-26	25-Apr-26	11-Jun-26 A	13-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B6-S-567	Pouring Concrete for Grade Beams	1	26-Apr-26	26-Apr-26	15-Jun-26 A	15-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B6-S-717	Damp proof /Bitumin paint on Grade Beams	2	27-Apr-26	28-Apr-26	20-Jun-26 A	22-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		106	29-Apr-26	07-Jul-26	28-Jun-26 A	11-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B6-S-747	Backfilling / Compaction for Slab on Grade	7	29-Apr-26	06-May-26	28-Jun-26 A	06-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B6-S-577	Pouring Concrete for Ground Slab	4	11-May-26	14-May-26	18-Aug-26 A	23-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B6-S-697	Anti Termite Treatment below Ground Slab	1	07-May-26	07-May-26	18-Aug-26 A	23-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B6-S-727	Vapour barrier for below Ground Slab	2	09-May-26	10-May-26	18-Aug-26 A	23-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	04-Nov-26	11-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		65	07-May-26	07-Jun-26	08-Jun-26 A	06-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B6-S-6101	Rebar for Tie Beams	4	19-May-26	23-May-26	08-Jun-26 A	13-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B6-S-6102	Formwork for Tie Beams	2	24-May-26	25-May-26	11-Jun-26 A	14-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B6-S-6103	Pouring Concrete for Tie Beams	1	30-May-26	30-May-26	15-Jun-26 A	15-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B6-S-5101	Rebar for column	5	07-May-26	12-May-26	18-Jul-26 A	20-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B6-S-5102	Formwork for column	4	13-May-26	17-May-26	23-Jul-26 A	11-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B6-S-5103	Pouring Concrete for column	1	18-May-26	18-May-26	26-Jul-26 A	13-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B6-S-6113	Rebar for Beams	4	31-May-26	03-Jun-26	21-Sep-26 A	22-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B6-S-6123	Formwork for Beams	2	04-Jun-26	06-Jun-26	28-Sep-26 A	04-Oct-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B6-S-6133	Pouring Concrete for Beams	1	07-Jun-26	07-Jun-26	01-Oct-26 A	06-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		83	16-May-26	12-Jul-26	06-Jul-26 A	03-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B6-SS-150	Installation of columns	3	16-May-26	18-May-26	06-Jul-26 A	06-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B6-SS-160	Installation of raft and purlins	5	19-May-26	24-May-26	06-Jul-26 A	07-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B6-SS-1020	Intumescent paint to steel works	7	25-May-26	04-Jun-26	25-Jul-26 A	17-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B6-SS-190	Installation of roof sheet	5	07-Jul-26	12-Jul-26	24-Aug-26 A	30-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B6-SS-1050	Steel members for external platform	7	08-Jun-26	15-Jun-26	30-Aug-26 A	31-Aug-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B6-SS-180	Installation of wall sandwich panel	5	30-Jun-26	05-Jul-26	11-Oct-26 A	13-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B6-SS-1030	Steel members for office area	7	25-May-26	04-Jun-26	11-Oct-26 A	12-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B6-SS-1040	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	27-Oct-26	03-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-1060	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	27-Oct-26	01-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		93	25-May-26	03-Nov-26	15-Aug-26 A	28-Dec-26	900,244.66	784,824.90	393,527.69	87.18%	43.71%
MASONARY WORKS		35	25-May-26	07-Jul-26	29-Aug-26 A	15-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B6-A-170	Block work at factory area	10	25-May-26	08-Jun-26	29-Aug-26 A	07-Sep-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B6-A-200	Block work at office area	7	22-Jun-26	29-Jun-26	30-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B6-A-620	Block work at toilet area	7	30-Jun-26	07-Jul-26	31-Aug-26 A	15-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		35	08-Jul-26	06-Oct-26	15-Oct-26 A	05-Dec-26	92,757.47	92,757.47	70,673.82	100%	76.19%
DAM3-C-B6-A-630	Internal Wall Plaster	15	08-Jul-26	25-Jul-26	15-Oct-26 A	19-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	29-Sep-26	06-Oct-26	24-Oct-26 A	05-Dec-26	44,167.30	44,167.30	22,083.65	100%	50%
CIELING FINISHES		5	20-Sep-26	26-Sep-26	23-Nov-26	29-Nov-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B6-A-690	Installation of Ceiling Gypsum Board	5	20-Sep-26	26-Sep-26	23-Nov-26	29-Nov-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		32	13-Aug-26	03-Nov-26	26-Oct-26 A	28-Dec-26	189,488.90	74,069.14	34,898.03	39.09%	18.42%
DAM3-C-B6-A-670	Tiles for Toilet	7	13-Aug-26	20-Aug-26	26-Oct-26 A	23-Nov-26	46,530.71	46,530.71	34,898.03	100%	75%
DAM3-C-B6-A-700	Tiles for Office Area	2	27-Sep-26	28-Sep-26	29-Nov-26	01-Dec-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B6-A-830	Granite strip	2	29-Sep-26	30-Sep-26	01-Dec-26	03-Dec-26	671.12	671.12	0.00	100%	0%
DAM3-C-B6-A-850	Epoxy paint	5	27-Oct-26	03-Nov-26	22-Dec-26	28-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		16	07-Jul-26	08-Aug-26	20-Oct-26 A	16-Nov-26	248,575.06	248,575.06	70,629.91	100%	28.41%
DAM3-C-B6-A-1010	Window (CW1)	7	07-Jul-26	14-Jul-26	20-Oct-26 A	05-Nov-26	94,173.21	94,173.21	70,629.91	100%	75%
DAM3-C-B6-A-640	Roll up Shutter Door	1	15-Jul-26	15-Jul-26	05-Nov-26	07-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B6-A-650	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	16-Jul-26	16-Jul-26	07-Nov-26	08-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B6-A-710	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	18-Jul-26	18-Jul-26	08-Nov-26	09-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B6-A-720	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	19-Jul-26	19-Jul-26	09-Nov-26	10-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B6-A-940	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	20-Jul-26	20-Jul-26	10-Nov-26	11-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B6-A-950	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	30-Jul-26	30-Jul-26	11-Nov-26	12-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B6-A-960	Skylight fixtures installation	3	01-Aug-26	08-Aug-26	12-Nov-26	16-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	09-Aug-26	12-Aug-26	16-Nov-26	21-Nov-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B6-A-810	Waterproofing membrane for toilets	4	09-Aug-26	12-Aug-26	16-Nov-26	21-Nov-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		18	01-Oct-26	15-Oct-26	15-Aug-26 A	12-Dec-26	193,717.06	193,717.06	138,371.73	100%	71.43%
DAM3-C-B6-A-750	Galvanised Steel Gratings	2	14-Oct-26	15-Oct-26	15-Aug-26 A	15-Aug-26 A	6,455.16	6,455.16	6,455.16	100%	100%
DAM3-C-B6-A-760	Aluminium composite panel	5	08-Oct-26	13-Oct-26	20-Oct-26 A	12-Dec-26	175,888.76	175,888.76	131,916.57	100%	75%
DAM3-C-B6-A-740	Steel Ladder	2	01-Oct-26	03-Oct-26	03-Dec-26	06-Dec-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B6-A-840	Steel railing works	4	04-Oct-26	07-Oct-26	06-Dec-26	10-Dec-26	1,533.98	1,533.98	0.00	100%	0%
SPECIALTIES		9	17-Oct-26	26-Oct-26	12-Dec-26	22-Dec-26	45,080.66	45,080.66	0.00	100%	0%
DAM3-C-B6-A-770	Installation of fittings	5	17-Oct-26	21-Oct-26	12-Dec-26	17-Dec-26	22,981.27	22,981.27	0.00	100%	0%
DAM3-C-B6-A-1000	Identification sign; ID01 & ID02	3	22-Oct-26	25-Oct-26	17-Dec-26	21-Dec-26	9,630.56	9,630.56	0.00	100%	0%
DAM3-C-B6-A-790	Furniture Installation	1	26-Oct-26	26-Oct-26	21-Dec-26	22-Dec-26	12,468.83	12,468.83	0.00	100%	0%
MECHANICAL		131	29-Apr-26	03-Nov-26	14-Jul-26 A	28-Dec-26	467,522.66	456,750.53	326,975.51	97.7%	69.94%
HVAC		17	15-Oct-26	31-Oct-26	25-Oct-26 A	24-Dec-26	233,183.33	225,464.93	170,694.73	96.69%	73.2%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	22-Oct-26	26-Oct-26	25-Oct-26 A	27-Oct-26 A	170,694.73	170,694.73	170,694.73	100%	100%
DAM3-C-B6-M-450	Installation of HVAC Ducts	2	22-Oct-26	24-Oct-26	25-Oct-26 A	27-Oct-26 A	149,489.33	149,489.33	149,489.33	100%	100%
DAM3-C-B6-M-480	Installation of Duct insulation	2	25-Oct-26	26-Oct-26	25-Oct-26 A	27-Oct-26 A	21,205.40	21,205.40	21,205.40	100%	100%
SECOND STAGE		17	15-Oct-26	31-Oct-26	06-Dec-26	24-Dec-26	62,488.60	54,770.20	0.00	87.65%	0%
DAM3-C-B6-M-440	Installation of Exhaust Fans	2	15-Oct-26	17-Oct-26	06-Dec-26	07-Dec-26	7,938.56	7,938.56	0.00	100%	0%
DAM3-C-B6-M-470	Installation of Wall Propeller Type Exhaust Fan	4	18-Oct-26	21-Oct-26	08-Dec-26	12-Dec-26	46,831.64	46,831.64	0.00	100%	0%
DAM3-C-B6-M-460	Installation of Diffuser	2	27-Oct-26	28-Oct-26	13-Dec-26	14-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B6-M-650	Supply, install, test and commission door grilles & exhaust louvers	2	29-Oct-26	31-Oct-26	22-Dec-26	24-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		21	07-Oct-26	03-Nov-26	11-Oct-26 A	28-Dec-26	102,458.78	99,752.72	84,594.16	97.36%	82.56%
FIRST STAGE		12	07-Oct-26	20-Oct-26	11-Oct-26 A	15-Oct-26 A	84,594.16	84,594.16	84,594.16	100%	100%
DAM3-C-B6-M-610	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	07-Oct-26	14-Oct-26	11-Oct-26 A	15-Oct-26 A	72,394.75	72,394.75	72,394.75	100%	100%
DAM3-C-B6-M-620	Installation of Fire Fighting Valve	5	15-Oct-26	20-Oct-26	11-Oct-26 A	15-Oct-26 A	12,199.40	12,199.40	12,199.40	100%	100%
SECOND STAGE		20	21-Oct-26	03-Nov-26	06-Dec-26	28-Dec-26	17,864.62	15,158.56	0.00	84.85%	0%
DAM3-C-B6-M-630	Installation of Fire Hose Cabinet	3	21-Oct-26	24-Oct-26	06-Dec-26	08-Dec-26	15,158.56	15,158.56	0.00	100%	0%
DAM3-C-B6-M-680	Supply, install, test and commission Fire Department Connection(FDC)	3	01-Nov-26	03-Nov-26	24-Dec-26	28-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		116	29-Apr-26	27-Oct-26	14-Jul-26 A	12-Dec-26	90,009.74	89,662.07	30,093.94	99.61%	33.43%
FIRST STAGE		102	29-Apr-26	29-Aug-26	14-Jul-26 A	25-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B6-M-510	Installation of Sanitary Waste / Drainage Pipes	4	29-Apr-26	03-May-26	14-Jul-26 A	18-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B6-M-690	Installation of Trench drain	5	24-Aug-26	29-Aug-26	15-Jul-26 A	18-Jul-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B6-M-530	Installation of Floor Drain	2	22-Aug-26	23-Aug-26	23-Nov-26	25-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	28-Sep-26	27-Oct-26	25-Nov-26	12-Dec-26	48,859.84	48,512.17	0.00	99.29%	0%
DAM3-C-B6-M-490	Installation of Electric Water Heater	2	28-Sep-26	29-Sep-26	25-Nov-26	28-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B6-M-500	Installation of Sanitary Fixture and Accessories	4	13-Oct-26	18-Oct-26	28-Nov-26	02-Dec-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B6-M-520	Installation of Lavotary /Wash Basin	2	18-Oct-26	20-Oct-26	02-Dec-26	05-Dec-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B6-M-580	Installation of Bib Tap	2	20-Oct-26	22-Oct-26	05-Dec-26	07-Dec-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B6-M-540	Installation of Water Tap	2	22-Oct-26	25-Oct-26	07-Dec-26	09-Dec-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B6-M-550	Installation of Roof Vent Cap	2	25-Oct-26	27-Oct-26	09-Dec-26	12-Dec-26	927.12	579.45	0.00	62.5%	0%
WATER SUPPLY SYSTEM		16	07-Oct-26	19-Oct-26	03-Oct-26 A	08-Dec-26	41,870.81	41,870.81	41,592.68	100%	99.34%
FIRST STAGE		6	07-Oct-26	13-Oct-26	03-Oct-26 A	07-Oct-26 A	41,592.68	41,592.68	41,592.68	100%	100%
DAM3-C-B6-M-590	Installation of Water Supply Valve	2	12-Oct-26	13-Oct-26	03-Oct-26 A	07-Oct-26 A	18,274.27	18,274.27	18,274.27	100%	100%
DAM3-C-B6-M-600	Installation of Water Supply Pipes	4	07-Oct-26	11-Oct-26	03-Oct-26 A	07-Oct-26 A	23,318.41	23,318.41	23,318.41	100%	100%
SECOND STAGE		3	14-Oct-26	19-Oct-26	06-Dec-26	08-Dec-26	278.13	278.13	0.00	100%	0%
DAM3-C-B6-M-640	Capped connection	3	14-Oct-26	19-Oct-26	06-Dec-26	08-Dec-26	278.13	278.13	0.00	100%	0%
ELECTRICAL		163	20-May-26	23-Nov-26	08-Jun-26 A	07-Jan-27	752,044.76	172,402.90	71,373.28	22.92%	9.49%
FIRST STAGE		161	20-May-26	05-Nov-26	08-Jun-26 A	28-Dec-26	86,114.12	60,725.20	27,642.87	70.52%	32.1%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	08-Jun-26 A	27-Oct-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	08-Jun-26 A	31-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm System	4	14-Oct-26	18-Oct-26	09-Jun-26 A	14-Dec-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	01-Oct-26 A	23-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	27-Oct-26	31-Oct-26	36,389.98	36,389.98	0.00	100%	0%
DAM3-C-B6-E-463	Installation of Wires	4	02-Nov-26	05-Nov-26	23-Dec-26	28-Dec-26	16,925.94	0.00	0.00	0%	0%
SECOND STAGE		78	07-Oct-26	23-Nov-26	10-Oct-26 A	07-Jan-27	665,930.64	111,677.69	43,730.41	16.77%	6.57%
DAM3-C-B6-E-473	Installation of LP-1 Panel	2	14-Nov-26	15-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B6-E-730	Installation of Solar power plant	7	31-Oct-26	07-Nov-26	12-Oct-26 A	03-Nov-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	27-Oct-26	31-Oct-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	01-Nov-26	02-Nov-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	03-Nov-26	04-Nov-26	185.40	0.00	0.00	0%	0%
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weather proof	2	04-Nov-26	05-Nov-26	03-Nov-26	04-Nov-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B6-E-403	Installation of Wiring Devices	4	07-Oct-26	11-Oct-26	06-Dec-26	09-Dec-26	19,435.09	19,435.09	0.00	100%	0%

2026 2027

27-Oct-2 Installatio 24-Dec Installa Installa Installa Supply 28-Dec 15-Oct-26 Installatio Installatio 28-Dec Installa Supply 12-Dec 25-Nov- Installation Installation Installat 12-Dec Installat Installat Installa Installat Installat Installat 08-Dec 07-Oct-26 Installatio Installatio 08-Dec Cappe 07-Jar 28-Dec Installatio Installatio Installa Installa Installatio Installa 07-Jar Installatio Installatio Installatio Monitor Line Isol Firewarn Installa

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B6-E-433	Installation of Disconnect Switches	2	12-Oct-26	13-Oct-26	10-Dec-26	12-Dec-26	30,235.95	30,235.95	0.00	100%	0%
DAM3-C-B6-E-353	Installation of Fire Alarm Control Panel	3	19-Oct-26	22-Oct-26	15-Dec-26	17-Dec-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B6-E-363	Installation of Fire Detectors & Accessories	4	24-Oct-26	27-Oct-26	19-Dec-26	22-Dec-26	56,740.37	42,555.28	0.00	75%	0%
DAM3-C-B6-E-383	Installation of Lighting fixtures	2	07-Nov-26	10-Nov-26	28-Dec-26	30-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B6-E-423	Installation of Main Distribution Board	2	11-Nov-26	12-Nov-26	30-Dec-26	02-Jan-27	32,472.73	0.00	0.00	0%	0%
DAM3-C-B6-E-483	Installation of PP-AC panel	2	16-Nov-26	17-Nov-26	02-Jan-27	04-Jan-27	21,648.48	0.00	0.00	0%	0%
DAM3-C-B6-E-443	Installation of Telephone Cabinet	2	18-Nov-26	19-Nov-26	04-Jan-27	06-Jan-27	26,991.08	0.00	0.00	0%	0%
DAM3-C-B6-E-720	Installation of CCTV System	3	18-Nov-26	23-Nov-26	04-Jan-27	07-Jan-27	76,349.24	0.00	0.00	0%	0%
BLOCK B5		242	19-Feb-26	23-Nov-26	16-Feb-26 A	23-Dec-26	5,075,523.09	4,822,254.38	3,443,717.57	95.01%	67.85%
STRUCTURAL		194	19-Feb-26	25-Jul-26	16-Feb-26 A	03-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		44	19-Feb-26	25-Mar-26	16-Feb-26 A	05-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B5-S-250	Excavation for footings	4	19-Feb-26	25-Feb-26	16-Feb-26 A	18-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B5-S-6163	Soil replacement - rock fill	4	25-Feb-26	02-Mar-26	30-Mar-26 A	02-Apr-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B5-S-6173	Engineering fill	4	03-Mar-26	07-Mar-26	07-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B5-S-1057	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	21-Apr-26 A	21-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B5-S-1207	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	21-Apr-26 A	21-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B5-S-1297	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	21-Apr-26 A	21-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B5-S-1107	Rebar for Footings	4	12-Mar-26	16-Mar-26	28-Apr-26 A	29-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B5-S-1117	Formwork for Footings	4	21-Mar-26	24-Mar-26	02-May-26 A	03-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B5-S-1067	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	05-May-26 A	05-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		20	26-Mar-26	11-Apr-26	03-May-26 A	24-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B5-S-1157	Rebar for column neck	2	26-Mar-26	28-Mar-26	03-May-26 A	05-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B5-S-1167	Formwork for column neck	2	29-Mar-26	30-Mar-26	06-May-26 A	09-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B5-S-1147	Pouring Concrete for column neck	1	31-Mar-26	31-Mar-26	10-May-26 A	10-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B5-S-1197	Damp proof /Bitumin paint on Footings & column neck	2	01-Apr-26	02-Apr-26	11-May-26 A	12-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B5-S-1257	Backfilling / Compaction up to Bottom of Grade Beams	7	04-Apr-26	11-Apr-26	20-May-26 A	24-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		13	12-Apr-26	28-Apr-26	01-Jun-26 A	18-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B5-S-1077	Lean Concrete Below Grade Beams	2	15-Apr-26	16-Apr-26	01-Jun-26 A	01-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B5-S-1227	Vapour barrier for Grade Beams	2	13-Apr-26	14-Apr-26	01-Jun-26 A	01-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B5-S-1307	Anti Termite Below Grade Beams	1	12-Apr-26	12-Apr-26	01-Jun-26 A	01-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B5-S-1287	Anchor bolts installation	2	23-Apr-26	25-Apr-26	02-Jun-26 A	04-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B5-S-1127	Rebar for Grade Beams	5	18-Apr-26	22-Apr-26	03-Jun-26 A	04-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B5-S-1137	Formwork for Grade Beams	2	23-Apr-26	25-Apr-26	03-Jun-26 A	07-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B5-S-1087	Pouring Concrete for Grade Beams	1	26-Apr-26	26-Apr-26	11-Jun-26 A	11-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B5-S-1237	Damp proof /Bitumin paint on Grade Beams	2	27-Apr-26	28-Apr-26	14-Jun-26 A	18-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		115	29-Apr-26	29-Jun-26	21-Jun-26 A	03-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B5-S-1267	Backfilling / Compaction for Slab on Grade	7	29-Apr-26	06-May-26	21-Jun-26 A	24-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B5-S-1097	Pouring Concrete for Ground Slab	4	11-May-26	14-May-26	01-Aug-26 A	04-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B5-S-1217	Anti Termite Treatment below Ground Slab	1	07-May-26	07-May-26	01-Aug-26 A	04-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B5-S-1247	Vapour barrier for below Ground Slab	2	09-May-26	10-May-26	01-Aug-26 A	04-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B5-S-1277	Concrete pad	7	22-Jun-26	29-Jun-26	27-Oct-26	03-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		77	07-May-26	25-Jul-26	03-Jun-26 A	22-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B5-S-6101	Rebar for Tie Beams	4	19-May-26	23-May-26	03-Jun-26 A	09-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B5-S-6102	Formwork for Tie Beams	2	24-May-26	25-May-26	04-Jun-26 A	10-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B5-S-6103	Pouring Concrete for Tie Beams	1	30-May-26	30-May-26	11-Jun-26 A	11-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B5-S-5101	Rebar for column	5	07-May-26	12-May-26	14-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B5-S-5102	Formwork for column	4	13-May-26	17-May-26	16-Jul-26 A	20-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B5-S-5103	Pouring Concrete for column	1	18-May-26	18-May-26	18-Jul-26 A	21-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B5-S-6113	Rebar for Beams	4	16-Jul-26	21-Jul-26	07-Sep-26 A	15-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B5-S-6123	Formwork for Beams	2	21-Jul-26	23-Jul-26	15-Sep-26 A	20-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B5-S-6133	Pouring Concrete for Beams	1	23-Jul-26	25-Jul-26	17-Sep-26 A	22-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		99	16-May-26	30-Jul-26	02-Jul-26 A	03-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B5-SS-270	Installation of columns	3	16-May-26	18-May-26	02-Jul-26 A	05-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B5-SS-280	Installation of raft and purlins	5	19-May-26	24-May-26	02-Jul-26 A	06-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B5-SS-1840	Intumescent paint to steel works	7	25-May-26	04-Jun-26	12-Jul-26 A	20-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B5-SS-310	Installation of roof sheet	5	25-Jul-26	30-Jul-26	29-Jul-26 A	08-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B5-SS-1030	Steel members for external platform	7	14-Jun-26	21-Jun-26	31-Aug-26 A	01-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B5-SS-300	Installation of wall sandwich panel	5	22-Jun-26	27-Jun-26	04-Oct-26 A	08-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B5-SS-1850	Steel members for office area	7	06-Jun-26	13-Jun-26	05-Oct-26 A	06-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B5-SS-1020	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	27-Oct-26	03-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-1040	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	27-Oct-26	01-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		108	25-May-26	21-Sep-26	08-Aug-26 A	15-Dec-26	900,244.66	900,244.66	222,951.47	100%	24.77%
MASONARY WORKS		26	25-May-26	29-Jun-26	09-Aug-26 A	09-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B5-A-290	Block work at factory area	10	25-May-26	08-Jun-26	09-Aug-26 A	12-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B5-A-320	Block work at office area	7	14-Jun-26	21-Jun-26	13-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B5-A-1440	Block work at toilet area	7	22-Jun-26	29-Jun-26	15-Aug-26 A	09-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		25	09-Jul-26	24-Aug-26	26-Sep-26 A	14-Nov-26	92,757.47	92,757.47	86,132.37	100%	92.86%
DAM3-C-B5-A-1450	Internal Wall Plaster	15	09-Jul-26	26-Jul-26	26-Sep-26 A	11-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B5-A-1500	Paint to Plaster (Primer, Putty & First Coat)	7	17-Aug-26	24-Aug-26	11-Oct-26 A	14-Nov-26	44,167.30	44,167.30	37,542.21	100%	85%
CIELING FINISHES		5	09-Aug-26	13-Aug-26	04-Nov-26	09-Nov-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B5-A-1510	Installation of Ceiling Gypsum Board	5	09-Aug-26	13-Aug-26	04-Nov-26	09-Nov-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		46	01-Aug-26	21-Sep-26	11-Oct-26 A	15-Dec-26	189,488.90	189,488.90	46,530.71	100%	24.56%
DAM3-C-B5-A-1490	Tiles for Toilet	7	01-Aug-26	08-Aug-26	11-Oct-26 A	13-Oct-26 A	46,530.71	46,530.71	46,530.71	100%	100%
DAM3-C-B5-A-1520	Tiles for Office Area	2	15-Aug-26	16-Aug-26	10-Nov-26	11-Nov-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B5-A-1650	Granite strip	2	17-Aug-26	18-Aug-26	12-Nov-26	14-Nov-26	671.12	671.12	0.00	100%	0%
DAM3-C-B5-A-1670	Epoxy paint	7	14-Sep-26	21-Sep-26	08-Dec-26	15-Dec-26	115,419.76	115,419.76	0.00	100%	0%
DOORS & WINDOWS		14	28-Jun-26	13-Jul-26	27-Oct-26	11-Nov-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B5-A-1830	Window (CW1)	7	28-Jun-26	05-Jul-26	27-Oct-26	03-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B5-A-1460	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	04-Nov-26	04-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-1470	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	07-Jul-26	07-Jul-26	05-Nov-26	05-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-1530	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	08-Jul-26	08-Jul-26	07-Nov-26	07-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-1540	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	09-Jul-26	09-Jul-26	08-Nov-26	08-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-1760	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	11-Jul-26	11-Jul-26	09-Nov-26	09-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-1770	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	12-Jul-26	12-Jul-26	10-Nov-26	10-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B5-A-1780	Skylight fixtures installation	1	13-Jul-26	13-Jul-26	11-Nov-26	11-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	27-Jul-26	30-Jul-26	14-Oct-26 A	17-Oct-26 A	4,879.02	4,879.02	4,879.02	100%	100%
DAM3-C-B5-A-1630	Waterproofing membrane for toilets	4	27-Jul-26	30-Jul-26	14-Oct-26 A	17-Oct-26 A	4,879.02	4,879.02	4,879.02	100%	100%
METAL WORKS		24	19-Aug-26	02-Sep-26	08-Aug-26 A	26-Nov-26	193,717.06	193,717.06	6,455.16	100%	3.33%
DAM3-C-B5-A-1570	Galvanised Steel Gratings	2	01-Sep-26	02-Sep-26	08-Aug-26 A	08-Aug-26 A	6,455.16	6,455.16	6,455.16	100%	100%
DAM3-C-B5-A-1560	Steel Ladder	2	19-Aug-26	20-Aug-26	15-Nov-26	16-Nov-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B5-A-1660	Steel railing works	4	22-Aug-26	25-Aug-26	17-Nov-26	21-Nov-26	1,533.98	1,533.98	0.00	100%	0%
DAM3-C-B5-A-1580	Aluminium composite panel	5	26-Aug-26	31-Aug-26	22-Nov-26	26-Nov-26	175,888.76	175,888.76	0.00	100%	0%
SPECIALTIES		9	03-Sep-26	13-Sep-26	28-Nov-26	07-Dec-26	45,080.66	45,080.66	0.00	100%	0%
DAM3-C-B5-A-1590	Installation of fittings	5	03-Sep-26	08-Sep-26	28-Nov-26	02-Dec-26	22,981.27	22,981.27	0.00	100%	0%
DAM3-C-B5-A-1820	Identification sign; ID01 & ID02	3	09-Sep-26	12-Sep-26	03-Dec-26	06-Dec-26	9,630.56	9,630.56	0.00	100%	0%
DAM3-C-B5-A-1610	Furniture Installation	1	13-Sep-26	13-Sep-26	07-Dec-26	07-Dec-26	12,468.83	12,468.83	0.00	100%	0%
MECHANICAL		119	29-Apr-26	13-Sep-26	08-Jul-26 A	03-Dec-26	467,522.66	467,522.66	156,280.78	100%	33.43%
HVAC		14	25-Aug-26	09-Sep-26	14-Nov-26	30-Nov-26	233,183.33	233,183.33	0.00	100%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	01-Sep-26	05-Sep-26	21-Nov-26	25-Nov-26	170,694.73	170,694.73	0.00	100%	0%
DAM3-C-B5-M-1070	Installation of HVAC Ducts	2	01-Sep-26	02-Sep-26	21-Nov-26	23-Nov-26	149,489.33	149,489.33	0.00	100%	0%
DAM3-C-B5-M-1100	Installation of Duct insulation	2	03-Sep-26	05-Sep-26	23-Nov-26	25-Nov-26	21,205.40	21,205.40	0.00	100%	0%
SECOND STAGE		14	25-Aug-26	09-Sep-26	14-Nov-26	30-Nov-26	62,488.60	62,488.60	0.00	100%	0%
DAM3-C-B5-M-1060	Installation of Exhaust Fans	2	25-Aug-26	26-Aug-26	14-Nov-26	16-Nov-26	7,938.56	7,938.56	0.00	100%	0%
DAM3-C-B5-M-1090	Installation of Wall Propeller Type Exhaust Fan	4	27-Aug-26	31-Aug-26	16-Nov-26	21-Nov-26	46,831.64	46,831.64	0.00	100%	0%
DAM3-C-B5-M-1080	Installation of Diffuser	2	06-Sep-26	07-Sep-26	25-Nov-26	28-Nov-26	2,144.00	2,144.00	0.00	100%	0%
DAM3-C-B5-M-1270	Supply, install, test and commission door grilles & exhaust louvers	2	08-Sep-26	09-Sep-26	28-Nov-26	30-Nov-26	5,574.40	5,574.40	0.00	100%	0%
FIRE FIGHTING SYSTEM		20	25-Aug-26	13-Sep-26	11-Oct-26 A	03-Dec-26	102,458.78	102,458.78	84,594.16	100%	82.56%
FIRST STAGE		12	25-Aug-26	07-Sep-26	11-Oct-26 A	13-Oct-26 A	84,594.16	84,594.16	84,594.16	100%	100%
DAM3-C-B5-M-1230	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	25-Aug-26	01-Sep-26	11-Oct-26 A	13-Oct-26 A	72,394.75	72,394.75	72,394.75	100%	100%
DAM3-C-B5-M-1240	Installation of Fire Fighting Valve	5	02-Sep-26	07-Sep-26	11-Oct-26 A	13-Oct-26 A	12,199.40	12,199.40	12,199.40	100%	100%
SECOND STAGE		17	08-Sep-26	13-Sep-26	14-Nov-26	03-Dec-26	17,864.62	17,864.62	0.00	100%	0%
DAM3-C-B5-M-1250	Installation of Fire Hose Cabinet	3	08-Sep-26	10-Sep-26	14-Nov-26	17-Nov-26	15,158.56	15,158.56	0.00	100%	0%
DAM3-C-B5-M-1300	Supply, install, test and commission Fire Department Connection(FDC)	3	10-Sep-26	13-Sep-26	30-Nov-26	03-Dec-26	2,706.06	2,706.06	0.00	100%	0%
SEWER AND DRAINAGE SYSTEM		106	29-Apr-26	01-Sep-26	08-Jul-26 A	18-Nov-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		92	29-Apr-26	16-Aug-26	08-Jul-26 A	02-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B5-M-1130	Installation of Sanitary Waste / Drainage Pipes	4	29-Apr-26	03-May-26	08-Jul-26 A	12-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B5-M-1310	Installation of Trench drain	5	11-Aug-26	16-Aug-26	11-Jul-26 A	14-Jul-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B5-M-1150	Installation of Floor Drain	2	09-Aug-26	10-Aug-26	01-Nov-26	02-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	17-Aug-26	01-Sep-26	03-Nov-26	18-Nov-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B5-M-1110	Installation of Electric Water Heater	2	17-Aug-26	18-Aug-26	03-Nov-26	04-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B5-M-1120	Installation of Sanitary Fixture and Accessories	4	19-Aug-26	23-Aug-26	05-Nov-26	09-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B5-M-1140	Installation of Lavotary /Wash Basin	2	24-Aug-26	25-Aug-26	10-Nov-26	11-Nov-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B5-M-1200	Installation of Bib Tap	2	26-Aug-26	27-Aug-26	12-Nov-26	14-Nov-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B5-M-1160	Installation of Water Tap	2	29-Aug-26	30-Aug-26	15-Nov-26	16-Nov-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B5-M-1170	Installation of Roof Vent Cap	2	31-Aug-26	01-Sep-26	17-Nov-26	18-Nov-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		18	25-Aug-26	06-Sep-26	29-Sep-26 A	19-Nov-26	41,870.81	41,870.81	41,592.68	100%	99.34%
FIRST STAGE		6	25-Aug-26	31-Aug-26	29-Sep-26 A	03-Oct-26 A	41,592.68	41,592.68	41,592.68	100%	100%
DAM3-C-B5-M-1210	Installation of Water Supply Valve	2	30-Aug-26	31-Aug-26	29-Sep-26 A	03-Oct-26 A	18,274.27	18,274.27	18,274.27	100%	100%
DAM3-C-B5-M-1220	Installation of Water Supply Pipes	4	25-Aug-26	29-Aug-26	29-Sep-26 A	03-Oct-26 A	23,318.41	23,318.41	23,318.41	100%	100%
SECOND STAGE		5	01-Sep-26	06-Sep-26	14-Nov-26	19-Nov-26	278.13	278.13	0.00	100%	0%
DAM3-C-B5-M-1260	Capped connection	5	01-Sep-26	06-Sep-26	14-Nov-26	19-Nov-26	278.13	278.13	0.00	100%	0%
ELECTRICAL		118	30-Jun-26	23-Nov-26	04-Jun-26 A	23-Dec-26	752,044.76	498,776.05	136,576.62	66.32%	18.16%
FIRST STAGE		118	30-Jun-26	13-Oct-26	04-Jun-26 A	16-Dec-26	86,114.12	86,114.12	36,105.84	100%	41.93%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	04-Jun-26 A	12-Dec-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm System	4	01-Sep-26	05-Sep-26	04-Jun-26 A	23-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	04-Jun-26 A	31-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	15-Sep-26	19-Sep-26	20-Sep-26 A	28-Nov-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B5-E-923	Installation of Wires	4	20-Sep-26	24-Sep-26	24-Oct-26 A	30-Nov-26	16,925.94	16,925.94	8,462.97	100%	50%
DAM3-C-B5-E-913	Installation of LV Cables	4	10-Oct-26	13-Oct-26	12-Dec-26	16-Dec-26	36,389.98	36,389.98	0.00	100%	0%
SECOND STAGE		52	25-Aug-26	23-Nov-26	10-Oct-26 A	23-Dec-26	665,930.64	412,661.93	100,470.78	61.97%	15.09%
DAM3-C-B5-E-933	Installation of LP-1 Panel	2	03-Oct-26	04-Oct-26	10-Oct-26 A	14-Oct-26 A	18,403.54	18,403.54	18,403.54	100%	100%
DAM3-C-B5-E-1350	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	11-Oct-26 A	17-Nov-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B5-E-823	Installation of Fire Detectors & Accessories	4	10-Sep-26	14-Sep-26	25-Oct-26 A	25-Oct-26 A	56,740.37	56,740.37	56,740.37	100%	100%
DAM3-C-B5-E-863	Installation of Wiring Devices	4	25-Aug-26	29-Aug-26	14-Nov-26	18-Nov-26	19,435.09	19,435.09	0.00	100%	0%
DAM3-C-B5-E-893	Installation of Disconnect Switches	2	30-Aug-26	31-Aug-26	18-Nov-26	21-Nov-26	30,235.95	30,235.95	0.00	100%	0%
DAM3-C-B5-E-813	Installation of Fire Alarm Control Panel	4	06-Sep-26	09-Sep-26	23-Nov-26	28-Nov-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B5-E-843	Installation of Lighting fixtures	4	26-Sep-26	29-Sep-26	30-Nov-26	05-Dec-26	76,166.74	76,166.74	0.00	100%	0%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B5-E-883	Installation of Main Distribution Board	2	30-Sep-26	01-Oct-26	05-Dec-26	07-Dec-26	32,472.73	32,472.73	0.00	100%	0%
DAM3-C-B5-E-943	Installation of PP-AC panel	2	05-Oct-26	06-Oct-26	07-Dec-26	09-Dec-26	21,648.48	21,648.48	0.00	100%	0%
DAM3-C-B5-E-903	Installation of Telephone Cabinet	2	07-Oct-26	08-Oct-26	09-Dec-26	12-Dec-26	26,991.08	26,991.08	0.00	100%	0%
DAM3-C-B5-E-1340	Installation of CCTV System	7	07-Oct-26	14-Oct-26	09-Dec-26	17-Dec-26	76,349.24	76,349.24	0.00	100%	0%
DAM3-C-B5-E-963	Installation of Access Control System	4	10-Oct-26	13-Oct-26	12-Dec-26	16-Dec-26	27,616.86	27,616.86	0.00	100%	0%
DAM3-C-B5-E-973	Monitor Modules for Fire Alarm	2	14-Oct-26	15-Oct-26	16-Dec-26	19-Dec-26	3,882.38	3,882.38	0.00	100%	0%
DAM3-C-B5-E-983	Line Isolator Modules for Fire Alarm	2	17-Oct-26	18-Oct-26	19-Dec-26	21-Dec-26	185.40	185.40	0.00	100%	0%
DAM3-C-B5-E-993	Firewarning flash light with sounder; wall mounted, Weather proof	2	19-Oct-26	20-Oct-26	21-Dec-26	23-Dec-26	3,082.69	3,082.69	0.00	100%	0%
BLOCK B4		246	25-Feb-26	01-Dec-26	17-Feb-26 A	07-Jan-27	5,075,523.09	4,761,515.06	3,443,717.57	93.81%	67.85%
STRUCTURAL		204	25-Feb-26	21-Jul-26	17-Feb-26 A	19-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		36	25-Feb-26	30-Mar-26	17-Feb-26 A	30-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B4-S-210	Excavation for footings	4	25-Feb-26	02-Mar-26	17-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B4-S-6183	Soil replacement - rock fill	4	03-Mar-26	07-Mar-26	26-Mar-26 A	29-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B4-S-6193	Engineering fill	4	08-Mar-26	11-Mar-26	02-Apr-26 A	05-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B4-S-797	Lean Concrete Below Footings	2	15-Mar-26	16-Mar-26	15-Apr-26 A	15-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B4-S-947	Vapour Barrier for Footings	1	14-Mar-26	14-Mar-26	15-Apr-26 A	15-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B4-S-1037	Anti Termite Below Footings	1	12-Mar-26	12-Mar-26	15-Apr-26 A	15-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B4-S-857	Formwork for Footings	4	25-Mar-26	29-Mar-26	20-Apr-26 A	22-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B4-S-847	Rebar for Footings	4	21-Mar-26	24-Mar-26	23-Apr-26 A	28-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B4-S-807	Pouring Concrete for Footings	1	30-Mar-26	30-Mar-26	30-Apr-26 A	30-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		17	31-Mar-26	15-Apr-26	23-Apr-26 A	19-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B4-S-897	Rebar for column neck	2	31-Mar-26	01-Apr-26	23-Apr-26 A	28-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B4-S-907	Formwork for column neck	2	02-Apr-26	04-Apr-26	03-May-26 A	05-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B4-S-887	Pouring Concrete for column neck	1	05-Apr-26	05-Apr-26	05-May-26 A	05-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B4-S-937	Damp proof /Bitumin paint on Footings & column neck	2	06-Apr-26	07-Apr-26	07-May-26 A	10-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B4-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	08-Apr-26	15-Apr-26	13-May-26 A	19-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		17	16-Apr-26	06-May-26	20-May-26 A	09-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B4-S-817	Lean Concrete Below Grade Beams	2	20-Apr-26	21-Apr-26	20-May-26 A	20-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B4-S-967	Vapour barrier for Grade Beams	2	18-Apr-26	19-Apr-26	20-May-26 A	20-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B4-S-1047	Anti Termite Below Grade Beams	1	16-Apr-26	16-Apr-26	20-May-26 A	20-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B4-S-867	Rebar for Grade Beams	5	22-Apr-26	27-Apr-26	21-May-26 A	24-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B4-S-877	Formwork for Grade Beams	2	28-Apr-26	29-Apr-26	24-May-26 A	02-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B4-S-1027	Anchor bolts installation	2	28-Apr-26	29-Apr-26	31-May-26 A	01-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B4-S-827	Pouring Concrete for Grade Beams	1	30-Apr-26	30-Apr-26	03-Jun-26 A	03-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B4-S-977	Damp proof /Bitumin paint on Grade Beams	5	02-May-26	06-May-26	07-Jun-26 A	09-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		134	07-May-26	21-Jul-26	14-Jun-26 A	19-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B4-S-1007	Backfilling / Compaction for Slab on Grade	7	07-May-26	14-May-26	14-Jun-26 A	22-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B4-S-837	Pouring Concrete for Ground Slab	4	19-May-26	23-May-26	29-Jul-26 A	01-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B4-S-957	Anti Termite Treatment below Ground Slab	1	16-May-26	16-May-26	29-Jul-26 A	01-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B4-S-987	Vapour barrier for below Ground Slab	2	17-May-26	18-May-26	29-Jul-26 A	01-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B4-S-1017	Concrete pad	7	14-Jul-26	21-Jul-26	12-Nov-26	19-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		61	16-May-26	15-Jun-26	21-May-26 A	14-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B4-S-6101	Rebar for Tie Beams	4	31-May-26	03-Jun-26	21-May-26 A	24-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B4-S-6102	Formwork for Tie Beams	2	04-Jun-26	06-Jun-26	24-May-26 A	02-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B4-S-6103	Pouring Concrete for Tie Beams	1	07-Jun-26	07-Jun-26	03-Jun-26 A	03-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B4-S-5101	Rebar for column	5	16-May-26	20-May-26	22-Jun-26 A	02-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B4-S-5102	Formwork for column	4	21-May-26	25-May-26	29-Jun-26 A	05-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B4-S-5103	Pouring Concrete for column	1	30-May-26	30-May-26	09-Jul-26 A	12-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B4-S-6113	Rebar for Beams	4	08-Jun-26	11-Jun-26	30-Aug-26 A	01-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B4-S-6123	Formwork for Beams	2	13-Jun-26	14-Jun-26	02-Sep-26 A	08-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B4-S-6133	Pouring Concrete for Beams	1	15-Jun-26	15-Jun-26	08-Sep-26 A	14-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		104	25-May-26	19-Jul-26	24-Jun-26 A	11-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B4-A-210	Installation of columns	3	25-May-26	31-May-26	24-Jun-26 A	24-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B4-A-220	Installation of raft and purlins	5	01-Jun-26	06-Jun-26	25-Jun-26 A	25-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-A-1430	Intumescent paint to steel works	7	07-Jun-26	14-Jun-26	08-Jul-26 A	14-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B4-A-250	Installation of roof sheet	5	21-Jun-26	25-Jun-26	26-Jul-26 A	30-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B4-SS-1030	Steel members for external platform	7	23-Jun-26	30-Jun-26	01-Sep-26 A	02-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B4-A-1440	Steel members for office area	7	15-Jun-26	22-Jun-26	01-Oct-26 A	04-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B4-A-240	Installation of wall sandwich panel	5	14-Jul-26	19-Jul-26	03-Oct-26 A	20-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-SS-1040	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	27-Oct-26	01-Nov-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-1020	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	04-Nov-26	11-Nov-26	23,161.04	23,161.04	0.00	100%	0%
ARCHITECTURAL		119	09-Jun-26	17-Oct-26	03-Aug-26 A	03-Jan-27	900,244.66	900,244.66	222,951.47	100%	24.77%
MASONARY WORKS		30	09-Jun-26	21-Jul-26	05-Aug-26 A	01-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B4-A-1030	Block work at toilet area	7	14-Jul-26	21-Jul-26	05-Aug-26 A	24-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B4-A-230	Block work at factory area	10	09-Jun-26	20-Jun-26	05-Aug-26 A	10-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B4-A-260	Block work at office area	7	06-Jul-26	13-Jul-26	05-Aug-26 A	01-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		28	01-Aug-26	15-Sep-26	24-Sep-26 A	30-Nov-26	92,757.47	92,757.47	86,132.37	100%	92.86%
DAM3-C-B4-A-1040	Internal Wall Plaster	10	01-Aug-26	17-Aug-26	24-Sep-26 A	06-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B4-A-1090	Paint to Plaster (Primer, Putty & First Coat)	7	08-Sep-26	15-Sep-26	07-Oct-26 A	30-Nov-26	44,167.30	44,167.30	37,542.21	100%	85%
CIELING FINISHES		5	31-Aug-26	05-Sep-26	21-Nov-26	25-Nov-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B4-A-1100	Installation of Ceiling Gypsum Board	5	31-Aug-26	05-Sep-26	21-Nov-26	25-Nov-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		49	23-Aug-26	17-Oct-26	05-Oct-26 A	03-Jan-27	189,488.90	189,488.90	46,530.71	100%	24.56%
DAM3-C-B4-A-1080	Tiles for Toilet	7	23-Aug-26	30-Aug-26	05-Oct-26 A	10-Oct-26 A	46,530.71	46,530.71	46,530.71	100%	100%
DAM3-C-B4-A-1110	Tiles for Office Area	2	06-Sep-26	07-Sep-26	26-Nov-26	28-Nov-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B4-A-1240	Granite strip	2	08-Sep-26	09-Sep-26	29-Nov-26	30-Nov-26	671.12	671.12	0.00	100%	0%
DAM3-C-B4-A-1260	Epoxy paint	7	10-Oct-26	17-Oct-26	27-Dec-26	03-Jan-27	115,419.76	115,419.76	0.00	100%	0%
DOORS & WINDOWS		14	20-Jul-26	04-Aug-26	12-Nov-26	28-Nov-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B4-A-1420	Window (CW1)	7	20-Jul-26	27-Jul-26	12-Nov-26	19-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B4-A-1050	Roll up Shutter Door	1	28-Jul-26	28-Jul-26	21-Nov-26	21-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B4-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	29-Jul-26	29-Jul-26	22-Nov-26	22-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B4-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	30-Jul-26	30-Jul-26	23-Nov-26	23-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B4-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	01-Aug-26	01-Aug-26	24-Nov-26	24-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B4-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	02-Aug-26	02-Aug-26	25-Nov-26	25-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B4-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	03-Aug-26	03-Aug-26	26-Nov-26	26-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B4-A-1370	Skylight fixtures installation	1	04-Aug-26	04-Aug-26	28-Nov-26	28-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	18-Aug-26	22-Aug-26	18-Oct-26 A	20-Oct-26 A	4,879.02	4,879.02	4,879.02	100%	100%
DAM3-C-B4-A-1220	Waterproofing membrane for toilets	4	18-Aug-26	22-Aug-26	18-Oct-26 A	20-Oct-26 A	4,879.02	4,879.02	4,879.02	100%	100%
METAL WORKS		26	10-Sep-26	26-Sep-26	03-Aug-26 A	13-Dec-26	193,717.06	193,717.06	6,455.16	100%	3.33%
DAM3-C-B4-A-1160	Galvanised Steel Gratings	2	24-Sep-26	26-Sep-26	03-Aug-26 A	03-Aug-26 A	6,455.16	6,455.16	6,455.16	100%	100%
DAM3-C-B4-A-1150	Steel Ladder	2	10-Sep-26	12-Sep-26	01-Dec-26	02-Dec-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B4-A-1250	Steel railing works	4	13-Sep-26	16-Sep-26	03-Dec-26	07-Dec-26	1,533.98	1,533.98	0.00	100%	0%
DAM3-C-B4-A-1170	Aluminium composite panel	5	17-Sep-26	22-Sep-26	08-Dec-26	13-Dec-26	175,888.76	175,888.76	0.00	100%	0%
SPECIALTIES		11	27-Sep-26	08-Oct-26	14-Dec-26	26-Dec-26	45,080.66	45,080.66	0.00	100%	0%
DAM3-C-B4-A-1180	Installation of fittings	7	27-Sep-26	04-Oct-26	14-Dec-26	21-Dec-26	22,981.27	22,981.27	0.00	100%	0%
DAM3-C-B4-A-1410	Identification sign; ID01 & ID02	3	05-Oct-26	07-Oct-26	22-Dec-26	24-Dec-26	9,630.56	9,630.56	0.00	100%	0%
DAM3-C-B4-A-1200	Furniture Installation	1	08-Oct-26	08-Oct-26	26-Dec-26	26-Dec-26	12,468.83	12,468.83	0.00	100%	0%
MECHANICAL		150	07-May-26	06-Oct-26	25-Jun-26 A	20-Dec-26	467,522.66	467,522.66	156,280.78	100%	33.43%
HVAC		14	16-Sep-26	03-Oct-26	30-Nov-26	16-Dec-26	233,183.33	233,183.33	0.00	100%	0%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	24-Sep-26	28-Sep-26	07-Dec-26	12-Dec-26	170,694.73	170,694.73	0.00	100%	0%
DAM3-C-B4-M-760	Installation of HVAC Ducts	2	24-Sep-26	26-Sep-26	07-Dec-26	09-Dec-26	149,489.33	149,489.33	0.00	100%	0%
DAM3-C-B4-M-790	Installation of Duct insulation	2	27-Sep-26	28-Sep-26	09-Dec-26	12-Dec-26	21,205.40	21,205.40	0.00	100%	0%
SECOND STAGE		14	16-Sep-26	03-Oct-26	30-Nov-26	16-Dec-26	62,488.60	62,488.60	0.00	100%	0%
DAM3-C-B4-M-750	Installation of Exhaust Fans	2	16-Sep-26	17-Sep-26	30-Nov-26	02-Dec-26	7,938.56	7,938.56	0.00	100%	0%
DAM3-C-B4-M-780	Installation of Wall Propeller Type Exhaust Fan	4	19-Sep-26	22-Sep-26	02-Dec-26	07-Dec-26	46,831.64	46,831.64	0.00	100%	0%
DAM3-C-B4-M-770	Installation of Diffuser	2	29-Sep-26	30-Sep-26	12-Dec-26	14-Dec-26	2,144.00	2,144.00	0.00	100%	0%
DAM3-C-B4-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	01-Oct-26	03-Oct-26	14-Dec-26	16-Dec-26	5,574.40	5,574.40	0.00	100%	0%
FIRE FIGHTING SYSTEM		18	16-Sep-26	06-Oct-26	30-Sep-26 A	20-Dec-26	102,458.78	102,458.78	84,594.16	100%	82.56%
FIRST STAGE		12	16-Sep-26	30-Sep-26	30-Sep-26 A	04-Oct-26 A	84,594.16	84,594.16	84,594.16	100%	100%
DAM3-C-B4-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	16-Sep-26	24-Sep-26	30-Sep-26 A	04-Oct-26 A	72,394.75	72,394.75	72,394.75	100%	100%
DAM3-C-B4-M-930	Installation of Fire Fighting Valve	5	26-Sep-26	30-Sep-26	30-Sep-26 A	04-Oct-26 A	12,199.40	12,199.40	12,199.40	100%	100%
SECOND STAGE		17	01-Oct-26	06-Oct-26	30-Nov-26	20-Dec-26	17,864.62	17,864.62	0.00	100%	0%
DAM3-C-B4-M-940	Installation of Fire Hose Cabinet	3	01-Oct-26	04-Oct-26	30-Nov-26	03-Dec-26	15,158.56	15,158.56	0.00	100%	0%
DAM3-C-B4-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	04-Oct-26	06-Oct-26	16-Dec-26	20-Dec-26	2,706.06	2,706.06	0.00	100%	0%
SEWER AND DRAINAGE SYSTEM		139	07-May-26	24-Sep-26	25-Jun-26 A	08-Dec-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		125	07-May-26	07-Sep-26	25-Jun-26 A	22-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B4-M-1000	Installation of Trench drain	5	02-Sep-26	07-Sep-26	25-Jun-26 A	28-Jun-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B4-M-820	Installation of Sanitary Waste / Drainage Pipes	4	07-May-26	11-May-26	27-Jun-26 A	29-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B4-M-840	Installation of Floor Drain	2	31-Aug-26	01-Sep-26	21-Nov-26	22-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	08-Sep-26	24-Sep-26	23-Nov-26	08-Dec-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B4-M-800	Installation of Electric Water Heater	2	08-Sep-26	09-Sep-26	23-Nov-26	24-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B4-M-810	Installation of Sanitary Fixture and Accessories	4	10-Sep-26	14-Sep-26	25-Nov-26	29-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B4-M-830	Installation of Lavotary /Wash Basin	2	15-Sep-26	16-Sep-26	30-Nov-26	01-Dec-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B4-M-890	Installation of Bib Tap	2	17-Sep-26	19-Sep-26	02-Dec-26	03-Dec-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B4-M-850	Installation of Water Tap	2	20-Sep-26	21-Sep-26	05-Dec-26	06-Dec-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B4-M-860	Installation of Roof Vent Cap	2	22-Sep-26	24-Sep-26	07-Dec-26	08-Dec-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		12	16-Sep-26	29-Sep-26	22-Sep-26 A	06-Dec-26	41,870.81	41,870.81	41,592.68	100%	99.34%
FIRST STAGE		7	16-Sep-26	22-Sep-26	22-Sep-26 A	29-Sep-26 A	41,592.68	41,592.68	41,592.68	100%	100%
DAM3-C-B4-M-910	Installation of Water Supply Pipes	4	16-Sep-26	20-Sep-26	22-Sep-26 A	29-Sep-26 A	23,318.41	23,318.41	23,318.41	100%	100%
DAM3-C-B4-M-900	Installation of Water Supply Valve	2	21-Sep-26	22-Sep-26	24-Sep-26 A	29-Sep-26 A	18,274.27	18,274.27	18,274.27	100%	100%
SECOND STAGE		5	24-Sep-26	29-Sep-26	30-Nov-26	06-Dec-26	278.13	278.13	0.00	100%	0%
DAM3-C-B4-M-950	Capped connection	5	24-Sep-26	29-Sep-26	30-Nov-26	06-Dec-26	278.13	278.13	0.00	100%	0%
ELECTRICAL		104	22-Jul-26	01-Dec-26	24-May-26 A	07-Jan-27	752,044.76	438,036.73	136,576.62	58.25%	18.16%
FIRST STAGE		103	22-Jul-26	28-Oct-26	24-May-26 A	06-Jan-27	86,114.12	58,095.90	36,105.84	67.46%	41.93%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	24-May-26 A	03-Jan-27	19,646.47	9,823.23	17,681.82	50%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	24-Sep-26	28-Sep-26	24-May-26 A	09-Dec-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	24-May-26 A	16-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	12-Sep-26 A	14-Dec-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B4-E-693	Installation of Wires	4	13-Oct-26	17-Oct-26	17-Nov-26 A	28-Dec-26	16,925.94	16,925.94	8,462.97	100%	50%
DAM3-C-B4-E-683	Installation of LV Cables	4	25-Oct-26	28-Oct-26	03-Jan-27	06-Jan-27	36,389.98	18,194.99	0.00	50%	0%
SECOND STAGE		52	16-Sep-26	01-Dec-26	10-Oct-26 A	07-Jan-27	665,930.64	379,940.83	100,470.78	57.05%	15.09%
DAM3-C-B4-E-1040	Installation of Solar power plant	7	24-Nov-26	01-Dec-26	10-Oct-26 A	25-Nov-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B4-E-703	Installation of LP-1 Panel	2	20-Oct-26	21-Oct-26	10-Oct-26 A	14-Oct-26 A	18,403.54	18,403.54	18,403.54	100%	100%
DAM3-C-B4-E-593	Installation of Fire Detectors & Accessories	4	04-Oct-26	07-Oct-26	25-Oct-26 A	25-Oct-26 A	56,740.37	56,740.37	56,740.37	100%	100%
DAM3-C-B4-E-633	Installation of Wiring Devices	4	16-Sep-26	20-Sep-26	30-Nov-26	05-Dec-26	19,435.09	19,435.09	0.00	100%	0%
DAM3-C-B4-E-663	Installation of Disconnect Switches	2	21-Sep-26	22-Sep-26	05-Dec-26	07-Dec-26	30,235.95	30,235.95	0.00	100%	0%
DAM3-C-B4-E-583	Installation of Fire Alarm Control Panel	4	29-Sep-26	03-Oct-26	09-Dec-26	14-Dec-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B4-E-733	Installation of Access Control System	5	08-Oct-26	13-Oct-26	14-Dec-26	20-Dec-26	27,616.86	27,616.86	0.00	100%	0%




Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B4-E-743	Monitor Modules for Fire Alarm	2	14-Oct-26	15-Oct-26	20-Dec-26	22-Dec-26	3,882.38	3,882.38	0.00	100%	0%
DAM3-C-B4-E-753	Line Isolator Modules for Fire Alarm	2	17-Oct-26	18-Oct-26	22-Dec-26	24-Dec-26	185.40	185.40	0.00	100%	0%
DAM3-C-B4-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	19-Oct-26	20-Oct-26	24-Dec-26	27-Dec-26	3,082.69	3,082.69	0.00	100%	0%
DAM3-C-B4-E-613	Installation of Lighting fixtures	4	18-Oct-26	21-Oct-26	29-Dec-26	02-Jan-27	76,166.74	76,166.74	0.00	100%	0%
DAM3-C-B4-E-653	Installation of Main Distribution Board	2	18-Oct-26	19-Oct-26	29-Dec-26	30-Dec-26	32,472.73	32,472.73	0.00	100%	0%
DAM3-C-B4-E-1030	Installation of CCTV System	7	22-Oct-26	29-Oct-26	31-Dec-26	07-Jan-27	76,349.24	43,628.13	0.00	57.14%	0%
DAM3-C-B4-E-713	Installation of PP-AC panel	2	22-Oct-26	24-Oct-26	31-Dec-26	02-Jan-27	21,648.48	21,648.48	0.00	100%	0%
DAM3-C-B4-E-673	Installation of Telephone Cabinet	2	25-Oct-26	26-Oct-26	03-Jan-27	04-Jan-27	26,991.08	26,991.08	0.00	100%	0%
BLOCK B3		303	03-Mar-26	28-Dec-26	17-Feb-26 A	06-Feb-27	5,075,523.09	3,476,170.36	3,342,582.89	68.49%	65.86%
STRUCTURAL		186	03-Mar-26	18-Jul-26	17-Feb-26 A	03-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		46	03-Mar-26	04-Apr-26	17-Feb-26 A	17-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B3-S-210	Excavation for footings	4	03-Mar-26	07-Mar-26	17-Feb-26 A	12-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B3-S-6203	Soil replacement - rock fill	4	08-Mar-26	11-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B3-S-6213	Engineering fill	4	12-Mar-26	16-Mar-26	28-Mar-26 A	07-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B3-S-797	Lean Concrete Below Footings	2	23-Mar-26	24-Mar-26	11-Apr-26 A	11-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B3-S-947	Vapour Barrier for Footings	1	22-Mar-26	22-Mar-26	11-Apr-26 A	11-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B3-S-1037	Anti Termite Below Footings	1	21-Mar-26	21-Mar-26	11-Apr-26 A	11-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B3-S-847	Rebar for Footings	4	25-Mar-26	29-Mar-26	06-May-26 A	11-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B3-S-857	Formwork for Footings	4	30-Mar-26	02-Apr-26	11-May-26 A	13-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B3-S-807	Pouring Concrete for Footings	1	04-Apr-26	04-Apr-26	17-May-26 A	17-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		12	05-Apr-26	20-Apr-26	11-May-26 A	09-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B3-S-897	Rebar for column neck	2	05-Apr-26	06-Apr-26	11-May-26 A	14-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B3-S-887	Pouring Concrete for column neck	1	09-Apr-26	09-Apr-26	20-May-26 A	20-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B3-S-937	Damp proof /Bitumin paint on Footings & column neck	2	11-Apr-26	12-Apr-26	20-May-26 A	23-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B3-S-907	Formwork for column neck	2	07-Apr-26	08-Apr-26	21-May-26 A	23-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B3-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	13-Apr-26	20-Apr-26	24-May-26 A	09-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		15	21-Apr-26	11-May-26	14-Jun-26 A	30-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B3-S-817	Lean Concrete Below Grade Beams	2	25-Apr-26	26-Apr-26	14-Jun-26 A	14-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B3-S-967	Vapour barrier for Grade Beams	2	22-Apr-26	23-Apr-26	14-Jun-26 A	14-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B3-S-1047	Anti Termite Below Grade Beams	1	21-Apr-26	21-Apr-26	14-Jun-26 A	14-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B3-S-867	Rebar for Grade Beams	5	27-Apr-26	02-May-26	16-Jun-26 A	20-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B3-S-877	Formwork for Grade Beams	2	03-May-26	04-May-26	18-Jun-26 A	22-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B3-S-1027	Anchor bolts installation	2	03-May-26	04-May-26	18-Jun-26 A	20-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B3-S-827	Pouring Concrete for Grade Beams	1	05-May-26	05-May-26	24-Jun-26 A	24-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B3-S-977	Damp proof /Bitumin paint on Grade Beams	5	06-May-26	11-May-26	27-Jun-26 A	30-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		103	12-May-26	18-Jul-26	06-Jul-26 A	03-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B3-S-1007	Backfilling / Compaction for Slab on Grade	7	12-May-26	19-May-26	06-Jul-26 A	09-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B3-S-837	Pouring Concrete for Ground Slab	4	24-May-26	31-May-26	11-Aug-26 A	15-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B3-S-957	Anti Termite Treatment below Ground Slab	1	20-May-26	20-May-26	11-Aug-26 A	15-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B3-S-987	Vapour barrier for below Ground Slab	2	21-May-26	23-May-26	11-Aug-26 A	15-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B3-S-1017	Concrete pad	7	11-Jul-26	18-Jul-26	27-Oct-26	03-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		59	20-May-26	20-Jun-26	16-Jun-26 A	05-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B3-S-6101	Rebar for Tie Beams	4	04-Jun-26	08-Jun-26	16-Jun-26 A	20-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B3-S-6102	Formwork for Tie Beams	2	09-Jun-26	10-Jun-26	18-Jun-26 A	22-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B3-S-6103	Pouring Concrete for Tie Beams	1	11-Jun-26	11-Jun-26	24-Jun-26 A	24-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B3-S-5101	Rebar for column	5	20-May-26	25-May-26	22-Jul-26 A	25-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B3-S-5102	Formwork for column	4	30-May-26	02-Jun-26	27-Jul-26 A	02-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B3-S-5103	Pouring Concrete for column	1	03-Jun-26	03-Jun-26	29-Jul-26 A	03-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B3-S-6113	Rebar for Beams	4	13-Jun-26	16-Jun-26	08-Sep-26 A	15-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B3-S-6123	Formwork for Beams	2	17-Jun-26	18-Jun-26	23-Sep-26 A	29-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B3-S-6133	Pouring Concrete for Beams	1	20-Jun-26	20-Jun-26	26-Sep-26 A	05-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		87	07-Jun-26	15-Jul-26	15-Jul-26 A	03-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B3-A-210	Installation of columns	3	07-Jun-26	09-Jun-26	15-Jul-26 A	15-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B3-A-220	Installation of raft and purlins	5	10-Jun-26	15-Jun-26	15-Jul-26 A	16-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B3-A-1430	Intumescent paint to steel works	7	16-Jun-26	23-Jun-26	25-Jul-26 A	29-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B3-A-250	Installation of roof sheet	5	02-Jul-26	07-Jul-26	16-Aug-26 A	23-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	07-Oct-26 A	20-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	11-Jul-26	15-Jul-26	12-Oct-26 A	20-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B3-SS-1030	Steel members for external platform	7	02-Jul-26	09-Jul-26	24-Oct-26 A	25-Oct-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B3-SS-1020	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	27-Oct-26	03-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-1040	Epoxy paint for external platform	5	11-Jul-26	15-Jul-26	27-Oct-26	01-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		137	21-Jun-26	20-Dec-26	18-Aug-26 A	01-Feb-27	900,244.66	427,529.16	187,020.13	47.49%	20.77%
MASONARY WORKS		25	21-Jun-26	18-Jul-26	24-Aug-26 A	09-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B3-A-230	Block work at factory area	10	21-Jun-26	01-Jul-26	24-Aug-26 A	01-Sep-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B3-A-1030	Block work at toilet area	7	11-Jul-26	18-Jul-26	25-Aug-26 A	03-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B3-A-260	Block work at office area	7	02-Jul-26	09-Jul-26	25-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		62	28-Jul-26	19-Nov-26	12-Oct-26 A	07-Jan-27	92,757.47	48,590.16	48,590.16	52.38%	52.38%
DAM3-C-B3-A-1040	Internal Wall Plaster	10	28-Jul-26	13-Aug-26	12-Oct-26 A	20-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B3-A-1090	Paint to Plaster (Primer, Putty & First Coat)	2	12-Nov-26	19-Nov-26	05-Jan-27	07-Jan-27	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		5	04-Nov-26	09-Nov-26	28-Dec-26	03-Jan-27	46,792.30	0.00	0.00	0%	0%
DAM3-C-B3-A-1100	Installation of Ceiling Gypsum Board	5	04-Nov-26	09-Nov-26	28-Dec-26	03-Jan-27	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		70	19-Aug-26	20-Dec-26	18-Oct-26 A	01-Feb-27	189,488.90	46,530.71	46,530.71	24.56%	24.56%
DAM3-C-B3-A-1080	Tiles for Toilet	7	19-Aug-26	26-Aug-26	18-Oct-26 A	26-Oct-26 A	46,530.71	46,530.71	46,530.71	100%	100%
DAM3-C-B3-A-1110	Tiles for Office Area	2	10-Nov-26	11-Nov-26	03-Jan-27	05-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B3-A-1240	Granite strip	2	12-Nov-26	14-Nov-26	05-Jan-27	07-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B3-A-1260	Epoxy paint	3	13-Dec-26	20-Dec-26	28-Jan-27	01-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		13	16-Jul-26	01-Aug-26	18-Oct-26 A	10-Nov-26	248,575.06	248,575.06	6,489.89	100%	2.61%
DAM3-C-B3-A-1370	Skylight fixtures installation	1	01-Aug-26	01-Aug-26	18-Oct-26 A	20-Oct-26 A	6,489.89	6,489.89	6,489.89	100%	100%
DAM3-C-B3-A-1420	Window (CW1)	7	16-Jul-26	23-Jul-26	27-Oct-26	03-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B3-A-1050	Roll up Shutter Door	1	25-Jul-26	25-Jul-26	04-Nov-26	04-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B3-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	26-Jul-26	26-Jul-26	05-Nov-26	05-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	27-Jul-26	27-Jul-26	07-Nov-26	07-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B3-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	28-Jul-26	28-Jul-26	08-Nov-26	08-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B3-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	29-Jul-26	29-Jul-26	09-Nov-26	09-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	30-Jul-26	30-Jul-26	10-Nov-26	10-Nov-26	16,711.52	16,711.52	0.00	100%	0%
WATER PROOFING WORKS		4	15-Aug-26	18-Aug-26	07-Nov-26	11-Nov-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B3-A-1220	Waterproofing membrane for toilets	4	15-Aug-26	18-Aug-26	07-Nov-26	11-Nov-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		13	15-Nov-26	29-Nov-26	18-Aug-26 A	20-Jan-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B3-A-1160	Galvanised Steel Gratings	2	28-Nov-26	29-Nov-26	18-Aug-26 A	18-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B3-A-1150	Steel Ladder	2	15-Nov-26	16-Nov-26	07-Jan-27	10-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B3-A-1250	Steel railing works	4	17-Nov-26	21-Nov-26	10-Jan-27	14-Jan-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B3-A-1170	Aluminium composite panel	5	22-Nov-26	26-Nov-26	14-Jan-27	20-Jan-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	30-Nov-26	12-Dec-26	20-Jan-27	28-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B3-A-1180	Installation of fittings	3	30-Nov-26	07-Dec-26	20-Jan-27	24-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B3-A-1410	Identification sign; ID01 & ID02	3	08-Dec-26	10-Dec-26	24-Jan-27	27-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B3-A-1200	Furniture Installation	1	12-Dec-26	12-Dec-26	27-Jan-27	28-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		154	12-May-26	09-Dec-26	30-Jul-26 A	27-Jan-27	467,522.66	90,009.74	156,280.78	19.25%	33.43%
HVAC		14	21-Nov-26	06-Dec-26	07-Jan-27	24-Jan-27	233,183.33	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	28-Nov-26	01-Dec-26	14-Jan-27	19-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B3-M-760	Installation of HVAC Ducts	2	28-Nov-26	29-Nov-26	14-Jan-27	17-Jan-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B3-M-790	Installation of Duct insulation	2	30-Nov-26	01-Dec-26	17-Jan-27	19-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	21-Nov-26	06-Dec-26	07-Jan-27	24-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B3-M-750	Installation of Exhaust Fans	2	21-Nov-26	22-Nov-26	07-Jan-27	10-Jan-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B3-M-780	Installation of Wall Propeller Type Exhaust Fan	4	23-Nov-26	26-Nov-26	10-Jan-27	14-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B3-M-770	Installation of Diffuser	2	02-Dec-26	03-Dec-26	19-Jan-27	21-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B3-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	05-Dec-26	06-Dec-26	21-Jan-27	24-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		17	21-Nov-26	09-Dec-26	21-Sep-26 A	27-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		12	21-Nov-26	03-Dec-26	21-Sep-26 A	28-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B3-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	21-Nov-26	28-Nov-26	21-Sep-26 A	28-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B3-M-930	Installation of Fire Fighting Valve	5	29-Nov-26	03-Dec-26	22-Sep-26 A	28-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	05-Dec-26	09-Dec-26	07-Jan-27	27-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B3-M-940	Installation of Fire Hose Cabinet	3	05-Dec-26	07-Dec-26	07-Jan-27	11-Jan-27	15,158.56	0.00	0.00	0%	0%
DAM3-C-B3-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	07-Dec-26	09-Dec-26	24-Jan-27	27-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		104	12-May-26	20-Sep-26	30-Jul-26 A	30-Nov-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		90	12-May-26	03-Sep-26	30-Jul-26 A	14-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B3-M-820	Installation of Sanitary Waste / Drainage Pipes	4	12-May-26	16-May-26	30-Jul-26 A	03-Aug-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B3-M-1000	Installation of Trench drain	5	30-Aug-26	03-Sep-26	08-Aug-26 A	09-Aug-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B3-M-840	Installation of Floor Drain	2	27-Aug-26	29-Aug-26	11-Nov-26	14-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	05-Sep-26	20-Sep-26	14-Nov-26	30-Nov-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B3-M-800	Installation of Electric Water Heater	2	05-Sep-26	06-Sep-26	14-Nov-26	16-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B3-M-810	Installation of Sanitary Fixture and Accessories	4	07-Sep-26	10-Sep-26	16-Nov-26	21-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B3-M-830	Installation of Lavotary /Wash Basin	2	12-Sep-26	13-Sep-26	21-Nov-26	23-Nov-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B3-M-890	Installation of Bib Tap	2	14-Sep-26	15-Sep-26	23-Nov-26	25-Nov-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B3-M-850	Installation of Water Tap	2	16-Sep-26	17-Sep-26	25-Nov-26	28-Nov-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B3-M-860	Installation of Roof Vent Cap	2	19-Sep-26	20-Sep-26	28-Nov-26	30-Nov-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		15	21-Nov-26	02-Dec-26	01-Oct-26 A	13-Jan-27	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	21-Nov-26	26-Nov-26	01-Oct-26 A	04-Oct-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B3-M-900	Installation of Water Supply Valve	2	25-Nov-26	26-Nov-26	01-Oct-26 A	04-Oct-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B3-M-910	Installation of Water Supply Pipes	4	21-Nov-26	24-Nov-26	01-Oct-26 A	04-Oct-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	28-Nov-26	02-Dec-26	07-Jan-27	13-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B3-M-950	Capped connection	5	28-Nov-26	02-Dec-26	07-Jan-27	13-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		166	19-Jul-26	28-Dec-26	17-Jun-26 A	06-Feb-27	752,044.76	2,920.45	71,373.28	0.39%	9.49%
FIRST STAGE		166	19-Jul-26	24-Dec-26	17-Jun-26 A	03-Feb-27	86,114.12	2,920.45	27,642.87	3.39%	32.1%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	17-Jun-26 A	31-Jan-27	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	17-Jun-26 A	07-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	28-Nov-26	01-Dec-26	21-Jul-26 A	17-Jan-27	1,768.31	0.00	884.15	0%	50%
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	12-Dec-26	15-Dec-26	23-Sep-26 A	27-Jan-27	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B3-E-693	Installation of Wires	2	16-Dec-26	20-Dec-26	27-Jan-27	30-Jan-27	16,925.94	0.00	0.00	0%	0%
DAM3-C-B3-E-683	Installation of LV Cables	4	21-Dec-26	24-Dec-26	30-Jan-27	03-Feb-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		79	21-Nov-26	28-Dec-26	10-Oct-26 A	06-Feb-27	665,930.64	0.00	43,730.41	0%	6.57%
DAM3-C-B3-E-703	Installation of LP-1 Panel	2	23-Dec-26	24-Dec-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B3-E-1040	Installation of Solar power plant	7	02-Dec-26	09-Dec-26	12-Oct-26 A	02-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B3-E-633	Installation of Wiring Devices	4	21-Nov-26	24-Nov-26	07-Jan-27	12-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B3-E-663	Installation of Disconnect Switches	2	25-Nov-26	26-Nov-26	12-Jan-27	14-Jan-27	30,235.95	0.00	0.00	0%	0%
DAM3-C-B3-E-583	Installation of Fire Alarm Control Panel	4	02-Dec-26	06-Dec-26	17-Jan-27	21-Jan-27	19,451.37	0.00	0.00	0%	0%
DAM3-C-B3-E-593	Installation of Fire Detectors & Accessories	4	07-Dec-26	10-Dec-26	21-Jan-27	26-Jan-27	56,740.37	0.00	0.00	0%	0%
DAM3-C-B3-E-733	Installation of Access Control System	3	12-Dec-26	16-Dec-26	26-Jan-27	30-Jan-27	27,616.86	0.00	0.00	0%	0%



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-C-B3-E-613	Installation of Lighting fixtures	4	21-Dec-26	24-Dec-26	30-Jan-27	03-Feb-27	76,166.74	0.00	0.00	0%	0%	Install
DAM3-C-B3-E-653	Installation of Main Distribution Board	2	21-Dec-26	22-Dec-26	30-Jan-27	01-Feb-27	32,472.73	0.00	0.00	0%	0%	Install
DAM3-C-B3-E-743	Monitor Modules for Fire Alarm	2	17-Dec-26	19-Dec-26	30-Jan-27	01-Feb-27	3,882.38	0.00	0.00	0%	0%	Monit
DAM3-C-B3-E-1030	Installation of CCTV System	3	23-Dec-26	28-Dec-26	01-Feb-27	04-Feb-27	76,349.24	0.00	0.00	0%	0%	Install
DAM3-C-B3-E-713	Installation of PP-AC panel	2	23-Dec-26	24-Dec-26	01-Feb-27	03-Feb-27	21,648.48	0.00	0.00	0%	0%	Install
DAM3-C-B3-E-753	Line Isolator Modules for Fire Alarm	2	20-Dec-26	21-Dec-26	01-Feb-27	03-Feb-27	185.40	0.00	0.00	0%	0%	Line I
DAM3-C-B3-E-673	Installation of Telephone Cabinet	2	26-Dec-26	27-Dec-26	03-Feb-27	06-Feb-27	26,991.08	0.00	0.00	0%	0%	Install
DAM3-C-B3-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	22-Dec-26	23-Dec-26	03-Feb-27	06-Feb-27	3,082.69	0.00	0.00	0%	0%	Firew
BLOCK B2		265	08-Mar-26	02-Jan-27	17-Feb-26 A	06-Feb-27	5,075,523.09	3,598,298.21	3,380,125.10	70.9%	66.6%	06-Fe
STRUCTURAL		199	08-Mar-26	29-Sep-26	17-Feb-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%	21-Nov
FOOTING		43	08-Mar-26	08-Apr-26	17-Feb-26 A	13-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%	13-May-26 A,
DAM3-C-B2-S-150	Excavation for footings	4	08-Mar-26	11-Mar-26	17-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%	Excavation for
DAM3-C-B2-S-6223	Soil replacement - rock fill	4	12-Mar-26	16-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%	Soil replacemer
DAM3-C-B2-S-6233	Engineering fill	4	21-Mar-26	24-Mar-26	28-Mar-26 A	06-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Engineering fill
DAM3-C-B2-S-103	Lean Concrete Below Footings	2	28-Mar-26	29-Mar-26	13-Apr-26 A	13-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%	Lean Concrete
DAM3-C-B2-S-102	Vapour Barrier for Footings	1	26-Mar-26	26-Mar-26	13-Apr-26 A	13-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%	Vapour Barrier
DAM3-C-B2-S-101	Anti Termite Below Footings	1	25-Mar-26	25-Mar-26	13-Apr-26 A	13-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite Be
DAM3-C-B2-S-104	Rebar for Footings	4	30-Mar-26	02-Apr-26	06-May-26 A	11-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%	Rebar for Foo
DAM3-C-B2-S-105	Formwork for Footings	4	04-Apr-26	07-Apr-26	10-May-26 A	12-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%	Formwork for
DAM3-C-B2-S-106	Pouring Concrete for Footings	1	08-Apr-26	08-Apr-26	13-May-26 A	13-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%	Pouring Conc
COLUMN NECK		16	09-Apr-26	27-Apr-26	10-May-26 A	09-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%	09-Jun-26 A,
DAM3-C-B2-S-257	Rebar for column neck	4	09-Apr-26	13-Apr-26	10-May-26 A	12-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%	Rebar for colu
DAM3-C-B2-S-267	Formwork for column neck	2	14-Apr-26	15-Apr-26	14-May-26 A	16-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%	Formwork for
DAM3-C-B2-S-297	Pouring Concrete for column neck	1	16-Apr-26	16-Apr-26	17-May-26 A	18-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%	Pouring Conc
DAM3-C-B2-S-307	Damp proof /Bitumin paint on Footings & column neck	2	18-Apr-26	19-Apr-26	19-May-26 A	20-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof /
DAM3-C-B2-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	20-Apr-26	27-Apr-26	24-May-26 A	09-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Backfilling / C
GRADE BEAM		16	28-Apr-26	18-May-26	13-Jun-26 A	25-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%	25-Jun-26 A,
DAM3-C-B2-S-338	Lean Concrete Below Grade Beams	2	02-May-26	03-May-26	13-Jun-26 A	13-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%	Lean Concre
DAM3-C-B2-S-337	Vapour barrier for Grade Beams	2	29-Apr-26	30-Apr-26	13-Jun-26 A	13-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%	Vapour barre
DAM3-C-B2-S-527	Anti Termite Below Grade Beams	1	28-Apr-26	28-Apr-26	13-Jun-26 A	13-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite
DAM3-C-B2-S-339	Rebar for Grade Beams	5	04-May-26	09-May-26	15-Jun-26 A	18-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%	Rebar for Gr
DAM3-C-B2-S-340	Formwork for Grade Beams	2	10-May-26	11-May-26	17-Jun-26 A	21-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%	Formwork fo
DAM3-C-B2-S-341	Anchor bolts installation	2	10-May-26	11-May-26	18-Jun-26 A	20-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%	Anchor bolts
DAM3-C-B2-S-342	Pouring Concrete for Grade Beams	1	12-May-26	12-May-26	22-Jun-26 A	22-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%	Pouring Con
DAM3-C-B2-S-347	Damp proof /Bitumin paint on Grade Beams	5	13-May-26	18-May-26	24-Jun-26 A	25-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof
SLAB ON GRADE		120	19-May-26	29-Sep-26	02-Jul-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%	21-Nov
DAM3-C-B2-S-377	Backfilling / Compaction for Slab on Grade	7	19-May-26	30-May-26	02-Jul-26 A	06-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%	Backfilling /
DAM3-C-B2-S-382	Pouring Concrete for Ground Slab	4	25-Jul-26	29-Jul-26	09-Aug-26 A	10-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%	Pouring Co
DAM3-C-B2-S-378	Anti Termite Treatment below Ground Slab	1	04-Jun-26	04-Jun-26	09-Aug-26 A	10-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%	Anti Termite
DAM3-C-B2-S-379	Vapour barrier for below Ground Slab	2	06-Jun-26	07-Jun-26	09-Aug-26 A	10-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%	Vapour bar
DAM3-C-B2-S-517	Concrete pad	7	20-Sep-26	29-Sep-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%	Concre
COLUMNS & BEAMS		66	31-May-26	29-Jun-26	15-Jun-26 A	04-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%	04-Oct-26
DAM3-C-B2-S-6101	Rebar for Tie Beams	4	11-Jun-26	15-Jun-26	15-Jun-26 A	18-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%	Rebar for Tie
DAM3-C-B2-S-6102	Formwork for Tie Beams	2	16-Jun-26	17-Jun-26	17-Jun-26 A	21-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%	Formwork fo
DAM3-C-B2-S-6103	Pouring Concrete for Tie Beams	1	21-Jun-26	21-Jun-26	22-Jun-26 A	22-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%	Pouring Con
DAM3-C-B2-S-5101	Rebar for column	5	31-May-26	04-Jun-26	22-Jul-26 A	30-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%	Rebar for c
DAM3-C-B2-S-5102	Formwork for column	4	06-Jun-26	09-Jun-26	11-Aug-26 A	18-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%	Formwork f
DAM3-C-B2-S-5103	Pouring Concrete for column	1	10-Jun-26	10-Jun-26	13-Aug-26 A	22-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%	Pouring Co
DAM3-C-B2-S-6113	Rebar for Beams	4	22-Jun-26	25-Jun-26	17-Sep-26 A	20-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%	Rebar for

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B2-S-6123	Formwork for Beams	2	27-Jun-26	28-Jun-26	28-Sep-26 A	01-Oct-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B2-S-6133	Pouring Concrete for Beams	1	29-Jun-26	29-Jun-26	03-Oct-26 A	04-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		63	08-Aug-26	01-Oct-26	12-Jul-26 A	21-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B2-SS-0100	Installation of columns	3	08-Aug-26	10-Aug-26	12-Jul-26 A	13-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B2-SS-0110	Installation of raft and purlins	5	11-Aug-26	16-Aug-26	12-Jul-26 A	14-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B2-SS-610	Intumescent paint to steel works	7	26-Aug-26	03-Sep-26	30-Jul-26 A	01-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B2-SS-0140	Installation of roof sheet	5	03-Sep-26	09-Sep-26	06-Aug-26 A	13-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B2-SS-0130	Installation of wall sandwich panel	5	26-Sep-26	01-Oct-26	18-Oct-26 A	22-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B2-SS-620	Steel members for office area	7	03-Sep-26	12-Sep-26	24-Oct-26 A	25-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B2-SS-1030	Steel members for external platform	7	12-Sep-26	20-Sep-26	24-Oct-26 A	25-Oct-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B2-SS-1020	Epoxy paint to steel members at office area	7	12-Sep-26	20-Sep-26	12-Nov-26	21-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B2-SS-1040	Epoxy paint for external platform	5	20-Sep-26	27-Sep-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		89	17-Aug-26	02-Jan-27	12-Aug-26 A	06-Feb-27	900,244.66	376,424.37	224,562.33	41.81%	24.94%
MASONARY WORKS		19	17-Aug-26	29-Sep-26	22-Aug-26 A	27-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B2-A-170	Block work at toilet area	7	20-Sep-26	29-Sep-26	22-Aug-26 A	27-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B2-A-0120	Block work at factory area	8	17-Aug-26	27-Aug-26	22-Aug-26 A	25-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B2-A-0150	Block work at office area	7	12-Sep-26	20-Sep-26	22-Aug-26 A	08-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		25	08-Oct-26	24-Nov-26	04-Oct-26 A	01-Dec-26	92,757.47	48,590.16	86,132.37	52.38%	92.86%
DAM3-C-B2-A-180	Internal Wall Plaster	15	08-Oct-26	26-Oct-26	04-Oct-26 A	15-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B2-A-230	Paint to Plaster (Primer, Putty & First Coat)	7	16-Nov-26	24-Nov-26	18-Oct-26 A	01-Dec-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		5	08-Nov-26	14-Nov-26	22-Nov-26	28-Nov-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B2-A-240	Installation of Ceiling Gypsum Board	5	08-Nov-26	14-Nov-26	22-Nov-26	28-Nov-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		60	31-Oct-26	02-Jan-27	20-Oct-26 A	06-Feb-27	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B2-A-220	Tiles for Toilet	7	31-Oct-26	08-Nov-26	20-Oct-26 A	25-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B2-A-250	Tiles for Office Area	2	14-Nov-26	16-Nov-26	28-Nov-26	30-Nov-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B2-A-390	Granite strip	2	16-Nov-26	18-Nov-26	03-Dec-26	06-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B2-A-420	Epoxy paint	3	22-Dec-26	02-Jan-27	02-Feb-27	06-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		18	01-Oct-26	18-Oct-26	11-Oct-26 A	03-Dec-26	248,575.06	248,575.06	6,489.89	100%	2.61%
DAM3-C-B2-A-558	Skylight fixtures installation	1	17-Oct-26	18-Oct-26	11-Oct-26 A	14-Oct-26 A	6,489.89	6,489.89	6,489.89	100%	100%
DAM3-C-B2-A-552	Window (CW1)	5	01-Oct-26	10-Oct-26	21-Nov-26	26-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B2-A-553	Roll up Shutter Door	1	10-Oct-26	11-Oct-26	26-Nov-26	28-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B2-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	11-Oct-26	12-Oct-26	28-Nov-26	29-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B2-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	12-Oct-26	13-Oct-26	29-Nov-26	30-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B2-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	13-Oct-26	14-Oct-26	30-Nov-26	01-Dec-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B2-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	14-Oct-26	15-Oct-26	01-Dec-26	02-Dec-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B2-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	15-Oct-26	17-Oct-26	02-Dec-26	03-Dec-26	16,711.52	16,711.52	0.00	100%	0%
WATER PROOFING WORKS		4	26-Oct-26	31-Oct-26	17-Nov-26	22-Nov-26	4,879.02	304.94	0.00	6.25%	0%
DAM3-C-B2-A-370	Waterproofing membrane for toilets	4	26-Oct-26	31-Oct-26	17-Nov-26	22-Nov-26	4,879.02	304.94	0.00	6.25%	0%
METAL WORKS		38	18-Nov-26	03-Dec-26	12-Aug-26 A	19-Dec-26	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B2-A-300	Galvanised Steel Gratings	2	01-Dec-26	03-Dec-26	12-Aug-26 A	12-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B2-A-290	Steel Ladder	2	18-Nov-26	21-Nov-26	06-Dec-26	08-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B2-A-291	Steel railing works	4	21-Nov-26	25-Nov-26	08-Dec-26	13-Dec-26	1,533.98	0.00	0.00	0%	0%
DAM3-C-B2-A-292	Aluminium composite panel	5	25-Nov-26	01-Dec-26	13-Dec-26	19-Dec-26	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		39	03-Dec-26	21-Dec-26	19-Dec-26	02-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B2-A-320	Installation of fittings	5	03-Dec-26	09-Dec-26	19-Dec-26	24-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B2-A-570	Identification sign; ID01 & ID02	3	09-Dec-26	13-Dec-26	24-Dec-26	28-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B2-A-340	Furniture Installation	1	21-Dec-26	21-Dec-26	01-Feb-27	02-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		147	19-May-26	14-Dec-26	23-Jul-26 A	21-Dec-26	467,522.66	18,585.14	156,280.78	3.98%	33.43%
HVAC		14	24-Nov-26	10-Dec-26	01-Dec-26	17-Dec-26	233,183.33	0.00	0.00	0%	0%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	01-Dec-26	06-Dec-26	08-Dec-26	13-Dec-26	170,694.73	0.00	0.00	0%	0%
DAM3-C-B2-M-140	Installation of HVAC Ducts	2	01-Dec-26	03-Dec-26	08-Dec-26	10-Dec-26	149,489.33	0.00	0.00	0%	0%
DAM3-C-B2-M-170	Installation of Duct insulation	2	03-Dec-26	06-Dec-26	10-Dec-26	13-Dec-26	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	24-Nov-26	10-Dec-26	01-Dec-26	17-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B2-M-130	Installation of Exhaust Fans	2	24-Nov-26	26-Nov-26	01-Dec-26	03-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B2-M-160	Installation of Wall Propeller Type Exhaust Fan	4	26-Nov-26	01-Dec-26	03-Dec-26	08-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B2-M-339	Installation of Diffuser	2	06-Dec-26	08-Dec-26	13-Dec-26	15-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B2-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	08-Dec-26	10-Dec-26	15-Dec-26	17-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		27	24-Nov-26	14-Dec-26	10-Sep-26 A	21-Dec-26	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		12	24-Nov-26	08-Dec-26	10-Sep-26 A	21-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B2-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	24-Nov-26	02-Dec-26	10-Sep-26 A	21-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B2-M-310	Installation of Fire Fighting Valve	5	02-Dec-26	08-Dec-26	10-Sep-26 A	21-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	08-Dec-26	14-Dec-26	01-Dec-26	21-Dec-26	17,864.62	0.00	0.00	0%	0%
DAM3-C-B2-M-320	Installation of Fire Hose Cabinet	3	08-Dec-26	12-Dec-26	01-Dec-26	05-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B2-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	10-Dec-26	14-Dec-26	17-Dec-26	21-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		127	19-May-26	02-Dec-26	23-Jul-26 A	10-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		127	19-May-26	16-Nov-26	23-Jul-26 A	24-Nov-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B2-M-200	Installation of Sanitary Waste / Drainage Pipes	4	19-May-26	23-May-26	23-Jul-26 A	27-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B2-M-380	Installation of Trench drain	5	10-Nov-26	16-Nov-26	03-Aug-26 A	04-Aug-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B2-M-220	Installation of Floor Drain	2	08-Nov-26	10-Nov-26	22-Nov-26	24-Nov-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	16-Nov-26	02-Dec-26	24-Nov-26	10-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B2-M-180	Installation of Electric Water Heater	2	16-Nov-26	18-Nov-26	24-Nov-26	26-Nov-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B2-M-190	Installation of Sanitary Fixture and Accessories	4	18-Nov-26	23-Nov-26	26-Nov-26	01-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B2-M-210	Installation of Lavotary /Wash Basin	2	23-Nov-26	25-Nov-26	01-Dec-26	03-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B2-M-270	Installation of Bib Tap	2	25-Nov-26	28-Nov-26	03-Dec-26	06-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B2-M-428	Installation of Water Tap	2	28-Nov-26	30-Nov-26	06-Dec-26	08-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B2-M-429	Installation of Roof Vent Cap	2	30-Nov-26	02-Dec-26	08-Dec-26	10-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		36	24-Nov-26	07-Dec-26	01-Oct-26 A	07-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	24-Nov-26	01-Dec-26	01-Oct-26 A	04-Oct-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B2-M-280	Installation of Water Supply Valve	2	29-Nov-26	01-Dec-26	01-Oct-26 A	04-Oct-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B2-M-290	Installation of Water Supply Pipes	4	24-Nov-26	29-Nov-26	01-Oct-26 A	04-Oct-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	01-Dec-26	07-Dec-26	01-Dec-26	07-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B2-M-330	Capped connection	5	01-Dec-26	07-Dec-26	01-Dec-26	07-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		65	29-Sep-26	21-Dec-26	17-Jun-26 A	31-Dec-26	752,044.76	247,577.69	71,373.28	32.92%	9.49%
FIRST STAGE		49	29-Sep-26	11-Nov-26	17-Jun-26 A	21-Dec-26	86,114.12	30,077.67	27,642.87	34.93%	32.1%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	29-Sep-26	04-Oct-26	17-Jun-26 A	15-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	18-Jun-26 A	21-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	18-Jun-26 A	17-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	13-Oct-26	18-Oct-26	29-Sep-26 A	25-Nov-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B2-E-233	Installation of Wires	4	18-Oct-26	22-Oct-26	03-Dec-26	08-Dec-26	16,925.94	16,925.94	0.00	100%	0%
DAM3-C-B2-E-223	Installation of LV Cables	4	01-Nov-26	05-Nov-26	15-Dec-26	20-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		49	04-Oct-26	21-Dec-26	10-Oct-26 A	31-Dec-26	665,930.64	217,500.02	43,730.41	32.66%	6.57%
DAM3-C-B2-E-243	Installation of LP-1 Panel	2	25-Oct-26	27-Oct-26	10-Oct-26 A	14-Oct-26 A	18,403.54	11,502.21	18,403.54	62.5%	100%
DAM3-C-B2-E-420	Installation of Solar power plant	10	10-Dec-26	21-Dec-26	13-Oct-26 A	31-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B2-E-123	Installation of Fire Alarm Control Panel	4	04-Oct-26	08-Oct-26	15-Nov-26	19-Nov-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B2-E-133	Installation of Fire Detectors & Accessories	4	08-Oct-26	13-Oct-26	19-Nov-26	24-Nov-26	56,740.37	56,740.37	0.00	100%	0%
DAM3-C-B2-E-173	Installation of Wiring Devices	4	24-Nov-26	29-Nov-26	01-Dec-26	06-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B2-E-203	Installation of Disconnect Switches	2	29-Nov-26	01-Dec-26	06-Dec-26	08-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B2-E-153	Installation of Lighting fixtures	4	22-Oct-26	27-Oct-26	08-Dec-26	13-Dec-26	76,166.74	61,885.48	0.00	81.25%	0%

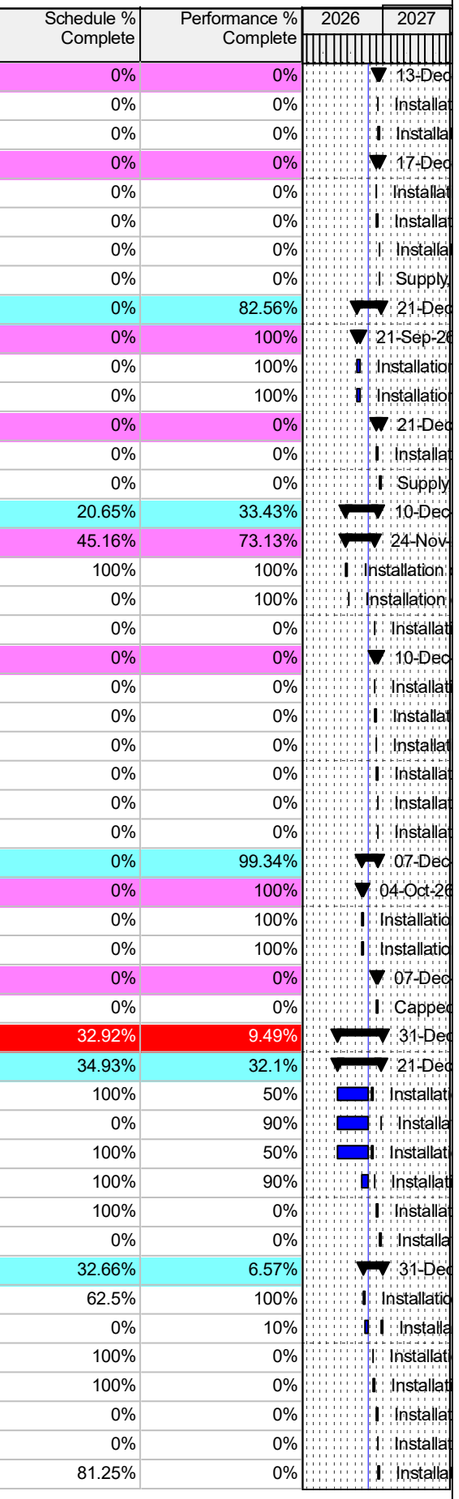

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B2-E-193	Installation of Main Distribution Board	2	22-Oct-26	25-Oct-26	08-Dec-26	10-Dec-26	32,472.73	32,472.73	0.00	100%	0%
DAM3-C-B2-E-410	Installation of CCTV System	6	22-Oct-26	31-Oct-26	08-Dec-26	15-Dec-26	76,349.24	35,447.86	0.00	46.43%	0%
DAM3-C-B2-E-253	Installation of PP-AC panel	2	27-Oct-26	29-Oct-26	10-Dec-26	13-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B2-E-213	Installation of Telephone Cabinet	2	29-Oct-26	01-Nov-26	13-Dec-26	15-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B2-E-273	Installation of Access Control System	5	31-Oct-26	05-Nov-26	15-Dec-26	21-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B2-E-283	Monitor Modules for Fire Alarm	2	05-Nov-26	08-Nov-26	21-Dec-26	23-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B2-E-293	Line Isolator Modules for Fire Alarm	2	08-Nov-26	10-Nov-26	23-Dec-26	26-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B2-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	10-Nov-26	12-Nov-26	26-Dec-26	28-Dec-26	3,082.69	0.00	0.00	0%	0%
BLOCK B1		264	12-Mar-26	03-Jan-27	17-Mar-26 A	06-Feb-27	5,075,523.09	3,410,593.75	3,296,052.18	67.2%	64.94%
STRUCTURAL		198	12-Mar-26	21-Sep-26	17-Mar-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		101	12-Mar-26	29-Apr-26	17-Mar-26 A	07-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B1-S-150	Excavation for footings	4	12-Mar-26	16-Mar-26	17-Mar-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B1-S-6243	Soil replacement - rock fill	4	21-Mar-26	24-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B1-S-6253	Engineering fill	4	25-Mar-26	29-Mar-26	07-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B1-S-103	Lean Concrete Below Footings	2	13-Apr-26	14-Apr-26	25-Apr-26 A	25-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B1-S-102	Vapour Barrier for Footings	1	31-Mar-26	31-Mar-26	25-Apr-26 A	25-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B1-S-101	Anti Termite Below Footings	1	30-Mar-26	30-Mar-26	25-Apr-26 A	25-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B1-S-104	Rebar for Footings	4	20-Apr-26	23-Apr-26	02-May-26 A	05-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B1-S-105	Formwork for Footings	4	25-Apr-26	28-Apr-26	05-May-26 A	06-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B1-S-106	Pouring Concrete for Footings	1	29-Apr-26	29-Apr-26	07-May-26 A	07-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		10	30-Apr-26	18-May-26	05-May-26 A	01-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B1-S-257	Rebar for column neck	4	30-Apr-26	04-May-26	05-May-26 A	06-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B1-S-267	Formwork for column neck	2	05-May-26	06-May-26	11-May-26 A	12-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B1-S-297	Pouring Concrete for column neck	1	07-May-26	07-May-26	13-May-26 A	13-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B1-S-307	Damp proof /Bitumin paint on Footings & column neck	2	09-May-26	10-May-26	16-May-26 A	17-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B1-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	11-May-26	18-May-26	21-May-26 A	01-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		11	19-May-26	11-Jun-26	06-Jun-26 A	25-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B1-S-338	Lean Concrete Below Grade Beams	2	23-May-26	24-May-26	06-Jun-26 A	06-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B1-S-337	Vapour barrier for Grade Beams	2	20-May-26	21-May-26	06-Jun-26 A	06-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B1-S-527	Anti Termite Below Grade Beams	1	19-May-26	19-May-26	06-Jun-26 A	06-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B1-S-339	Rebar for Grade Beams	5	25-May-26	02-Jun-26	08-Jun-26 A	09-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B1-S-340	Formwork for Grade Beams	2	03-Jun-26	04-Jun-26	11-Jun-26 A	15-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B1-S-341	Anchor bolts installation	2	03-Jun-26	04-Jun-26	11-Jun-26 A	13-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B1-S-342	Pouring Concrete for Grade Beams	1	06-Jun-26	06-Jun-26	17-Jun-26 A	17-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B1-S-347	Damp proof /Bitumin paint on Grade Beams	5	07-Jun-26	11-Jun-26	23-Jun-26 A	25-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		113	13-Jun-26	21-Sep-26	27-Jun-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B1-S-377	Backfilling / Compaction for Slab on Grade	7	13-Jun-26	20-Jun-26	27-Jun-26 A	05-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B1-S-382	Pouring Concrete for Ground Slab	4	24-Jun-26	28-Jun-26	06-Aug-26 A	08-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B1-S-378	Anti Termite Treatment below Ground Slab	1	21-Jun-26	21-Jun-26	06-Aug-26 A	08-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B1-S-379	Vapour barrier for below Ground Slab	2	22-Jun-26	23-Jun-26	06-Aug-26 A	08-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B1-S-517	Concrete pad	7	14-Sep-26	21-Sep-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		63	21-Jun-26	18-Jul-26	08-Jun-26 A	10-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B1-S-6101	Rebar for Tie Beams	4	02-Jul-26	06-Jul-26	08-Jun-26 A	09-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B1-S-6102	Formwork for Tie Beams	2	07-Jul-26	08-Jul-26	11-Jun-26 A	15-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B1-S-6103	Pouring Concrete for Tie Beams	1	09-Jul-26	09-Jul-26	17-Jun-26 A	17-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B1-S-5101	Rebar for column	5	21-Jun-26	25-Jun-26	26-Jul-26 A	28-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B1-S-5102	Formwork for column	4	27-Jun-26	30-Jun-26	22-Aug-26 A	27-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B1-S-5103	Pouring Concrete for column	1	01-Jul-26	01-Jul-26	25-Aug-26 A	29-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B1-S-6113	Rebar for Beams	4	11-Jul-26	14-Jul-26	27-Sep-26 A	04-Oct-26 A	13,379.11	13,379.11	13,379.11	100%	100%


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B1-S-6123	Formwork for Beams	2	15-Jul-26	16-Jul-26	29-Sep-26 A	06-Oct-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B1-S-6133	Pouring Concrete for Beams	1	18-Jul-26	18-Jul-26	07-Oct-26 A	10-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		60	11-Aug-26	19-Sep-26	11-Jul-26 A	21-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B1-SS-0100	Installation of columns	3	11-Aug-26	13-Aug-26	11-Jul-26 A	11-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B1-SS-0110	Installation of raft and purlins	5	15-Aug-26	19-Aug-26	11-Jul-26 A	13-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B1-SS-610	Intumescent paint to steel works	7	20-Aug-26	27-Aug-26	25-Jul-26 A	28-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B1-SS-0140	Installation of roof sheet	5	01-Sep-26	06-Sep-26	04-Aug-26 A	11-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B1-SS-0130	Installation of wall sandwich panel	5	14-Sep-26	19-Sep-26	18-Oct-26 A	22-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B1-SS-620	Steel members for office area	7	29-Aug-26	05-Sep-26	24-Oct-26 A	25-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B1-SS-1030	Steel members for external platform	7	06-Sep-26	13-Sep-26	24-Oct-26 A	25-Oct-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B1-SS-1020	Epoxy paint to steel members at office area	7	06-Sep-26	13-Sep-26	12-Nov-26	21-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B1-SS-1040	Epoxy paint for external platform	5	14-Sep-26	19-Sep-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		86	20-Aug-26	03-Jan-27	10-Aug-26 A	06-Feb-27	900,244.66	346,954.13	140,489.42	38.54%	15.61%
MASONARY WORKS		28	20-Aug-26	07-Oct-26	15-Aug-26 A	07-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B1-A-0120	Block work at factory area	10	20-Aug-26	31-Aug-26	15-Aug-26 A	23-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B1-A-0150	Block work at office area	7	06-Sep-26	13-Sep-26	23-Aug-26 A	06-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B1-A-170	Block work at toilet area	7	30-Sep-26	07-Oct-26	02-Sep-26 A	07-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		32	18-Oct-26	06-Dec-26	19-Oct-26 A	13-Jan-27	92,757.47	25,914.75	48,590.16	27.94%	52.38%
DAM3-C-B1-A-180	Internal Wall Plaster	10	18-Oct-26	03-Nov-26	19-Oct-26 A	26-Oct-26 A	48,590.16	25,914.75	48,590.16	53.33%	100%
DAM3-C-B1-A-230	Paint to Plaster (Primer, Putty & First Coat)	3	29-Nov-26	06-Dec-26	10-Jan-27	13-Jan-27	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		3	21-Nov-26	25-Nov-26	13-Dec-26	15-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B1-A-240	Installation of Ceiling Gypsum Board	3	21-Nov-26	25-Nov-26	13-Dec-26	15-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		51	11-Nov-26	03-Jan-27	08-Dec-26	06-Feb-27	189,488.90	0.00	0.00	0%	0%
DAM3-C-B1-A-220	Tiles for Toilet	4	11-Nov-26	18-Nov-26	08-Dec-26	12-Dec-26	46,530.71	0.00	0.00	0%	0%
DAM3-C-B1-A-250	Tiles for Office Area	2	26-Nov-26	28-Nov-26	07-Jan-27	10-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B1-A-390	Granite strip	2	29-Nov-26	30-Nov-26	10-Jan-27	12-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B1-A-420	Epoxy paint	7	27-Dec-26	03-Jan-27	28-Jan-27	06-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		25	20-Sep-26	28-Oct-26	15-Oct-26 A	03-Dec-26	248,575.06	242,085.17	6,489.89	97.39%	2.61%
DAM3-C-B1-A-558	Skylight fixtures installation	1	27-Oct-26	28-Oct-26	15-Oct-26 A	17-Oct-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B1-A-552	Window (CW1)	5	20-Sep-26	28-Sep-26	21-Nov-26	26-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B1-A-553	Roll up Shutter Door	1	29-Sep-26	29-Sep-26	26-Nov-26	28-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B1-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	30-Sep-26	30-Sep-26	28-Nov-26	29-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B1-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	01-Oct-26	01-Oct-26	29-Nov-26	30-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B1-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	03-Oct-26	03-Oct-26	30-Nov-26	01-Dec-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B1-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	04-Oct-26	04-Oct-26	01-Dec-26	02-Dec-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B1-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	05-Oct-26	05-Oct-26	02-Dec-26	03-Dec-26	16,711.52	16,711.52	0.00	100%	0%
WATER PROOFING WORKS		4	07-Nov-26	10-Nov-26	03-Dec-26	07-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B1-A-370	Waterproofing membrane for toilets	4	07-Nov-26	10-Nov-26	03-Dec-26	07-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		18	01-Dec-26	15-Dec-26	10-Aug-26 A	20-Jan-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B1-A-300	Galvanised Steel Gratings	2	14-Dec-26	15-Dec-26	10-Aug-26 A	10-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B1-A-290	Steel Ladder	2	01-Dec-26	02-Dec-26	12-Jan-27	14-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B1-A-291	Steel railing works	2	03-Dec-26	07-Dec-26	14-Jan-27	17-Jan-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B1-A-292	Aluminium composite panel	3	08-Dec-26	13-Dec-26	17-Jan-27	20-Jan-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	16-Dec-26	26-Dec-26	20-Jan-27	28-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B1-A-320	Installation of fittings	3	16-Dec-26	21-Dec-26	20-Jan-27	24-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B1-A-570	Identification sign; ID01 & ID02	3	22-Dec-26	24-Dec-26	24-Jan-27	27-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B1-A-340	Furniture Installation	1	26-Dec-26	26-Dec-26	27-Jan-27	28-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		168	13-Jun-26	26-Dec-26	18-Jul-26 A	31-Jan-27	467,522.66	18,585.14	156,280.78	3.98%	33.43%
HVAC		12	07-Dec-26	22-Dec-26	13-Jan-27	27-Jan-27	233,183.33	0.00	0.00	0%	0%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	14-Dec-26	17-Dec-26	18-Jan-27	23-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B1-M-140	Installation of HVAC Ducts	2	14-Dec-26	15-Dec-26	18-Jan-27	20-Jan-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B1-M-170	Installation of Duct insulation	2	16-Dec-26	17-Dec-26	20-Jan-27	23-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		12	07-Dec-26	22-Dec-26	13-Jan-27	27-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B1-M-130	Installation of Exhaust Fans	2	07-Dec-26	08-Dec-26	13-Jan-27	16-Jan-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B1-M-160	Installation of Wall Propeller Type Exhaust Fan	2	09-Dec-26	13-Dec-26	16-Jan-27	18-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B1-M-339	Installation of Diffuser	2	19-Dec-26	20-Dec-26	23-Jan-27	25-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B1-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	21-Dec-26	22-Dec-26	25-Jan-27	27-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		17	07-Dec-26	26-Dec-26	06-Sep-26 A	31-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		10	07-Dec-26	20-Dec-26	06-Sep-26 A	09-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B1-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	07-Dec-26	14-Dec-26	06-Sep-26 A	09-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B1-M-310	Installation of Fire Fighting Valve	5	15-Dec-26	20-Dec-26	08-Sep-26 A	09-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		15	21-Dec-26	26-Dec-26	13-Jan-27	31-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B1-M-320	Installation of Fire Hose Cabinet	3	21-Dec-26	23-Dec-26	13-Jan-27	17-Jan-27	15,158.56	0.00	0.00	0%	0%
DAM3-C-B1-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	23-Dec-26	26-Dec-26	27-Jan-27	31-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		139	13-Jun-26	13-Dec-26	18-Jul-26 A	30-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		127	13-Jun-26	26-Nov-26	18-Jul-26 A	14-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B1-M-200	Installation of Sanitary Waste / Drainage Pipes	4	13-Jun-26	16-Jun-26	18-Jul-26 A	25-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B1-M-380	Installation of Trench drain	5	22-Nov-26	26-Nov-26	19-Jul-26 A	25-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B1-M-220	Installation of Floor Drain	2	19-Nov-26	21-Nov-26	13-Dec-26	14-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	28-Nov-26	13-Dec-26	15-Dec-26	30-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B1-M-180	Installation of Electric Water Heater	2	28-Nov-26	29-Nov-26	15-Dec-26	16-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B1-M-190	Installation of Sanitary Fixture and Accessories	4	30-Nov-26	03-Dec-26	17-Dec-26	21-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B1-M-210	Installation of Lavotary /Wash Basin	2	05-Dec-26	06-Dec-26	22-Dec-26	23-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B1-M-270	Installation of Bib Tap	2	07-Dec-26	08-Dec-26	24-Dec-26	26-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B1-M-428	Installation of Water Tap	2	09-Dec-26	10-Dec-26	27-Dec-26	28-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B1-M-429	Installation of Roof Vent Cap	2	12-Dec-26	13-Dec-26	29-Dec-26	30-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		16	07-Dec-26	19-Dec-26	13-Oct-26 A	19-Jan-27	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	07-Dec-26	13-Dec-26	13-Oct-26 A	17-Oct-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B1-M-280	Installation of Water Supply Valve	2	12-Dec-26	13-Dec-26	13-Oct-26 A	17-Oct-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B1-M-290	Installation of Water Supply Pipes	4	07-Dec-26	10-Dec-26	13-Oct-26 A	17-Oct-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	14-Dec-26	19-Dec-26	13-Jan-27	19-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B1-M-330	Capped connection	5	14-Dec-26	19-Dec-26	13-Jan-27	19-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		63	08-Oct-26	29-Dec-26	08-Jun-26 A	20-Jan-27	752,044.76	89,343.47	71,373.28	11.88%	9.49%
FIRST STAGE		44	08-Oct-26	22-Nov-26	08-Jun-26 A	28-Dec-26	86,114.12	13,151.73	27,642.87	15.27%	32.1%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	08-Jun-26 A	28-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	08-Jun-26 A	02-Dec-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	08-Oct-26	12-Oct-26	09-Jun-26 A	30-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	22-Oct-26	26-Oct-26	01-Oct-26 A	10-Dec-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B1-E-233	Installation of Wires	4	28-Oct-26	02-Nov-26	12-Dec-26	16-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B1-E-223	Installation of LV Cables	4	11-Nov-26	16-Nov-26	23-Dec-26	28-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		43	13-Oct-26	29-Dec-26	10-Oct-26 A	20-Jan-27	665,930.64	76,191.74	43,730.41	11.44%	6.57%
DAM3-C-B1-E-243	Installation of LP-1 Panel	2	04-Nov-26	07-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B1-E-420	Installation of Solar power plant	7	22-Dec-26	29-Dec-26	14-Oct-26 A	07-Jan-27	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B1-E-123	Installation of Fire Alarm Control Panel	4	13-Oct-26	17-Oct-26	01-Dec-26	05-Dec-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B1-E-133	Installation of Fire Detectors & Accessories	4	18-Oct-26	21-Oct-26	06-Dec-26	09-Dec-26	56,740.37	56,740.37	0.00	100%	0%
DAM3-C-B1-E-153	Installation of Lighting fixtures	4	02-Nov-26	07-Nov-26	16-Dec-26	21-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B1-E-193	Installation of Main Distribution Board	2	02-Nov-26	04-Nov-26	16-Dec-26	19-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B1-E-410	Installation of CCTV System	7	02-Nov-26	10-Nov-26	16-Dec-26	24-Dec-26	76,349.24	0.00	0.00	0%	0%

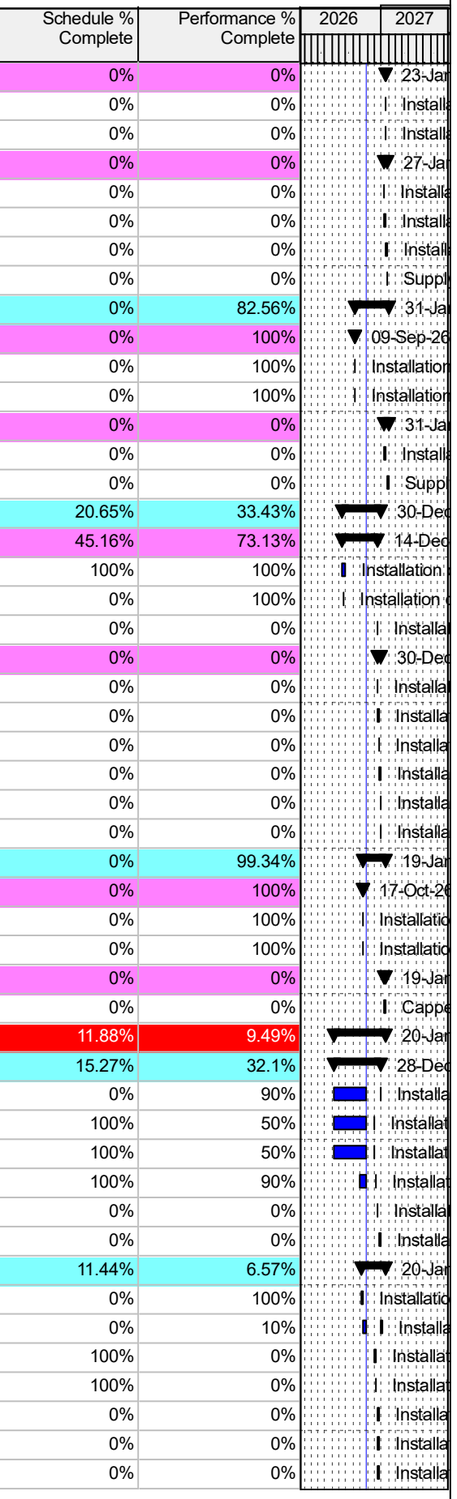

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B1-E-253	Installation of PP-AC panel	2	07-Nov-26	09-Nov-26	19-Dec-26	21-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B1-E-213	Installation of Telephone Cabinet	2	09-Nov-26	11-Nov-26	21-Dec-26	23-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B1-E-273	Installation of Access Control System	5	10-Nov-26	16-Nov-26	24-Dec-26	30-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B1-E-283	Monitor Modules for Fire Alarm	2	16-Nov-26	18-Nov-26	30-Dec-26	02-Jan-27	3,882.38	0.00	0.00	0%	0%
DAM3-C-B1-E-293	Line Isolator Modules for Fire Alarm	2	18-Nov-26	21-Nov-26	02-Jan-27	04-Jan-27	185.40	0.00	0.00	0%	0%
DAM3-C-B1-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	21-Nov-26	23-Nov-26	04-Jan-27	06-Jan-27	3,082.69	0.00	0.00	0%	0%
DAM3-C-B1-E-173	Installation of Wiring Devices	4	07-Dec-26	10-Dec-26	13-Jan-27	18-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B1-E-203	Installation of Disconnect Switches	2	12-Dec-26	13-Dec-26	18-Jan-27	20-Jan-27	30,235.95	0.00	0.00	0%	0%
BLOCK B7		273	10-Feb-26	06-Jan-27	16-Feb-26 A	26-Dec-26	5,075,523.09	3,674,477.95	4,200,300.33	72.4%	82.76%
STRUCTURAL		212	10-Feb-26	26-Sep-26	16-Feb-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		32	10-Feb-26	25-Mar-26	16-Feb-26 A	11-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B7-S-150	Excavation for footings	8	10-Feb-26	19-Feb-26	16-Feb-26 A	19-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B7-S-6263	Soil replacement - rock fill	6	19-Feb-26	28-Feb-26	21-Feb-26 A	26-Feb-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B7-S-6273	Engineering fill	6	01-Mar-26	07-Mar-26	05-Mar-26 A	11-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B7-S-103	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	25-Mar-26 A	25-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B7-S-102	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	25-Mar-26 A	25-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B7-S-101	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	25-Mar-26 A	25-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B7-S-104	Rebar for Footings	4	12-Mar-26	16-Mar-26	05-Apr-26 A	09-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B7-S-105	Formwork for Footings	4	21-Mar-26	24-Mar-26	06-Apr-26 A	09-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B7-S-106	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	11-Apr-26 A	11-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		19	26-Mar-26	13-Apr-26	09-Apr-26 A	10-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B7-S-257	Rebar for column neck	4	26-Mar-26	30-Mar-26	09-Apr-26 A	11-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B7-S-267	Formwork for column neck	2	31-Mar-26	01-Apr-26	15-Apr-26 A	15-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B7-S-297	Pouring Concrete for column neck	1	02-Apr-26	02-Apr-26	16-Apr-26 A	16-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B7-S-307	Damp proof /Bitumin paint on Footings & column neck	2	04-Apr-26	05-Apr-26	20-Apr-26 A	23-Apr-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B7-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	06-Apr-26	13-Apr-26	02-May-26 A	10-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		14	14-Apr-26	04-May-26	13-May-26 A	31-May-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B7-S-338	Lean Concrete Below Grade Beams	2	18-Apr-26	19-Apr-26	13-May-26 A	13-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B7-S-337	Vapour barrier for Grade Beams	2	15-Apr-26	16-Apr-26	13-May-26 A	13-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B7-S-527	Anti Termite Below Grade Beams	1	14-Apr-26	14-Apr-26	13-May-26 A	13-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B7-S-339	Rebar for Grade Beams	5	20-Apr-26	25-Apr-26	16-May-26 A	18-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B7-S-341	Anchor bolts installation	2	26-Apr-26	27-Apr-26	16-May-26 A	18-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B7-S-340	Formwork for Grade Beams	2	26-Apr-26	27-Apr-26	18-May-26 A	19-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B7-S-342	Pouring Concrete for Grade Beams	1	28-Apr-26	28-Apr-26	20-May-26 A	20-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B7-S-347	Damp proof /Bitumin paint on Grade Beams	5	29-Apr-26	04-May-26	23-May-26 A	31-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		143	05-May-26	26-Sep-26	01-Jun-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B7-S-377	Backfilling / Compaction for Slab on Grade	7	05-May-26	12-May-26	01-Jun-26 A	08-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B7-S-382	Pouring Concrete for Ground Slab	4	17-May-26	20-May-26	08-Jul-26 A	12-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B7-S-378	Anti Termite Treatment below Ground Slab	1	13-May-26	13-May-26	08-Jul-26 A	12-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B7-S-379	Vapour barrier for below Ground Slab	2	14-May-26	16-May-26	08-Jul-26 A	12-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B7-S-517	Concrete pad	7	17-Sep-26	26-Sep-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		58	13-May-26	13-Jun-26	11-May-26 A	29-Aug-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B7-S-6101	Rebar for Tie Beams	4	25-May-26	01-Jun-26	11-May-26 A	12-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B7-S-6102	Formwork for Tie Beams	2	02-Jun-26	03-Jun-26	13-May-26 A	13-May-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B7-S-6103	Pouring Concrete for Tie Beams	1	04-Jun-26	04-Jun-26	14-May-26 A	14-May-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B7-S-5102	Formwork for column	4	19-May-26	23-May-26	01-Jun-26 A	07-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B7-S-5101	Rebar for column	5	13-May-26	18-May-26	25-Jun-26 A	02-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B7-S-5103	Pouring Concrete for column	1	24-May-26	24-May-26	05-Jul-26 A	22-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B7-S-6113	Rebar for Beams	4	06-Jun-26	09-Jun-26	16-Aug-26 A	19-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B7-S-6123	Formwork for Beams	2	10-Jun-26	11-Jun-26	20-Aug-26 A	26-Aug-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B7-S-6133	Pouring Concrete for Beams	1	13-Jun-26	13-Jun-26	26-Aug-26 A	29-Aug-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		41	15-Aug-26	22-Sep-26	13-Jun-26 A	21-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B7-SS-0100	Installation of columns	3	15-Aug-26	17-Aug-26	13-Jun-26 A	13-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B7-SS-0110	Installation of raft and purlins	5	18-Aug-26	23-Aug-26	14-Jun-26 A	15-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B7-SS-610	Intumescent paint to steel works	7	24-Aug-26	31-Aug-26	14-Jun-26 A	21-Jun-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B7-SS-0140	Installation of roof sheet	5	05-Sep-26	09-Sep-26	07-Jul-26 A	25-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B7-SS-1030	Steel members for external platform	7	09-Sep-26	16-Sep-26	24-Aug-26 A	19-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B7-SS-0130	Installation of wall sandwich panel	5	17-Sep-26	22-Sep-26	01-Sep-26 A	24-Sep-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B7-SS-620	Steel members for office area	7	01-Sep-26	08-Sep-26	21-Sep-26 A	24-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B7-SS-1020	Epoxy paint to steel members at office area	7	09-Sep-26	16-Sep-26	12-Nov-26	21-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B7-SS-1040	Epoxy paint for external platform	5	17-Sep-26	22-Sep-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		75	24-Aug-26	19-Dec-26	01-Jul-26 A	26-Dec-26	900,244.66	379,778.69	597,809.94	42.19%	66.41%
MASONARY WORKS		23	24-Aug-26	26-Sep-26	22-Jul-26 A	17-Aug-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B7-A-0120	Block work at factory area	10	24-Aug-26	03-Sep-26	22-Jul-26 A	26-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B7-A-0150	Block work at office area	7	09-Sep-26	16-Sep-26	25-Jul-26 A	17-Aug-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B7-A-170	Block work at toilet area	7	17-Sep-26	26-Sep-26	26-Jul-26 A	17-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		15	06-Oct-26	21-Nov-26	03-Sep-26 A	22-Nov-26	92,757.47	48,590.16	86,132.37	52.38%	92.86%
DAM3-C-B7-A-180	Internal Wall Plaster	15	06-Oct-26	22-Oct-26	03-Sep-26 A	24-Sep-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	28-Sep-26 A	22-Nov-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		5	05-Nov-26	10-Nov-26	04-Oct-26 A	15-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
DAM3-C-B7-A-240	Installation of Ceiling Gypsum Board	5	05-Nov-26	10-Nov-26	04-Oct-26 A	15-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
FLOOR FINISHES		29	28-Oct-26	19-Dec-26	19-Sep-26 A	26-Dec-26	189,488.90	0.00	73,398.02	0%	38.73%
DAM3-C-B7-A-220	Tiles for Toilet	7	28-Oct-26	04-Nov-26	19-Sep-26 A	28-Sep-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B7-A-250	Tiles for Office Area	2	11-Nov-26	12-Nov-26	19-Oct-26 A	25-Oct-26 A	26,867.31	0.00	26,867.31	0%	100%
DAM3-C-B7-A-390	Granite strip	2	14-Nov-26	15-Nov-26	26-Nov-26	29-Nov-26	671.12	0.00	0.00	0%	0%
DAM3-C-B7-A-420	Epoxy paint	7	12-Dec-26	19-Dec-26	19-Dec-26	26-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		8	24-Sep-26	10-Oct-26	21-Sep-26 A	26-Nov-26	248,575.06	248,575.06	169,282.30	100%	68.1%
DAM3-C-B7-A-558	Skylight fixtures installation	1	10-Oct-26	10-Oct-26	21-Sep-26 A	26-Sep-26 A	6,489.89	6,489.89	6,489.89	100%	100%
DAM3-C-B7-A-552	Window (CW1)	7	24-Sep-26	01-Oct-26	05-Oct-26 A	22-Oct-26 A	94,173.21	94,173.21	94,173.21	100%	100%
DAM3-C-B7-A-553	Roll up Shutter Door	1	03-Oct-26	03-Oct-26	18-Oct-26 A	20-Oct-26 A	68,619.20	68,619.20	68,619.20	100%	100%
DAM3-C-B7-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	04-Oct-26	04-Oct-26	21-Nov-26	22-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B7-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	05-Oct-26	05-Oct-26	22-Nov-26	23-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B7-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	06-Oct-26	06-Oct-26	23-Nov-26	24-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B7-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	07-Oct-26	07-Oct-26	24-Nov-26	25-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B7-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	08-Oct-26	08-Oct-26	25-Nov-26	26-Nov-26	16,711.52	16,711.52	0.00	100%	0%
WATER PROOFING WORKS		4	24-Oct-26	27-Oct-26	01-Oct-26 A	04-Oct-26 A	4,879.02	3,659.26	4,879.02	75%	100%
DAM3-C-B7-A-370	Waterproofing membrane for toilets	4	24-Oct-26	27-Oct-26	01-Oct-26 A	04-Oct-26 A	4,879.02	3,659.26	4,879.02	75%	100%
METAL WORKS		25	16-Nov-26	30-Nov-26	01-Jul-26 A	07-Dec-26	193,717.06	0.00	138,371.73	0%	71.43%
DAM3-C-B7-A-300	Galvanised Steel Gratings	2	29-Nov-26	30-Nov-26	01-Jul-26 A	01-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	30-Sep-26 A	07-Dec-26	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B7-A-290	Steel Ladder	2	16-Nov-26	17-Nov-26	29-Nov-26	01-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B7-A-291	Steel railing works	4	18-Nov-26	22-Nov-26	01-Dec-26	06-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		9	01-Dec-26	10-Dec-26	08-Dec-26	17-Dec-26	45,080.66	0.00	0.00	0%	0%
DAM3-C-B7-A-320	Installation of fittings	5	01-Dec-26	06-Dec-26	08-Dec-26	13-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B7-A-570	Identification sign; ID01 & ID02	3	07-Dec-26	09-Dec-26	14-Dec-26	16-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B7-A-340	Furniture Installation	1	10-Dec-26	10-Dec-26	17-Dec-26	17-Dec-26	12,468.83	0.00	0.00	0%	0%
MECHANICAL		178	05-May-26	10-Dec-26	10-Jun-26 A	07-Dec-26	467,522.66	18,585.14	343,953.58	3.98%	73.57%
HVAC		22	22-Nov-26	07-Dec-26	05-Oct-26 A	02-Dec-26	233,183.33	0.00	170,694.73	0%	73.2%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		6	29-Nov-26	02-Dec-26	05-Oct-26 A	11-Oct-26 A	170,694.73	0.00	170,694.73	0%	100%
DAM3-C-B7-M-140	Installation of HVAC Ducts	2	29-Nov-26	30-Nov-26	05-Oct-26 A	11-Oct-26 A	149,489.33	0.00	149,489.33	0%	100%
DAM3-C-B7-M-170	Installation of Duct insulation	2	01-Dec-26	02-Dec-26	06-Oct-26 A	11-Oct-26 A	21,205.40	0.00	21,205.40	0%	100%
SECOND STAGE		9	22-Nov-26	07-Dec-26	22-Nov-26	02-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B7-M-130	Installation of Exhaust Fans	2	22-Nov-26	23-Nov-26	22-Nov-26	24-Nov-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B7-M-160	Installation of Wall Propeller Type Exhaust Fan	3	24-Nov-26	28-Nov-26	24-Nov-26	28-Nov-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B7-M-339	Installation of Diffuser	2	03-Dec-26	05-Dec-26	28-Nov-26	30-Nov-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B7-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	06-Dec-26	07-Dec-26	30-Nov-26	02-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		41	22-Nov-26	10-Dec-26	29-Jul-26 A	06-Dec-26	102,458.78	0.00	99,752.72	0%	97.36%
FIRST STAGE		17	22-Nov-26	05-Dec-26	29-Jul-26 A	12-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B7-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	22-Nov-26	29-Nov-26	29-Jul-26 A	10-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B7-M-310	Installation of Fire Fighting Valve	5	30-Nov-26	05-Dec-26	09-Aug-26 A	12-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		14	06-Dec-26	10-Dec-26	24-Oct-26 A	06-Dec-26	17,864.62	0.00	15,158.56	0%	84.85%
DAM3-C-B7-M-320	Installation of Fire Hose Cabinet	3	06-Dec-26	08-Dec-26	24-Oct-26 A	25-Oct-26 A	15,158.56	0.00	15,158.56	0%	100%
DAM3-C-B7-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	08-Dec-26	10-Dec-26	02-Dec-26	06-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		153	05-May-26	29-Nov-26	10-Jun-26 A	07-Dec-26	90,009.74	18,585.14	31,913.45	20.65%	35.46%
FIRST STAGE		153	05-May-26	12-Nov-26	10-Jun-26 A	23-Nov-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B7-M-200	Installation of Sanitary Waste / Drainage Pipes	4	05-May-26	09-May-26	10-Jun-26 A	14-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B7-M-380	Installation of Trench drain	5	08-Nov-26	12-Nov-26	16-Jun-26 A	18-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B7-M-220	Installation of Floor Drain	2	05-Nov-26	07-Nov-26	21-Nov-26	23-Nov-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		12	14-Nov-26	29-Nov-26	17-Oct-26 A	07-Dec-26	48,859.84	0.00	1,819.51	0%	3.72%
DAM3-C-B7-M-180	Installation of Electric Water Heater	2	14-Nov-26	15-Nov-26	17-Oct-26 A	18-Oct-26 A	1,819.51	0.00	1,819.51	0%	100%
DAM3-C-B7-M-190	Installation of Sanitary Fixture and Accessories	4	16-Nov-26	19-Nov-26	23-Nov-26	28-Nov-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B7-M-210	Installation of Lavotary /Wash Basin	2	21-Nov-26	22-Nov-26	28-Nov-26	30-Nov-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B7-M-270	Installation of Bib Tap	2	23-Nov-26	24-Nov-26	30-Nov-26	02-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B7-M-428	Installation of Water Tap	2	25-Nov-26	26-Nov-26	02-Dec-26	05-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B7-M-429	Installation of Roof Vent Cap	2	28-Nov-26	29-Nov-26	05-Dec-26	07-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		43	22-Nov-26	03-Dec-26	30-Aug-26 A	28-Nov-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		9	22-Nov-26	28-Nov-26	30-Aug-26 A	03-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B7-M-290	Installation of Water Supply Pipes	4	22-Nov-26	25-Nov-26	30-Aug-26 A	03-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B7-M-280	Installation of Water Supply Valve	2	26-Nov-26	28-Nov-26	31-Aug-26 A	03-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		5	29-Nov-26	03-Dec-26	22-Nov-26	28-Nov-26	278.13	0.00	0.00	0%	0%
DAM3-C-B7-M-330	Capped connection	5	29-Nov-26	03-Dec-26	22-Nov-26	28-Nov-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		67	27-Sep-26	06-Jan-27	16-May-26 A	20-Dec-26	752,044.76	320,403.11	330,628.11	42.6%	43.96%
FIRST STAGE		63	27-Sep-26	08-Nov-26	16-May-26 A	12-Dec-26	86,114.12	30,077.67	36,105.84	34.93%	41.93%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	16-May-26 A	12-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	27-Sep-26	30-Sep-26	16-May-26 A	15-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	18-May-26 A	17-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	06-Sep-26 A	25-Nov-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B7-E-233	Installation of Wires	4	15-Oct-26	19-Oct-26	04-Oct-26 A	29-Nov-26	16,925.94	16,925.94	8,462.97	100%	50%
DAM3-C-B7-E-223	Installation of LV Cables	4	29-Oct-26	02-Nov-26	06-Dec-26	10-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		66	01-Oct-26	06-Jan-27	21-Sep-26 A	20-Dec-26	665,930.64	290,325.44	294,522.27	43.6%	44.23%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	21-Sep-26 A	02-Dec-26	76,166.74	76,166.74	22,850.02	100%	30%
DAM3-C-B7-E-420	Installation of Solar power plant	7	30-Dec-26	06-Jan-27	04-Oct-26 A	06-Oct-26 A	253,268.71	0.00	253,268.71	0%	100%
DAM3-C-B7-E-243	Installation of LP-1 Panel	2	22-Oct-26	24-Oct-26	10-Oct-26 A	14-Oct-26 A	18,403.54	18,403.54	18,403.54	100%	100%
DAM3-C-B7-E-123	Installation of Fire Alarm Control Panel	4	01-Oct-26	05-Oct-26	15-Nov-26	19-Nov-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B7-E-133	Installation of Fire Detectors & Accessories	4	06-Oct-26	10-Oct-26	19-Nov-26	24-Nov-26	56,740.37	56,740.37	0.00	100%	0%
DAM3-C-B7-E-173	Installation of Wiring Devices	4	22-Nov-26	25-Nov-26	22-Nov-26	26-Nov-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B7-E-203	Installation of Disconnect Switches	2	26-Nov-26	28-Nov-26	26-Nov-26	29-Nov-26	30,235.95	0.00	0.00	0%	0%

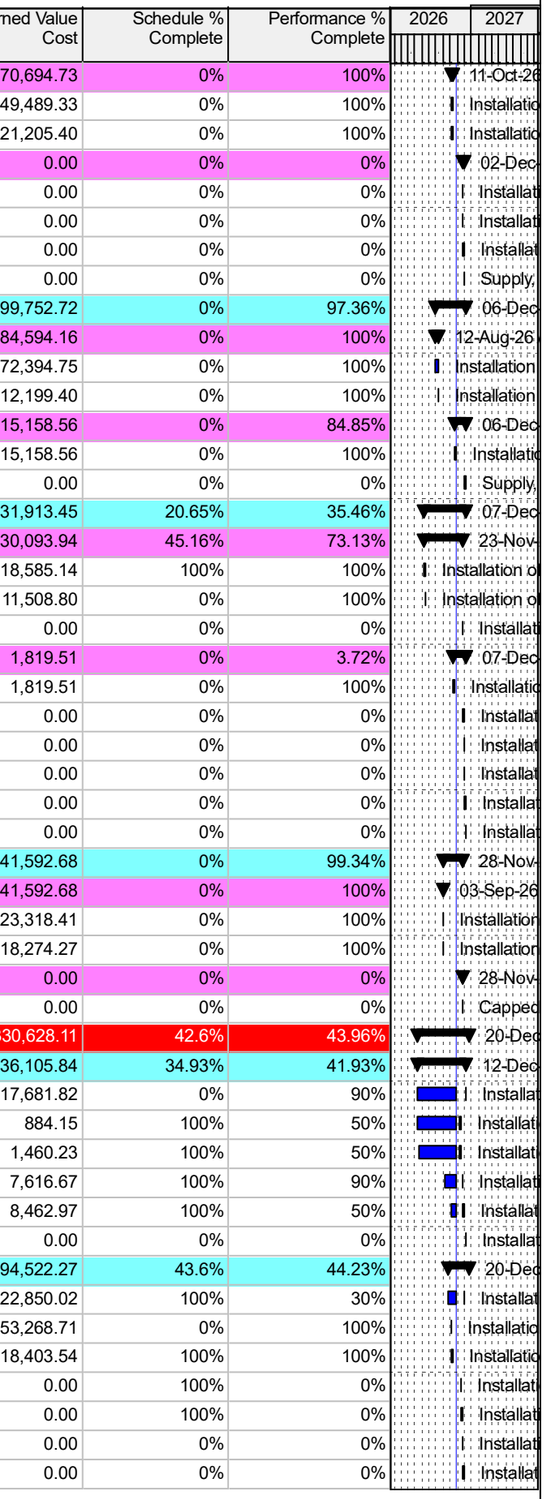

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B7-E-193	Installation of Main Distribution Board	2	20-Oct-26	21-Oct-26	29-Nov-26	01-Dec-26	32,472.73	32,472.73	0.00	100%	0%
DAM3-C-B7-E-410	Installation of CCTV System	7	20-Oct-26	27-Oct-26	29-Nov-26	07-Dec-26	76,349.24	65,442.20	0.00	85.71%	0%
DAM3-C-B7-E-253	Installation of PP-AC panel	2	25-Oct-26	26-Oct-26	01-Dec-26	03-Dec-26	21,648.48	21,648.48	0.00	100%	0%
DAM3-C-B7-E-213	Installation of Telephone Cabinet	2	27-Oct-26	28-Oct-26	03-Dec-26	06-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B7-E-273	Installation of Access Control System	5	28-Oct-26	02-Nov-26	07-Dec-26	13-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B7-E-283	Monitor Modules for Fire Alarm	2	03-Nov-26	04-Nov-26	13-Dec-26	15-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B7-E-293	Line Isolator Modules for Fire Alarm	2	05-Nov-26	07-Nov-26	15-Dec-26	17-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B7-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	08-Nov-26	09-Nov-26	17-Dec-26	20-Dec-26	3,082.69	0.00	0.00	0%	0%
BLOCK B8		282	19-Feb-26	14-Jan-27	17-Feb-26 A	13-Feb-27	5,075,523.09	3,278,936.91	3,965,623.39	64.6%	78.13%
STRUCTURAL		208	19-Feb-26	17-Oct-26	17-Feb-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		58	19-Feb-26	13-May-26	17-Feb-26 A	16-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B8-S-150	Excavation for footings	4	19-Feb-26	25-Feb-26	17-Feb-26 A	21-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B8-S-6283	Soil replacement - rock fill	4	25-Feb-26	02-Mar-26	28-Feb-26 A	02-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B8-S-6293	Engineering fill	4	03-Mar-26	07-Mar-26	08-Mar-26 A	16-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B8-S-103	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	28-Mar-26 A	28-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B8-S-102	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	28-Mar-26 A	28-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B8-S-101	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	28-Mar-26 A	28-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B8-S-104	Rebar for Footings	4	12-Mar-26	16-Mar-26	11-Apr-26 A	13-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B8-S-105	Formwork for Footings	4	09-May-26	12-May-26	13-Apr-26 A	14-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B8-S-106	Pouring Concrete for Footings	1	13-May-26	13-May-26	16-Apr-26 A	16-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		17	14-May-26	04-Jun-26	14-Apr-26 A	12-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B8-S-257	Rebar for column neck	4	14-May-26	18-May-26	14-Apr-26 A	15-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B8-S-267	Formwork for column neck	2	19-May-26	20-May-26	22-Apr-26 A	25-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B8-S-297	Pouring Concrete for column neck	1	21-May-26	21-May-26	23-Apr-26 A	25-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B8-S-307	Damp proof /Bitumin paint on Footings & column neck	2	23-May-26	24-May-26	27-Apr-26 A	30-Apr-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B8-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	25-May-26	04-Jun-26	05-May-26 A	12-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		24	20-Jun-26	09-Jul-26	13-May-26 A	03-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B8-S-338	Lean Concrete Below Grade Beams	2	23-Jun-26	24-Jun-26	13-May-26 A	13-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B8-S-337	Vapour barrier for Grade Beams	2	21-Jun-26	22-Jun-26	13-May-26 A	13-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B8-S-527	Anti Termite Below Grade Beams	1	20-Jun-26	20-Jun-26	13-May-26 A	13-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B8-S-339	Rebar for Grade Beams	5	25-Jun-26	30-Jun-26	16-May-26 A	20-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B8-S-341	Anchor bolts installation	2	01-Jul-26	02-Jul-26	17-May-26 A	20-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B8-S-340	Formwork for Grade Beams	2	01-Jul-26	02-Jul-26	20-May-26 A	23-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B8-S-342	Pouring Concrete for Grade Beams	1	04-Jul-26	04-Jul-26	24-May-26 A	25-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B8-S-347	Damp proof /Bitumin paint on Grade Beams	5	05-Jul-26	09-Jul-26	31-May-26 A	03-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		25	11-Jul-26	17-Oct-26	04-Jun-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B8-S-377	Backfilling / Compaction for Slab on Grade	7	11-Jul-26	18-Jul-26	04-Jun-26 A	09-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B8-S-382	Pouring Concrete for Ground Slab	4	22-Jul-26	26-Jul-26	13-Jul-26 A	16-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B8-S-378	Anti Termite Treatment below Ground Slab	1	19-Jul-26	19-Jul-26	13-Jul-26 A	16-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B8-S-379	Vapour barrier for below Ground Slab	2	20-Jul-26	21-Jul-26	13-Jul-26 A	16-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B8-S-517	Concrete pad	7	10-Oct-26	17-Oct-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		34	27-Jul-26	29-Aug-26	16-May-26 A	03-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B8-S-6103	Pouring Concrete for Tie Beams	1	19-Aug-26	20-Aug-26	16-May-26 A	25-May-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B8-S-6101	Rebar for Tie Beams	4	09-Aug-26	12-Aug-26	16-May-26 A	23-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B8-S-6102	Formwork for Tie Beams	2	13-Aug-26	15-Aug-26	16-May-26 A	24-May-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B8-S-5101	Rebar for column	5	27-Jul-26	01-Aug-26	02-Jul-26 A	11-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B8-S-5102	Formwork for column	4	02-Aug-26	05-Aug-26	07-Jul-26 A	25-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B8-S-5103	Pouring Concrete for column	1	08-Aug-26	08-Aug-26	13-Jul-26 A	26-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B8-S-6113	Rebar for Beams	4	20-Aug-26	25-Aug-26	23-Aug-26 A	26-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B8-S-6123	Formwork for Beams	2	25-Aug-26	27-Aug-26	29-Aug-26 A	01-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B8-S-6133	Pouring Concrete for Beams	1	27-Aug-26	29-Aug-26	01-Sep-26 A	03-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		44	05-Sep-26	14-Oct-26	14-Jun-26 A	24-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B8-SS-0100	Installation of columns	3	05-Sep-26	07-Sep-26	14-Jun-26 A	15-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B8-SS-0110	Installation of raft and purlins	5	08-Sep-26	13-Sep-26	15-Jun-26 A	16-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B8-SS-610	Intumescent paint to steel works	7	14-Sep-26	21-Sep-26	17-Jun-26 A	24-Jun-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B8-SS-0140	Installation of roof sheet	5	27-Sep-26	01-Oct-26	19-Jul-26 A	01-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B8-SS-0130	Installation of wall sandwich panel	5	10-Oct-26	14-Oct-26	02-Sep-26 A	22-Sep-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B8-SS-1030	Steel members for external platform	4	01-Oct-26	08-Oct-26	20-Sep-26 A	21-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B8-SS-620	Steel members for office area	4	22-Sep-26	30-Sep-26	26-Sep-26 A	28-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B8-SS-1020	Epoxy paint to steel members at office area	4	01-Oct-26	08-Oct-26	12-Nov-26	17-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B8-SS-1040	Epoxy paint for external platform	3	10-Oct-26	14-Oct-26	21-Nov-26	24-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		82	14-Sep-26	13-Jan-27	18-Jul-26 A	13-Feb-27	900,244.66	280,500.63	591,093.12	31.16%	65.66%
MASONARY WORKS		18	14-Sep-26	17-Oct-26	23-Jul-26 A	23-Aug-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B8-A-0120	Block work at factory area	5	14-Sep-26	26-Sep-26	23-Jul-26 A	27-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B8-A-0150	Block work at office area	5	01-Oct-26	08-Oct-26	23-Jul-26 A	23-Aug-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B8-A-170	Block work at toilet area	3	10-Oct-26	17-Oct-26	27-Jul-26 A	22-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		59	27-Oct-26	12-Dec-26	10-Sep-26 A	29-Dec-26	92,757.47	0.00	86,132.37	0%	92.86%
DAM3-C-B8-A-180	Internal Wall Plaster	10	27-Oct-26	12-Nov-26	10-Sep-26 A	28-Sep-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	01-Oct-26 A	29-Dec-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		3	26-Nov-26	01-Dec-26	15-Oct-26 A	20-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
DAM3-C-B8-A-240	Installation of Ceiling Gypsum Board	3	26-Nov-26	01-Dec-26	15-Oct-26 A	20-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
FLOOR FINISHES		40	18-Nov-26	13-Jan-27	30-Sep-26 A	13-Feb-27	189,488.90	0.00	66,681.19	0%	35.19%
DAM3-C-B8-A-220	Tiles for Toilet	4	18-Nov-26	25-Nov-26	30-Sep-26 A	04-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B8-A-250	Tiles for Office Area	2	02-Dec-26	03-Dec-26	24-Oct-26 A	29-Dec-26	26,867.31	0.00	20,150.48	0%	75%
DAM3-C-B8-A-390	Granite strip	2	05-Dec-26	06-Dec-26	29-Dec-26	31-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B8-A-420	Epoxy paint	2	06-Jan-27	13-Jan-27	10-Feb-27	13-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		9	15-Oct-26	31-Oct-26	27-Sep-26 A	18-Nov-26	248,575.06	201,546.42	169,282.30	81.08%	68.1%
DAM3-C-B8-A-558	Skylight fixtures installation	1	31-Oct-26	31-Oct-26	27-Sep-26 A	30-Sep-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B8-A-552	Window (CW1)	7	15-Oct-26	22-Oct-26	08-Oct-26 A	24-Oct-26 A	94,173.21	94,173.21	94,173.21	100%	100%
DAM3-C-B8-A-553	Roll up Shutter Door	1	24-Oct-26	24-Oct-26	19-Oct-26 A	21-Oct-26 A	68,619.20	68,619.20	68,619.20	100%	100%
DAM3-C-B8-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	25-Oct-26	25-Oct-26	12-Nov-26	14-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B8-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	26-Oct-26	26-Oct-26	14-Nov-26	15-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B8-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	27-Oct-26	27-Oct-26	15-Nov-26	16-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B8-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	28-Oct-26	28-Oct-26	16-Nov-26	17-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B8-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	29-Oct-26	29-Oct-26	17-Nov-26	18-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	14-Nov-26	17-Nov-26	05-Oct-26 A	08-Oct-26 A	4,879.02	0.00	4,879.02	0%	100%
DAM3-C-B8-A-370	Waterproofing membrane for toilets	4	14-Nov-26	17-Nov-26	05-Oct-26 A	08-Oct-26 A	4,879.02	0.00	4,879.02	0%	100%
METAL WORKS		39	07-Dec-26	21-Dec-26	18-Jul-26 A	21-Jan-27	193,717.06	0.00	138,371.73	0%	71.43%
DAM3-C-B8-A-300	Galvanised Steel Gratings	2	20-Dec-26	21-Dec-26	18-Jul-26 A	18-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B8-A-292	Aluminium composite panel	3	14-Dec-26	19-Dec-26	06-Oct-26 A	21-Jan-27	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B8-A-290	Steel Ladder	2	07-Dec-26	08-Dec-26	31-Dec-26	03-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B8-A-291	Steel railing works	4	09-Dec-26	13-Dec-26	03-Jan-27	07-Jan-27	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		7	27-Dec-26	05-Jan-27	02-Feb-27	10-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B8-A-320	Installation of fittings	3	27-Dec-26	31-Dec-26	02-Feb-27	06-Feb-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B8-A-570	Identification sign; ID01 & ID02	3	02-Jan-27	04-Jan-27	06-Feb-27	09-Feb-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B8-A-340	Furniture Installation	1	05-Jan-27	05-Jan-27	09-Feb-27	10-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		103	11-Jul-26	05-Jan-27	15-Jun-26 A	09-Feb-27	467,522.66	18,585.14	328,795.02	3.98%	70.33%
HVAC		18	13-Dec-26	28-Dec-26	11-Oct-26 A	10-Jan-27	233,183.33	0.00	170,694.73	0%	73.2%

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	20-Dec-26	23-Dec-26	11-Oct-26 A	15-Oct-26 A	170,694.73	0.00	170,694.73	0%	100%
DAM3-C-B8-M-140	Installation of HVAC Ducts	2	20-Dec-26	21-Dec-26	11-Oct-26 A	15-Oct-26 A	149,489.33	0.00	149,489.33	0%	100%
DAM3-C-B8-M-170	Installation of Duct insulation	2	22-Dec-26	23-Dec-26	11-Oct-26 A	15-Oct-26 A	21,205.40	0.00	21,205.40	0%	100%
SECOND STAGE		10	13-Dec-26	28-Dec-26	29-Dec-26	10-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B8-M-130	Installation of Exhaust Fans	2	13-Dec-26	14-Dec-26	29-Dec-26	31-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B8-M-160	Installation of Wall Propeller Type Exhaust Fan	4	15-Dec-26	19-Dec-26	31-Dec-26	05-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B8-M-339	Installation of Diffuser	2	24-Dec-26	26-Dec-26	05-Jan-27	07-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B8-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	27-Dec-26	28-Dec-26	07-Jan-27	10-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		30	13-Dec-26	05-Jan-27	12-Aug-26 A	09-Feb-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		11	13-Dec-26	26-Dec-26	12-Aug-26 A	16-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B8-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	4	13-Dec-26	20-Dec-26	12-Aug-26 A	16-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B8-M-310	Installation of Fire Fighting Valve	5	21-Dec-26	26-Dec-26	15-Aug-26 A	16-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		26	29-Dec-26	05-Jan-27	10-Jan-27	09-Feb-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B8-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	29-Dec-26	31-Dec-26	10-Jan-27	13-Jan-27	2,706.06	0.00	0.00	0%	0%
DAM3-C-B8-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	06-Feb-27	09-Feb-27	15,158.56	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		91	11-Jul-26	20-Dec-26	15-Jun-26 A	13-Jan-27	90,009.74	18,585.14	31,913.45	20.65%	35.46%
FIRST STAGE		91	11-Jul-26	03-Dec-26	15-Jun-26 A	30-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B8-M-200	Installation of Sanitary Waste / Drainage Pipes	4	11-Jul-26	14-Jul-26	15-Jun-26 A	20-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B8-M-380	Installation of Trench drain	5	29-Nov-26	03-Dec-26	20-Jun-26 A	21-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B8-M-220	Installation of Floor Drain	2	26-Nov-26	28-Nov-26	28-Dec-26	30-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		12	05-Dec-26	20-Dec-26	12-Oct-26 A	13-Jan-27	48,859.84	0.00	1,819.51	0%	3.72%
DAM3-C-B8-M-180	Installation of Electric Water Heater	2	05-Dec-26	06-Dec-26	12-Oct-26 A	14-Oct-26 A	1,819.51	0.00	1,819.51	0%	100%
DAM3-C-B8-M-190	Installation of Sanitary Fixture and Accessories	4	07-Dec-26	10-Dec-26	30-Dec-26	04-Jan-27	19,921.72	0.00	0.00	0%	0%
DAM3-C-B8-M-210	Installation of Lavotary /Wash Basin	2	12-Dec-26	13-Dec-26	04-Jan-27	06-Jan-27	21,416.68	0.00	0.00	0%	0%
DAM3-C-B8-M-270	Installation of Bib Tap	2	14-Dec-26	15-Dec-26	06-Jan-27	09-Jan-27	1,900.66	0.00	0.00	0%	0%
DAM3-C-B8-M-428	Installation of Water Tap	2	16-Dec-26	17-Dec-26	09-Jan-27	11-Jan-27	2,874.14	0.00	0.00	0%	0%
DAM3-C-B8-M-429	Installation of Roof Vent Cap	2	19-Dec-26	20-Dec-26	11-Jan-27	13-Jan-27	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		11	13-Dec-26	24-Dec-26	05-Sep-26 A	02-Jan-27	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		8	13-Dec-26	19-Dec-26	05-Sep-26 A	09-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B8-M-290	Installation of Water Supply Pipes	4	13-Dec-26	16-Dec-26	05-Sep-26 A	08-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B8-M-280	Installation of Water Supply Valve	2	17-Dec-26	19-Dec-26	06-Sep-26 A	09-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		3	20-Dec-26	24-Dec-26	29-Dec-26	02-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B8-M-330	Capped connection	3	20-Dec-26	24-Dec-26	29-Dec-26	02-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		68	18-Oct-26	14-Jan-27	19-May-26 A	13-Jan-27	752,044.76	24,140.13	117,826.56	3.21%	15.67%
FIRST STAGE		61	18-Oct-26	29-Nov-26	19-May-26 A	19-Dec-26	86,114.12	4,688.76	36,105.84	5.44%	41.93%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19-May-26 A	19-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	18-Oct-26	21-Oct-26	20-May-26 A	26-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	20-May-26 A	23-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	07-Sep-26 A	07-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B8-E-233	Installation of Wires	4	05-Nov-26	09-Nov-26	08-Oct-26 A	09-Dec-26	16,925.94	0.00	8,462.97	0%	50%
DAM3-C-B8-E-223	Installation of LV Cables	2	19-Nov-26	23-Nov-26	16-Dec-26	19-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		52	22-Oct-26	14-Jan-27	05-Oct-26 A	13-Jan-27	665,930.64	19,451.37	81,720.72	2.92%	12.27%
DAM3-C-B8-E-420	Installation of Solar power plant	7	07-Jan-27	14-Jan-27	05-Oct-26 A	13-Jan-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B8-E-243	Installation of LP-1 Panel	2	12-Nov-26	14-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B8-E-123	Installation of Fire Alarm Control Panel	4	22-Oct-26	26-Oct-26	26-Nov-26	01-Dec-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B8-E-133	Installation of Fire Detectors & Accessories	4	27-Oct-26	31-Oct-26	01-Dec-26	06-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B8-E-153	Installation of Lighting fixtures	4	10-Nov-26	14-Nov-26	09-Dec-26	14-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B8-E-193	Installation of Main Distribution Board	2	10-Nov-26	11-Nov-26	09-Dec-26	12-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B8-E-410	Installation of CCTV System	3	10-Nov-26	17-Nov-26	09-Dec-26	13-Dec-26	76,349.24	0.00	0.00	0%	0%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B8-E-253	Installation of PP-AC panel	2	15-Nov-26	16-Nov-26	12-Dec-26	14-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B8-E-273	Installation of Access Control System	3	18-Nov-26	23-Nov-26	13-Dec-26	16-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B8-E-213	Installation of Telephone Cabinet	2	17-Nov-26	18-Nov-26	14-Dec-26	16-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B8-E-283	Monitor Modules for Fire Alarm	2	24-Nov-26	25-Nov-26	16-Dec-26	19-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B8-E-293	Line Isolator Modules for Fire Alarm	2	26-Nov-26	28-Nov-26	19-Dec-26	21-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B8-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	29-Nov-26	30-Nov-26	21-Dec-26	23-Dec-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B8-E-173	Installation of Wiring Devices	3	13-Dec-26	16-Dec-26	29-Dec-26	02-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B8-E-203	Installation of Disconnect Switches	2	17-Dec-26	19-Dec-26	02-Jan-27	04-Jan-27	30,235.95	0.00	0.00	0%	0%
BLOCK B9		287	25-Feb-26	31-Jan-27	17-Feb-26 A	20-Jan-27	5,075,523.09	3,155,880.00	3,972,290.30	62.18%	78.26%
STRUCTURAL		211	25-Feb-26	20-Oct-26	17-Feb-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		96	25-Feb-26	13-May-26	17-Feb-26 A	23-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B9-S-150	Excavation for footings	4	25-Feb-26	02-Mar-26	17-Feb-26 A	21-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B9-S-6303	Soil replacement - rock fill	4	03-Mar-26	07-Mar-26	03-Mar-26 A	07-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B9-S-6313	Engineering fill	4	08-Mar-26	11-Mar-26	09-Mar-26 A	17-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B9-S-102	Vapour Barrier for Footings	1	14-Mar-26	14-Mar-26	29-Mar-26 A	29-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B9-S-101	Anti Termite Below Footings	1	12-Mar-26	12-Mar-26	29-Mar-26 A	29-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B9-S-103	Lean Concrete Below Footings	2	15-Mar-26	16-Mar-26	30-Mar-26 A	30-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B9-S-104	Rebar for Footings	4	04-May-26	07-May-26	18-Apr-26 A	20-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B9-S-105	Formwork for Footings	4	09-May-26	12-May-26	19-Apr-26 A	21-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B9-S-106	Pouring Concrete for Footings	1	13-May-26	13-May-26	23-Apr-26 A	23-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		14	14-May-26	04-Jun-26	21-Apr-26 A	14-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B9-S-257	Rebar for column neck	4	14-May-26	18-May-26	21-Apr-26 A	22-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B9-S-267	Formwork for column neck	2	19-May-26	20-May-26	22-Apr-26 A	23-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B9-S-297	Pouring Concrete for column neck	1	21-May-26	21-May-26	28-Apr-26 A	28-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B9-S-307	Damp proof /Bitumin paint on Footings & column neck	2	23-May-26	24-May-26	02-May-26 A	02-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B9-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	25-May-26	04-Jun-26	09-May-26 A	14-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		41	06-Jun-26	01-Jul-26	18-May-26 A	07-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B9-S-338	Lean Concrete Below Grade Beams	2	09-Jun-26	10-Jun-26	18-May-26 A	18-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B9-S-337	Vapour barrier for Grade Beams	2	07-Jun-26	08-Jun-26	18-May-26 A	18-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B9-S-527	Anti Termite Below Grade Beams	1	06-Jun-26	06-Jun-26	18-May-26 A	18-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B9-S-339	Rebar for Grade Beams	5	17-Jun-26	22-Jun-26	20-May-26 A	21-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B9-S-341	Anchor bolts installation	2	23-Jun-26	24-Jun-26	20-May-26 A	23-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B9-S-340	Formwork for Grade Beams	2	23-Jun-26	24-Jun-26	21-May-26 A	24-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B9-S-342	Pouring Concrete for Grade Beams	1	25-Jun-26	25-Jun-26	25-May-26 A	25-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B9-S-347	Damp proof /Bitumin paint on Grade Beams	5	27-Jun-26	01-Jul-26	02-Jun-26 A	07-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		82	15-Jul-26	20-Oct-26	09-Jun-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B9-S-377	Backfilling / Compaction for Slab on Grade	7	15-Jul-26	22-Jul-26	09-Jun-26 A	13-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B9-S-382	Pouring Concrete for Ground Slab	4	27-Jul-26	30-Jul-26	22-Jul-26 A	25-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B9-S-378	Anti Termite Treatment below Ground Slab	1	23-Jul-26	23-Jul-26	22-Jul-26 A	25-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B9-S-379	Vapour barrier for below Ground Slab	2	25-Jul-26	26-Jul-26	22-Jul-26 A	25-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B9-S-517	Concrete pad	7	13-Oct-26	20-Oct-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		74	23-Jul-26	19-Aug-26	21-May-26 A	12-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B9-S-6101	Rebar for Tie Beams	4	04-Aug-26	08-Aug-26	21-May-26 A	07-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B9-S-6102	Formwork for Tie Beams	2	09-Aug-26	10-Aug-26	23-May-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B9-S-6103	Pouring Concrete for Tie Beams	1	11-Aug-26	11-Aug-26	25-May-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B9-S-5101	Rebar for column	5	23-Jul-26	28-Jul-26	11-Jul-26 A	14-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B9-S-5102	Formwork for column	4	29-Jul-26	02-Aug-26	14-Jul-26 A	28-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B9-S-5103	Pouring Concrete for column	1	03-Aug-26	03-Aug-26	15-Jul-26 A	29-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B9-S-6113	Rebar for Beams	4	12-Aug-26	16-Aug-26	23-Aug-26 A	26-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B9-S-6123	Formwork for Beams	2	17-Aug-26	18-Aug-26	01-Sep-26 A	05-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B9-S-6133	Pouring Concrete for Beams	1	19-Aug-26	19-Aug-26	08-Sep-26 A	12-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		48	08-Sep-26	18-Oct-26	16-Jun-26 A	21-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B9-SS-0100	Installation of columns	3	08-Sep-26	10-Sep-26	16-Jun-26 A	17-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B9-SS-0110	Installation of raft and purlins	5	12-Sep-26	16-Sep-26	18-Jun-26 A	22-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B9-SS-610	Intumescent paint to steel works	7	17-Sep-26	26-Sep-26	05-Jul-26 A	07-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B9-SS-0140	Installation of roof sheet	5	30-Sep-26	05-Oct-26	22-Jul-26 A	01-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B9-SS-0130	Installation of wall sandwich panel	5	13-Oct-26	18-Oct-26	03-Sep-26 A	05-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B9-SS-1030	Steel members for external platform	7	05-Oct-26	12-Oct-26	21-Sep-26 A	26-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B9-SS-620	Steel members for office area	2	27-Sep-26	04-Oct-26	27-Sep-26 A	29-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B9-SS-1020	Epoxy paint to steel members at office area	7	05-Oct-26	12-Oct-26	12-Nov-26	21-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B9-SS-1040	Epoxy paint for external platform	5	13-Oct-26	18-Oct-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		88	17-Sep-26	12-Jan-27	27-Jul-26 A	17-Jan-27	900,244.66	173,127.42	597,760.02	19.23%	66.4%
MASONARY WORKS		19	17-Sep-26	20-Oct-26	28-Jul-26 A	29-Aug-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B9-A-0120	Block work at factory area	10	17-Sep-26	29-Sep-26	28-Jul-26 A	30-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B9-A-0150	Block work at office area	5	05-Oct-26	12-Oct-26	30-Jul-26 A	27-Aug-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B9-A-170	Block work at toilet area	5	13-Oct-26	20-Oct-26	02-Aug-26 A	29-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		27	31-Oct-26	15-Dec-26	17-Sep-26 A	29-Nov-26	92,757.47	0.00	86,132.37	0%	92.86%
DAM3-C-B9-A-180	Internal Wall Plaster	5	31-Oct-26	16-Nov-26	17-Sep-26 A	05-Oct-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	08-Dec-26	15-Dec-26	03-Oct-26 A	29-Nov-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		3	30-Nov-26	05-Dec-26	21-Oct-26 A	26-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
DAM3-C-B9-A-240	Installation of Ceiling Gypsum Board	3	30-Nov-26	05-Dec-26	21-Oct-26 A	26-Oct-26 A	46,792.30	0.00	46,792.30	0%	100%
FLOOR FINISHES		45	22-Nov-26	12-Jan-27	01-Oct-26 A	17-Jan-27	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B9-A-220	Tiles for Toilet	4	22-Nov-26	29-Nov-26	01-Oct-26 A	07-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B9-A-250	Tiles for Office Area	2	06-Dec-26	07-Dec-26	25-Nov-26	28-Nov-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B9-A-390	Granite strip	2	08-Dec-26	09-Dec-26	28-Nov-26	30-Nov-26	671.12	0.00	0.00	0%	0%
DAM3-C-B9-A-420	Epoxy paint	4	05-Jan-27	12-Jan-27	12-Jan-27	17-Jan-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		18	19-Oct-26	03-Nov-26	30-Sep-26 A	18-Nov-26	248,575.06	94,173.21	152,127.50	37.89%	61.2%
DAM3-C-B9-A-558	Skylight fixtures installation	1	03-Nov-26	03-Nov-26	30-Sep-26 A	04-Oct-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B9-A-552	Window (CW1)	7	19-Oct-26	26-Oct-26	10-Oct-26 A	25-Oct-26 A	94,173.21	94,173.21	94,173.21	100%	100%
DAM3-C-B9-A-553	Roll up Shutter Door	1	27-Oct-26	27-Oct-26	24-Oct-26 A	12-Nov-26	68,619.20	0.00	51,464.40	0%	75%
DAM3-C-B9-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	28-Oct-26	28-Oct-26	14-Nov-26	14-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B9-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	29-Oct-26	29-Oct-26	15-Nov-26	15-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B9-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	31-Oct-26	31-Oct-26	16-Nov-26	16-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B9-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	01-Nov-26	01-Nov-26	17-Nov-26	17-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B9-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	02-Nov-26	02-Nov-26	18-Nov-26	18-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	17-Nov-26	21-Nov-26	10-Oct-26 A	13-Oct-26 A	4,879.02	0.00	4,879.02	0%	100%
DAM3-C-B9-A-370	Waterproofing membrane for toilets	4	17-Nov-26	21-Nov-26	10-Oct-26 A	13-Oct-26 A	4,879.02	0.00	4,879.02	0%	100%
METAL WORKS		67	10-Dec-26	24-Dec-26	27-Jul-26 A	06-Dec-26	193,717.06	0.00	182,343.92	0%	94.13%
DAM3-C-B9-A-300	Galvanised Steel Gratings	2	23-Dec-26	24-Dec-26	27-Jul-26 A	27-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	29-Sep-26 A	06-Dec-26	175,888.76	0.00	175,888.76	0%	100%
DAM3-C-B9-A-290	Steel Ladder	2	10-Dec-26	12-Dec-26	30-Nov-26	02-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B9-A-291	Steel railing works	3	13-Dec-26	16-Dec-26	02-Dec-26	06-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		7	26-Dec-26	04-Jan-27	04-Jan-27	12-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B9-A-320	Installation of fittings	3	26-Dec-26	30-Dec-26	04-Jan-27	07-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B9-A-570	Identification sign; ID01 & ID02	3	31-Dec-26	03-Jan-27	07-Jan-27	11-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B9-A-340	Furniture Installation	1	04-Jan-27	04-Jan-27	11-Jan-27	12-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		158	02-Jul-26	04-Jan-27	21-Jun-26 A	14-Dec-26	467,522.66	18,585.14	328,795.02	3.98%	70.33%
HVAC		13	16-Dec-26	31-Dec-26	15-Oct-26 A	10-Dec-26	233,183.33	0.00	170,694.73	0%	73.2%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	23-Dec-26	27-Dec-26	15-Oct-26 A	18-Oct-26 A	170,694.73	0.00	170,694.73	0%	100%
DAM3-C-B9-M-140	Installation of HVAC Ducts	2	23-Dec-26	24-Dec-26	15-Oct-26 A	18-Oct-26 A	149,489.33	0.00	149,489.33	0%	100%
DAM3-C-B9-M-170	Installation of Duct insulation	2	26-Dec-26	27-Dec-26	15-Oct-26 A	18-Oct-26 A	21,205.40	0.00	21,205.40	0%	100%
SECOND STAGE		10	16-Dec-26	31-Dec-26	29-Nov-26	10-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B9-M-130	Installation of Exhaust Fans	2	16-Dec-26	17-Dec-26	29-Nov-26	01-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B9-M-160	Installation of Wall Propeller Type Exhaust Fan	4	19-Dec-26	22-Dec-26	01-Dec-26	06-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B9-M-339	Installation of Diffuser	2	28-Dec-26	29-Dec-26	06-Dec-26	08-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B9-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	30-Dec-26	31-Dec-26	08-Dec-26	10-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		20	16-Dec-26	04-Jan-27	17-Aug-26 A	14-Dec-26	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		10	16-Dec-26	29-Dec-26	17-Aug-26 A	23-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B9-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	16-Dec-26	23-Dec-26	17-Aug-26 A	22-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B9-M-310	Installation of Fire Fighting Valve	5	24-Dec-26	29-Dec-26	17-Aug-26 A	23-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		13	30-Dec-26	04-Jan-27	29-Nov-26	14-Dec-26	17,864.62	0.00	0.00	0%	0%
DAM3-C-B9-M-320	Installation of Fire Hose Cabinet	3	30-Dec-26	02-Jan-27	29-Nov-26	02-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B9-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	02-Jan-27	04-Jan-27	10-Dec-26	14-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		158	02-Jul-26	23-Dec-26	21-Jun-26 A	12-Dec-26	90,009.74	18,585.14	31,913.45	20.65%	35.46%
FIRST STAGE		158	02-Jul-26	07-Dec-26	21-Jun-26 A	28-Nov-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B9-M-200	Installation of Sanitary Waste / Drainage Pipes	4	02-Jul-26	06-Jul-26	21-Jun-26 A	24-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B9-M-380	Installation of Trench drain	5	02-Dec-26	07-Dec-26	22-Jun-26 A	24-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B9-M-220	Installation of Floor Drain	2	30-Nov-26	01-Dec-26	25-Nov-26	28-Nov-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		12	08-Dec-26	23-Dec-26	18-Oct-26 A	12-Dec-26	48,859.84	0.00	1,819.51	0%	3.72%
DAM3-C-B9-M-180	Installation of Electric Water Heater	2	08-Dec-26	09-Dec-26	18-Oct-26 A	19-Oct-26 A	1,819.51	0.00	1,819.51	0%	100%
DAM3-C-B9-M-190	Installation of Sanitary Fixture and Accessories	4	10-Dec-26	14-Dec-26	28-Nov-26	02-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B9-M-210	Installation of Lavotary /Wash Basin	2	15-Dec-26	16-Dec-26	02-Dec-26	05-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B9-M-270	Installation of Bib Tap	2	17-Dec-26	19-Dec-26	05-Dec-26	07-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B9-M-428	Installation of Water Tap	2	20-Dec-26	21-Dec-26	07-Dec-26	09-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B9-M-429	Installation of Roof Vent Cap	2	22-Dec-26	23-Dec-26	09-Dec-26	12-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		14	16-Dec-26	28-Dec-26	14-Sep-26 A	05-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		4	16-Dec-26	22-Dec-26	14-Sep-26 A	19-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B9-M-290	Installation of Water Supply Pipes	4	16-Dec-26	20-Dec-26	14-Sep-26 A	19-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B9-M-280	Installation of Water Supply Valve	2	21-Dec-26	22-Dec-26	15-Sep-26 A	19-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		5	23-Dec-26	28-Dec-26	29-Nov-26	05-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B9-M-330	Capped connection	5	23-Dec-26	28-Dec-26	29-Nov-26	05-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		77	21-Oct-26	31-Jan-27	20-May-26 A	20-Jan-27	752,044.76	8,456.43	117,826.56	1.12%	15.67%
FIRST STAGE		77	21-Oct-26	02-Dec-26	20-May-26 A	17-Dec-26	86,114.12	3,593.59	36,105.84	4.17%	41.93%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	20-May-26 A	17-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	21-Oct-26	25-Oct-26	21-May-26 A	23-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	21-May-26 A	25-Nov-26	2,920.45	1,825.28	1,460.23	62.5%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	08-Sep-26 A	03-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B9-E-233	Installation of Wires	4	09-Nov-26	12-Nov-26	11-Oct-26 A	06-Dec-26	16,925.94	0.00	8,462.97	0%	50%
DAM3-C-B9-E-223	Installation of LV Cables	4	23-Nov-26	26-Nov-26	13-Dec-26	17-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		63	26-Oct-26	31-Jan-27	06-Oct-26 A	20-Jan-27	665,930.64	4,862.84	81,720.72	0.73%	12.27%
DAM3-C-B9-E-420	Installation of Solar power plant	8	16-Jan-27	31-Jan-27	06-Oct-26 A	20-Jan-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B9-E-243	Installation of LP-1 Panel	2	16-Nov-26	17-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B9-E-123	Installation of Fire Alarm Control Panel	4	26-Oct-26	29-Oct-26	23-Nov-26	28-Nov-26	19,451.37	4,862.84	0.00	25%	0%
DAM3-C-B9-E-133	Installation of Fire Detectors & Accessories	4	31-Oct-26	03-Nov-26	28-Nov-26	02-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B9-E-173	Installation of Wiring Devices	4	16-Dec-26	20-Dec-26	29-Nov-26	03-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B9-E-203	Installation of Disconnect Switches	2	21-Dec-26	22-Dec-26	03-Dec-26	06-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B9-E-153	Installation of Lighting fixtures	4	14-Nov-26	17-Nov-26	06-Dec-26	10-Dec-26	76,166.74	0.00	0.00	0%	0%

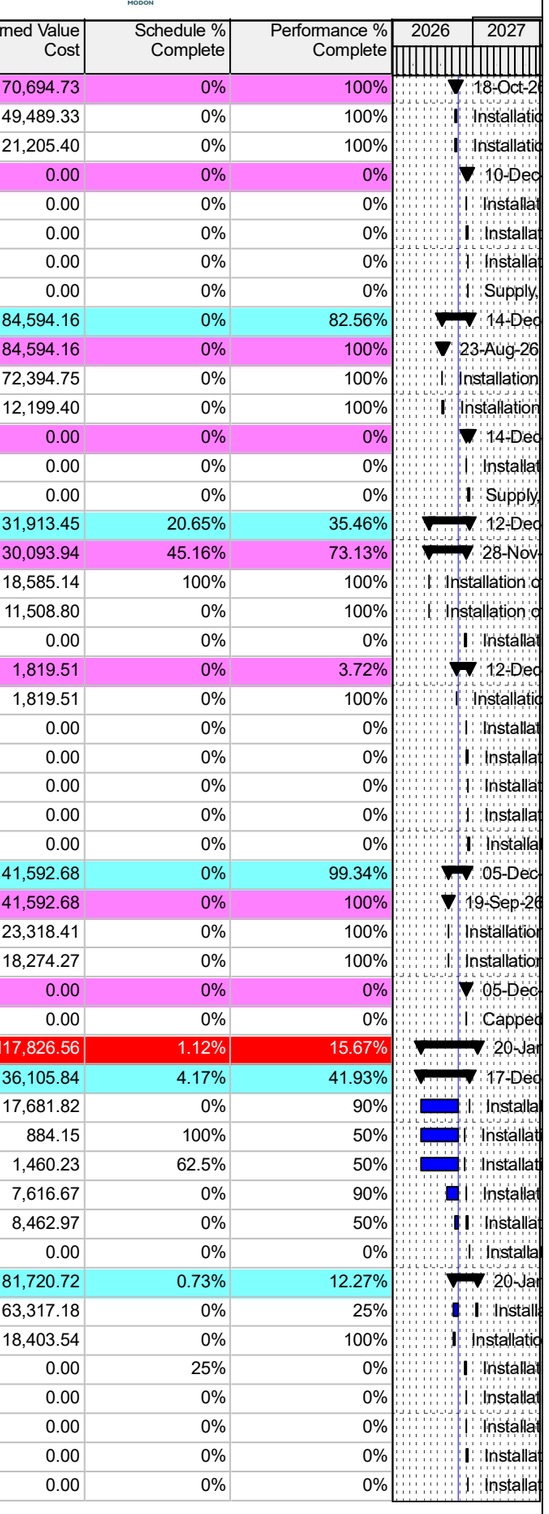


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B9-E-193	Installation of Main Distribution Board	2	14-Nov-26	15-Nov-26	06-Dec-26	08-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B9-E-410	Installation of CCTV System	5	14-Nov-26	21-Nov-26	06-Dec-26	12-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B9-E-253	Installation of PP-AC panel	2	18-Nov-26	19-Nov-26	08-Dec-26	10-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B9-E-213	Installation of Telephone Cabinet	2	21-Nov-26	22-Nov-26	10-Dec-26	13-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B9-E-273	Installation of Access Control System	5	22-Nov-26	26-Nov-26	12-Dec-26	17-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B9-E-283	Monitor Modules for Fire Alarm	2	28-Nov-26	29-Nov-26	17-Dec-26	20-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B9-E-293	Line Isolator Modules for Fire Alarm	2	30-Nov-26	01-Dec-26	20-Dec-26	22-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B9-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	02-Dec-26	03-Dec-26	22-Dec-26	24-Dec-26	3,082.69	0.00	0.00	0%	0%
BLOCK B10		293	03-Mar-26	08-Feb-27	18-Feb-26 A	25-Jan-27	5,075,523.09	3,108,677.89	3,732,431.34	61.25%	73.54%
STRUCTURAL		209	03-Mar-26	24-Oct-26	18-Feb-26 A	21-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		55	03-Mar-26	04-Apr-26	18-Feb-26 A	28-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B10-S-150	Excavation for footings	4	03-Mar-26	07-Mar-26	18-Feb-26 A	03-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B10-S-6323	Soil replacement - rock fill	4	08-Mar-26	11-Mar-26	07-Mar-26 A	11-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B10-S-6333	Engineering fill	4	12-Mar-26	16-Mar-26	18-Mar-26 A	31-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B10-S-103	Lean Concrete Below Footings	2	23-Mar-26	24-Mar-26	01-Apr-26 A	01-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B10-S-102	Vapour Barrier for Footings	1	22-Mar-26	22-Mar-26	01-Apr-26 A	01-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B10-S-101	Anti Termite Below Footings	1	21-Mar-26	21-Mar-26	01-Apr-26 A	01-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B10-S-104	Rebar for Footings	4	25-Mar-26	29-Mar-26	23-Apr-26 A	23-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B10-S-105	Formwork for Footings	4	30-Mar-26	02-Apr-26	23-Apr-26 A	25-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B10-S-106	Pouring Concrete for Footings	1	04-Apr-26	04-Apr-26	28-Apr-26 A	28-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		17	05-Apr-26	22-Apr-26	26-Apr-26 A	20-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B10-S-257	Rebar for column neck	4	05-Apr-26	08-Apr-26	26-Apr-26 A	27-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B10-S-267	Formwork for column neck	2	09-Apr-26	11-Apr-26	27-Apr-26 A	04-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B10-S-297	Pouring Concrete for column neck	1	12-Apr-26	12-Apr-26	02-May-26 A	05-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B10-S-307	Damp proof /Bitumin paint on Footings & column neck	2	13-Apr-26	14-Apr-26	05-May-26 A	09-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B10-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	15-Apr-26	22-Apr-26	13-May-26 A	20-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		16	23-Apr-26	13-May-26	25-May-26 A	15-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B10-S-338	Lean Concrete Below Grade Beams	2	27-Apr-26	28-Apr-26	25-May-26 A	25-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B10-S-337	Vapour barrier for Grade Beams	2	25-Apr-26	26-Apr-26	25-May-26 A	25-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B10-S-527	Anti Termite Below Grade Beams	1	23-Apr-26	23-Apr-26	25-May-26 A	25-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B10-S-339	Rebar for Grade Beams	5	29-Apr-26	04-May-26	31-May-26 A	03-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B10-S-341	Anchor bolts installation	2	05-May-26	06-May-26	02-Jun-26 A	03-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B10-S-340	Formwork for Grade Beams	2	05-May-26	06-May-26	07-Jun-26 A	09-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B10-S-342	Pouring Concrete for Grade Beams	1	07-May-26	07-May-26	09-Jun-26 A	09-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B10-S-347	Damp proof /Bitumin paint on Grade Beams	5	09-May-26	13-May-26	14-Jun-26 A	15-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		121	14-May-26	24-Oct-26	16-Jun-26 A	21-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B10-S-377	Backfilling / Compaction for Slab on Grade	7	14-May-26	21-May-26	16-Jun-26 A	22-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B10-S-382	Pouring Concrete for Ground Slab	4	30-May-26	02-Jun-26	18-Jul-26 A	21-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B10-S-378	Anti Termite Treatment below Ground Slab	1	23-May-26	23-May-26	18-Jul-26 A	21-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B10-S-379	Vapour barrier for below Ground Slab	2	24-May-26	25-May-26	18-Jul-26 A	21-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B10-S-517	Concrete pad	7	17-Oct-26	24-Oct-26	12-Nov-26	21-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		55	23-May-26	22-Jun-26	01-Jun-26 A	16-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B10-S-6101	Rebar for Tie Beams	4	07-Jun-26	10-Jun-26	01-Jun-26 A	03-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B10-S-6102	Formwork for Tie Beams	2	11-Jun-26	13-Jun-26	07-Jun-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B10-S-6103	Pouring Concrete for Tie Beams	1	14-Jun-26	14-Jun-26	09-Jun-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B10-S-5101	Rebar for column	5	23-May-26	31-May-26	12-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B10-S-5102	Formwork for column	4	01-Jun-26	04-Jun-26	04-Aug-26 A	06-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B10-S-5103	Pouring Concrete for column	1	06-Jun-26	06-Jun-26	05-Aug-26 A	09-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B10-S-6113	Rebar for Beams	4	15-Jun-26	18-Jun-26	31-Aug-26 A	02-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B10-S-6123	Formwork for Beams	2	20-Jun-26	21-Jun-26	08-Sep-26 A	15-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B10-S-6133	Pouring Concrete for Beams	1	22-Jun-26	22-Jun-26	12-Sep-26 A	16-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		48	12-Sep-26	21-Oct-26	25-Jun-26 A	18-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B10-SS-0100	Installation of columns	3	12-Sep-26	14-Sep-26	25-Jun-26 A	25-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B10-SS-0110	Installation of raft and purlins	5	15-Sep-26	20-Sep-26	25-Jun-26 A	28-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B10-SS-610	Intumescent paint to steel works	7	21-Sep-26	29-Sep-26	07-Jul-26 A	11-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B10-SS-0140	Installation of roof sheet	3	04-Oct-26	08-Oct-26	13-Aug-26 A	16-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B10-SS-0130	Installation of wall sandwich panel	5	17-Oct-26	21-Oct-26	03-Sep-26 A	30-Sep-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B10-SS-1030	Steel members for external platform	7	08-Oct-26	15-Oct-26	26-Sep-26 A	06-Oct-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B10-SS-620	Steel members for office area	4	30-Sep-26	07-Oct-26	29-Sep-26 A	30-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B10-SS-1020	Epoxy paint to steel members at office area	4	08-Oct-26	15-Oct-26	12-Nov-26	17-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B10-SS-1040	Epoxy paint for external platform	5	17-Oct-26	21-Oct-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		85	21-Sep-26	16-Jan-27	23-Jul-26 A	24-Dec-26	900,244.66	132,767.47	359,720.57	14.75%	39.96%
MASONARY WORKS		20	21-Sep-26	24-Oct-26	02-Aug-26 A	03-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B10-A-0120	Block work at factory area	3	21-Sep-26	03-Oct-26	02-Aug-26 A	23-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B10-A-0150	Block work at office area	4	08-Oct-26	15-Oct-26	08-Aug-26 A	01-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B10-A-170	Block work at toilet area	5	17-Oct-26	24-Oct-26	11-Aug-26 A	03-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		31	03-Nov-26	19-Dec-26	21-Sep-26 A	02-Dec-26	92,757.47	0.00	86,132.37	0%	92.86%
DAM3-C-B10-A-180	Internal Wall Plaster	5	03-Nov-26	19-Nov-26	21-Sep-26 A	12-Oct-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B10-A-230	Paint to Plaster (Primer, Putty & First Coat)	5	12-Dec-26	19-Dec-26	08-Oct-26 A	02-Dec-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		4	03-Dec-26	08-Dec-26	26-Oct-26 A	13-Dec-26	46,792.30	0.00	23,396.15	0%	50%
DAM3-C-B10-A-240	Installation of Ceiling Gypsum Board	4	03-Dec-26	08-Dec-26	26-Oct-26 A	13-Dec-26	46,792.30	0.00	23,396.15	0%	50%
FLOOR FINISHES		22	25-Nov-26	16-Jan-27	11-Oct-26 A	24-Dec-26	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B10-A-220	Tiles for Toilet	5	25-Nov-26	02-Dec-26	11-Oct-26 A	18-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B10-A-250	Tiles for Office Area	2	09-Dec-26	10-Dec-26	29-Nov-26	01-Dec-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B10-A-390	Granite strip	2	12-Dec-26	13-Dec-26	01-Dec-26	03-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B10-A-420	Epoxy paint	3	09-Jan-27	16-Jan-27	21-Dec-26	24-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		19	22-Oct-26	07-Nov-26	04-Oct-26 A	24-Nov-26	248,575.06	53,813.26	100,663.10	21.65%	40.5%
DAM3-C-B10-A-558	Skylight fixtures installation	1	07-Nov-26	07-Nov-26	04-Oct-26 A	06-Oct-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B10-A-552	Window (CW1)	7	22-Oct-26	29-Oct-26	14-Oct-26 A	26-Oct-26 A	94,173.21	53,813.26	94,173.21	57.14%	100%
DAM3-C-B10-A-553	Roll up Shutter Door	1	31-Oct-26	31-Oct-26	17-Nov-26	18-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B10-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	01-Nov-26	01-Nov-26	18-Nov-26	19-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B10-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	02-Nov-26	02-Nov-26	19-Nov-26	21-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B10-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	03-Nov-26	03-Nov-26	21-Nov-26	22-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B10-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	04-Nov-26	04-Nov-26	22-Nov-26	23-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B10-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	05-Nov-26	05-Nov-26	23-Nov-26	24-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	21-Nov-26	24-Nov-26	24-Nov-26	29-Nov-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B10-A-370	Waterproofing membrane for toilets	4	21-Nov-26	24-Nov-26	24-Nov-26	29-Nov-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		66	14-Dec-26	28-Dec-26	23-Jul-26 A	13-Dec-26	193,717.06	0.00	24,044.04	0%	12.41%
DAM3-C-B10-A-300	Galvanised Steel Gratings	2	27-Dec-26	28-Dec-26	23-Jul-26 A	23-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B10-A-292	Aluminium composite panel	3	21-Dec-26	26-Dec-26	14-Oct-26 A	13-Dec-26	175,888.76	0.00	17,588.88	0%	10%
DAM3-C-B10-A-290	Steel Ladder	2	14-Dec-26	15-Dec-26	03-Dec-26	06-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B10-A-291	Steel railing works	3	16-Dec-26	20-Dec-26	06-Dec-26	09-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		7	29-Dec-26	07-Jan-27	13-Dec-26	21-Dec-26	45,080.66	0.00	0.00	0%	0%
DAM3-C-B10-A-320	Installation of fittings	3	29-Dec-26	03-Jan-27	13-Dec-26	16-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B10-A-570	Identification sign; ID01 & ID02	3	04-Jan-27	06-Jan-27	16-Dec-26	20-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B10-A-340	Furniture Installation	1	07-Jan-27	07-Jan-27	20-Dec-26	21-Dec-26	12,468.83	0.00	0.00	0%	0%
MECHANICAL		168	14-May-26	07-Jan-27	01-Jul-26 A	17-Dec-26	467,522.66	18,585.14	326,975.51	3.98%	69.94%
HVAC		10	20-Dec-26	04-Jan-27	18-Oct-26 A	14-Dec-26	233,183.33	0.00	170,694.73	0%	73.2%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		2	27-Dec-26	30-Dec-26	18-Oct-26 A	20-Oct-26 A	170,694.73	0.00	170,694.73	0%	100%
DAM3-C-B10-M-140	Installation of HVAC Ducts	2	27-Dec-26	28-Dec-26	18-Oct-26 A	20-Oct-26 A	149,489.33	0.00	149,489.33	0%	100%
DAM3-C-B10-M-170	Installation of Duct insulation	2	29-Dec-26	30-Dec-26	18-Oct-26 A	20-Oct-26 A	21,205.40	0.00	21,205.40	0%	100%
SECOND STAGE		10	20-Dec-26	04-Jan-27	02-Dec-26	14-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B10-M-130	Installation of Exhaust Fans	2	20-Dec-26	21-Dec-26	02-Dec-26	05-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B10-M-160	Installation of Wall Propeller Type Exhaust Fan	4	22-Dec-26	26-Dec-26	05-Dec-26	09-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B10-M-339	Installation of Diffuser	2	31-Dec-26	02-Jan-27	09-Dec-26	12-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B10-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	03-Jan-27	04-Jan-27	12-Dec-26	14-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		20	20-Dec-26	07-Jan-27	23-Aug-26 A	17-Dec-26	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		8	20-Dec-26	02-Jan-27	23-Aug-26 A	29-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B10-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	20-Dec-26	27-Dec-26	23-Aug-26 A	27-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B10-M-310	Installation of Fire Fighting Valve	3	28-Dec-26	02-Jan-27	25-Aug-26 A	29-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		13	03-Jan-27	07-Jan-27	02-Dec-26	17-Dec-26	17,864.62	0.00	0.00	0%	0%
DAM3-C-B10-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	02-Dec-26	06-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B10-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	05-Jan-27	07-Jan-27	14-Dec-26	17-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		168	14-May-26	27-Dec-26	01-Jul-26 A	17-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		168	14-May-26	10-Dec-26	01-Jul-26 A	01-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B10-M-200	Installation of Sanitary Waste / Drainage Pipes	4	14-May-26	18-May-26	01-Jul-26 A	06-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B10-M-380	Installation of Trench drain	5	06-Dec-26	10-Dec-26	07-Jul-26 A	09-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B10-M-220	Installation of Floor Drain	2	03-Dec-26	05-Dec-26	29-Nov-26	01-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	12-Dec-26	27-Dec-26	01-Dec-26	17-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B10-M-180	Installation of Electric Water Heater	2	12-Dec-26	13-Dec-26	01-Dec-26	03-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B10-M-190	Installation of Sanitary Fixture and Accessories	4	14-Dec-26	17-Dec-26	03-Dec-26	08-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B10-M-210	Installation of Lavotary /Wash Basin	2	19-Dec-26	20-Dec-26	08-Dec-26	10-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B10-M-270	Installation of Bib Tap	2	21-Dec-26	22-Dec-26	10-Dec-26	13-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B10-M-428	Installation of Water Tap	2	23-Dec-26	24-Dec-26	13-Dec-26	15-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B10-M-429	Installation of Roof Vent Cap	2	26-Dec-26	27-Dec-26	15-Dec-26	17-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		19	20-Dec-26	31-Dec-26	17-Sep-26 A	08-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	20-Dec-26	26-Dec-26	17-Sep-26 A	21-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B10-M-280	Installation of Water Supply Valve	2	24-Dec-26	26-Dec-26	17-Sep-26 A	21-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B10-M-290	Installation of Water Supply Pipes	4	20-Dec-26	23-Dec-26	17-Sep-26 A	21-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	27-Dec-26	31-Dec-26	02-Dec-26	08-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B10-M-330	Capped connection	5	27-Dec-26	31-Dec-26	02-Dec-26	08-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		89	25-Oct-26	08-Feb-27	02-Jun-26 A	25-Jan-27	752,044.76	1,614.27	117,826.56	0.21%	15.67%
FIRST STAGE		81	25-Oct-26	06-Dec-26	02-Jun-26 A	09-Dec-26	86,114.12	1,614.27	36,105.84	1.87%	41.93%
DAM3-C-B10-E-113	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	02-Jun-26 A	09-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B10-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	25-Oct-26	28-Oct-26	03-Jun-26 A	15-Nov-26	1,768.31	884.15	884.15	50%	50%
DAM3-C-B10-E-183	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	03-Jun-26 A	15-Nov-26	2,920.45	730.11	1,460.23	25%	50%
DAM3-C-B10-E-163	Installation of Conduites for Lighting Fixture	4	08-Nov-26	11-Nov-26	21-Sep-26 A	25-Nov-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B10-E-233	Installation of Wires	4	12-Nov-26	16-Nov-26	14-Oct-26 A	28-Nov-26	16,925.94	0.00	8,462.97	0%	50%
DAM3-C-B10-E-223	Installation of LV Cables	4	26-Nov-26	30-Nov-26	05-Dec-26	09-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		75	29-Oct-26	08-Feb-27	07-Oct-26 A	25-Jan-27	665,930.64	0.00	81,720.72	0%	12.27%
DAM3-C-B10-E-420	Installation of Solar power plant	5	01-Feb-27	08-Feb-27	07-Oct-26 A	25-Jan-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B10-E-243	Installation of LP-1 Panel	2	19-Nov-26	21-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B10-E-123	Installation of Fire Alarm Control Panel	4	29-Oct-26	02-Nov-26	15-Nov-26	19-Nov-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B10-E-133	Installation of Fire Detectors & Accessories	4	03-Nov-26	07-Nov-26	19-Nov-26	24-Nov-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B10-E-153	Installation of Lighting fixtures	4	17-Nov-26	21-Nov-26	28-Nov-26	02-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B10-E-193	Installation of Main Distribution Board	2	17-Nov-26	18-Nov-26	28-Nov-26	30-Nov-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B10-E-410	Installation of CCTV System	7	17-Nov-26	24-Nov-26	28-Nov-26	06-Dec-26	76,349.24	0.00	0.00	0%	0%

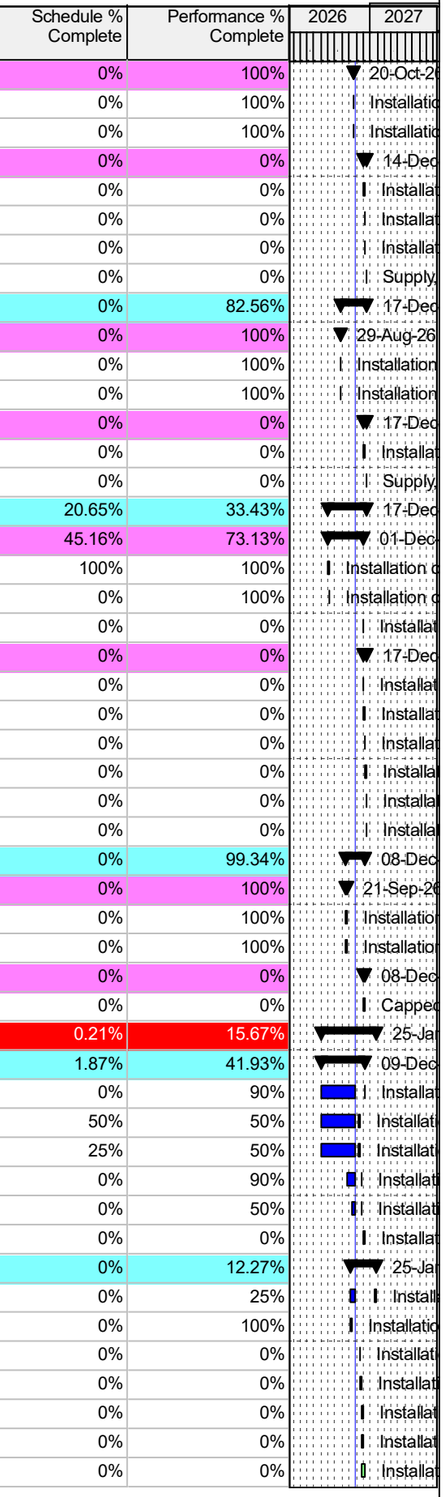


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B10-E-253	Installation of PP-AC panel	2	22-Nov-26	23-Nov-26	30-Nov-26	02-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B10-E-213	Installation of Telephone Cabinet	2	24-Nov-26	25-Nov-26	02-Dec-26	05-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B10-E-173	Installation of Wiring Devices	4	20-Dec-26	23-Dec-26	02-Dec-26	07-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B10-E-273	Installation of Access Control System	5	25-Nov-26	30-Nov-26	06-Dec-26	12-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B10-E-203	Installation of Disconnect Switches	2	24-Dec-26	26-Dec-26	07-Dec-26	09-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B10-E-283	Monitor Modules for Fire Alarm	2	01-Dec-26	02-Dec-26	12-Dec-26	14-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B10-E-293	Line Isolator Modules for Fire Alarm	2	03-Dec-26	05-Dec-26	14-Dec-26	16-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B10-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	06-Dec-26	07-Dec-26	16-Dec-26	19-Dec-26	3,082.69	0.00	0.00	0%	0%
BLOCK B11		288	08-Mar-26	16-Feb-27	18-Feb-26 A	28-Jan-27	5,075,523.09	3,064,511.75	3,672,612.19	60.38%	72.36%
STRUCTURAL		203	08-Mar-26	27-Oct-26	18-Feb-26 A	21-Nov-26	1,389,042.53	1,388,912.94	1,388,135.41	99.99%	99.93%
FOOTING		36	08-Mar-26	08-Apr-26	18-Feb-26 A	02-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B11-S-150	Excavation for footings	4	08-Mar-26	11-Mar-26	18-Feb-26 A	08-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B11-S-6343	Soil replacement - rock fill	4	12-Mar-26	16-Mar-26	08-Mar-26 A	16-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B11-S-6353	Engineering fill	4	21-Mar-26	24-Mar-26	26-Mar-26 A	31-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B11-S-103	Lean Concrete Below Footings	2	28-Mar-26	29-Mar-26	02-Apr-26 A	02-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B11-S-102	Vapour Barrier for Footings	1	26-Mar-26	26-Mar-26	02-Apr-26 A	02-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B11-S-101	Anti Termite Below Footings	1	25-Mar-26	25-Mar-26	02-Apr-26 A	02-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B11-S-104	Rebar for Footings	4	30-Mar-26	02-Apr-26	25-Apr-26 A	28-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B11-S-105	Formwork for Footings	4	04-Apr-26	07-Apr-26	28-Apr-26 A	29-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B11-S-106	Pouring Concrete for Footings	1	08-Apr-26	08-Apr-26	02-May-26 A	02-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		19	09-Apr-26	27-Apr-26	27-Apr-26 A	20-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B11-S-257	Rebar for column neck	4	09-Apr-26	13-Apr-26	27-Apr-26 A	28-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B11-S-267	Formwork for column neck	2	14-Apr-26	15-Apr-26	05-May-26 A	06-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B11-S-297	Pouring Concrete for column neck	1	16-Apr-26	16-Apr-26	07-May-26 A	07-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B11-S-307	Damp proof /Bitumin paint on Footings & column neck	2	18-Apr-26	19-Apr-26	11-May-26 A	13-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B11-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	20-Apr-26	27-Apr-26	17-May-26 A	20-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		18	28-Apr-26	18-May-26	24-May-26 A	13-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B11-S-338	Lean Concrete Below Grade Beams	2	02-May-26	03-May-26	24-May-26 A	24-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B11-S-337	Vapour barrier for Grade Beams	2	29-Apr-26	30-Apr-26	24-May-26 A	24-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B11-S-527	Anti Termite Below Grade Beams	1	28-Apr-26	28-Apr-26	24-May-26 A	24-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B11-S-339	Rebar for Grade Beams	5	04-May-26	09-May-26	01-Jun-26 A	03-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B11-S-340	Formwork for Grade Beams	2	10-May-26	11-May-26	02-Jun-26 A	06-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B11-S-341	Anchor bolts installation	2	10-May-26	11-May-26	02-Jun-26 A	03-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B11-S-342	Pouring Concrete for Grade Beams	1	12-May-26	12-May-26	06-Jun-26 A	06-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B11-S-347	Damp proof /Bitumin paint on Grade Beams	5	13-May-26	18-May-26	11-Jun-26 A	13-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		135	19-May-26	27-Oct-26	15-Jun-26 A	21-Nov-26	397,232.98	397,103.40	396,325.87	99.97%	99.77%
DAM3-C-B11-S-377	Backfilling / Compaction for Slab on Grade	7	19-May-26	30-May-26	15-Jun-26 A	21-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B11-S-382	Pouring Concrete for Ground Slab	4	03-Jun-26	07-Jun-26	26-Jul-26 A	28-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B11-S-378	Anti Termite Treatment below Ground Slab	1	31-May-26	31-May-26	26-Jul-26 A	28-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B11-S-379	Vapour barrier for below Ground Slab	2	01-Jun-26	02-Jun-26	26-Jul-26 A	28-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B11-S-517	Concrete pad	7	20-Oct-26	27-Oct-26	12-Nov-26	21-Nov-26	907.11	777.53	0.00	85.71%	0%
COLUMNS & BEAMS		81	31-May-26	27-Jun-26	02-Jun-26 A	01-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B11-S-6101	Rebar for Tie Beams	4	11-Jun-26	15-Jun-26	02-Jun-26 A	08-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B11-S-6102	Formwork for Tie Beams	2	16-Jun-26	17-Jun-26	03-Jun-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B11-S-6103	Pouring Concrete for Tie Beams	1	18-Jun-26	18-Jun-26	06-Jun-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B11-S-5101	Rebar for column	5	31-May-26	04-Jun-26	13-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B11-S-5102	Formwork for column	4	06-Jun-26	09-Jun-26	08-Aug-26 A	11-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B11-S-5103	Pouring Concrete for column	1	10-Jun-26	10-Jun-26	09-Aug-26 A	12-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B11-S-6113	Rebar for Beams	4	20-Jun-26	23-Jun-26	01-Sep-26 A	03-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B11-S-6123	Formwork for Beams	2	24-Jun-26	25-Jun-26	21-Sep-26 A	26-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B11-S-6133	Pouring Concrete for Beams	1	27-Jun-26	27-Jun-26	28-Sep-26 A	01-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		44	15-Sep-26	25-Oct-26	25-Jun-26 A	18-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B11-SS-0100	Installation of columns	3	15-Sep-26	17-Sep-26	25-Jun-26 A	28-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B11-SS-0110	Installation of raft and purlins	5	19-Sep-26	24-Sep-26	30-Jun-26 A	01-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B11-SS-610	Intumescent paint to steel works	7	26-Sep-26	03-Oct-26	19-Jul-26 A	25-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B11-SS-0140	Installation of roof sheet	5	07-Oct-26	12-Oct-26	01-Aug-26 A	08-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B11-SS-0130	Installation of wall sandwich panel	5	20-Oct-26	25-Oct-26	03-Sep-26 A	30-Sep-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B11-SS-620	Steel members for office area	7	04-Oct-26	11-Oct-26	27-Sep-26 A	30-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B11-SS-1030	Steel members for external platform	7	12-Oct-26	19-Oct-26	04-Oct-26 A	07-Oct-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B11-SS-1020	Epoxy paint to steel members at office area	4	12-Oct-26	19-Oct-26	12-Nov-26	17-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B11-SS-1040	Epoxy paint for external platform	5	20-Oct-26	25-Oct-26	12-Nov-26	18-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		88	26-Sep-26	19-Jan-27	30-Jul-26 A	20-Dec-26	900,244.66	90,345.19	308,364.39	10.04%	34.25%
MASONARY WORKS		21	26-Sep-26	27-Oct-26	06-Aug-26 A	06-Sep-26 A	78,954.21	76,891.88	78,954.21	97.39%	100%
DAM3-C-B11-A-0120	Block work at factory area	5	26-Sep-26	06-Oct-26	06-Aug-26 A	11-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B11-A-0150	Block work at office area	3	12-Oct-26	19-Oct-26	10-Aug-26 A	06-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B11-A-170	Block work at toilet area	4	20-Oct-26	27-Oct-26	13-Aug-26 A	06-Sep-26 A	14,436.31	12,373.98	14,436.31	85.71%	100%
WALL FINISHES		10	07-Nov-26	22-Dec-26	27-Sep-26 A	30-Nov-26	92,757.47	0.00	81,715.64	0%	88.1%
DAM3-C-B11-A-180	Internal Wall Plaster	10	07-Nov-26	23-Nov-26	27-Sep-26 A	15-Oct-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B11-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	15-Dec-26	22-Dec-26	24-Oct-26 A	30-Nov-26	44,167.30	0.00	33,125.48	0%	75%
CIELING FINISHES		5	07-Dec-26	12-Dec-26	26-Nov-26	02-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B11-A-240	Installation of Ceiling Gypsum Board	5	07-Dec-26	12-Dec-26	26-Nov-26	02-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		14	29-Nov-26	19-Jan-27	25-Oct-26 A	10-Dec-26	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B11-A-220	Tiles for Toilet	5	29-Nov-26	06-Dec-26	25-Oct-26 A	27-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B11-A-250	Tiles for Office Area	2	13-Dec-26	14-Dec-26	26-Nov-26	29-Nov-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B11-A-390	Granite strip	2	15-Dec-26	16-Dec-26	29-Nov-26	01-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B11-A-420	Epoxy paint	7	12-Jan-27	19-Jan-27	02-Dec-26	10-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		16	26-Oct-26	10-Nov-26	06-Oct-26 A	22-Nov-26	248,575.06	13,453.32	77,119.80	5.41%	31.02%
DAM3-C-B11-A-558	Skylight fixtures installation	1	10-Nov-26	10-Nov-26	06-Oct-26 A	08-Oct-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B11-A-552	Window (CW1)	7	26-Oct-26	02-Nov-26	20-Oct-26 A	15-Nov-26	94,173.21	13,453.32	70,629.91	14.29%	75%
DAM3-C-B11-A-553	Roll up Shutter Door	1	03-Nov-26	03-Nov-26	15-Nov-26	16-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B11-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	04-Nov-26	04-Nov-26	16-Nov-26	17-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B11-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	05-Nov-26	05-Nov-26	17-Nov-26	18-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B11-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	07-Nov-26	07-Nov-26	18-Nov-26	19-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B11-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	08-Nov-26	08-Nov-26	19-Nov-26	21-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B11-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	09-Nov-26	09-Nov-26	21-Nov-26	22-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	24-Nov-26	28-Nov-26	22-Nov-26	26-Nov-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B11-A-370	Waterproofing membrane for toilets	4	24-Nov-26	28-Nov-26	22-Nov-26	26-Nov-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		71	17-Dec-26	31-Dec-26	30-Jul-26 A	12-Dec-26	193,717.06	0.00	24,044.04	0%	12.41%
DAM3-C-B11-A-300	Galvanised Steel Gratings	2	30-Dec-26	31-Dec-26	30-Jul-26 A	30-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B11-A-292	Aluminium composite panel	3	24-Dec-26	29-Dec-26	15-Oct-26 A	12-Dec-26	175,888.76	0.00	17,588.88	0%	10%
DAM3-C-B11-A-290	Steel Ladder	2	17-Dec-26	19-Dec-26	01-Dec-26	03-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B11-A-291	Steel railing works	4	20-Dec-26	23-Dec-26	03-Dec-26	08-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		7	02-Jan-27	11-Jan-27	12-Dec-26	20-Dec-26	45,080.66	0.00	0.00	0%	0%
DAM3-C-B11-A-320	Installation of fittings	3	02-Jan-27	06-Jan-27	12-Dec-26	15-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B11-A-570	Identification sign; ID01 & ID02	3	07-Jan-27	10-Jan-27	15-Dec-26	19-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B11-A-340	Furniture Installation	1	11-Jan-27	11-Jan-27	19-Dec-26	20-Dec-26	12,468.83	0.00	0.00	0%	0%
MECHANICAL		182	19-May-26	11-Jan-27	05-Jul-26 A	15-Dec-26	467,522.66	18,585.14	326,975.51	3.98%	69.94%
HVAC		13	23-Dec-26	07-Jan-27	21-Oct-26 A	10-Dec-26	233,183.33	0.00	170,694.73	0%	73.2%


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	30-Dec-26	03-Jan-27	21-Oct-26 A	25-Oct-26 A	170,694.73	0.00	170,694.73	0%	100%
DAM3-C-B11-M-140	Installation of HVAC Ducts	2	30-Dec-26	31-Dec-26	21-Oct-26 A	25-Oct-26 A	149,489.33	0.00	149,489.33	0%	100%
DAM3-C-B11-M-170	Installation of Duct insulation	2	02-Jan-27	03-Jan-27	21-Oct-26 A	25-Oct-26 A	21,205.40	0.00	21,205.40	0%	100%
SECOND STAGE		9	23-Dec-26	07-Jan-27	30-Nov-26	10-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B11-M-130	Installation of Exhaust Fans	2	23-Dec-26	24-Dec-26	30-Nov-26	02-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B11-M-160	Installation of Wall Propeller Type Exhaust Fan	3	26-Dec-26	29-Dec-26	02-Dec-26	06-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B11-M-339	Installation of Diffuser	2	04-Jan-27	05-Jan-27	06-Dec-26	08-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B11-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	06-Jan-27	07-Jan-27	08-Dec-26	10-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		27	23-Dec-26	11-Jan-27	29-Aug-26 A	14-Dec-26	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		8	23-Dec-26	05-Jan-27	29-Aug-26 A	07-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B11-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	23-Dec-26	30-Dec-26	29-Aug-26 A	05-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B11-M-310	Installation of Fire Fighting Valve	3	31-Dec-26	05-Jan-27	30-Aug-26 A	07-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		12	06-Jan-27	11-Jan-27	30-Nov-26	14-Dec-26	17,864.62	0.00	0.00	0%	0%
DAM3-C-B11-M-320	Installation of Fire Hose Cabinet	3	06-Jan-27	09-Jan-27	30-Nov-26	03-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B11-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	09-Jan-27	11-Jan-27	10-Dec-26	14-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		182	19-May-26	30-Dec-26	05-Jul-26 A	15-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		182	19-May-26	14-Dec-26	05-Jul-26 A	29-Nov-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B11-M-200	Installation of Sanitary Waste / Drainage Pipes	4	19-May-26	23-May-26	05-Jul-26 A	08-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B11-M-380	Installation of Trench drain	5	09-Dec-26	14-Dec-26	06-Jul-26 A	08-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B11-M-220	Installation of Floor Drain	2	07-Dec-26	08-Dec-26	26-Nov-26	29-Nov-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	15-Dec-26	30-Dec-26	29-Nov-26	15-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B11-M-180	Installation of Electric Water Heater	2	15-Dec-26	16-Dec-26	29-Nov-26	01-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B11-M-190	Installation of Sanitary Fixture and Accessories	4	17-Dec-26	21-Dec-26	01-Dec-26	06-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B11-M-210	Installation of Lavotary /Wash Basin	2	22-Dec-26	23-Dec-26	06-Dec-26	08-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B11-M-270	Installation of Bib Tap	2	24-Dec-26	26-Dec-26	08-Dec-26	10-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B11-M-428	Installation of Water Tap	2	27-Dec-26	28-Dec-26	10-Dec-26	13-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B11-M-429	Installation of Roof Vent Cap	2	29-Dec-26	30-Dec-26	13-Dec-26	15-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		27	23-Dec-26	04-Jan-27	01-Oct-26 A	06-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	23-Dec-26	29-Dec-26	01-Oct-26 A	05-Oct-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B11-M-280	Installation of Water Supply Valve	2	28-Dec-26	29-Dec-26	01-Oct-26 A	05-Oct-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B11-M-290	Installation of Water Supply Pipes	4	23-Dec-26	27-Dec-26	01-Oct-26 A	05-Oct-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	30-Dec-26	04-Jan-27	30-Nov-26	06-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B11-M-330	Capped connection	5	30-Dec-26	04-Jan-27	30-Nov-26	06-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		125	28-Oct-26	16-Feb-27	01-Jun-26 A	28-Jan-27	752,044.76	0.00	109,363.59	0%	14.54%
FIRST STAGE		78	28-Oct-26	09-Dec-26	01-Jun-26 A	16-Dec-26	86,114.12	0.00	27,642.87	0%	32.1%
DAM3-C-B11-E-113	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	01-Jun-26 A	16-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	28-Oct-26	01-Nov-26	02-Jun-26 A	19-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B11-E-183	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	02-Jun-26 A	22-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B11-E-163	Installation of Conduites for Lighting Fixture	4	11-Nov-26	15-Nov-26	27-Sep-26 A	30-Nov-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B11-E-233	Installation of Wires	4	16-Nov-26	19-Nov-26	30-Nov-26	05-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B11-E-223	Installation of LV Cables	4	30-Nov-26	03-Dec-26	12-Dec-26	16-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		67	02-Nov-26	16-Feb-27	08-Oct-26 A	28-Jan-27	665,930.64	0.00	81,720.72	0%	12.27%
DAM3-C-B11-E-420	Installation of Solar power plant	4	09-Feb-27	16-Feb-27	08-Oct-26 A	28-Jan-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B11-E-243	Installation of LP-1 Panel	2	23-Nov-26	24-Nov-26	10-Oct-26 A	14-Oct-26 A	18,403.54	0.00	18,403.54	0%	100%
DAM3-C-B11-E-123	Installation of Fire Alarm Control Panel	4	02-Nov-26	05-Nov-26	19-Nov-26	24-Nov-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B11-E-133	Installation of Fire Detectors & Accessories	4	07-Nov-26	10-Nov-26	24-Nov-26	29-Nov-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B11-E-173	Installation of Wiring Devices	4	23-Dec-26	27-Dec-26	30-Nov-26	05-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B11-E-153	Installation of Lighting fixtures	4	21-Nov-26	24-Nov-26	05-Dec-26	09-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B11-E-193	Installation of Main Distribution Board	2	21-Nov-26	22-Nov-26	05-Dec-26	07-Dec-26	32,472.73	0.00	0.00	0%	0%

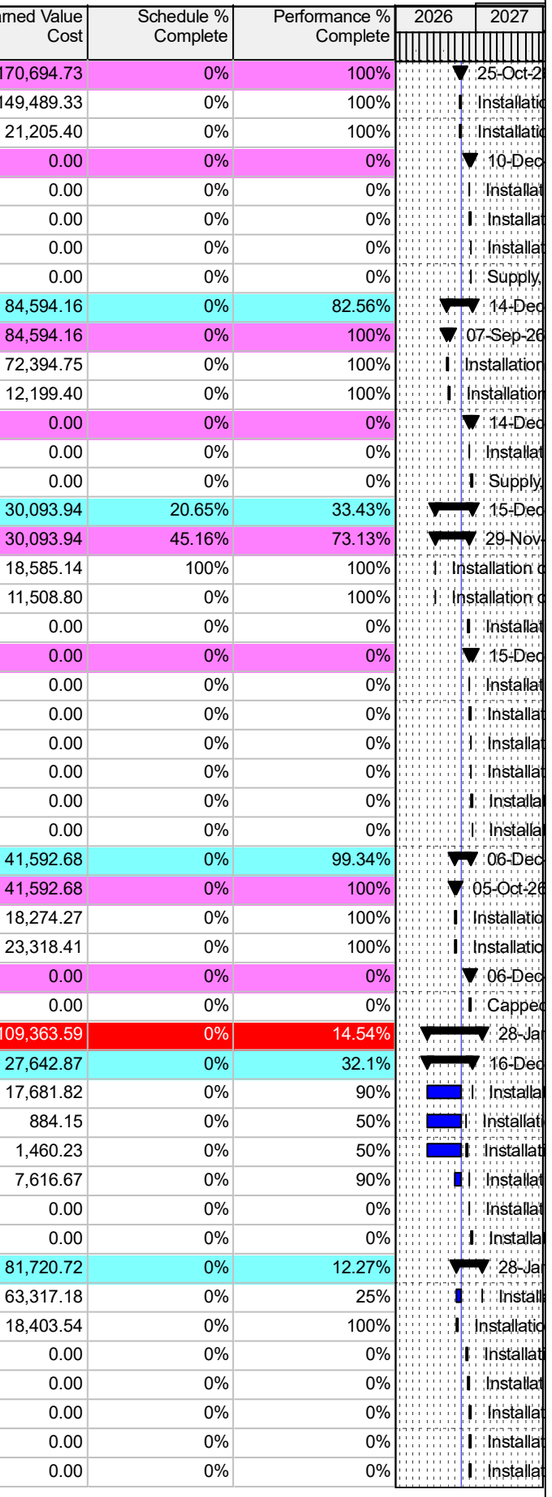

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B11-E-410	Installation of CCTV System	5	21-Nov-26	28-Nov-26	05-Dec-26	10-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B11-E-203	Installation of Disconnect Switches	2	28-Dec-26	29-Dec-26	05-Dec-26	07-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B11-E-253	Installation of PP-AC panel	2	25-Nov-26	26-Nov-26	07-Dec-26	09-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B11-E-213	Installation of Telephone Cabinet	2	28-Nov-26	29-Nov-26	09-Dec-26	12-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B11-E-273	Installation of Access Control System	5	29-Nov-26	03-Dec-26	10-Dec-26	16-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B11-E-283	Monitor Modules for Fire Alarm	2	05-Dec-26	06-Dec-26	16-Dec-26	19-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B11-E-293	Line Isolator Modules for Fire Alarm	2	07-Dec-26	08-Dec-26	19-Dec-26	21-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B11-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	09-Dec-26	10-Dec-26	21-Dec-26	23-Dec-26	3,082.69	0.00	0.00	0%	0%
SITE INFRASTRUCTURE		288	10-Feb-26	21-Feb-27	19-Jan-26 A	24-Feb-27	8,476,025.35	2,219,077.88	2,904,440.55	26.18%	34.27%
SITE WORKS		23	10-Feb-26	10-Mar-26	19-Jan-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
DAM3-C-GEN-180	Initial Site Survey and Setting out	3	10-Feb-26	12-Feb-26	19-Jan-26 A	24-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-C-GEN-190	Excavation to the target grading level	20	14-Feb-26	10-Mar-26	10-Feb-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
NETWORKS		86	07-Sep-26	23-Dec-26	01-Aug-26 A	27-Jan-27	1,901,944.63	1,098,134.71	1,401,571.13	57.74%	73.69%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UNITS)		42	07-Sep-26	21-Oct-26	01-Aug-26 A	23-Nov-26	571,716.96	571,716.96	514,545.27	100%	90%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	07-Sep-26	14-Sep-26	01-Aug-26 A	14-Nov-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	15-Sep-26	27-Sep-26	02-Aug-26 A	15-Nov-26	364,244.28	364,244.28	327,819.85	100%	90%
DAM3-C-ENV-F-192	Installation of Valves	5	30-Sep-26	05-Oct-26	02-Aug-26 A	22-Nov-26	86,057.93	86,057.93	77,452.13	100%	90%
DAM3-C-ENV-F-202	Warning Tapes	2	28-Sep-26	29-Sep-26	03-Aug-26 A	21-Nov-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	06-Oct-26	21-Oct-26	05-Aug-26 A	23-Nov-26	40,471.58	40,471.58	36,424.43	100%	90%
WATER SUPPLY SYSTEM		37	15-Sep-26	23-Dec-26	04-Oct-26 A	26-Dec-26	290,579.64	187,004.81	203,908.20	64.36%	70.17%
DAM3-C-ENV-WS-806	Construction of Washout Chamber	7	06-Oct-26	13-Oct-26	04-Oct-26 A	05-Dec-26	17,314.15	17,314.15	13,851.32	100%	80%
DAM3-C-ENV-WS-846	Construction of Air Valve Chamber	7	14-Oct-26	21-Oct-26	04-Oct-26 A	06-Dec-26	16,236.37	16,236.37	12,989.09	100%	80%
DAM3-C-ENV-WS-786	Excavation for Water Suppy Works	7	15-Sep-26	22-Sep-26	12-Oct-26 A	01-Dec-26	13,950.39	13,950.39	11,160.32	100%	80%
DAM3-C-ENV-WS-746	Installation of HDPE PN16 Pipes for Cold Water Supply	7	24-Sep-26	05-Oct-26	17-Oct-26 A	02-Dec-26	125,553.50	125,553.50	100,442.80	100%	80%
DAM3-C-ENV-WS-766	Installation of Valves	5	16-Nov-26	21-Nov-26	17-Oct-26 A	06-Dec-26	53,930.05	0.00	43,144.04	0%	80%
DAM3-C-ENV-WS-776	Warning Tape	2	14-Oct-26	15-Oct-26	18-Oct-26 A	05-Dec-26	13,950.39	13,950.39	11,160.32	100%	80%
DAM3-C-ENV-WS-796	Backfilling for Water Supply	14	22-Nov-26	07-Dec-26	18-Oct-26 A	09-Dec-26	13,950.39	0.00	11,160.32	0%	80%
DAM3-C-ENV-WS-826	Supply and install Service connection -HDPE	14	08-Dec-26	23-Dec-26	09-Dec-26	26-Dec-26	35,694.38	0.00	0.00	0%	0%
SEWER & DRAINAGE SYSTEM		36	06-Oct-26	08-Dec-26	22-Aug-26 A	22-Dec-26	772,226.27	268,602.69	683,117.66	34.78%	88.46%
DAM3-C-ENV-SW-496	Construction of inspection chambers	7	03-Nov-26	10-Nov-26	22-Aug-26 A	03-Oct-26 A	249,925.25	0.00	249,925.25	0%	100%
DAM3-C-ENV-SW-516	Excavation for Sewer Works	7	06-Oct-26	13-Oct-26	22-Aug-26 A	04-Oct-26 A	22,261.94	22,261.94	22,261.94	100%	100%
DAM3-C-ENV-SW-536	Construction of Manhole	7	26-Oct-26	02-Nov-26	22-Aug-26 A	10-Sep-26 A	166,049.07	23,721.30	166,049.07	14.29%	100%
DAM3-C-ENV-SW-486	Installation of UPVC Pipes for Sewer	4	14-Oct-26	25-Oct-26	16-Sep-26 A	05-Oct-26 A	222,619.45	222,619.45	222,619.45	100%	100%
DAM3-C-ENV-SW-526	Backfilling for Sewer Drainage	14	03-Nov-26	18-Nov-26	17-Sep-26 A	06-Oct-26 A	22,261.94	0.00	22,261.94	0%	100%
DAM3-C-ENV-SW-506	Gully trap	10	19-Nov-26	30-Nov-26	02-Dec-26	14-Dec-26	53,541.58	0.00	0.00	0%	0%
DAM3-C-ENV-SW-546	UPVC pipe service connection	7	01-Dec-26	08-Dec-26	14-Dec-26	22-Dec-26	35,567.03	0.00	0.00	0%	0%
IRRIGATION SYSTEM		48	06-Oct-26	22-Dec-26	02-Dec-26	27-Jan-27	267,421.77	70,810.25	0.00	26.48%	0%
DAM3-C-ENV-SW-556	Excavation for HDPE pipes	7	06-Oct-26	13-Oct-26	02-Dec-26	10-Dec-26	6,309.39	6,309.39	0.00	100%	0%
DAM3-C-ENV-SW-566	Installation of HDPE Pipes	10	14-Oct-26	25-Oct-26	10-Dec-26	22-Dec-26	63,093.94	63,093.94	0.00	100%	0%
DAM3-C-ENV-SW-586	Construction of Washout valve chamber	5	26-Oct-26	31-Oct-26	22-Dec-26	28-Dec-26	3,247.85	649.57	0.00	20%	0%
DAM3-C-ENV-SW-576	Construction of Air valve chamber	5	26-Oct-26	31-Oct-26	22-Dec-26	28-Dec-26	3,786.75	757.35	0.00	20%	0%
DAM3-C-ENV-SW-596	Backfilling for HDPE pipes	14	01-Nov-26	16-Nov-26	28-Dec-26	13-Jan-27	6,309.39	0.00	0.00	0%	0%
DAM3-C-ENV-SW-606	Installation of valves	5	09-Dec-26	14-Dec-26	13-Jan-27	19-Jan-27	84,556.00	0.00	0.00	0%	0%
DAM3-C-ENV-SW-616	Main program system and controller for irrigation system	7	15-Dec-26	22-Dec-26	19-Jan-27	27-Jan-27	100,118.45	0.00	0.00	0%	0%
EXTERNAL WORKS		74	15-Sep-26	25-Jan-27	01-Jul-26 A	24-Feb-27	3,338,525.71	923,252.29	1,305,178.54	27.65%	39.09%
MECHANICAL		34	26-Oct-26	10-Jan-27	01-Jul-26 A	08-Dec-26	1,375,655.38	162.39	1,305,178.54	0.01%	94.88%
DAM3-C-ENV-M-1371	Installation of GRP Tanks	10	30-Nov-26	10-Dec-26	08-Aug-26 A	08-Oct-26 A	585,839.88	0.00	585,839.88	0%	100%
DAM3-C-ENV-M-1301	Installation of Fire Fighting Pump	4	31-Dec-26	04-Jan-27	22-Sep-26 A	22-Sep-26 A	345,880.31	0.00	345,880.31	0%	100%
DAM3-C-ENV-M-1341	Installation of Booster Pump	5	26-Dec-26	30-Dec-26	07-Oct-26 A	07-Oct-26 A	38,967.27	0.00	38,967.27	0%	100%

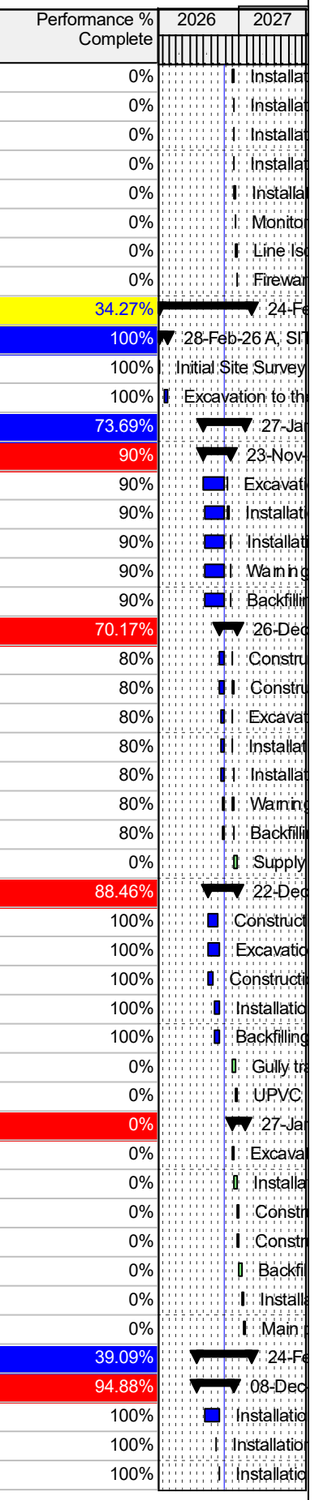

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-ENV-M-1381	Valves for GRP Tank	3	12-Dec-26	14-Dec-26	19-Oct-26 A	06-Dec-26	58,583.98	0.00	52,725.59	0%	90%
DAM3-C-ENV-M-1311	CO2 fire extinguisher	1	05-Jan-27	05-Jan-27	02-Dec-26	03-Dec-26	217.29	0.00	0.00	0%	0%
DAM3-C-ENV-M-1361	Powder fire extinguisher	1	06-Jan-27	06-Jan-27	03-Dec-26	05-Dec-26	188.33	0.00	0.00	0%	0%
DAM3-C-ENV-M-1351	Valves for Water Supply Pump	2	03-Jan-27	04-Jan-27	05-Dec-26	07-Dec-26	4,329.70	0.00	0.00	0%	0%
DAM3-C-ENV-M-1391	Access Ladder for GRP Tank	2	15-Dec-26	16-Dec-26	06-Dec-26	08-Dec-26	58,583.98	0.00	0.00	0%	0%
GRP Tank Foundation		31	31-Oct-26	29-Nov-26	27-Jul-26 A	27-Aug-26 A	180,037.46	0.00	180,037.46	0%	100%
DAM3-C-GRP-S-0101	Excavation for Foundation	4	31-Oct-26	03-Nov-26	27-Jul-26 A	27-Jul-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0103	Lean Concrete Below Foundation	2	07-Nov-26	08-Nov-26	06-Aug-26 A	06-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
DAM3-C-GRP-S-0102	Vapour Barrier for Foundation	2	04-Nov-26	05-Nov-26	06-Aug-26 A	06-Aug-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0104	Rebar for Foundation	4	09-Nov-26	12-Nov-26	11-Aug-26 A	16-Aug-26 A	36,007.49	0.00	36,007.49	0%	100%
DAM3-C-GRP-S-0105	Formwork for Foundation	4	14-Nov-26	17-Nov-26	12-Aug-26 A	23-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
DAM3-C-GRP-S-0106	Pouring Concrete for Foundation	1	18-Nov-26	18-Nov-26	18-Aug-26 A	23-Aug-26 A	63,013.11	0.00	63,013.11	0%	100%
DAM3-C-GRP-S-0107	Damp proof /Bitumin paint on Foundation	2	19-Nov-26	21-Nov-26	24-Aug-26 A	25-Aug-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0108	Backfilling / Compaction Around Foundation	7	22-Nov-26	29-Nov-26	26-Aug-26 A	27-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
Pump Shed		34	26-Oct-26	10-Jan-27	01-Jul-26 A	08-Dec-26	103,027.17	162.39	101,728.03	0.16%	98.74%
DAM3-C-PR-S-108	Excavation for Footings	4	26-Oct-26	29-Oct-26	01-Jul-26 A	02-Jul-26 A	649.57	162.39	649.57	25%	100%
DAM3-C-PR-S-138	Lean Concrete Below Footings	2	02-Nov-26	03-Nov-26	23-Jul-26 A	23-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-308	Vapour Barrier for Footings	2	31-Oct-26	01-Nov-26	23-Jul-26 A	23-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-198	Rebar for Footings	4	04-Nov-26	08-Nov-26	25-Jul-26 A	25-Jul-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-208	Formwork for Footings	4	09-Nov-26	12-Nov-26	25-Jul-26 A	25-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-148	Pouring Concrete for Footings	1	14-Nov-26	14-Nov-26	26-Jul-26 A	26-Jul-26 A	5,846.13	0.00	5,846.13	0%	100%
DAM3-C-PR-S-298	Damp proof /Bitumin paint on Footing Sides	2	15-Nov-26	16-Nov-26	28-Jul-26 A	28-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-378	Backfilling / Compaction Around Footings to Bottom of Grade Beams	5	17-Nov-26	22-Nov-26	29-Jul-26 A	03-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-158	Lean Concrete Below Grade Beams	2	25-Nov-26	26-Nov-26	04-Aug-26 A	04-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-328	Vapour barrier for Grade Beams	2	23-Nov-26	24-Nov-26	04-Aug-26 A	04-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-218	Rebar for Grade Beams	2	28-Nov-26	29-Nov-26	15-Aug-26 A	15-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-228	Formwork for Grade Beams	2	30-Nov-26	01-Dec-26	16-Aug-26 A	17-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-188	Pedestal including anchor bolts	1	30-Nov-26	30-Nov-26	17-Aug-26 A	17-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-168	Pouring Concrete for Grade Beams	1	02-Dec-26	02-Dec-26	18-Aug-26 A	18-Aug-26 A	3,247.85	0.00	3,247.85	0%	100%
DAM3-C-PR-S-338	Damp proof /Bitumin paint on Grade Beams	2	03-Dec-26	05-Dec-26	20-Aug-26 A	22-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-388	Backfilling / Compaction for Slab on Grade	5	06-Dec-26	10-Dec-26	23-Aug-26 A	24-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-318	Anti Termite Treatment below Ground Slab	1	12-Dec-26	12-Dec-26	24-Aug-26 A	24-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-348	Vapour barrier for below Ground Slab	2	13-Dec-26	14-Dec-26	24-Aug-26 A	24-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-268	Rebar for Ground Slab	4	15-Dec-26	19-Dec-26	25-Aug-26 A	26-Aug-26 A	12,070.63	0.00	12,070.63	0%	100%
DAM3-C-PR-S-278	Formwork for Ground Slab	4	20-Dec-26	23-Dec-26	26-Aug-26 A	26-Aug-26 A	8,263.60	0.00	8,263.60	0%	100%
DAM3-C-PR-S-178	Pouring Concrete for Ground Slab	1	24-Dec-26	24-Dec-26	27-Aug-26 A	27-Aug-26 A	20,334.24	0.00	20,334.24	0%	100%
DAM3-C-PR-S-128	Installation of Columns	3	31-Dec-26	03-Jan-27	30-Aug-26 A	30-Aug-26 A	7,794.85	0.00	7,794.85	0%	100%
DAM3-C-PR-S-358	Installation of Raft & Purlins	4	04-Jan-27	07-Jan-27	30-Aug-26 A	30-Aug-26 A	11,042.69	0.00	11,042.69	0%	100%
DAM3-C-PR-S-368	Installation of Roof Sheet	2	09-Jan-27	10-Jan-27	31-Aug-26 A	31-Aug-26 A	19,487.12	0.00	19,487.12	0%	100%
DAM3-C-PR-S-288	Concrete Pad	5	26-Dec-26	30-Dec-26	02-Dec-26	08-Dec-26	1,299.14	0.00	0.00	0%	0%
ELECTRICAL		17	31-Dec-26	25-Jan-27	02-Dec-26	22-Dec-26	236,867.32	0.00	0.00	0%	0%
DAM3-C-ENV-E-176	Installation of Main MCC	2	31-Dec-26	02-Jan-27	02-Dec-26	05-Dec-26	13,498.43	0.00	0.00	0%	0%
DAM3-C-ENV-E-236	Installation of panel boards	2	05-Jan-27	06-Jan-27	02-Dec-26	05-Dec-26	5,953.91	0.00	0.00	0%	0%
DAM3-C-ENV-E-1321	Installation of wiring devices	5	07-Jan-27	12-Jan-27	05-Dec-26	10-Dec-26	5,632.31	0.00	0.00	0%	0%
DAM3-C-ENV-E-186	Installation of Earthing and Grounding	3	03-Jan-27	07-Jan-27	05-Dec-26	08-Dec-26	1,399.38	0.00	0.00	0%	0%
DAM3-C-ENV-E-1341	Installation of Cable tray	5	07-Jan-27	12-Jan-27	05-Dec-26	10-Dec-26	3,563.73	0.00	0.00	0%	0%
DAM3-C-ENV-E-206	Installation of Conduites for Lighting Fixture	4	09-Jan-27	12-Jan-27	08-Dec-26	13-Dec-26	798.20	0.00	0.00	0%	0%
DAM3-C-ENV-E-216	Installation of LV Cables	5	13-Jan-27	18-Jan-27	10-Dec-26	16-Dec-26	7,709.71	0.00	0.00	0%	0%
DAM3-C-ENV-E-226	Installation of Wires	2	13-Jan-27	14-Jan-27	13-Dec-26	15-Dec-26	1,596.40	0.00	0.00	0%	0%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-C-ENV-E-196	Installation of Lighting fixtures	2	16-Jan-27	17-Jan-27	15-Dec-26	17-Dec-26	7,183.81	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-1331	Installation of Programmable Logis Controller	4	18-Jan-27	25-Jan-27	17-Dec-26	22-Dec-26	189,531.43	0.00	0.00	0%	0%		Installa
EXTERNAL ELECTRICAL WORKS		56	15-Sep-26	01-Dec-26	30-Nov-26	02-Feb-27	1,711,707.92	923,089.90	0.00	53.93%	0%		02-Fe
DAM3-C-ENV-E-400	Installation of UPVC Pipe	5	15-Sep-26	20-Sep-26	30-Nov-26	05-Dec-26	76,356.22	76,356.22	0.00	100%	0%		Installa
DAM3-C-ENV-E-410	Construction of Concrete encased duct bank	8	21-Sep-26	03-Oct-26	06-Dec-26	14-Dec-26	687,205.97	687,205.97	0.00	100%	0%		Constru
DAM3-C-ENV-E-420	Installation of Sleeves for lighting poles	5	04-Oct-26	08-Oct-26	15-Dec-26	20-Dec-26	19,588.78	19,588.78	0.00	100%	0%		Installa
DAM3-C-ENV-E-390	Installation of Telecom manhole	4	10-Oct-26	20-Oct-26	21-Dec-26	24-Dec-26	120,350.16	120,350.16	0.00	100%	0%		Installa
DAM3-C-ENV-E-450	Foundation for Lighting poles	5	21-Oct-26	26-Oct-26	26-Dec-26	30-Dec-26	19,588.78	19,588.78	0.00	100%	0%		Founda
DAM3-C-ENV-E-440	Installation of Lighting poles	5	27-Oct-26	03-Nov-26	31-Dec-26	05-Jan-27	156,710.21	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-430	Installation of Lighting Fixture	5	04-Nov-26	09-Nov-26	06-Jan-27	11-Jan-27	39,177.55	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-380	Installation of LV Cables	7	10-Nov-26	17-Nov-26	12-Jan-27	19-Jan-27	98,914.91	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-460	Electrical Manhole	7	18-Nov-26	25-Nov-26	20-Jan-27	27-Jan-27	253,329.40	0.00	0.00	0%	0%		Electri
DAM3-C-ENV-E-470	Installation of Earthing and Grounding	5	26-Nov-26	01-Dec-26	28-Jan-27	02-Feb-27	19,643.55	0.00	0.00	0%	0%		Install
DAM3-C-ENV-E-480	Installation of Street Lighting Feeder pillars & KWH meter	5	26-Nov-26	01-Dec-26	28-Jan-27	02-Feb-27	220,842.40	0.00	0.00	0%	0%		Install
FENCES AND GATES		37	10-Nov-26	10-Jan-27	12-Jan-27	24-Feb-27	14,295.10	0.00	0.00	0%	0%		24-Fe
DAM3-C-ENV-S-1374	Excavation for Fence	2	10-Nov-26	17-Nov-26	12-Jan-27	13-Jan-27	597.56	0.00	0.00	0%	0%		Excava
DAM3-C-ENV-S-1354	Vapour Barrier for Fence	4	18-Nov-26	22-Nov-26	14-Jan-27	18-Jan-27	298.78	0.00	0.00	0%	0%		Vapou
DAM3-C-ENV-S-1274	Lean Concrete Below Fence	4	23-Nov-26	26-Nov-26	19-Jan-27	23-Jan-27	597.56	0.00	0.00	0%	0%		Lean
DAM3-C-ENV-S-1304	Rebar for Footings	7	28-Nov-26	05-Dec-26	24-Jan-27	31-Jan-27	1,195.12	0.00	0.00	0%	0%		Rebar
DAM3-C-ENV-S-1314	Formwork for Footings	4	06-Dec-26	09-Dec-26	01-Feb-27	04-Feb-27	597.56	0.00	0.00	0%	0%		Formw
DAM3-C-ENV-S-1284	Pouring Concrete for Footings	2	10-Dec-26	12-Dec-26	06-Feb-27	07-Feb-27	1,792.67	0.00	0.00	0%	0%		Pourin
DAM3-C-ENV-S-1344	Damp proof /Bitumin paint on Footing Sides	2	13-Dec-26	14-Dec-26	08-Feb-27	09-Feb-27	298.78	0.00	0.00	0%	0%		Damp
DAM3-C-ENV-S-1364	Backfilling / Compaction Around Footings	4	15-Dec-26	22-Dec-26	10-Feb-27	14-Feb-27	597.56	0.00	0.00	0%	0%		Backf
DAM3-C-ENV-S-1334	Installation of base plate	2	23-Dec-26	28-Dec-26	15-Feb-27	16-Feb-27	1,195.12	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1324	Installation of steel members	2	29-Dec-26	05-Jan-27	17-Feb-27	18-Feb-27	2,390.24	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1294	Installation of steel fence	2	06-Jan-27	07-Jan-27	20-Feb-27	21-Feb-27	2,390.24	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1384	Installation of steel gates	2	09-Jan-27	10-Jan-27	23-Feb-27	24-Feb-27	2,343.91	0.00	0.00	0%	0%		Instal
ROAD WORKS		34	23-Nov-26	21-Feb-27	14-Jan-27	23-Feb-27	2,873,764.57	0.00	0.00	0%	0%		23-Fe
DAM3-C-ENV-R-1390	SubGrade Preparation & Compaction	5	23-Nov-26	03-Dec-26	14-Jan-27	19-Jan-27	319,796.23	0.00	0.00	0%	0%		SubG
DAM3-C-ENV-R-1400	Aggregate Base Course Layer	5	05-Dec-26	12-Dec-26	20-Jan-27	25-Jan-27	262,382.32	0.00	0.00	0%	0%		Aggre
DAM3-C-ENV-R-1460	Curb Stones	4	13-Dec-26	04-Jan-27	26-Jan-27	30-Jan-27	291,156.54	0.00	0.00	0%	0%		Curb
DAM3-C-ENV-R-1480	Interlock Tiles	3	05-Jan-27	27-Jan-27	31-Jan-27	02-Feb-27	475,633.54	0.00	0.00	0%	0%		Interl
DAM3-C-ENV-R-890	Supply and install geotextile sheet	2	28-Jan-27	30-Jan-27	03-Feb-27	04-Feb-27	47,639.01	0.00	0.00	0%	0%		Suppl
DAM3-C-ENV-R-1490	Gravel Bedding	2	31-Jan-27	01-Feb-27	06-Feb-27	07-Feb-27	57,375.45	0.00	0.00	0%	0%		Grave
DAM3-C-ENV-R-1500	Road Signs	3	02-Feb-27	07-Feb-27	08-Feb-27	10-Feb-27	103,945.80	0.00	0.00	0%	0%		Road
DAM3-C-ENV-R-1450	Prime Coat	1	08-Feb-27	08-Feb-27	11-Feb-27	11-Feb-27	71,708.03	0.00	0.00	0%	0%		Prime
DAM3-C-ENV-R-1410	Asphalt Concrete Base Course Layer	2	09-Feb-27	10-Feb-27	13-Feb-27	14-Feb-27	645,372.33	0.00	0.00	0%	0%		Asphal
DAM3-C-ENV-R-1470	Tack Coat	1	11-Feb-27	11-Feb-27	15-Feb-27	15-Feb-27	52,885.08	0.00	0.00	0%	0%		Tack
DAM3-C-ENV-R-1420	Asphalt Concrete Wearing Course Layer	2	13-Feb-27	14-Feb-27	16-Feb-27	17-Feb-27	475,965.66	0.00	0.00	0%	0%		Asphal
DAM3-C-ENV-R-1430	Retroreflective Thermoplastic White Traffic lines	2	15-Feb-27	16-Feb-27	18-Feb-27	20-Feb-27	37,884.84	0.00	0.00	0%	0%		Retro
DAM3-C-ENV-R-1440	Installation of Concrete wheel bumper	2	17-Feb-27	21-Feb-27	21-Feb-27	23-Feb-27	32,019.76	0.00	0.00	0%	0%		Instal
LANDSCAPING		12	02-Feb-27	15-Feb-27	08-Feb-27	21-Feb-27	164,099.55	0.00	0.00	0%	0%		21-Fe
DAM3-C-ENV-R-1510	Planting of trees	5	02-Feb-27	07-Feb-27	08-Feb-27	13-Feb-27	110,131.54	0.00	0.00	0%	0%		Plant
DAM3-C-ENV-R-1520	Planting of shrubs	7	08-Feb-27	15-Feb-27	14-Feb-27	21-Feb-27	53,968.01	0.00	0.00	0%	0%		Plant
TESTING AND COMMISSIONING (10%)		181	24-May-26	18-Feb-27	17-Jun-26 A	14-Feb-27	9,599,652.50	7,261,418.79	7,322,308.25	75.64%	76.28%		14-Fe
TESTING AND COMMISSIONING 900 Sq.m-2		175	24-May-26	18-Feb-27	28-Jun-26 A	14-Feb-27	1,943,587.85	63,346.56	66,035.08	3.26%	3.4%		14-Fe
MECHANICAL		174	24-May-26	17-Jan-27	28-Jun-26 A	13-Feb-27	617,124.79	63,346.56	66,035.08	10.26%	10.7%		13-Fe
P001-C-TC-M-3406	Testing & Commissioning of Sewer & Drainage Pipes	7	24-May-26	03-Jun-26	28-Jun-26 A	08-Oct-26 A	63,346.56	63,346.56	63,346.56	100%	100%		Testing &
P001-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	18-Nov-26	26-Nov-26	19-Oct-26 A	29-Nov-26	2,987.25	0.00	2,688.52	0%	90%		Testing

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
P001-C-TC-M-3426	Testing and Commissioning of Sanitary Fixtures	7	23-Nov-26	01-Dec-26	02-Dec-26	10-Dec-26	32,707.31	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3376	Testing and Commissioning of Fire Fighting Pipes	7	02-Dec-26	10-Dec-26	07-Jan-27	16-Jan-27	118,857.06	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3396	Testing & Commissioning of Water Supply Pipes	7	29-Nov-26	07-Dec-26	07-Jan-27	16-Jan-27	38,283.97	0.00	0.00	0%	0%		Testing
P001-C-TC-M3446	Testing and Commissioning of Exhaust Fan	7	26-Nov-26	05-Dec-26	10-Jan-27	18-Jan-27	13,737.46	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3456	Testing and Commissioning of Wall propeller type exhaust fans	7	01-Dec-26	09-Dec-26	14-Jan-27	23-Jan-27	76,887.76	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3436	Testing and Commissioning of HVAC Duct	7	03-Dec-26	12-Dec-26	17-Jan-27	25-Jan-27	245,430.24	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	10-Jan-27	17-Jan-27	09-Feb-27	13-Feb-27	24,887.19	0.00	0.00	0%	0%		Testing
ELECTRICAL		28	29-Nov-26	18-Feb-27	12-Jan-27	14-Feb-27	1,326,463.06	0.00	0.00	0%	0%		14-Fe
P001-C-TC-E-3506	Testing and Commissioning of Wiring Devices	7	29-Nov-26	07-Dec-26	12-Jan-27	20-Jan-27	33,207.17	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3496	Testing and Commissioning of Fire Alarm System	2	07-Dec-26	08-Dec-26	21-Jan-27	24-Jan-27	139,733.70	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3466	Testing and Commissioning of Disconnect Switches	7	30-Dec-26	06-Jan-27	25-Jan-27	02-Feb-27	50,288.02	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3556	Testing and Commissioning of Solar power plant	2	17-Feb-27	18-Feb-27	28-Jan-27	31-Jan-27	415,814.30	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3546	Testing and Commissioning of Access Control System	2	17-Dec-26	19-Dec-26	30-Jan-27	01-Feb-27	45,341.12	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3486	Testing and Commissioning of Grounding	2	26-Dec-26	27-Dec-26	31-Jan-27	02-Feb-27	32,570.63	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3456	Testing and Commissioning of Main Distribution Board	3	23-Dec-26	30-Dec-26	01-Feb-27	04-Feb-27	53,313.44	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3446	Testing and Commissioning of LV cables	2	26-Dec-26	27-Dec-26	03-Feb-27	06-Feb-27	149,517.23	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3526	Testing and Commissioning of PP-AC panel	2	26-Dec-26	30-Dec-26	03-Feb-27	06-Feb-27	35,542.28	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3516	Testing and Commissioning of LP panel board	2	31-Dec-26	02-Jan-27	04-Feb-27	07-Feb-27	30,214.76	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3566	Testing and Commissioning of CCTV System	2	29-Dec-26	30-Dec-26	04-Feb-27	07-Feb-27	125,349.49	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3536	Testing and Commissioning of Telephone and data system	2	28-Dec-26	02-Jan-27	06-Feb-27	08-Feb-27	44,313.72	0.00	0.00	0%	0%		Testing
P001-C-TC-E-3476	Testing and Commissioning of Lighting Fixtures	1	18-Jan-27	18-Jan-27	13-Feb-27	14-Feb-27	171,257.21	0.00	0.00	0%	0%		Testing
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		85	06-Oct-26	06-Feb-27	13-Oct-26 A	10-Feb-27	530,478.84	72,486.43	130,687.36	13.66%	24.64%		10-Fe
PUMP ROOM SHED		19	12-Dec-26	06-Feb-27	02-Dec-26	24-Dec-26	306,247.54	0.00	0.00	0%	0%		24-Dec
S001-C-TC-M-3576	Testing & Commissioning of Fire Fighting pump	5	05-Jan-27	10-Jan-27	02-Dec-26	08-Dec-26	51,684.47	0.00	0.00	0%	0%		Testing
S001-C-TC-M-3586	Testing & Commissioning of Booster pump	7	31-Dec-26	07-Jan-27	02-Dec-26	10-Dec-26	6,462.23	0.00	0.00	0%	0%		Testing
S001-C-TC-M-3596	Testing & Commissioning of GRP tank	3	12-Dec-26	14-Dec-26	02-Dec-26	06-Dec-26	104,926.55	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3616	Testing and Commissioning of Panel Board	2	07-Jan-27	09-Jan-27	05-Dec-26	07-Dec-26	36,675.69	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3636	Testing and Commissioning of Grounding	5	09-Jan-27	13-Jan-27	08-Dec-26	14-Dec-26	208.86	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3646	Testing and Commissioning of Wiring devices	2	13-Jan-27	14-Jan-27	10-Dec-26	13-Dec-26	193.73	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3621	Testing and Commissioning of LV cables	3	19-Jan-27	24-Jan-27	16-Dec-26	20-Dec-26	76,378.12	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3626	Testing and Commissioning of Lighting Fixtures	2	18-Jan-27	19-Jan-27	17-Dec-26	20-Dec-26	1,429.61	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3656	Testing and Commissioning of Programmable Logic Controller	2	26-Jan-27	06-Feb-27	22-Dec-26	24-Dec-26	28,288.27	0.00	0.00	0%	0%		Testing
EXTERNAL		26	18-Nov-26	09-Dec-26	12-Jan-27	10-Feb-27	52,779.67	0.00	0.00	0%	0%		10-Fe
S001-C-TC-EX-E-3646	Testing and Commissioning of Street Lighting pole	15	22-Nov-26	08-Dec-26	12-Jan-27	28-Jan-27	35,084.37	0.00	0.00	0%	0%		Testing
S001-C-TC-EX-E-3626	Testing and Commissioning of LV cables	7	18-Nov-26	25-Nov-26	20-Jan-27	27-Jan-27	14,763.42	0.00	0.00	0%	0%		Testing
S001-C-TC-EX-E-3656	Testing and Commissioning of Grounding	7	02-Dec-26	09-Dec-26	03-Feb-27	10-Feb-27	2,931.87	0.00	0.00	0%	0%		Testing
ENVIRONMENTAL		85	06-Oct-26	19-Jan-27	13-Oct-26 A	09-Feb-27	171,451.64	72,486.43	130,687.36	42.28%	76.22%		09-Fe
S001-C-TC-ENV-F-1051	Testing & Commissioning of External Fire Fighting System 200 Dia	15	06-Oct-26	22-Oct-26	13-Oct-26 A	23-Nov-26	72,486.43	72,486.43	65,237.78	100%	90%		Testing
S001-C-TC-ENV-SW-60	Testing & Commissioning of Sewer & Drainage System	3	03-Jan-27	19-Jan-27	13-Oct-26 A	09-Feb-27	67,394.23	0.00	60,654.81	0%	90%		Testing
S001-C-TC-ENV-WS-11	Testing & Commissioning of Water Supply System	15	22-Nov-26	08-Dec-26	19-Oct-26 A	08-Dec-26	5,327.52	0.00	4,794.77	0%	90%		Testing
S001-C-TC-ENV-SW-70	Testing & Commissioning of Irrigaiton System	15	15-Dec-26	31-Dec-26	19-Jan-27	06-Feb-27	11,300.41	0.00	0.00	0%	0%		Testing
S001-C-TC-ENV-3666	Testing and Commissioning of Main program system & controller	10	23-Dec-26	09-Jan-27	30-Jan-27	09-Feb-27	14,943.05	0.00	0.00	0%	0%		Testing
SNAGG WORKS		79	10-Jun-26	16-Jul-26	17-Jun-26 A	26-Jul-26 A	7,125,585.81	7,125,585.81	7,125,585.81	100%	100%		26-Jul-26 A
S001-C-TC-C-80	Civil & Architectural Snagg works-1	5	05-Jul-26	11-Jul-26	17-Jun-26 A	20-Jun-26 A	1,520,575.29	1,520,575.29	1,520,575.29	100%	100%		Civil & Archite
S001-C-TC-A-90	Civil & Architectural Snagg works-2	5	11-Jul-26	16-Jul-26	21-Jun-26 A	22-Jun-26 A	1,000,000.00	1,000,000.00	1,000,000.00	100%	100%		Civil & Archite
S001-C-TC-E-3676	External Snagg works	5	02-Jul-26	07-Jul-26	22-Jun-26 A	05-Jul-26 A	3,231,301.32	3,231,301.32	3,231,301.32	100%	100%		External Sna
S001-C-TC-M-100	Mechanical Snagg works	5	10-Jun-26	15-Jun-26	05-Jul-26 A	06-Jul-26 A	1,206,604.05	1,206,604.05	1,206,604.05	100%	100%		Mechanical
S001-C-TC-E-3606	Electrical Snagg works	5	08-Jul-26	13-Jul-26	05-Jul-26 A	26-Jul-26 A	167,105.15	167,105.15	167,105.15	100%	100%		Electrical Sn
PREOJECT CLOSEOUT		20	02-Feb-27	06-Mar-27	08-Feb-27	03-Mar-27	0.00	0.00	0.00	0%	0%		03-M

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
ENGINEERING		8	02-Feb-27	10-Feb-27	08-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
AS BUILT DRAWINGS		6	02-Feb-27	08-Feb-27	08-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
CIVIL DRAWINGS		2	02-Feb-27	03-Feb-27	08-Feb-27	09-Feb-27	0.00	0.00	0.00	0%	0%		09-Fe
PREPARATION AND SUBMITTALS		2	02-Feb-27	03-Feb-27	08-Feb-27	09-Feb-27	0.00	0.00	0.00	0%	0%		09-Fe
DAM3-AB-1010	Civil drawings	2	02-Feb-27	03-Feb-27	08-Feb-27	09-Feb-27	0.00	0.00	0.00	0%	0%		Civil d
REVIEW AND APPROVALS		2	02-Feb-27	03-Feb-27	08-Feb-27	09-Feb-27	0.00	0.00	0.00	0%	0%		09-Fe
DAM3-AB-1053	Civil drawings	2	02-Feb-27	03-Feb-27	08-Feb-27	09-Feb-27	0.00	0.00	0.00	0%	0%		Civil d
ARCHITECTURAL DRAWINGS		4	04-Feb-27	08-Feb-27	10-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1011	Architectural drawings	2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Archi
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1023	Architectural drawings	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Archi
MECHANICAL DRAWINGS		4	04-Feb-27	08-Feb-27	10-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1013	Mechanical drawings	2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Mech
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1033	Mechanical drawings	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Mech
ELECTRICAL DRAWINGS		4	04-Feb-27	08-Feb-27	10-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1012	Electrical drawings	2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Electr
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1043	Electrical drawings	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Electr
EXTERNAL WORKS DRAWINGS		4	04-Feb-27	08-Feb-27	10-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1054	External works drawings	2	04-Feb-27	06-Feb-27	10-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Exter
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1055	External works drawings	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Exter
WARRANTIES AND GUARANTEES		4	07-Feb-27	10-Feb-27	13-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
SYSTEM		4	07-Feb-27	10-Feb-27	13-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
PREPARATION AND SUBMITTALS		2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-WG-1010	Warraties and Guarantees For Mechanical Equipments	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Warra
DAM3-WG-1011	Warraties and Guarantees For Electrical Systems	2	07-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Warra
REVIEW AND APPROVAL		2	09-Feb-27	10-Feb-27	15-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-WG-1012	Warraties and Guarantees For Mechanical Equipments	2	09-Feb-27	10-Feb-27	15-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Warra
DAM3-WG-1013	Warraties and Guarantees For Electrical Systems	2	09-Feb-27	10-Feb-27	15-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Warra
TRAINING AND MANUALS		10	11-Feb-27	23-Feb-27	17-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		01-M
TRAINING		6	11-Feb-27	17-Feb-27	17-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		24-Fe
SYSTEM		6	11-Feb-27	17-Feb-27	17-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		24-Fe
PREPARATION AND SUBMITTALS		2	11-Feb-27	13-Feb-27	17-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		18-Fe
DAM3-WG-1014	The Proposed Coursework For Mechanical Equipment	2	11-Feb-27	13-Feb-27	17-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1015	The Proposed Coursework For Electircal systems	2	11-Feb-27	13-Feb-27	17-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		The P
REVIEW AND APPROVAL		2	14-Feb-27	15-Feb-27	20-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		21-Fe
DAM3-WG-1016	The Proposed Coursework For Mechanical Equipment	2	14-Feb-27	15-Feb-27	20-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1017	The Proposed Coursework For Electircal systems	2	14-Feb-27	15-Feb-27	20-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		The P
DELIVERY		2	16-Feb-27	17-Feb-27	23-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		24-Fe
DAM3-WG-1018	The Proposed Coursework For Mechanical Equipment	2	16-Feb-27	17-Feb-27	23-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1019	The Proposed Coursework For Electircal systems	2	16-Feb-27	17-Feb-27	23-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		The P
MANUALS		4	18-Feb-27	23-Feb-27	25-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		01-M
SYSTEM		4	18-Feb-27	23-Feb-27	25-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		01-M

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
PREPARATION AND SUBMITTALS		2	18-Feb-27	20-Feb-27	25-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		▼ 27-F
DAM3-WG-1020	Manual and Catalogue For Mechanical Equipment	2	18-Feb-27	20-Feb-27	25-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		Man
DAM3-WG-1021	Manual and Catalogue For For Electircal systems	2	18-Feb-27	20-Feb-27	25-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		Man
REVIEW AND APPROVAL		2	21-Feb-27	23-Feb-27	28-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		▼ 01-M
DAM3-WG-1022	Manual and Catalogue For Mechanical Equipment	2	21-Feb-27	23-Feb-27	28-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		Man
DAM3-WG-1023	Manual and Catalogue For For Electircal systems	2	21-Feb-27	23-Feb-27	28-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		Man
DEMOBILIZATION		13	09-Feb-27	24-Feb-27	15-Feb-27	02-Mar-27	0.00	0.00	0.00	0%	0%		▼ 02-M
DAM3-D.MOB-1013	Demobilization of manpower	2	09-Feb-27	10-Feb-27	15-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Dem
DAM3-D.MOB-1020	Demobilization of equipment	2	11-Feb-27	13-Feb-27	17-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		Dem
DAM3-D.MOB-1010	Dismantling and removal offices	1	24-Feb-27	24-Feb-27	02-Mar-27	02-Mar-27	0.00	0.00	0.00	0%	0%		Dism
FINAL HANDOVER		6	23-Feb-27	06-Mar-27	25-Feb-27	03-Mar-27	0.00	0.00	0.00	0%	0%		▼ 03-M
DAM3-FH-1000	Snag List Rectification	3	23-Feb-27	03-Mar-27	25-Feb-27	28-Feb-27	0.00	0.00	0.00	0%	0%		Snag
DAM3-FH-1010	Handover Letter	1	04-Mar-27	04-Mar-27	01-Mar-27	01-Mar-27	0.00	0.00	0.00	0%	0%		Hand
DAM3-FH-1020	Intial Handingover	1	06-Mar-27	06-Mar-27	03-Mar-27	03-Mar-27	0.00	0.00	0.00	0%	0%		Intial

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
27-Oct-26	Weekly Report		
