
Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
DEVELOPMENT OF SUDAIR INDUSTRIAL CITY PHASE 2 - Update 28/09/2026.		245	07-Jul-26	26-May-27	18-May-26 A	02-Nov-26	27.76%	28.37%
Construction		245	07-Jul-26	26-May-27	18-May-26	02-Nov-26	27.76%	28.37%
ROAD WORKS		119	03-Aug-26	26-Dec-26	18-May-26	01-Nov-26	38.49%	19.08%
ZONE A		95	26-Aug-26	26-Dec-26	01-Jun-26 A	01-Nov-26	30.55%	13.61%
ROAD WORKS IN (PH2-COL-MC10)		31	09-Sep-26	18-Oct-26	31-Aug-26	15-Oct-26	57.84%	64.48%
Base Course		21	09-Sep-26	04-Oct-26	31-Aug-26	01-Oct-26	71.77%	80%
SDR-2-CON-RW-ZA-1070	Aggregate base course layer	21	09-Sep-26	04-Oct-26	31-Aug-26	01-Oct-26	71.43%	80%
Demolition Work		12	05-Oct-26	18-Oct-26	01-Oct-26	15-Oct-26	0%	0%
SDR-2-CON-RW-ZA-1080	Milling of wearing course	12	05-Oct-26	18-Oct-26	01-Oct-26	15-Oct-26	0%	0%
ROAD WORKS IN (PH2-COL-MC20)		19	01-Oct-26	22-Oct-26	26-Sep-26	19-Oct-26	0%	20%
Base Course		19	01-Oct-26	22-Oct-26	26-Sep-26	19-Oct-26	0%	20%
SDR-2-CON-RW-ZA-1210	Aggregate base course layer	19	01-Oct-26	22-Oct-26	26-Sep-26	19-Oct-26	0%	20%
ROAD WORKS IN (PH2-A-MCI0)		26	26-Aug-26	10-Oct-26	28-Sep-26	27-Oct-26	96.72%	0%
Subgrade		20	26-Aug-26	17-Sep-26	28-Sep-26	20-Oct-26	100%	0%
SDR-2-CON-RW-ZA-1320	Subgrade layer works	20	26-Aug-26	17-Sep-26	28-Sep-26	20-Oct-26	100%	0%
Kerbstone Installation		18	19-Sep-26	10-Oct-26	07-Oct-26	27-Oct-26	38.89%	0%
SDR-2-CON-RW-ZA-3420	Kerbstone Installation "all Types" Part 1	18	19-Sep-26	10-Oct-26	07-Oct-26	27-Oct-26	38.89%	0%
ROAD WORKS IN (PH2-A-MCA0)		84	31-Aug-26	07-Dec-26	22-Jun-26 A	26-Oct-26	80.92%	19.71%
Subgrade		21	31-Aug-26	24-Sep-26	01-Sep-26	01-Oct-26	100%	25%
SDR-2-CON-RW-ZA-1460	Subgrade layer works	21	31-Aug-26	24-Sep-26	01-Sep-26	01-Oct-26	100%	25%
Earth Works Plot		57	26-Sep-26	07-Dec-26	22-Jun-26 A	26-Oct-26	6.43%	0%
SDR-2-CON-RW-ZA-1480	Embankments to the Plot 2 Layer	21	14-Nov-26	07-Dec-26	22-Jun-26 A	28-Sep-26	0%	0%
SDR-2-CON-RW-ZA-1470	Plot Excavation for cuttings (all types of soil)	21	26-Sep-26	19-Oct-26	03-Oct-26	26-Oct-26	9.52%	0%
Base Course		15	26-Sep-26	12-Oct-26	03-Oct-26	19-Oct-26	13.33%	0%
SDR-2-CON-RW-ZA-1490	Aggregate base course layer	15	26-Sep-26	12-Oct-26	03-Oct-26	19-Oct-26	13.33%	0%
Kerbstone Installation		21	26-Sep-26	19-Oct-26	03-Oct-26	26-Oct-26	9.52%	0%
SDR-2-CON-RW-ZA-3440	Kerbstone Installation "all Types" Part 1	21	26-Sep-26	19-Oct-26	03-Oct-26	26-Oct-26	9.52%	0%
ROAD WORKS IN (PH2-A-MCB0)		81	07-Sep-26	10-Dec-26	08-Jun-26 A	21-Oct-26	79.74%	25.07%
Subgrade		16	07-Sep-26	26-Sep-26	01-Sep-26	28-Sep-26	100%	25%
SDR-2-CON-RW-ZA-1600	Subgrade layer works	16	07-Sep-26	26-Sep-26	01-Sep-26	28-Sep-26	100%	25%
Earth Works Plot		65	27-Sep-26	10-Dec-26	08-Jun-26 A	28-Sep-26	3.21%	57.36%
SDR-2-CON-RW-ZA-1620	Embankments to the Plot 2 Layer	21	17-Nov-26	10-Dec-26	30-Jun-26 A	28-Sep-26	0%	0%
SDR-2-CON-RW-ZA-1610	Plot Excavation for cuttings (all types of soil)	21	27-Sep-26	20-Oct-26	08-Jun-26 A	28-Sep-26	4.76%	85%
Base Course		20	27-Sep-26	19-Oct-26	29-Sep-26	21-Oct-26	5%	0%
SDR-2-CON-RW-ZA-1630	Aggregate base course layer	20	27-Sep-26	19-Oct-26	29-Sep-26	21-Oct-26	5%	0%
Kerbstone Installation		20	27-Sep-26	19-Oct-26	29-Sep-26	21-Oct-26	5%	0%
SDR-2-CON-RW-ZA-3430	Kerbstone Installation "all Types" Part 1	20	27-Sep-26	19-Oct-26	29-Sep-26	21-Oct-26	5%	0%
ROAD WORKS IN (PH2-A-MCC0)		25	03-Oct-26	29-Oct-26	31-Aug-26	18-Oct-26	0%	42.97%
Base Course		21	03-Oct-26	26-Oct-26	31-Aug-26	30-Sep-26	0%	65%
SDR-2-CON-RW-ZA-1770	Aggregate base course layer	21	03-Oct-26	26-Oct-26	31-Aug-26	30-Sep-26	0%	65%
Demolition Work		3	27-Oct-26	29-Oct-26	01-Oct-26	04-Oct-26	0%	0%
SDR-2-CON-RW-ZA-1780	Milling of wearing course	3	27-Oct-26	29-Oct-26	01-Oct-26	04-Oct-26	0%	0%
Kerbstone Installation		18	03-Oct-26	22-Oct-26	28-Sep-26	18-Oct-26	0%	0%
SDR-2-CON-RW-ZA-3450	Kerbstone Installation "all Types" Part 1	18	03-Oct-26	22-Oct-26	28-Sep-26	18-Oct-26	0%	0%
ROAD WORKS IN (PH2-A-MCD0)		72	07-Oct-26	20-Dec-26	15-Jun-26 A	18-Oct-26	0%	33.02%
Earth Works Plot		64	07-Oct-26	20-Dec-26	15-Jun-26 A	28-Sep-26	0%	30%

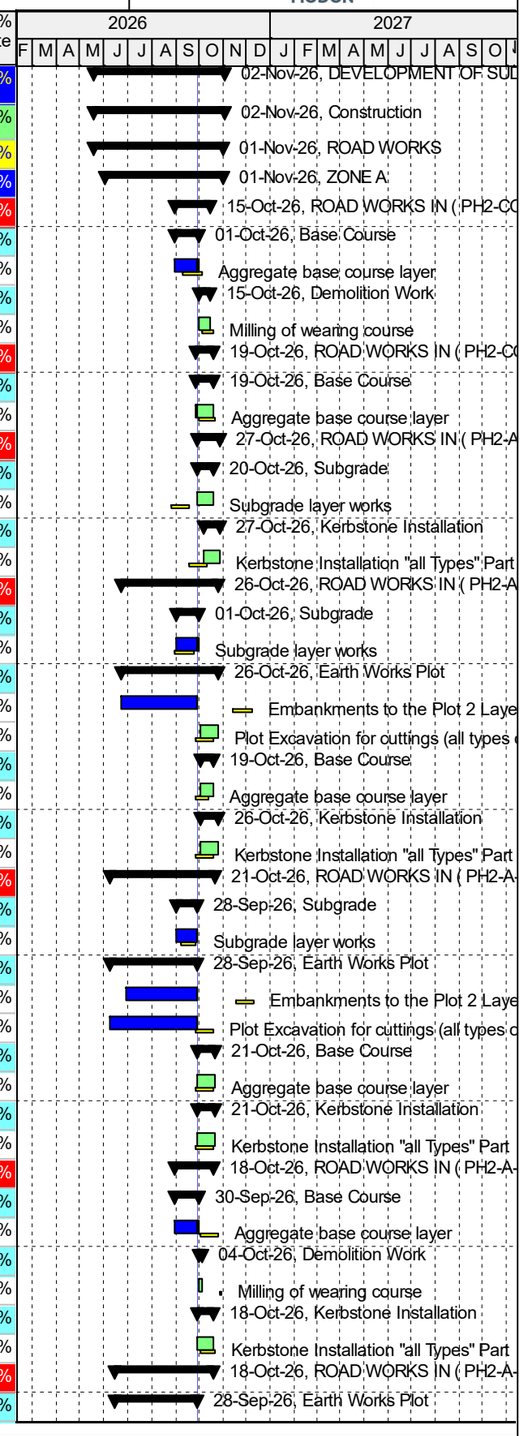

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-RW-ZA-1900	Embankments to the Plot 2 Layer	21	26-Nov-26	20-Dec-26	23-Jun-26 A	28-Sep-26	0%	30%
SDR-2-CON-RW-ZA-1890	Plot Excavation for cuttings (all types of soil)	21	07-Oct-26	31-Oct-26	15-Jun-26 A	28-Sep-26	0%	30%
Base Course		20	07-Oct-26	29-Oct-26	30-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-RW-ZA-1910	Aggregate base course layer	20	07-Oct-26	29-Oct-26	30-Aug-26	28-Sep-26	0%	60%
Kerbstone Installation		18	07-Oct-26	27-Oct-26	28-Sep-26	18-Oct-26	0%	0%
SDR-2-CON-RW-ZA-3460	Kerbstone Installation "all Types" Part 1	18	07-Oct-26	27-Oct-26	28-Sep-26	18-Oct-26	0%	0%
ROAD WORKS IN (PH2-A-MCE0)		20	15-Sep-26	08-Oct-26	28-Sep-26	20-Oct-26	50%	0%
Subgrade		20	15-Sep-26	08-Oct-26	28-Sep-26	20-Oct-26	50%	0%
SDR-2-CON-RW-ZA-2020	Subgrade layer works	20	15-Sep-26	08-Oct-26	28-Sep-26	20-Oct-26	50%	0%
ROAD WORKS IN (PH2-A-MCF0)		20	29-Sep-26	21-Oct-26	28-Sep-26	20-Oct-26	0%	0%
Subgrade		20	29-Sep-26	21-Oct-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2160	Subgrade layer works	20	29-Sep-26	21-Oct-26	28-Sep-26	20-Oct-26	0%	0%
ROAD WORKS IN (PH2-A-MCG0)		18	04-Oct-26	24-Oct-26	28-Sep-26	18-Oct-26	0%	0%
Subgrade		18	04-Oct-26	24-Oct-26	28-Sep-26	18-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2300	Subgrade layer works	18	04-Oct-26	24-Oct-26	28-Sep-26	18-Oct-26	0%	0%
ROAD WORKS IN (PH2-A-MCH0)		56	05-Oct-26	26-Dec-26	01-Jun-26 A	27-Oct-26	0%	2.51%
Subgrade		8	05-Oct-26	13-Oct-26	28-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2440	Subgrade layer works	8	05-Oct-26	13-Oct-26	28-Sep-26	06-Oct-26	0%	0%
Earth Works Plot		55	08-Nov-26	26-Dec-26	01-Jun-26 A	22-Oct-26	0%	40%
SDR-2-CON-RW-ZA-3310	Embankments to the Plot 1 Layer	21	08-Nov-26	01-Dec-26	01-Jun-26 A	28-Sep-26	0%	80%
SDR-2-CON-RW-ZA-2460	Embankments to the Plot 2 Layer	21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Base Course		15	14-Oct-26	31-Oct-26	07-Oct-26	24-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2470	Aggregate base course layer	15	14-Oct-26	31-Oct-26	07-Oct-26	24-Oct-26	0%	0%
Kerbstone Installation		18	14-Oct-26	03-Nov-26	07-Oct-26	27-Oct-26	0%	0%
SDR-2-CON-RW-ZA-3500	Kerbstone Installation "all Types" Part 1	18	14-Oct-26	03-Nov-26	07-Oct-26	27-Oct-26	0%	0%
ROAD WORKS IN (PH2-ART-MC00)		30	20-Oct-26	17-Nov-26	31-Aug-26	18-Oct-26	0%	15.14%
Base Course		11	20-Oct-26	01-Nov-26	31-Aug-26	28-Sep-26	0%	86%
SDR-2-CON-RW-ZA-2610	Aggregate base course layer	11	20-Oct-26	01-Nov-26	31-Aug-26	28-Sep-26	0%	86%
Demolition Work		2	02-Nov-26	03-Nov-26	29-Sep-26	30-Sep-26	0%	0%
SDR-2-CON-RW-ZA-2620	Milling of wearing course	2	02-Nov-26	03-Nov-26	29-Sep-26	30-Sep-26	0%	0%
Asphalt Works		12	04-Nov-26	17-Nov-26	01-Oct-26	14-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2630	Asphalt works 1st Layer with MC-01	12	04-Nov-26	17-Nov-26	01-Oct-26	14-Oct-26	0%	0%
Kerbstone Installation		18	20-Oct-26	09-Nov-26	28-Sep-26	18-Oct-26	0%	0%
SDR-2-CON-RW-ZA-3510	Kerbstone Installation "all Types" Part 1	18	20-Oct-26	09-Nov-26	28-Sep-26	18-Oct-26	0%	0%
ROAD WORKS IN (PH2-ART-MC10)		30	05-Oct-26	08-Nov-26	24-Sep-26	01-Nov-26	0%	21.74%
Subgrade		12	05-Oct-26	18-Oct-26	24-Sep-26	11-Oct-26	0%	25%
SDR-2-CON-RW-ZA-2720	Subgrade layer works	12	05-Oct-26	18-Oct-26	24-Sep-26	11-Oct-26	0%	25%
Base Course		11	19-Oct-26	31-Oct-26	12-Oct-26	24-Oct-26	0%	0%
SDR-2-CON-RW-ZA-2750	Aggregate base course layer	11	19-Oct-26	31-Oct-26	12-Oct-26	24-Oct-26	0%	0%
Kerbstone Installation		18	19-Oct-26	08-Nov-26	12-Oct-26	01-Nov-26	0%	0%
SDR-2-CON-RW-ZA-3520	Kerbstone Installation "all Types" Part 1	18	19-Oct-26	08-Nov-26	12-Oct-26	01-Nov-26	0%	0%
ZONE G		99	03-Aug-26	30-Nov-26	18-May-26	01-Nov-26	64.23%	36.78%
ROAD WORKS IN (PH2-COL-MC50)		68	03-Aug-26	14-Oct-26	23-Jun-26 A	21-Oct-26	94.14%	70.42%
Subgrade		21	03-Aug-26	26-Aug-26	16-Jul-26 A	28-Sep-26	100%	80%
SDR-2-CON-RW-ZG-1040	Subgrade layer works	21	03-Aug-26	26-Aug-26	16-Jul-26 A	28-Sep-26	100%	80%
Earth Works Plot		21	27-Aug-26	20-Sep-26	23-Jun-26 A	28-Sep-26	100%	80%
SDR-2-CON-RW-ZG-1050	Plot Excavation for cuttings (all types of soil)	21	27-Aug-26	20-Sep-26	23-Jun-26 A	28-Sep-26	100%	80%

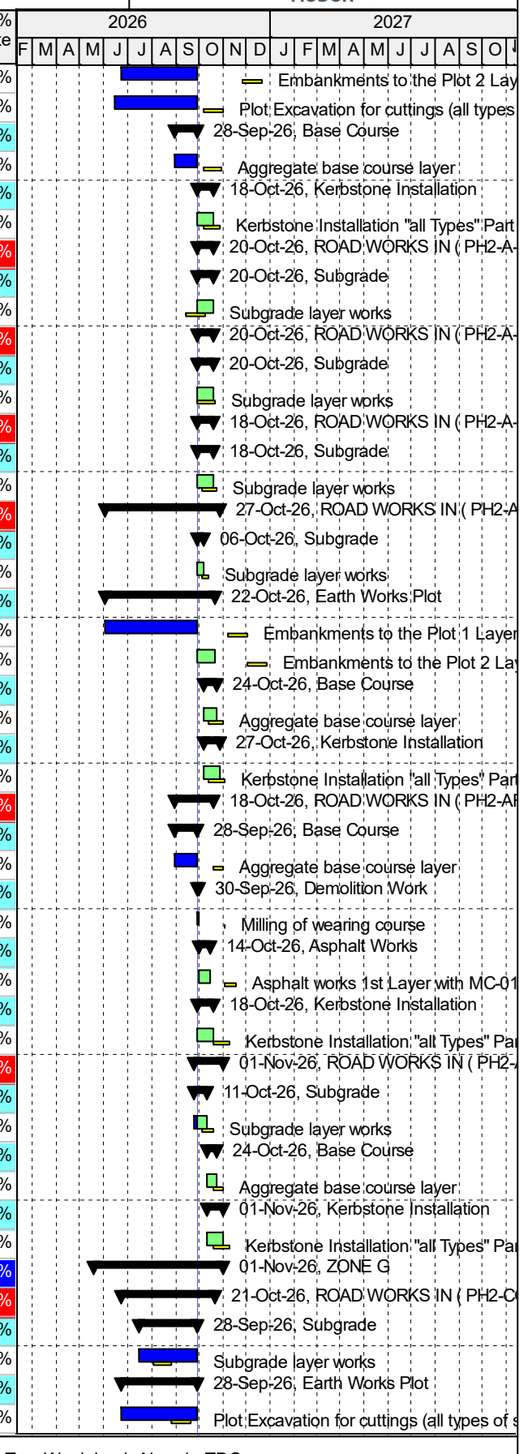

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Base Course		21	27-Aug-26	20-Sep-26	20-Aug-26	28-Sep-26	100%	50%
SDR-2-CON-RW-ZG-1070	Aggregate base course layer	21	27-Aug-26	20-Sep-26	20-Aug-26	28-Sep-26	100%	50%
Demolition Work		20	21-Sep-26	14-Oct-26	29-Sep-26	21-Oct-26	1.21%	0%
SDR-2-CON-RW-ZG-1090	Milling of wearing course	9	05-Oct-26	14-Oct-26	12-Oct-26	21-Oct-26	0%	0%
SDR-2-CON-RW-ZG-1080	Removal of curbstone	11	21-Sep-26	04-Oct-26	29-Sep-26	11-Oct-26	45.45%	0%
Kerbstone Installation		18	21-Sep-26	12-Oct-26	29-Sep-26	19-Oct-26	27.78%	0%
SDR-2-CON-RW-ZG-2550	Kerbstone Installation "all Types" Part 1	18	21-Sep-26	12-Oct-26	29-Sep-26	19-Oct-26	27.78%	0%
ROAD WORKS IN (PH2-ART-MC00)		52	23-Aug-26	11-Oct-26	20-Aug-26	22-Oct-26	85.7%	52.89%
Base Course		21	23-Aug-26	15-Sep-26	20-Aug-26	28-Sep-26	100%	80%
SDR-2-CON-RW-ZG-1220	Aggregate base course layer	21	23-Aug-26	15-Sep-26	20-Aug-26	28-Sep-26	100%	80%
Demolition Work		21	16-Sep-26	11-Oct-26	29-Sep-26	22-Oct-26	10.16%	0%
SDR-2-CON-RW-ZG-1240	Milling of wearing course	13	27-Sep-26	11-Oct-26	08-Oct-26	22-Oct-26	7.69%	0%
SDR-2-CON-RW-ZG-1230	Removal of curbstone	8	16-Sep-26	26-Sep-26	29-Sep-26	07-Oct-26	100%	0%
Kerbstone Installation		18	23-Aug-26	12-Sep-26	28-Sep-26	18-Oct-26	100%	0%
SDR-2-CON-RW-ZG-2560	Kerbstone Installation "all Types" Part 1	18	23-Aug-26	12-Sep-26	28-Sep-26	18-Oct-26	100%	0%
ROAD WORKS IN (PH2-G-MCA0)		30	27-Oct-26	30-Nov-26	28-Sep-26	01-Nov-26	0%	0%
Demolition Work		16	27-Oct-26	14-Nov-26	28-Sep-26	15-Oct-26	0%	0%
SDR-2-CON-RW-ZG-1390	Milling of wearing course	7	07-Nov-26	14-Nov-26	08-Oct-26	15-Oct-26	0%	0%
SDR-2-CON-RW-ZG-1380	Removal of curbstone	9	27-Oct-26	05-Nov-26	28-Sep-26	07-Oct-26	0%	0%
Asphalt Works		30	27-Oct-26	30-Nov-26	28-Sep-26	01-Nov-26	0%	0%
SDR-2-CON-RW-ZG-1410	Asphalt works 2nd layer with RC-02	18	10-Nov-26	30-Nov-26	12-Oct-26	01-Nov-26	0%	0%
SDR-2-CON-RW-ZG-1400	Asphalt works 1st Layer with MC-01	12	27-Oct-26	09-Nov-26	28-Sep-26	11-Oct-26	0%	0%
ROAD WORKS IN (PH2-G-MCE0)		18	19-Sep-26	14-Oct-26	28-Sep-26	18-Oct-26	37.99%	0%
Demolition Work		4	11-Oct-26	14-Oct-26	28-Sep-26	01-Oct-26	0%	0%
SDR-2-CON-RW-ZG-1530	Removal of curbstone	4	11-Oct-26	14-Oct-26	28-Sep-26	01-Oct-26	0%	0%
Kerbstone Installation		18	19-Sep-26	10-Oct-26	28-Sep-26	18-Oct-26	38.89%	0%
SDR-2-CON-RW-ZG-2580	Kerbstone Installation "all Types" Part 1	18	19-Sep-26	10-Oct-26	28-Sep-26	18-Oct-26	38.89%	0%
ROAD WORKS IN (PH2-G-MCD0)		62	20-Aug-26	08-Oct-26	18-May-26	01-Nov-26	91.94%	39.89%
Subgrade		21	20-Aug-26	13-Sep-26	10-Sep-26	11-Oct-26	100%	45%
SDR-2-CON-RW-ZG-1640	Subgrade layer works	21	20-Aug-26	13-Sep-26	10-Sep-26	11-Oct-26	100%	45%
Earth Works Plot		21	14-Sep-26	08-Oct-26	18-May-26	11-Oct-26	52.38%	60%
SDR-2-CON-RW-ZG-1650	Plot Excavation for cuttings (all types of soil)	21	14-Sep-26	08-Oct-26	18-May-26	11-Oct-26	52.38%	60%
Base Course		16	14-Sep-26	03-Oct-26	12-Oct-26	29-Oct-26	68.75%	0%
SDR-2-CON-RW-ZG-1670	Aggregate base course layer	16	14-Sep-26	03-Oct-26	12-Oct-26	29-Oct-26	68.75%	0%
Kerbstone Installation		18	14-Sep-26	05-Oct-26	12-Oct-26	01-Nov-26	61.11%	0%
SDR-2-CON-RW-ZG-2590	Kerbstone Installation "all Types" Part 1	18	14-Sep-26	05-Oct-26	12-Oct-26	01-Nov-26	61.11%	0%
ROAD WORKS IN (PH2-G-MCF0)		18	05-Sep-26	07-Oct-26	28-Sep-26	18-Oct-26	97.69%	0%
Demolition Work		7	30-Sep-26	07-Oct-26	28-Sep-26	05-Oct-26	0%	0%
SDR-2-CON-RW-ZG-1830	Removal of curbstone	7	30-Sep-26	07-Oct-26	28-Sep-26	05-Oct-26	0%	0%
Kerbstone Installation		18	05-Sep-26	26-Sep-26	28-Sep-26	18-Oct-26	100%	0%
SDR-2-CON-RW-ZG-2600	Kerbstone Installation "all Types" Part 1	18	05-Sep-26	26-Sep-26	28-Sep-26	18-Oct-26	100%	0%
ROAD WORKS IN (PH2-G-MCG0)		63	14-Sep-26	26-Nov-26	18-May-26	18-Oct-26	32.38%	25.38%
Earth Works Plot		63	14-Sep-26	26-Nov-26	18-May-26	29-Sep-26	26.68%	30.67%
SDR-2-CON-RW-ZG-2500	Embankments to the Plot 1 Layer	21	10-Oct-26	02-Nov-26	11-Jun-26 A	28-Sep-26	0%	80%
SDR-2-CON-RW-ZG-1960	Embankments to the Plot 2 Layer	21	03-Nov-26	26-Nov-26	22-Jun-26 A	29-Sep-26	0%	45%
SDR-2-CON-RW-ZG-1950	Plot Excavation for cuttings (all types of soil)	21	14-Sep-26	08-Oct-26	18-May-26	28-Sep-26	52.38%	0%
Demolition Work		8	10-Oct-26	18-Oct-26	28-Sep-26	06-Oct-26	0%	0%

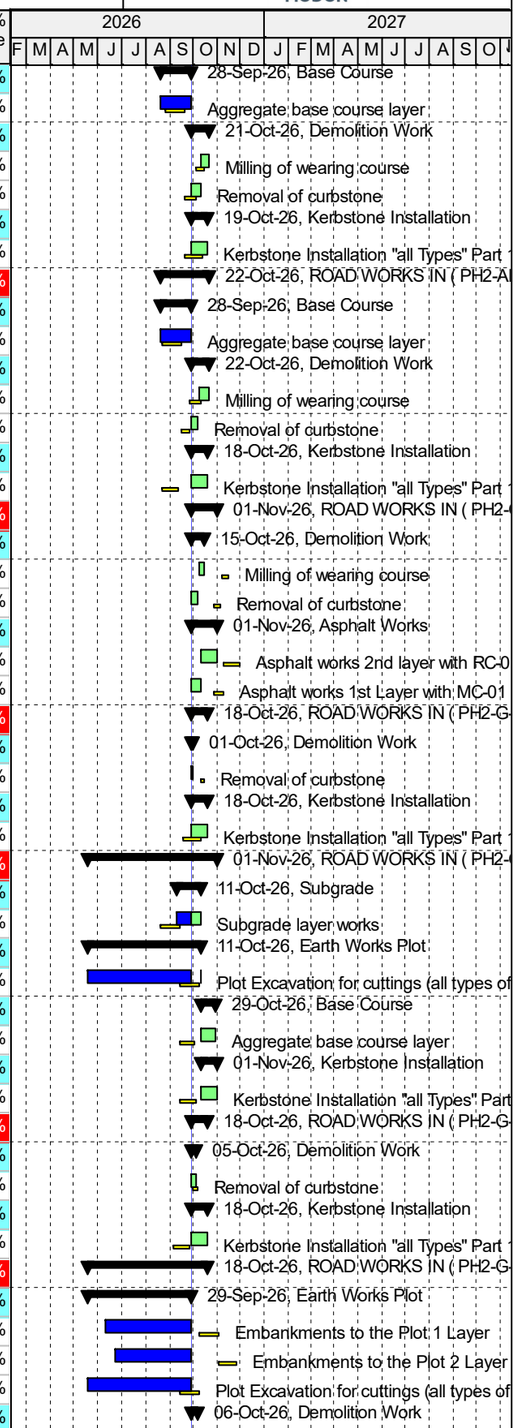

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-RW-ZG-1980	Removal of curbstone	8	10-Oct-26	18-Oct-26	28-Sep-26	06-Oct-26	0%	0%
Kerbstone Installation		18	14-Sep-26	05-Oct-26	28-Sep-26	18-Oct-26	61.11%	0%
SDR-2-CON-RW-ZG-2610	Kerbstone Installation "all Types" Part 1	18	14-Sep-26	05-Oct-26	28-Sep-26	18-Oct-26	61.11%	0%
ROAD WORKS IN (PH2-G-MCZ0)		18	05-Oct-26	25-Oct-26	28-Sep-26	18-Oct-26	0%	0%
Kerbstone Installation		18	05-Oct-26	25-Oct-26	28-Sep-26	18-Oct-26	0%	0%
SDR-2-CON-RW-ZG-2620	Kerbstone Installation "all Types" Part 1	18	05-Oct-26	25-Oct-26	28-Sep-26	18-Oct-26	0%	0%
Storm Water Drainage Network		175	08-Jul-26	28-Jan-27	06-Jul-26 A	31-Oct-26	30.47%	34.97%
ZONE A		145	08-Jul-26	26-Jan-27	06-Jul-26 A	31-Oct-26	30.7%	35.04%
STORM WATER LINE IN (PH2-A-MCB0)		68	23-Nov-26	10-Jan-27	16-Aug-26	22-Oct-26	0%	20%
Catch basin		68	23-Nov-26	10-Jan-27	16-Aug-26	22-Oct-26	0%	20%
Excavation		68	23-Nov-26	10-Jan-27	16-Aug-26	22-Oct-26	0%	20%
SDR-2-CON-ST-ZA-6930	Excavation for Catch basin Section 1	21	23-Nov-26	16-Dec-26	16-Aug-26	28-Sep-26	0%	40%
SDR-2-CON-ST-ZA-1300	Excavation for Catch basin Section 2	21	17-Dec-26	10-Jan-27	29-Sep-26	22-Oct-26	0%	0%
STORM WATER LINE IN (PH2-A-MCD0)		63	28-Sep-26	03-Jan-27	16-Aug-26	24-Oct-26	0%	47.7%
Pipes Works		42	28-Sep-26	09-Dec-26	20-Aug-26	22-Oct-26	0%	66.67%
bedding Works		21	28-Sep-26	21-Oct-26	20-Aug-26	28-Sep-26	0%	80%
SDR-2-CON-ST-ZA-4090	Sand bedding for GRP Pipes	21	28-Sep-26	21-Oct-26	20-Aug-26	28-Sep-26	0%	80%
Pipes Laying		21	22-Oct-26	15-Nov-26	26-Aug-26	28-Sep-26	0%	80%
SDR-2-CON-ST-ZA-4040	Install ST GRP Pipes	21	22-Oct-26	15-Nov-26	26-Aug-26	28-Sep-26	0%	80%
Testing		21	16-Nov-26	09-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4080	Testing ST GRP Pipes	21	16-Nov-26	09-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		42	28-Sep-26	09-Dec-26	27-Aug-26	24-Oct-26	0%	23.23%
bedding Works		21	28-Sep-26	21-Oct-26	27-Aug-26	28-Sep-26	0%	25%
SDR-2-CON-ST-ZA-4100	Sand bedding for Manholes	21	28-Sep-26	21-Oct-26	27-Aug-26	28-Sep-26	0%	25%
Install Manholes		21	22-Oct-26	15-Nov-26	30-Aug-26	29-Sep-26	0%	28%
SDR-2-CON-ST-ZA-4110	Manholes Installation	21	22-Oct-26	15-Nov-26	30-Aug-26	29-Sep-26	0%	28%
Testing		21	16-Nov-26	09-Dec-26	30-Sep-26	24-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4120	Testing for Manholes	21	16-Nov-26	09-Dec-26	30-Sep-26	24-Oct-26	0%	0%
Catch basin		61	16-Nov-26	03-Jan-27	16-Aug-26	24-Oct-26	0%	25%
Excavation		61	16-Nov-26	03-Jan-27	16-Aug-26	24-Oct-26	0%	25%
SDR-2-CON-ST-ZA-6970	Excavation for Catch basin Section 1	21	16-Nov-26	09-Dec-26	16-Aug-26	29-Sep-26	0%	50%
SDR-2-CON-ST-ZA-6410	Excavation for Catch basin Section 2	21	10-Dec-26	03-Jan-27	30-Sep-26	24-Oct-26	0%	0%
STORM WATER LINE IN (PH2-A-MCE0)		75	13-Oct-26	26-Jan-27	16-Aug-26	31-Oct-26	0%	37.05%
Pipes Works		55	14-Oct-26	26-Dec-26	20-Aug-26	22-Oct-26	0%	56.67%
bedding Works		21	14-Oct-26	07-Nov-26	20-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-ST-ZA-4240	Sand bedding for GRP Pipes	21	14-Oct-26	07-Nov-26	20-Aug-26	28-Sep-26	0%	50%
Pipes Laying		21	08-Nov-26	01-Dec-26	27-Aug-26	28-Sep-26	0%	70%
SDR-2-CON-ST-ZA-4190	Install ST GRP Pipes	21	08-Nov-26	01-Dec-26	27-Aug-26	28-Sep-26	0%	70%
Testing		21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4230	Testing ST GRP Pipes	21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		54	13-Oct-26	24-Dec-26	20-Aug-26	22-Oct-26	0%	23.23%
bedding Works		21	13-Oct-26	05-Nov-26	20-Aug-26	28-Sep-26	0%	25%
SDR-2-CON-ST-ZA-4250	Sand bedding for Manholes	21	13-Oct-26	05-Nov-26	20-Aug-26	28-Sep-26	0%	25%
Install Manholes		21	07-Nov-26	30-Nov-26	27-Aug-26	28-Sep-26	0%	28%
SDR-2-CON-ST-ZA-4260	Manholes Installation	21	07-Nov-26	30-Nov-26	27-Aug-26	28-Sep-26	0%	28%
Testing		21	01-Dec-26	24-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4270	Testing for Manholes	21	01-Dec-26	24-Dec-26	29-Sep-26	22-Oct-26	0%	0%

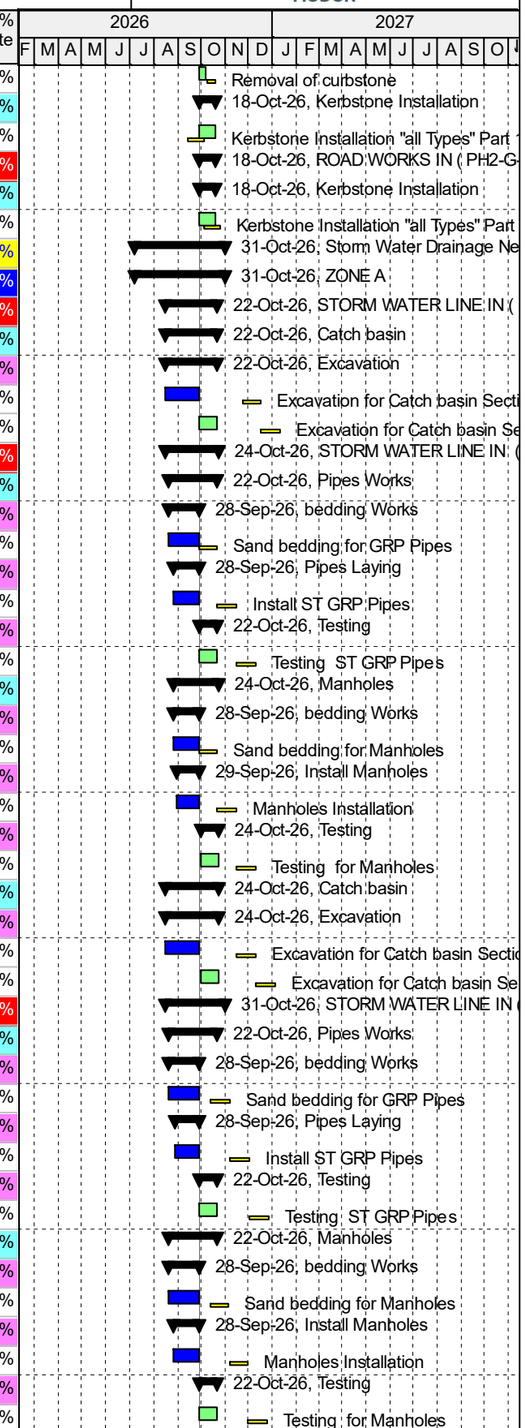

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Catch basin		68	01-Dec-26	26-Jan-27	16-Aug-26	31-Oct-26	0%	25%
Excavation		68	01-Dec-26	26-Jan-27	16-Aug-26	31-Oct-26	0%	25%
SDR-2-CON-ST-ZA-6440	Excavation for Catch basin Section 1	21	01-Dec-26	24-Dec-26	16-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-ST-ZA-4220	Excavation for Catch basin Section 2	21	03-Jan-27	26-Jan-27	07-Oct-26	31-Oct-26	0%	0%
STORM WATER LINE IN (PH2-A-MCF0)		84	25-Aug-26	01-Dec-26	06-Jul-26 A	22-Oct-26	17.74%	38.24%
Pipes Works		56	14-Oct-26	01-Dec-26	10-Sep-26	21-Oct-26	0%	45%
bedding Works		21	14-Oct-26	07-Nov-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4390	Sand bedding for GRP Pipes	21	14-Oct-26	07-Nov-26	28-Sep-26	21-Oct-26	0%	0%
Pipes Laying		21	08-Nov-26	01-Dec-26	10-Sep-26	21-Oct-26	0%	50%
SDR-2-CON-ST-ZA-4340	Install ST GRP Pipes	21	08-Nov-26	01-Dec-26	10-Sep-26	21-Oct-26	0%	50%
Manholes		50	25-Aug-26	13-Oct-26	06-Jul-26 A	22-Oct-26	61.9%	21.43%
Excavation		21	25-Aug-26	17-Sep-26	06-Jul-26 A	28-Sep-26	100%	50%
SDR-2-CON-ST-ZA-4360	Excavation Manholes Section 2	21	25-Aug-26	17-Sep-26	06-Jul-26 A	28-Sep-26	100%	50%
bedding Works		21	19-Sep-26	13-Oct-26	29-Sep-26	22-Oct-26	33.33%	0%
SDR-2-CON-ST-ZA-4400	Sand bedding for Manholes	21	19-Sep-26	13-Oct-26	29-Sep-26	22-Oct-26	33.33%	0%
STORM WATER LINE IN (PH2-A-MCG0)		42	03-Sep-26	22-Oct-26	29-Jul-26 A	22-Oct-26	33.26%	16.25%
Pipes Works		21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.57%	0%
bedding Works		21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.57%	0%
SDR-2-CON-ST-ZA-4540	Sand bedding for GRP Pipes	21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.52%	0%
Manholes		42	03-Sep-26	22-Oct-26	29-Jul-26 A	22-Oct-26	40.82%	21.43%
Excavation		21	03-Sep-26	28-Sep-26	29-Jul-26 A	28-Sep-26	95.24%	50%
SDR-2-CON-ST-ZA-4510	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	29-Jul-26 A	28-Sep-26	95.24%	50%
bedding Works		21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4550	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
STORM WATER LINE IN (PH2-A-MCH0)		42	03-Sep-26	22-Oct-26	13-Jul-26 A	22-Oct-26	34.01%	16.76%
Pipes Works		21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.57%	0%
bedding Works		21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.57%	0%
SDR-2-CON-ST-ZA-4690	Sand bedding for GRP Pipes	21	26-Sep-26	19-Oct-26	28-Sep-26	21-Oct-26	9.52%	0%
Manholes		42	03-Sep-26	22-Oct-26	13-Jul-26 A	22-Oct-26	40.82%	21.43%
Excavation		21	03-Sep-26	28-Sep-26	13-Jul-26 A	28-Sep-26	95.24%	50%
SDR-2-CON-ST-ZA-6350	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	13-Jul-26 A	28-Sep-26	95.24%	50%
bedding Works		21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4700	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
STORM WATER LINE IN (PH2-A-MCA0)		46	30-Aug-26	18-Oct-26	14-Jul-26 A	22-Oct-26	27.97%	7.96%
Pipes Works		21	24-Sep-26	18-Oct-26	28-Sep-26	21-Oct-26	14.35%	0%
bedding Works		21	24-Sep-26	18-Oct-26	28-Sep-26	21-Oct-26	14.35%	0%
SDR-2-CON-ST-ZA-4840	Sand bedding for GRP Pipes	21	24-Sep-26	18-Oct-26	28-Sep-26	21-Oct-26	14.29%	0%
Manholes		46	30-Aug-26	18-Oct-26	14-Jul-26 A	22-Oct-26	51.02%	21.43%
Excavation		21	30-Aug-26	22-Sep-26	14-Jul-26 A	28-Sep-26	100%	50%
SDR-2-CON-ST-ZA-4810	Excavation Manholes Section 2	21	30-Aug-26	22-Sep-26	14-Jul-26 A	28-Sep-26	100%	50%
bedding Works		21	24-Sep-26	18-Oct-26	29-Sep-26	22-Oct-26	14.29%	0%
SDR-2-CON-ST-ZA-4850	Sand bedding for Manholes	21	24-Sep-26	18-Oct-26	29-Sep-26	22-Oct-26	14.29%	0%
STORM WATER LINE IN From MH - A2 / 2 TO STA-A2/10		42	03-Sep-26	22-Oct-26	30-Jul-26 A	22-Oct-26	15.83%	8.31%
Pipes Works		21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%
bedding Works		21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-ST-ZA-4990	Sand bedding for GRP Pipes	21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%
Manholes		42	03-Sep-26	22-Oct-26	30-Jul-26 A	22-Oct-26	40.82%	21.43%

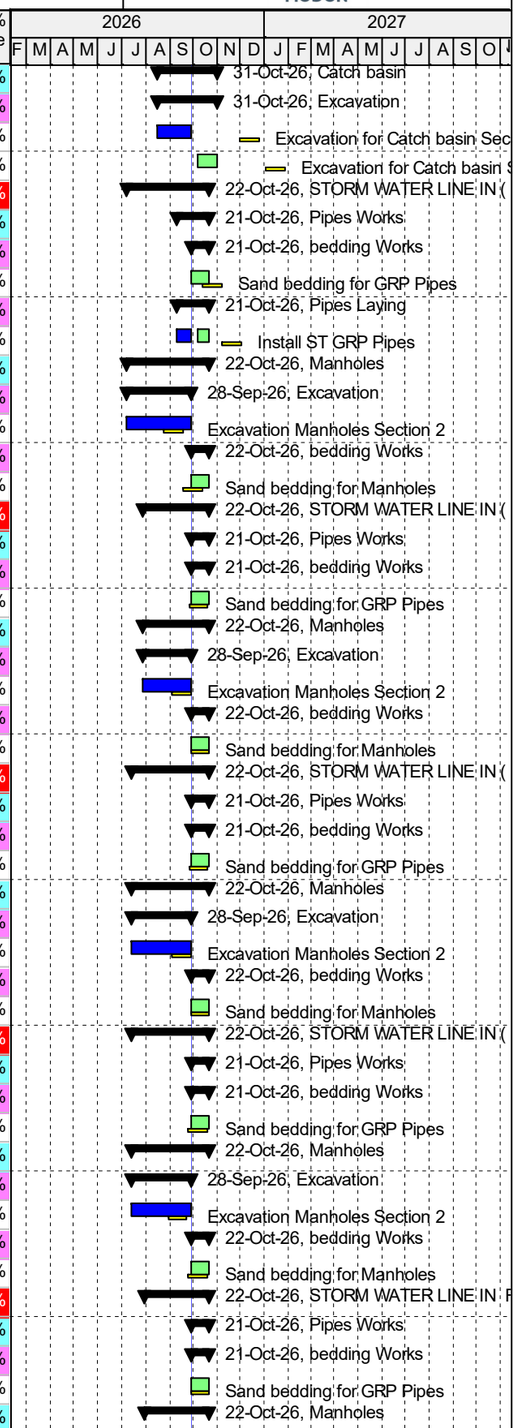

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	03-Sep-26	28-Sep-26	30-Jul-26 A	28-Sep-26	95.24%	50%
SDR-2-CON-ST-ZA-4960	Excavation Manholes Section 2	21	03-Sep-26	28-Sep-26	30-Jul-26 A	28-Sep-26	95.24%	50%
bedding Works		21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-5000	Sand bedding for Manholes	21	29-Sep-26	22-Oct-26	29-Sep-26	22-Oct-26	0%	0%
STORM WATER LINE From STA-A2/10 TO STA-A2/1		21	15-Aug-26	27-Oct-26	28-Sep-26	21-Oct-26	12.48%	0%
Pipes Works		21	04-Oct-26	27-Oct-26	28-Sep-26	21-Oct-26	0%	0%
bedding Works		21	04-Oct-26	27-Oct-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-ST-ZA-5140	Sand bedding for GRP Pipes	21	04-Oct-26	27-Oct-26	28-Sep-26	21-Oct-26	0%	0%
Manholes		21	15-Aug-26	07-Sep-26	28-Sep-26	21-Oct-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	28-Sep-26	21-Oct-26	100%	0%
SDR-2-CON-ST-ZA-6610	Excavation Manholes Section 1	21	15-Aug-26	07-Sep-26	28-Sep-26	21-Oct-26	100%	0%
STORM WATER LINE From IP A7 To Pond A		55	19-Aug-26	04-Nov-26	12-Aug-26	22-Oct-26	58.33%	70%
Pipes Works		55	19-Aug-26	04-Nov-26	12-Aug-26	22-Oct-26	57.14%	72%
Excavation		45	19-Aug-26	11-Oct-26	12-Aug-26	28-Sep-26	71.43%	90%
SDR-2-CON-ST-ZA-6630	Excavation for GRP Pipes Section 1	21	19-Aug-26	12-Sep-26	12-Aug-26	28-Sep-26	100%	90%
SDR-2-CON-ST-ZA-5830	Excavation for GRP Pipes Section 2	21	16-Sep-26	11-Oct-26	12-Aug-26	28-Sep-26	42.86%	90%
bedding Works		21	12-Oct-26	04-Nov-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-ST-ZA-5890	Sand bedding for GRP Pipes	21	12-Oct-26	04-Nov-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		21	19-Aug-26	12-Sep-26	28-Sep-26	21-Oct-26	100%	0%
Excavation		21	19-Aug-26	12-Sep-26	28-Sep-26	21-Oct-26	100%	0%
SDR-2-CON-ST-ZA-6640	Excavation Manholes Section 1	21	19-Aug-26	12-Sep-26	28-Sep-26	21-Oct-26	100%	0%
Concrete Box culverts		14	25-Jul-26	15-Oct-26	28-Sep-26	13-Oct-26	16.5%	0%
For Pond A		14	30-Sep-26	15-Oct-26	28-Sep-26	13-Oct-26	0%	0%
Plain Concrete		6	30-Sep-26	06-Oct-26	28-Sep-26	04-Oct-26	0%	0%
SDR-2-CON-ST-ZA-3290	Plain Concrete for box culvert	6	30-Sep-26	06-Oct-26	28-Sep-26	04-Oct-26	0%	0%
Steel Reinforcement		8	07-Oct-26	15-Oct-26	05-Oct-26	13-Oct-26	0%	0%
SDR-2-CON-ST-ZA-3300	Steel Reinforcement for box culverts	8	07-Oct-26	15-Oct-26	05-Oct-26	13-Oct-26	0%	0%
For Pond B		14	25-Jul-26	09-Aug-26	28-Sep-26	13-Oct-26	100%	0%
Backfilling with common / suitable excavated material		8	25-Jul-26	02-Aug-26	28-Sep-26	06-Oct-26	100%	0%
SDR-2-CON-ST-ZA-6260	Backfilling with common / suitable excavated material or with suitable imported materia	8	25-Jul-26	02-Aug-26	28-Sep-26	06-Oct-26	100%	0%
Plain Concrete		6	03-Aug-26	09-Aug-26	07-Oct-26	13-Oct-26	100%	0%
SDR-2-CON-ST-ZA-6270	Plain Concrete for box culvert	6	03-Aug-26	09-Aug-26	07-Oct-26	13-Oct-26	100%	0%
For Pond C		10	06-Aug-26	17-Aug-26	01-Oct-26	12-Oct-26	100%	0%
Excavation		10	06-Aug-26	17-Aug-26	01-Oct-26	12-Oct-26	100%	0%
SDR-2-CON-ST-ZA-6300	Excavation for Box Culvert.	10	06-Aug-26	17-Aug-26	01-Oct-26	12-Oct-26	100%	0%
Drainage works for ponds and open canals		96	08-Jul-26	14-Sep-26	31-Aug-26	28-Oct-26	100%	14.96%
Pond A		82	25-Jul-26	14-Sep-26	31-Aug-26	28-Oct-26	100%	15%
Sand lining for pond bed		82	25-Jul-26	14-Sep-26	31-Aug-26	28-Oct-26	100%	15%
SDR-2-CON-ST-ZA-6690	Sand lining for pond bed Section 1 & Section 2	21	25-Jul-26	17-Aug-26	31-Aug-26	30-Sep-26	100%	30%
SDR-2-CON-ST-ZA-6150	Sand lining for pond bed Section 3 & Section 4	21	22-Aug-26	14-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Pond C		93	08-Jul-26	30-Aug-26	31-Aug-26	25-Oct-26	100%	11.67%
Excavation		93	08-Jul-26	30-Aug-26	31-Aug-26	25-Oct-26	100%	11.67%
SDR-2-CON-ST-ZA-6740	Excavation for cutting material. Section 2	21	08-Jul-26	01-Aug-26	31-Aug-26	30-Sep-26	100%	25%
SDR-2-CON-ST-ZA-3320	Excavation for cutting material. Section 3	21	06-Aug-26	30-Aug-26	01-Oct-26	25-Oct-26	100%	0%
ZONE G		60	21-Nov-26	28-Jan-27	31-Aug-26	07-Oct-26	0%	25%
STORM WATER LINE IN (PH2-G-MCE0)		21	05-Jan-27	28-Jan-27	31-Aug-26	30-Sep-26	0%	25%
Manholes		21	05-Jan-27	28-Jan-27	31-Aug-26	30-Sep-26	0%	25%

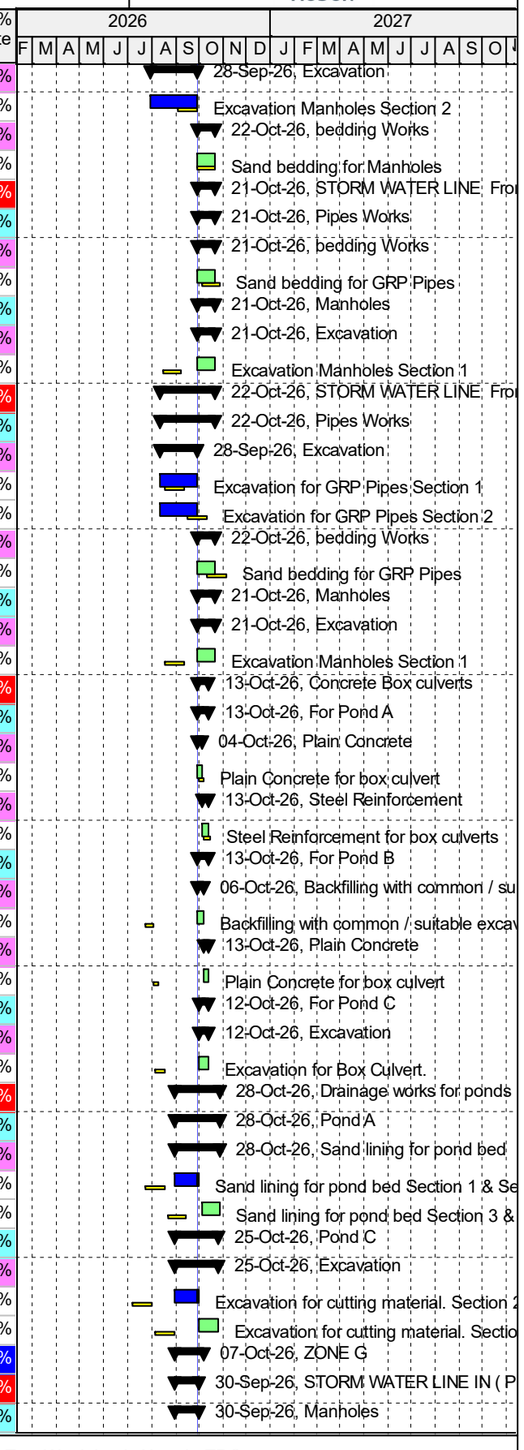

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Testing		21	05-Jan-27	28-Jan-27	31-Aug-26	30-Sep-26	0%	25%
SDR-2-CON-ST-ZA-5470	Testing for Manholes	21	05-Jan-27	28-Jan-27	31-Aug-26	30-Sep-26	0%	25%
STORM WATER LINE IN (PH2-G-MCF0)		21	22-Nov-26	15-Dec-26	31-Aug-26	30-Sep-26	0%	25%
Manholes		21	22-Nov-26	15-Dec-26	31-Aug-26	30-Sep-26	0%	25%
Testing		21	22-Nov-26	15-Dec-26	31-Aug-26	30-Sep-26	0%	25%
SDR-2-CON-ST-ZA-5620	Testing for Manholes	21	22-Nov-26	15-Dec-26	31-Aug-26	30-Sep-26	0%	25%
STORM WATER LINE IN (PH2-G-MCG0)		21	21-Nov-26	14-Dec-26	07-Sep-26	07-Oct-26	0%	25%
Manholes		21	21-Nov-26	14-Dec-26	07-Sep-26	07-Oct-26	0%	25%
Testing		21	21-Nov-26	14-Dec-26	07-Sep-26	07-Oct-26	0%	25%
SDR-2-CON-ST-ZA-6070	Testing for Manholes	21	21-Nov-26	14-Dec-26	07-Sep-26	07-Oct-26	0%	25%
Sewerage Network		126	09-Dec-26	25-Mar-27	22-Jun-26 A	29-Oct-26	0%	62.63%
ZONE A		121	09-Dec-26	25-Mar-27	22-Jun-26 A	29-Oct-26	0%	65.65%
LINE 1 (PH2-A-MCA0)		101	09-Dec-26	17-Feb-27	22-Jun-26 A	22-Oct-26	0%	68.64%
Pipes Work		21	09-Dec-26	02-Jan-27	22-Jun-26 A	28-Sep-26	0%	90%
Pipes Laying		21	09-Dec-26	02-Jan-27	22-Jun-26 A	28-Sep-26	0%	90%
SDR-2-CON-SE-ZA-1010	200 mm GRP Pipe Laying	21	09-Dec-26	02-Jan-27	22-Jun-26 A	28-Sep-26	0%	90%
Manholes		101	31-Dec-26	17-Feb-27	09-Jul-26 A	22-Oct-26	0%	20%
Testing		21	31-Dec-26	24-Jan-27	09-Jul-26 A	28-Sep-26	0%	60%
SDR-2-CON-SE-ZA-1050	Testing	21	31-Dec-26	24-Jan-27	09-Jul-26 A	28-Sep-26	0%	60%
Backfilling		21	25-Jan-27	17-Feb-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-SE-ZA-1440	Backfilling	21	25-Jan-27	17-Feb-27	29-Sep-26	22-Oct-26	0%	0%
LINE 2 AND LINE 3 (PH2-A-MCC0)		21	22-Dec-26	14-Jan-27	07-Jul-26 A	28-Sep-26	0%	90%
Manholes		21	22-Dec-26	14-Jan-27	07-Jul-26 A	28-Sep-26	0%	90%
Install Manholes		21	22-Dec-26	14-Jan-27	07-Jul-26 A	28-Sep-26	0%	90%
SDR-2-CON-SE-ZA-1500	Manhole Installation	21	22-Dec-26	14-Jan-27	07-Jul-26 A	28-Sep-26	0%	90%
LINE 4 AND LINE 5 (PH2-A-MCD0)		21	27-Dec-26	19-Jan-27	21-Jul-26 A	28-Sep-26	0%	80%
Pipes Work		21	27-Dec-26	19-Jan-27	21-Jul-26 A	28-Sep-26	0%	80%
Pipes Laying		21	27-Dec-26	19-Jan-27	21-Jul-26 A	28-Sep-26	0%	80%
SDR-2-CON-SE-ZA-1570	200 mm GRP Pipe Laying	21	27-Dec-26	19-Jan-27	21-Jul-26 A	28-Sep-26	0%	80%
LINE 6 AND LINE 7 (PH2-A-MCE0)		21	03-Jan-27	26-Jan-27	15-Jul-26 A	28-Sep-26	0%	75%
Manholes		21	03-Jan-27	26-Jan-27	15-Jul-26 A	28-Sep-26	0%	75%
Install Manholes		21	03-Jan-27	26-Jan-27	15-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SE-ZA-1700	Manhole Installation	21	03-Jan-27	26-Jan-27	15-Jul-26 A	28-Sep-26	0%	75%
LINE 8 AND LINE 9 (PH2-A-MCF0)		121	30-Dec-26	25-Mar-27	08-Jul-26 A	29-Oct-26	0%	51.41%
Pipes Work		121	30-Dec-26	18-Mar-27	27-Jul-26 A	22-Oct-26	0%	53%
Pipes Laying		21	30-Dec-26	23-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SE-ZA-1770	200 mm GRP Pipe Laying	21	30-Dec-26	23-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
Testing		21	24-Jan-27	16-Feb-27	18-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-SE-ZA-1780	Testing of 200 mm GRP Pipe.	21	24-Jan-27	16-Feb-27	18-Aug-26	28-Sep-26	0%	60%
Backfilling		21	17-Feb-27	18-Mar-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-SE-ZA-1830	Backfilling of 200 mm GRP Pipe.	21	17-Feb-27	18-Mar-27	29-Sep-26	22-Oct-26	0%	0%
Manholes		112	30-Dec-26	25-Mar-27	08-Jul-26 A	29-Oct-26	0%	49%
Install Manholes		21	30-Dec-26	23-Jan-27	08-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SE-ZA-1800	Manhole Installation	21	30-Dec-26	23-Jan-27	08-Jul-26 A	28-Sep-26	0%	75%
Testing		21	24-Jan-27	16-Feb-27	27-Aug-26	29-Sep-26	0%	30%
SDR-2-CON-SE-ZA-1810	Testing	21	24-Jan-27	16-Feb-27	27-Aug-26	29-Sep-26	0%	30%
Backfilling		18	01-Mar-27	25-Mar-27	10-Oct-26	29-Oct-26	0%	0%

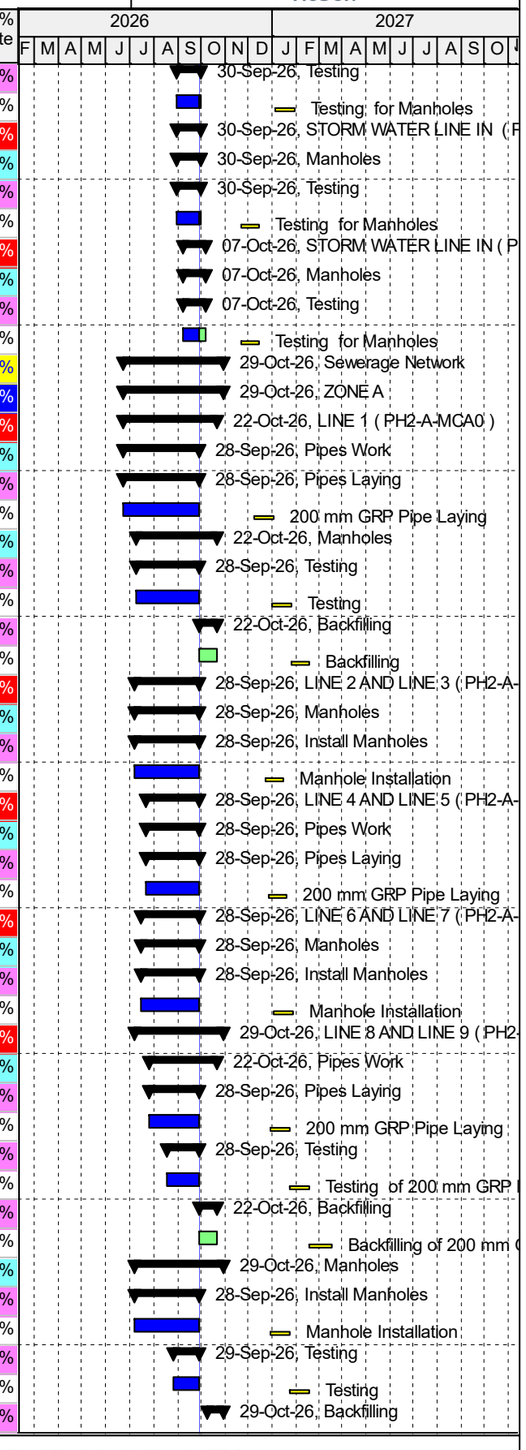

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-SE-ZA-1840	Backfilling	18	01-Mar-27	25-Mar-27	10-Oct-26	29-Oct-26	0%	0%
LINE 10 AND LINE 11 (PH2-A-MCG0)		24	14-Dec-26	10-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
Pipes Work		21	17-Dec-26	10-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
Pipes Laying		21	17-Dec-26	10-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SE-ZA-1870	200 mm GRP Pipe Laying	21	17-Dec-26	10-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
Manholes		21	14-Dec-26	06-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
Install Manholes		21	14-Dec-26	06-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SE-ZA-1900	Manhole Installation	21	14-Dec-26	06-Jan-27	27-Jul-26 A	28-Sep-26	0%	75%
LINE 12 AND LINE 13 (PH2-A-MCH0)		112	23-Dec-26	03-Mar-27	25-Jul-26 A	22-Oct-26	0%	57.27%
Pipes Work		94	23-Dec-26	09-Feb-27	25-Jul-26 A	22-Oct-26	0%	57.27%
Pipes Laying		21	23-Dec-26	16-Jan-27	25-Jul-26 A	28-Sep-26	0%	70%
SDR-2-CON-SE-ZA-1970	200 mm GRP Pipe Laying	21	23-Dec-26	16-Jan-27	25-Jul-26 A	28-Sep-26	0%	70%
Testing		21	17-Jan-27	09-Feb-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-SE-ZA-1980	Testing of 200 mm GRP Pipe.	21	17-Jan-27	09-Feb-27	29-Sep-26	22-Oct-26	0%	0%
Manholes		112	13-Jan-27	03-Mar-27	27-Jul-26 A	22-Oct-26	0%	57.27%
Install Manholes		21	13-Jan-27	06-Feb-27	27-Jul-26 A	28-Sep-26	0%	70%
SDR-2-CON-SE-ZA-2000	Manhole Installation	21	13-Jan-27	06-Feb-27	27-Jul-26 A	28-Sep-26	0%	70%
Testing		21	07-Feb-27	03-Mar-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-SE-ZA-2010	Testing	21	07-Feb-27	03-Mar-27	29-Sep-26	22-Oct-26	0%	0%
ZONE G		43	04-Jan-27	23-Feb-27	07-Sep-26	07-Oct-26	0%	10%
LINE 49 AND LINE 51 (PH2-G-MCE0)		21	24-Jan-27	16-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Manholes		21	24-Jan-27	16-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Testing		21	24-Jan-27	16-Feb-27	07-Sep-26	07-Oct-26	0%	10%
SDR-2-CON-SE-ZA-2110	Testing	21	24-Jan-27	16-Feb-27	07-Sep-26	07-Oct-26	0%	10%
LINE 50 (PH2-G-MCD0)		21	30-Jan-27	23-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Manholes		21	30-Jan-27	23-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Testing		21	30-Jan-27	23-Feb-27	07-Sep-26	07-Oct-26	0%	10%
SDR-2-CON-SE-ZA-2210	Testing	21	30-Jan-27	23-Feb-27	07-Sep-26	07-Oct-26	0%	10%
LINE 52 AND LINE 53 (PH2-G-MCF0)		21	04-Jan-27	27-Jan-27	07-Sep-26	07-Oct-26	0%	10%
Manholes		21	04-Jan-27	27-Jan-27	07-Sep-26	07-Oct-26	0%	10%
Testing		21	04-Jan-27	27-Jan-27	07-Sep-26	07-Oct-26	0%	10%
SDR-2-CON-SE-ZA-2310	Testing	21	04-Jan-27	27-Jan-27	07-Sep-26	07-Oct-26	0%	10%
LINE 54 AND LINE 55 (PH2-G-MCG0)		21	18-Jan-27	10-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Manholes		21	18-Jan-27	10-Feb-27	07-Sep-26	07-Oct-26	0%	10%
Testing		21	18-Jan-27	10-Feb-27	07-Sep-26	07-Oct-26	0%	10%
SDR-2-CON-SE-ZA-2410	Testing	21	18-Jan-27	10-Feb-27	07-Sep-26	07-Oct-26	0%	10%
TSE Network		138	23-Nov-26	28-Mar-27	12-Aug-26	22-Oct-26	0%	19.07%
ZONE A		21	23-Nov-26	16-Jan-27	24-Sep-26	21-Oct-26	0%	11.27%
TSE NETWORK IN (PH2-A-MCC0)		21	02-Dec-26	26-Dec-26	24-Sep-26	21-Oct-26	0%	36.45%
Pipes Work		21	02-Dec-26	26-Dec-26	24-Sep-26	21-Oct-26	0%	50%
Excavation		21	02-Dec-26	26-Dec-26	24-Sep-26	21-Oct-26	0%	50%
SDR-2-CON-TS-ZA-3240	Excavation for TSE HDPE Pipes 125 mm Section 1	21	02-Dec-26	26-Dec-26	24-Sep-26	21-Oct-26	0%	50%
Valve Chambers & Valves		21	02-Dec-26	26-Dec-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	02-Dec-26	26-Dec-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3250	Excavation for Valve Chambers Section 1	21	02-Dec-26	26-Dec-26	28-Sep-26	21-Oct-26	0%	0%
TSE NETWORK IN (PH2-A-MCD0)		20	02-Dec-26	16-Jan-27	24-Sep-26	20-Oct-26	0%	9.35%
Pipes Work		19	26-Dec-26	16-Jan-27	24-Sep-26	19-Oct-26	0%	25%

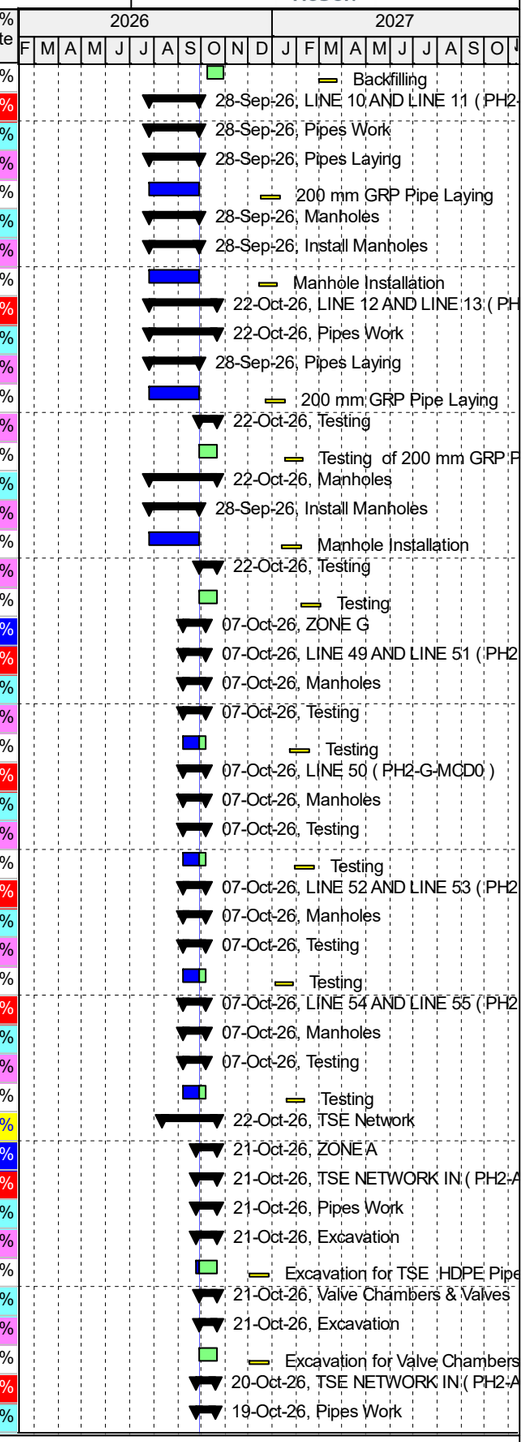

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		19	26-Dec-26	16-Jan-27	24-Sep-26	19-Oct-26	0%	25%
SDR-2-CON-TS-ZA-1270	Excavation for TSE HDPE Pipes 90 mm Section 2	19	26-Dec-26	16-Jan-27	24-Sep-26	19-Oct-26	0%	25%
Valve Chambers & Valves		20	02-Dec-26	24-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	02-Dec-26	24-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3270	Excavation for Valve Chambers Section 1	20	02-Dec-26	24-Dec-26	28-Sep-26	20-Oct-26	0%	0%
TSE NETWORK IN (PH2-A-MCE0)		21	13-Dec-26	05-Jan-27	28-Sep-26	21-Oct-26	0%	0%
Valve Chambers & Valves		21	13-Dec-26	05-Jan-27	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	13-Dec-26	05-Jan-27	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3290	Excavation for Valve Chambers Section 1	21	13-Dec-26	05-Jan-27	28-Sep-26	21-Oct-26	0%	0%
TSE NETWORK IN (PH2-A-MCF0)		20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Pipes Work		20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3300	Excavation for TSE HDPE Pipes 90 mm Section 1	20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Valve Chambers & Valves		20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3310	Excavation for Valve Chambers Section 1	20	06-Dec-26	28-Dec-26	28-Sep-26	20-Oct-26	0%	0%
TSE NETWORK IN (PH2-A-MCG0)		20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Pipes Work		20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3320	Excavation for TSE HDPE Pipes 90 mm Section 1	20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Valve Chambers & Valves		20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3330	Excavation for Valve Chambers Section 1	20	23-Nov-26	15-Dec-26	28-Sep-26	20-Oct-26	0%	0%
TSE NETWORK IN (PH2-A-MCH0)		20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Pipes Work		20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3340	Excavation for TSE HDPE Pipes 250 mm Section 1	20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Valve Chambers & Valves		20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3350	Excavation for Valve Chambers Section 1	20	29-Nov-26	21-Dec-26	28-Sep-26	20-Oct-26	0%	0%
ZONE G		138	30-Nov-26	28-Mar-27	12-Aug-26	22-Oct-26	0%	21.3%
TSE NETWORK IN (PH2-G-MCA0)		138	30-Nov-26	28-Mar-27	12-Aug-26	20-Oct-26	0%	19.35%
Pipes Work		137	30-Nov-26	28-Mar-27	12-Aug-26	13-Oct-26	0%	20%
Excavation		42	30-Nov-26	17-Jan-27	12-Aug-26	28-Sep-26	0%	30%
SDR-2-CON-TS-ZA-3400	Excavation for TSE HDPE Pipes 225 mm Section 1	21	30-Nov-26	23-Dec-26	12-Aug-26	28-Sep-26	0%	30%
SDR-2-CON-TS-ZA-2300	Excavation for TSE HDPE Pipes 225 mm Section 2	21	24-Dec-26	17-Jan-27	12-Aug-26	28-Sep-26	0%	30%
bedding Works		21	18-Jan-27	10-Feb-27	24-Aug-26	28-Sep-26	0%	20%
SDR-2-CON-TS-ZA-2380	Sand bedding for TSE HDPE Pipes 225 mm	21	18-Jan-27	10-Feb-27	24-Aug-26	28-Sep-26	0%	20%
Pipes Laying		21	11-Feb-27	08-Mar-27	25-Aug-26	28-Sep-26	0%	20%
SDR-2-CON-TS-ZA-2310	Install TSE 225 mm HDPE Pipe	21	11-Feb-27	08-Mar-27	25-Aug-26	28-Sep-26	0%	20%
Testing		13	14-Mar-27	28-Mar-27	29-Sep-26	13-Oct-26	0%	0%
SDR-2-CON-TS-ZA-2370	Testing of TSE HDPE Pipe 225 mm.	13	14-Mar-27	28-Mar-27	29-Sep-26	13-Oct-26	0%	0%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3410	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
TSE NETWORK IN (PH2-G-MCE0)		96	02-Dec-26	11-Feb-27	12-Aug-26	22-Oct-26	0%	20.89%
Pipes Work		96	02-Dec-26	11-Feb-27	12-Aug-26	22-Oct-26	0%	24%

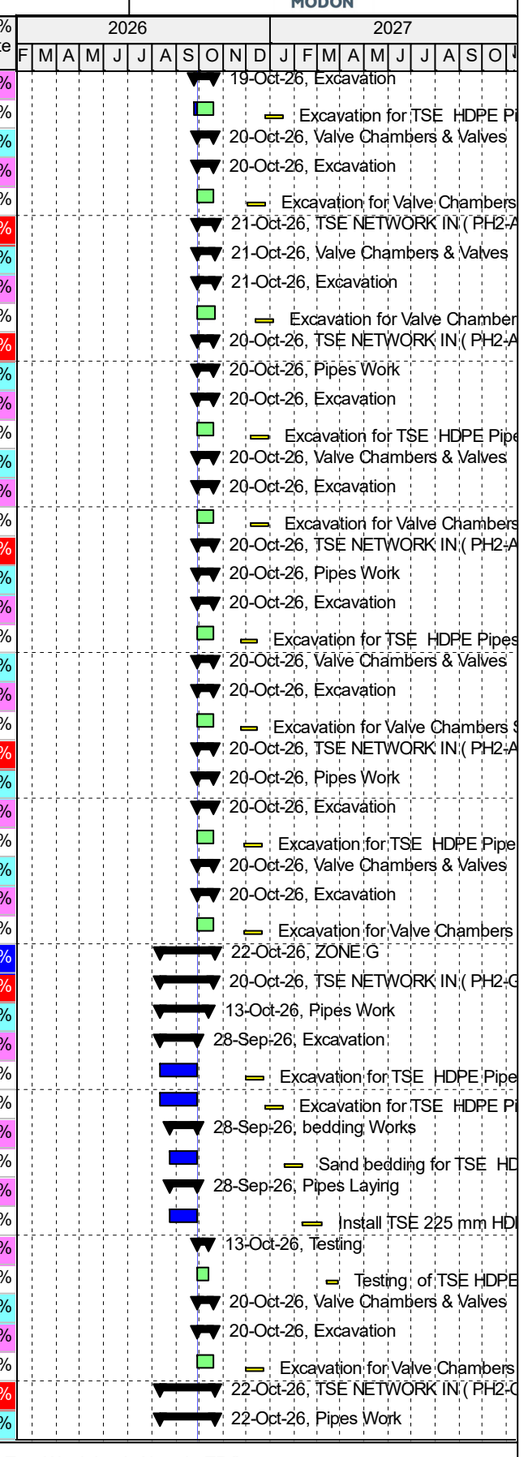

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		41	02-Dec-26	18-Jan-27	12-Aug-26	28-Sep-26	0%	30%
SDR-2-CON-TS-ZA-3420	Excavation for TSE HDPE Pipes 125 mm Section 1	21	02-Dec-26	26-Dec-26	12-Aug-26	28-Sep-26	0%	30%
SDR-2-CON-TS-ZA-2400	Excavation for TSE HDPE Pipes 125 mm Section 2	20	27-Dec-26	18-Jan-27	12-Aug-26	28-Sep-26	0%	30%
bedding Works		21	19-Jan-27	11-Feb-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TS-ZA-2430	Sand bedding for TSE HDPE Pipes 125 mm	21	19-Jan-27	11-Feb-27	29-Sep-26	22-Oct-26	0%	0%
Valve Chambers & Valves		21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Excavation		21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3430	Excavation for Valve Chambers Section 1	21	02-Dec-26	26-Dec-26	29-Sep-26	22-Oct-26	0%	0%
TSE NETWORK IN (PH2-G-MCG0)		94	30-Nov-26	08-Feb-27	13-Aug-26	22-Oct-26	0%	12.6%
Pipes Work		93	23-Dec-26	08-Feb-27	13-Aug-26	22-Oct-26	0%	26.67%
Excavation		20	23-Dec-26	14-Jan-27	13-Aug-26	28-Sep-26	0%	40%
SDR-2-CON-TS-ZA-3000	Excavation for TSE HDPE Pipes 90 mm Section 2	20	23-Dec-26	14-Jan-27	13-Aug-26	28-Sep-26	0%	40%
bedding Works		21	16-Jan-27	08-Feb-27	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3030	Sand bedding for TSE HDPE Pipes 90 mm	21	16-Jan-27	08-Feb-27	29-Sep-26	22-Oct-26	0%	0%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3470	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
TSE NETWORK IN (PH2-G-MCZ0)		95	30-Nov-26	16-Jan-27	13-Aug-26	20-Oct-26	0%	33.73%
Pipes Work		41	30-Nov-26	16-Jan-27	13-Aug-26	28-Sep-26	0%	40%
Excavation		41	30-Nov-26	16-Jan-27	13-Aug-26	28-Sep-26	0%	40%
SDR-2-CON-TS-ZA-3480	Excavation for TSE HDPE Pipes 125 mm Section 1	21	30-Nov-26	23-Dec-26	13-Aug-26	28-Sep-26	0%	40%
SDR-2-CON-TS-ZA-2500	Excavation for TSE HDPE Pipes 125 mm Section 2	20	24-Dec-26	16-Jan-27	13-Aug-26	28-Sep-26	0%	40%
Valve Chambers & Valves		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TS-ZA-3490	Excavation for Valve Chambers Section 1	20	30-Nov-26	22-Dec-26	28-Sep-26	20-Oct-26	0%	0%
Portable Water		175	07-Jan-27	26-May-27	01-Aug-26	26-Oct-26	0%	51.97%
ZONE A		20	07-Jan-27	30-Jan-27	28-Sep-26	20-Oct-26	0%	0%
PORTABLE WATER IN (PH2-A-MCE0)		20	07-Jan-27	30-Jan-27	28-Sep-26	20-Oct-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		20	07-Jan-27	30-Jan-27	28-Sep-26	20-Oct-26	0%	0%
Excavation		20	07-Jan-27	30-Jan-27	28-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-PW-ZA-3840	Excavation for Valve Chambers Section 1	20	07-Jan-27	30-Jan-27	28-Sep-26	20-Oct-26	0%	0%
ZONE G		175	16-Jan-27	26-May-27	01-Aug-26	26-Oct-26	0%	52.58%
PORTABLE WATER IN (PH2-G-MCA0)		170	18-Jan-27	15-May-27	01-Aug-26	24-Oct-26	0%	56.25%
Pipes Work		169	14-Mar-27	15-May-27	01-Aug-26	24-Oct-26	0%	57.5%
bedding Works		16	14-Mar-27	31-Mar-27	01-Aug-26	28-Sep-26	0%	92%
SDR-2-CON-PW-ZG-1500	Sand bedding for PW HDPE Pipes 400 mm	16	14-Mar-27	31-Mar-27	01-Aug-26	28-Sep-26	0%	92%
Pipes Laying		16	01-Apr-27	19-Apr-27	13-Aug-26	28-Sep-26	0%	92%
SDR-2-CON-PW-ZG-1010	Install PW 400 mm HDPE Pipe	16	01-Apr-27	19-Apr-27	13-Aug-26	28-Sep-26	0%	92%
Testing		10	20-Apr-27	01-May-27	29-Sep-26	10-Oct-26	0%	0%
SDR-2-CON-PW-ZG-1080	Testing of PW HDPE Pipe 400 mm.	10	20-Apr-27	01-May-27	29-Sep-26	10-Oct-26	0%	0%
Backfilling		12	02-May-27	15-May-27	11-Oct-26	24-Oct-26	0%	0%
SDR-2-CON-PW-ZG-1510	Backfilling of PW HDPE Pipe 400 mm.	12	02-May-27	15-May-27	11-Oct-26	24-Oct-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	18-Jan-27	10-Feb-27	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	18-Jan-27	10-Feb-27	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-PW-ZA-3950	Excavation for Valve Chambers Section 1	21	18-Jan-27	10-Feb-27	28-Sep-26	21-Oct-26	0%	0%
PORTABLE WATER IN (PH2-G-MCE0)		174	15-Mar-27	24-May-27	13-Aug-26	21-Oct-26	0%	57.94%
Pipes Work		174	15-Mar-27	24-May-27	13-Aug-26	21-Oct-26	0%	57.94%

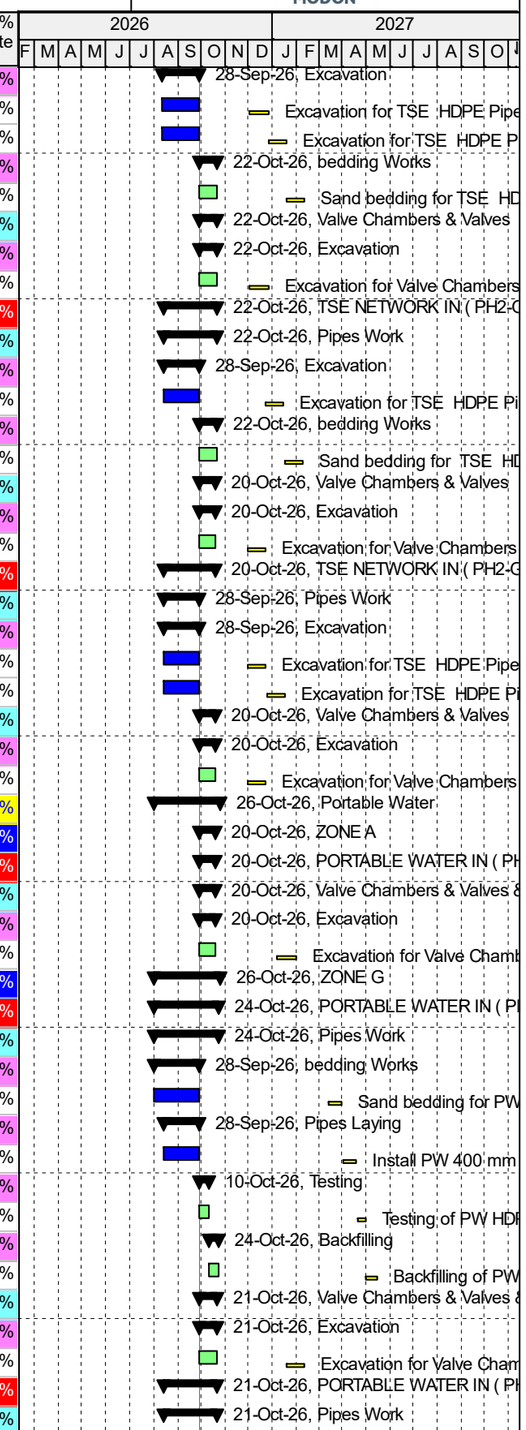

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
bedding Works		18	15-Mar-27	04-Apr-27	26-Aug-26	28-Sep-26	0%	45%
SDR-2-CON-PW-ZA-2940	Sand bedding for PW HDPE Pipe 225 mm.	18	15-Mar-27	04-Apr-27	26-Aug-26	28-Sep-26	0%	45%
Pipes Laying		18	05-Apr-27	25-Apr-27	13-Aug-26	28-Sep-26	0%	98%
SDR-2-CON-PW-ZA-2920	Install PW 225 mm HDPE Pipe	18	05-Apr-27	25-Apr-27	13-Aug-26	28-Sep-26	0%	98%
Testing		7	26-Apr-27	03-May-27	29-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-PW-ZA-2930	Testing of PW HDPE Pipe 225 mm.	7	26-Apr-27	03-May-27	29-Sep-26	06-Oct-26	0%	0%
Backfilling		13	04-May-27	24-May-27	07-Oct-26	21-Oct-26	0%	0%
SDR-2-CON-PW-ZA-2950	Backfilling of PW HDPE Pipe 225 mm.	13	04-May-27	24-May-27	07-Oct-26	21-Oct-26	0%	0%
PORTABLE WATER IN (PH2-G-MCG0)		154	16-Jan-27	22-May-27	26-Aug-26	26-Oct-26	0%	5.85%
Pipes Work		154	07-Mar-27	22-May-27	26-Aug-26	26-Oct-26	0%	7.14%
bedding Works		18	07-Mar-27	31-Mar-27	26-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-PW-ZA-3140	Sand bedding for PW HDPE Pipe 225 mm.	18	07-Mar-27	31-Mar-27	26-Aug-26	28-Sep-26	0%	50%
Testing		8	18-Apr-27	26-Apr-27	28-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-PW-ZA-3130	Testing of PW HDPE Pipe 225 mm.	8	18-Apr-27	26-Apr-27	28-Sep-26	06-Oct-26	0%	0%
Backfilling		17	27-Apr-27	22-May-27	07-Oct-26	26-Oct-26	0%	0%
SDR-2-CON-PW-ZA-3150	Backfilling of PW HDPE Pipe 225 mm.	17	27-Apr-27	22-May-27	07-Oct-26	26-Oct-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	16-Jan-27	08-Feb-27	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	16-Jan-27	08-Feb-27	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-PW-ZA-4010	Excavation for Valve Chambers Section 1	21	16-Jan-27	08-Feb-27	28-Sep-26	21-Oct-26	0%	0%
PORTABLE WATER IN (PH2-G-MCZ0)		174	19-Jan-27	26-May-27	13-Aug-26	25-Oct-26	0%	54.09%
Pipes Work		173	15-Mar-27	26-May-27	13-Aug-26	25-Oct-26	0%	56.56%
bedding Works		19	15-Mar-27	05-Apr-27	26-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-PW-ZA-2640	Sand bedding for PW HDPE Pipes 315 mm	19	15-Mar-27	05-Apr-27	26-Aug-26	28-Sep-26	0%	50%
Pipes Laying		16	06-Apr-27	24-Apr-27	13-Aug-26	28-Sep-26	0%	95%
SDR-2-CON-PW-ZA-2570	Install PW 315 mm HDPE Pipe	16	06-Apr-27	24-Apr-27	13-Aug-26	28-Sep-26	0%	95%
Testing		6	25-Apr-27	01-May-27	29-Sep-26	05-Oct-26	0%	0%
SDR-2-CON-PW-ZA-2630	Testing of PW HDPE Pipe 315 mm.	6	25-Apr-27	01-May-27	29-Sep-26	05-Oct-26	0%	0%
Backfilling		17	02-May-27	26-May-27	06-Oct-26	25-Oct-26	0%	0%
SDR-2-CON-PW-ZA-2650	Backfilling of PW HDPE Pipe 315 mm.	17	02-May-27	26-May-27	06-Oct-26	25-Oct-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	19-Jan-27	11-Feb-27	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	19-Jan-27	11-Feb-27	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-PW-ZA-4030	Excavation for Valve Chambers Section 1	21	19-Jan-27	11-Feb-27	28-Sep-26	21-Oct-26	0%	0%
Electrical Works		169	07-Jul-26	20-Jan-27	01-Jul-26 A	02-Nov-26	22.4%	30.02%
ZONE A		138	07-Jul-26	17-Dec-26	01-Jul-26 A	01-Nov-26	31.63%	33.97%
Street Lighting Network		115	07-Jul-26	13-Dec-26	01-Jul-26 A	01-Nov-26	40.53%	31.19%
Street Lighting Network IN (PH2-COL-MC10)		44	07-Jul-26	26-Aug-26	20-Jul-26 A	28-Sep-26	100%	50%
Excavation		44	07-Jul-26	26-Aug-26	20-Jul-26 A	28-Sep-26	100%	50%
SDR-2-CON-SL-ZA-3590	Excavation for LV Cable Drawpits	21	07-Jul-26	30-Jul-26	20-Jul-26 A	28-Sep-26	100%	80%
SDR-2-CON-SL-ZA-1000	Excavation for LV Cable Trenches	21	03-Aug-26	26-Aug-26	12-Aug-26	28-Sep-26	100%	20%
Street Lighting Network IN (PH2-COL-MC20)		92	13-Jul-26	19-Oct-26	01-Jul-26 A	28-Oct-26	69.84%	30%
Excavation		42	13-Jul-26	30-Aug-26	01-Jul-26 A	28-Sep-26	100%	60%
SDR-2-CON-SL-ZA-3600	Excavation for LV Cable Drawpits	21	13-Jul-26	05-Aug-26	01-Jul-26 A	28-Sep-26	100%	70%
SDR-2-CON-SL-ZA-2870	Excavation for LV Cable Trenches	21	06-Aug-26	30-Aug-26	13-Jul-26 A	28-Sep-26	100%	50%
Install Footings		21	31-Aug-26	24-Sep-26	03-Sep-26	04-Oct-26	100%	30%
SDR-2-CON-SL-ZA-2880	Install Footings	21	31-Aug-26	24-Sep-26	03-Sep-26	04-Oct-26	100%	30%
Backfilling		21	26-Sep-26	19-Oct-26	05-Oct-26	28-Oct-26	9.52%	0%
SDR-2-CON-SL-ZA-2900	Backfilling over LV Cables of Street lighting	21	26-Sep-26	19-Oct-26	05-Oct-26	28-Oct-26	9.52%	0%

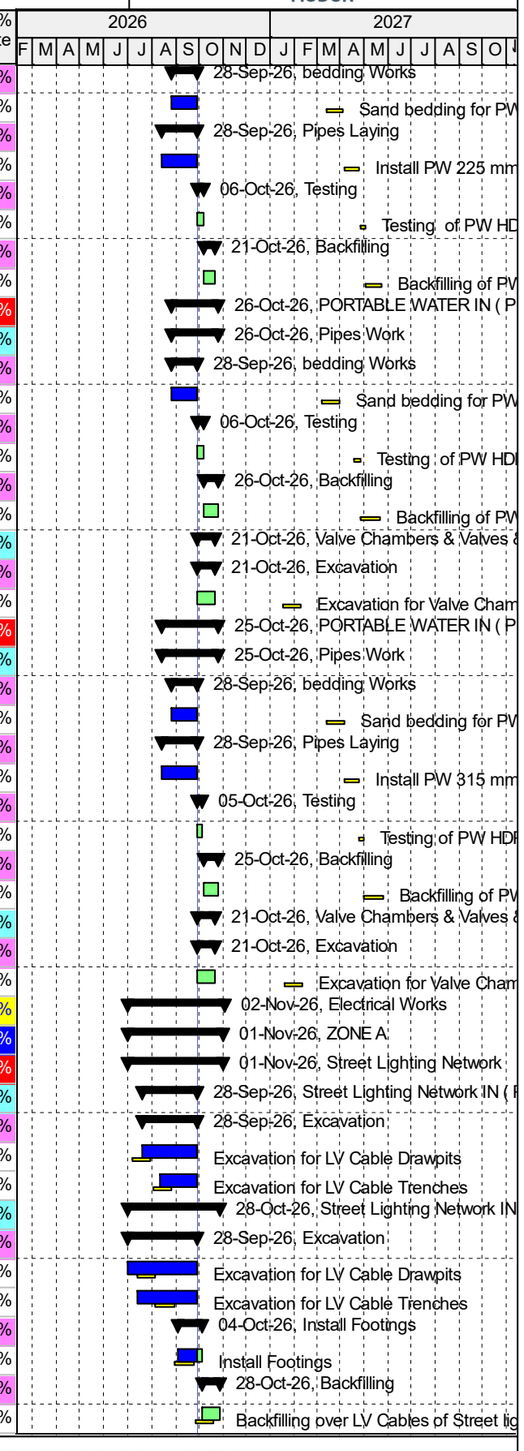

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Street Lighting Network IN (PH2-A-MCA0)		42	19-Jul-26	05-Sep-26	01-Aug-26	28-Sep-26	100%	57.5%
Excavation		42	19-Jul-26	05-Sep-26	01-Aug-26	28-Sep-26	100%	57.5%
SDR-2-CON-SL-ZA-3610	Excavation for LV Cable Drawpits	21	19-Jul-26	11-Aug-26	01-Aug-26	28-Sep-26	100%	65%
SDR-2-CON-SL-ZA-1300	Excavation for LV Cable Trenches	21	12-Aug-26	05-Sep-26	12-Aug-26	28-Sep-26	100%	50%
Street Lighting Network IN (PH2-A-MCB0)		79	25-Jul-26	31-Oct-26	04-Aug-26	25-Oct-26	53.97%	29.17%
Excavation		42	25-Jul-26	10-Sep-26	04-Aug-26	28-Sep-26	100%	57.5%
SDR-2-CON-SL-ZA-3620	Excavation for LV Cable Drawpits	21	25-Jul-26	17-Aug-26	04-Aug-26	28-Sep-26	100%	65%
SDR-2-CON-SL-ZA-2950	Excavation for LV Cable Trenches	21	18-Aug-26	10-Sep-26	12-Aug-26	28-Sep-26	100%	50%
Install Footings		21	12-Sep-26	06-Oct-26	31-Aug-26	30-Sep-26	61.9%	30%
SDR-2-CON-SL-ZA-2960	Install Footings	21	12-Sep-26	06-Oct-26	31-Aug-26	30-Sep-26	61.9%	30%
Backfilling		21	07-Oct-26	31-Oct-26	01-Oct-26	25-Oct-26	0%	0%
SDR-2-CON-SL-ZA-2980	Backfilling over LV Cables of Street lighting	21	07-Oct-26	31-Oct-26	01-Oct-26	25-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCC0)		77	30-Jul-26	05-Nov-26	20-Jul-26 A	28-Oct-26	46.03%	30.83%
Excavation		42	30-Jul-26	16-Sep-26	20-Jul-26 A	28-Sep-26	100%	62.5%
SDR-2-CON-SL-ZA-3630	Excavation for LV Cable Drawpits	21	30-Jul-26	23-Aug-26	20-Jul-26 A	28-Sep-26	100%	75%
SDR-2-CON-SL-ZA-2990	Excavation for LV Cable Trenches	21	24-Aug-26	16-Sep-26	01-Aug-26	28-Sep-26	100%	50%
Install Footings		21	17-Sep-26	12-Oct-26	03-Sep-26	04-Oct-26	38.1%	30%
SDR-2-CON-SL-ZA-3000	Install Footings	21	17-Sep-26	12-Oct-26	03-Sep-26	04-Oct-26	38.1%	30%
Backfilling		21	13-Oct-26	05-Nov-26	05-Oct-26	28-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3020	Backfilling over LV Cables of Street lighting	21	13-Oct-26	05-Nov-26	05-Oct-26	28-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCD0)		72	05-Aug-26	11-Nov-26	20-Jul-26 A	28-Oct-26	38.1%	33.33%
Excavation		42	05-Aug-26	22-Sep-26	20-Jul-26 A	28-Sep-26	100%	60%
SDR-2-CON-SL-ZA-3640	Excavation for LV Cable Drawpits	21	05-Aug-26	29-Aug-26	20-Jul-26 A	28-Sep-26	100%	70%
SDR-2-CON-SL-ZA-3030	Excavation for LV Cable Trenches	21	30-Aug-26	22-Sep-26	01-Aug-26	28-Sep-26	100%	50%
Install Footings		21	24-Sep-26	18-Oct-26	03-Sep-26	04-Oct-26	14.29%	40%
SDR-2-CON-SL-ZA-3040	Install Footings	21	24-Sep-26	18-Oct-26	03-Sep-26	04-Oct-26	14.29%	40%
Backfilling		21	19-Oct-26	11-Nov-26	05-Oct-26	28-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3060	Backfilling over LV Cables of Street lighting	21	19-Oct-26	11-Nov-26	05-Oct-26	28-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCE0)		67	11-Aug-26	17-Nov-26	02-Jul-26 A	28-Oct-26	31.75%	29.17%
Excavation		42	11-Aug-26	29-Sep-26	02-Jul-26 A	28-Sep-26	95.24%	57.5%
SDR-2-CON-SL-ZA-3650	Excavation for LV Cable Drawpits	21	11-Aug-26	03-Sep-26	02-Jul-26 A	28-Sep-26	100%	65%
SDR-2-CON-SL-ZA-3070	Excavation for LV Cable Trenches	21	05-Sep-26	29-Sep-26	14-Jul-26 A	28-Sep-26	90.48%	50%
Install Footings		21	30-Sep-26	24-Oct-26	03-Sep-26	04-Oct-26	0%	30%
SDR-2-CON-SL-ZA-3080	Install Footings	21	30-Sep-26	24-Oct-26	03-Sep-26	04-Oct-26	0%	30%
Backfilling		21	25-Oct-26	17-Nov-26	05-Oct-26	28-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3100	Backfilling over LV Cables of Street lighting	21	25-Oct-26	17-Nov-26	05-Oct-26	28-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCF0)		64	17-Aug-26	21-Nov-26	01-Jul-26 A	31-Oct-26	27.78%	29.17%
Excavation		42	17-Aug-26	05-Oct-26	01-Jul-26 A	07-Oct-26	83.33%	57.5%
SDR-2-CON-SL-ZA-3660	Excavation for LV Cable Drawpits	21	17-Aug-26	09-Sep-26	01-Jul-26 A	07-Oct-26	100%	65%
SDR-2-CON-SL-ZA-3110	Excavation for LV Cable Trenches	21	10-Sep-26	05-Oct-26	14-Jul-26 A	07-Oct-26	66.67%	50%
Install Footings		20	06-Oct-26	28-Oct-26	31-Aug-26	07-Oct-26	0%	30%
SDR-2-CON-SL-ZA-3120	Install Footings	20	06-Oct-26	28-Oct-26	31-Aug-26	07-Oct-26	0%	30%
Backfilling		20	29-Oct-26	21-Nov-26	08-Oct-26	31-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3140	Backfilling over LV Cables of Street lighting	20	29-Oct-26	21-Nov-26	08-Oct-26	31-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCG0)		62	23-Aug-26	25-Nov-26	06-Jul-26 A	29-Oct-26	23.81%	29.17%
Excavation		42	23-Aug-26	11-Oct-26	06-Jul-26 A	07-Oct-26	71.43%	57.5%
SDR-2-CON-SL-ZA-3670	Excavation for LV Cable Drawpits	21	23-Aug-26	15-Sep-26	06-Jul-26 A	07-Oct-26	100%	65%

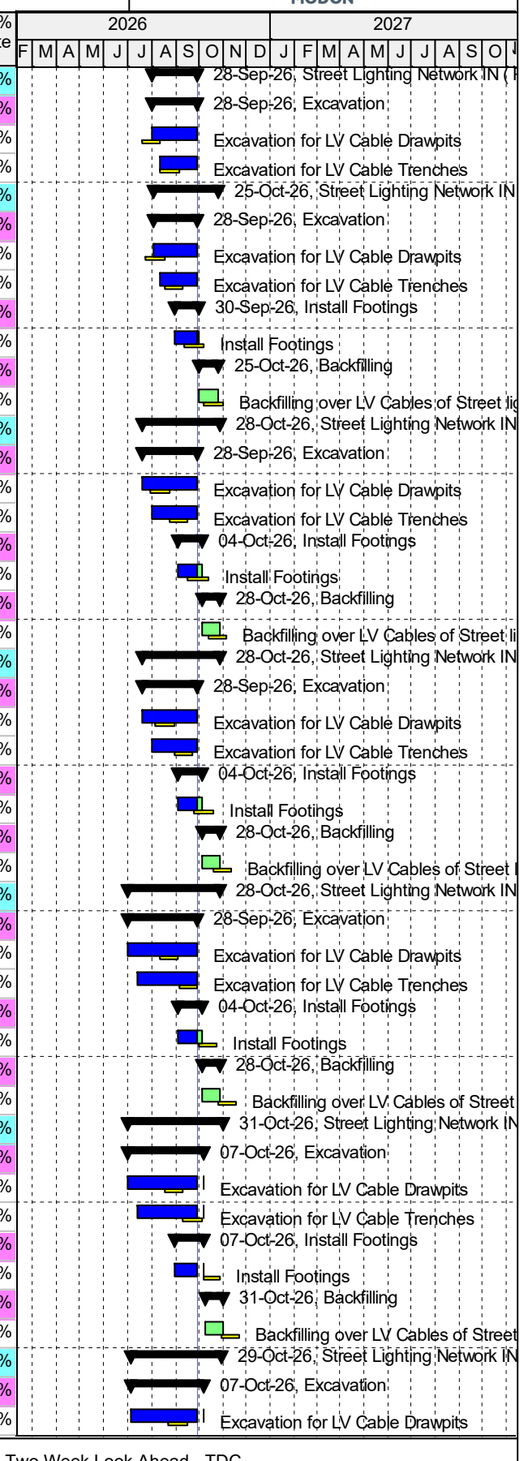

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-SL-ZA-3150	Excavation for LV Cable Trenches	21	16-Sep-26	11-Oct-26	16-Jul-26 A	07-Oct-26	42.86%	50%
Install Footings		20	12-Oct-26	03-Nov-26	03-Sep-26	07-Oct-26	0%	30%
SDR-2-CON-SL-ZA-3160	Install Footings	20	12-Oct-26	03-Nov-26	03-Sep-26	07-Oct-26	0%	30%
Backfilling		19	04-Nov-26	25-Nov-26	08-Oct-26	29-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3180	Backfilling over LV Cables of Street lighting	19	04-Nov-26	25-Nov-26	08-Oct-26	29-Oct-26	0%	0%
Street Lighting Network IN (PH2-A-MCH0)		62	30-Aug-26	02-Dec-26	20-Jul-26 A	29-Oct-26	19.05%	29.17%
Excavation		42	30-Aug-26	18-Oct-26	20-Jul-26 A	07-Oct-26	57.14%	57.5%
SDR-2-CON-SL-ZA-3680	Excavation for LV Cable Drawpits	21	30-Aug-26	22-Sep-26	20-Jul-26 A	07-Oct-26	100%	65%
SDR-2-CON-SL-ZA-3190	Excavation for LV Cable Trenches	21	24-Sep-26	18-Oct-26	01-Aug-26	07-Oct-26	14.29%	50%
Install Footings		20	19-Oct-26	10-Nov-26	03-Sep-26	07-Oct-26	0%	30%
SDR-2-CON-SL-ZA-3200	Install Footings	20	19-Oct-26	10-Nov-26	03-Sep-26	07-Oct-26	0%	30%
Backfilling		19	11-Nov-26	02-Dec-26	08-Oct-26	29-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3220	Backfilling over LV Cables of Street lighting	19	11-Nov-26	02-Dec-26	08-Oct-26	29-Oct-26	0%	0%
Street Lighting Network IN (PH2-ART-MC10)		63	06-Sep-26	13-Dec-26	20-Jul-26 A	01-Nov-26	14.29%	30%
Excavation		42	06-Sep-26	25-Oct-26	20-Jul-26 A	07-Oct-26	42.86%	60%
SDR-2-CON-SL-ZA-3690	Excavation for LV Cable Drawpits	21	06-Sep-26	30-Sep-26	20-Jul-26 A	07-Oct-26	85.71%	70%
SDR-2-CON-SL-ZA-2910	Excavation for LV Cable Trenches	21	01-Oct-26	25-Oct-26	01-Aug-26	07-Oct-26	0%	50%
Install Footings		21	26-Oct-26	18-Nov-26	03-Sep-26	07-Oct-26	0%	30%
SDR-2-CON-SL-ZA-2920	Install Footings	21	26-Oct-26	18-Nov-26	03-Sep-26	07-Oct-26	0%	30%
Backfilling		21	19-Nov-26	13-Dec-26	08-Oct-26	01-Nov-26	0%	0%
SDR-2-CON-SL-ZA-2940	Backfilling over LV Cables of Street lighting	21	19-Nov-26	13-Dec-26	08-Oct-26	01-Nov-26	0%	0%
Lighting Pole Panels		21	12-Sep-26	06-Oct-26	08-Oct-26	01-Nov-26	61.9%	0%
Excavation		21	12-Sep-26	06-Oct-26	08-Oct-26	01-Nov-26	61.9%	0%
SDR-2-CON-SL-ZA-2650	Street Lighting Panels Excavation	21	12-Sep-26	06-Oct-26	08-Oct-26	01-Nov-26	61.9%	0%
Ring Main Unit		20	12-Sep-26	05-Oct-26	08-Oct-26	31-Oct-26	65%	0%
Leveling		20	12-Sep-26	05-Oct-26	08-Oct-26	31-Oct-26	65%	0%
SDR-2-CON-SL-ZA-2660	Ring Main Unit leveling	20	12-Sep-26	05-Oct-26	08-Oct-26	31-Oct-26	65%	0%
MV Network		72	09-Aug-26	21-Nov-26	14-Jul-26 A	01-Nov-26	31.82%	35.18%
LOOP 3		72	09-Aug-26	14-Nov-26	14-Jul-26 A	01-Nov-26	30.48%	28%
Excavation		21	09-Aug-26	01-Sep-26	14-Jul-26 A	28-Sep-26	100%	70%
SDR-2-CON-MV-ZA-1000	Excavation Works	21	09-Aug-26	01-Sep-26	14-Jul-26 A	28-Sep-26	100%	70%
Pipe laying		20	02-Sep-26	26-Sep-26	25-Jul-26 A	28-Sep-26	100%	70%
SDR-2-CON-MV-ZA-1070	Pipe Laying	20	02-Sep-26	26-Sep-26	25-Jul-26 A	28-Sep-26	100%	70%
Backfilling		21	27-Sep-26	20-Oct-26	03-Aug-26	28-Sep-26	4.76%	70%
SDR-2-CON-MV-ZA-1150	Backfilling Works	21	27-Sep-26	20-Oct-26	03-Aug-26	28-Sep-26	4.76%	70%
Pulling Cable		21	21-Oct-26	14-Nov-26	08-Oct-26	01-Nov-26	0%	0%
SDR-2-CON-MV-ZA-1100	Pulling Cable	21	21-Oct-26	14-Nov-26	08-Oct-26	01-Nov-26	0%	0%
LOOP 4		54	20-Aug-26	02-Nov-26	25-Jul-26 A	22-Oct-26	51.19%	48.5%
Excavation		21	20-Aug-26	13-Sep-26	25-Jul-26 A	28-Sep-26	100%	70%
SDR-2-CON-MV-ZA-1160	Excavation Works	21	20-Aug-26	13-Sep-26	25-Jul-26 A	28-Sep-26	100%	70%
Pipe laying		21	14-Sep-26	08-Oct-26	13-Aug-26	28-Sep-26	52.38%	62%
SDR-2-CON-MV-ZA-1170	Pipe Laying	21	14-Sep-26	08-Oct-26	13-Aug-26	28-Sep-26	52.38%	62%
Backfilling		21	10-Oct-26	02-Nov-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-MV-ZA-1190	Backfilling Works	21	10-Oct-26	02-Nov-26	29-Sep-26	22-Oct-26	0%	0%
LOOP 5		45	31-Aug-26	12-Nov-26	13-Aug-26	22-Oct-26	29.76%	37.5%
Excavation		21	31-Aug-26	24-Sep-26	13-Aug-26	28-Sep-26	100%	50%
SDR-2-CON-MV-ZA-1200	Excavation Works	21	31-Aug-26	24-Sep-26	13-Aug-26	28-Sep-26	100%	50%

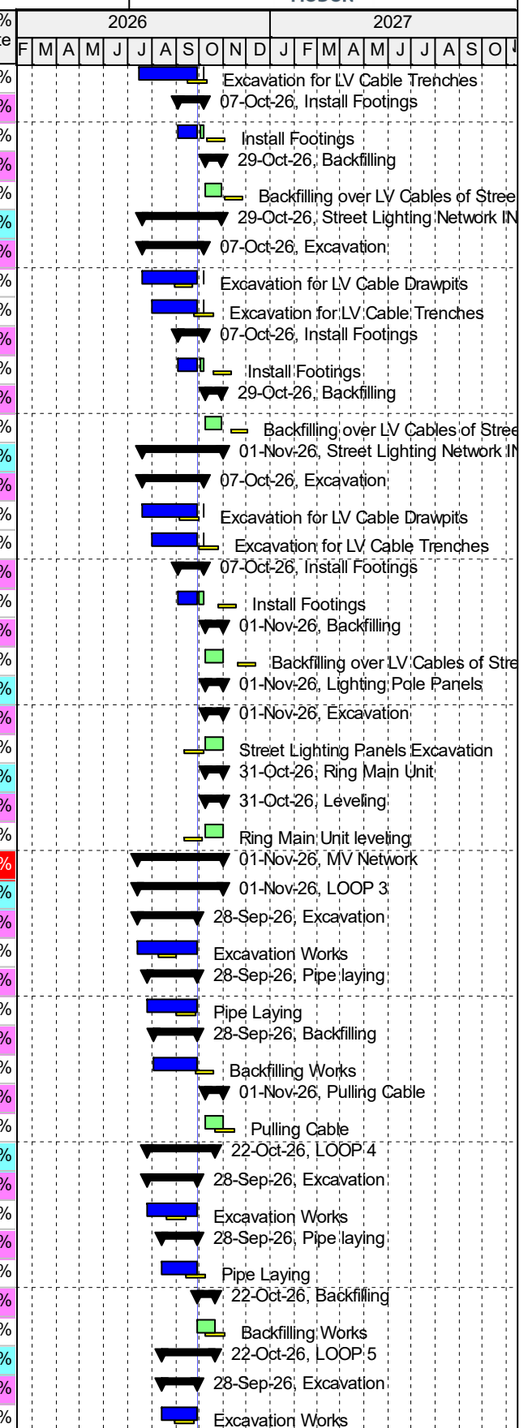


© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Pipe laying		21	26-Sep-26	19-Oct-26	13-Aug-26	28-Sep-26	9.52%	50%
SDR-2-CON-MV-ZA-1210	Pipe Laying	21	26-Sep-26	19-Oct-26	13-Aug-26	28-Sep-26	9.52%	50%
Backfilling		21	20-Oct-26	12-Nov-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-MV-ZA-1230	Backfilling Works	21	20-Oct-26	12-Nov-26	29-Sep-26	22-Oct-26	0%	0%
LOOP 6		41	09-Sep-26	21-Nov-26	13-Aug-26	22-Oct-26	17.86%	37.5%
Excavation		21	09-Sep-26	04-Oct-26	13-Aug-26	28-Sep-26	71.43%	50%
SDR-2-CON-MV-ZA-1240	Excavation Works	21	09-Sep-26	04-Oct-26	13-Aug-26	28-Sep-26	71.43%	50%
Pipe laying		20	05-Oct-26	27-Oct-26	13-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-MV-ZA-1250	Pipe Laying	20	05-Oct-26	27-Oct-26	13-Aug-26	28-Sep-26	0%	50%
Backfilling		21	28-Oct-26	21-Nov-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-MV-ZA-1270	Backfilling Works	21	28-Oct-26	21-Nov-26	29-Sep-26	22-Oct-26	0%	0%
TELECOMMUNICATIONS Works		94	27-Aug-26	17-Dec-26	09-Jul-26 A	01-Nov-26	9.98%	30.62%
TELECOMMUNICATION IN (PH2-COL-MC10)		40	27-Aug-26	13-Oct-26	13-Sep-26	14-Oct-26	55.82%	35.01%
Ducts		21	27-Aug-26	20-Sep-26	13-Sep-26	13-Oct-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	13-Sep-26	13-Oct-26	100%	50%
SDR-2-CON-TE-ZA-4560	Excavation for telecom crossing ducts	21	27-Aug-26	20-Sep-26	13-Sep-26	13-Oct-26	100%	50%
Manholes		19	21-Sep-26	13-Oct-26	15-Sep-26	14-Oct-26	26.32%	25%
Bedding Work		19	21-Sep-26	13-Oct-26	15-Sep-26	14-Oct-26	26.32%	25%
SDR-2-CON-TE-ZA-1850	Sand bedding for Telecom Manhole	19	21-Sep-26	13-Oct-26	15-Sep-26	14-Oct-26	26.32%	25%
TELECOMMUNICATION IN (PH2-COL-MC20)		61	02-Sep-26	07-Dec-26	14-Jul-26 A	22-Oct-26	13.28%	37.26%
Ducts		61	02-Sep-26	07-Dec-26	14-Jul-26 A	22-Oct-26	10%	28.5%
Excavation		21	02-Sep-26	27-Sep-26	14-Jul-26 A	28-Sep-26	100%	75%
SDR-2-CON-TE-ZA-3210	Excavation for telecom crossing ducts & trenches	21	02-Sep-26	27-Sep-26	14-Jul-26 A	28-Sep-26	100%	75%
Pipe laying		20	28-Sep-26	20-Oct-26	21-Jul-26 A	28-Sep-26	0%	70%
SDR-2-CON-TE-ZA-3220	HDPE Pipes for Telecom Installation	20	28-Sep-26	20-Oct-26	21-Jul-26 A	28-Sep-26	0%	70%
Backfilling		20	21-Oct-26	12-Nov-26	01-Aug-26	28-Sep-26	0%	70%
SDR-2-CON-TE-ZA-3230	Backfilling over HDPE Telecom Pipes	20	21-Oct-26	12-Nov-26	01-Aug-26	28-Sep-26	0%	70%
Pulling Cable		21	14-Nov-26	07-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3280	Pulling Cable	21	14-Nov-26	07-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		61	02-Sep-26	29-Nov-26	03-Sep-26	20-Oct-26	18.75%	51.87%
Excavation		21	02-Sep-26	27-Sep-26	03-Sep-26	04-Oct-26	100%	95%
SDR-2-CON-TE-ZA-3240	Excavation for Telecom Manholes	21	02-Sep-26	27-Sep-26	03-Sep-26	04-Oct-26	100%	95%
Bedding Work		20	28-Sep-26	20-Oct-26	05-Sep-26	04-Oct-26	0%	25%
SDR-2-CON-TE-ZA-3290	Sand bedding for Telecom Manhole	20	28-Sep-26	20-Oct-26	05-Sep-26	04-Oct-26	0%	25%
Install Manholes		20	21-Oct-26	12-Nov-26	03-Sep-26	04-Oct-26	0%	55%
SDR-2-CON-TE-ZA-3250	Installation of Telecom Manhole	20	21-Oct-26	12-Nov-26	03-Sep-26	04-Oct-26	0%	55%
Testting		14	14-Nov-26	29-Nov-26	05-Oct-26	20-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3260	Telecom Manhole finishing works	14	14-Nov-26	29-Nov-26	05-Oct-26	20-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCA0)		47	06-Sep-26	24-Oct-26	01-Aug-26	01-Nov-26	37.35%	19.23%
Ducts		38	06-Sep-26	22-Oct-26	01-Aug-26	20-Oct-26	28.57%	20%
Excavation		21	06-Sep-26	30-Sep-26	01-Aug-26	28-Sep-26	85.71%	60%
SDR-2-CON-TE-ZA-3300	Excavation for telecom crossing ducts & trenches	21	06-Sep-26	30-Sep-26	01-Aug-26	28-Sep-26	85.71%	60%
Pipe laying		19	01-Oct-26	22-Oct-26	29-Sep-26	20-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3310	HDPE Pipes for Telecom Installation	19	01-Oct-26	22-Oct-26	29-Sep-26	20-Oct-26	0%	0%
Manholes		47	06-Sep-26	24-Oct-26	07-Sep-26	01-Nov-26	51.43%	18%
Excavation		21	06-Sep-26	30-Sep-26	07-Sep-26	08-Oct-26	85.71%	30%
SDR-2-CON-TE-ZA-3330	Excavation for Telecom Manholes	21	06-Sep-26	30-Sep-26	07-Sep-26	08-Oct-26	85.71%	30%

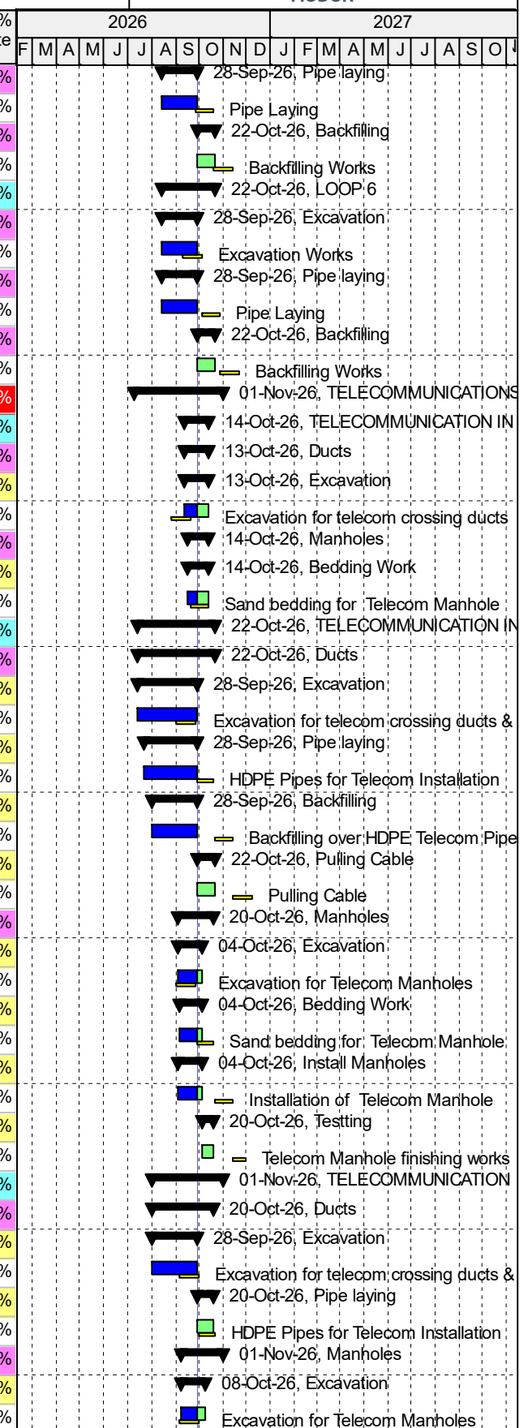

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Bedding Work		20	01-Oct-26	24-Oct-26	08-Oct-26	01-Nov-26	0%	0%
SDR-2-CON-TE-ZA-3380	Sand bedding for Telecom Manhole	20	01-Oct-26	24-Oct-26	08-Oct-26	01-Nov-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCB0)		35	12-Sep-26	31-Oct-26	08-Aug-26	22-Oct-26	31.88%	14.23%
Ducts		35	12-Sep-26	31-Oct-26	08-Aug-26	22-Oct-26	20.63%	8.33%
Excavation		21	12-Sep-26	06-Oct-26	08-Aug-26	28-Sep-26	61.9%	25%
SDR-2-CON-TE-ZA-3390	Excavation for telecom crossing ducts & trenches	21	12-Sep-26	06-Oct-26	08-Aug-26	28-Sep-26	61.9%	25%
Pipe laying		21	07-Oct-26	31-Oct-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3400	HDPE Pipes for Telecom Installation	21	07-Oct-26	31-Oct-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		21	12-Sep-26	06-Oct-26	13-Sep-26	14-Oct-26	61.9%	30%
Excavation		21	12-Sep-26	06-Oct-26	13-Sep-26	14-Oct-26	61.9%	30%
SDR-2-CON-TE-ZA-3420	Excavation for Telecom Manholes	21	12-Sep-26	06-Oct-26	13-Sep-26	14-Oct-26	61.9%	30%
TELECOMMUNICATION IN (PH2-A-MCC0)		41	17-Sep-26	28-Nov-26	20-Jul-26 A	26-Oct-26	13.77%	39.78%
Ducts		41	17-Sep-26	28-Nov-26	20-Jul-26 A	26-Oct-26	9.52%	31.25%
Excavation		21	17-Sep-26	12-Oct-26	20-Jul-26 A	28-Sep-26	38.1%	75%
SDR-2-CON-TE-ZA-3480	Excavation for telecom crossing ducts & trenches	21	17-Sep-26	12-Oct-26	20-Jul-26 A	28-Sep-26	38.1%	75%
Pipe laying		20	13-Oct-26	04-Nov-26	03-Sep-26	03-Oct-26	0%	25%
SDR-2-CON-TE-ZA-3490	HDPE Pipes for Telecom Installation	20	13-Oct-26	04-Nov-26	03-Sep-26	03-Oct-26	0%	25%
Backfilling		20	05-Nov-26	28-Nov-26	04-Oct-26	26-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3500	Backfilling over HDPE Telecom Pipes	20	05-Nov-26	28-Nov-26	04-Oct-26	26-Oct-26	0%	0%
Manholes		41	17-Sep-26	04-Nov-26	10-Sep-26	12-Oct-26	22.86%	58%
Excavation		21	17-Sep-26	12-Oct-26	10-Sep-26	12-Oct-26	38.1%	80%
SDR-2-CON-TE-ZA-3510	Excavation for Telecom Manholes	21	17-Sep-26	12-Oct-26	10-Sep-26	12-Oct-26	38.1%	80%
Bedding Work		20	13-Oct-26	04-Nov-26	10-Sep-26	12-Oct-26	0%	25%
SDR-2-CON-TE-ZA-3560	Sand bedding for Telecom Manhole	20	13-Oct-26	04-Nov-26	10-Sep-26	12-Oct-26	0%	25%
TELECOMMUNICATION IN (PH2-A-MCD0)		41	24-Sep-26	01-Dec-26	20-Jul-26 A	24-Oct-26	5.17%	35.95%
Ducts		41	24-Sep-26	01-Dec-26	20-Jul-26 A	24-Oct-26	3.57%	31.25%
Excavation		21	24-Sep-26	18-Oct-26	20-Jul-26 A	28-Sep-26	14.29%	75%
SDR-2-CON-TE-ZA-3570	Excavation for telecom crossing ducts & trenches	21	24-Sep-26	18-Oct-26	20-Jul-26 A	28-Sep-26	14.29%	75%
Pipe laying		20	19-Oct-26	10-Nov-26	03-Sep-26	03-Oct-26	0%	25%
SDR-2-CON-TE-ZA-3580	HDPE Pipes for Telecom Installation	20	19-Oct-26	10-Nov-26	03-Sep-26	03-Oct-26	0%	25%
Backfilling		18	11-Nov-26	01-Dec-26	04-Oct-26	24-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3590	Backfilling over HDPE Telecom Pipes	18	11-Nov-26	01-Dec-26	04-Oct-26	24-Oct-26	0%	0%
Manholes		41	24-Sep-26	10-Nov-26	10-Sep-26	15-Oct-26	8.57%	46%
Excavation		21	24-Sep-26	18-Oct-26	10-Sep-26	12-Oct-26	14.29%	60%
SDR-2-CON-TE-ZA-3600	Excavation for Telecom Manholes	21	24-Sep-26	18-Oct-26	10-Sep-26	12-Oct-26	14.29%	60%
Bedding Work		20	19-Oct-26	10-Nov-26	15-Sep-26	15-Oct-26	0%	25%
SDR-2-CON-TE-ZA-3650	Sand bedding for Telecom Manhole	20	19-Oct-26	10-Nov-26	15-Sep-26	15-Oct-26	0%	25%
TELECOMMUNICATION IN (PH2-A-MCE0)		39	29-Sep-26	06-Dec-26	14-Jul-26 A	22-Oct-26	0%	24.4%
Ducts		38	29-Sep-26	06-Dec-26	14-Jul-26 A	22-Oct-26	0%	31.25%
Excavation		21	29-Sep-26	22-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-3660	Excavation for telecom crossing ducts & trenches	21	29-Sep-26	22-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
Pipe laying		17	24-Oct-26	11-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
SDR-2-CON-TE-ZA-3670	HDPE Pipes for Telecom Installation	17	24-Oct-26	11-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
Backfilling		21	12-Nov-26	06-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3680	Backfilling over HDPE Telecom Pipes	21	12-Nov-26	06-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%

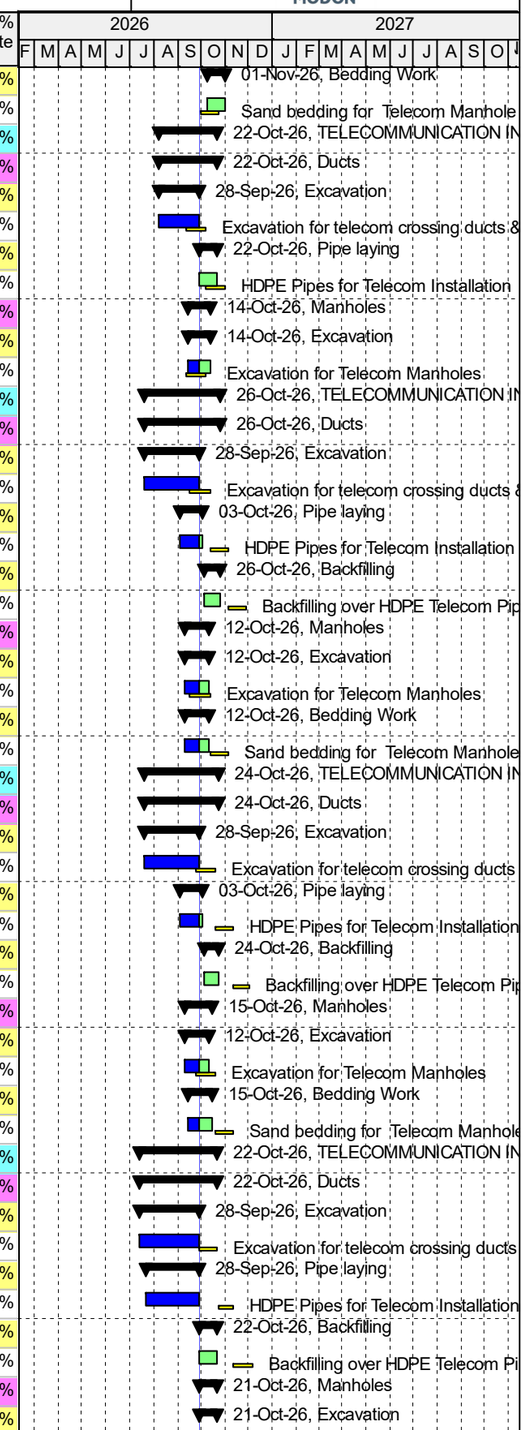

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-TE-ZA-3690	Excavation for Telecom Manholes	21	29-Sep-26	22-Oct-26	28-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCF0)		45	03-Oct-26	13-Dec-26	14-Jul-26 A	22-Oct-26	0%	24.4%
Ducts		44	03-Oct-26	13-Dec-26	14-Jul-26 A	22-Oct-26	0%	31.25%
Excavation		21	03-Oct-26	26-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-3750	Excavation for telecom crossing ducts & trenches	21	03-Oct-26	26-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
Pipe laying		20	27-Oct-26	18-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
SDR-2-CON-TE-ZA-3760	HDPE Pipes for Telecom Installation	20	27-Oct-26	18-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
Backfilling		21	19-Nov-26	13-Dec-26	29-Sep-26	22-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3770	Backfilling over HDPE Telecom Pipes	21	19-Nov-26	13-Dec-26	29-Sep-26	22-Oct-26	0%	0%
Manholes		21	03-Oct-26	26-Oct-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	03-Oct-26	26-Oct-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3780	Excavation for Telecom Manholes	21	03-Oct-26	26-Oct-26	28-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCG0)		48	06-Oct-26	15-Dec-26	14-Jul-26 A	21-Oct-26	0%	24.4%
Ducts		47	06-Oct-26	15-Dec-26	14-Jul-26 A	21-Oct-26	0%	31.25%
Excavation		21	06-Oct-26	29-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-3840	Excavation for telecom crossing ducts & trenches	21	06-Oct-26	29-Oct-26	14-Jul-26 A	28-Sep-26	0%	75%
Pipe laying		20	31-Oct-26	22-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
SDR-2-CON-TE-ZA-3850	HDPE Pipes for Telecom Installation	20	31-Oct-26	22-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
Backfilling		20	23-Nov-26	15-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3860	Backfilling over HDPE Telecom Pipes	20	23-Nov-26	15-Dec-26	29-Sep-26	21-Oct-26	0%	0%
Manholes		21	06-Oct-26	29-Oct-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	06-Oct-26	29-Oct-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3870	Excavation for Telecom Manholes	21	06-Oct-26	29-Oct-26	28-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-A-MCH0)		30	08-Oct-26	24-Nov-26	30-Jul-26 A	21-Oct-26	0%	19.4%
Ducts		29	08-Oct-26	24-Nov-26	30-Jul-26 A	21-Oct-26	0%	26.67%
Excavation		21	08-Oct-26	01-Nov-26	30-Jul-26 A	28-Sep-26	0%	80%
SDR-2-CON-TE-ZA-3930	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	30-Jul-26 A	28-Sep-26	0%	80%
Pipe laying		20	02-Nov-26	24-Nov-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3940	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	29-Sep-26	21-Oct-26	0%	0%
Manholes		21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-3960	Excavation for Telecom Manholes	21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-ART-MC00)		30	08-Oct-26	24-Nov-26	09-Jul-26 A	21-Oct-26	0%	16.98%
Ducts		29	08-Oct-26	24-Nov-26	09-Jul-26 A	21-Oct-26	0%	23.33%
Excavation		21	08-Oct-26	01-Nov-26	09-Jul-26 A	28-Sep-26	0%	70%
SDR-2-CON-TE-ZA-4020	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	09-Jul-26 A	28-Sep-26	0%	70%
Pipe laying		20	02-Nov-26	24-Nov-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4030	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	29-Sep-26	21-Oct-26	0%	0%
Manholes		21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4050	Excavation for Telecom Manholes	21	08-Oct-26	01-Nov-26	28-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-ART-MC10)		67	08-Oct-26	17-Dec-26	14-Jul-26 A	21-Oct-26	0%	44.11%
Ducts		49	08-Oct-26	17-Dec-26	14-Jul-26 A	21-Oct-26	0%	31.25%
Excavation		21	08-Oct-26	01-Nov-26	14-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-4110	Excavation for telecom crossing ducts & trenches	21	08-Oct-26	01-Nov-26	14-Jul-26 A	28-Sep-26	0%	75%
Pipe laying		20	02-Nov-26	24-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%
SDR-2-CON-TE-ZA-4120	HDPE Pipes for Telecom Installation	20	02-Nov-26	24-Nov-26	21-Jul-26 A	28-Sep-26	0%	25%

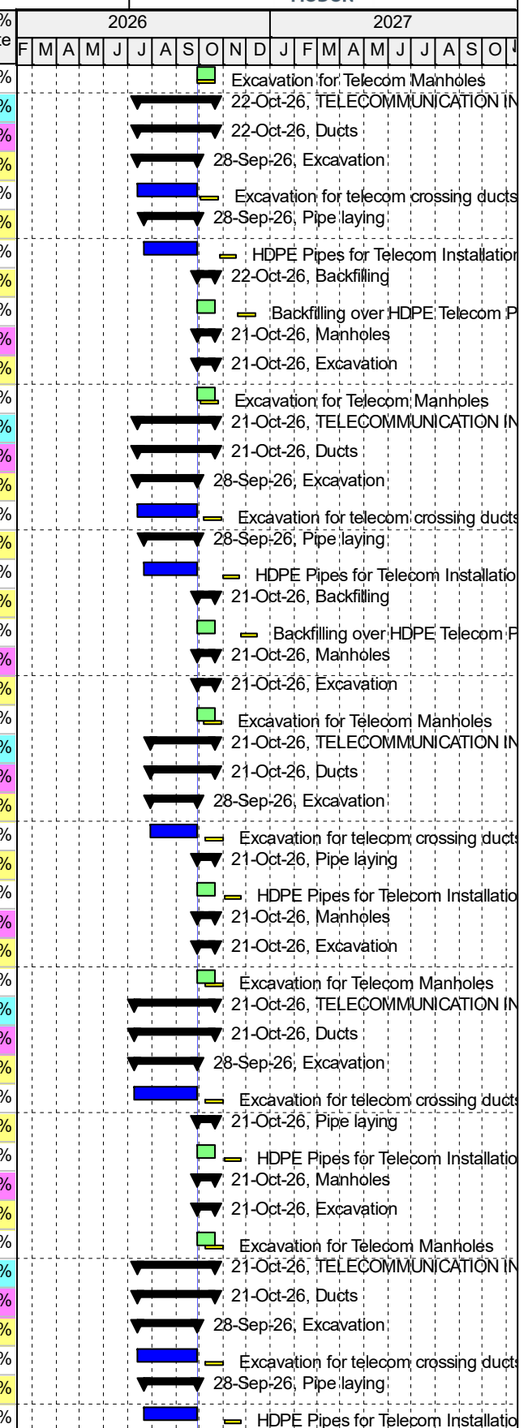

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Backfilling		20	25-Nov-26	17-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4130	Backfilling over HDPE Telecom Pipes	20	25-Nov-26	17-Dec-26	29-Sep-26	21-Oct-26	0%	0%
Manholes		59	08-Oct-26	15-Dec-26	12-Sep-26	14-Oct-26	0%	53.93%
Excavation		21	08-Oct-26	01-Nov-26	12-Sep-26	13-Oct-26	0%	85%
SDR-2-CON-TE-ZA-4140	Excavation for Telecom Manholes	21	08-Oct-26	01-Nov-26	12-Sep-26	13-Oct-26	0%	85%
Bedding Work		18	02-Nov-26	22-Nov-26	16-Sep-26	14-Oct-26	0%	25%
SDR-2-CON-TE-ZA-4190	Sand bedding for Telecom Manhole	18	02-Nov-26	22-Nov-26	16-Sep-26	14-Oct-26	0%	25%
Install Manholes		20	23-Nov-26	15-Dec-26	13-Sep-26	14-Oct-26	0%	50%
SDR-2-CON-TE-ZA-4150	Installation of Telecom Manhole	20	23-Nov-26	15-Dec-26	13-Sep-26	14-Oct-26	0%	50%
ZONE G		125	27-Aug-26	20-Jan-27	01-Jul-26 A	02-Nov-26	11.86%	25.51%
Street Lighting Network		112	12-Sep-26	20-Jan-27	01-Jul-26 A	21-Oct-26	2.84%	48.84%
Street Lighting IN (PH2-G-MCA0)		43	30-Sep-26	10-Dec-26	13-Aug-26	21-Oct-26	0%	45%
Excavation		21	30-Sep-26	24-Oct-26	13-Aug-26	28-Sep-26	0%	75%
SDR-2-CON-SL-ZA-3230	Excavation for LV Cable drawpits & trenches	21	30-Sep-26	24-Oct-26	13-Aug-26	28-Sep-26	0%	75%
Install Footings		21	25-Oct-26	17-Nov-26	13-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-SL-ZA-3240	Install Footings	21	25-Oct-26	17-Nov-26	13-Aug-26	28-Sep-26	0%	60%
Backfilling		20	18-Nov-26	10-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3260	Backfilling over LV Cables of Street lighting	20	18-Nov-26	10-Dec-26	29-Sep-26	21-Oct-26	0%	0%
Street Lighting IN (PH2-G-MCE0)		42	12-Sep-26	23-Nov-26	04-Jul-26 A	21-Oct-26	20.63%	45%
Excavation		21	12-Sep-26	06-Oct-26	04-Jul-26 A	28-Sep-26	61.9%	75%
SDR-2-CON-SL-ZA-3270	Excavation for LV Cable drawpits & trenches	21	12-Sep-26	06-Oct-26	04-Jul-26 A	28-Sep-26	61.9%	75%
Install Footings		21	07-Oct-26	31-Oct-26	13-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-SL-ZA-3280	Install Footings	21	07-Oct-26	31-Oct-26	13-Aug-26	28-Sep-26	0%	60%
Backfilling		20	01-Nov-26	23-Nov-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3300	Backfilling over LV Cables of Street lighting	20	01-Nov-26	23-Nov-26	29-Sep-26	21-Oct-26	0%	0%
Street Lighting IN (PH2-G-MCF0)		42	30-Sep-26	09-Dec-26	04-Jul-26 A	21-Oct-26	0%	45%
Excavation		21	30-Sep-26	24-Oct-26	04-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SL-ZA-3310	Excavation for LV Cable drawpits & trenches	21	30-Sep-26	24-Oct-26	04-Jul-26 A	28-Sep-26	0%	75%
Install Footings		20	25-Oct-26	16-Nov-26	13-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-SL-ZA-3320	Install Footings	20	25-Oct-26	16-Nov-26	13-Aug-26	28-Sep-26	0%	60%
Backfilling		20	17-Nov-26	09-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3340	Backfilling over LV Cables of Street lighting	20	17-Nov-26	09-Dec-26	29-Sep-26	21-Oct-26	0%	0%
Street Lighting IN (PH2-G-MCG0)		42	30-Sep-26	09-Dec-26	04-Jul-26 A	21-Oct-26	0%	46%
Excavation		21	30-Sep-26	24-Oct-26	04-Jul-26 A	28-Sep-26	0%	76%
SDR-2-CON-SL-ZA-3350	Excavation for LV Cable drawpits & trenches	21	30-Sep-26	24-Oct-26	04-Jul-26 A	28-Sep-26	0%	76%
Install Footings		20	25-Oct-26	16-Nov-26	13-Aug-26	28-Sep-26	0%	62%
SDR-2-CON-SL-ZA-3360	Install Footings	20	25-Oct-26	16-Nov-26	13-Aug-26	28-Sep-26	0%	62%
Backfilling		20	17-Nov-26	09-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3380	Backfilling over LV Cables of Street lighting	20	17-Nov-26	09-Dec-26	29-Sep-26	21-Oct-26	0%	0%
Street Lighting IN (PH2-G-MCZ0)		94	04-Oct-26	20-Jan-27	01-Jul-26 A	28-Sep-26	0%	53.5%
Excavation		21	04-Oct-26	27-Oct-26	01-Jul-26 A	28-Sep-26	0%	75%
SDR-2-CON-SL-ZA-3390	Excavation for LV Cable drawpits & trenches	21	04-Oct-26	27-Oct-26	01-Jul-26 A	28-Sep-26	0%	75%
Install Footings		21	28-Oct-26	21-Nov-26	13-Aug-26	28-Sep-26	0%	60%
SDR-2-CON-SL-ZA-3400	Install Footings	21	28-Oct-26	21-Nov-26	13-Aug-26	28-Sep-26	0%	60%
Backfilling		21	22-Nov-26	15-Dec-26	20-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-SL-ZA-3420	Backfilling over LV Cables of Street lighting	21	22-Nov-26	15-Dec-26	20-Jul-26 A	28-Sep-26	0%	50%
Install pole		21	28-Dec-26	20-Jan-27	30-Jul-26 A	28-Sep-26	0%	50%

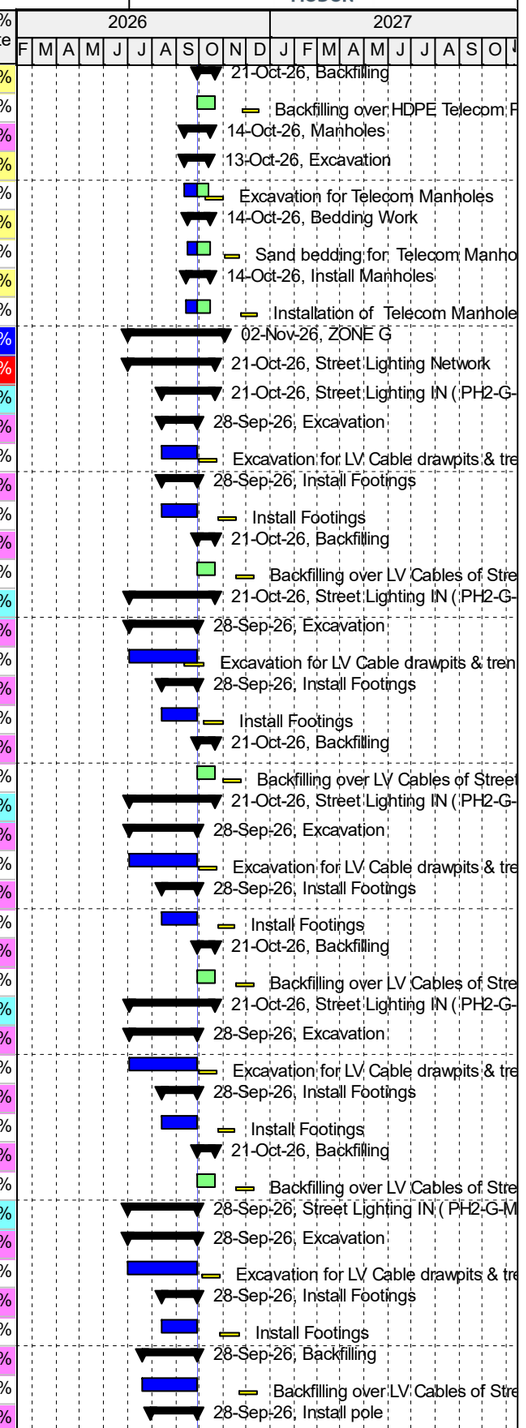

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-2-CON-SL-ZA-3410	Install Pole	21	28-Dec-26	20-Jan-27	30-Jul-26 A	28-Sep-26	0%	50%
Lighting Pole Panels		21	10-Oct-26	02-Nov-26	28-Sep-26	21-Oct-26	0%	0%
Excavation		21	10-Oct-26	02-Nov-26	28-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-SL-ZA-3430	Street Lighting Panels Excavation	21	10-Oct-26	02-Nov-26	28-Sep-26	21-Oct-26	0%	0%
MV Network		61	27-Aug-26	12-Dec-26	19-Jul-26 A	02-Nov-26	14.88%	17.5%
LOOP 1		57	27-Aug-26	03-Dec-26	19-Jul-26 A	02-Nov-26	14.76%	17.5%
Excavation		21	27-Aug-26	20-Sep-26	19-Jul-26 A	28-Sep-26	100%	50%
SDR-2-CON-MV-ZA-1280	Excavation Works	21	27-Aug-26	20-Sep-26	19-Jul-26 A	28-Sep-26	100%	50%
Pipe laying		21	21-Sep-26	15-Oct-26	04-Aug-26	28-Sep-26	23.81%	50%
SDR-2-CON-MV-ZA-1290	Pipe Laying	21	21-Sep-26	15-Oct-26	04-Aug-26	28-Sep-26	23.81%	50%
Backfilling		12	17-Oct-26	29-Oct-26	08-Aug-26	28-Sep-26	0%	25%
SDR-2-CON-MV-ZA-1310	Backfilling Works	12	17-Oct-26	29-Oct-26	08-Aug-26	28-Sep-26	0%	25%
Pulling Cable		20	11-Nov-26	03-Dec-26	11-Oct-26	02-Nov-26	0%	0%
SDR-2-CON-MV-ZA-1300	Pulling Cable	20	11-Nov-26	03-Dec-26	11-Oct-26	02-Nov-26	0%	0%
LOOP 2		61	27-Aug-26	12-Dec-26	01-Aug-26	02-Nov-26	15%	17.5%
Excavation		21	27-Aug-26	20-Sep-26	01-Aug-26	28-Sep-26	100%	50%
SDR-2-CON-MV-ZA-1320	Excavation Works	21	27-Aug-26	20-Sep-26	01-Aug-26	28-Sep-26	100%	50%
Pipe laying		20	21-Sep-26	14-Oct-26	04-Aug-26	28-Sep-26	25%	50%
SDR-2-CON-MV-ZA-1330	Pipe Laying	20	21-Sep-26	14-Oct-26	04-Aug-26	28-Sep-26	25%	50%
Backfilling		20	15-Oct-26	07-Nov-26	08-Aug-26	28-Sep-26	0%	25%
SDR-2-CON-MV-ZA-1350	Backfilling Works	20	15-Oct-26	07-Nov-26	08-Aug-26	28-Sep-26	0%	25%
Pulling Cable		20	19-Nov-26	12-Dec-26	11-Oct-26	02-Nov-26	0%	0%
SDR-2-CON-MV-ZA-1340	Pulling Cable	20	19-Nov-26	12-Dec-26	11-Oct-26	02-Nov-26	0%	0%
TELECOMMUNICATIONS Works		102	14-Sep-26	18-Jan-27	01-Jul-26 A	31-Oct-26	4.58%	45.94%
TELECOMMUNICATION IN (PH2-G-MCA0)		64	14-Sep-26	21-Dec-26	01-Jul-26 A	21-Oct-26	9.68%	34.89%
Ducts		39	14-Sep-26	22-Nov-26	01-Jul-26 A	21-Oct-26	13.1%	39%
Excavation		21	14-Sep-26	08-Oct-26	01-Jul-26 A	28-Sep-26	52.38%	52%
SDR-2-CON-TE-ZA-4200	Excavation for telecom crossing ducts & trenches	21	14-Sep-26	08-Oct-26	01-Jul-26 A	28-Sep-26	52.38%	52%
Pipe laying		18	10-Oct-26	29-Oct-26	13-Aug-26	28-Sep-26	0%	52%
SDR-2-CON-TE-ZA-4210	HDPE Pipes for Telecom Installation	18	10-Oct-26	29-Oct-26	13-Aug-26	28-Sep-26	0%	52%
Backfilling		20	31-Oct-26	22-Nov-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4220	Backfilling over HDPE Telecom Pipes	20	31-Oct-26	22-Nov-26	29-Sep-26	21-Oct-26	0%	0%
Manholes		64	14-Sep-26	21-Dec-26	15-Aug-26	21-Oct-26	7.86%	32.7%
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	53%
SDR-2-CON-TE-ZA-4230	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	53%
Bedding Work		17	10-Oct-26	28-Oct-26	24-Aug-26	28-Sep-26	0%	20%
SDR-2-CON-TE-ZA-4280	Sand bedding for Telecom Manhole	17	10-Oct-26	28-Oct-26	24-Aug-26	28-Sep-26	0%	20%
Install Manholes		19	29-Oct-26	19-Nov-26	15-Aug-26	28-Sep-26	0%	45%
SDR-2-CON-TE-ZA-4240	Installation of Telecom Manhole	19	29-Oct-26	19-Nov-26	15-Aug-26	28-Sep-26	0%	45%
Testting		7	21-Nov-26	28-Nov-26	02-Sep-26	28-Sep-26	0%	25%
SDR-2-CON-TE-ZA-4250	Telecom Manhole finishing works	7	21-Nov-26	28-Nov-26	02-Sep-26	28-Sep-26	0%	25%
Backfilling		20	29-Nov-26	21-Dec-26	29-Sep-26	21-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4260	Backfilling over Telecom Manhole	20	29-Nov-26	21-Dec-26	29-Sep-26	21-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCE0)		81	14-Sep-26	20-Dec-26	16-Jul-26 A	31-Oct-26	3.57%	43.39%
Ducts		60	10-Oct-26	17-Dec-26	16-Jul-26 A	28-Sep-26	0%	50%
Pipe laying		20	10-Oct-26	01-Nov-26	16-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4300	HDPE Pipes for Telecom Installation	20	10-Oct-26	01-Nov-26	16-Jul-26 A	28-Sep-26	0%	50%

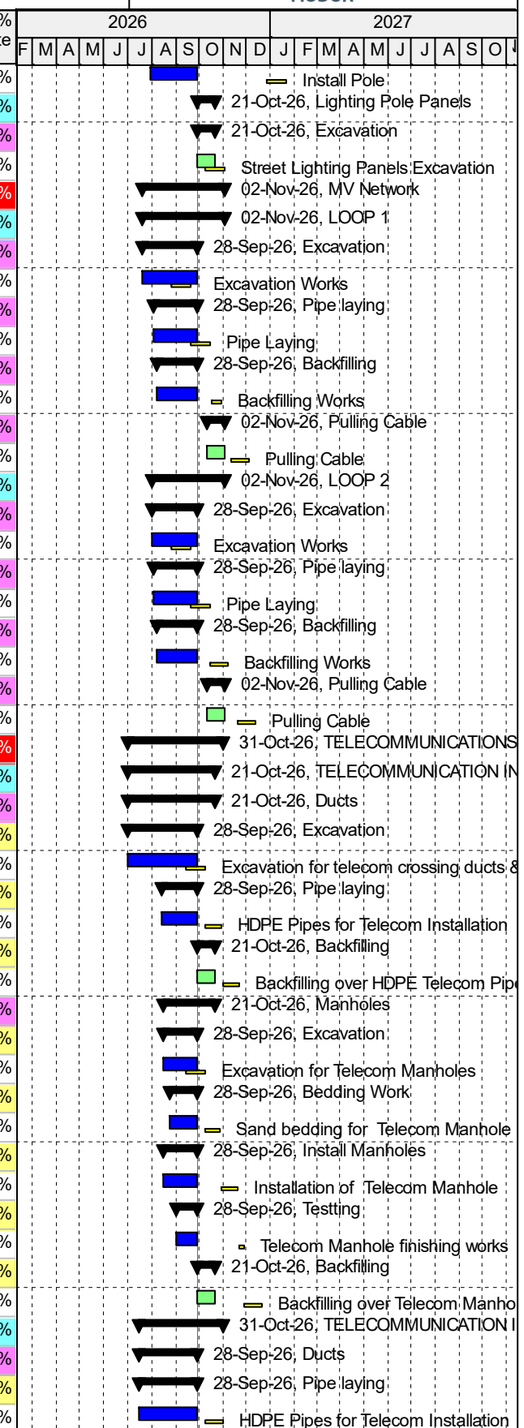

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Backfilling		20	02-Nov-26	24-Nov-26	20-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4310	Backfilling over HDPE Telecom Pipes	20	02-Nov-26	24-Nov-26	20-Jul-26 A	28-Sep-26	0%	50%
Pulling Cable		20	25-Nov-26	17-Dec-26	16-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4360	Pulling Cable	20	25-Nov-26	17-Dec-26	16-Jul-26 A	28-Sep-26	0%	50%
Manholes		55	14-Sep-26	20-Dec-26	15-Aug-26	31-Oct-26	7.86%	35.45%
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	53%
SDR-2-CON-TE-ZA-4320	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	53%
Bedding Work		15	10-Oct-26	26-Oct-26	17-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4370	Sand bedding for Telecom Manhole	15	10-Oct-26	26-Oct-26	17-Aug-26	28-Sep-26	0%	50%
Install Manholes		19	27-Oct-26	17-Nov-26	19-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4330	Installation of Telecom Manhole	19	27-Oct-26	17-Nov-26	19-Aug-26	28-Sep-26	0%	50%
Testting		7	18-Nov-26	25-Nov-26	29-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4340	Telecom Manhole finishing works	7	18-Nov-26	25-Nov-26	29-Sep-26	06-Oct-26	0%	0%
Backfilling		21	26-Nov-26	20-Dec-26	07-Oct-26	31-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4350	Backfilling over Telecom Manhole	21	26-Nov-26	20-Dec-26	07-Oct-26	31-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCF0)		90	10-Oct-26	18-Jan-27	06-Jul-26 A	29-Oct-26	0%	43.9%
Ducts		81	10-Oct-26	11-Jan-27	06-Jul-26 A	28-Sep-26	0%	50%
Excavation		21	10-Oct-26	02-Nov-26	06-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4380	Excavation for telecom crossing ducts & trenches	21	10-Oct-26	02-Nov-26	06-Jul-26 A	28-Sep-26	0%	50%
Pipe laying		19	03-Nov-26	24-Nov-26	16-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4390	HDPE Pipes for Telecom Installation	19	03-Nov-26	24-Nov-26	16-Jul-26 A	28-Sep-26	0%	50%
Backfilling		20	25-Nov-26	17-Dec-26	16-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4400	Backfilling over HDPE Telecom Pipes	20	25-Nov-26	17-Dec-26	16-Aug-26	28-Sep-26	0%	50%
Pulling Cable		21	19-Dec-26	11-Jan-27	16-Jul-26 A	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4450	Pulling Cable	21	19-Dec-26	11-Jan-27	16-Jul-26 A	28-Sep-26	0%	50%
Manholes		69	10-Oct-26	18-Jan-27	15-Aug-26	29-Oct-26	0%	35.75%
Excavation		21	10-Oct-26	02-Nov-26	15-Aug-26	28-Sep-26	0%	55%
SDR-2-CON-TE-ZA-4410	Excavation for Telecom Manholes	21	10-Oct-26	02-Nov-26	15-Aug-26	28-Sep-26	0%	55%
Bedding Work		20	03-Nov-26	25-Nov-26	17-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4460	Sand bedding for Telecom Manhole	20	03-Nov-26	25-Nov-26	17-Aug-26	28-Sep-26	0%	50%
Install Manholes		19	26-Nov-26	17-Dec-26	19-Aug-26	28-Sep-26	0%	50%
SDR-2-CON-TE-ZA-4420	Installation of Telecom Manhole	19	26-Nov-26	17-Dec-26	19-Aug-26	28-Sep-26	0%	50%
Testting		7	19-Dec-26	26-Dec-26	29-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4430	Telecom Manhole finishing works	7	19-Dec-26	26-Dec-26	29-Sep-26	06-Oct-26	0%	0%
Backfilling		20	27-Dec-26	18-Jan-27	07-Oct-26	29-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4440	Backfilling over Telecom Manhole	20	27-Dec-26	18-Jan-27	07-Oct-26	29-Oct-26	0%	0%
TELECOMMUNICATION IN (PH2-G-MCG0)		79	14-Sep-26	15-Dec-26	06-Jul-26 A	06-Oct-26	6.95%	58.74%
Ducts		79	14-Sep-26	15-Dec-26	06-Jul-26 A	28-Sep-26	5.24%	54.5%
Excavation		21	14-Sep-26	08-Oct-26	06-Jul-26 A	28-Sep-26	52.38%	50%
SDR-2-CON-TE-ZA-4470	Excavation for telecom crossing ducts & trenches	21	14-Sep-26	08-Oct-26	06-Jul-26 A	28-Sep-26	52.38%	50%
Pipe laying		18	10-Oct-26	29-Oct-26	15-Jul-26 A	28-Sep-26	0%	55%
SDR-2-CON-TE-ZA-4480	HDPE Pipes for Telecom Installation	18	10-Oct-26	29-Oct-26	15-Jul-26 A	28-Sep-26	0%	55%
Backfilling		20	31-Oct-26	22-Nov-26	16-Aug-26	28-Sep-26	0%	55%
SDR-2-CON-TE-ZA-4490	Backfilling over HDPE Telecom Pipes	20	31-Oct-26	22-Nov-26	16-Aug-26	28-Sep-26	0%	55%
Pulling Cable		20	23-Nov-26	15-Dec-26	14-Jul-26 A	28-Sep-26	0%	55%
SDR-2-CON-TE-ZA-4540	Pulling Cable	20	23-Nov-26	15-Dec-26	14-Jul-26 A	28-Sep-26	0%	55%
Manholes		56	14-Sep-26	26-Nov-26	15-Aug-26	06-Oct-26	9.82%	65.81%

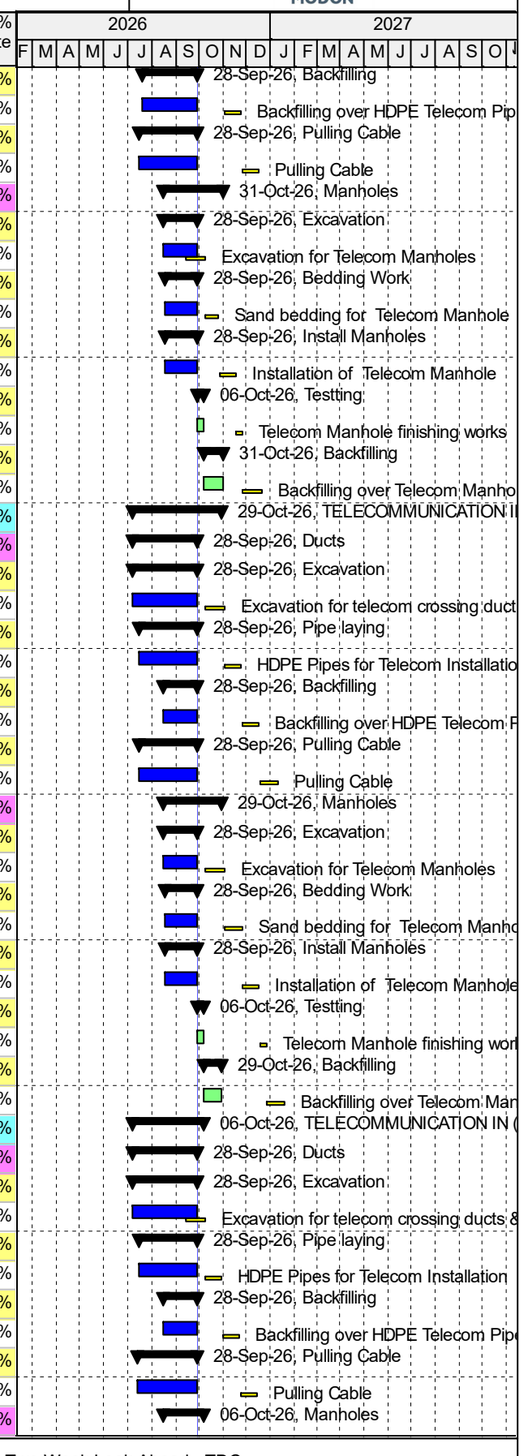

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Infrastructure Network Development Project in Sudair City for Industry and Business - Phase Two - Part Two

Two Week Look Ahead Plan - infra.

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	76%
SDR-2-CON-TE-ZA-4500	Excavation for Telecom Manholes	21	14-Sep-26	08-Oct-26	15-Aug-26	28-Sep-26	52.38%	76%
Bedding Work		15	10-Oct-26	26-Oct-26	17-Aug-26	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-4550	Sand bedding for Telecom Manhole	15	10-Oct-26	26-Oct-26	17-Aug-26	28-Sep-26	0%	75%
Install Manholes		20	27-Oct-26	18-Nov-26	19-Aug-26	28-Sep-26	0%	75%
SDR-2-CON-TE-ZA-4510	Installation of Telecom Manhole	20	27-Oct-26	18-Nov-26	19-Aug-26	28-Sep-26	0%	75%
Testting		7	19-Nov-26	26-Nov-26	29-Sep-26	06-Oct-26	0%	0%
SDR-2-CON-TE-ZA-4520	Telecom Manhole finishing works	7	19-Nov-26	26-Nov-26	29-Sep-26	06-Oct-26	0%	0%
CCTV Works		70	02-Sep-26	23-Nov-26	30-Jul-26 A	15-Oct-26	14.16%	30.18%
ZONE G		70	02-Sep-26	23-Nov-26	30-Jul-26 A	15-Oct-26	14.16%	30.18%
Poles 1st and 2nd Fix Works		37	02-Sep-26	06-Oct-26	30-Jul-26 A	15-Oct-26	30%	8%
Excavation		7	02-Sep-26	09-Sep-26	30-Jul-26 A	28-Sep-26	100%	50%
SDR-2-CON-CC-ZA-1670	Excavation 1Sst & 2nd Fix Works	7	02-Sep-26	09-Sep-26	30-Jul-26 A	28-Sep-26	100%	50%
Install Footings		7	10-Sep-26	17-Sep-26	03-Sep-26	28-Sep-26	100%	30%
SDR-2-CON-CC-ZA-1700	Install Footings	7	10-Sep-26	17-Sep-26	03-Sep-26	28-Sep-26	100%	30%
Backfilling		7	19-Sep-26	27-Sep-26	29-Sep-26	06-Oct-26	100%	0%
SDR-2-CON-CC-ZA-1720	Backfilling 1Sst & 2nd Fix Works	7	19-Sep-26	27-Sep-26	29-Sep-26	06-Oct-26	100%	0%
Install pole		8	28-Sep-26	06-Oct-26	07-Oct-26	15-Oct-26	0%	0%
SDR-2-CON-CC-ZA-1730	Install Pole	8	28-Sep-26	06-Oct-26	07-Oct-26	15-Oct-26	0%	0%
25m Pole Package		20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
Excavation		20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
SDR-2-CON-CC-ZA-1750	25 Meters Pole Excavation	20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
7m Pole Package		20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
Excavation		20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
SDR-2-CON-CC-ZA-1790	7m Meters Pole Excavation	20	07-Oct-26	29-Oct-26	03-Sep-26	15-Oct-26	0%	50%
35m Pole Package		21	31-Oct-26	23-Nov-26	03-Sep-26	15-Oct-26	0%	50%
Excavation		21	31-Oct-26	23-Nov-26	03-Sep-26	15-Oct-26	0%	50%
SDR-2-CON-CC-ZA-1830	35m Meters Pole Excavation	21	31-Oct-26	23-Nov-26	03-Sep-26	15-Oct-26	0%	50%

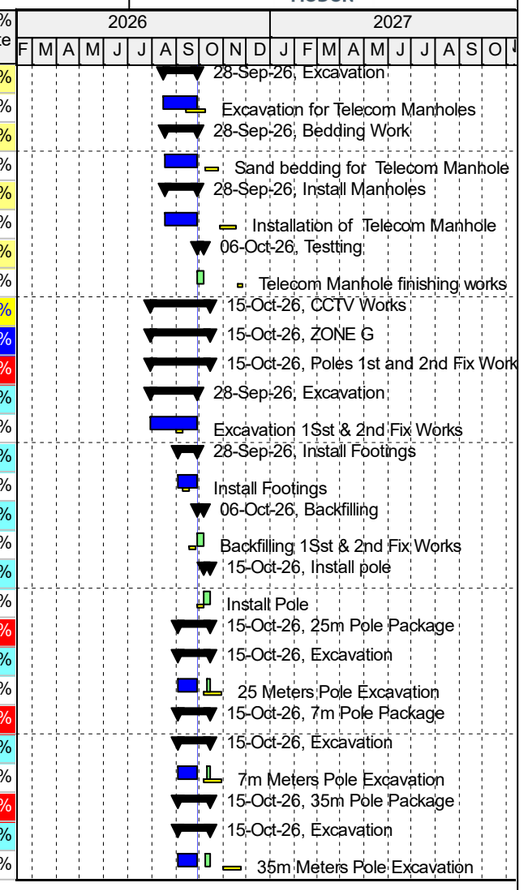

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone

TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation
