Playgrounds Initiative: Qassim Oasis, Hail and Tabuk Industrial City

مبادرة الملاعب بالمنطقة الوسطى (حائل, واحة القصيم, تبوك)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Advanced Construction & Contracting Co.	Egis	Bader Alrowaidan	17-Feb-2026	16-Dec-2026

Scope: playgrounds at three locations (Qassim Oasis, Hail and Tabuk Industrial City), with civil, architectural, electrical, mechanical and landscape works and general site works, including air domes at Qassim and Tabuk and a toilet building at each site.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (weekly report, Physical Progress sheet). At 25-Oct-2026 the project is 77.64% complete against 83.26% planned, behind by 5.62% (SPI 0.93). It gained 2.85% this week against 3.01% planned, so the gap widened slightly.

PHYSICAL % COMPLETE

77.64% / 83.26% plan

▼ SPI 0.93 5.62% behind plan

PROGRESS THIS WEEK

+2.85% / +3.01% plan

▼ 0.16% below the weekly plan

CONTRACT TIME ELAPSED

82.8% · day 250 of 302

▼ P6 finish 14-Feb-2027

INVOICED TO DATE (GROSS)

9.4% · 3.36M SAR

2 invoices, last period ends 30-Sep-2026

The schedule now finishes the project 60 days after the contract date.

The P6 update (data date 23-Oct-2026) and the weekly report both forecast handover on 14-Feb-2027 against the contract completion date of 16-Dec-2026, with −50.8 days of float; last week's report forecast 07-Feb-2027. 169 of the 300 open activities have negative float and 39 activities have failed to start. The air domes are furthest behind: Qassim 39.96% against 79.84% planned and Tabuk 35.13% against 74.55%.

Site photos this week

Six photos from the weekly report of 25-Oct-2026, stamped 22 and 24 Oct 2026 where the stamp is visible. Asphalt, curbs, fencing, hardscape and tank works continue at the three sites. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt core test, Tabuk

Core sample from the new asphalt. Stamped 24-Oct-2026, 09:50, Tabuk.



Asphalt work

Finished asphalt lane along the site fence. No date stamp.




Playground area, Qassim

Curbs and slab works. GPS-stamped 22-Oct-2026, 14:02, Buraydah.



Mesh and fence installation, Qassim

Fenced court beside the toilet building. GPS-stamped 22-Oct-2026, 14:00.

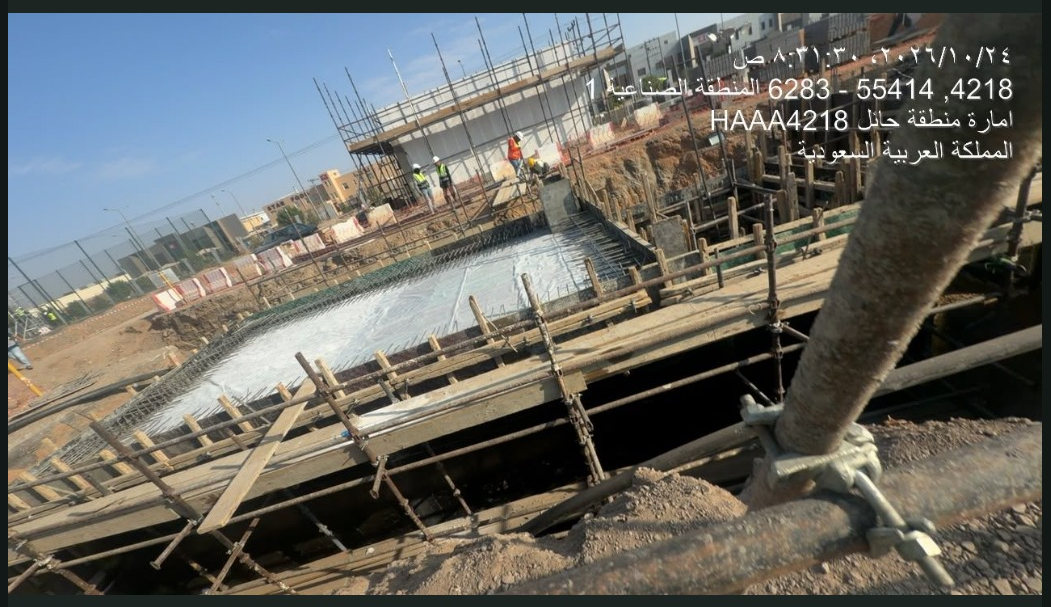

Concrete tank works, Hail

Formwork and reinforcement in place. Stamped 24-Oct-2026, 08:31, Hail region.




Hardscape works, Qassim

Circular slabs and curbs. GPS-stamped 22-Oct-2026, 14:02.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet of the weekly report.

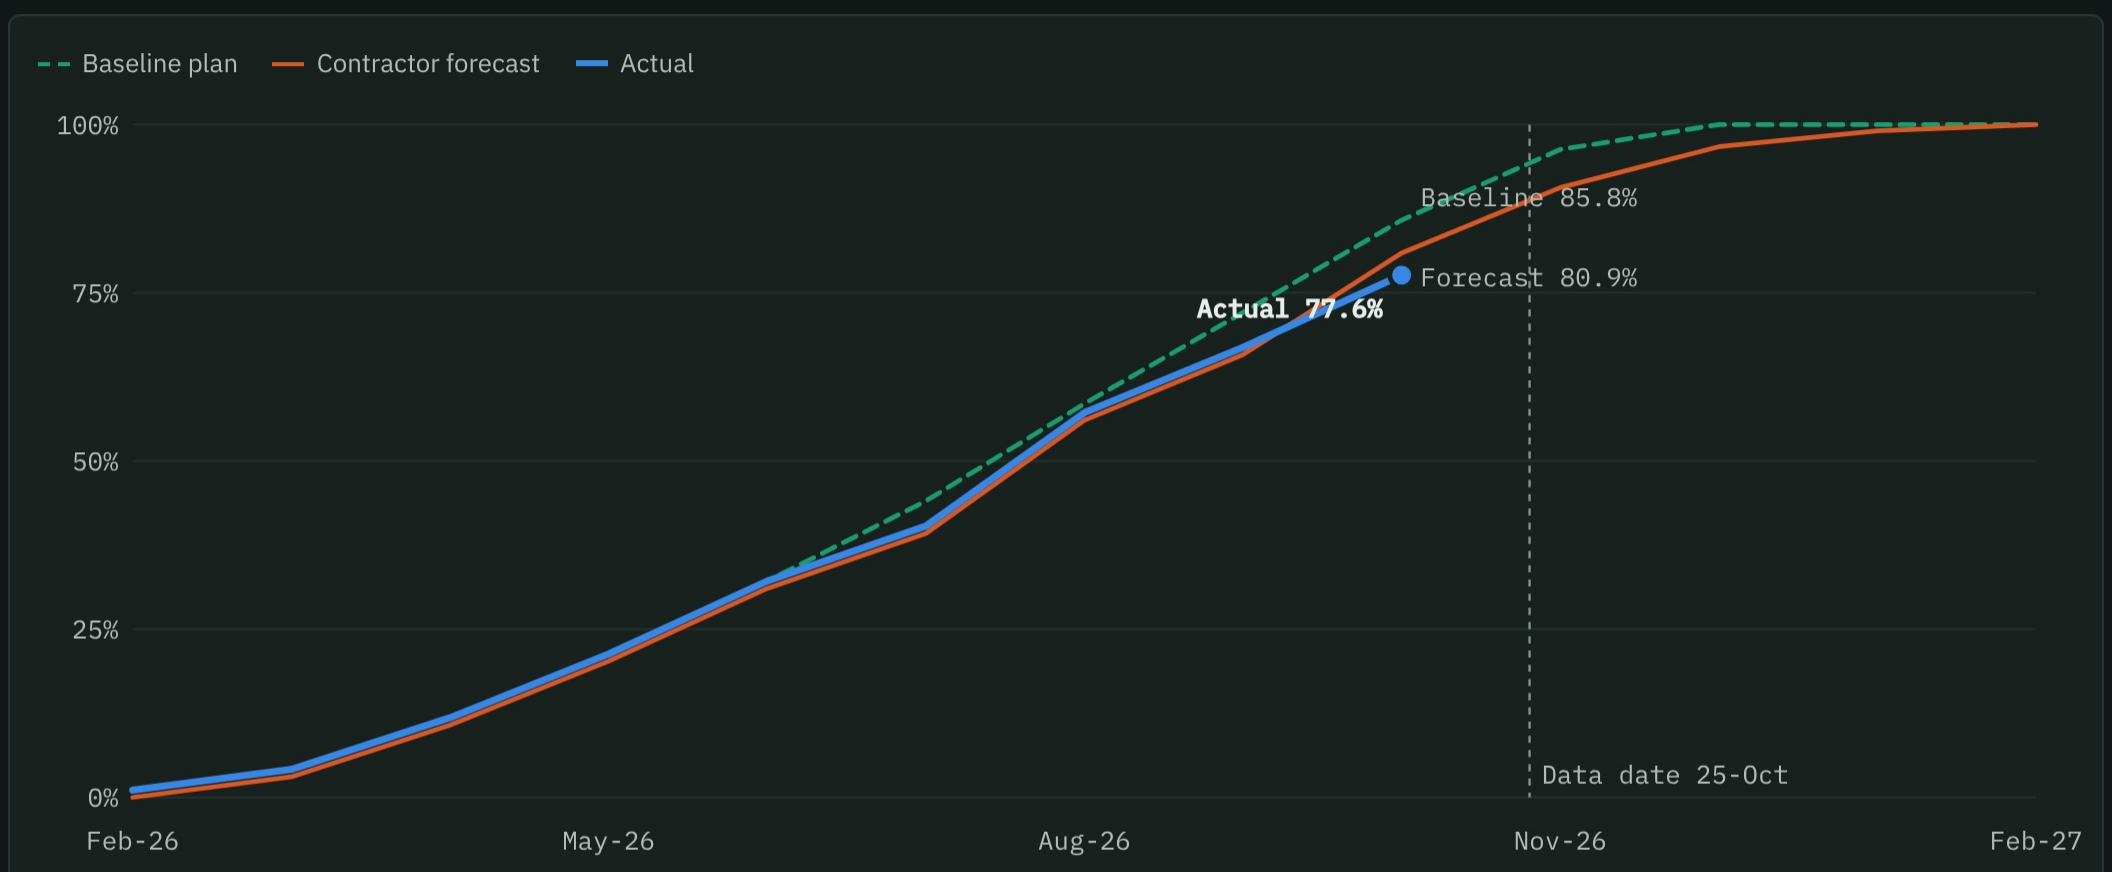

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
18-Oct-2026	80.25	74.79	−5.46	–	0.93
25-Oct-2026	**83.26**	**77.64**	**−5.62**	**+2.85**	**0.93**

Physical % complete from the weekly reports of 18 and 25 Oct 2026, the only two weekly reports uploaded so far. The monthly baseline in the chart reaches 85.82% at the end of October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (weekly report, Progress sheet). Engineering and procurement carry no man-hours in the report, so they are not shown.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Project milestone (management time)	**30.0%**	**81.66%**	**81.71%**	**+0.05%**	**1.00**	▲ Ahead
Construction	**66.6%**	**88.16%**	**79.05%**	**-9.11%**	**0.90**	▼ Behind
Qassim Oasis	24.3%	87.27%	78.50%	-8.76%	0.90	▼ Behind
Hail	17.9%	93.11%	80.57%	-12.54%	0.87	▼ Behind
Tabuk	24.3%	85.42%	78.48%	-6.94%	0.92	▼ Behind
Closeout	**3.5%**	**2.86%**	**15.28%**	**+12.41%**	**5.33**	▲ Ahead
Total	100%	**83.26%**	**77.64%**	**-5.62%**	**0.93**	▼ Behind

Within construction, the air domes are furthest behind: Qassim 446 of 1,116 man-hours earned against 891 planned, and Tabuk 392 against 832. The P6 update (data date 23-Oct-2026) has 1,929 activities: 1,629 completed, 220 in progress and 80 not started.

Scope of work: quantities

Total, finished and remaining quantity of the major items, all three sites together, from the Major Quantities sheet of the 25-Oct-2026 weekly report. The last column is the quantity planned to date. “This week” compares with the 18-Oct-2026 report.

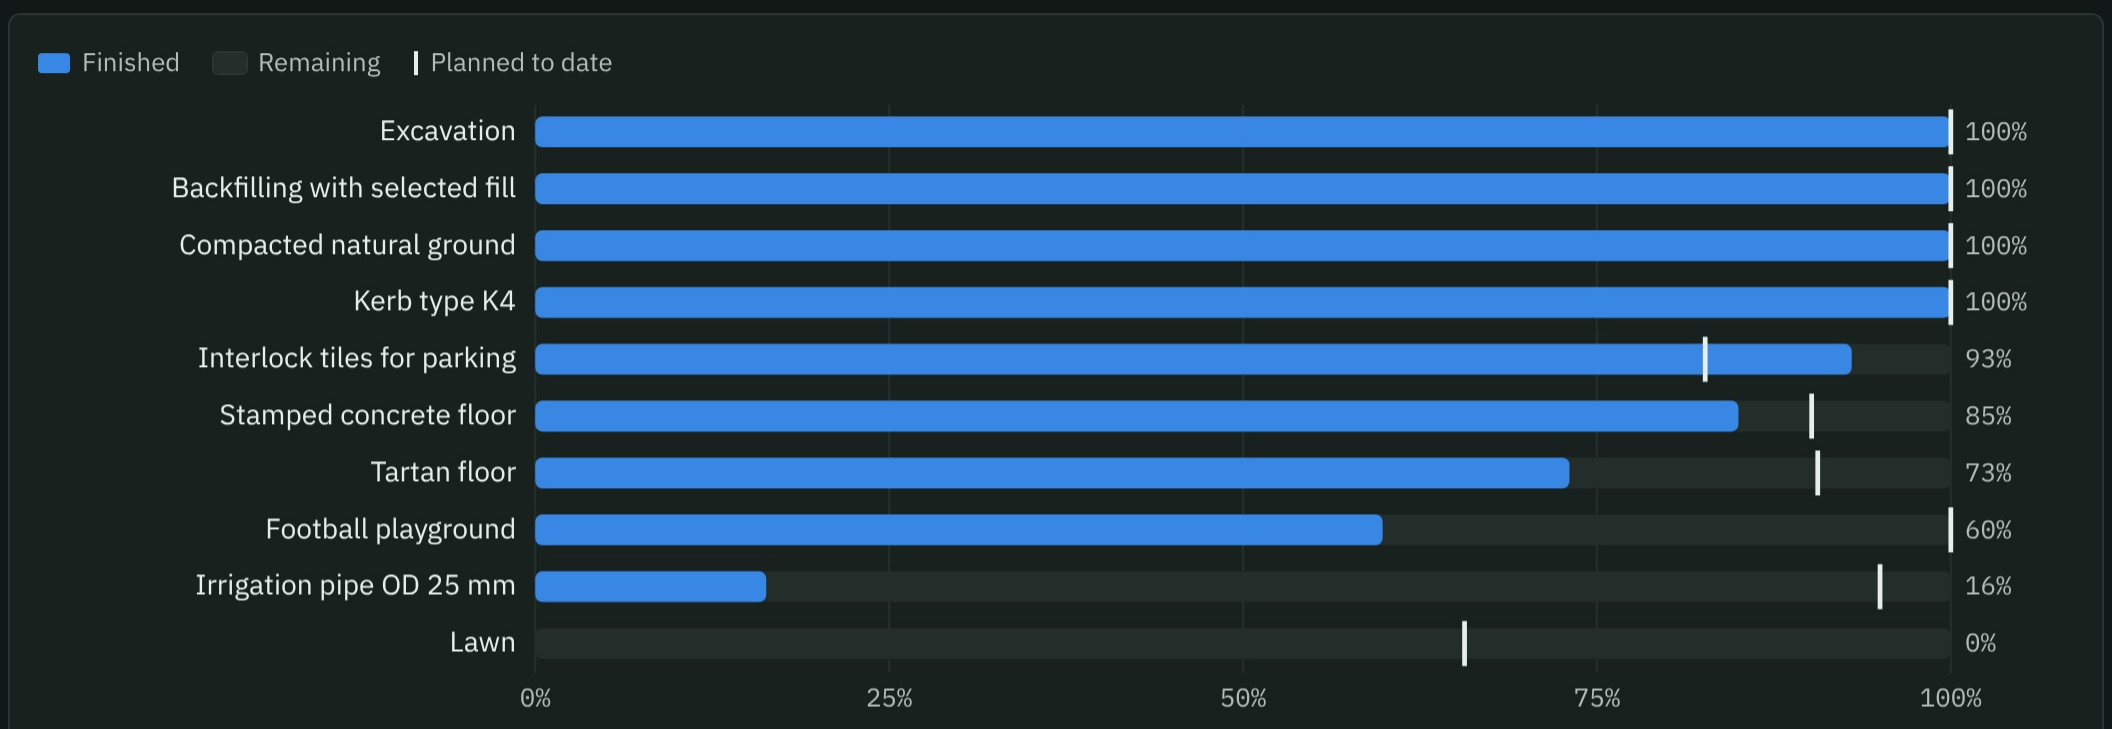

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Excavation	All	m³	29,400	29,400	0	0	100.0%	100.0%
Backfilling with selected fill	All	m³	29,400	29,400	0	0	100.0%	100.0%
Compacted natural ground	All	m²	33,300	33,300	0	0	100.0%	100.0%
Kerb type K4	All	LM	27,100	27,100	0	0	100.0%	100.0%
Interlock tiles for parking	All	m²	7,140	6,640	0	499.8	93.0%	82.7%
Stamped concrete floor	All	m²	7,800	6,630	0	1,170	85.0%	90.2%
Tartan floor	All	m²	10,950	8,000	0	2,950	73.1%	90.6%
Football playground	All	m²	7,350	4,400	0	2,950	59.9%	100.0%
Irrigation pipe OD 25 mm	All	m	11,100	1,812	0	9,288	16.3%	95.0%

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Lawn	All	m²	19,100	0	0	19,100	0.0%	65.6%

Reported this week

Irrigation main line, curbstone, core test for the asphalt in the football playground area, compaction test for the tartan, mesh and fence installation, plumbing in the toilets and asphalt work (weekly executive summary). Next week: compaction and levelling, asphalt, curbstone, stamped concrete, concrete for the septic and irrigation tanks and GRP tank installation.

Lawn, irrigation pipe and playgrounds lag

Lawn is at 0 of 12,539 m² planned to date, the 25 mm irrigation pipe at 1,812 of 10,545 m, the football playground at 4,400 of 7,350 m² and the tartan floor at 8,000 of 9,921 m². All major quantities are unchanged from the 18-Oct-2026 report.

Milestones

The weekly report's milestone sheet and the P6 update disagree on some dates. Both are shown so the difference can be resolved with the contractor. P6 float is from the update with data date 23-Oct-2026.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	17-Feb-2026	17-Feb-2026	17-Feb-2026 (actual)	–	✓ Done
Complete mobilisation	18-Mar-2026	14-Apr-2026	–	–	✓ Done late
Complete engineering	16-Aug-2026	25-Oct-2026 (+70 d)	–	–	▼ Late
Complete procurement	27-Aug-2026	25-Oct-2026 (+59 d)	–	–	▼ Late
Completion of toilet building	28-Oct-2026	–	05-Nov-2026	+13.2	▼ At risk
Completion of playground works	07-Dec-2026	–	14-Dec-2026	+2.6	▼ At risk
Complete construction	14-Dec-2026	28-Oct-2026 (−47 d)	30-Jan-2027	–	? Conflicts with P6
Completion of landscape works	16-Dec-2026	–	10-Jan-2027	−20.9	▼ Late
Complete all works, ready for initial handover	16-Dec-2026	09-Feb-2027 (+55 d)	14-Feb-2027	−50.8	▼ Late
Complete demobilisation	16-Dec-2026	13-Feb-2027 (+59 d)	–	–	▼ Late
Project handover	16-Dec-2026	14-Feb-2027 (+60 d)	14-Feb-2027	−50.8	▼ Late

The weekly report's “Complete construction” forecast of 28-Oct-2026 conflicts with P6.

P6 finishes the construction stage on 25-Jan-2027 at Qassim, 21-Dec-2026 at Hail and 30-Jan-2027 at Tabuk, and the project on 14-Feb-2027. The handover forecast moved from 07-Feb-2027 in last week's report to 14-Feb-2027. Of the contractual milestones, only the toilet building (+13.2 days) and the playground works (+2.6 days) keep positive float.

Procurement of key materials

Physical % complete of the open “delivery to site” activities with the lowest progress (P6 update, data date 23-Oct-2026). All other open delivery activities are at 90–95%.

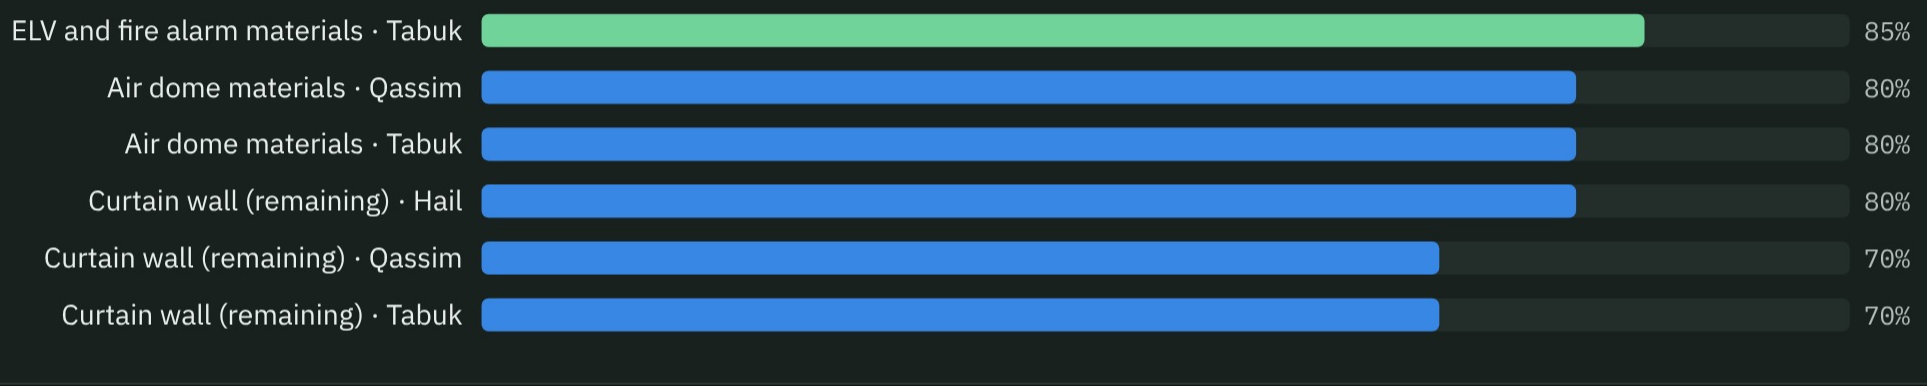

Air dome materials: 80% delivered


At both Qassim and Tabuk, with −50.8 and −49.0 days of float, the same order as project completion. The procurement log still shows the air dome purchase order as “under process” with a 150-day lead time.

Purchase orders and materials on site

The weekly report's procurement summary lists 57 materials: 33 purchase orders issued, 25 remaining and 8 materials on site. The curtain wall remainder is at 70% at Qassim and Tabuk and 80% at Hail.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet of the weekly report.

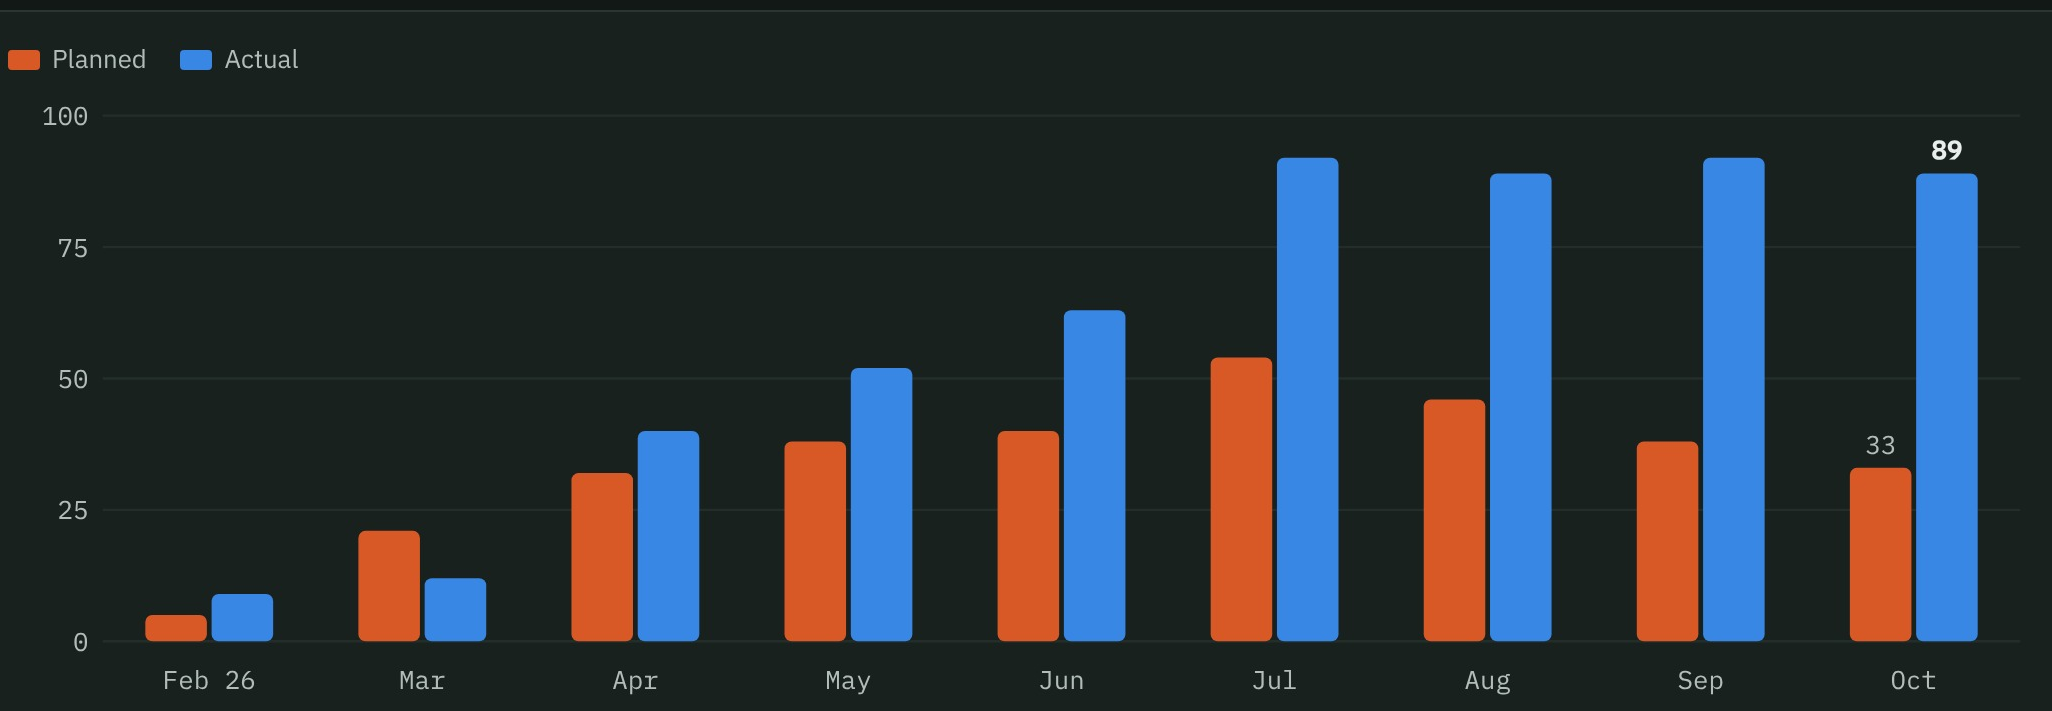

October head count is 89 against 33 planned (16 non-manual and 73 manual). The dashboard of the same report shows 93 against 40. Equipment on site: 30 against 8 planned.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	35,709,993
Revised contract value	35,709,993
Change orders	0
Potential changes	0

All values in SAR. No contract change orders are registered.

Invoices

Invoices in the log	2
Gross value	3,357,105
Advance payment recovery	−335,711
Deductions and penalties	−38,000
Approved by MODON PM	0
FIR value to date	3,485,668

Invoicing is 9.4% of the contract value against 77.64% physical progress. IPC-01 (2,317,493) and IPC-02 (1,039,612) are approved by the consultant; neither is approved by the MODON PM.

Health, safety and quality

Safety Score 0.92

Safe man-hours (cumulative)	107,530
Man-hours this week	9,660
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	238 / 588

MODON HSE inspection no. 29 (22-Oct-2026): 16 items good practice, 7 need improvement, 0 fail.

Quality Score 0.91

FIRs issued / closed / pending	717 / 606 / 111
MIRs issued / closed / pending	81 / 67 / 14
NCRs issued / closed / pending	22 / 8 / 14
Site instructions issued / closed	7 / 6
Shop drawings approved (A+B) / total	316 / 432
Material approvals (A+B) / total	130 / 150

55 shop drawings and 12 material submittals are pending.

Open issues and risks

The issue log of the weekly report has one issue, now closed (Hail work permit, closed 19-Apr-2026). The items below come from the progress, quantity, schedule and risk sheets.

ISSUE	SITE	DETAIL
Air dome works	Qassim, Tabuk	Physical progress 39.96% (Qassim) and 35.13% (Tabuk) against 79.84% and 74.55% planned; no air dome man-hours were earned this week. Air dome materials are 80% delivered.
Schedule slippage	All sites	Forecast handover moved from 07-Feb-2027 to 14-Feb-2027 in one week. 169 of 300 open activities have negative float, 170 activities are on the critical path and 39 have failed to start (42 last week).
Landscaping and irrigation	All sites	Lawn not started against 12,539 m² planned to date; 25 mm irrigation pipe at 1,812 of 10,545 m planned. Landscape completion is forecast for 10-Jan-2027 (−20.9 days of float).
Playground surfaces	All sites	Football playground at 4,400 of 7,350 m² and tartan floor at 8,000 of 9,921 m² planned to date.
Procurement	All sites	25 of 57 purchase orders remain to be issued and 8 materials are on site; the curtain wall remainder is at 70–80%.
Soil investigation (risk register)	Tabuk	Open risk: borehole test results take 7–10 days from the laboratory, which may delay the start of excavation.

Data notes

- Progress figures are the weekly report's physical progress (effort), weighted by 33,340 budgeted man-hours, of which 10,000 belong to the “Project milestone” management line. The report's cover and dashboard also show cost-based progress labelled as actual; this report uses physical progress only.
- The report states “Current Contract Weeks: 0 of 0”, so the week number is counted from site handover (17-Feb-2026): week 35.
- The “Weekly Physical Progress” columns hold 75.05% planned and 68.08% earned, which match neither week's to-date figures. Progress this week is taken as the change in to-date progress since the 18-Oct-2026 report.
- All major quantities are identical to the 18-Oct-2026 report, although work was reported this week; the sheet appears not to have been updated.
- Man-hours by site: Tabuk toilet building shows 0 of 1,708 man-hours earned with only 40 planned, and Tabuk closeout has no budget but 62 man-hours earned.
- The milestone sheet gives complete mobilisation as 14-Apr-2026 against 18-Mar-2026 with 0 days change, and complete construction as 28-Oct-2026 (47 days early), which P6 does not support.
- Procurement: the summary has 8 of 57 materials on site, while the P6 delivery activities are 70–95% complete. The procurement log has no delivered quantities or dates.

- Invoices: the summary shows 0 submitted invoices while the log lists IPC-01 and IPC-02. Paid invoices (3,436,604 SAR) exceed the gross submitted value although none is PM-approved. The dashboard's penalties of −373,711 combine advance payment recovery and deductions.
- Manpower: October in the Manpower sheet is 25 manual planned and 73 actual, while the dashboard shows 32 and 77. The DB sheet still holds another project's data (HAL1-02-005).
- The P6 update has a data date of 23-Oct-2026, against 25-Oct-2026 for the weekly report; 118 in-progress activities have a finish date before the data date. Three PDFs are named MLTX-05-047 although they belong to MLTX-02-003.
- The contractor forecast in the Physical-Chart Data sheet starts at 0 in February, 365 man-hours below the actual, so it stays slightly below actual until October.

Compiled 01-Nov-2026 from the weekly reports of 18 and 25 Oct 2026 and the P6 update with data date 23-Oct-2026.
