ENJAZCO

Tel.:4108184 - 4108180
Email: info@enjaz-co.com


JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026

Progress Certificate # 02

egis

MODON

Activity ID	Activity Name	Budget At Completion	Original Duration	BL Project Start	BL Project Finish	Schedule % Complete	Performance % Complete	Planned Value Cost	Earned Value Cost
JDH1.02.003-Up-20.10.2026	JDH1-02-003 - Infrastructure Development For Industrial Cit	86,756,415.73	763	19-Nov-25	18-Nov-27	53.2%	78.74%	46,153,496.78	68,315,968.81
JDH1.02.003-Up-20.10.2026.5	Milestones	0.00	763	19-Nov-25	18-Nov-27	0%	0%	0.00	0.00
JDH1.02.003-Up-20.10.2026.2	Mobilization	0.00	112	19-Nov-25	18-Dec-25	0%	0%	0.00	0.00
JDH1.02.003-Up-20.10.2026.3	Engineering	2,601,460.39	287	26-Nov-25	19-Jan-26	100%	99.14%	2,601,460.39	2,579,200.39
JDH1.02.003-Up-20.10.2026.4	Procurement	17,355,662.10	502	28-Dec-25	14-Sep-27	77.89%	90.68%	13,518,577.10	15,737,880.10
JDH1.02.003-Up-20.10.2026.1	Construction	58,121,602.04	710	20-Dec-25	18-Oct-27	51.67%	76.69%	30,033,459.29	44,572,325.02
JDH1.02.003-Up-20.10.2026.1.9	Site Demolition	279,942.75	93	20-Dec-25	03-Mar-26	100%	100%	279,942.75	279,942.75
JDH1.02.003-Up-20.10.2026.1.1	Roads & Meduim Voltage	11,810,038.74	423	06-Jan-26	17-Sep-26	100%	73.25%	11,810,038.74	8,650,438.79
JDH1.02.003-Up-20.10.2026.1.6	Deep Infrastructure network	10,009,830.20	277	01-Apr-26	18-Nov-26	99.59%	97.41%	9,968,870.03	9,750,710.50
JDH1.02.003-Up-20.10.2026.1.7	Shallow infrastructure network	12,539,076.30	433	15-Jun-26	18-Mar-27	24.08%	83.37%	3,020,014.97	10,453,768.19
JDH1.02.003-Up-20.10.2026.1.3	Bridge	2,513,306.98	452	04-Mar-26	01-Jun-27	53.13%	72.83%	1,335,298.31	1,830,342.88
JDH1.02.003-Up-20.10.2026.1.4	Outside Boundary Area (Tie-in Lines)	2,681,726.27	419	01-Jan-26	04-May-27	52.6%	99.31%	1,410,519.88	2,663,147.17
JDH1.02.003-Up-20.10.2026.1.8	Roads Finishing	8,138,565.00	204	25-Jan-27	03-Aug-27	0%	68.7%	0.00	5,591,559.17
JDH1.02.003-Up-20.10.2026.1.5	Fence and Gate	8,127,691.90	558	07-Feb-26	18-Oct-27	27.18%	65.85%	2,208,774.60	5,352,415.58
JDH1.02.003-Up-20.10.2026.1.2	Roundabout & Landscape	2,021,423.90	226	14-Mar-27	18-Oct-27	0%	0%	0.00	0.00
JDH1.02.003-Up-20.10.2026.6	Testing & Commissioning	8,677,691.20	167	04-Aug-27	26-Oct-27	0%	62.53%	0.00	5,426,563.31
JDH1.02.003-Up-20.10.2026.7	Project Close-out	0.00	145	14-Aug-27	18-Nov-27	0%	0%	0.00	0.00

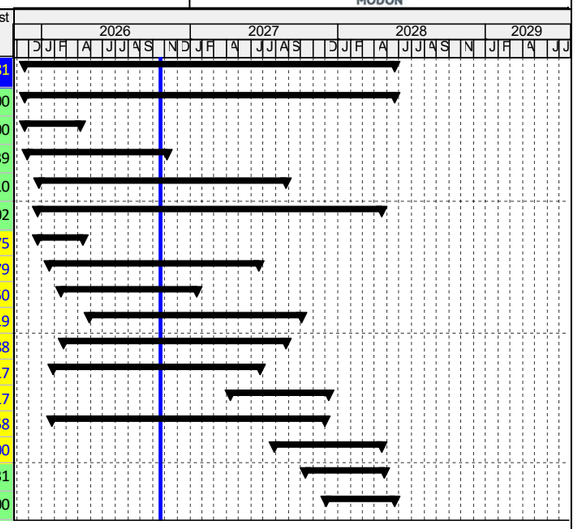

◆ Milestone
summary

TASK filter: All Activities

© Oracle Corporation

19-Oct-26 13:35
