
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R R	190	57.6%	55.58%	04-May-26	16-Dec-26	01-Jun-26 A	13-Dec-26	1,515,850.40	1,462,761.11	2,631,890.59	4
ARAR		108	65.96%	44.08%	27-Jun-26	28-Nov-26	11-Jun-26 A	13-Dec-26	486,568.72	325,136.04	737,674.36	-12
ENGINEERING		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
SHOP DRAWINGS		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
SHOP DRAWINGS SUBMISSION		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
ELECTRICAL WORKS		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
MLTX-02-005-EN-2580	Shop DWG Submittal for Power Layout	27	100%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
PROCUREMENT		40	0%	0%	27-Jun-26	28-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-12
SHORT LEAD ITEM		40	0%	0%	27-Jun-26	28-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-12
TOILET/SERVICE WORKS		40	0%	0%	27-Jun-26	28-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-12
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-8490	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-104
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	1
MLTX-02-005-PR-8530	Material Delivery for Switches/Sockets	27	0%	0%	28-Oct-26	28-Nov-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	1
FURNITURES		29	0%	0%	30-Aug-26	03-Oct-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-8150	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-49
PLAYGROUND WORKS		30	0%	0%	15-Jul-26	24-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-32
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-48
MARKING PAINT		15	0%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-9090	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
CCTV MATERIALS		25	0%	0%	26-Sep-26	24-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9410	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-27
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-88
LANDSCAPE WORKS		30	0%	0%	15-Jul-26	17-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-11
PAVEMENT MARKING		5	0%	0%	15-Jul-26	20-Jul-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-88
TRAFFIC SIGNS		30	0%	0%	13-Aug-26	16-Sep-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-9640	Material Delivery for Traffic Signs	30	100%	0%	13-Aug-26	16-Sep-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-63
AGRICULTURE SOIL		22	0%	0%	18-Aug-26	12-Sep-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-9720	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	-59
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-9800	Material Delivery for Grass/Trees	25	24%	0%	20-Oct-26	17-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-6
LONG LEAD ITEM		25	0%	0%	27-Sep-26	23-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-1
PLAYGROUND WORKS		25	0%	0%	27-Sep-26	23-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-1
STEEL TENSION CABLES		15	0%	0%	27-Sep-26	13-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-8690	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-26
EMERGENCY DOORS		20	0%	0%	26-Oct-26	17-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-8730	Material Delivery for Emergency Doors	20	5%	0%	26-Oct-26	17-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-1
PRESSURE UNITS		25	0%	0%	26-Oct-26	23-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-8770	Material Delivery for Pressure Units	25	4%	0%	26-Oct-26	23-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-1
AIR LOCK DOORS		20	0%	0%	14-Oct-26	05-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-8800	Material Fabrication for Lock Doors	20	55%	0%	14-Oct-26	05-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-11
CONSTRUCTION PHASE		108	65.96%	44.08%	13-Sep-26	22-Nov-26	11-Jun-26 A	13-Dec-26	486,568.72	325,136.04	737,674.36	-17
SITE WORKS		90	56.28%	47.33%	01-Oct-26	22-Nov-26	11-Jun-26 A	13-Dec-26	323,278.14	271,853.15	574,383.78	-17
LANDSCAPE WORKS		90	56.28%	47.33%	01-Oct-26	22-Nov-26	11-Jun-26 A	13-Dec-26	323,278.14	271,853.15	574,383.78	-17
PLAYGROUND AREA		20	100%	0%	01-Oct-26	24-Oct-26	27-Oct-26	18-Nov-26	30,677.48	0.00	30,677.48	-22
PADEL FENCE		20	100%	0%	01-Oct-26	24-Oct-26	27-Oct-26	18-Nov-26	30,677.48	0.00	30,677.48	-22
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	27-Oct-26	18-Nov-26	30,677.48	0.00	30,677.48	-22
WALKING/BIKE PATHS		24	79.59%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	13-Dec-26	292,600.66	183,816.95	367,633.90	-35
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	13-Dec-26	187,554.12	93,777.06	187,554.12	-47
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	58.33%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	13-Dec-26	105,046.54	90,039.89	180,079.78	-35
GENERAL/FURNITURE		13	0%	50%	08-Nov-26	22-Nov-26	18-Oct-26 A	10-Nov-26	0.00	88,036.20	176,072.40	10
MLTX-02-005-CN-11800	Installing of Site Light Poles	13	0%	50%	08-Nov-26	22-Nov-26	18-Oct-26 A	10-Nov-26	0.00	88,036.20	176,072.40	10
TOILET/SERVICE BUILDING		53	100%	32.63%	13-Sep-26	22-Oct-26	03-Oct-26 A	14-Nov-26	163,290.58	53,282.89	163,290.58	-19
THERMAL & MOISTER PROTECTION		8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-37
MLTX-02-005-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-37
MECHANICAL WORK		13	100%	16.57%	29-Sep-26	17-Oct-26	22-Oct-26 A	08-Nov-26	36,762.98	6,093.32	36,762.98	-19
SEWER/DRAINAGE SYSTEM		13	100%	16.57%	29-Sep-26	17-Oct-26	22-Oct-26 A	08-Nov-26	36,762.98	6,093.32	36,762.98	-19
MLTX-02-005-CN-11580	Installing UPVC Pipes for External Connection for Sewage Network	4	100%	0%	05-Oct-26	08-Oct-26	02-Nov-26	05-Nov-26	14,217.67	0.00	14,217.67	-24
MLTX-02-005-CN-11600	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	07-Nov-26	08-Nov-26	10,358.68	0.00	10,358.68	-19

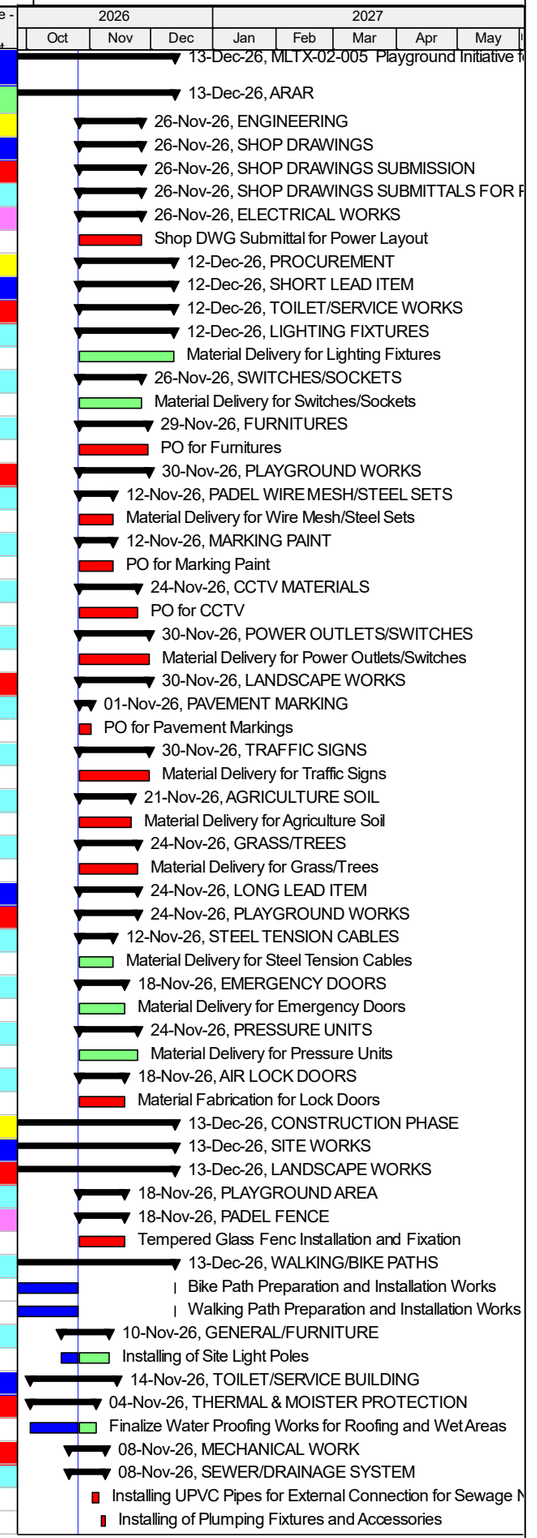

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	50%	29-Sep-26	04-Oct-26	22-Oct-26 A	01-Nov-26	12,186.63	6,093.32	12,186.63	-24
DOORS/WINDOWS		2	100%	0%	17-Sep-26	19-Sep-26	27-Oct-26	28-Oct-26	52,646.24	0.00	52,646.24	-33
MLTX-02-005-CN-11100	Preliminary Works For Windows/Curtain Wall	2	100%	0%	17-Sep-26	19-Sep-26	27-Oct-26	28-Oct-26	52,646.24	0.00	52,646.24	-33
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	27-Oct-26	31-Oct-26	3,899.72	0.00	3,899.72	-36
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	27-Oct-26	31-Oct-26	3,899.72	0.00	3,899.72	-36
FINISHING WORKS		9	100%	83.21%	06-Oct-26	13-Oct-26	20-Oct-26 A	03-Nov-26	38,750.40	32,243.02	38,750.40	-18
FLOOR FINISHES		4	100%	0%	06-Oct-26	10-Oct-26	27-Oct-26	31-Oct-26	2,924.82	0.00	2,924.82	-18
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	27-Oct-26	31-Oct-26	2,924.82	0.00	2,924.82	-18
WALL FINISHES		7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	03-Nov-26	35,825.58	32,243.02	35,825.58	-18
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	03-Nov-26	35,825.58	32,243.02	35,825.58	-18
SPECIALTIES WORK		5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	14-Nov-26	14,623.96	0.00	14,623.96	-19
MLTX-02-005-CN-11390	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	14-Nov-26	14,623.96	0.00	14,623.96	-19
HASA OASIS		190	57.37%	64.54%	04-May-26	16-Dec-26	01-Jun-26 A	30-Nov-26	767,153.73	863,074.97	1,337,216.48	14
ENGINEERING		25	0%	0%	04-May-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
SHOP DRAWINGS		25	0%	0%	04-May-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
SHOP DRAWINGS APPROVALS		25	0%	0%	28-Oct-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		25	0%	0%	28-Oct-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
ELECTRICAL WORKS		25	0%	0%	28-Oct-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
MLTX-02-005-EN-1184(	Shop DWG Approval for Power Installation Details	25	0%	0%	28-Oct-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
PROCUREMENT		30	0%	0%	16-Jun-26	10-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-17
SHORT LEAD ITEM		30	0%	0%	16-Jun-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
TOILET/SERVICE WORKS		20	0%	0%	16-Jun-26	19-Oct-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-26
LIGHTING FIXTURES		20	0%	0%	16-Jun-26	08-Jul-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-10300	Material Delivery for Lighting Fixtures	20	100%	0%	16-Jun-26	08-Jul-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-113
SWITCHES/SOCKETS		15	0%	0%	16-Jun-26	02-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-10310	PO for Switches/Sockets	15	100%	0%	16-Jun-26	02-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-113
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-10130	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-10140	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	02-Nov-26	18-Nov-26	0.00	0.00	0.00	-26
FURNITURES		19	0%	0%	16-Jun-26	07-Jul-26	27-Oct-26	17-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-10330	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	27-Oct-26	17-Nov-26	0.00	0.00	0.00	-113
PLAYGROUND WORKS		30	0%	0%	28-Jun-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	30	76.67%	0%	30-Sep-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-31
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-34
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-34
MARKING PAINT		15	0%	0%	28-Jun-26	14-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-10350	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-103
AIR DIFUSSERS/GRILLS		15	0%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
GALVANIZED DUCTS		15	0%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-10490	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
EXHAUST FANS		15	0%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-10510	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
CCTV MATERIALS		15	0%	0%	04-Jul-26	20-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-10690	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-98
LANDSCAPE WORKS		25	0%	0%	21-Sep-26	26-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-25
TRAFFIC SIGNS		5	0%	0%	21-Sep-26	27-Sep-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-10080	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-30
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-10920	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-25
LONG LEAD ITEM		25	0%	0%	21-Sep-26	10-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-12
PLAYGROUND WORKS		25	0%	0%	21-Sep-26	10-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-12
STEEL TENSION CABLES		16	0%	0%	21-Sep-26	10-Oct-26	27-Oct-26	14-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-10560	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	27-Oct-26	14-Nov-26	0.00	0.00	0.00	-30
PRESSURE UNITS		25	0%	0%	13-Oct-26	10-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-12

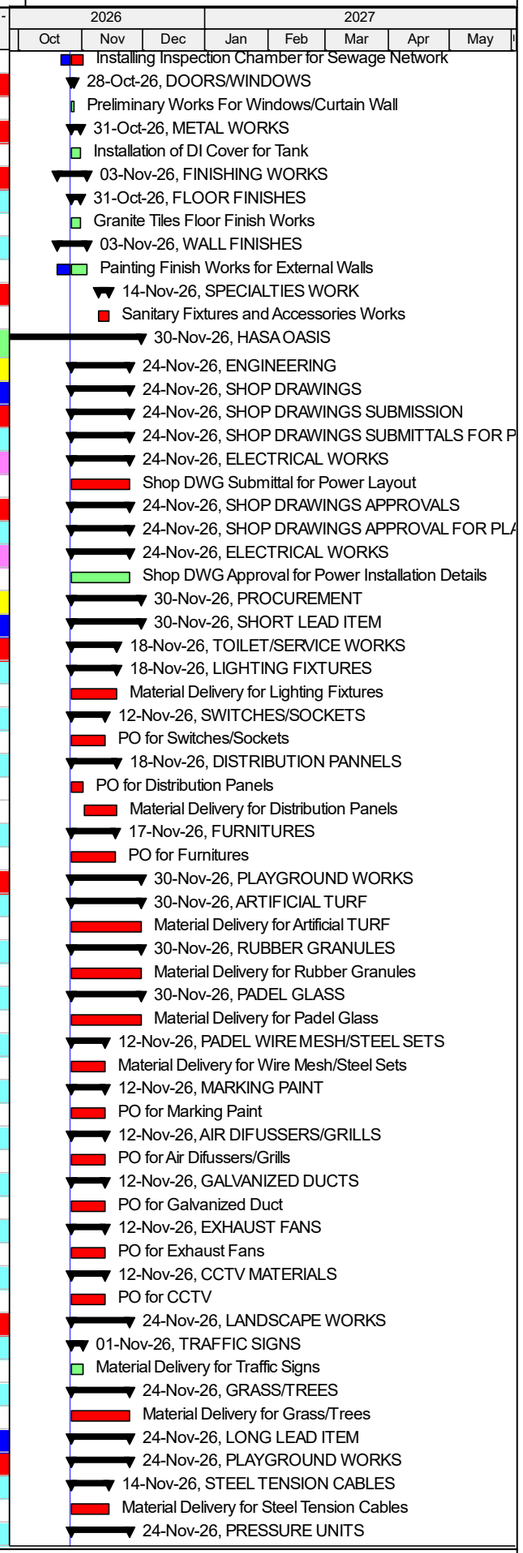

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-10600	Material Delivery for Pressure Units	25	48%	0%	13-Oct-26	10-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-12
AIR LOCK DOORS		25	0%	0%	03-Oct-26	31-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-PR-10620	Material Delivery for Lock Doors	25	84%	0%	03-Oct-26	31-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-21
CONSTRUCTION PHASE		190	57.37%	64.54%	30-Jul-26	16-Dec-26	01-Jun-26 A	28-Nov-26	767,153.73	863,074.97	1,337,216.48	16
SITE WORKS		135	58.44%	66.13%	29-Sep-26	07-Dec-26	01-Jun-26 A	28-Nov-26	700,096.91	792,292.07	1,198,014.82	8
LANDSCAPE WORKS		135	58.44%	66.13%	29-Sep-26	07-Dec-26	01-Jun-26 A	28-Nov-26	700,096.91	792,292.07	1,198,014.82	8
PLAYGROUND AREA		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	29-Oct-26	180,520.67	144,416.54	180,520.67	-24
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	29-Oct-26	180,520.67	144,416.54	180,520.67	-24
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	29-Oct-26	180,520.67	144,416.54	180,520.67	-24
NATURAL GROUND		15	0%	63.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	01-Nov-26	0.00	121,870.00	191,740.00	31
MLTX-02-005-CN-11980	Tartan Floor Installation Works for Landscape (Including Finishing Works)	3	0%	50%	05-Dec-26	07-Dec-26	14-Oct-26 A	29-Oct-26	0.00	63,370.00	126,740.00	33
MLTX-02-005-CN-11990	Compacted Natural Ground Soil Installation Works for Landscape	5	0%	90%	29-Nov-26	03-Dec-26	13-Oct-26 A	01-Nov-26	0.00	58,500.00	65,000.00	28
PLANTING		101	30%	56%	24-Oct-26	02-Nov-26	03-Oct-26 A	29-Oct-26	104,175.44	194,460.82	347,251.46	3
MLTX-02-005-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	3	100%	70%	24-Oct-26	26-Oct-26	03-Oct-26 A	29-Oct-26	104,175.44	72,922.81	104,175.44	-3
MLTX-02-005-CN-12060	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	29-Oct-26	0.00	70,866.25	141,732.50	3
MLTX-02-005-CN-12070	Placement and Fixation of Trees	3	0%	50%	27-Oct-26	29-Oct-26	14-Oct-26 A	29-Oct-26	0.00	50,671.76	101,343.52	0
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	27-Oct-26	367,633.90	294,107.12	367,633.90	-8
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	27-Oct-26	187,554.12	150,043.30	187,554.12	-16
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	27-Oct-26	180,079.78	144,063.82	180,079.78	-8
GENERAL/FURNITURE		37	43.08%	33.77%	15-Oct-26	16-Nov-26	14-Oct-26 A	28-Nov-26	47,766.90	37,437.60	110,868.79	-10
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	18	44.44%	40%	18-Oct-26	07-Nov-26	14-Oct-26 A	16-Nov-26	41,597.33	37,437.60	93,594.00	-8
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	28	35.71%	0%	15-Oct-26	16-Nov-26	27-Oct-26	28-Nov-26	6,169.57	0.00	17,274.79	-10
TOILET/SERVICE BUILDING		190	48.17%	50.85%	30-Jul-26	16-Dec-26	20-Sep-26 A	16-Nov-26	67,056.82	70,782.89	139,201.66	26
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	16-Nov-26	16,607.28	14,946.55	16,607.28	-75
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	16-Nov-26	16,607.28	14,946.55	16,607.28	-75
DOORS/WINDOWS		115	0%	18%	21-Nov-26	16-Dec-26	24-Oct-26 A	08-Nov-26	0.00	10,529.25	58,495.82	33
MLTX-02-005-CN-13040	Finalize Glazzed Curtain Wall Works	11	0%	0%	05-Dec-26	16-Dec-26	27-Oct-26	08-Nov-26	0.00	0.00	5,849.58	33
MLTX-02-005-CN-13120	Preliminary Works For Windows/Curtain Wall	12	0%	20%	21-Nov-26	03-Dec-26	24-Oct-26 A	27-Oct-26	0.00	10,529.25	52,646.24	33
FINISHING WORKS		52	72.41%	67.93%	18-Oct-26	03-Nov-26	27-Sep-26 A	29-Oct-26	35,825.58	33,607.92	49,474.60	4
WALL FINISHES		52	72.41%	67.93%	18-Oct-26	03-Nov-26	27-Sep-26 A	29-Oct-26	35,825.58	33,607.92	49,474.60	4
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	29-Oct-26	35,825.58	32,243.02	35,825.58	-8
MLTX-02-005-CN-13140	Glass Partitions including all accessories and doors	5	0%	10%	29-Oct-26	03-Nov-26	24-Oct-26 A	27-Oct-26	0.00	1,364.90	13,649.02	7
SPECIALTIES WORK		3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	29-Oct-26	14,623.96	11,699.17	14,623.96	-26
MLTX-02-005-CN-12700	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	29-Oct-26	14,623.96	11,699.17	14,623.96	-26
DAMMAM		158	47.06%	49.29%	21-May-26	14-Dec-26	06-Sep-26 A	10-Dec-26	262,127.95	274,550.10	556,999.75	3
ENGINEERING		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
SHOP DRAWINGS		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
SHOP DRAWINGS SUBMISSION		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
MLTX-02-005-EN-1293(	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-129
MLTX-02-005-EN-1296(	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
PROCUREMENT		29	0%	0%	21-May-26	02-Dec-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	3
SHORT LEAD ITEM		29	0%	0%	21-May-26	02-Dec-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	3
TOILET/SERVICE WORKS		29	0%	0%	17-Jun-26	29-Oct-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-26
DISTRIBUTION PANNELS		15	0%	0%	13-Oct-26	29-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-11210	PO for Distribution Panels	15	80%	0%	13-Oct-26	29-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-12
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-11410	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	27-Oct-26	05-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-11420	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-112
PLAYGROUND WORKS		28	0%	0%	21-May-26	02-Dec-26	27-Oct-26	28-Nov-26	0.00	0.00	0.00	4
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	27-Oct-26	19-Nov-26	0.00	0.00	0.00	-132
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	27-Oct-26	19-Nov-26	0.00	0.00	0.00	-132
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	-127
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	-127
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	27-Oct-26	28-Nov-26	0.00	0.00	0.00	-7
MLTX-02-005-PR-11900	Material Delivery for Padel Glass	28	25%	0%	19-Oct-26	19-Nov-26	27-Oct-26	28-Nov-26	0.00	0.00	0.00	-7
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-122
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-122
BITUMINOUS BASE & WEARING COURSE		15	0%	0%	15-Jun-26	01-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-11080	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-114
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-102
MLTX-02-005-PR-11730	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-102
MLTX-02-005-PR-11740	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-102

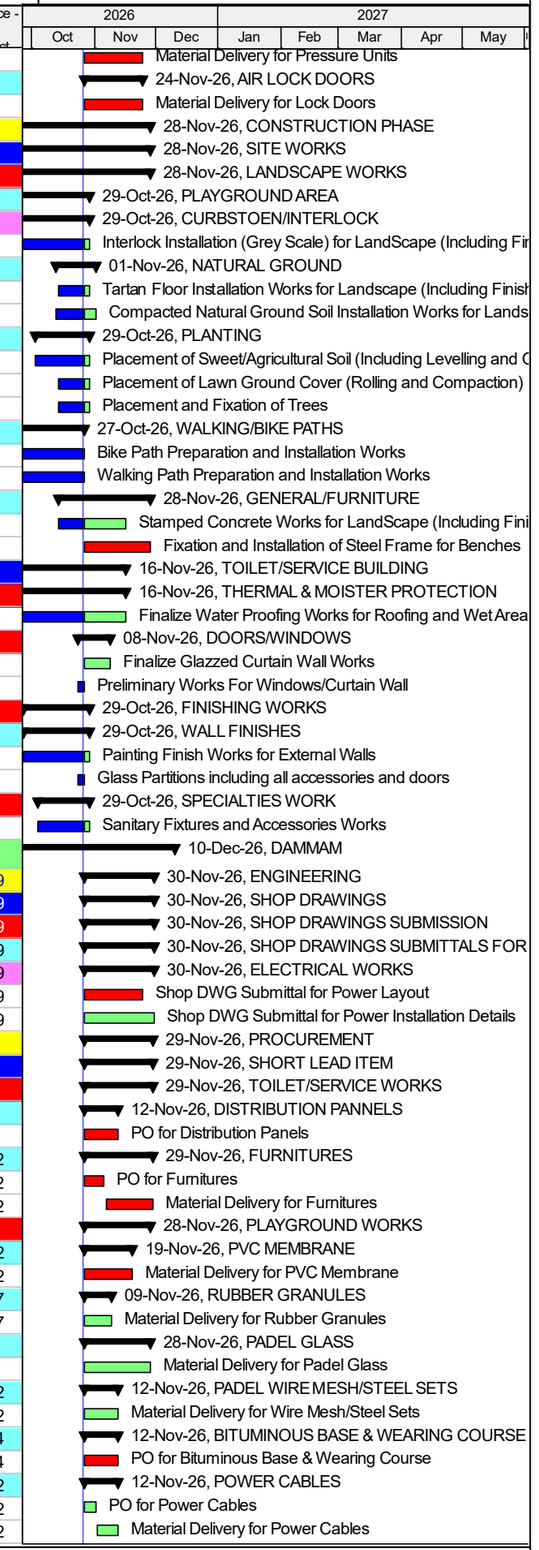

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-11760	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	7
CCTV MATERIALS		5	0%	0%	30-Jul-26	04-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-75
LONG LEAD ITEM		15	0%	0%	07-Sep-26	21-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	7
PLAYGROUND WORKS		15	0%	0%	07-Sep-26	21-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	7
STEEL TENSION CABLES		15	0%	0%	07-Sep-26	24-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-11640	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-42
EMERGENCY DOORS		15	0%	0%	04-Nov-26	21-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-11660	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	7
PRESSURE UNITS		10	0%	0%	05-Nov-26	16-Nov-26	27-Oct-26	07-Nov-26	0.00	0.00	0.00	8
MLTX-02-005-PR-11680	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	27-Oct-26	07-Nov-26	0.00	0.00	0.00	8
AIR LOCK DOORS		12	0%	0%	05-Nov-26	18-Nov-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	8
MLTX-02-005-PR-11700	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	8
CONSTRUCTION PHASE		158	47.06%	49.29%	18-Aug-26	14-Dec-26	06-Sep-26 A	10-Dec-26	262,127.95	274,550.10	556,999.75	3
SITE WORKS		104	46.7%	47.15%	15-Sep-26	14-Dec-26	15-Oct-26 A	18-Nov-26	245,520.67	247,904.38	525,768.51	22
LANDSCAPE WORKS		104	46.7%	47.15%	15-Sep-26	14-Dec-26	15-Oct-26 A	18-Nov-26	245,520.67	247,904.38	525,768.51	22
PLAYGROUND AREA		6	100%	20%	15-Sep-26	21-Sep-26	21-Oct-26 A	02-Nov-26	180,520.67	36,104.13	180,520.67	-35
CURBSTOEN/INTERLOCK		6	100%	20%	15-Sep-26	21-Sep-26	21-Oct-26 A	02-Nov-26	180,520.67	36,104.13	180,520.67	-35
MLTX-02-005-CN-1339(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	6	100%	20%	15-Sep-26	21-Sep-26	21-Oct-26 A	02-Nov-26	180,520.67	36,104.13	180,520.67	-35
NATURAL GROUND		15	100%	50%	10-Oct-26	26-Oct-26	20-Oct-26 A	12-Nov-26	65,000.00	32,500.00	65,000.00	-15
MLTX-02-005-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	15	100%	50%	10-Oct-26	26-Oct-26	20-Oct-26 A	12-Nov-26	65,000.00	32,500.00	65,000.00	-15
PLANTING		6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	02-Nov-26	0.00	20,835.09	104,175.44	34
MLTX-02-005-CN-13480	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	02-Nov-26	0.00	20,835.09	104,175.44	34
GENERAL/FURNITURE		20	0%	90%	22-Nov-26	14-Dec-26	15-Oct-26 A	18-Nov-26	0.00	158,465.16	176,072.40	22
MLTX-02-005-CN-14360	Installing of Site Light Poles	20	0%	90%	22-Nov-26	14-Dec-26	15-Oct-26 A	18-Nov-26	0.00	158,465.16	176,072.40	22
TOILET/SERVICE BUILDING		130	53.18%	85.32%	18-Aug-26	31-Oct-26	06-Sep-26 A	10-Dec-26	16,607.28	26,645.72	31,231.24	-35
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-59
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-59
SPECIALTIES WORK		4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	10-Dec-26	0.00	11,699.17	14,623.96	-35
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	10-Dec-26	0.00	11,699.17	14,623.96	-35

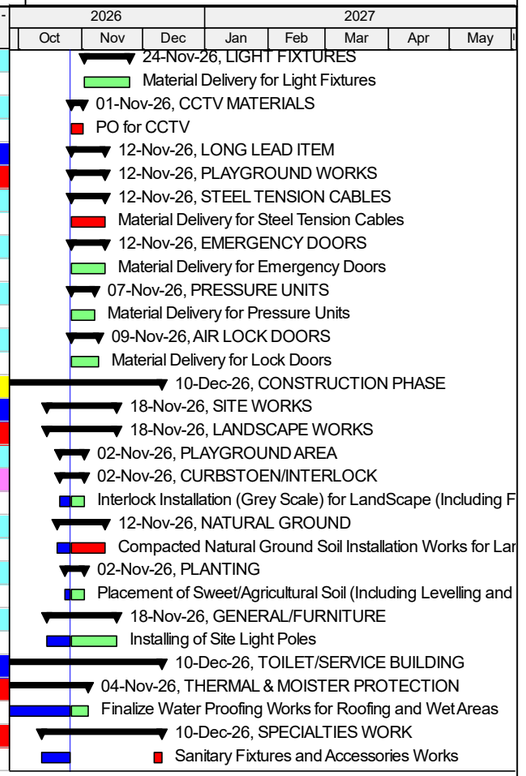

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
