
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	314	40.01%	40.46%	03-Mar-26	02-Jan-27	03-Mar-26 A	14-Mar-27	12,002,792.56	12,137,851.02	29,997,851.67	-57
KEY MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	14-Mar-27	0.00	0.00	0.00	-57
GENERAL MILESTONES		312	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	14-Mar-27	0.00	0.00	0.00	-57
CONTRACTUAL MILESTONE		280	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	09-Mar-27	0.00	0.00	0.00	-56
ARAR		314	38.44%	36.14%	03-Mar-26	02-Jan-27	04-Mar-26 A	01-Mar-27	3,931,450.77	3,695,828.11	10,226,640.03	-49
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		247	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	27-Dec-26	0.00	0.00	0.00	-12
PROCUREMENT		206	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	04-Feb-27	0.00	0.00	0.00	-44
CONSTRUCTION PHASE		280	38.44%	36.14%	15-Apr-26	31-Dec-26	04-Apr-26 A	01-Mar-27	3,931,450.77	3,695,828.11	10,226,640.03	-50
SITE WORKS		270	34.8%	33.24%	15-Apr-26	30-Dec-26	04-Apr-26 A	01-Mar-27	3,152,481.94	3,010,993.45	9,058,565.25	-51
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
LANDSCAPE WORKS		237	31.25%	28.9%	24-May-26	30-Dec-26	17-May-26 A	01-Mar-27	2,657,594.92	2,457,613.09	8,505,184.90	-51
PLAYGROUND AREA		237	47.97%	49.89%	24-May-26	27-Dec-26	19-May-26 A	01-Mar-27	657,179.52	683,464.16	1,369,978.66	-54
FOOTBALL PLAYGROUND		204	35%	35%	24-May-26	13-Dec-26	19-May-26 A	20-Jan-27	110,897.50	110,897.50	316,849.99	-33
PADEL PLAYGROUND		184	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	20-Jan-27	105,292.80	163,788.80	233,984.00	-28
BASKETBALL PLAYGROUND		167	69.52%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	25-Jan-27	221,133.58	221,133.58	318,089.68	-28
PADEL FENCE		87	27.44%	4.22%	01-Sep-26	16-Nov-26	08-Aug-26 A	12-Dec-26	38,071.30	5,859.94	138,749.98	-22
CURBSTOEN/INTERLOCK		125	50.17%	50.17%	06-Oct-26	27-Dec-26	15-Aug-26 A	01-Mar-27	181,784.34	181,784.34	362,305.01	-54
AIR DOME		120	23.18%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	11-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-45
CIVIL WORKS		96	48.29%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	14-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-33
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	1,233,296.81	-32
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	19-Jan-27	30-Jan-27	0.00	0.00	1,513,591.54	-35
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	06-Feb-27	11-Feb-27	0.00	0.00	168,176.84	-45
IRRIGATION NETWORK		164	83.53%	83.53%	28-Jun-26	30-Nov-26	18-Aug-26 A	05-Jan-27	127,308.67	127,308.67	152,414.87	-31
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	23-Dec-26	05-Jan-27	0.00	0.00	191,740.00	-31
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	01-Dec-26	17-Dec-26	205,518.96	0.00	347,251.46	-41
WALKING/BIKE PATHS		24	79.59%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	13-Dec-26	292,600.66	183,816.95	367,633.90	-35
GENERAL/FURNITURE		94	16.05%	34.77%	19-Oct-26	30-Dec-26	03-Oct-26 A	04-Feb-27	75,459.60	163,495.80	470,271.40	-31
PARKING		24	0%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	0.00	58,493.33	58,493.33	40
TOILET/SERVICE BUILDING		216	66.69%	58.63%	02-Jul-26	31-Dec-26	21-May-26 A	23-Jan-27	778,968.83	684,834.67	1,168,074.78	-19
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		54	100%	95.21%	29-Aug-26	21-Sep-26	26-Sep-26 A	04-Nov-26	34,698.32	33,037.59	34,698.32	-37
MECHANICAL WORK		167	62.8%	51.87%	16-Jul-26	19-Dec-26	18-Jul-26 A	21-Jan-27	166,205.09	137,290.30	264,673.10	-29
ELECTRICAL WORKS		113	53.29%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	23-Jan-27	206,217.32	206,217.32	386,998.59	-30
DOORS/WINDOWS		120	88.57%	14.29%	17-Sep-26	31-Dec-26	20-Oct-26 A	17-Jan-27	60,445.68	9,749.30	68,245.12	-14
METAL WORKS		75	57.14%	71.43%	14-Sep-26	23-Nov-26	16-Sep-26 A	31-Oct-26	7,799.44	9,749.30	13,649.02	20
FINISHING WORKS		102	68.5%	68.38%	22-Sep-26	12-Dec-26	10-Aug-26 A	17-Jan-27	113,795.19	113,607.03	166,130.97	-31
SPECIALTIES WORK		64	25%	0%	18-Oct-26	17-Dec-26	09-Nov-26	21-Jan-27	14,623.96	0.00	58,495.83	-30
TESTING & COMMISSIONING		31	0%	0%	20-Dec-26	02-Jan-27	24-Jan-27	01-Mar-27	0.00	0.00	0.00	-49
HASA OASIS		312	40.75%	45.35%	03-Mar-26	02-Jan-27	04-Mar-26 A	09-Mar-27	4,056,947.25	4,515,094.04	9,955,979.43	-56
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
ENGINEERING		246	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	23-Dec-26	0.00	0.00	0.00	-5
PROCUREMENT		221	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	06-Feb-27	0.00	0.00	0.00	-57
CONSTRUCTION PHASE		293	40.75%	45.35%	29-Mar-26	31-Dec-26	04-Apr-26 A	15-Feb-27	4,056,947.25	4,515,094.04	9,955,979.43	-39
SITE WORKS		292	36.4%	41.87%	29-Mar-26	31-Dec-26	04-Apr-26 A	15-Feb-27	3,199,774.35	3,680,378.78	8,789,975.14	-39
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
LANDSCAPE WORKS		251	34.43%	39.44%	16-May-26	31-Dec-26	16-May-26 A	15-Feb-27	2,904,948.04	3,327,059.14	8,436,655.50	-39
PLAYGROUND AREA		251	73.52%	76.9%	16-May-26	31-Dec-26	18-May-26 A	08-Feb-27	956,764.68	1,000,815.42	1,301,449.27	-33
FOOTBALL PLAYGROUND		189	81.43%	85%	16-May-26	09-Dec-26	18-May-26 A	26-Dec-26	258,006.42	269,322.49	316,849.99	-14
PADEL PLAYGROUND		187	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	16-Jan-27	105,292.80	163,788.80	233,984.00	-13
BASKETBALL PLAYGROUND		165	69.34%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	16-Jan-27	231,160.45	236,425.54	333,381.64	-13
PADEL FENCE		87	0%	9.24%	28-Nov-26	31-Dec-26	06-Aug-26 A	08-Feb-27	0.00	5,077.72	54,928.63	-33
CURBSTOEN/INTERLOCK		19	100%	90.03%	09-Sep-26	01-Oct-26	12-Aug-26 A	29-Oct-26	362,305.01	326,200.88	362,305.01	-24
AIR DOME		171	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	15-Feb-27	1,299,527.51	1,299,527.51	5,605,894.61	-57
CIVIL WORKS		144	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	14-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-33
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	23-Dec-26	09-Jan-27	0.00	0.00	1,233,296.81	-28
ELECTRICAL WORKS		31	0%	0%	02-Dec-26	10-Dec-26	11-Jan-27	15-Feb-27	0.00	0.00	1,513,591.54	-57
FINISHES WORKS		47	0%	0%	15-Nov-26	10-Dec-26	23-Dec-26	15-Feb-27	0.00	0.00	168,176.84	-57
IRRIGATION NETWORK		100	35.18%	83.53%	03-Sep-26	07-Dec-26	18-Jul-26 A	29-Dec-26	53,620.00	127,308.67	152,414.87	-19
NATURAL GROUND		15	0%	63.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	01-Nov-26	0.00	121,870.00	191,740.00	31
PLANTING		101	30%	56%	24-Oct-26	02-Nov-26	03-Oct-26 A	29-Oct-26	104,175.44	194,460.82	347,251.46	3
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	27-Oct-26	367,633.90	294,107.12	367,633.90	-8

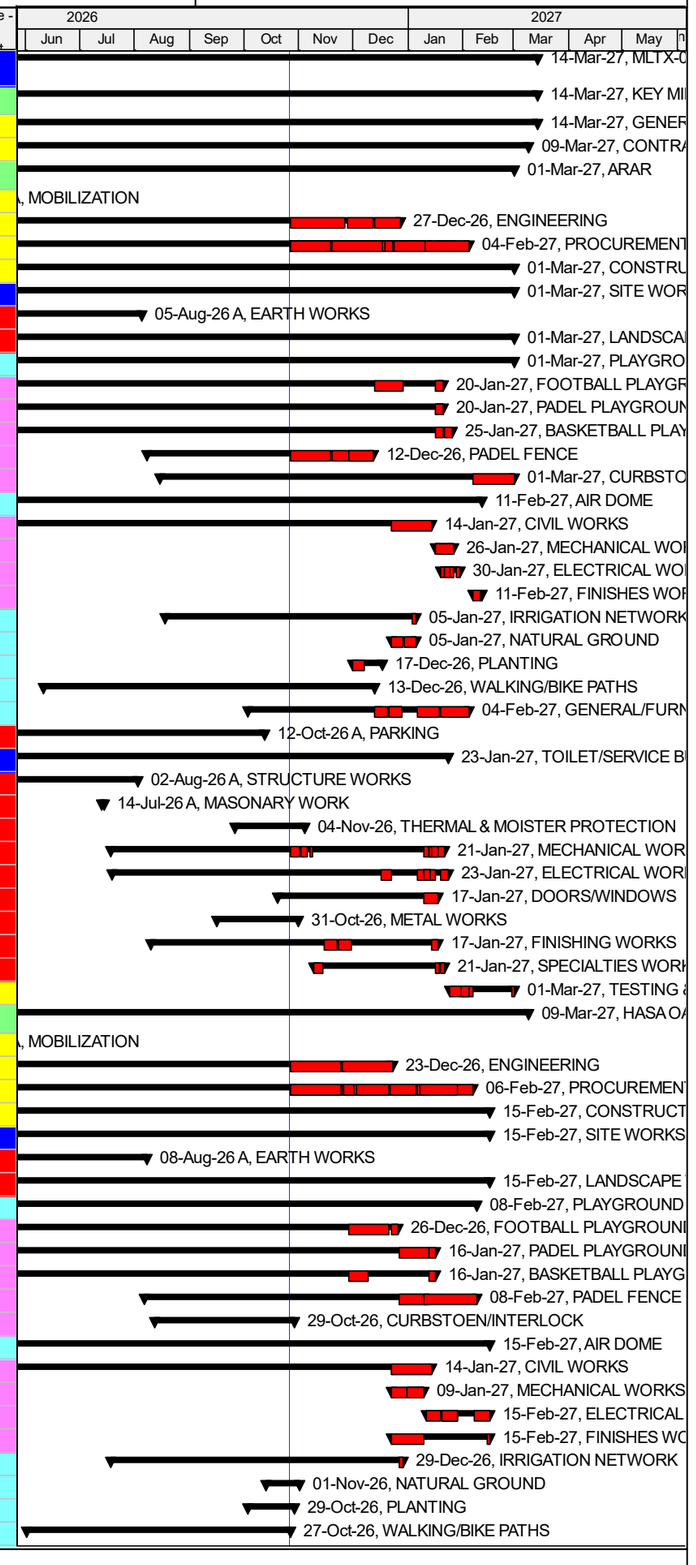

Remaining Work
Actual Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	92	26.2%	61.45%	06-Oct-26	24-Dec-26	03-Sep-26 A	20-Jan-27	123,226.50	288,969.60	470,271.40	-23
	PARKING	12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
	TOILET/SERVICE BUILDING	258	73.51%	71.59%	09-May-26	23-Dec-26	24-May-26 A	21-Jan-27	857,172.90	834,715.25	1,166,004.29	-25
	STRUCTURE WORKS	45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
	MASONARY WORK	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
	THERMAL & MOISTER PROTECTION	41	100%	95.21%	04-Jul-26	19-Aug-26	10-Sep-26 A	16-Nov-26	34,698.32	33,037.59	34,698.32	-75
	MECHANICAL WORK	116	99.26%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	06-Jan-27	262,723.23	262,723.23	264,673.10	-14
	ELECTRICAL WORKS	117	53.29%	53.29%	03-Sep-26	21-Dec-26	14-Jul-26 A	18-Jan-27	206,217.58	206,217.58	386,998.85	-24
	DOORS/WINDOWS	213	14.29%	29.71%	04-Jul-26	16-Dec-26	28-Sep-26 A	08-Nov-26	9,749.30	20,278.55	68,245.12	33
	METAL WORKS	57	100%	71.43%	03-Sep-26	20-Oct-26	06-Sep-26 A	05-Dec-26	13,649.02	9,749.30	13,649.02	-39
	FINISHING WORKS	110	85.53%	70.6%	20-Aug-26	16-Dec-26	17-Aug-26 A	21-Jan-27	140,327.66	115,826.00	164,060.22	-31
	SPECIALTIES WORK	92	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	11-Jan-27	14,623.96	11,699.17	58,495.83	-16
	TESTING & COMMISSIONING	45	0%	0%	08-Dec-26	02-Jan-27	16-Jan-27	09-Mar-27	0.00	0.00	0.00	-56
	DAMMAM	303	40.9%	40.01%	03-Mar-26	02-Jan-27	04-Mar-26 A	28-Feb-27	4,014,394.54	3,926,928.87	9,815,232.20	-48
	MOBILIZATION	33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
	ENGINEERING	250	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	23-Dec-26	0.00	0.00	0.00	-10
	PROCUREMENT	251	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	09-Feb-27	0.00	0.00	0.00	-43
	CONSTRUCTION PHASE	268	40.9%	40.01%	16-Apr-26	31-Dec-26	04-Apr-26 A	28-Feb-27	4,014,394.54	3,926,928.87	9,815,232.20	-49
	SITE WORKS	268	36.32%	35.01%	16-Apr-26	31-Dec-26	04-Apr-26 A	28-Feb-27	3,141,483.40	3,028,380.41	8,649,227.95	-49
	EARTH WORKS	44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
	LANDSCAPE WORKS	246	34.04%	32.5%	12-May-26	31-Dec-26	19-May-26 A	28-Feb-27	2,834,641.51	2,706,649.30	8,327,496.85	-49
	PLAYGROUND AREA	239	78.28%	55.89%	12-May-26	31-Dec-26	19-May-26 A	03-Feb-27	1,006,771.87	718,786.07	1,286,157.31	-29
	FOOTBALL PLAYGROUND	216	85%	35%	12-May-26	15-Dec-26	19-May-26 A	23-Jan-27	269,322.49	110,897.50	316,849.99	-33
	PADEL PLAYGROUND	214	70%	70%	24-May-26	24-Dec-26	19-May-26 A	01-Feb-27	163,788.80	163,788.80	233,984.00	-33
	BASKETBALL PLAYGROUND	165	66.45%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	03-Feb-27	211,355.57	221,133.58	318,089.68	-29
	PADEL FENCE	51	0%	9.24%	25-Nov-26	24-Dec-26	08-Aug-26 A	23-Jan-27	0.00	5,077.72	54,928.63	-25
	CURBSTOEN/INTERLOCK	150	100%	60.14%	27-Aug-26	21-Sep-26	10-Aug-26 A	02-Nov-26	362,305.01	217,888.47	362,305.01	-35
	AIR DOME	190	23.18%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	26-Jan-27	1,299,527.51	1,299,527.51	5,605,894.61	-28
	CIVIL WORKS	180	48.29%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	14-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-33
	MECHANICAL WORKS	5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	1,233,296.81	-33
	ELECTRICAL WORKS	10	0%	0%	08-Dec-26	24-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	1,513,591.54	-28
	FINISHES WORKS	4	0%	0%	12-Dec-26	15-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	168,176.84	-33
	IRRIGATION NETWORK	122	83.53%	83.53%	10-Sep-26	02-Dec-26	24-Aug-26 A	31-Jan-27	127,308.67	127,308.67	152,414.87	-51
	NATURAL GROUND	35	33.9%	16.95%	10-Oct-26	12-Nov-26	20-Oct-26 A	30-Nov-26	65,000.00	32,500.00	191,740.00	-15
	PLANTING	23	0%	6%	06-Dec-26	31-Dec-26	24-Oct-26 A	25-Feb-27	0.00	20,835.09	347,251.46	-47
	WALKING/BIKE PATHS	31	90.27%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	247,137.91	273,767.20	273,767.20	35
	GENERAL/FURNITURE	135	18.9%	49.74%	22-Sep-26	31-Dec-26	20-Sep-26 A	28-Feb-27	88,895.55	233,924.76	470,271.40	-49
	PARKING	15	74.55%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	43,604.12	58,493.33	58,493.33	35
	TOILET/SERVICE BUILDING	228	74.86%	77.06%	01-Jun-26	29-Dec-26	23-May-26 A	23-Feb-27	872,911.14	898,548.46	1,166,004.25	-47
	STRUCTURE WORKS	54	100%	100%	01-Jun-26	02-Aug-26	23-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	0
	MASONARY WORK	5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2
	THERMAL & MOISTER PROTECTION	21	100%	95.21%	03-Aug-26	26-Aug-26	25-Aug-26 A	04-Nov-26	34,698.32	33,037.59	34,698.32	-59
	MECHANICAL WORK	104	99.26%	99.26%	09-Sep-26	26-Dec-26	12-Jul-26 A	09-Jan-27	262,723.23	262,723.23	264,673.10	-12
	ELECTRICAL WORKS	113	53.29%	53.29%	12-Sep-26	29-Dec-26	14-Jul-26 A	21-Jan-27	206,217.55	206,217.55	386,998.82	-20
	DOORS/WINDOWS	118	91.43%	100%	19-Sep-26	27-Dec-26	17-Sep-26 A	26-Oct-26 A	62,395.54	68,245.12	68,245.12	53
	METAL WORKS	66	100%	71.43%	10-Sep-26	26-Oct-26	05-Sep-26 A	10-Dec-26	13,649.02	9,749.30	13,649.02	-39
	FINISHING WORKS	105	71.95%	80.27%	27-Aug-26	21-Dec-26	17-Aug-26 A	11-Jan-27	118,043.65	131,692.67	164,060.21	-18
	SPECIALTIES WORK	52	0%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	23-Feb-27	0.00	11,699.17	58,495.83	-52
	TESTING & COMMISSIONING	7	0%	0%	24-Dec-26	02-Jan-27	20-Feb-27	28-Feb-27	0.00	0.00	0.00	-48
	PROJECT CLOSEOUT & DEMOBILIZATION	46	0%	0%	08-Dec-26	02-Jan-27	16-Jan-27	14-Mar-27	0.00	0.00	0.00	-57
	As-Built DWGs	42	0%	0%	08-Dec-26	31-Dec-26	16-Jan-27	06-Mar-27	0.00	0.00	0.00	-54
	Demobilization	8	0%	0%	28-Dec-26	02-Jan-27	02-Mar-27	14-Mar-27	0.00	0.00	0.00	-57

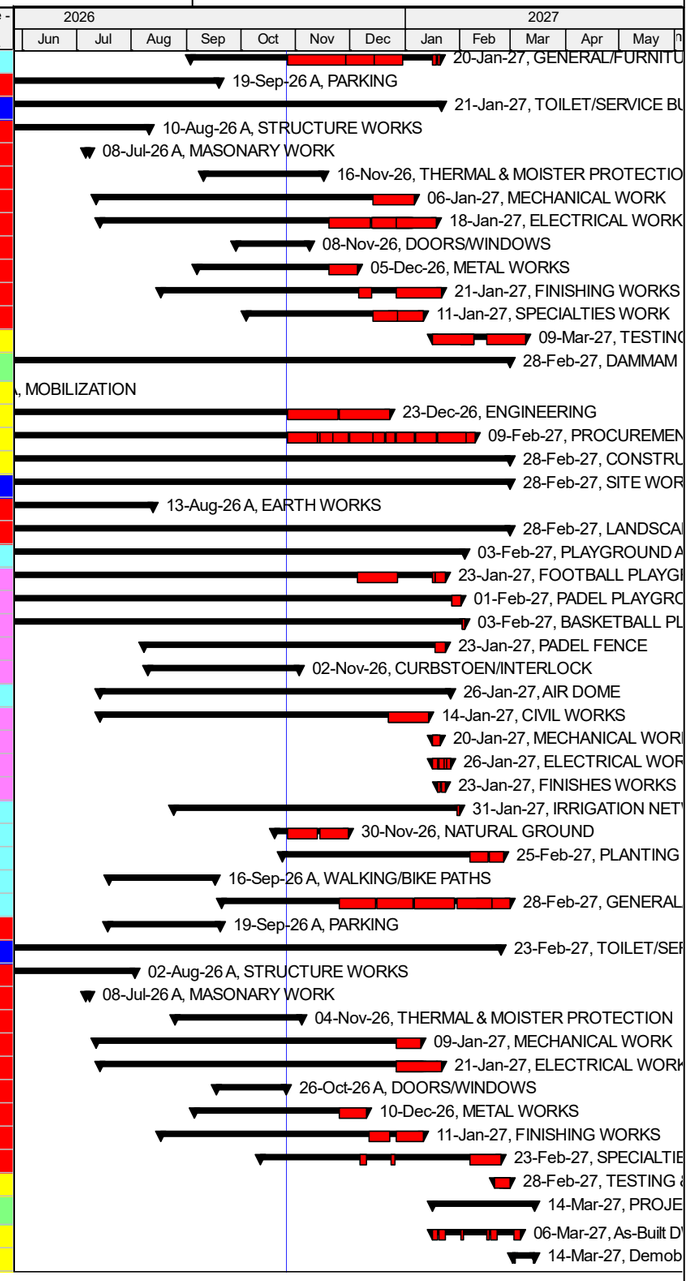

Remaining Work
Actual Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
